ID	Task Name	Duration	Start	Finish	Predecessors
1	**Hendy - Canolfan Gwili Centre**	**290 days**	**Mon 16/09/24**	**Fri 24/10/25**	
2	**Site Setup**	**28 days**	**Mon 16/09/24**	**Wed 23/10/24**	
3	Site Clearance	14 days	Mon 16/09/24	Thu 03/10/24	
4	Site Perimeter Fencing Installation	3 days	Fri 04/10/24	Tue 08/10/24	3
5	Site Office Installation	1 day	Wed 09/10/24	Wed 09/10/24	4
6	Welfare Facilities Installation	1 day	Thu 10/10/24	Thu 10/10/24	5
7	Storage Area Setup	3 days	Thu 10/10/24	Mon 14/10/24	5
8	Waste Management Setup	2 days	Tue 15/10/24	Wed 16/10/24	7
9	Setting out of proposed footprint	5 days	Thu 17/10/24	Wed 23/10/24	8
10					
11	**Construction of Extension**	**148 days**	**Thu 24/10/24**	**Mon 19/05/25**	**2**
12	**Foundation Construction**	**74 days**	**Thu 24/10/24**	**Tue 04/02/25**	
13	Excavation of Footings	15 days	Thu 24/10/24	Wed 13/11/24	2
14	Excavation for Services	15 days	Thu 14/11/24	Wed 04/12/24	13
15	**Installation of services**	**15 days**	**Thu 05/12/24**	**Wed 25/12/24**	**14**
16	Drainage	13 days	Thu 05/12/24	Mon 23/12/24	13
17	Plumbing Services	15 days	Thu 05/12/24	Wed 25/12/24	13
18	Electrical cables	10 days	Thu 05/12/24	Wed 18/12/24	13
19	Backfill of Service Trench	3 days	Thu 26/12/24	Mon 30/12/24	15
20	Foundation Reinforcement Installati	12 days	Tue 31/12/24	Wed 15/01/25	19
21	Foundation Concrete Pour	2 days	Thu 16/01/25	Fri 17/01/25	20
22	Concrete Curing Time	7 days	Mon 20/01/25	Tue 28/01/25	21
23	Backfill to reinstate ground level	5 days	Wed 29/01/25	Tue 04/02/25	22
24	Foundation Complete	0 days	Tue 04/02/25	Tue 04/02/25	23
25	**Slab Construction**	**113 days**	**Thu 24/10/24**	**Mon 31/03/25**	
26	Leveling of ground for slab	8 days	Thu 24/10/24	Mon 04/11/24	13SS
27	100mm Binding Layer Installation	5 days	Wed 05/02/25	Tue 11/02/25	24
28	Compaction of Binding Layer	3 days	Wed 12/02/25	Fri 14/02/25	27
29	25mm Sand Layer Installation	3 days	Mon 17/02/25	Wed 19/02/25	28
30	Sand Compaction	2 days	Thu 20/02/25	Fri 21/02/25	29
31	Installation of DPC	1 day	Mon 24/02/25	Mon 24/02/25	30
32	Slab Reinforcement Installation	8 days	Tue 25/02/25	Thu 06/03/25	31
33	Slab Concrete Pour	1 day	Fri 07/03/25	Fri 07/03/25	32
34	Slab Concrete Curing Time	7 days	Mon 10/03/25	Tue 18/03/25	33
35	Installation of Rigid Insulation Boarc	2 days	Wed 19/03/25	Thu 20/03/25	34
36	Installation of Separation layer	1 day	Fri 21/03/25	Fri 21/03/25	35
37	Final Flooring Screed Pour	1 day	Mon 24/03/25	Mon 24/03/25	36
38	Screed Curing Time	5 days	Tue 25/03/25	Mon 31/03/25	37
39	Flooring Complete	0 days	Mon 31/03/25	Mon 31/03/25	38
40	**Wall Construction**	20 days	Tue 01/04/25	Mon 28/04/25	39
41	**Roof Construction**	15 days	Tue 29/04/25	Mon 19/05/25	40

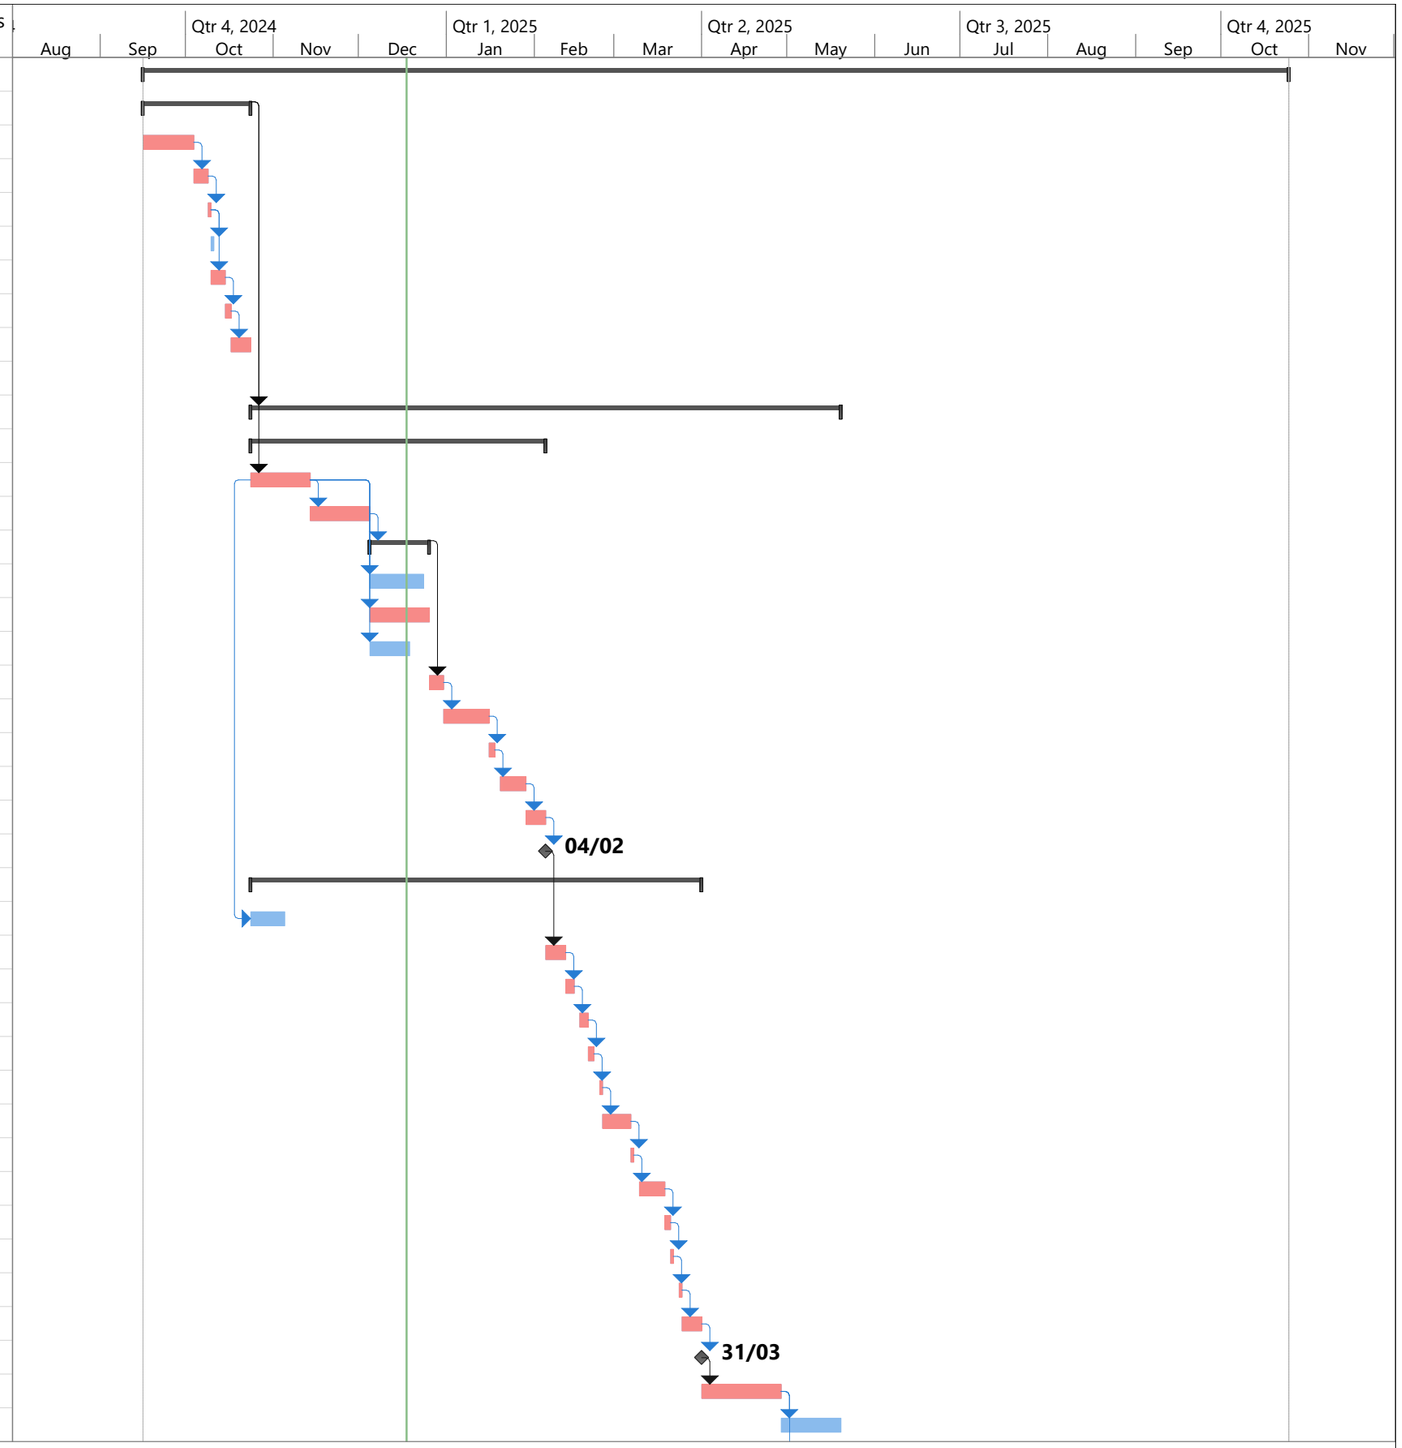

Project: Hendy - Project Schedu
Date: Wed 18/12/24

Critical Split		Summary		Inactive Summary		Manual Summary		External Milestone	
Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Manual Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Critical	

ID	Task Name	Duration	Start	Finish	Predecessors
42					
43	**Renovation of Existing**	**79 days**	**Tue 29/04/25**	**Fri 15/08/25**	**40**
44	Demolition of Internals	5 days	Tue 29/04/25	Mon 05/05/25	40
45	Opening in External Walls to Extension	3 days	Tue 06/05/25	Thu 08/05/25	44
46	Opening in Flooring to Upper Ground Floor	7 days	Fri 09/05/25	Mon 19/05/25	45
47	Construction of Internal walls	10 days	Tue 20/05/25	Mon 02/06/25	46
48	First Fix	27 days	Tue 03/06/25	Wed 09/07/25	47
49	Second Fix	27 days	Thu 10/07/25	Fri 15/08/25	48
50	Renovation of existing Completion	0 days	Fri 15/08/25	Fri 15/08/25	49
51					
52	**Car Park Construction**	**40 days**	**Mon 18/08/25**	**Fri 10/10/25**	**50**
53	Area clearing and levelling.	10 days	Mon 18/08/25	Fri 29/08/25	
54	Setting out	3 days	Mon 01/09/25	Wed 03/09/25	53
55	Installation of Kirbs	7 days	Thu 04/09/25	Fri 12/09/25	54
56	Installation of road	10 days	Mon 15/09/25	Fri 26/09/25	55
57	Installation of vegitation	5 days	Mon 29/09/25	Fri 03/10/25	56
58	Road & parking bay markings	5 days	Mon 06/10/25	Fri 10/10/25	57
59	Car Par Construction Completion	0 days	Fri 10/10/25	Fri 10/10/25	58
60					
61	**Site Handover**	**10 days**	**Mon 13/10/25**	**Fri 24/10/25**	
62	Snagging List Completion	5 days	Mon 13/10/25	Fri 17/10/25	58
63	Removal of Site Office	1 day	Mon 20/10/25	Mon 20/10/25	62
64	Removal of all Waste Management	1 day	Tue 21/10/25	Tue 21/10/25	63
65	Removal of Storage container	1 day	Wed 22/10/25	Wed 22/10/25	64
66	Removal of Site Fencing	1 day	Thu 23/10/25	Thu 23/10/25	65
67	Client Walk Through	1 day	Fri 24/10/25	Fri 24/10/25	66
68	Project Completion	0 days	Fri 24/10/25	Fri 24/10/25	67
69					
70	**Long Term Equipment/Facilities**	**276 days**	**Fri 04/10/24**	**Fri 24/10/25**	
71	Fencing	276 days	Fri 04/10/24	Fri 24/10/25	
72	Site Office	273 days	Wed 09/10/24	Fri 24/10/25	
73	Welfare Facilities	272 days	Thu 10/10/24	Fri 24/10/25	
74	Storage Container	272 days	Thu 10/10/24	Fri 24/10/25	
75	Waste Management	269 days	Tue 15/10/24	Fri 24/10/25	

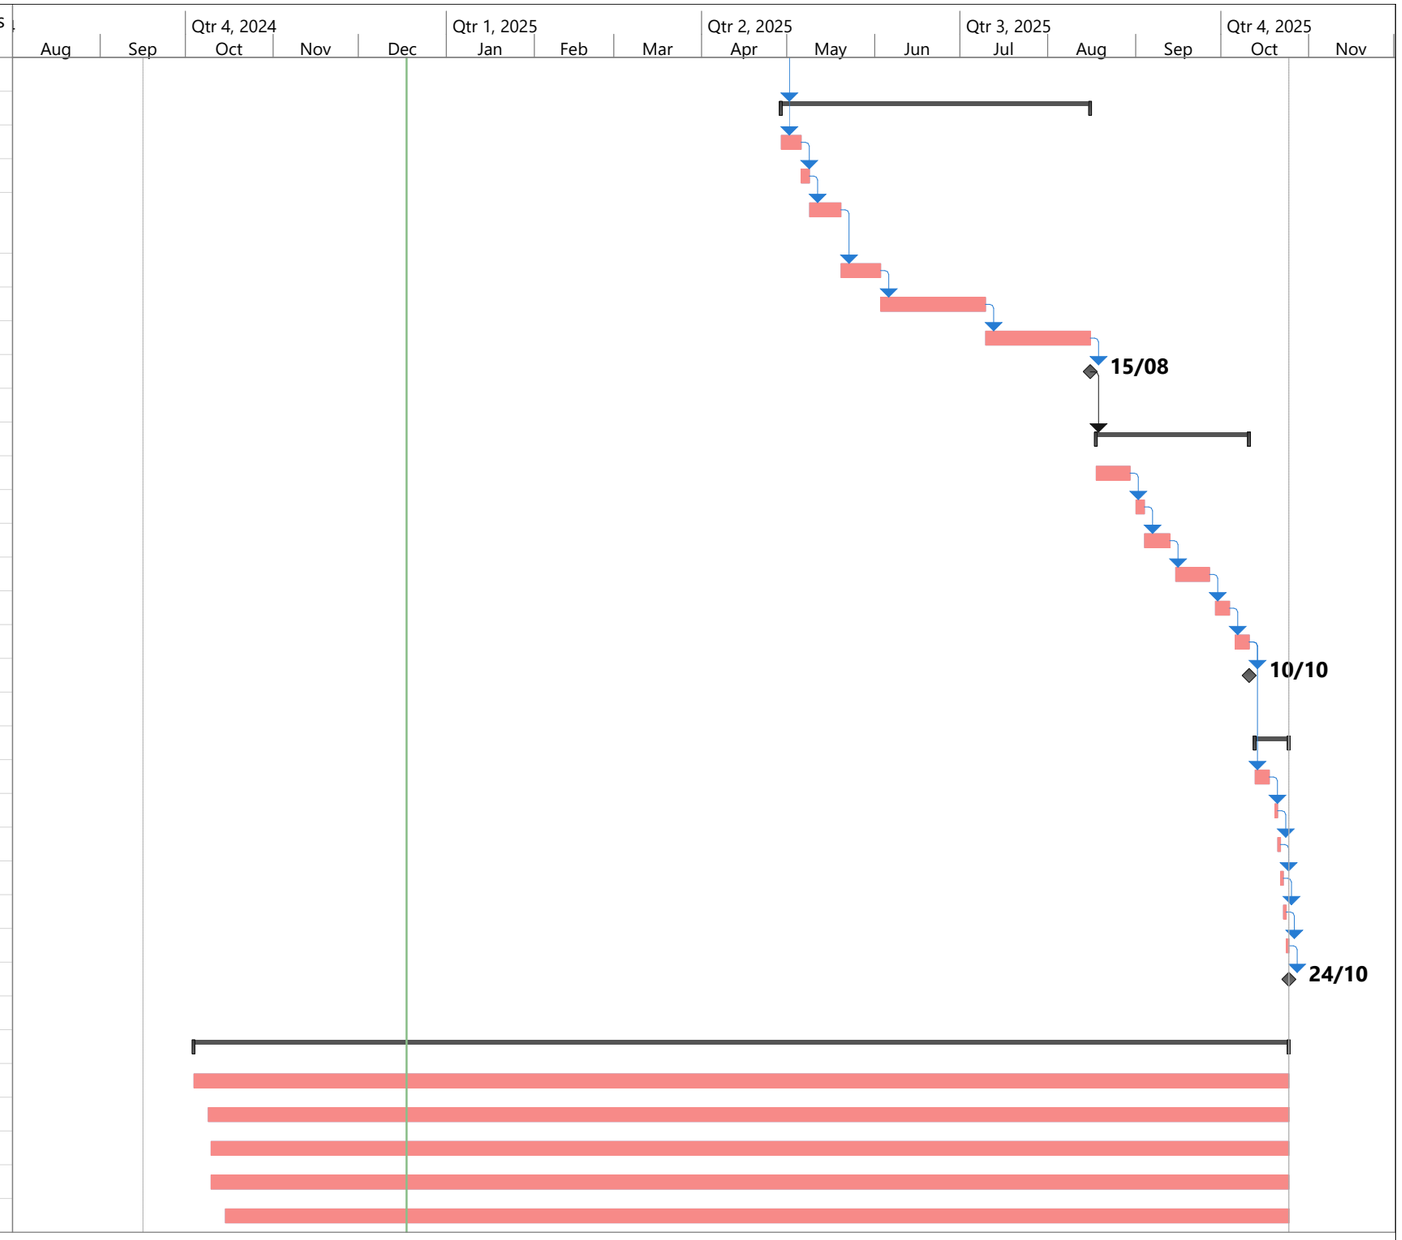

Project: Hendy - Project Schedu
Date: Wed 18/12/24

Critical Split	Summary	Inactive Summary	Manual Summary	External Milestone
Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Manual Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Critical
