


| ID |  | Task Mode                                                                         | Task Name               | Duration | Start        | Finish       | Predecessors | Feb | Mar | Qtr 2, 2020<br>Apr | May                                                                                 |
|----|-----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-------------------------|----------|--------------|--------------|--------------|-----|-----|--------------------|-------------------------------------------------------------------------------------|
| 1  |                                                                                   |  | site set up             | 7 days   | Wed 06/05/20 | Thu 14/05/20 |              |     |     |                    |  |
| 2  |                                                                                   |  | access to the site      | 2 days   | Wed 06/05/20 | Thu 07/05/20 |              |     |     |                    |                                                                                     |
| 3  |  |  | site preparation        | 2 days   | Fri 08/05/20 | Mon 11/05/20 | 2            |     |     |                    |                                                                                     |
| 4  |  |  | material delivery       | 5 days   | Fri 08/05/20 | Thu 14/05/20 | 2            |     |     |                    |                                                                                     |
| 5  |                                                                                   |  | sub-structure           | 60 days  | Fri 15/05/20 | Thu 06/08/20 |              |     |     |                    |                                                                                     |
| 6  |                                                                                   |  | excavation              | 53 days  | Fri 15/05/20 | Tue 28/07/20 |              |     |     |                    |                                                                                     |
| 7  |  |  | surveying               | 53 days  | Fri 15/05/20 | Tue 28/07/20 |              |     |     |                    |                                                                                     |
| 8  |                                                                                   |  | excavation pile line1   | 13 days  | Fri 15/05/20 | Tue 02/06/20 | 4            |     |     |                    |                                                                                     |
| 9  |  |  | excavation pile line2   | 9 days   | Wed 03/06/20 | Mon 15/06/20 | 8            |     |     |                    |                                                                                     |
| 10 |  |  | excavation pile line3   | 9 days   | Tue 16/06/20 | Fri 26/06/20 | 9            |     |     |                    |                                                                                     |
| 11 |  |  | excavation pile line4   | 9 days   | Mon 29/06/20 | Thu 09/07/20 | 10           |     |     |                    |                                                                                     |
| 12 |  |  | excavation pile line5   | 13 days  | Fri 10/07/20 | Tue 28/07/20 | 11           |     |     |                    |                                                                                     |
| 13 |                                                                                   |  | reinforcement of piles  | 46 days  | Wed 03/06/20 | Wed 05/08/20 |              |     |     |                    |                                                                                     |
| 14 |  |  | surveying               | 46 days  | Wed 03/06/20 | Wed 05/08/20 |              |     |     |                    |                                                                                     |
| 15 |  |  | reinforcment pile line1 | 6 days   | Wed 03/06/20 | Wed 10/06/20 | 8            |     |     |                    |                                                                                     |
| 16 |  |  | reinforcment pile line2 | 4 days   | Tue 16/06/20 | Fri 19/06/20 | 9            |     |     |                    |                                                                                     |
| 17 |  |  | reinforcment pile line3 | 4 days   | Mon 29/06/20 | Thu 02/07/20 | 10           |     |     |                    |                                                                                     |



Project: Project assignment 1  
Date: Mon 04/05/20

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |    | Task Mode                                                                           | Task Name                        | Duration         | Start               | Finish              | Predecessors | Feb | Mar | Qtr 2, 2020<br>Apr | May |
|----|-------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|----------------------------------|------------------|---------------------|---------------------|--------------|-----|-----|--------------------|-----|
| 18 |    |    | reinforcment pile line4          | 4 days           | Fri 10/07/20        | Wed 15/07/20        | 11           |     |     |                    |     |
| 19 |    |    | reinforcment pile line5          | 6 days           | Wed 29/07/20        | Wed 05/08/20        | 12           |     |     |                    |     |
| 20 |                                                                                     |    | <b>pouring concrete of piles</b> | <b>41 days</b>   | <b>Thu 11/06/20</b> | <b>Thu 06/08/20</b> |              |     |     |                    |     |
| 21 |    |    | pouring concrete pile line1      | 1 day            | Thu 11/06/20        | Thu 11/06/20        | 15           |     |     |                    |     |
| 22 |    |    | pouring concrete pile line2      | 1 day            | Mon 22/06/20        | Mon 22/06/20        | 16           |     |     |                    |     |
| 23 |    |    | pouring concrete pile line3      | 1 day            | Fri 03/07/20        | Fri 03/07/20        | 17           |     |     |                    |     |
| 24 |    |    | pouring concrete pile line4      | 1 day            | Thu 16/07/20        | Thu 16/07/20        | 18           |     |     |                    |     |
| 25 |                                                                                     |    | pouring concrete pile line5      | 1 day            | Thu 06/08/20        | Thu 06/08/20        | 19           |     |     |                    |     |
| 26 |                                                                                     |    | <b>pilecap reinforcement</b>     | <b>46 days</b>   | <b>Tue 23/06/20</b> | <b>Tue 25/08/20</b> |              |     |     |                    |     |
| 27 |    |    | <b>surveying</b>                 | <b>44 days</b>   | <b>Tue 23/06/20</b> | <b>Fri 21/08/20</b> |              |     |     |                    |     |
| 28 |                                                                                     |    | <b>reinforcement</b>             | <b>44 days</b>   | <b>Tue 23/06/20</b> | <b>Fri 21/08/20</b> |              |     |     |                    |     |
| 34 |                                                                                     |    | <b>surveying</b>                 | <b>33.5 days</b> | <b>Wed 08/07/20</b> | <b>Mon 24/08/20</b> |              |     |     |                    |     |
| 35 |                                                                                     |    | <b>concrete case (formwork)</b>  | <b>33.5 days</b> | <b>Wed 08/07/20</b> | <b>Mon 24/08/20</b> |              |     |     |                    |     |
| 36 |  |  | concrete case pilecap line1      | 1 day            | Thu 09/07/20        | Thu 09/07/20        | 29           |     |     |                    |     |

Project: Project assignment 1  
Date: Mon 04/05/20

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |    | Task Mode                                                                           | Task Name                            | Duration         | Start               | Finish              | Predecessors | Feb | Mar | Qtr 2, 2020<br>Apr | May |
|----|-------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|--------------------------------------|------------------|---------------------|---------------------|--------------|-----|-----|--------------------|-----|
| 37 |    |    | concrete case pilecap line2          | 1 day            | Wed 08/07/20        | Thu 09/07/20        | 30           |     |     |                    |     |
| 38 |    |    | concrete case pilecap line3          | 1 day            | Mon 20/07/20        | Mon 20/07/20        | 31           |     |     |                    |     |
| 39 |    |    | concrete case pilecap line4          | 1 day            | Fri 31/07/20        | Fri 31/07/20        | 32           |     |     |                    |     |
| 40 |                                                                                     |    | concrete case pilecap line5          | 1 day            | Mon 24/08/20        | Mon 24/08/20        | 33           |     |     |                    |     |
| 41 |                                                                                     |    | <b>pouring concrete</b>              | <b>33.5 days</b> | <b>Thu 09/07/20</b> | <b>Tue 25/08/20</b> |              |     |     |                    |     |
| 42 |    |    | pouring concrete pilecap line1       | 1 day            | Fri 10/07/20        | Fri 10/07/20        | 36           |     |     |                    |     |
| 43 |    |    | pouring concrete pilecap line2       | 1 day            | Thu 09/07/20        | Fri 10/07/20        | 37           |     |     |                    |     |
| 44 |    |    | pouring concrete pilecap line3       | 1 day            | Tue 21/07/20        | Tue 21/07/20        | 38           |     |     |                    |     |
| 45 |    |    | pouring concrete pilecap line4       | 1 day            | Mon 03/08/20        | Mon 03/08/20        | 39           |     |     |                    |     |
| 46 |                                                                                     |    | pouring concrete pilecap line5       | 1 day            | Tue 25/08/20        | Tue 25/08/20        | 40           |     |     |                    |     |
| 47 |                                                                                     |    | <b>ABUTMENTS/PIERS</b>               | <b>35.5 days</b> | <b>Tue 21/07/20</b> | <b>Tue 08/09/20</b> |              |     |     |                    |     |
| 48 |    |    | <b>survaing</b>                      | <b>33.5 days</b> | <b>Tue 21/07/20</b> | <b>Fri 04/09/20</b> |              |     |     |                    |     |
| 49 |                                                                                     |    | <b>reinforcement</b>                 | <b>33.5 days</b> | <b>Tue 21/07/20</b> | <b>Fri 04/09/20</b> |              |     |     |                    |     |
| 50 |  |  | ABUTMENTS/PIERS reinforcement line 1 | 1 day            | Wed 22/07/20        | Wed 22/07/20        | 42FS+7 days  |     |     |                    |     |

Project: Project assignment 1  
Date: Mon 04/05/20

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |  | Task Mode                                                                         | Task Name                            | Duration         | Start               | Finish              | Predecessors | Feb | Mar | Qtr 2, 2020<br>Apr | May |
|----|-----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|--------------------------------------|------------------|---------------------|---------------------|--------------|-----|-----|--------------------|-----|
| 51 |  |  | ABUTMENTS/PIERS reinforcement line 2 | 1 day            | Tue 21/07/20        | Wed 22/07/20        | 43FS+7 days  |     |     |                    |     |
| 52 |  |  | ABUTMENTS/PIERS reinforcement line 3 | 1 day            | Fri 31/07/20        | Fri 31/07/20        | 44FS+7 days  |     |     |                    |     |
| 53 |                                                                                   |  | ABUTMENTS/PIERS reinforcement line 4 | 1 day            | Thu 13/08/20        | Thu 13/08/20        | 45FS+7 days  |     |     |                    |     |
| 54 |                                                                                   |  | ABUTMENTS/PIERS reinforcement line 5 | 1 day            | Fri 04/09/20        | Fri 04/09/20        | 46FS+7 days  |     |     |                    |     |
| 55 |                                                                                   |  | <b>surveying</b>                     | <b>33.5 days</b> | <b>Wed 22/07/20</b> | <b>Mon 07/09/20</b> |              |     |     |                    |     |
| 56 |                                                                                   |  | <b>concrete case</b>                 | <b>33.5 days</b> | <b>Wed 22/07/20</b> | <b>Mon 07/09/20</b> |              |     |     |                    |     |
| 57 |  |  | ABUTMENT/PIER concrete case line 1   | 1 day            | Thu 23/07/20        | Thu 23/07/20        | 50           |     |     |                    |     |
| 58 |  |  | ABUTMENT/PIER concrete case line 2   | 1 day            | Wed 22/07/20        | Thu 23/07/20        | 51           |     |     |                    |     |
| 59 |  |  | ABUTMENT/PIER concrete case line 3   | 1 day            | Mon 03/08/20        | Mon 03/08/20        | 52           |     |     |                    |     |
| 60 |  |  | ABUTMENT/PIER concrete case line 4   | 1 day            | Fri 14/08/20        | Fri 14/08/20        | 53           |     |     |                    |     |
| 61 |                                                                                   |  | ABUTMENT/PIER concrete case line 5   | 1 day            | Mon 07/09/20        | Mon 07/09/20        | 54           |     |     |                    |     |
| 62 |                                                                                   |  | <b>pouring concrete</b>              | <b>33.5 days</b> | <b>Thu 23/07/20</b> | <b>Tue 08/09/20</b> |              |     |     |                    |     |
| 63 |  |  | pouring concrete ABUTMENT/PIER line1 | 1 day            | Fri 24/07/20        | Fri 24/07/20        | 57           |     |     |                    |     |
| 64 |  |  | pouring concrete ABUTMENT/PIER line2 | 1 day            | Thu 23/07/20        | Fri 24/07/20        | 58           |     |     |                    |     |

Project: Project assignment 1  
Date: Mon 04/05/20

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |  | Task Mode                                                                           | Task Name                            | Duration       | Start               | Finish              | Predecessors            | Feb | Mar | Qtr 2, 2020<br>Apr | May |
|----|-----------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|--------------------------------------|----------------|---------------------|---------------------|-------------------------|-----|-----|--------------------|-----|
| 65 |  |    | pouring concrete ABUTMENT/PIER line3 | 1 day          | Tue 04/08/20        | Tue 04/08/20        | 59                      |     |     |                    |     |
| 66 |                                                                                   |    | pouring concrete ABUTMENT/PIER line4 | 1 day          | Mon 17/08/20        | Mon 17/08/20        | 60                      |     |     |                    |     |
| 67 |                                                                                   |    | pouring concrete ABUTMENT/PIER line5 | 1 day          | Tue 08/09/20        | Tue 08/09/20        | 61                      |     |     |                    |     |
| 68 |                                                                                   |    | <b>steel beams</b>                   | <b>33 days</b> | <b>Wed 05/08/20</b> | <b>Fri 18/09/20</b> |                         |     |     |                    |     |
| 69 |  |    | steel beams in span 1                | 1.33 days      | Wed 05/08/20        | Thu 06/08/20        | 63FS+7 days,64FS+7 days |     |     |                    |     |
| 70 |  |    | steel beams in span 2                | 1 day          | Fri 14/08/20        | Fri 14/08/20        | 64FS+7 days,65FS+7 days |     |     |                    |     |
| 71 |  |    | steel beams on span 3                | 1 day          | Thu 27/08/20        | Thu 27/08/20        | 65FS+7 days,66FS+7 days |     |     |                    |     |
| 72 |                                                                                   |    | steel beamsc in span 4               | 1 day          | Fri 18/09/20        | Fri 18/09/20        | 66FS+7 days,67FS+7 days |     |     |                    |     |
| 73 |                                                                                   |    | <b>RC deck slab on steel beams</b>   | <b>9 days</b>  | <b>Mon 21/09/20</b> | <b>Thu 01/10/20</b> |                         |     |     |                    |     |
| 74 |                                                                                   |    | <b>surveying</b>                     | <b>9 days</b>  | <b>Mon 21/09/20</b> | <b>Thu 01/10/20</b> |                         |     |     |                    |     |
| 75 |                                                                                   |    | reinforcement deck slab              | 5 days         | Mon 21/09/20        | Fri 25/09/20        | 72                      |     |     |                    |     |
| 76 |                                                                                   |    | concrete case deck slab              | 2 days         | Mon 28/09/20        | Tue 29/09/20        | 75                      |     |     |                    |     |
| 77 |                                                                                   |   | pouring concrete of deck slab        | 2 days         | Wed 30/09/20        | Thu 01/10/20        | 76                      |     |     |                    |     |
| 78 |                                                                                   |  | <b>surface</b>                       | <b>12 days</b> | <b>Tue 13/10/20</b> | <b>Wed 28/10/20</b> |                         |     |     |                    |     |


Project: Project assignment 1  
Date: Mon 04/05/20


|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

| ID |  | Task Mode                                                                         | Task Name               | Duration       | Start               | Finish              | Predecessors | Feb | Mar | Qtr 2, 2020<br>Apr | May |
|----|-----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------|-------------------------|----------------|---------------------|---------------------|--------------|-----|-----|--------------------|-----|
| 79 |                                                                                   |  | <b>surveying</b>        | <b>12 days</b> | <b>Tue 13/10/20</b> | <b>Wed 28/10/20</b> |              |     |     |                    |     |
| 80 |                                                                                   |  | substructure of road    | 2 days         | Tue 13/10/20        | Wed 14/10/20        | 77FS+7 days  |     |     |                    |     |
| 81 |  |  | curb                    | 5 days         | Thu 15/10/20        | Wed 21/10/20        | 80           |     |     |                    |     |
| 82 |  |  | footway and cycle track | 7 days         | Thu 15/10/20        | Fri 23/10/20        | 80           |     |     |                    |     |
| 83 |  |  | asphalt or tar          | 2 days         | Thu 22/10/20        | Fri 23/10/20        | 81           |     |     |                    |     |
| 84 |                                                                                   |  | 1.5m high RC parapet    | 3 days         | Mon 26/10/20        | Wed 28/10/20        | 82           |     |     |                    |     |


Project: Project assignment 1  
Date: Mon 04/05/20

|                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Task               |  | Inactive Summary      |  | External Tasks     |  |
| Split              |  | Manual Task           |  | External Milestone |  |
| Milestone          |  | Duration-only         |  | Deadline           |  |
| Summary            |  | Manual Summary Rollup |  | Progress           |  |
| Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
| Inactive Task      |  | Start-only            |  |                    |                                                                                       |
| Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |

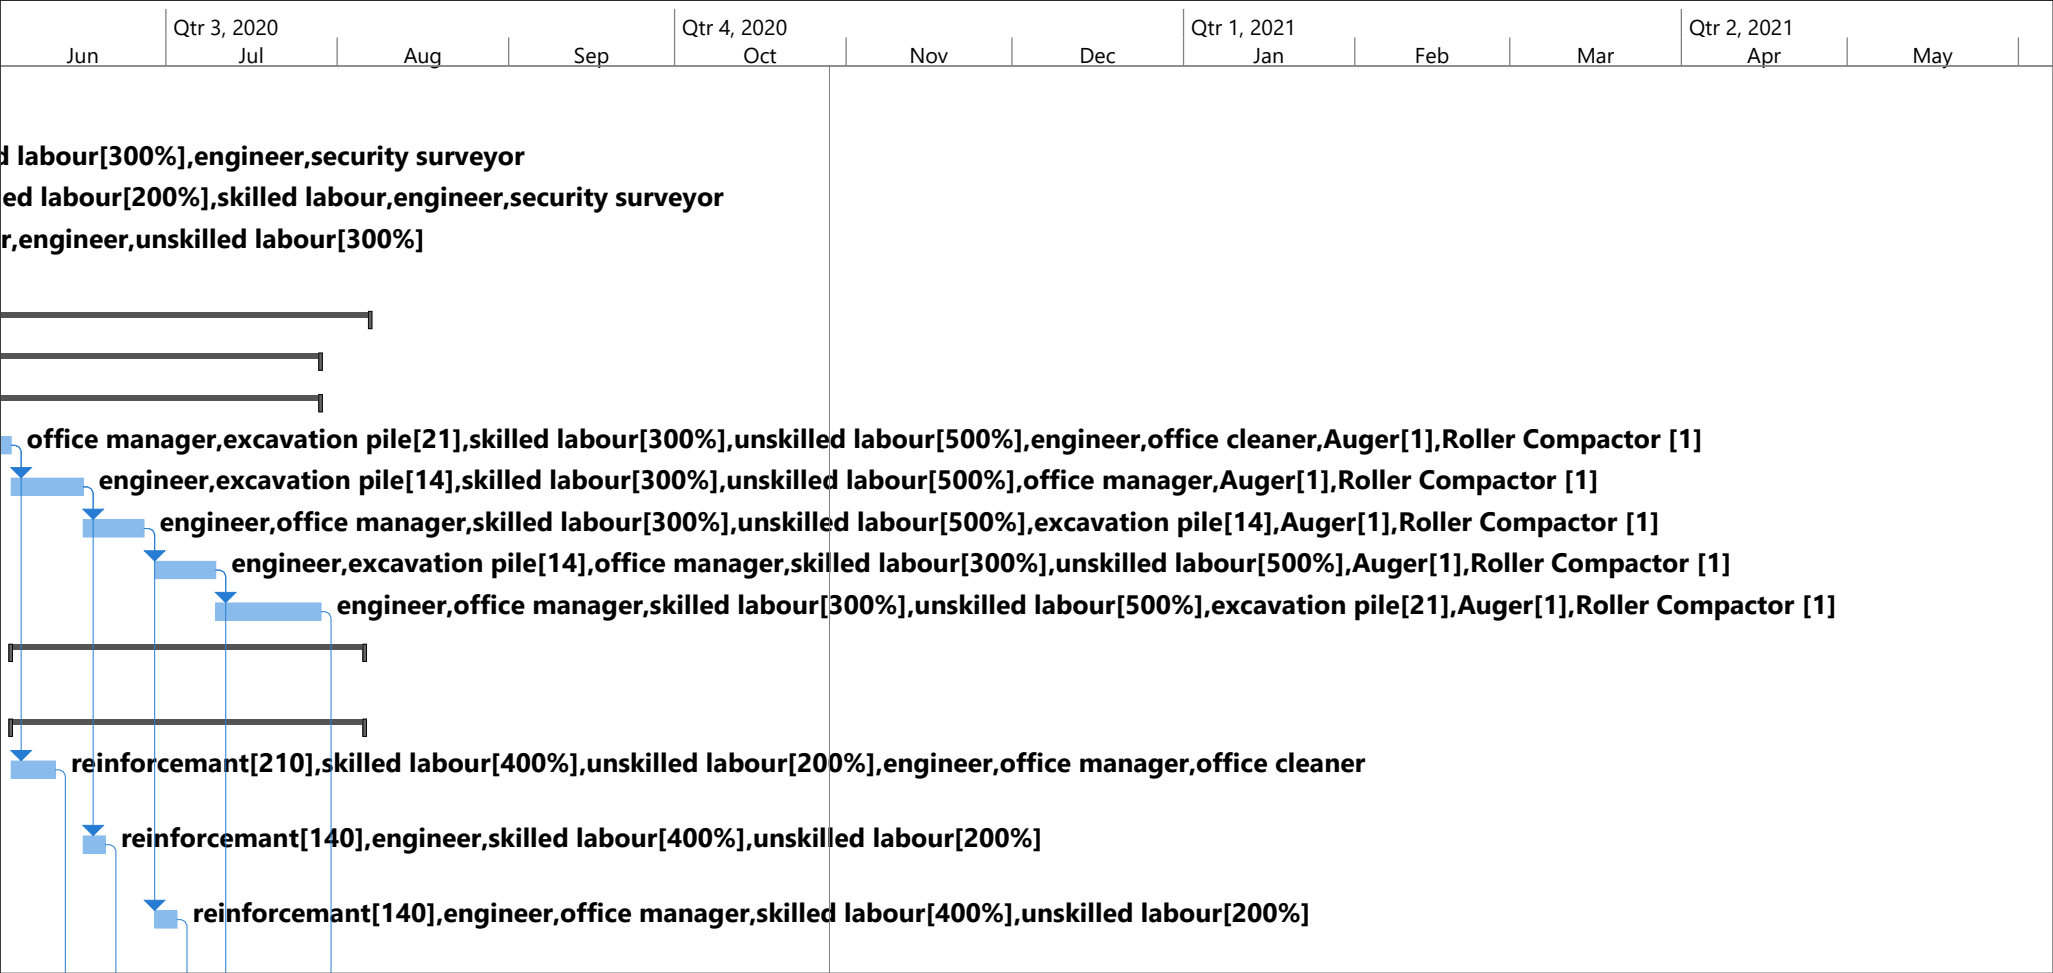


|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |
|-----------------------------------------------------|--------------------|-------------------------------------------------------------------------------------|-----------------------|---------------------------------------------------------------------------------------|--------------------|---------------------------------------------------------------------------------------|
| Project: Project assignment 1<br>Date: Mon 04/05/20 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |                                                                                       |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |                                                                                       |
|                                                     |                    |                                                                                     |                       |                                                                                       |                    |                                                                                       |




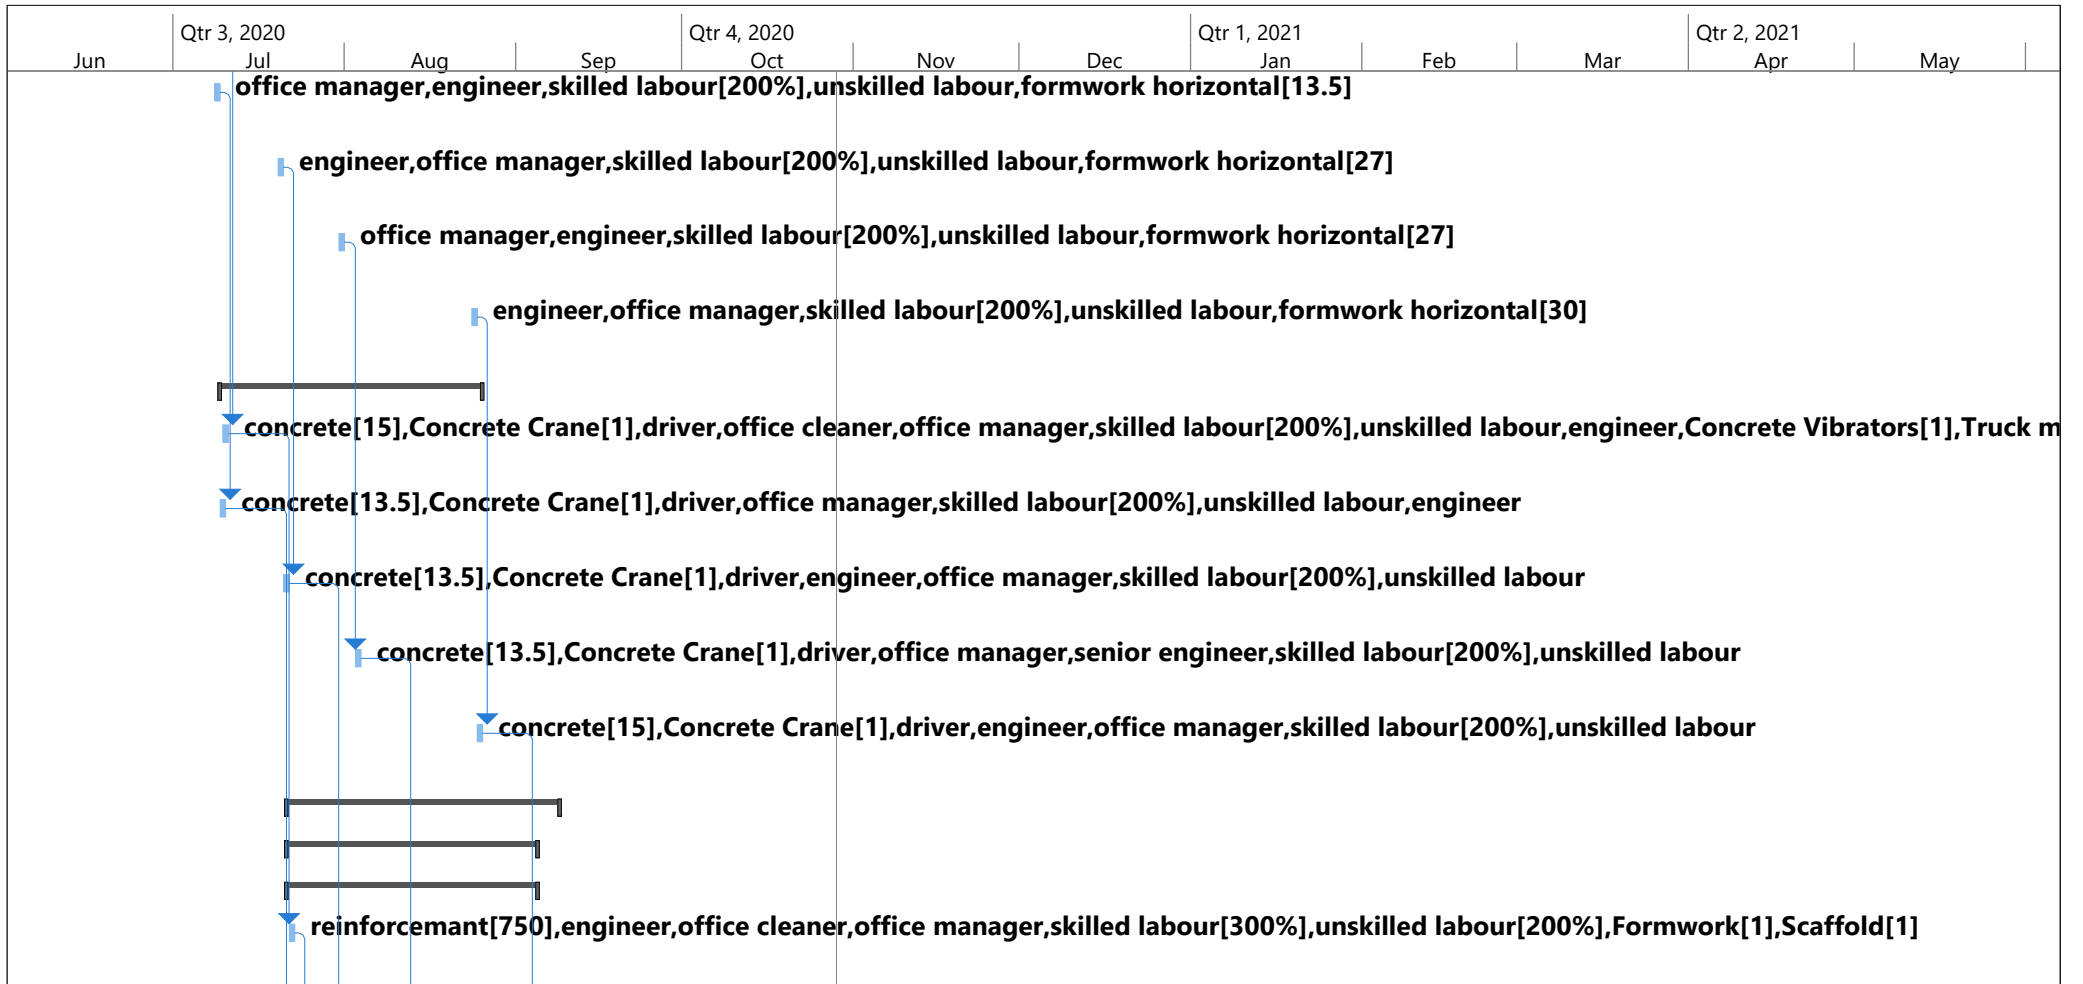


|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Project assignment 1<br>Date: Mon 04/05/20 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

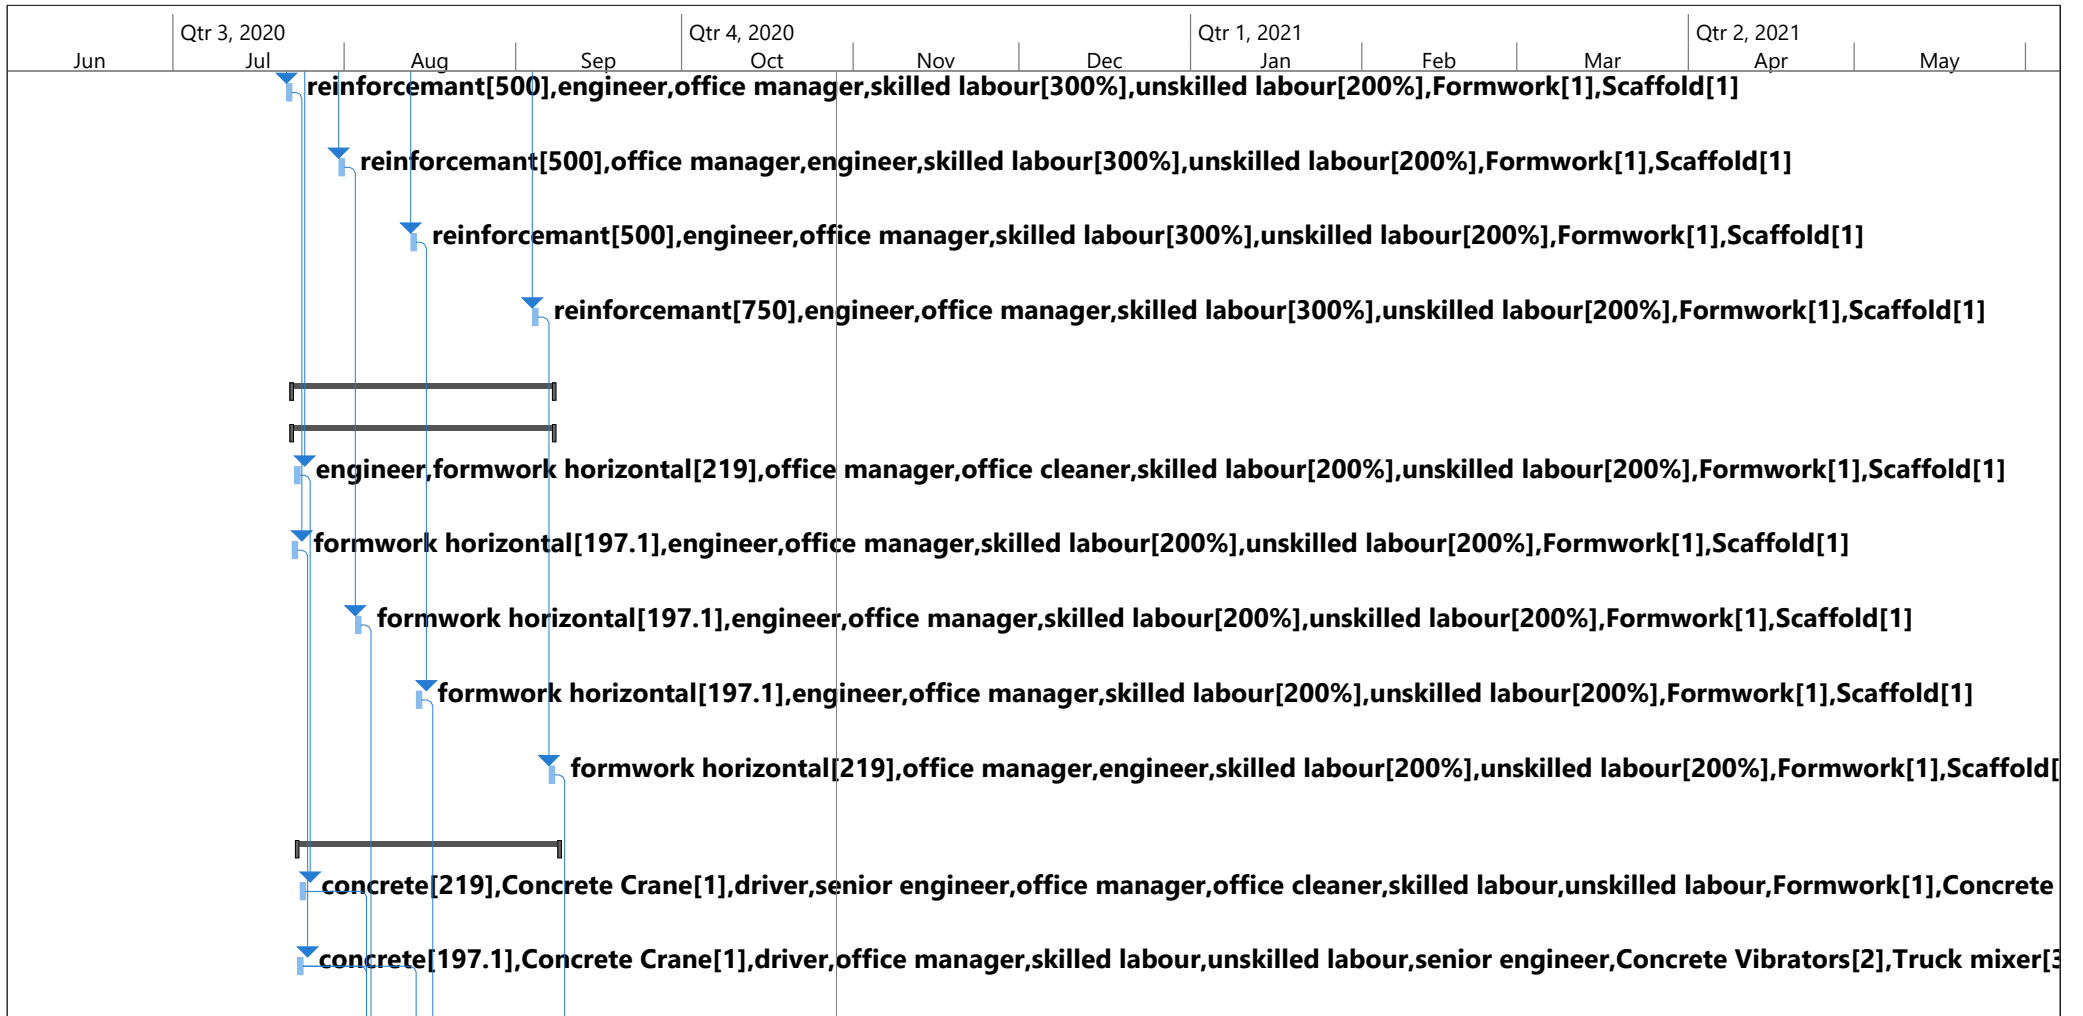

|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Project assignment 1<br>Date: Mon 04/05/20 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |

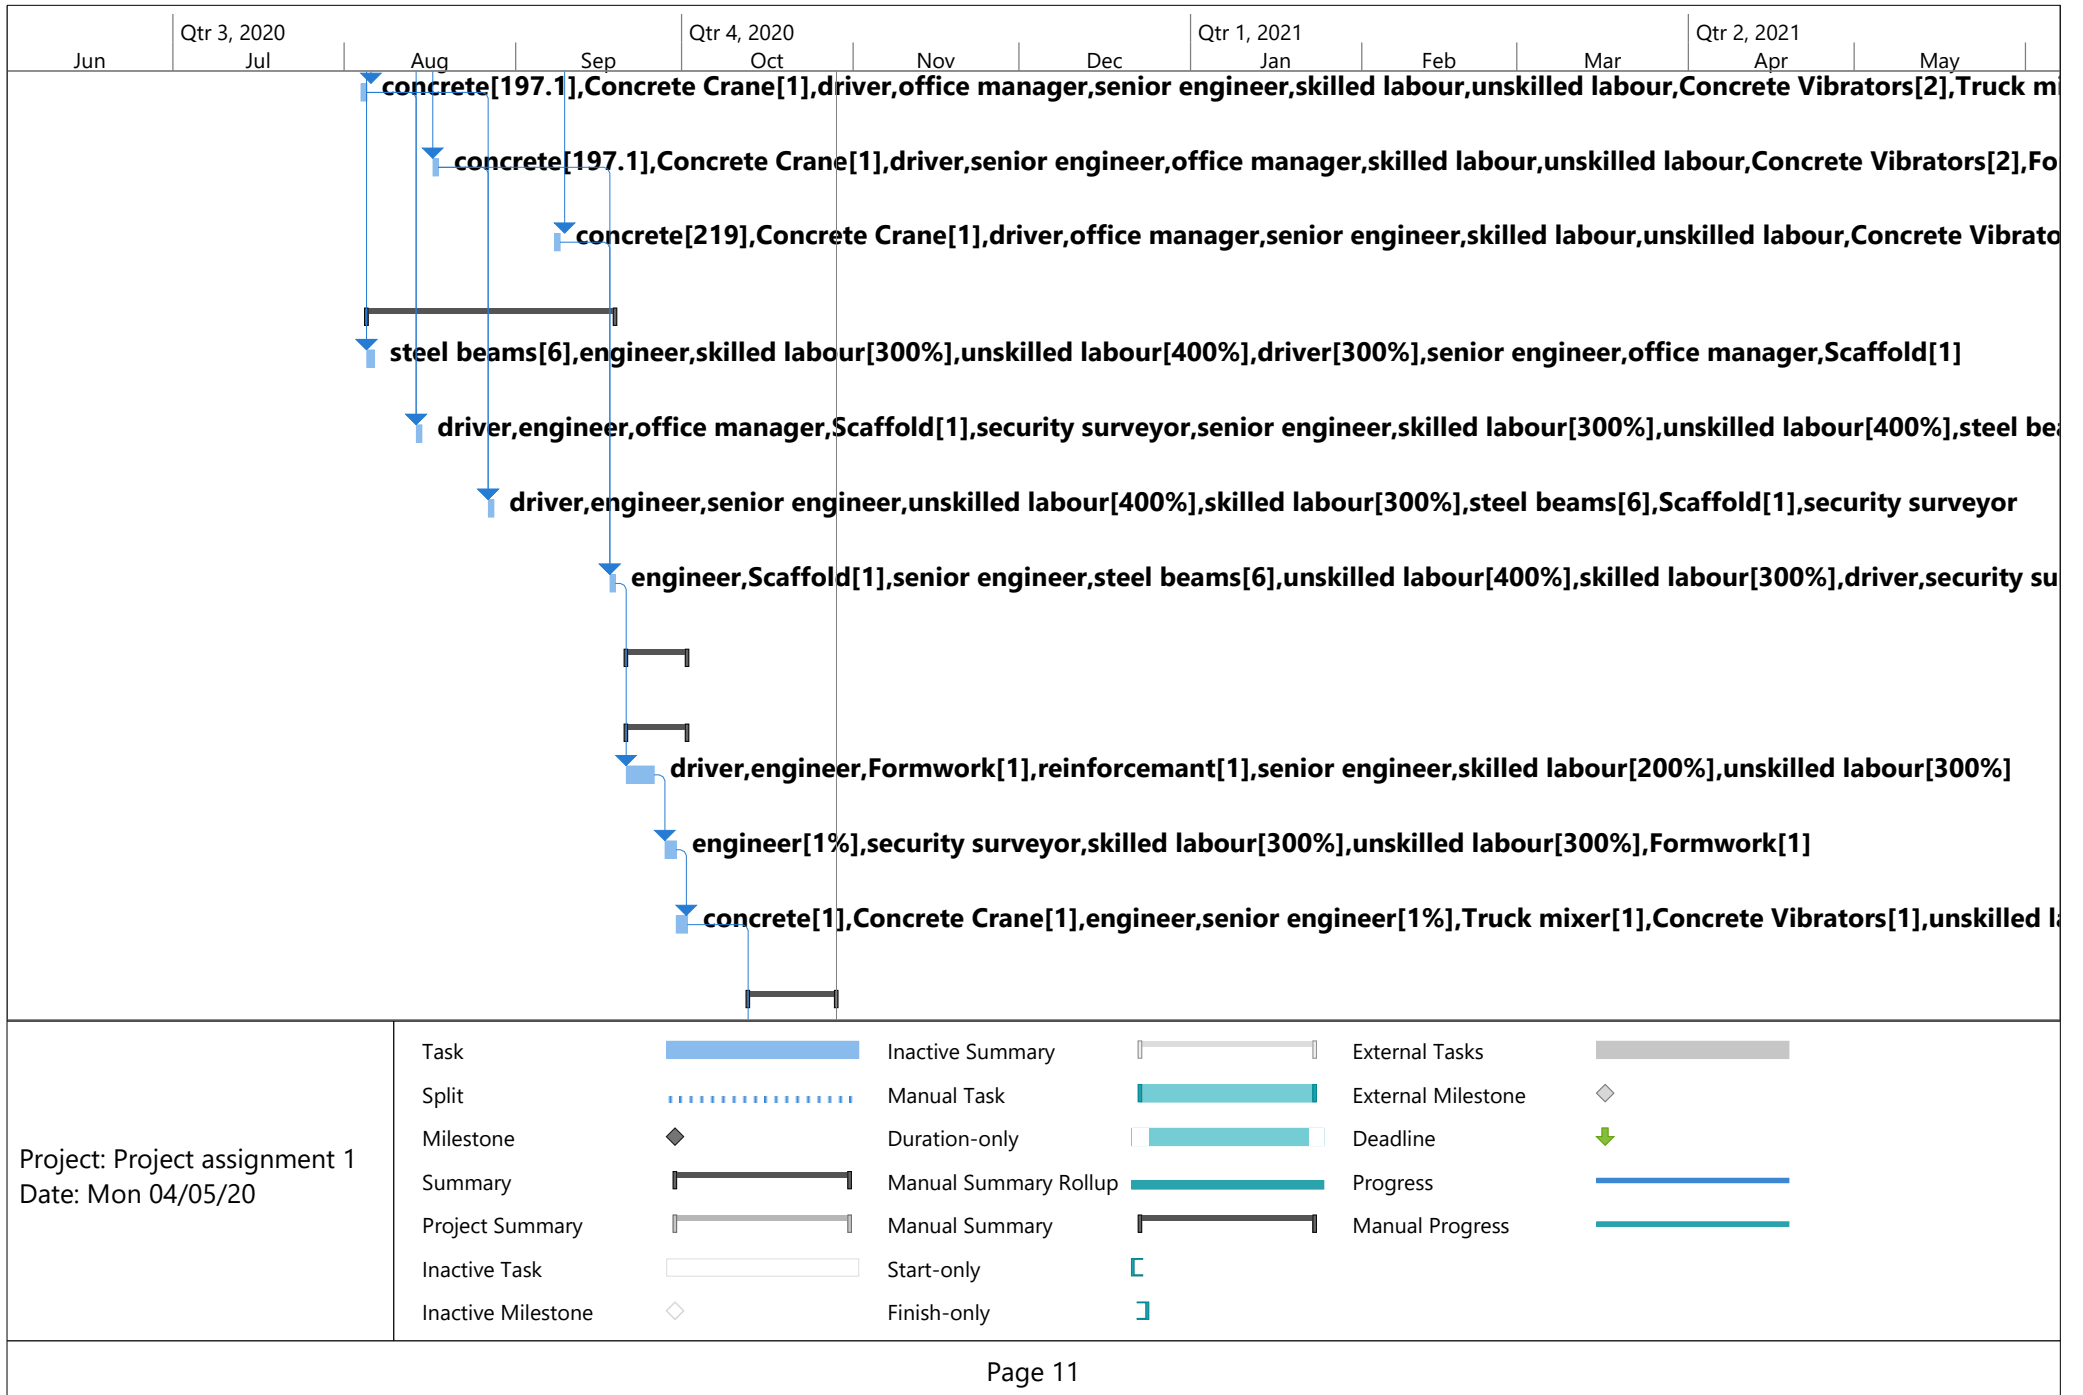

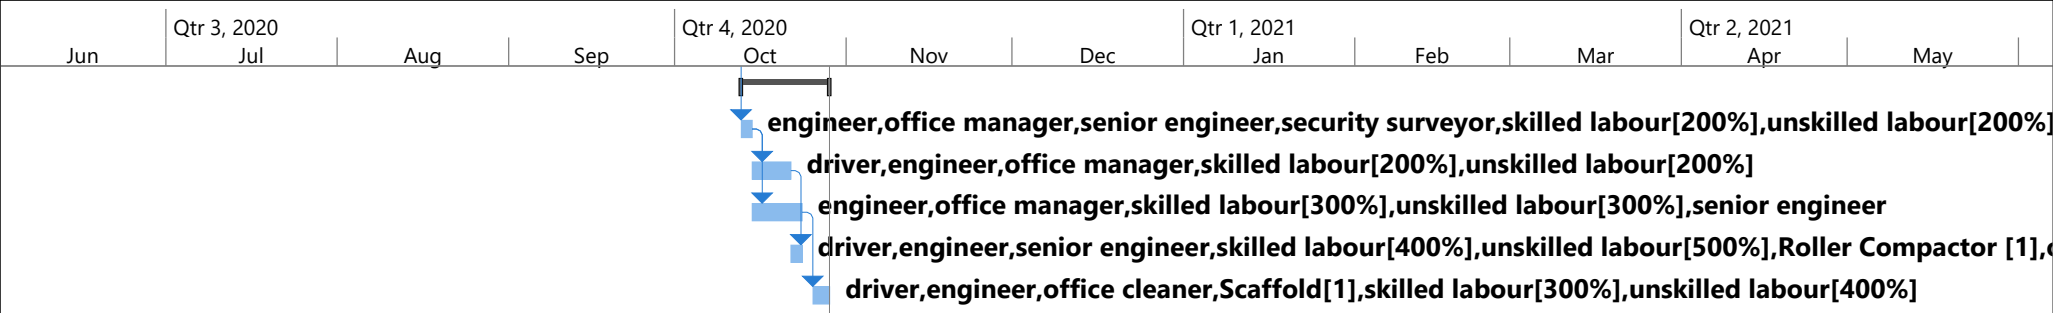

|                                                     |                    |  |                       |  |                    |  |
|-----------------------------------------------------|--------------------|--|-----------------------|--|--------------------|--|
| Project: Project assignment 1<br>Date: Mon 04/05/20 | Task               |  | Inactive Summary      |  | External Tasks     |  |
|                                                     | Split              |  | Manual Task           |  | External Milestone |  |
|                                                     | Milestone          |  | Duration-only         |  | Deadline           |  |
|                                                     | Summary            |  | Manual Summary Rollup |  | Progress           |  |
|                                                     | Project Summary    |  | Manual Summary        |  | Manual Progress    |  |
|                                                     | Inactive Task      |  | Start-only            |  |                    |  |
|                                                     | Inactive Milestone |  | Finish-only           |  |                    |  |
|                                                     |                    |  |                       |  |                    |  |

| ID |  | Resource Name            | Type        | Material Label | Initials | Group | Max. Units  |
|----|-----------------------------------------------------------------------------------|--------------------------|-------------|----------------|----------|-------|-------------|
| 1  |  | <b>unskilled labour</b>  | <b>Work</b> |                | <b>u</b> |       | <b>600%</b> |
| 2  |  | <b>skilled labour</b>    | <b>Work</b> |                | <b>s</b> |       | <b>800%</b> |
| 3  |  | <b>senior engineer</b>   | <b>Work</b> |                | <b>s</b> |       | <b>100%</b> |
| 4  |  | <b>engineer</b>          | <b>Work</b> |                | <b>e</b> |       | <b>100%</b> |
| 5  |  | <b>office manager</b>    | <b>Work</b> |                | <b>o</b> |       | <b>100%</b> |
| 6  |  | <b>security surveyor</b> | <b>Work</b> |                | <b>s</b> |       | <b>100%</b> |
| 7  |  | <b>driver</b>            | <b>Work</b> |                | <b>d</b> |       | <b>200%</b> |
| 8  |                                                                                   | office cleaner           | Work        |                | o        |       | 100%        |
| 9  |  | <b>Chainman</b>          | <b>Work</b> |                | <b>C</b> |       | <b>100%</b> |
| 10 |                                                                                   | reinforcement            | Material    |                | r        |       |             |
| 11 |                                                                                   | excavation pile          | Material    |                | e        |       |             |
| 12 |                                                                                   | concrete                 | Material    |                | c        |       |             |
| 13 |                                                                                   | formwork horizontal      | Material    |                | f        |       |             |
| 14 |                                                                                   | Concrete Crane           | Material    |                | C        |       |             |
| 15 |                                                                                   | Auger                    | Material    |                | A        |       |             |
| 16 |                                                                                   | Roller Compactor         | Material    |                | R        |       |             |
| 17 |                                                                                   | Truck mixer              | Material    |                | T        |       |             |
| 18 |                                                                                   | Formwork                 | Material    |                | F        |       |             |
| 19 |                                                                                   | Concrete Vibrators       | Material    |                | C        |       |             |
| 20 |                                                                                   | steel beams              | Material    |                | s        |       |             |
| 21 |                                                                                   | Scaffold                 | Material    |                | S        |       |             |

| Std. Rate        | Ovt. Rate       | Cost/Use     | Accrue At       | Base Calendar   | Code |
|------------------|-----------------|--------------|-----------------|-----------------|------|
| <b>£14.55/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| <b>£15.00/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| <b>£46.58/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| <b>£27.50/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| <b>£36.35/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| <b>£13.60/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| <b>£16.85/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| £9.06/hr         | £0.00/hr        | £0.00        | Prorated        | Standard        |      |
| <b>£15.46/hr</b> | <b>£0.00/hr</b> | <b>£0.00</b> | <b>Prorated</b> | <b>Standard</b> |      |
| £6.17            |                 | £0.00        | Prorated        |                 |      |
| £83.00           |                 | £0.00        | Prorated        |                 |      |
| £25.54           |                 | £0.00        | Prorated        |                 |      |
| £9.28            |                 | £0.00        | Prorated        |                 |      |
| £29.45           |                 | £0.00        | Prorated        |                 |      |
| £301.00          |                 | £0.00        | Prorated        |                 |      |
| £22.00           |                 | £0.00        | Prorated        |                 |      |
| £9.20            |                 | £0.00        | Prorated        |                 |      |
| £33.44           |                 | £0.00        | Prorated        |                 |      |
| £50.00           |                 | £0.00        | Prorated        |                 |      |
| £3,500.00        |                 | £0.00        | Prorated        |                 |      |
| £35.00           |                 | £0.00        | Prorated        |                 |      |
