


ID		Task Mode	Task Name	Duration	Start	Finish	Precedence	Calendar																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
								5	O	N	D	Half 1, 2026					Half 2, 2026					Half 1, 2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													</

Project: Construction excellence Date: Wed 25/03/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID	</
----	---

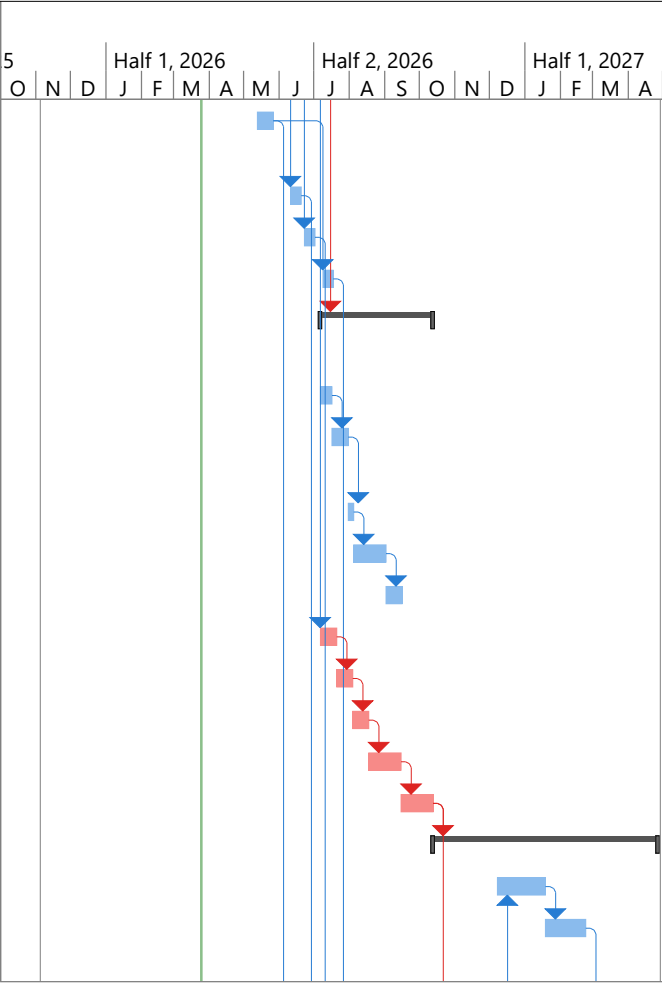

Project: Construction excellence Date: Wed 25/03/26	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Critical	
	Project Summary		Manual Summary		Critical Split	
	Inactive Task		Start-only		Progress	
	Inactive Milestone		Finish-only		Manual Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Precedence	Gantt Chart																											
								5	O	N	D	Half 1, 2026					Half 2, 2026					Half 1, 2027													
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M											
75			main connerctions first first and second fixing (testing chamber)	10 days	Tue 23/02/27	Mon 08/03/27	74																												
76			M&E containment and ducting communal areas GF	10 days	Tue 13/10/26	Mon 26/10/26	98																												
77			M&E containment and ducting communal areas FF	10 days	Tue 27/10/26	Mon 09/11/26	76																												
78			M&E containment and ducting communal areas SF	10 days	Tue 10/11/26	Mon 23/11/26	77																												
79			first fix M&E GF comunal areas	10 days	Tue 27/10/26	Mon 09/11/26	76																												
80			first fix M&E FF Zcomunal areas	10 days	Tue 10/11/26	Mon 23/11/26	77																												
81			First fix M&E SF comunal areas	10 days	Tue 24/11/26	Mon 07/12/26	78																												
82			second fix M&E GF Comunal areas	5 days	Tue 09/03/27	Mon 15/03/27	75																												
83			second fix M&E FF Comunal areas	5 days	Tue 16/03/27	Mon 22/03/27	82																												
84			second fix M&E SF Comunal areas	5 days	Tue 23/03/27	Mon 29/03/27	83																												
85			testing and commisioning	20 days	Tue 30/03/27	Mon 26/04/27	84																												
86			Roads/access/Egress/Carpark	109 days	Tue 13/10/26	Fri 12/03/27	71																												
87			Curbs	20 days	Tue 13/10/26	Mon 09/11/26																													
88			manholes and gullys	20 days	Tue 10/11/26	Mon 07/12/26	87																												
89			Sub base	10 days	Tue 08/12/26	Mon 21/12/26	88																												
90			path edgings	10 days	Tue 22/12/26	Mon 04/01/27	89																												
91			Top Coat	5 days	Mon 01/03/27	Fri 05/03/27	126																												
92			line Painting	5 days	Mon 08/03/27	Fri 12/03/27	91																												

Project: Construction excellence

Date: Wed 25/03/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Prec																												
								S	O	N	D	Half 1, 2026							Half 2, 2026							Half 1, 2027									
								J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M											
93			Internal works	241 days	Wed 27/05/26	Wed 28/04/27																													
94			insulating testing chamber walls and ceiling and boarding to finish (high performance detail)	30 days	Wed 27/05/26	Tue 07/07/26	57																												
95			screed concrete floors comunal areas GF	10 days	Mon 22/06/26	Fri 03/07/26	58																												
96			screed concrete floors comunal areas FF	10 days	Thu 02/07/26	Wed 15/07/26	59																												
97			screed concrete floors comunal areas SF	10 days	Mon 20/07/26	Fri 31/07/26	60																												
98			internal platerboarding partitions GF	15 days	Mon 06/07/26	Fri 24/07/26	95																												
99			internal platerboarding partitions FF	15 days	Thu 16/07/26	Wed 05/08/26	96																												
100			internal platerboarding partitions SF	15 days	Mon 03/08/26	Fri 21/08/26	97																												
101			faulse floor install for M&E (communal Areas)	10 days	Thu 06/08/26	Wed 19/08/26	99																												
102			faulse floor install for M&E (communal Areas)	10 days	Thu 20/08/26	Wed 02/09/26	101																												
103			2nd fix boarding (closing in Firstfix M&E) GF	10 days	Tue 10/11/26	Mon 23/11/26	79																												
104			2nd fix boarding (closing in Firstfix M&E) FF	10 days	Tue 24/11/26	Mon 07/12/26	80																												
105			2nd fix boarding (closing in Firstfix M&E) SF	10 days	Tue 08/12/26	Mon 21/12/26	81																												
106			Plastering Communals GF	15 days	Tue 24/11/26	Mon 14/12/26	103																												
107			Plastering Communals FF	15 days	Tue 15/12/26	Mon 04/01/27	106																												
108			Plastering Communals SF	15 days	Tue 05/01/27	Mon 25/01/27	107																												
109			Mist coat paint GF	5 days	Tue 15/12/26	Mon 21/12/26	106																												
110			Mist coat paint FF	5 days	Tue 05/01/27	Mon 11/01/27	107																												
111			Mist coat paint SF	5 days	Tue 26/01/27	Mon 01/02/27	108																												
112			2nd fix carpentry GF communal Areas	15 days	Tue 22/12/26	Mon 11/01/27	109																												
Project: Construction excellence Date: Wed 25/03/26			Task		Inactive Summary		External Tasks																												
			Split		Manual Task		External Milestone																												
			Milestone		Duration-only		Deadline																												
			Summary		Manual Summary Rollup		Critical																												
			Project Summary		Manual Summary		Critical Split																												
			Inactive Task		Start-only		Progress																												
			Inactive Milestone		Finish-only		Manual Progress																												
Page 6																																			

ID		Task Mode	Task Name	Duration	Start	Finish	Precedence	Gantt Chart																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
								5	O	N	D	Half 1, 2026					Half 2, 2026					Half 1, 2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																					

Project: Construction excellence

Date: Wed 25/03/26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress
