



ID		Task Mode	Task Name	Duration	Start	Finish	11 Mar '24							18 Mar '24			
	i						M	T	W	T	F	S	S	M	T	W	T
1		➡	Steel museum	322 days	Wed 13/03/24	Thu 05/06/25											
2		➡	Pre-Contract works	19 days	Wed 13/03/24	Mon 08/04/24											
3		➡	Project Proposal	1 day	Wed 13/03/24	Wed 13/03/24											
4		➡	Project approval	0 days	Wed 13/03/24	Wed 13/03/24											
5		➡	Concept design	14 days	Thu 14/03/24	Tue 02/04/24											
6		➡	Cost plan	14 days	Thu 14/03/24	Tue 02/04/24											
7		➡	Consult planning authority	3 days	Wed 03/04/24	Fri 05/04/24											
8		➡	Final Project brief	1 day	Mon 08/04/24	Mon 08/04/24											
9		➡	Contract Works	1 day	Tue 09/04/24	Tue 09/04/24											
10		➡	Signing of contracts	1 day	Tue 09/04/24	Tue 09/04/24											
11		➡	Lead in period for contractors	1 day	Tue 09/04/24	Tue 09/04/24											
12		➡	Site investigation	15 days	Wed 10/04/24	Tue 30/04/24											
13		➡	Retaining wall structural survey	15 days	Wed 10/04/24	Tue 30/04/24											
14		➡	UXO Survey	15 days	Wed 10/04/24	Tue 30/04/24											
15		➡	Radon/Methane Survey	15 days	Wed 10/04/24	Tue 30/04/24											
16		➡	Borehole Survey	15 days	Wed 10/04/24	Tue 30/04/24											
17		➡	Contaminated land Survey	15 days	Wed 10/04/24	Tue 30/04/24											
18		➡	Materials	5 days	Tue 09/04/24	Mon 15/04/24											
19		➡	Purchasing of materials	5 days	Tue 09/04/24	Mon 15/04/24											
20		➡	Site setup	30 days	Tue 16/04/24	Mon 27/05/24											
21		➡	Construct temporary riverside retaining wall	2 days	Tue 16/04/24	Wed 17/04/24											
22		➡	Demolition works phase 1	28 days	Thu 18/04/24	Mon 27/05/24											

Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

[illegible]


ID		Task Mode	Task Name	Duration	Start	Finish	11 Mar '24							18 Mar '24			
							M	T	W	T	F	S	S	M	T	W	T
67			Install brickwork and blockwork	3 days	Tue 15/04/25	Thu 17/04/25											
68			Insert wood fibre Insulation	6 days	Fri 18/04/25	Fri 25/04/25											
69			Level 1 metal decking	3 days	Mon 28/04/25	Wed 30/04/25											
70			Level 1 floor reinforcement and concrete pour	3 days	Thu 01/05/25	Mon 05/05/25											
71			Construct staircase to level 1	3 days	Tue 06/05/25	Thu 08/05/25											
72			Construct lift pit	3 days	Tue 06/05/25	Thu 08/05/25											
73			Level 1	319 days	Mon 18/03/24	Thu 05/06/25											
74			Erect scaffolding	2 days	Fri 09/05/25	Mon 12/05/25											
75			Position mewps into place ready for steel erection	2 days	Tue 13/05/25	Wed 14/05/25											
76			Insert prefabricated materials (steel frame, columns, truss)	4 days	Thu 15/05/25	Tue 20/05/25											
77			Install brickwork and blockwork	3 days	Wed 21/05/25	Fri 23/05/25											
78			Insert wood fibre Insulation	6 days	Mon 26/05/25	Mon 02/06/25											
79			Level 2 metal decking	3 days	Tue 03/06/25	Thu 05/06/25											
80			Level 2 floor reinforcement and concrete pour	3 days	Mon 18/03/24	Wed 20/03/24											
81			Construct staircase to level 2	3 days	Thu 21/03/24	Mon 25/03/24											
82			Construct lift pit	3 days	Thu 21/03/24	Mon 25/03/24											
83			Level 2	26 days	Wed 13/03/24	Wed 17/04/24											
84			Erect scaffolding	2 days	Tue 26/03/24	Wed 27/03/24											
85			Position mewps into place ready for steel erection	2 days	Thu 28/03/24	Fri 29/03/24											
86			Insert prefabricated materials (steel frame, columns, truss)	4 days	Mon 01/04/24	Thu 04/04/24											
87			Install brickwork and blockwork	3 days	Fri 05/04/24	Tue 09/04/24											
88			Install wood fibre Insulation	6 days	Wed 10/04/24	Wed 17/04/24											

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	11 Mar '24							18 Mar '24			
							M	T	W	T	F	S	S	M	T	W	T
89			Level 3 metal decking	3 days	Wed 13/03/24	Fri 15/03/24											
90			Level 3 floor reinforcement and concrete pour	3 days	Mon 18/03/24	Wed 20/03/24											
91			Construct staircase to level 3	3 days	Thu 21/03/24	Mon 25/03/24											
92			Construct lift pit	3 days	Thu 21/03/24	Mon 25/03/24											
93			Level 3	20 days	Tue 26/03/24	Mon 22/04/24											
94			Erect scaffolding	2 days	Tue 26/03/24	Wed 27/03/24											
95			Position mewps into place ready for steel erection	2 days	Thu 28/03/24	Fri 29/03/24											
96			Insert prefabricated materials (steel frame, columns, truss)	4 days	Mon 01/04/24	Thu 04/04/24											
97			Install brickwork and blockwork	3 days	Fri 05/04/24	Tue 09/04/24											
98			Install wood fibre Insulation	6 days	Wed 10/04/24	Wed 17/04/24											
99			construct lift pit	3 days	Thu 18/04/24	Mon 22/04/24											
100			Floor and Roof Installation	13 days	Tue 23/04/24	Thu 09/05/24											
101			Install steel floor joists and decking for each level	5 days	Tue 23/04/24	Mon 29/04/24											
102			Erect steel roof trusses	5 days	Tue 30/04/24	Mon 06/05/24											
103			Installation of insulation and waterproofing	3 days	Tue 07/05/24	Thu 09/05/24											
104			Finishes	8 days	Fri 10/05/24	Tue 21/05/24											
105			Install flooring and ceiling finishes	1 day	Fri 10/05/24	Fri 10/05/24											
106			Installation of windows and external doors	1 day	Fri 10/05/24	Fri 10/05/24											
107			Construction of internal walls and partitions	1 day	Fri 10/05/24	Fri 10/05/24											
108			Installation of internal doors	8 days	Fri 10/05/24	Tue 21/05/24											
109			wall finishes	8 days	Fri 10/05/24	Tue 21/05/24											
110			Services	1 day	Wed 22/05/24	Wed 22/05/24											

ID		Task Mode	Task Name	Duration	Start	Finish	11 Mar '24 M T W T F S S							18 Mar '24 M T W T			
111			Sanitary installations	1 day	Wed 22/05/24	Wed 22/05/24											
112			services equipment	1 day	Wed 22/05/24	Wed 22/05/24											
113			Disposal installation	1 day	Wed 22/05/24	Wed 22/05/24											
114			Water installations	1 day	Wed 22/05/24	Wed 22/05/24											
115			Heat sources	1 day	Wed 22/05/24	Wed 22/05/24											
116			Space heating and air conditioning	1 day	Wed 22/05/24	Wed 22/05/24											
117			Ventilation	1 day	Wed 22/05/24	Wed 22/05/24											
118			Electrical installations	1 day	Wed 22/05/24	Wed 22/05/24											
119			Fuel installations	1 day	Wed 22/05/24	Wed 22/05/24											
120			Lift and conveyor installations	1 day	Wed 22/05/24	Wed 22/05/24											
121			fire and lighting protections	1 day	Wed 22/05/24	Wed 22/05/24											
122			communication, security and control systems	1 day	Wed 22/05/24	Wed 22/05/24											
123			special installations - Bessemer	1 day	Wed 22/05/24	Wed 22/05/24											
124			External works	51 days	Thu 23/05/24	Thu 01/08/24											
125			Insert Bessemer	7 days	Thu 23/05/24	Fri 31/05/24											
126			Construct glass atrium	6 days	Mon 03/06/24	Mon 10/06/24											
127			Landscaping phae 1	15 days	Tue 11/06/24	Mon 01/07/24											
128			10% time contingency	23 days	Tue 02/07/24	Thu 01/08/24											
129			Fittings furnishings and equipment	97 days	Fri 02/08/24	Mon 16/12/24											
130			Level 0	10 days	Fri 02/08/24	Thu 15/08/24											
131			Main circulation area	10 days	Fri 02/08/24	Thu 15/08/24											
132			café/ restaurant	10 days	Fri 02/08/24	Thu 15/08/24											

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	11 Mar '24							18 Mar '24			
							M	T	W	T	F	S	S	M	T	W	T
177			Level 2 handover	1 day	Mon 16/12/24	Mon 16/12/24											
178			Project closure	0 days	Mon 16/12/24	Mon 16/12/24											
179			Closing meeting	0 days	Mon 16/12/24	Mon 16/12/24											

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline


Progress

Manual Progress














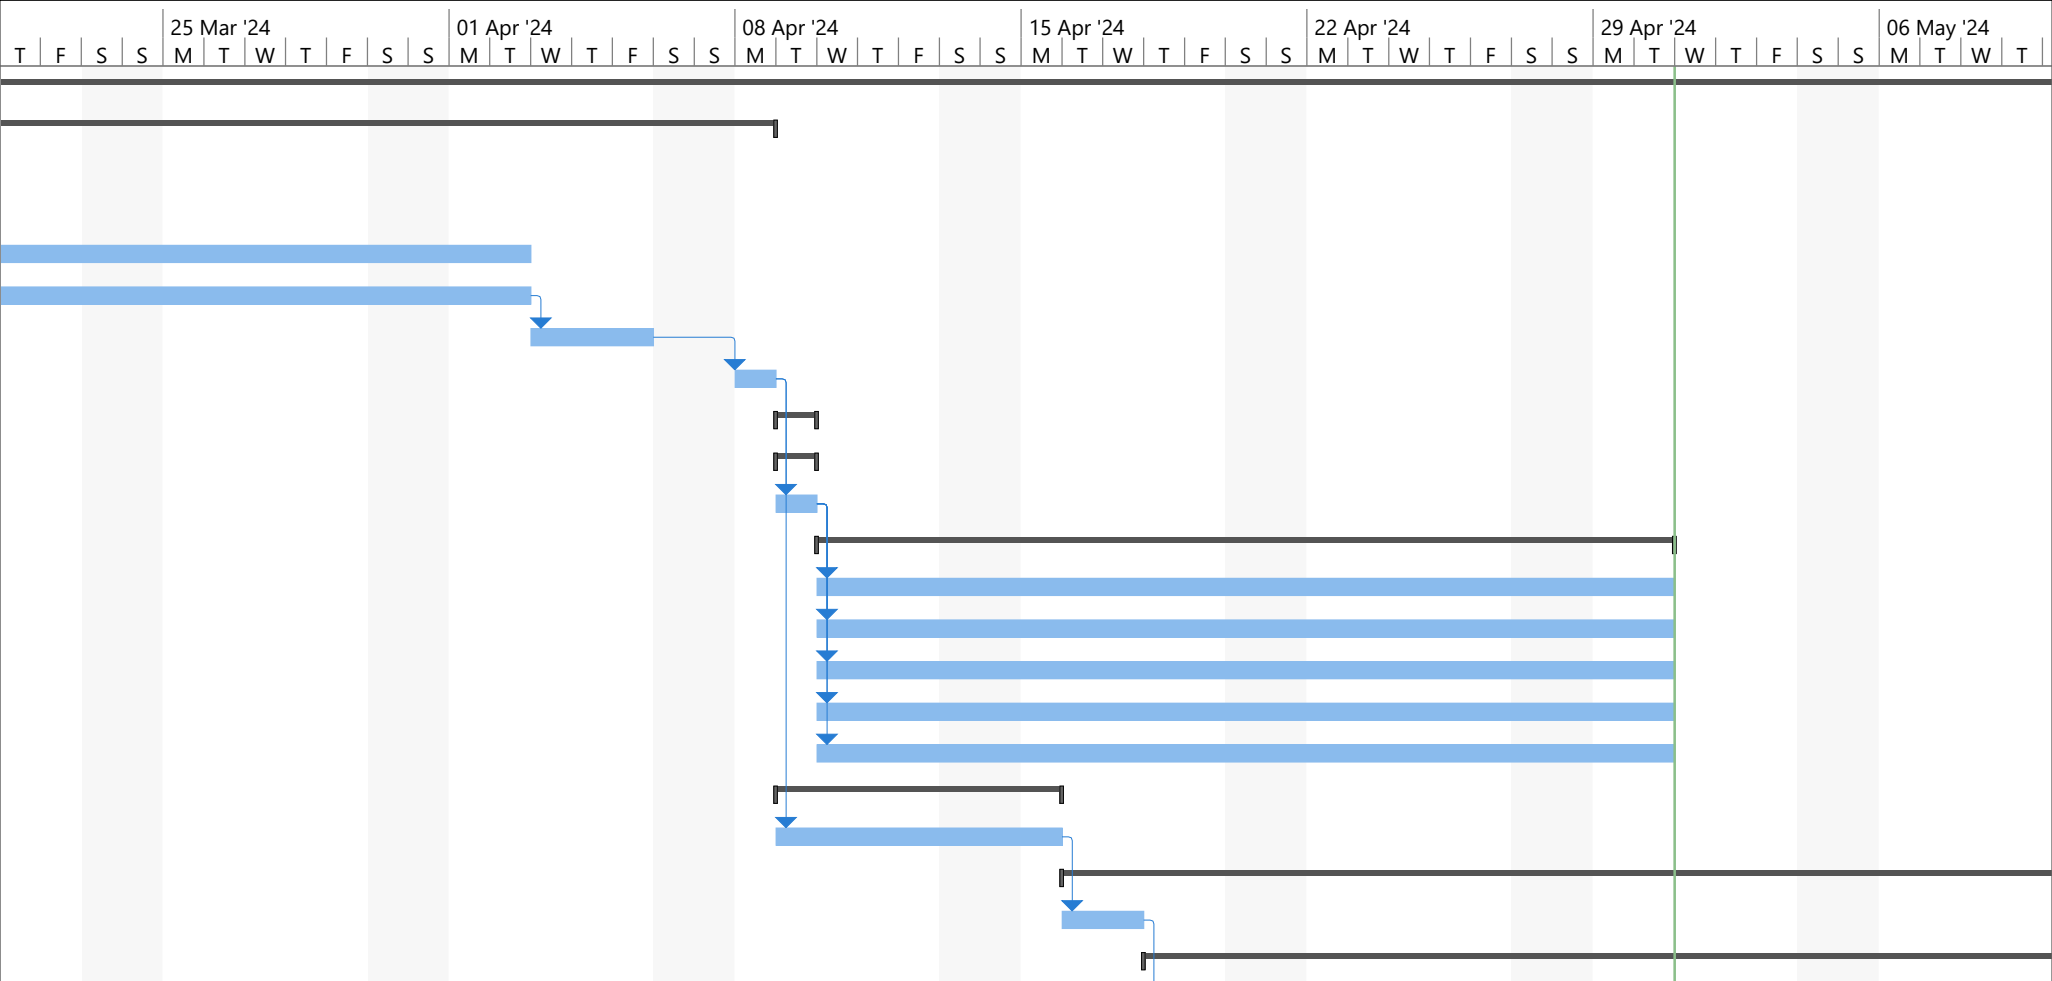


Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

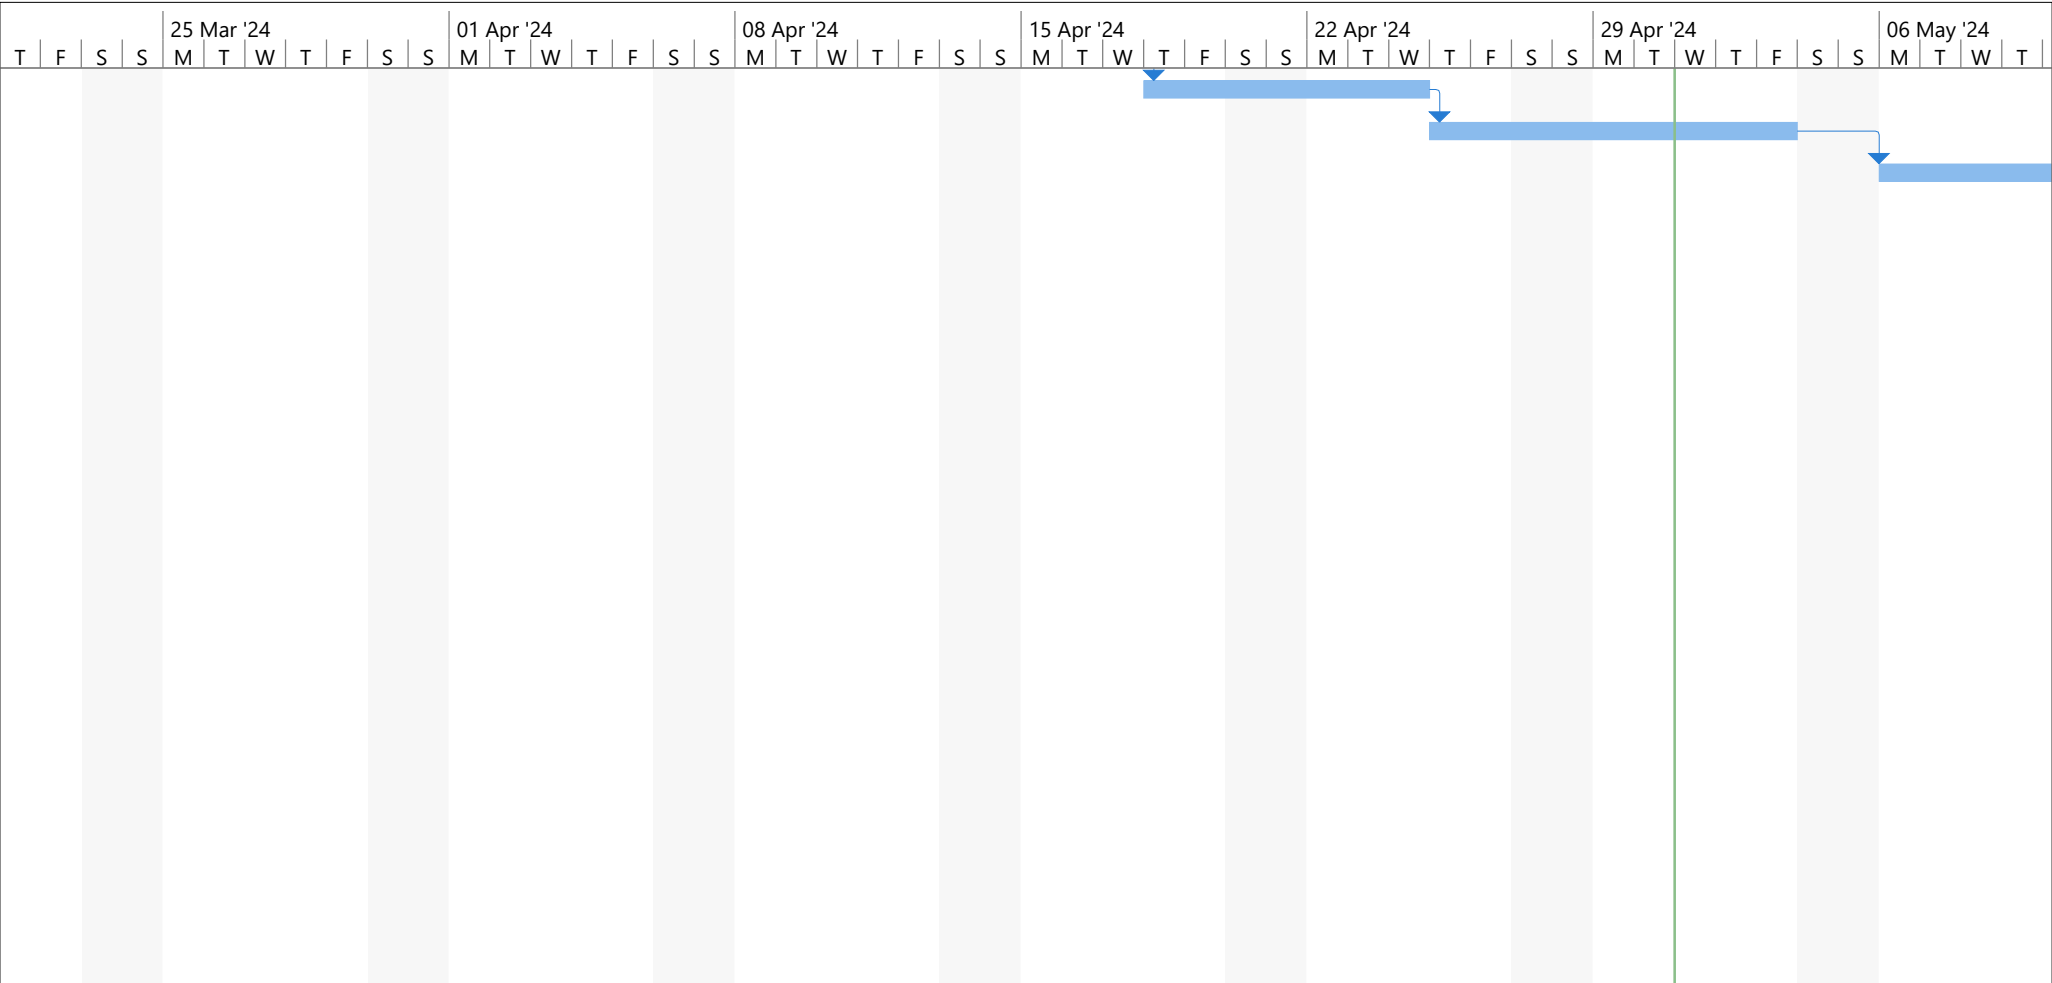



Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

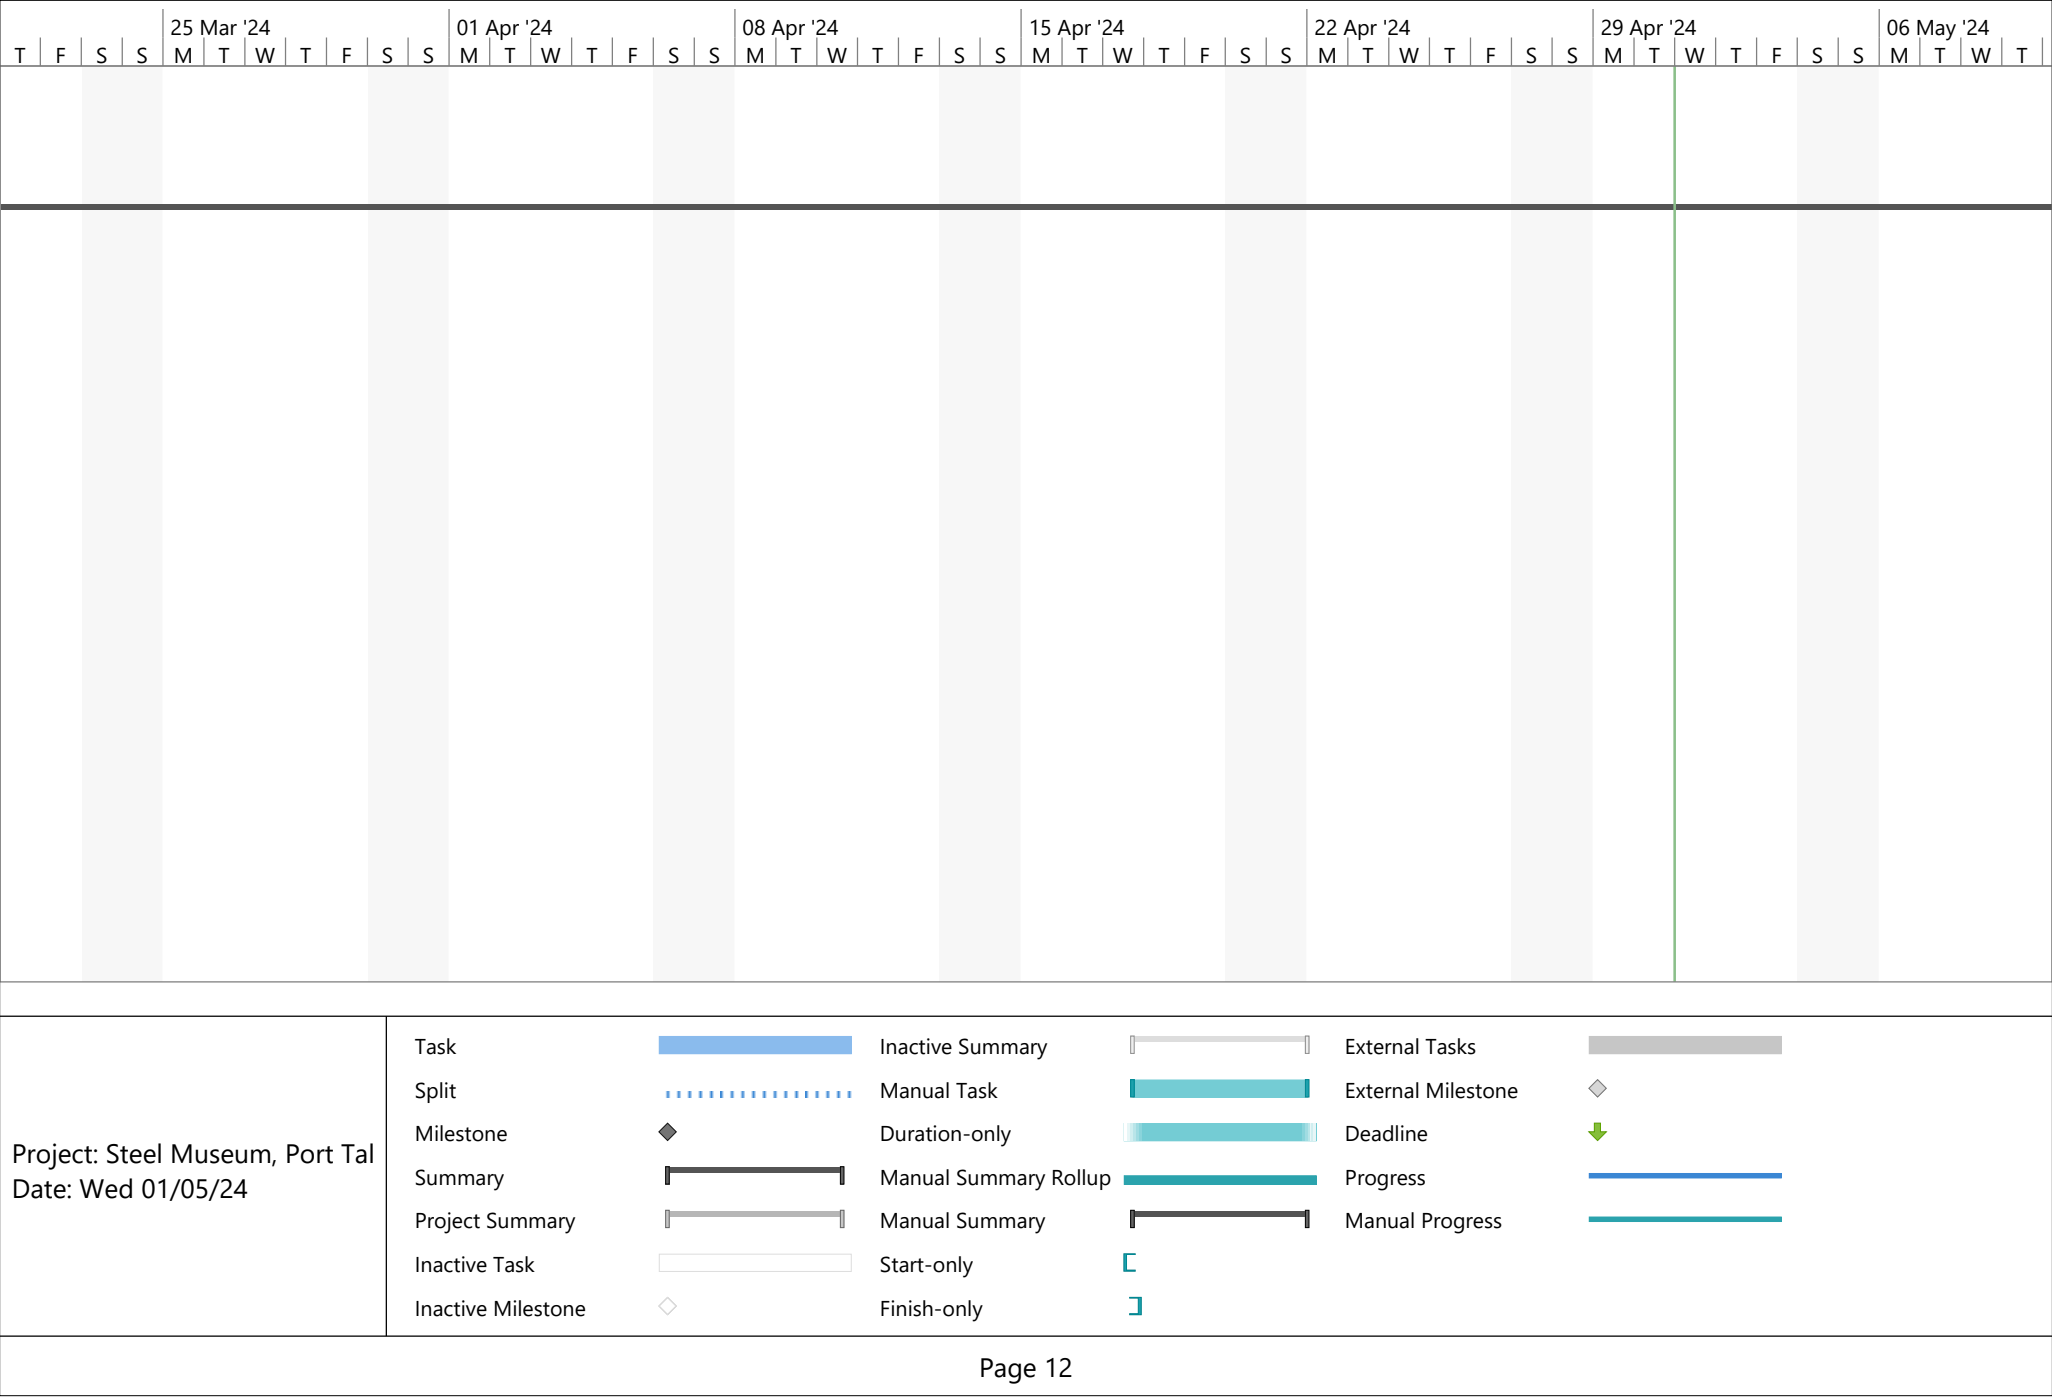


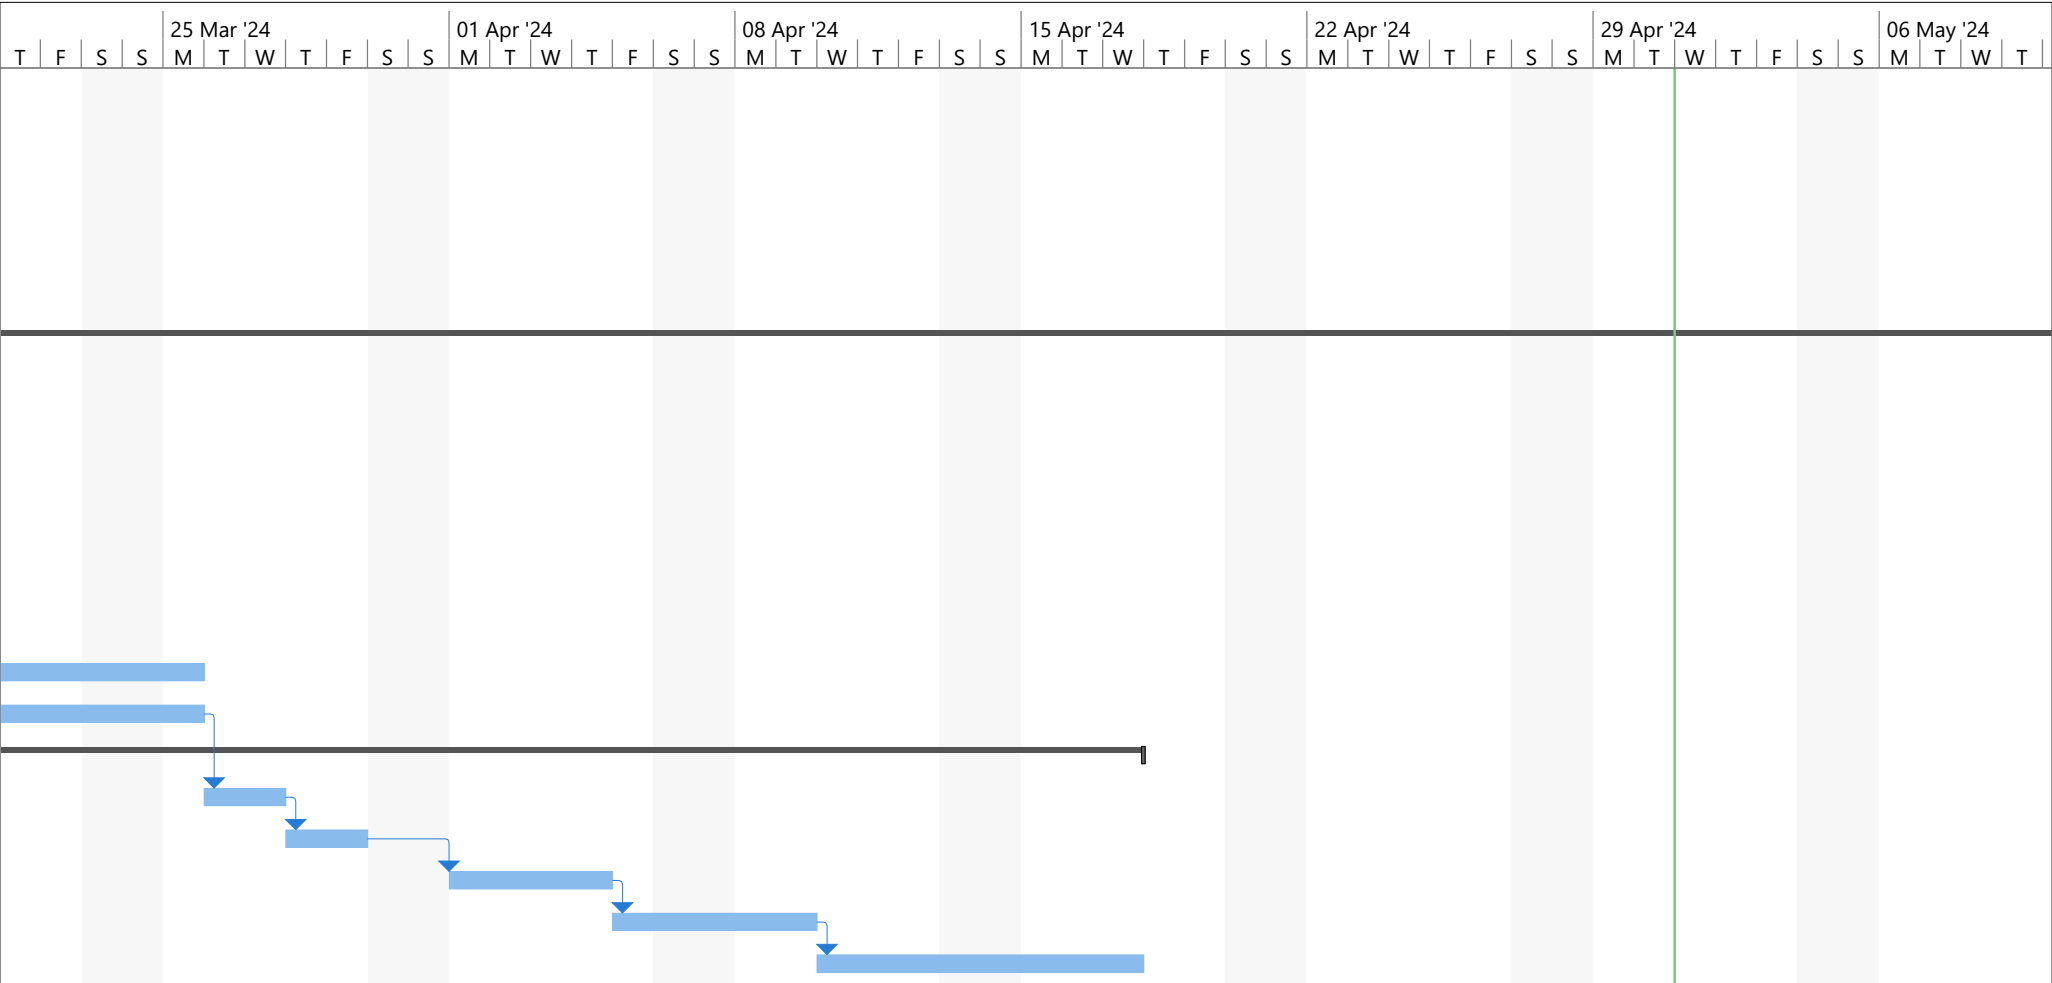

Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

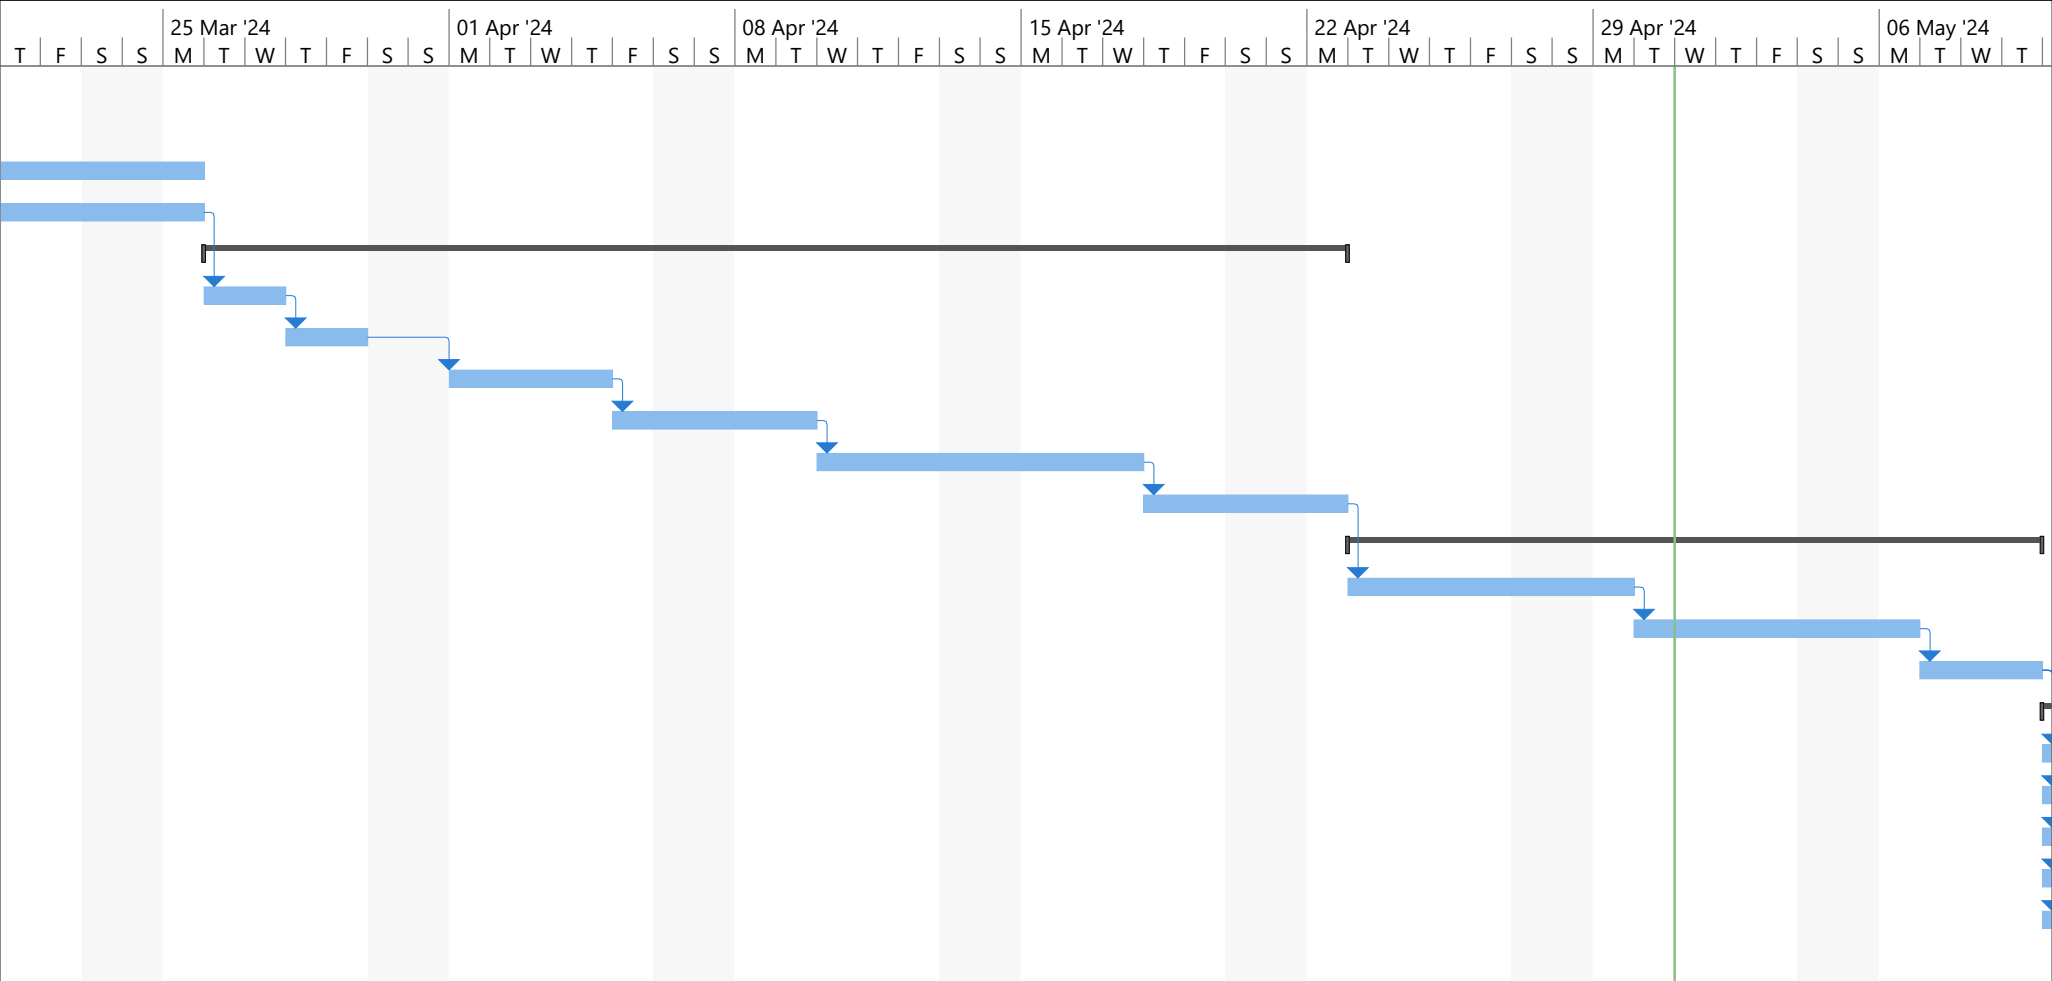


Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

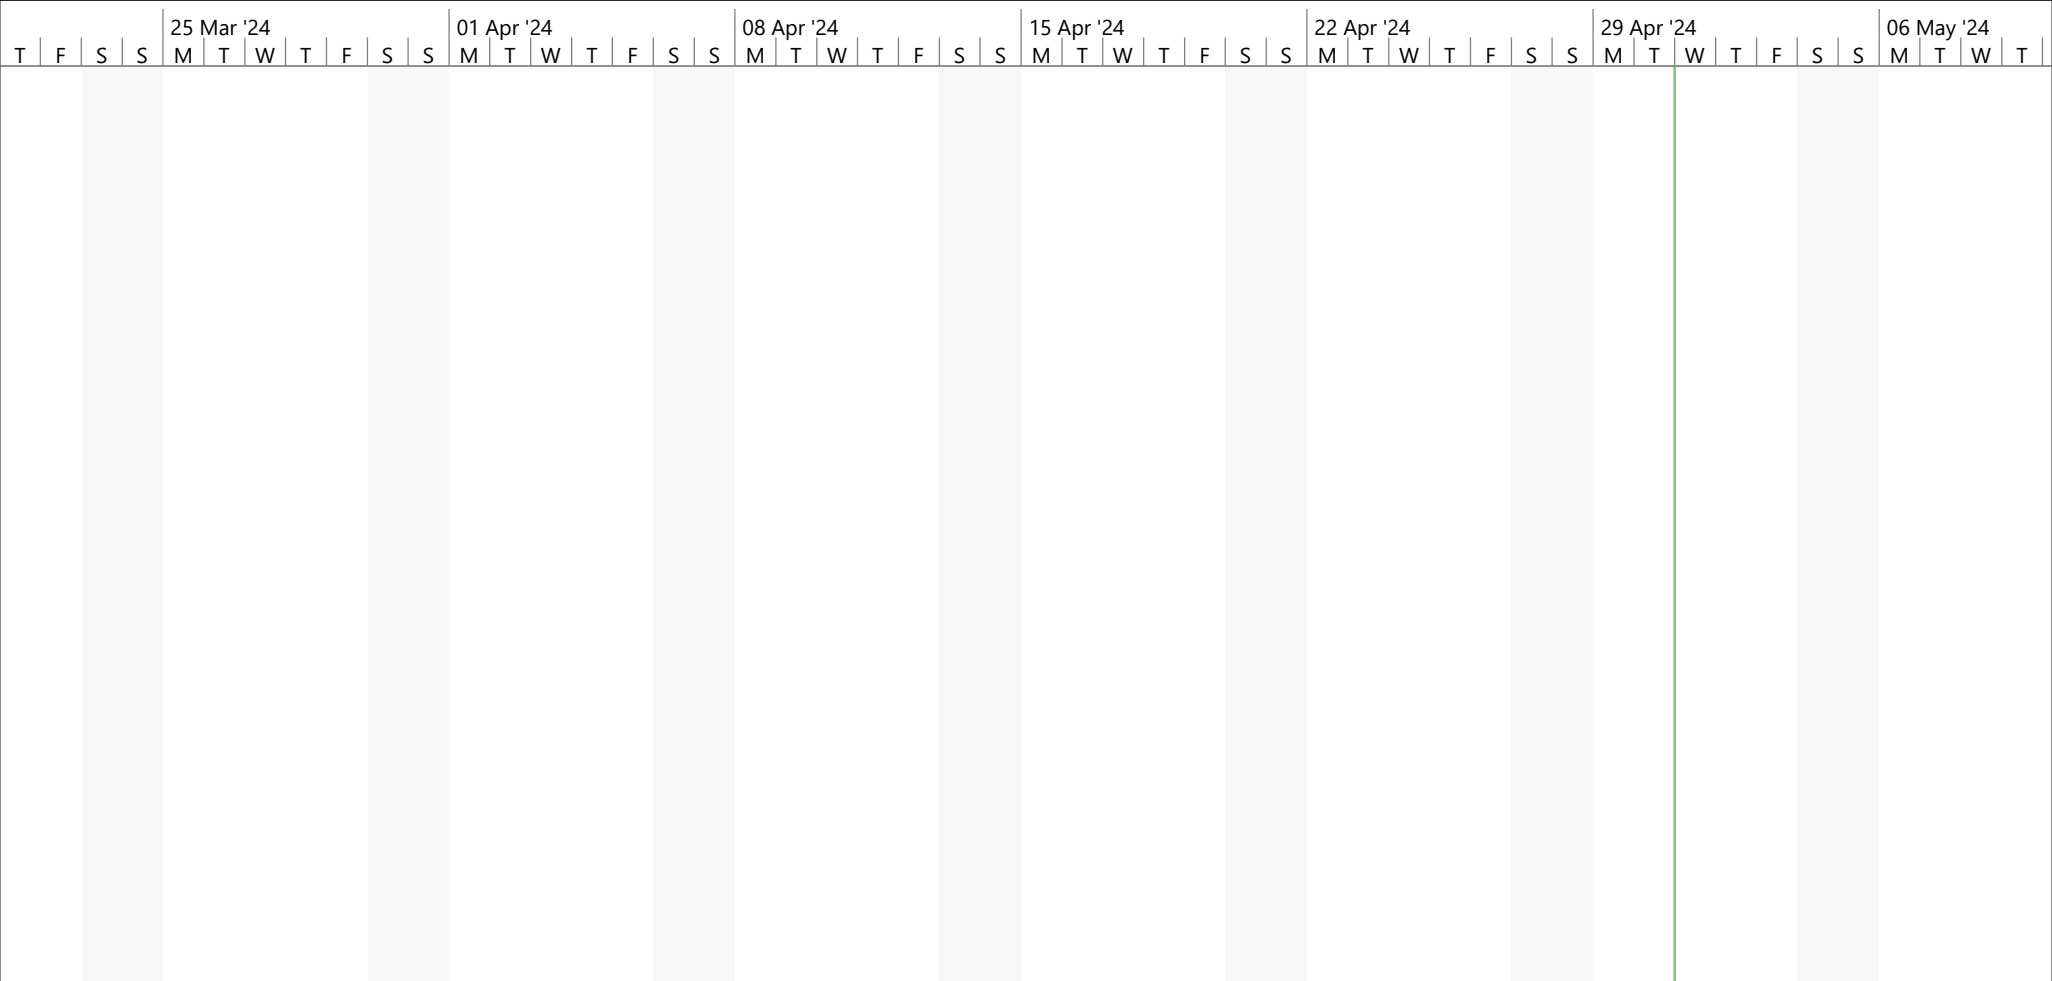


Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

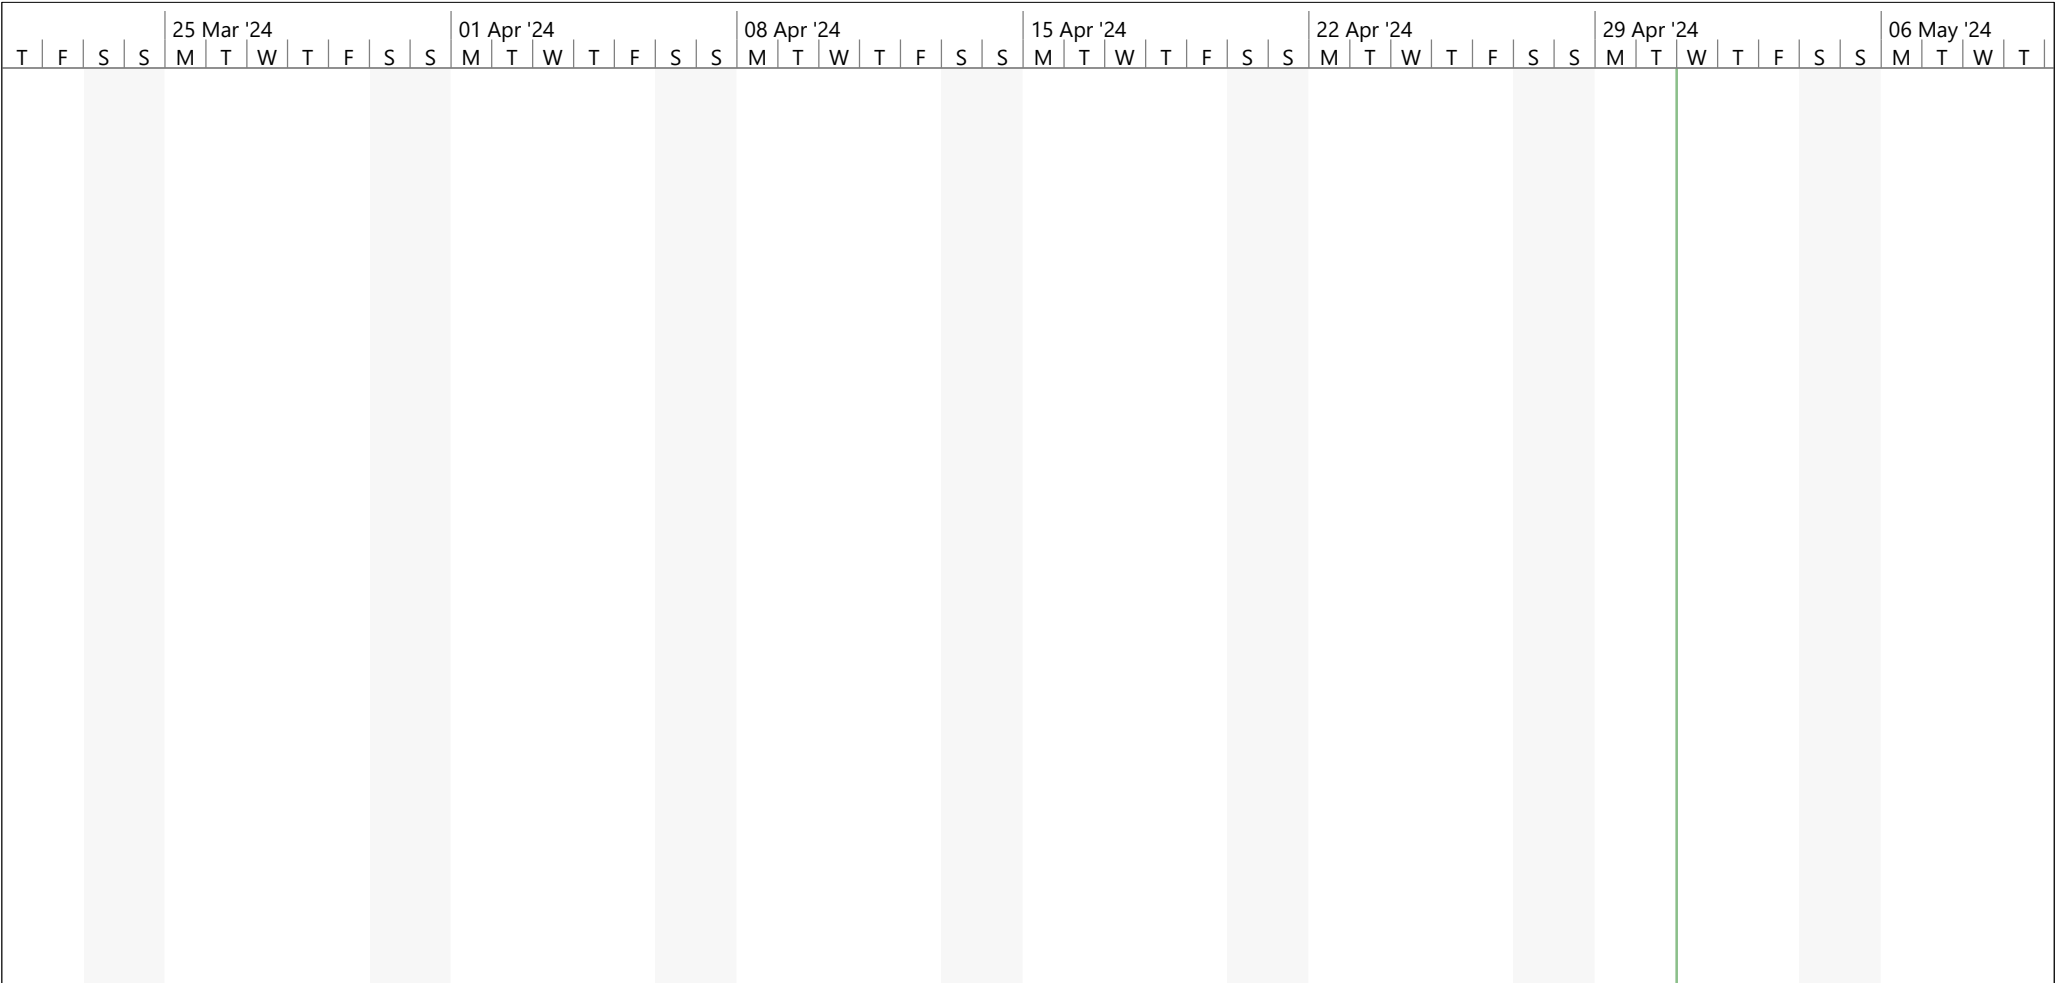



Project: Steel Museum, Port Tal
Date: Wed 01/05/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

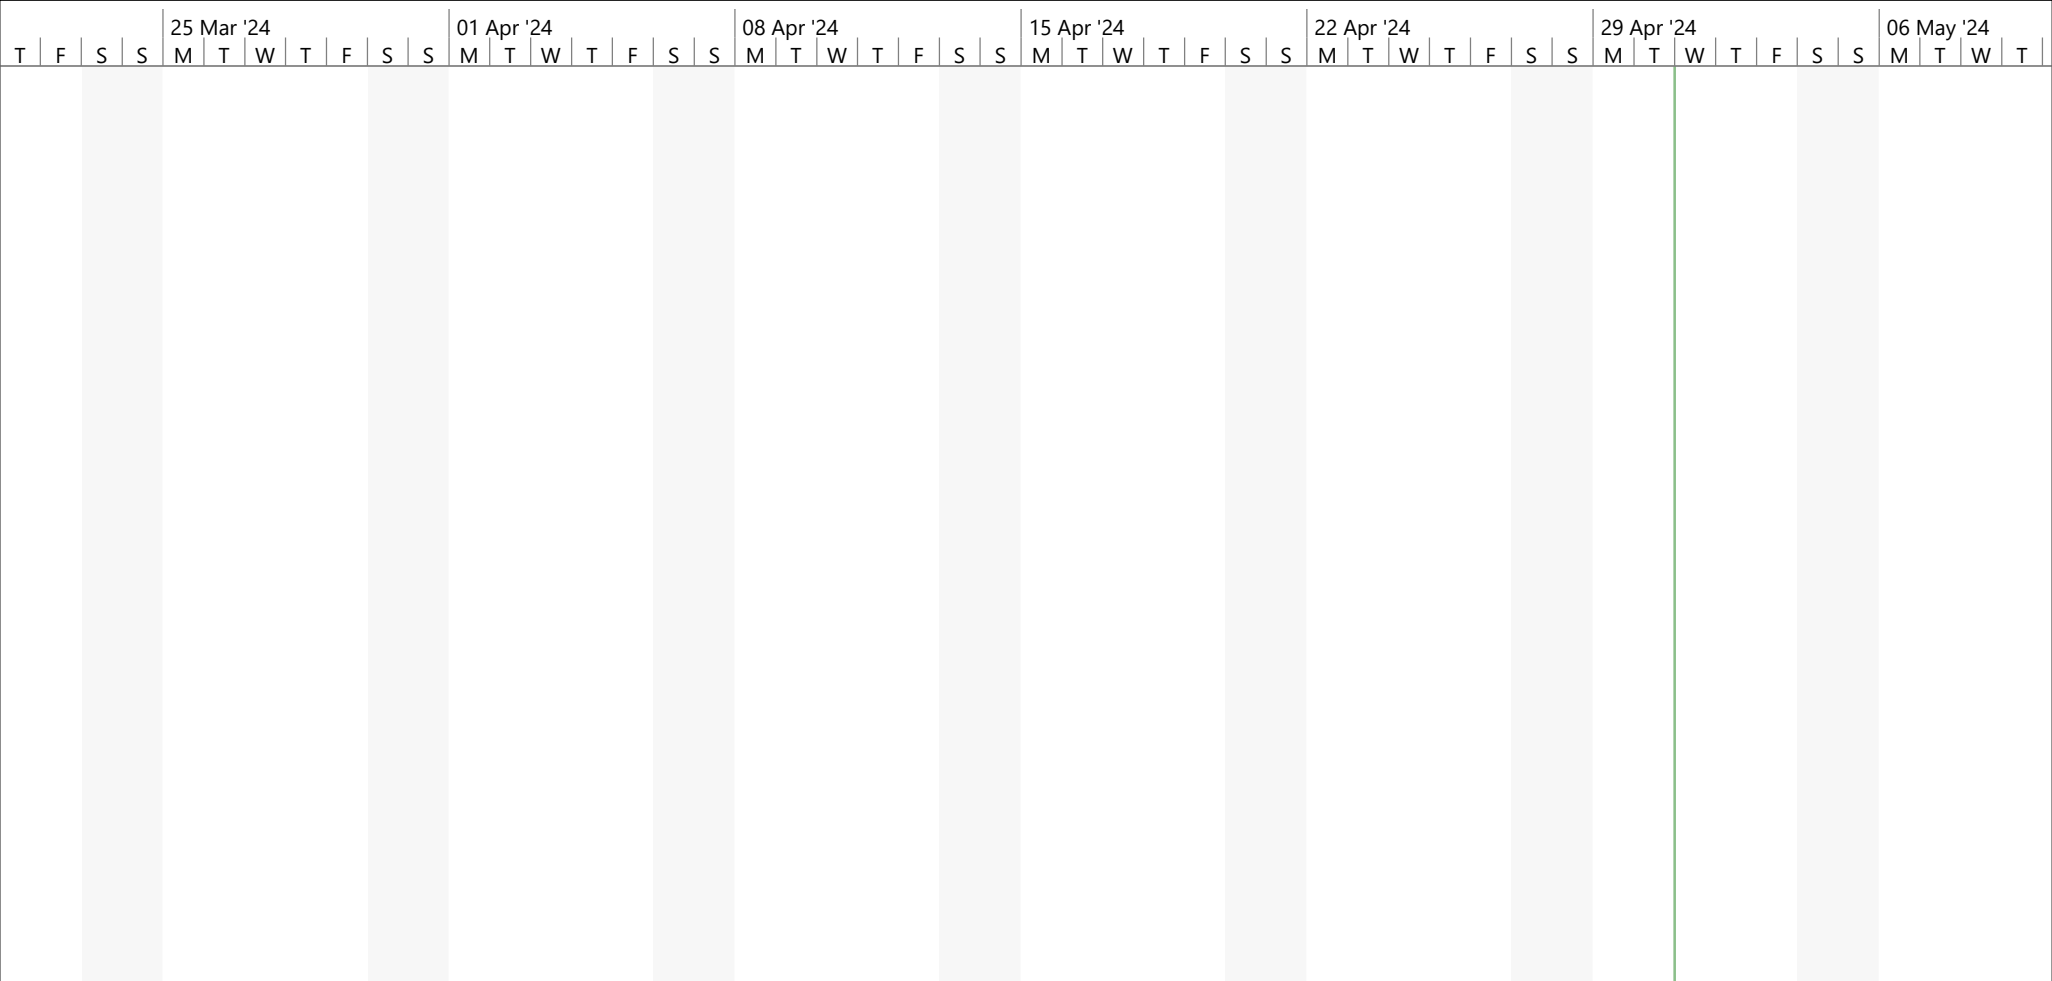


Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

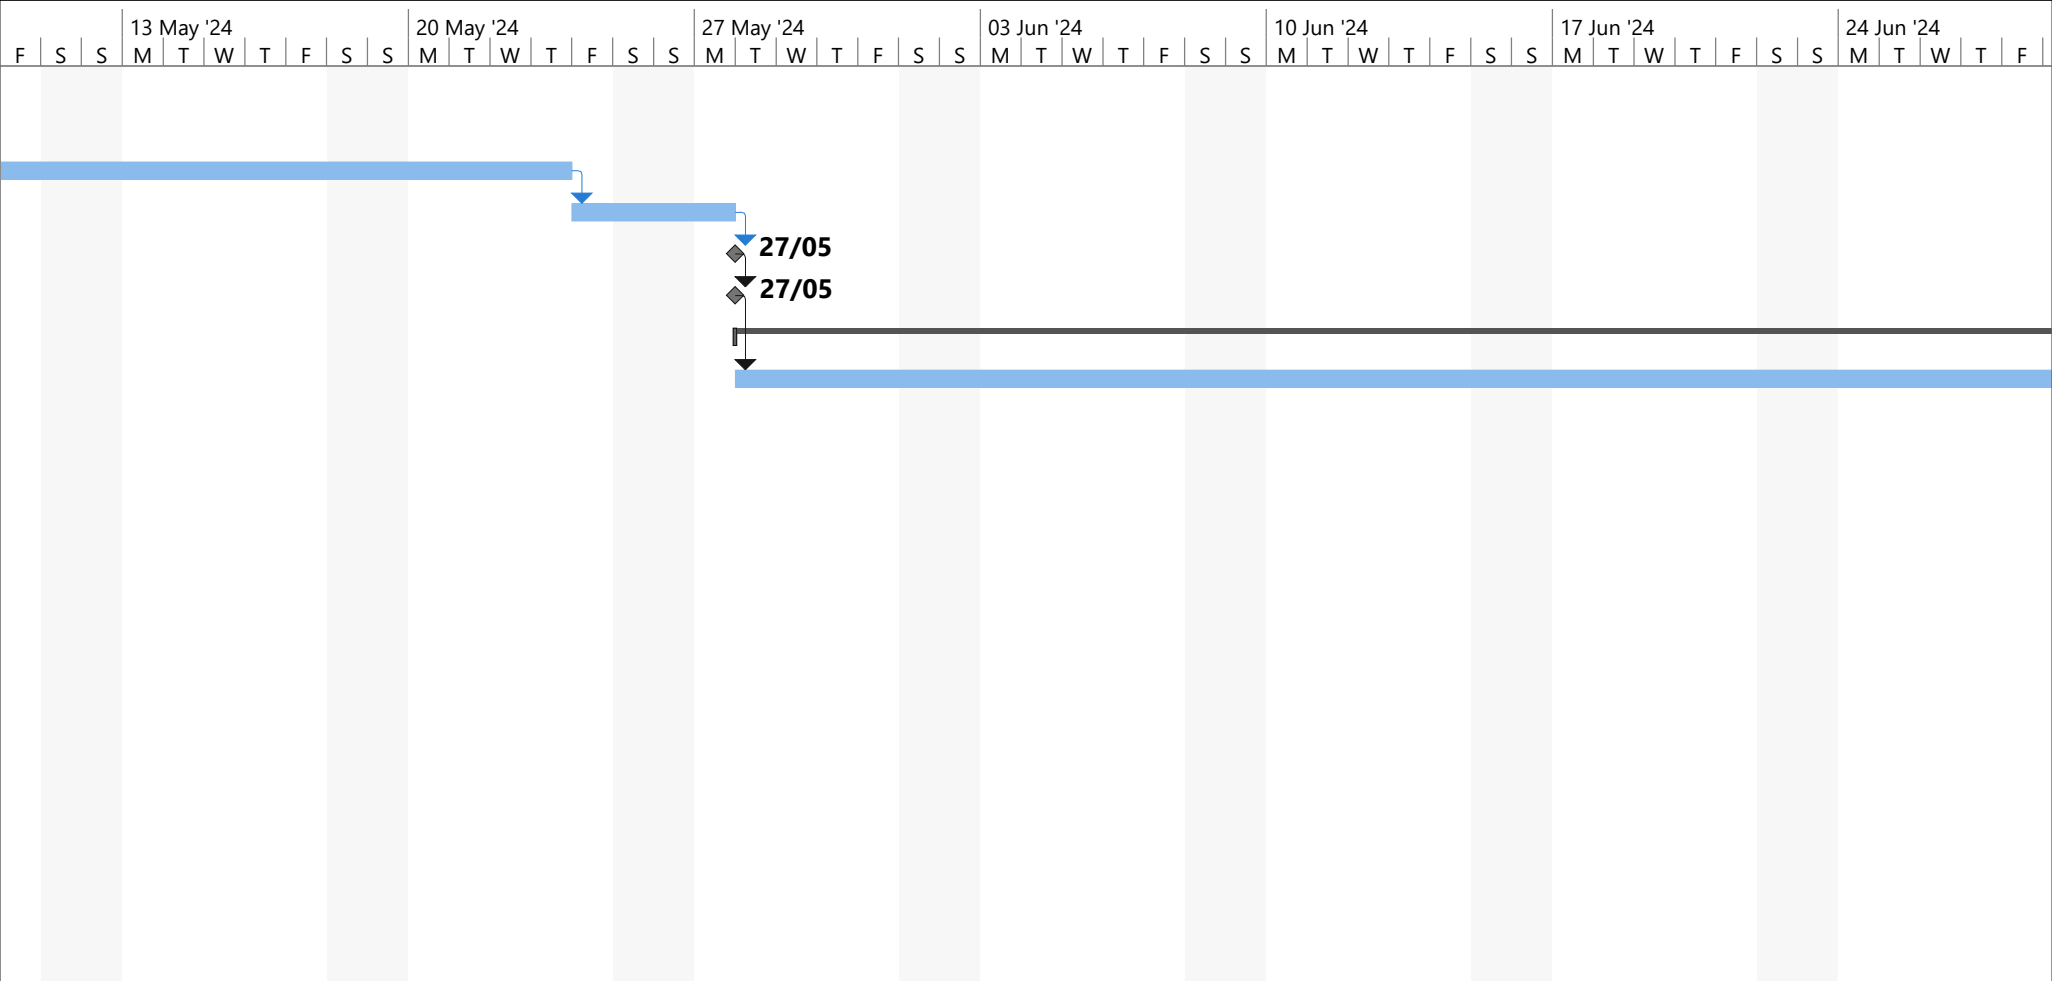


Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

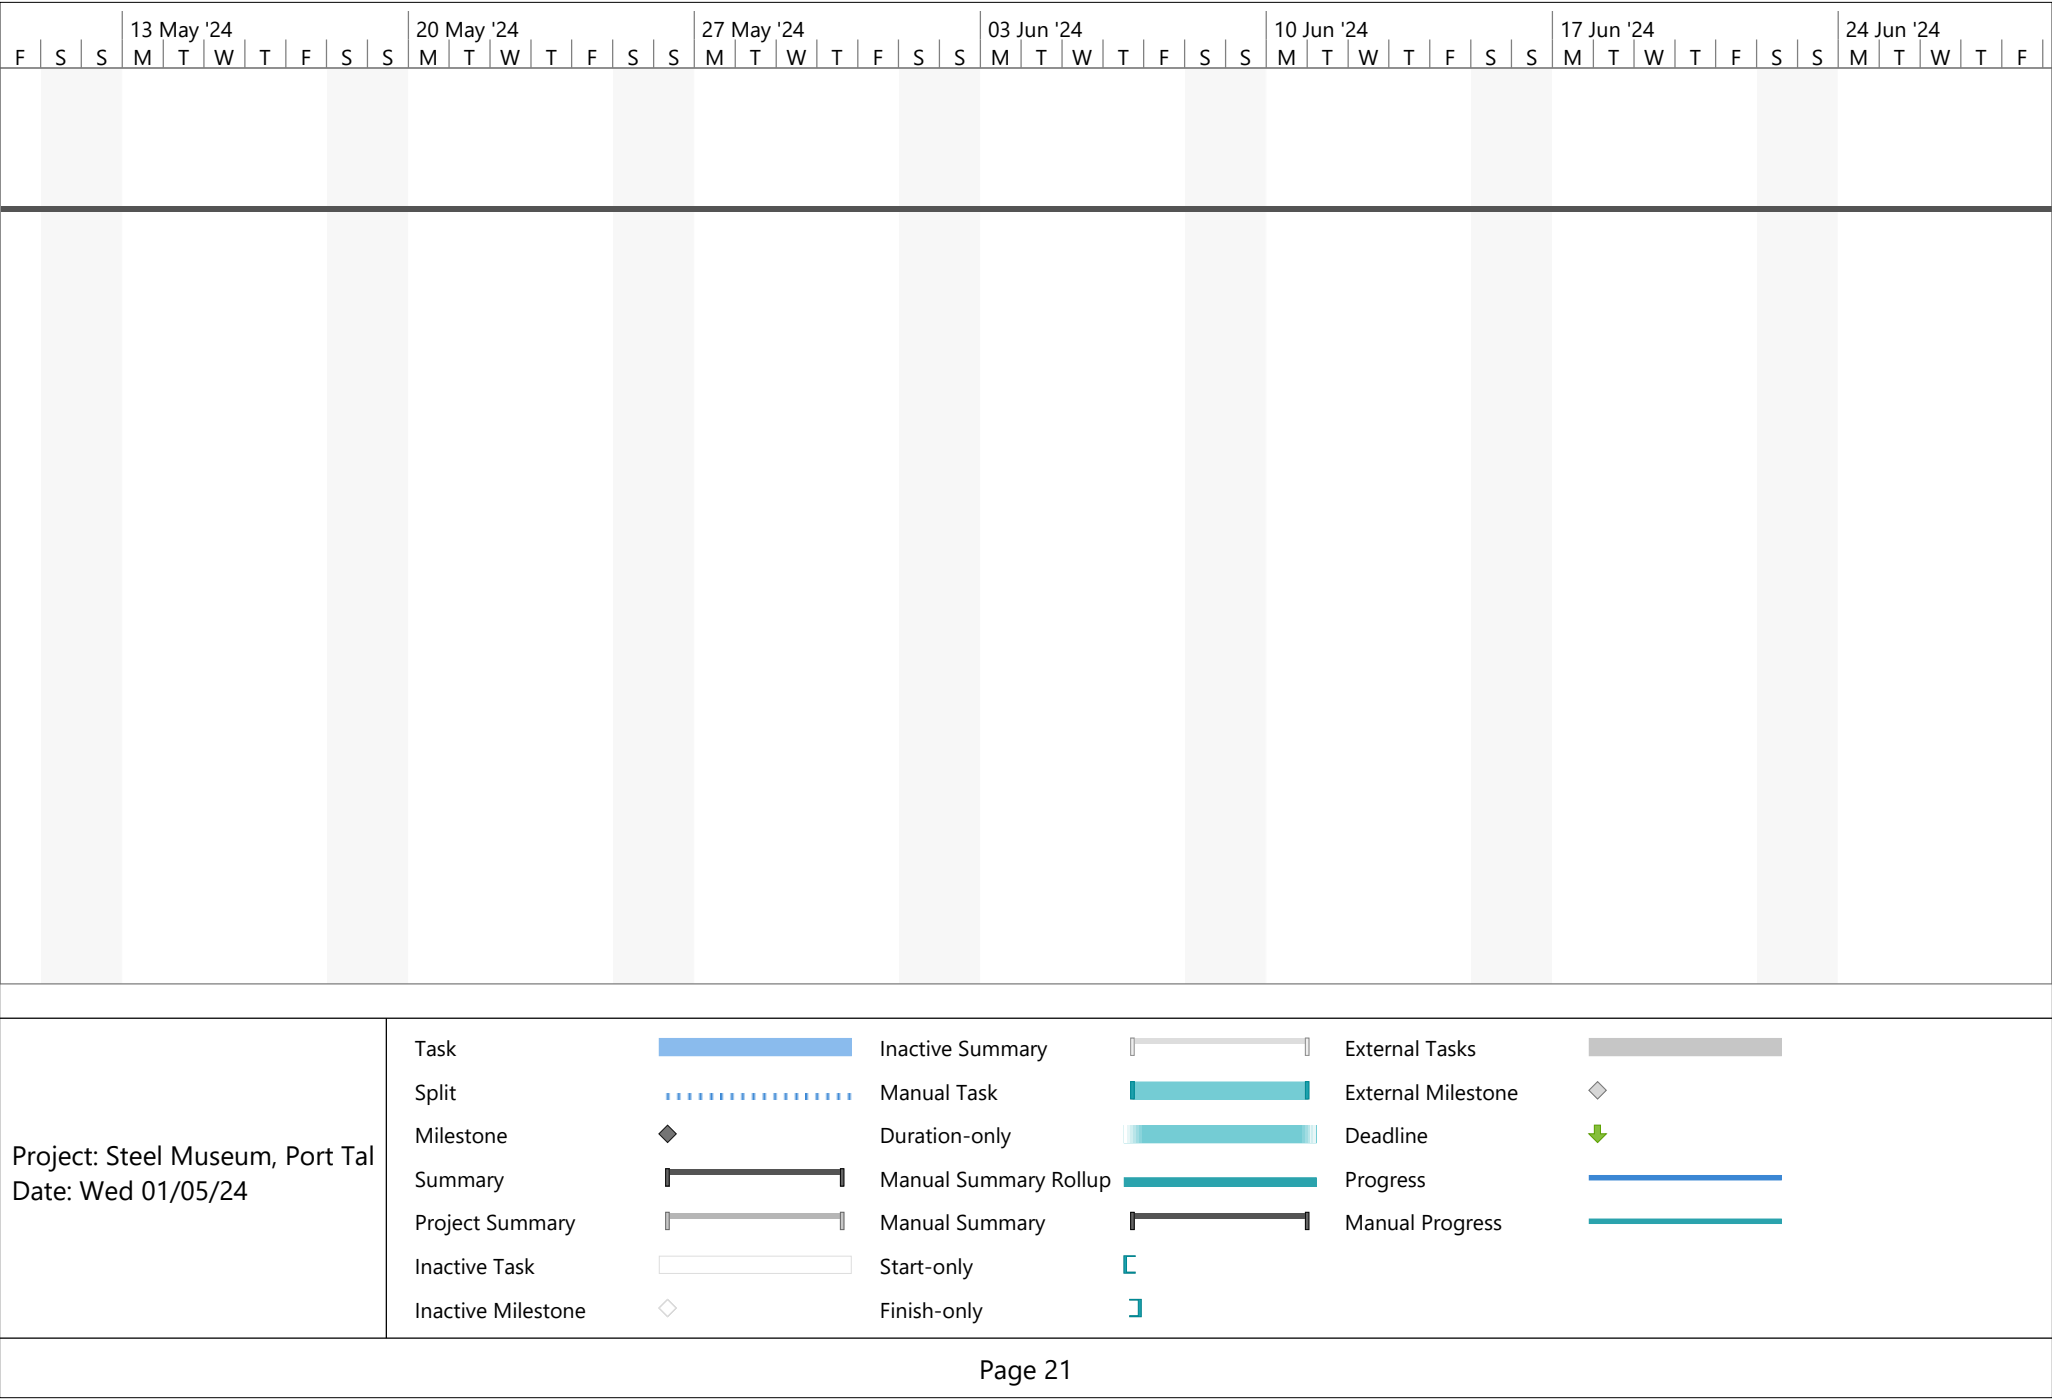

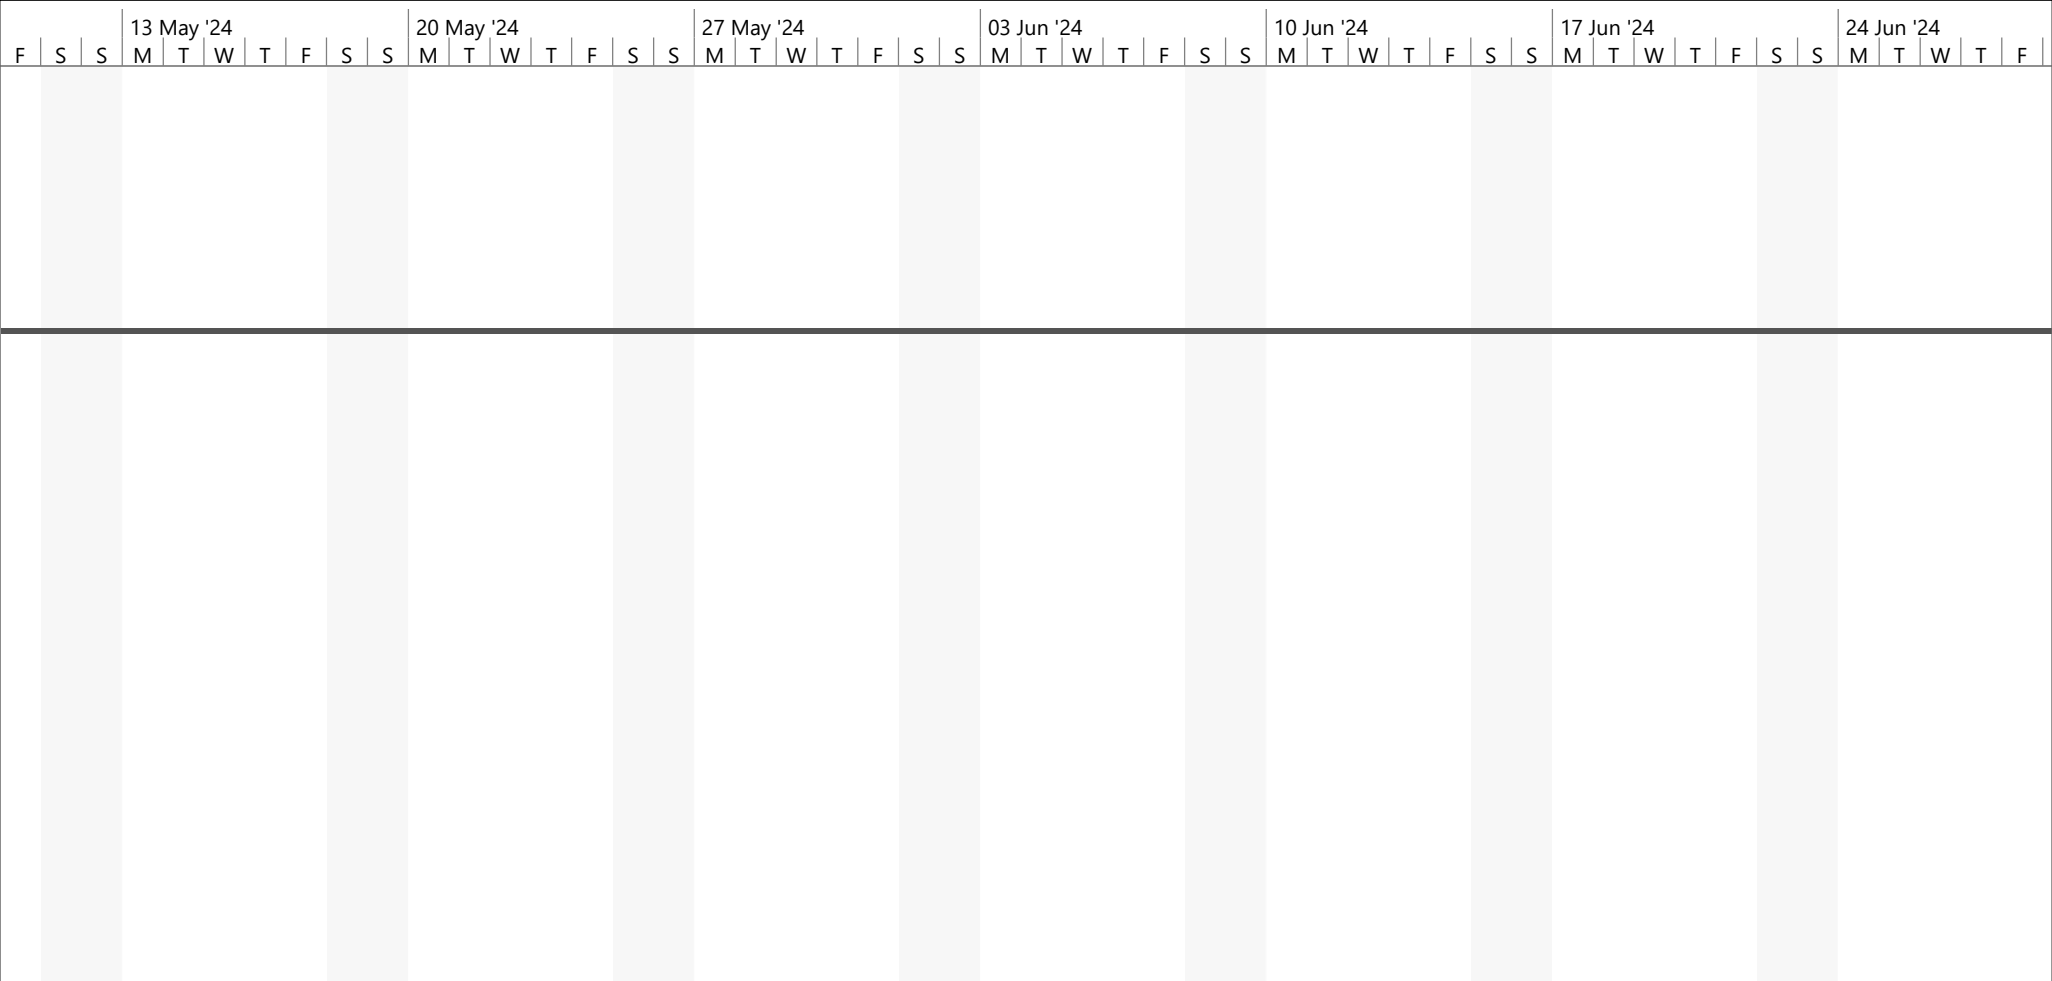


Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

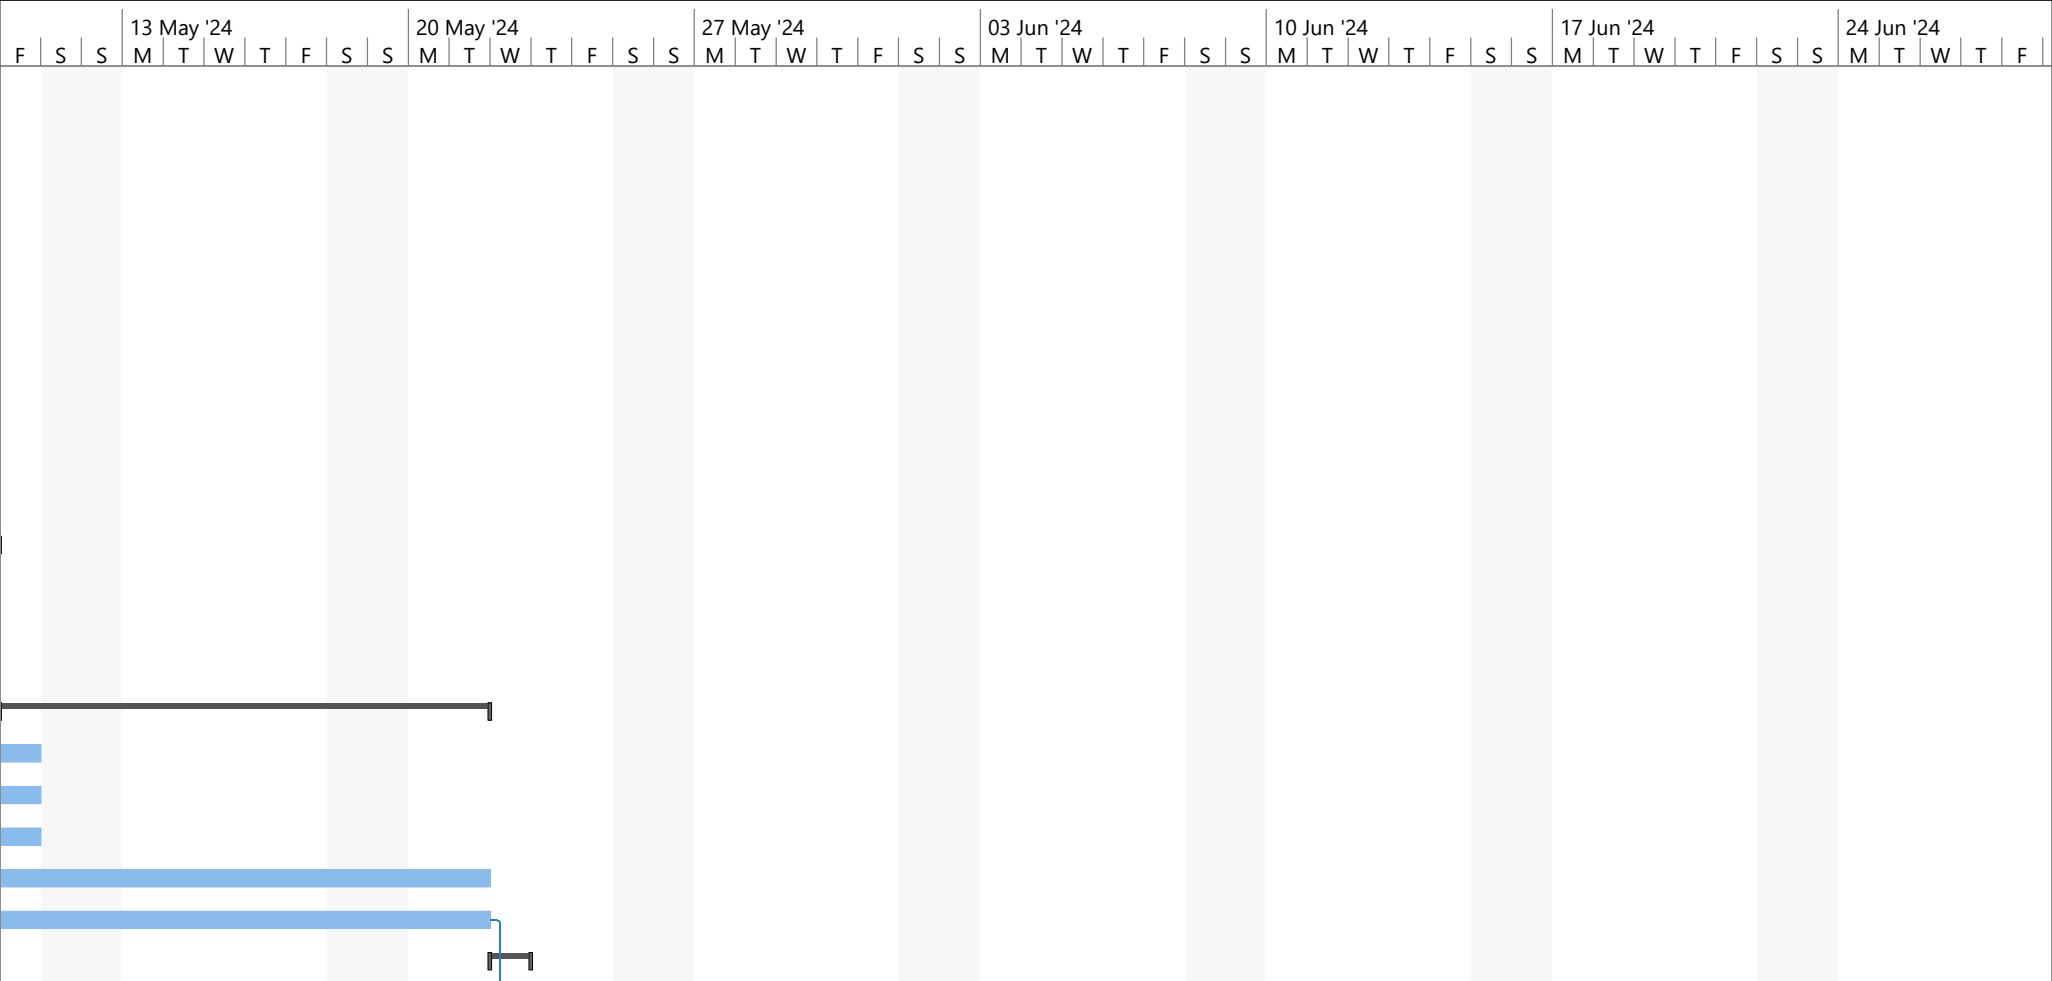


Project: Steel Museum, Port Talbot
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

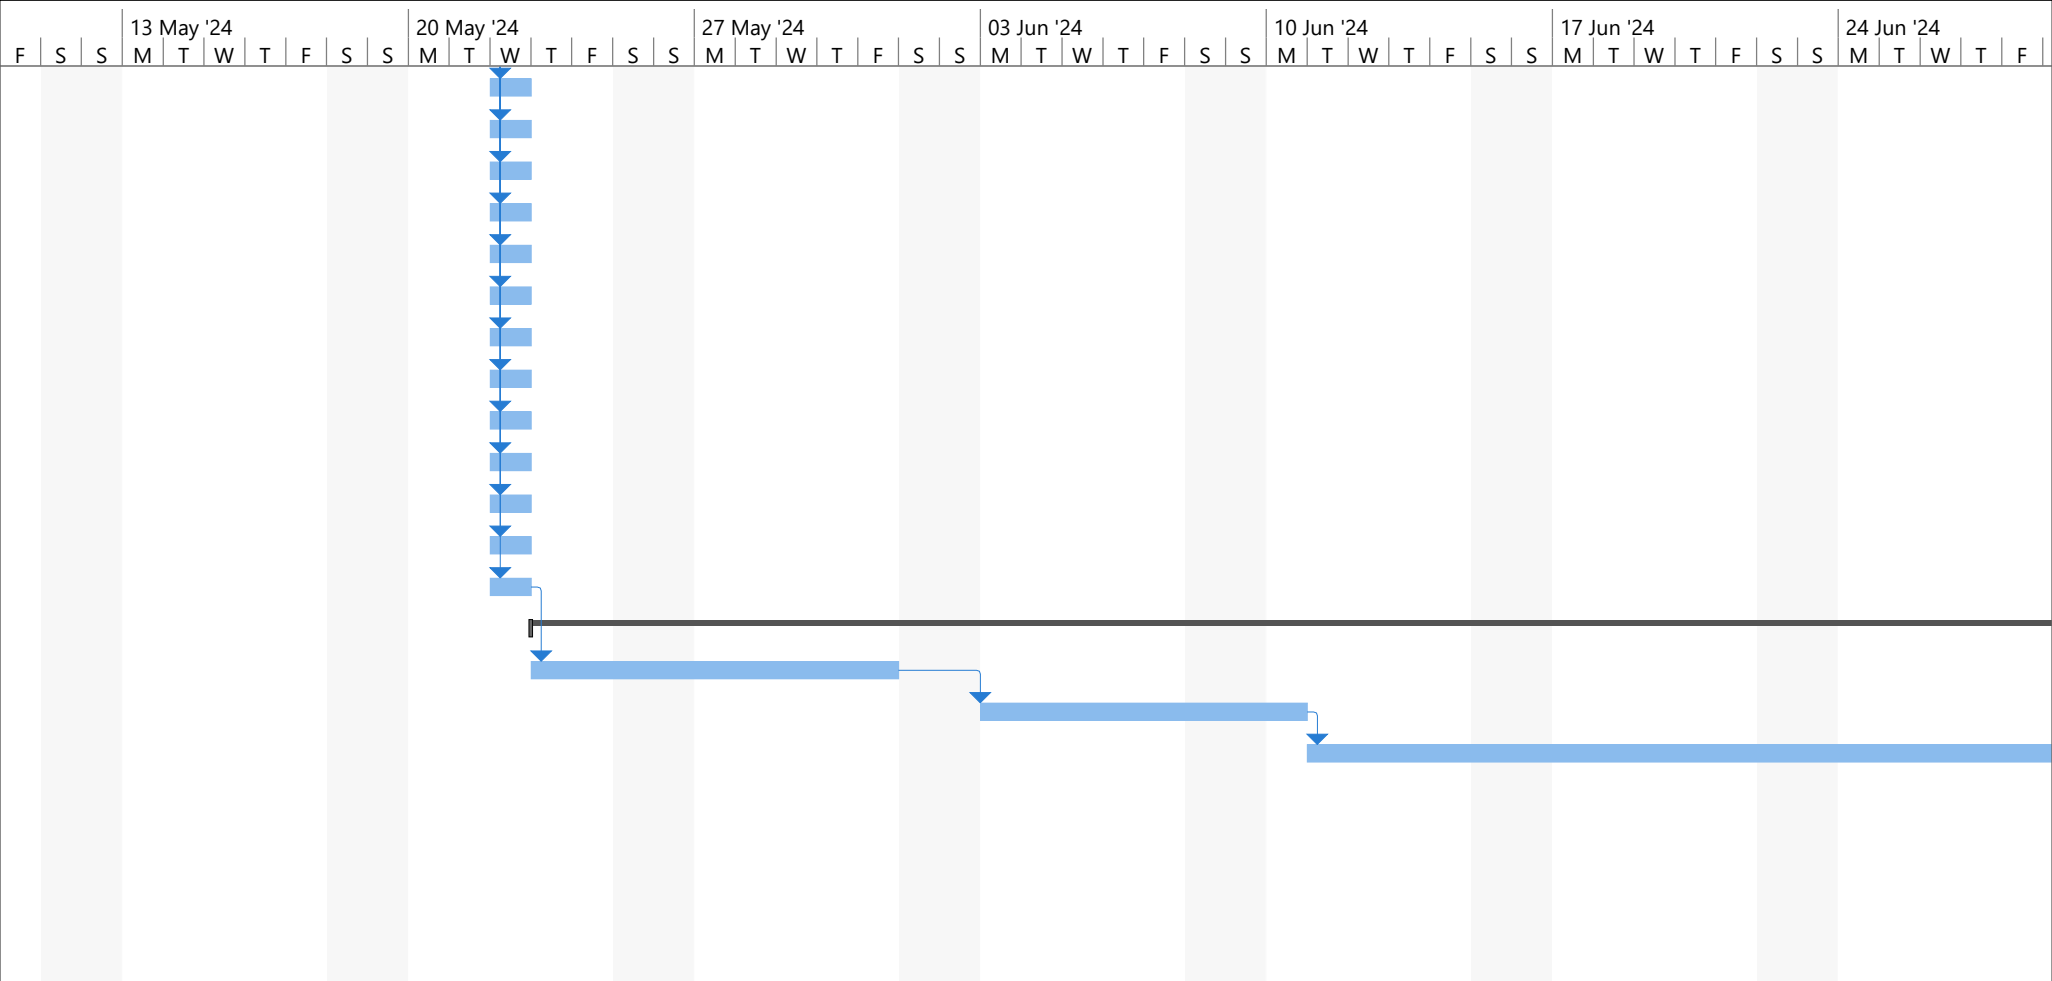

Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

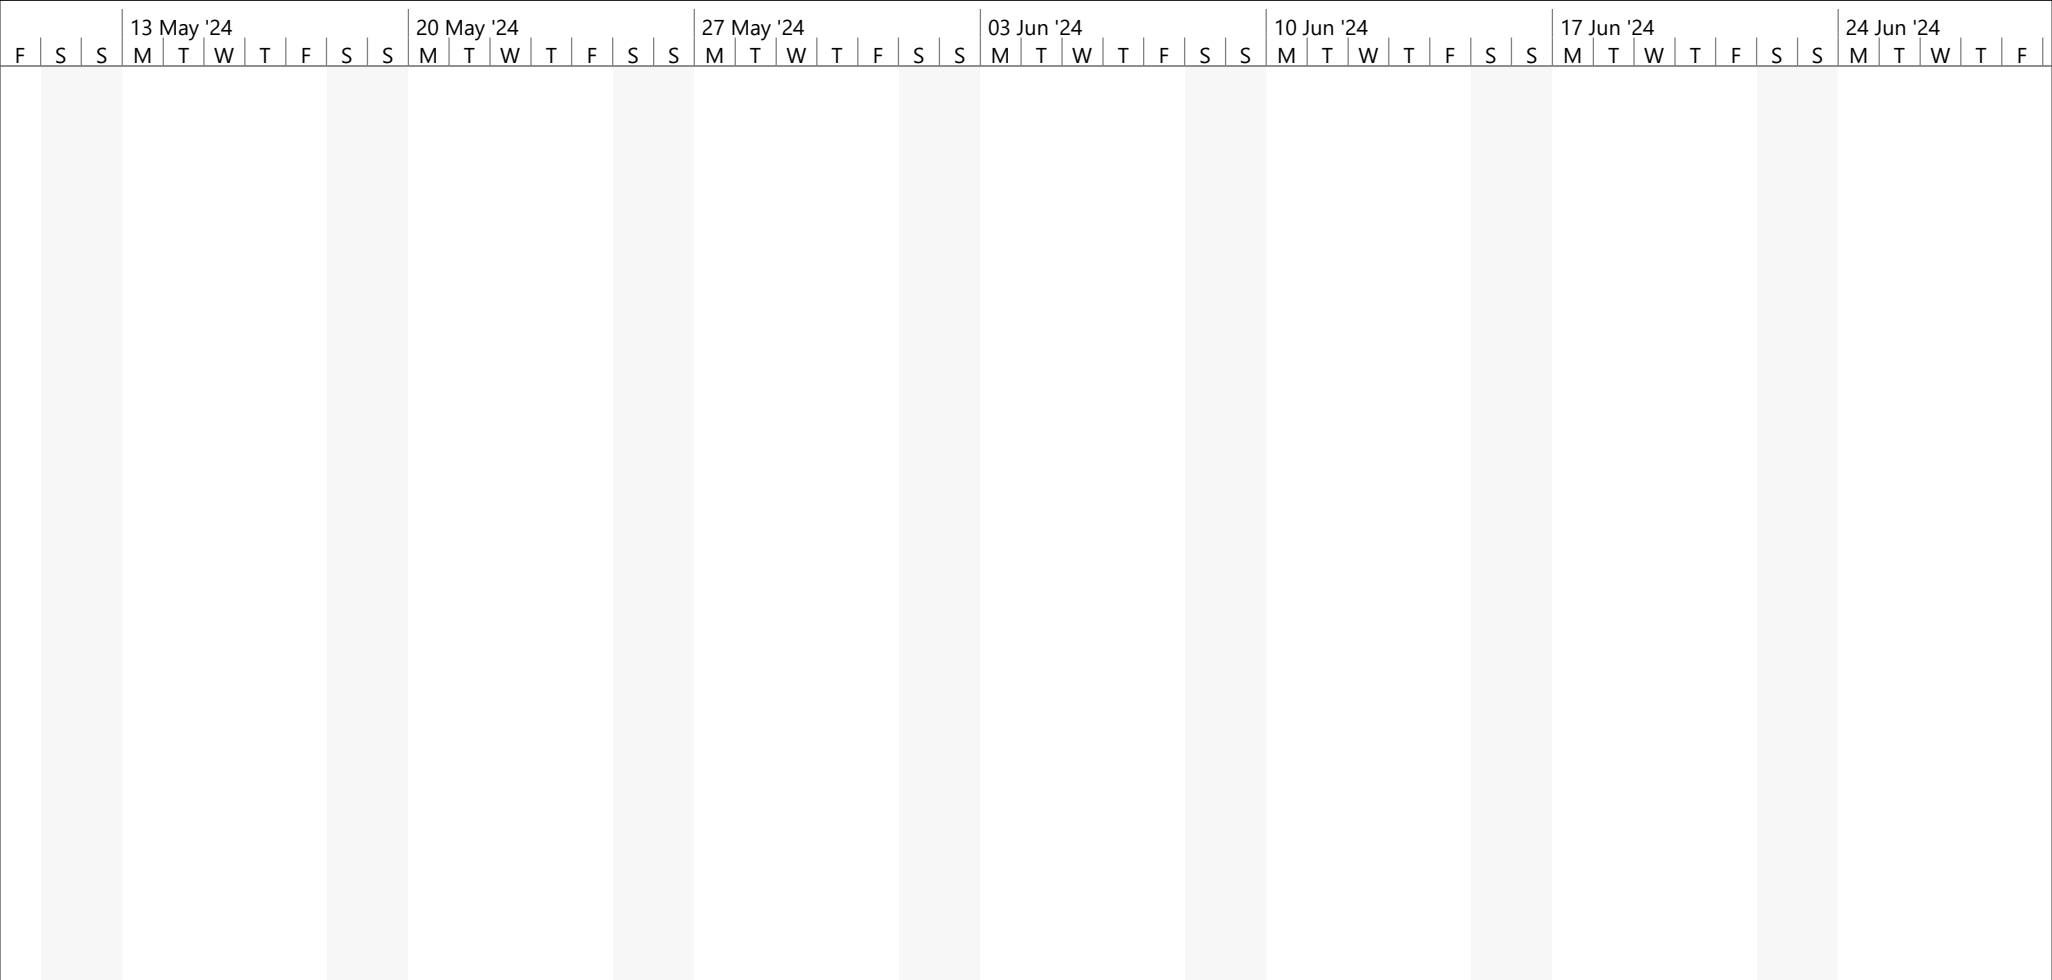


Project: Steel Museum, Port Tal
Date: Wed 01/05/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

			13 May '24							20 May '24							27 May '24							03 Jun '24							10 Jun '24							17 Jun '24							24 Jun '24				
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F							




Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

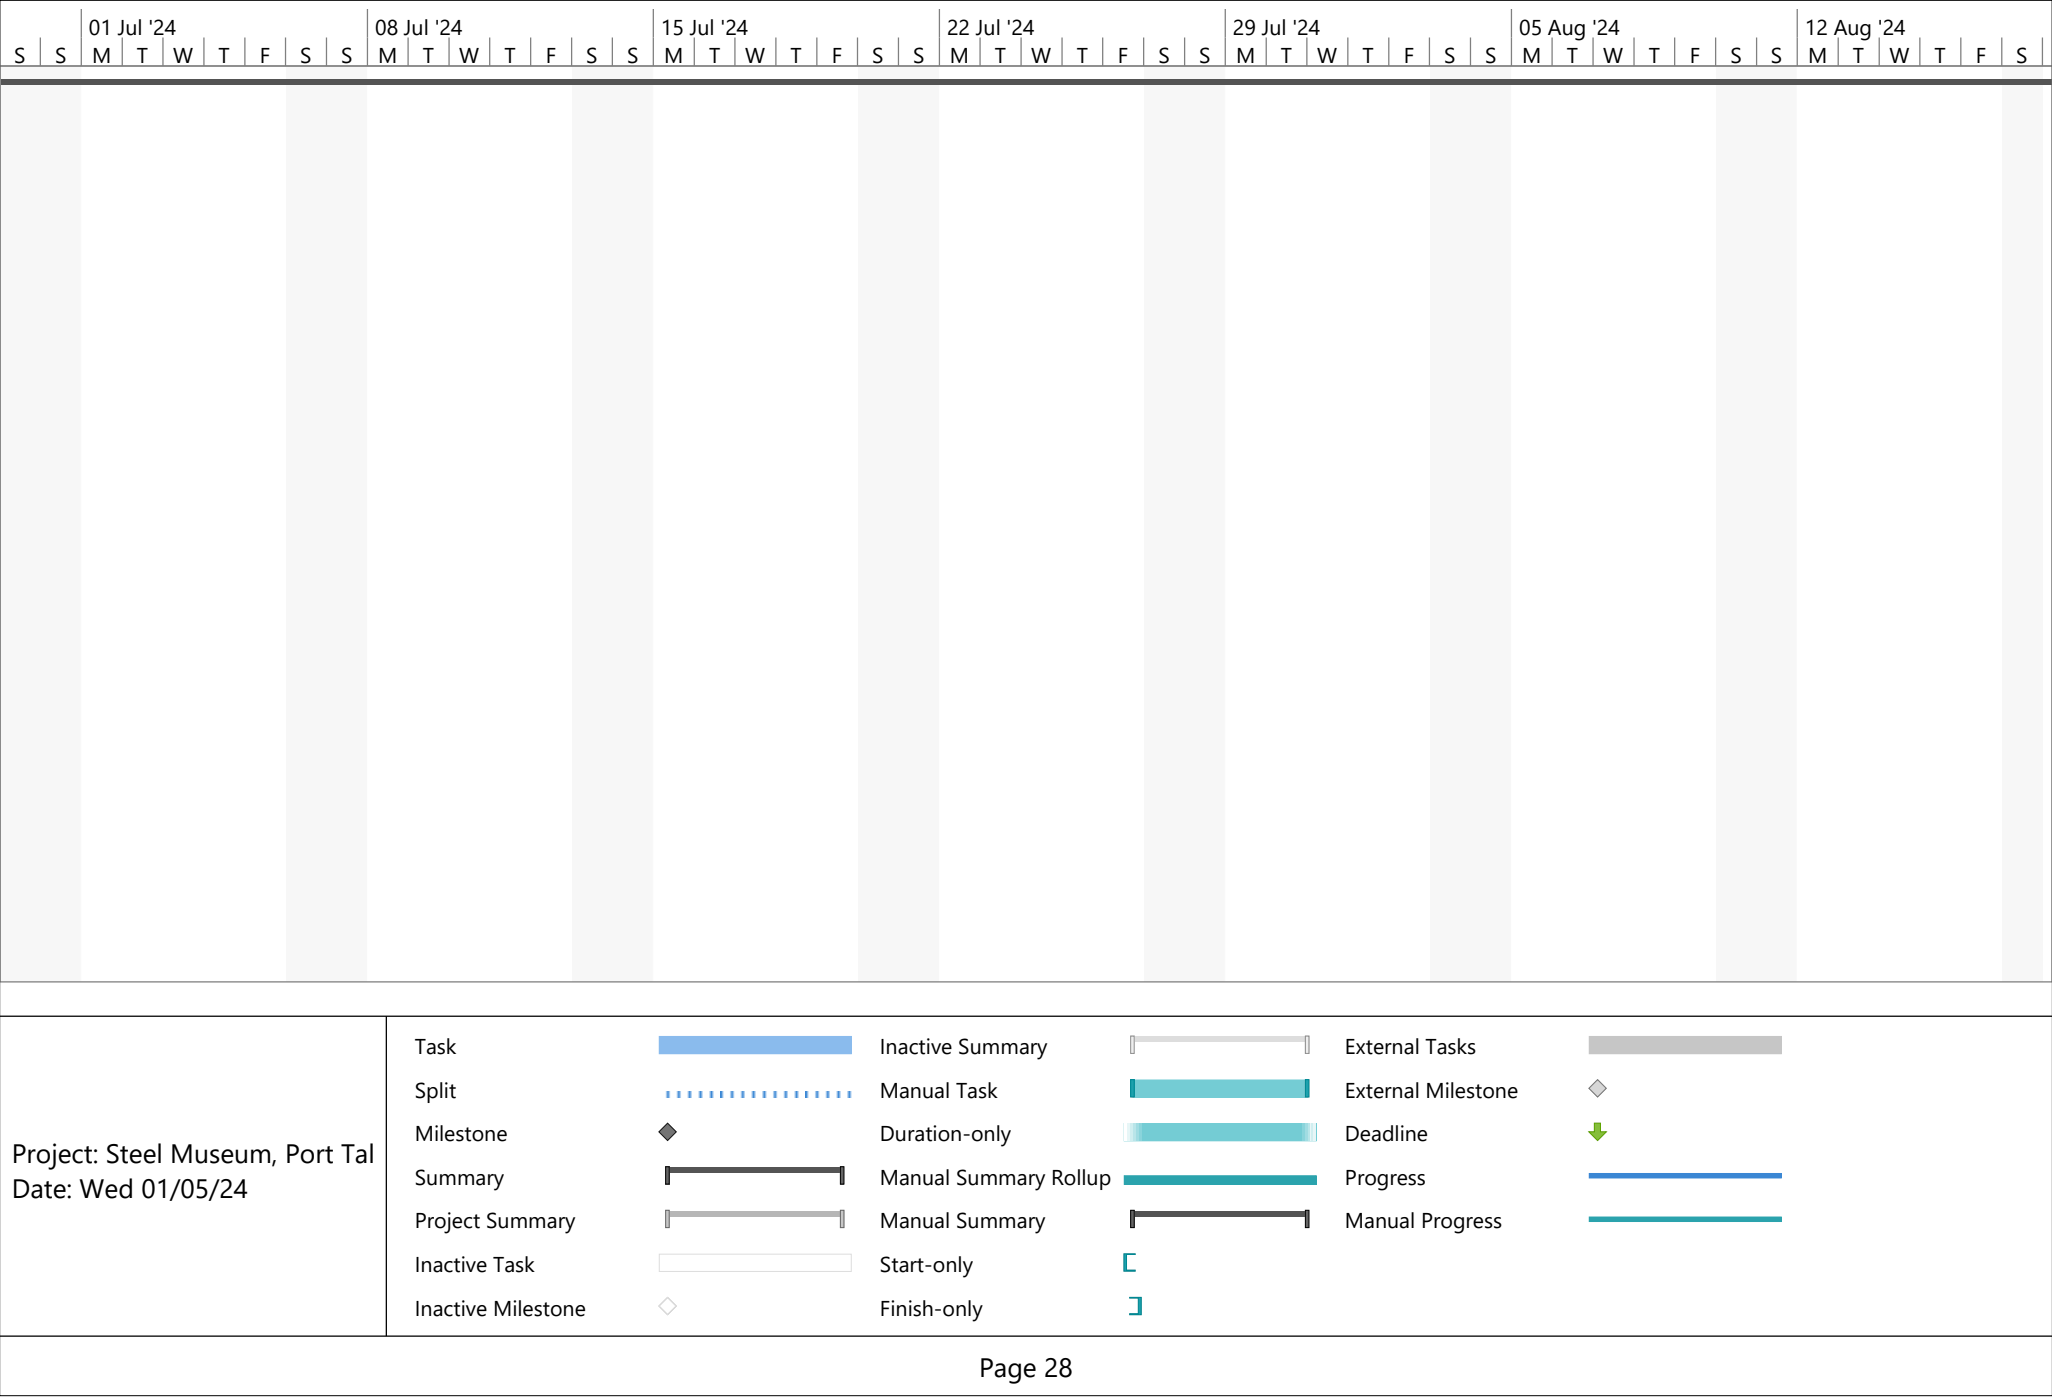

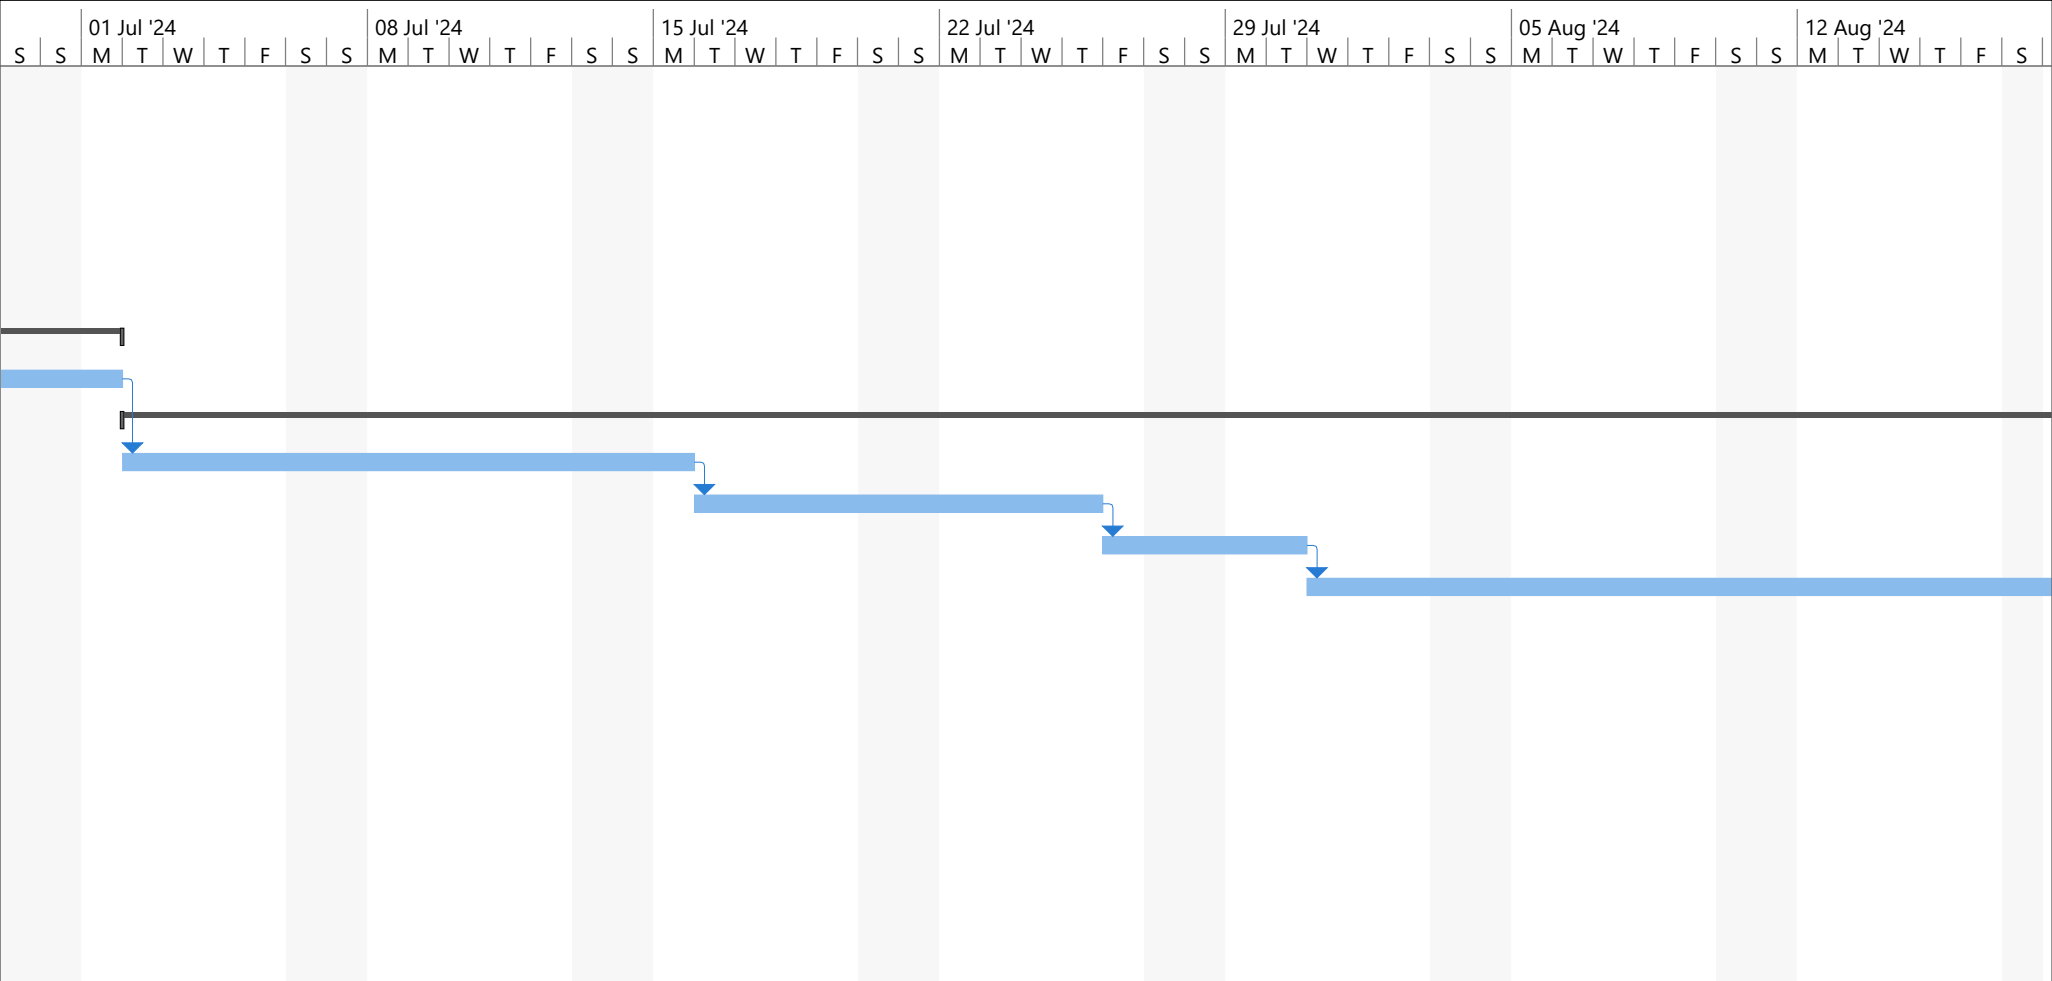


Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

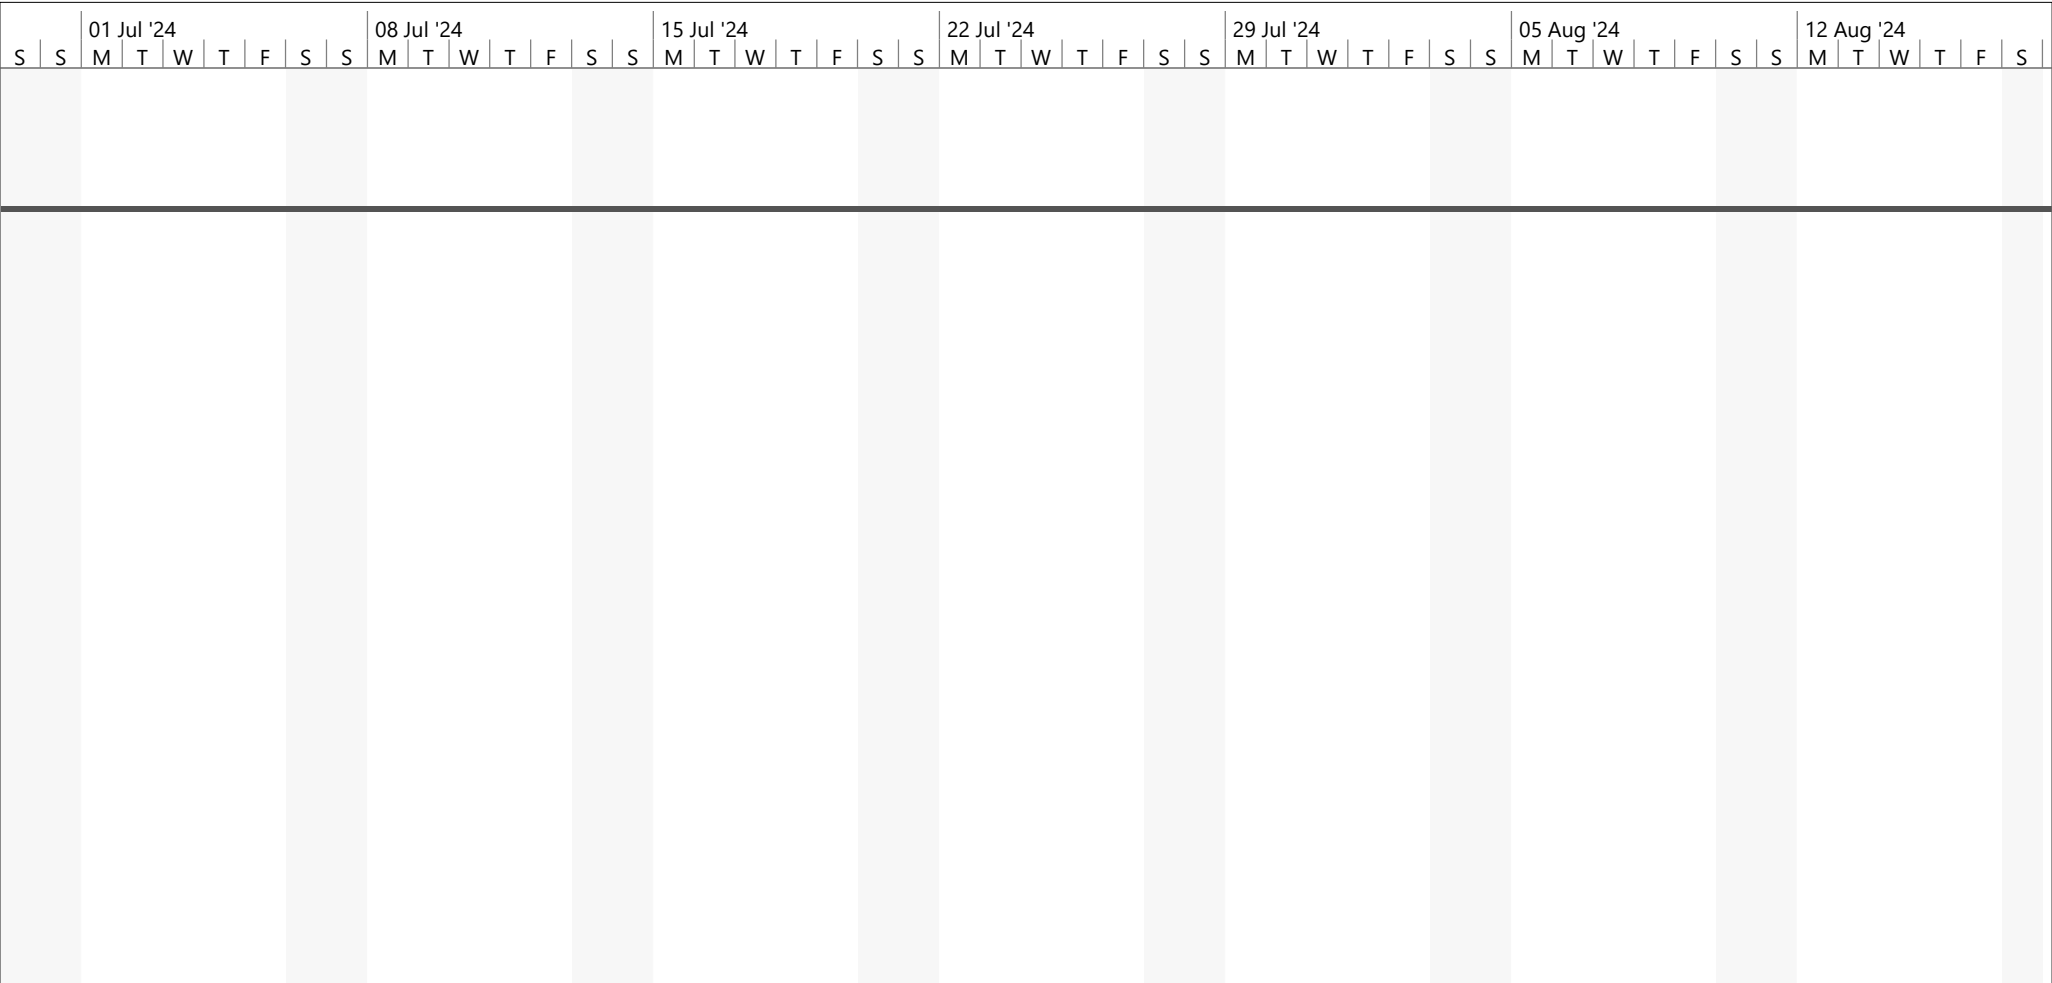


Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

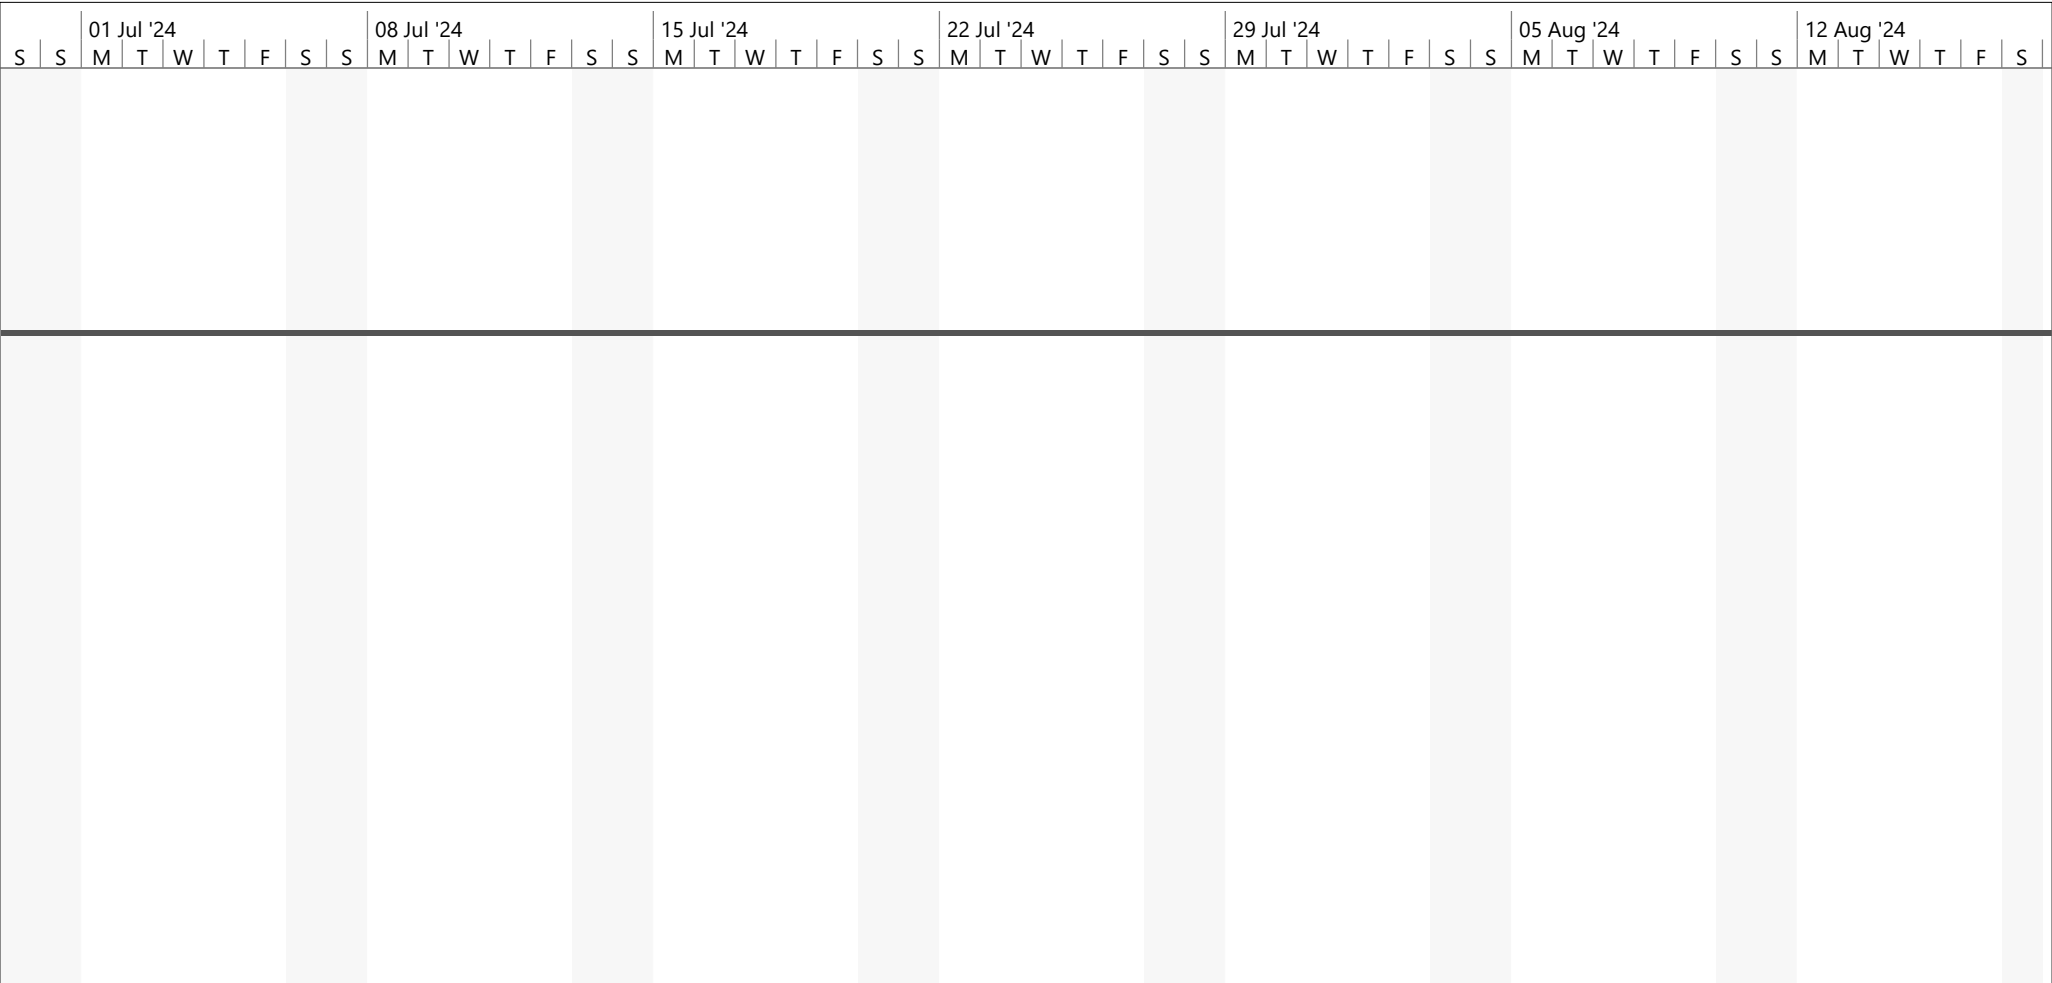


Project: Steel Museum, Port Talbot
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

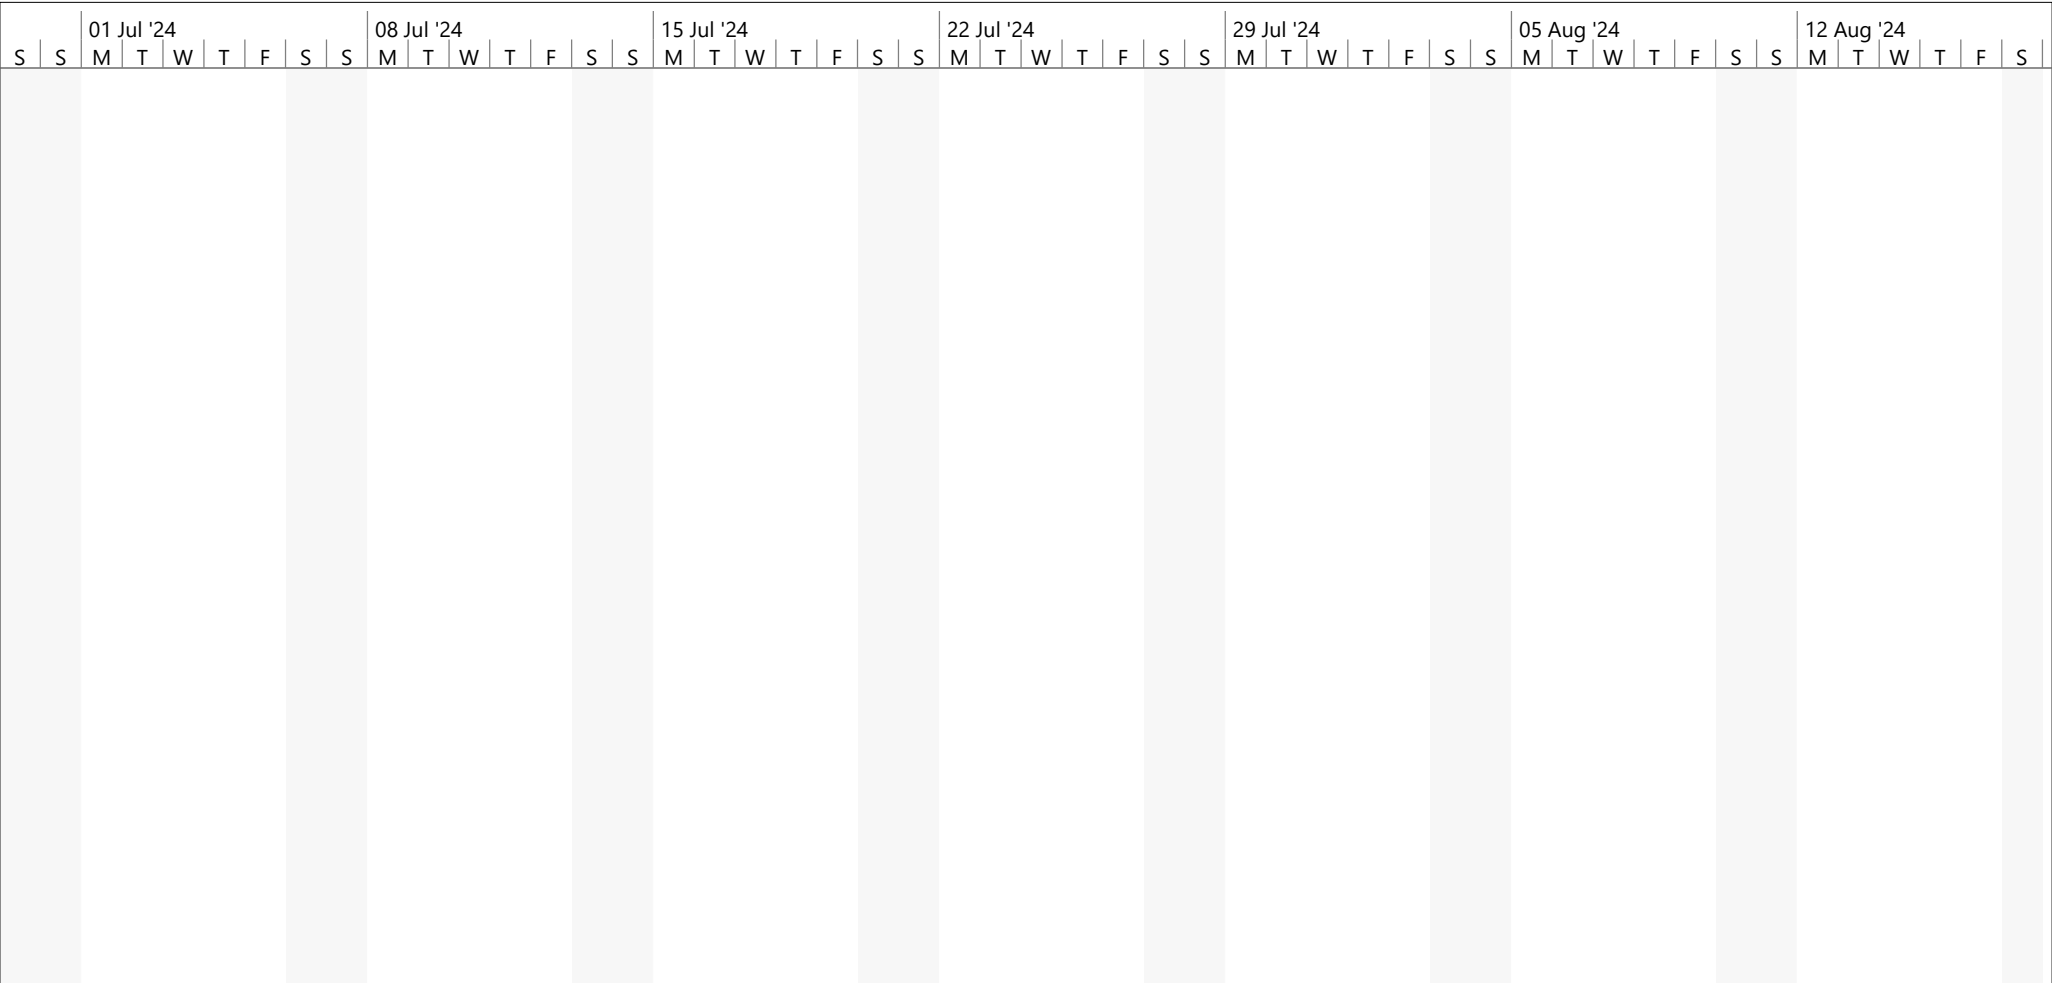


Project: Steel Museum, Port Tal
Date: Wed 01/05/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

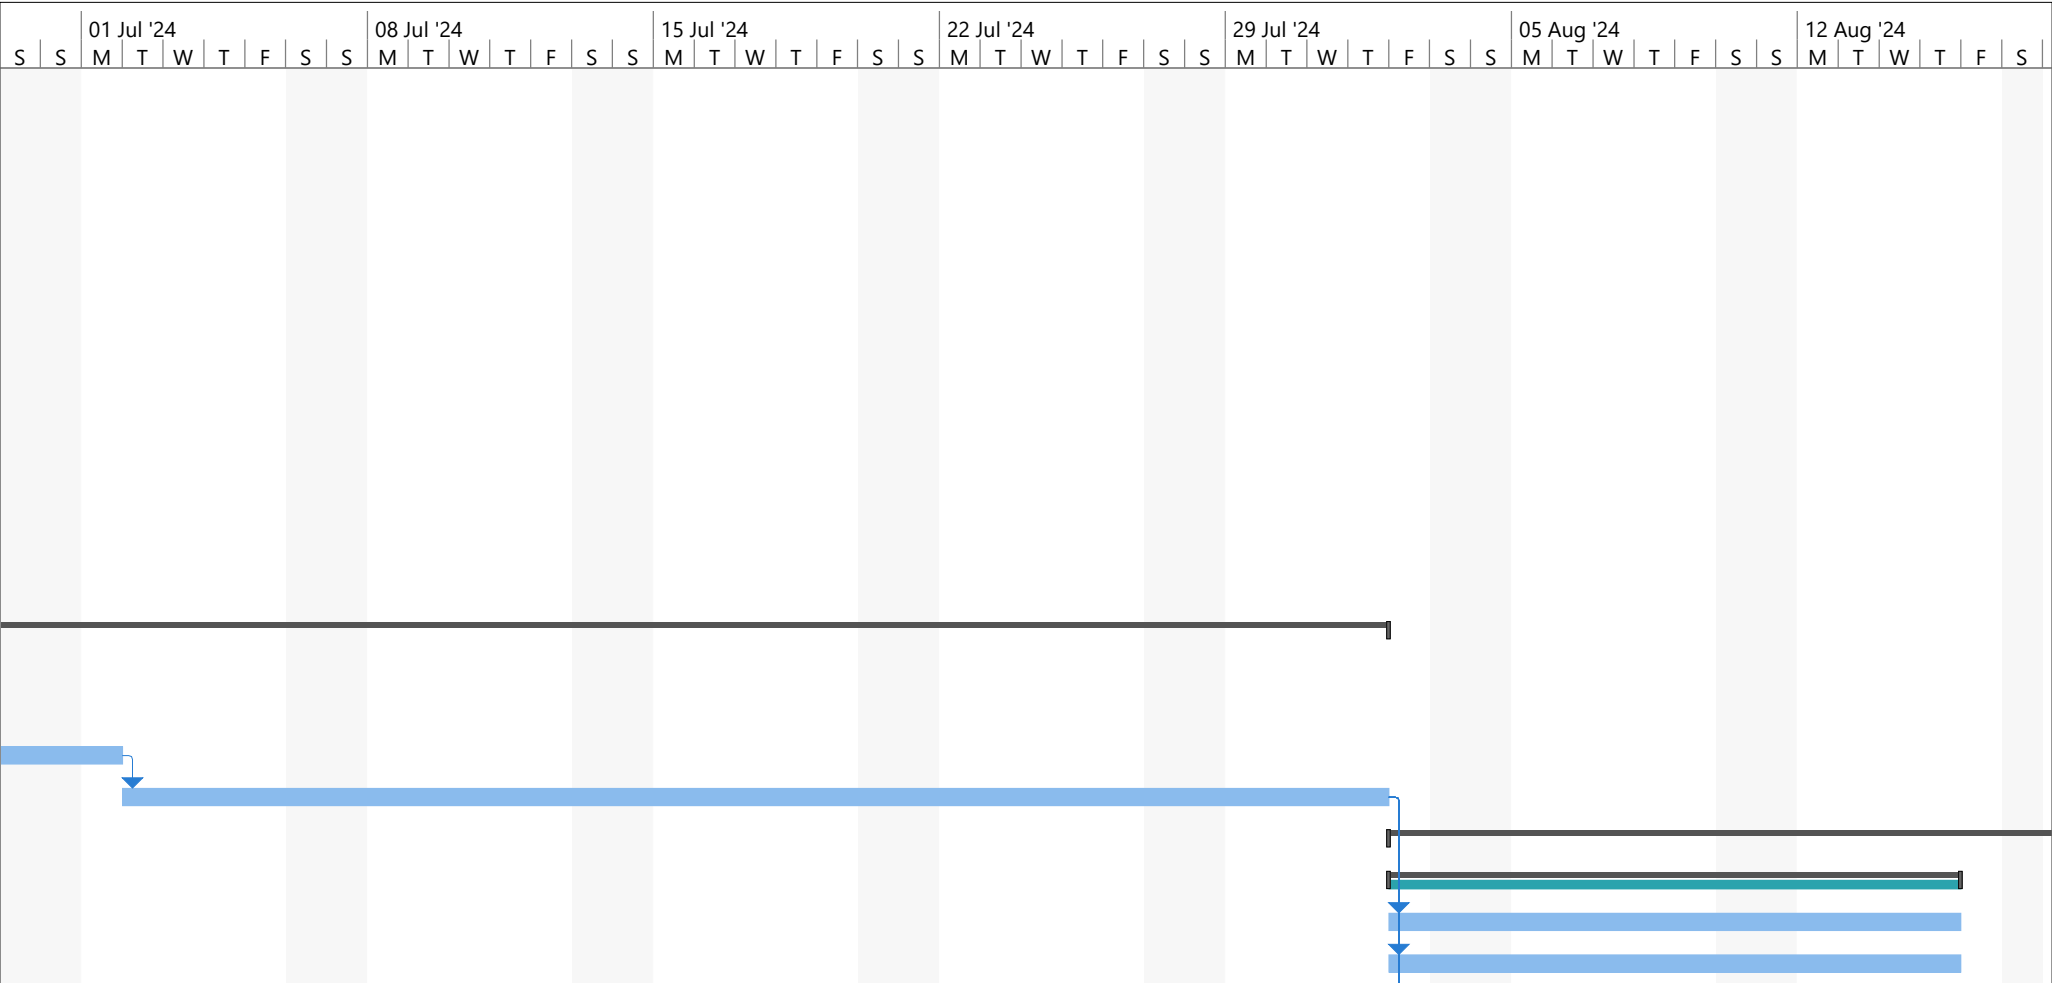

Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

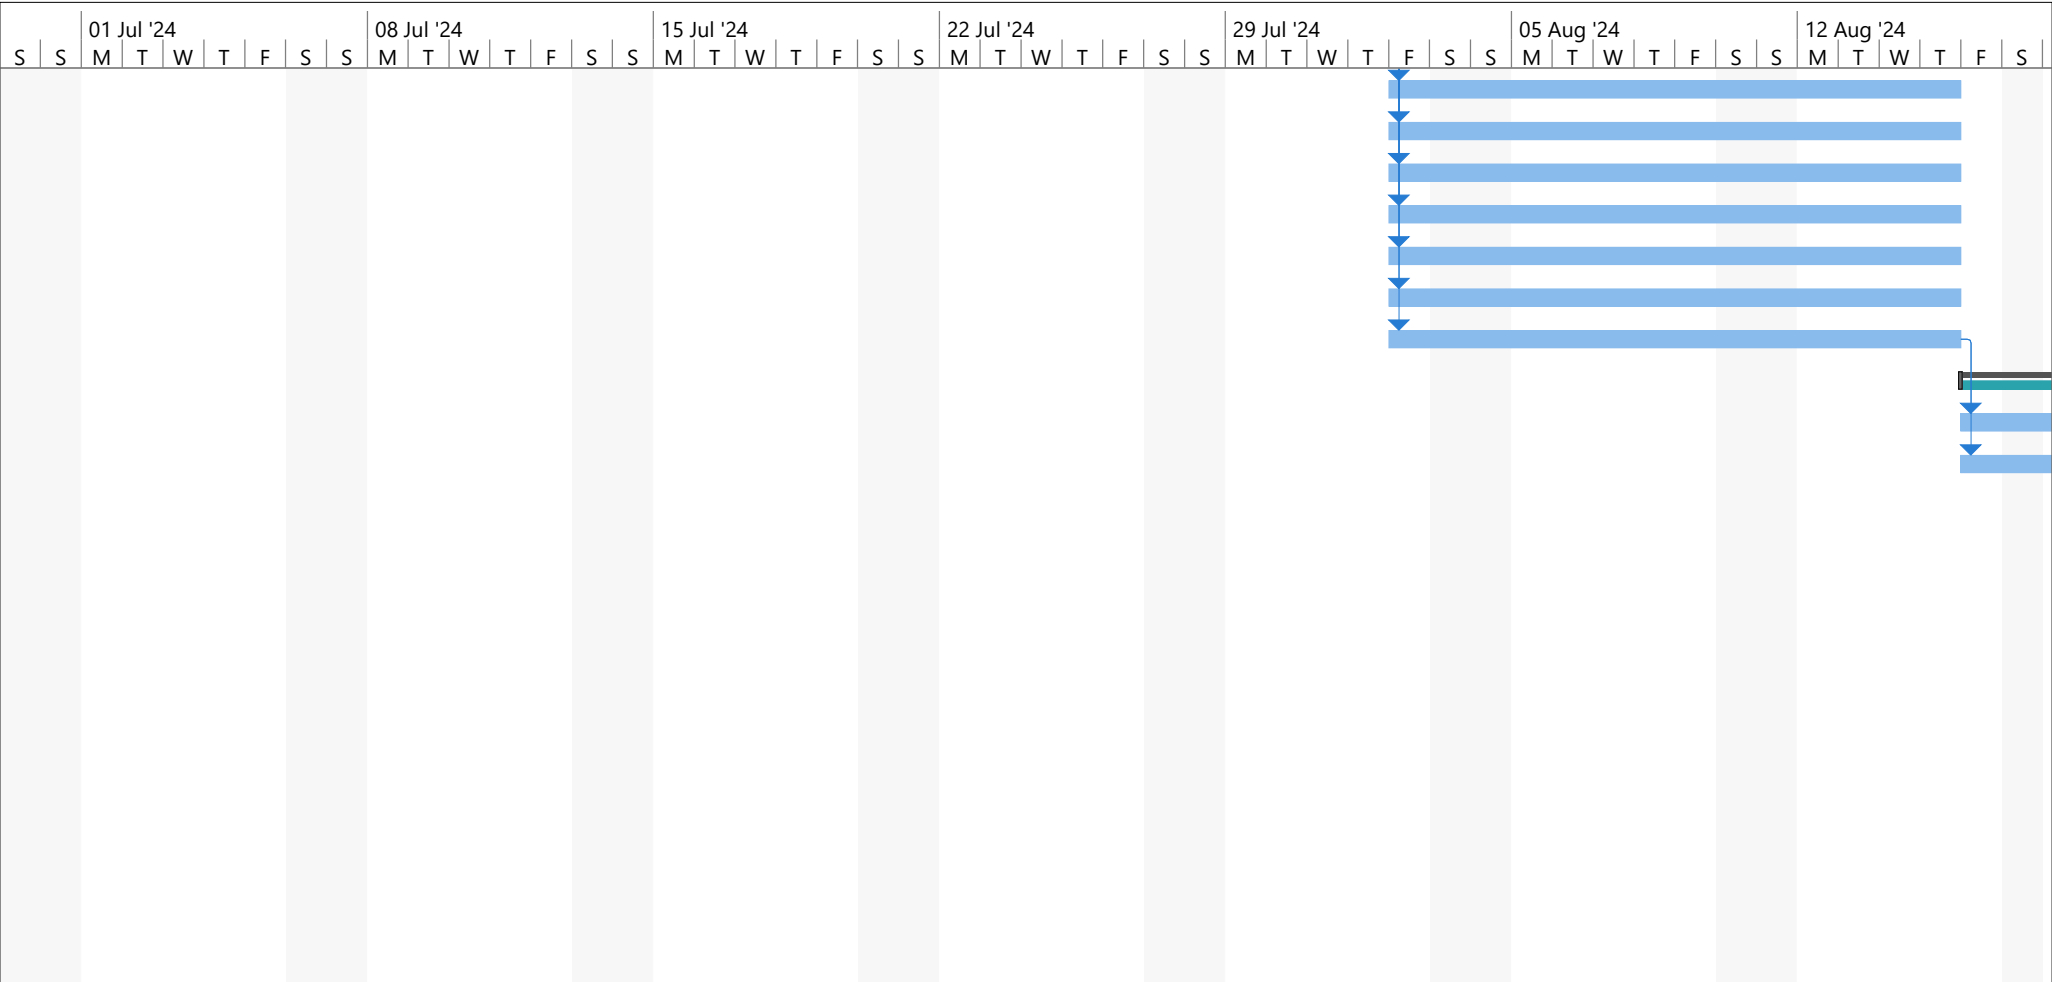

Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

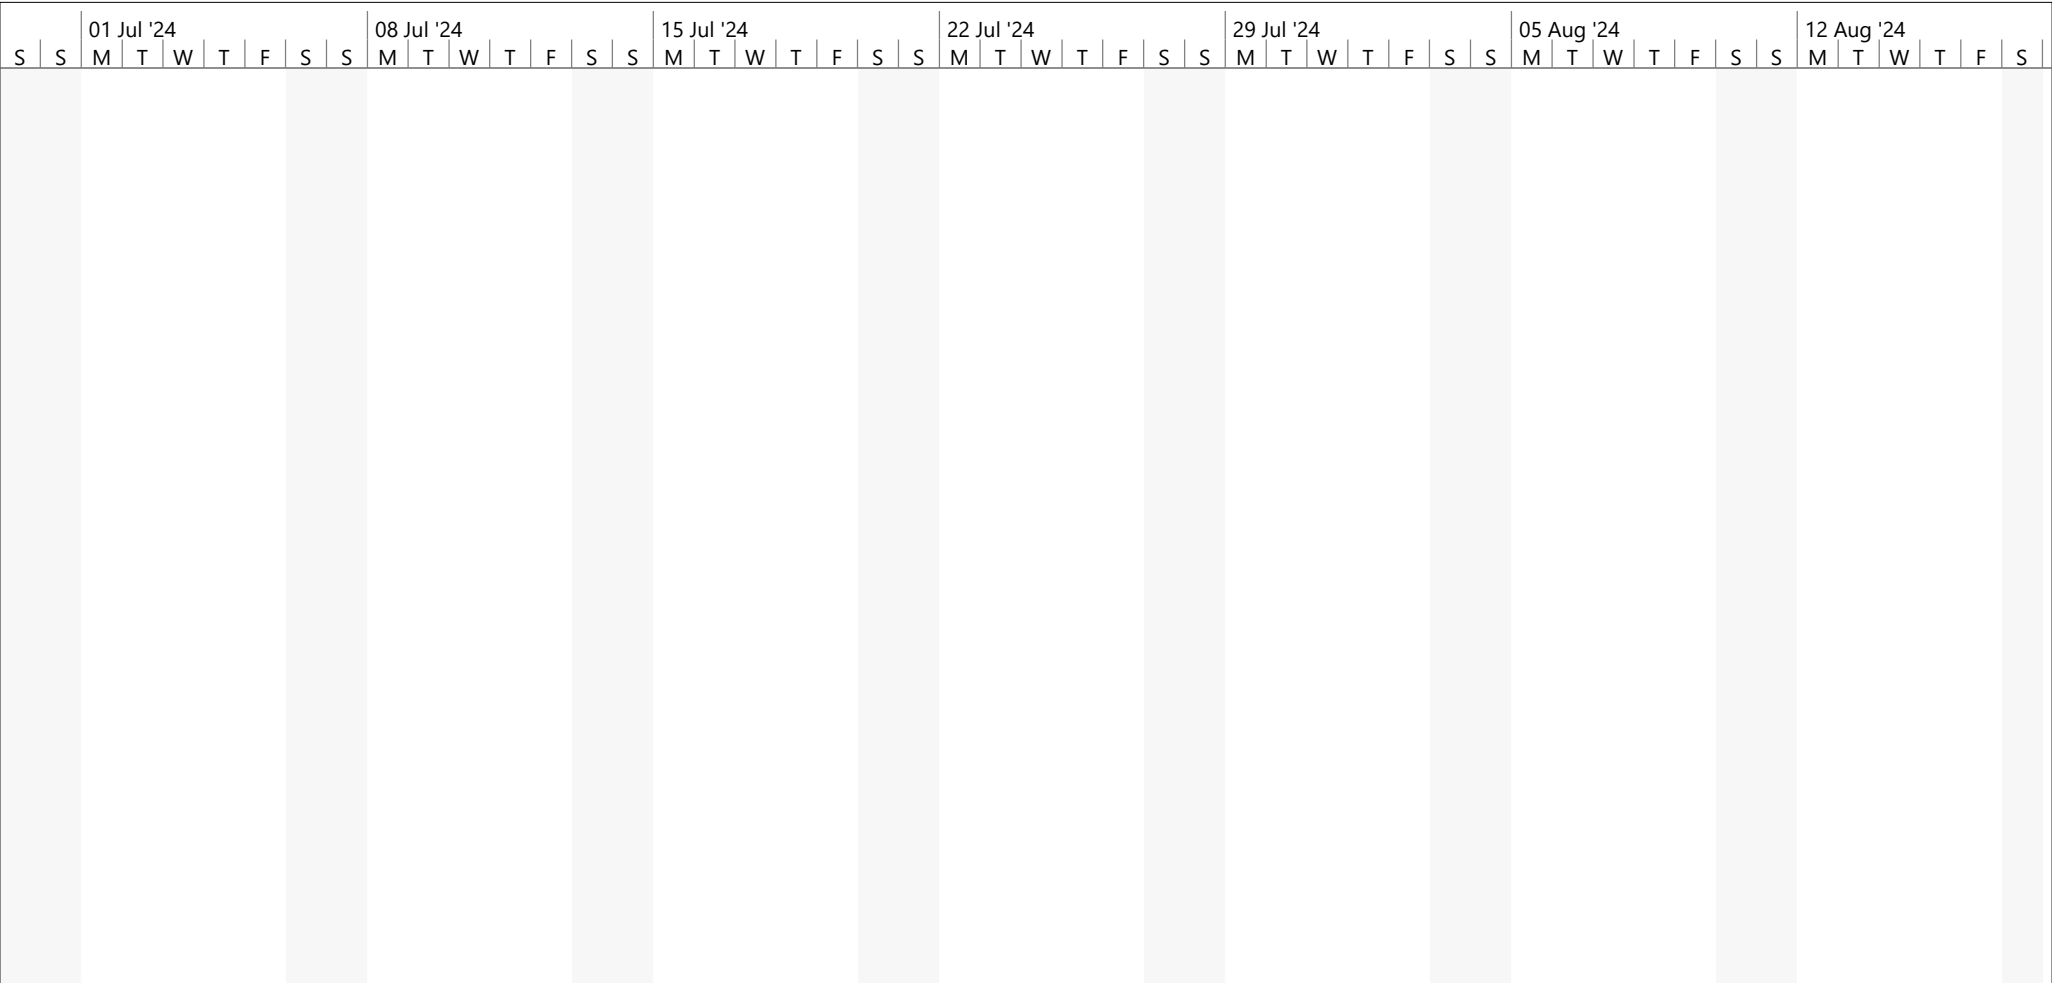


Project: Steel Museum, Port Tal
Date: Wed 01/05/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

S	S	01 Jul '24						S	S	08 Jul '24						S	S	15 Jul '24						S	S	22 Jul '24						S	S	29 Jul '24						S	S	05 Aug '24						S	S	12 Aug '24						S
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S																



Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

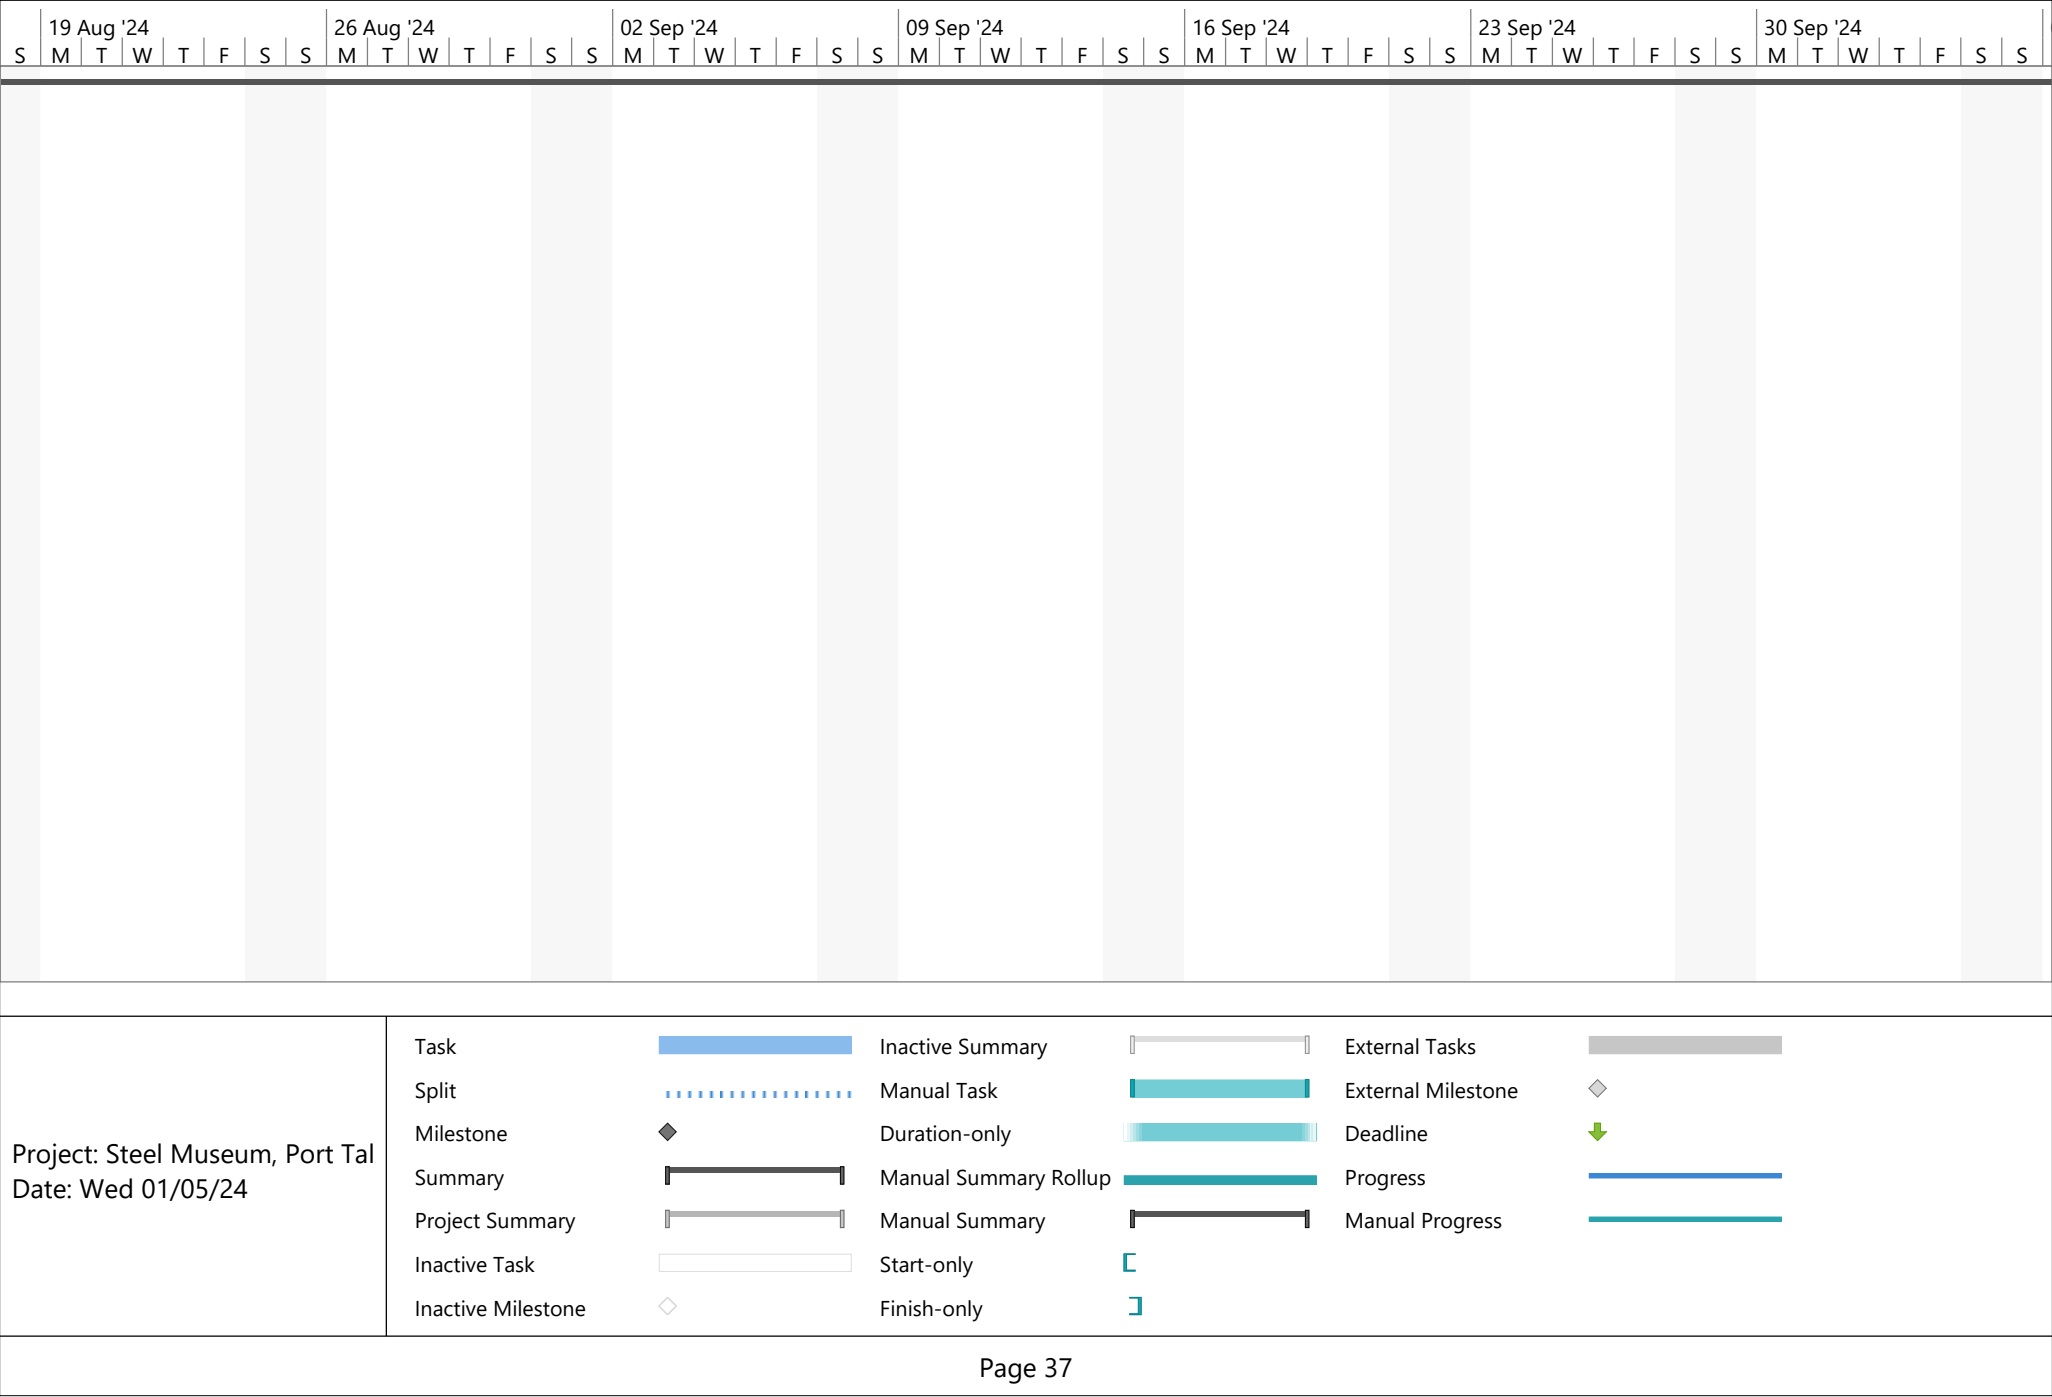

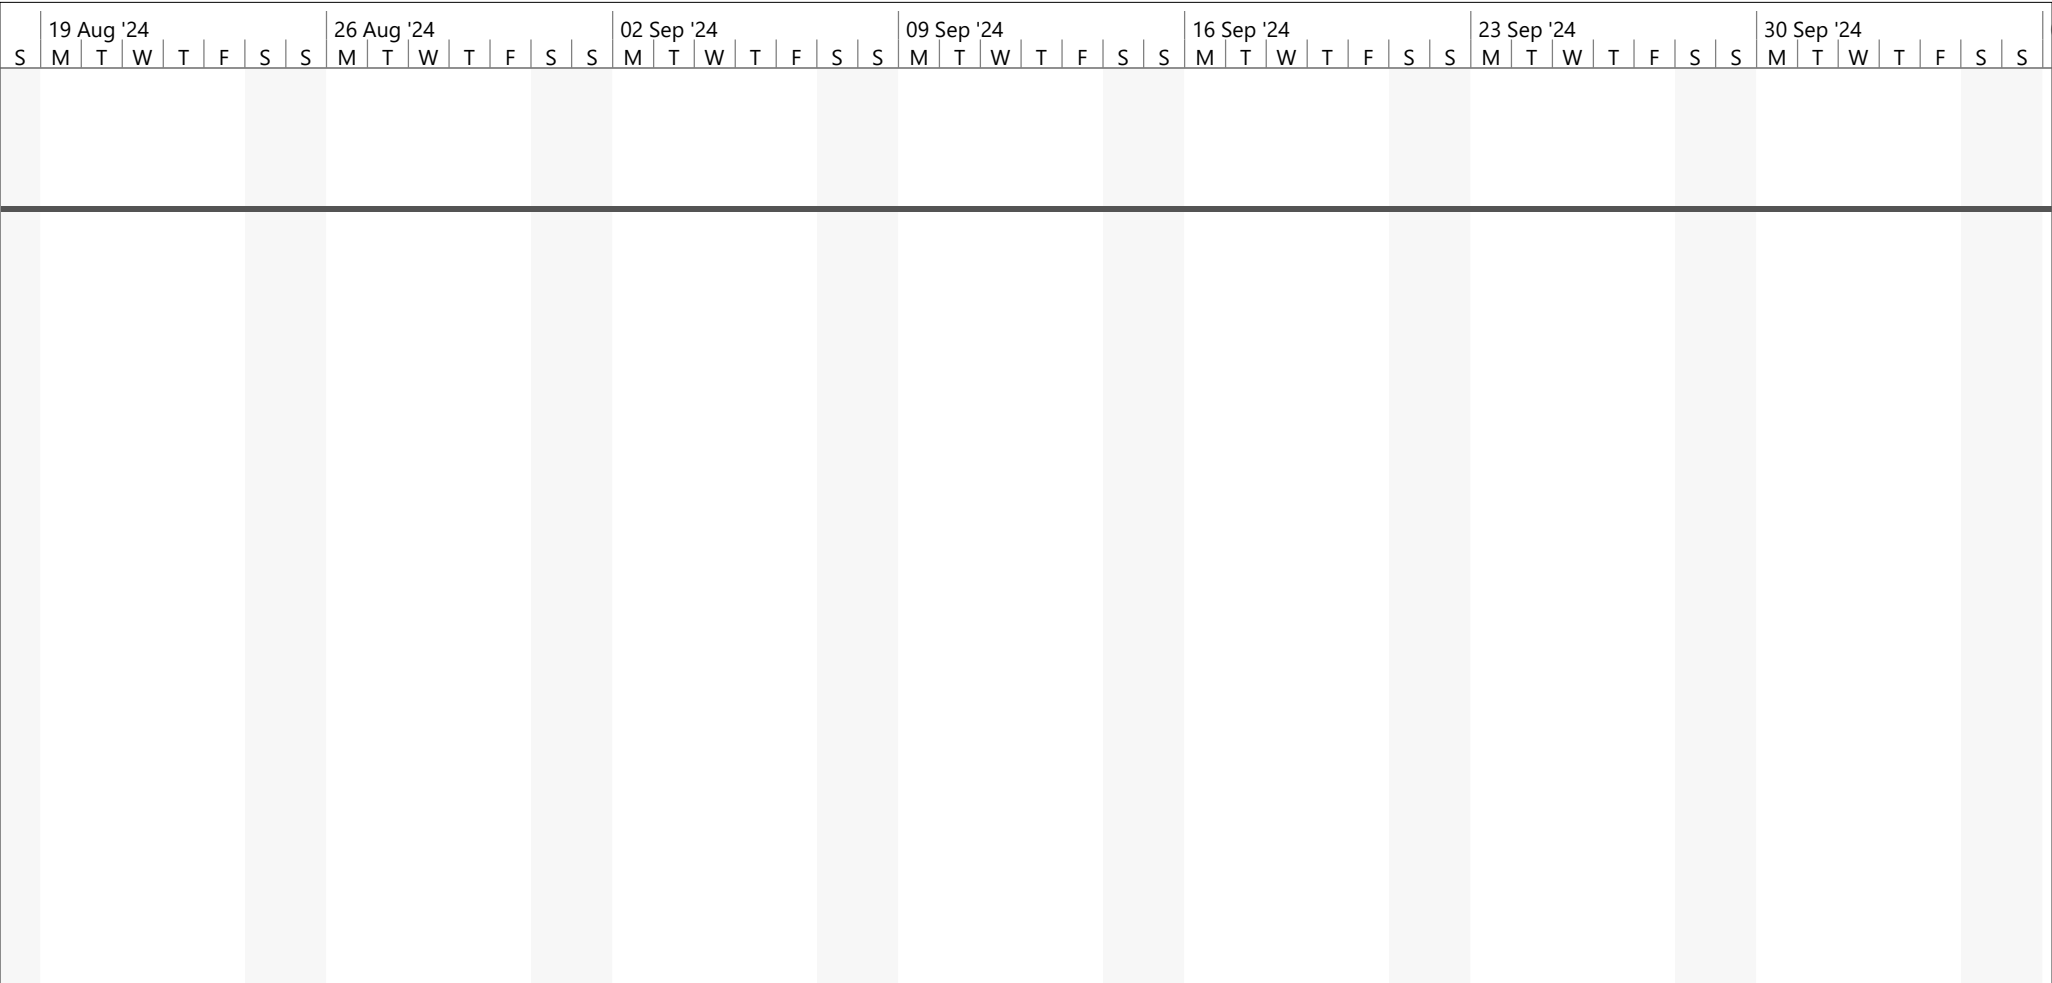

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 39

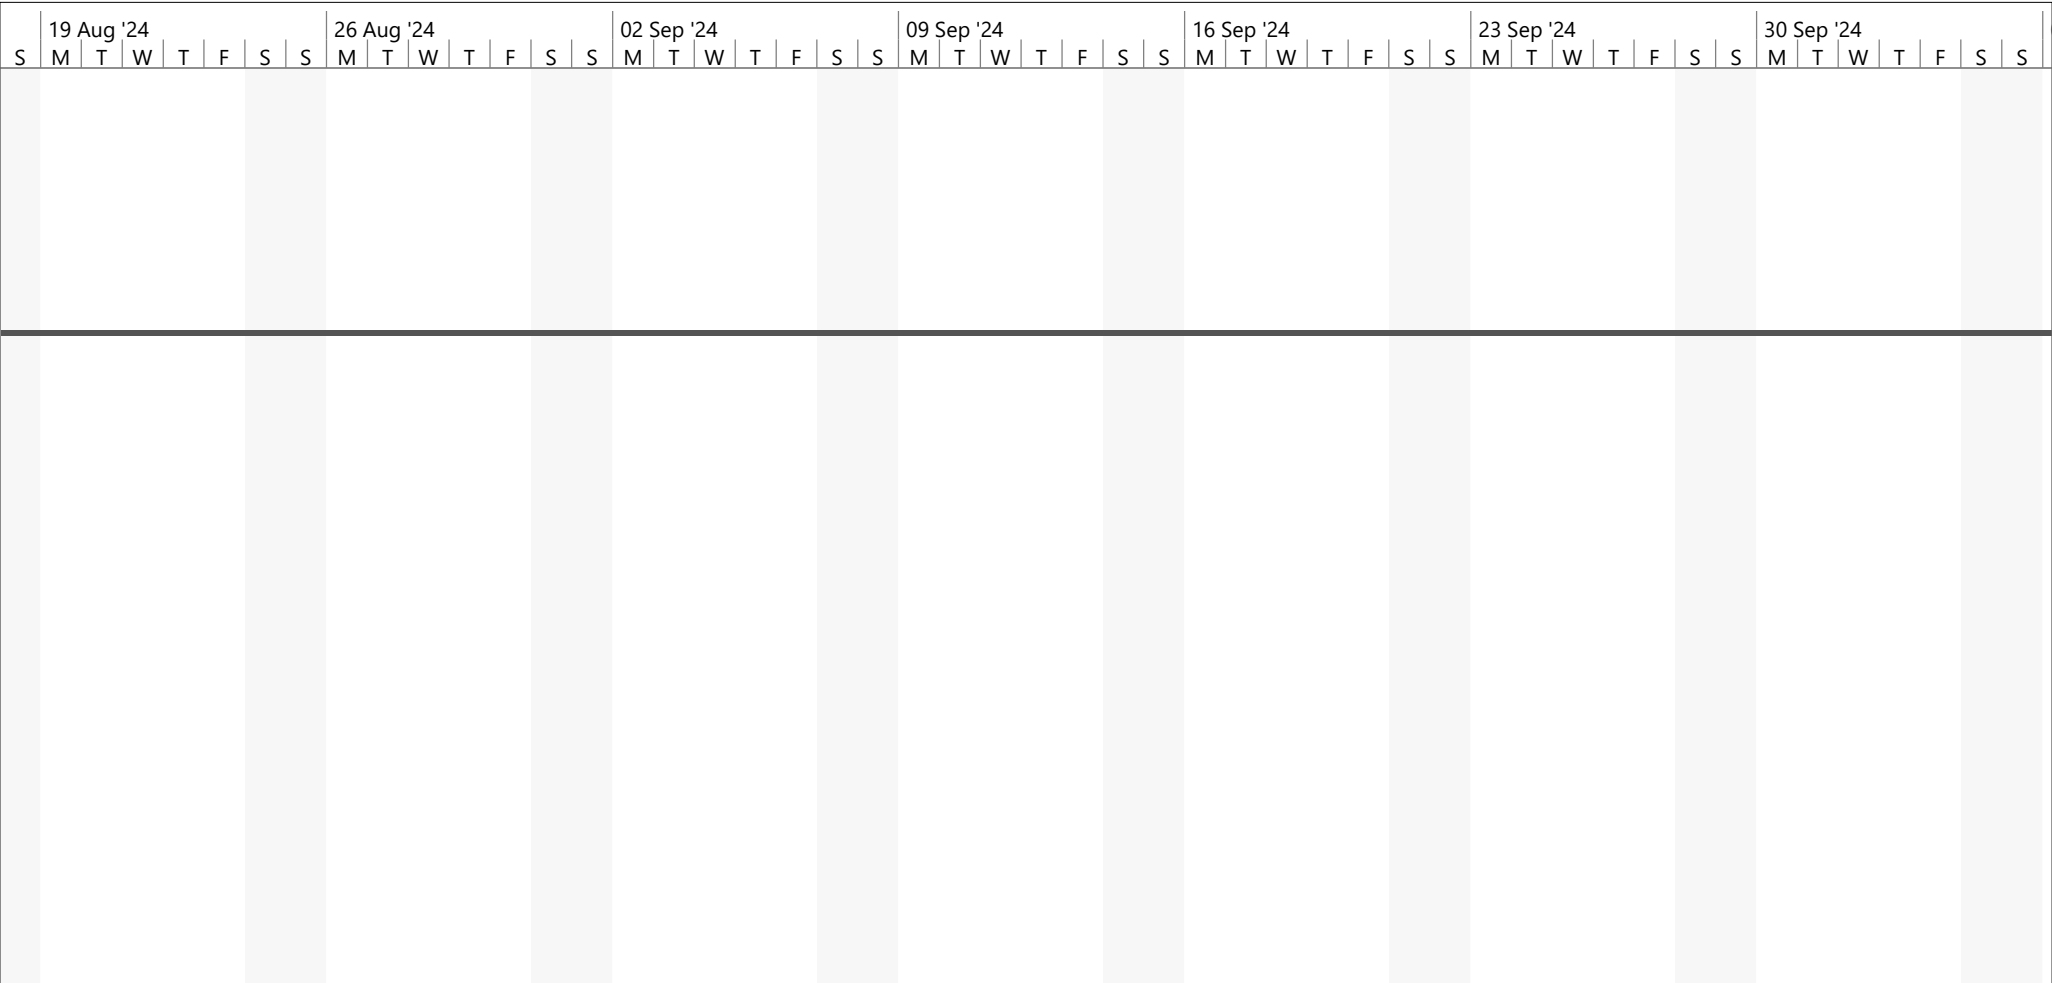

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone

Deadline


Progress

Manual Progress

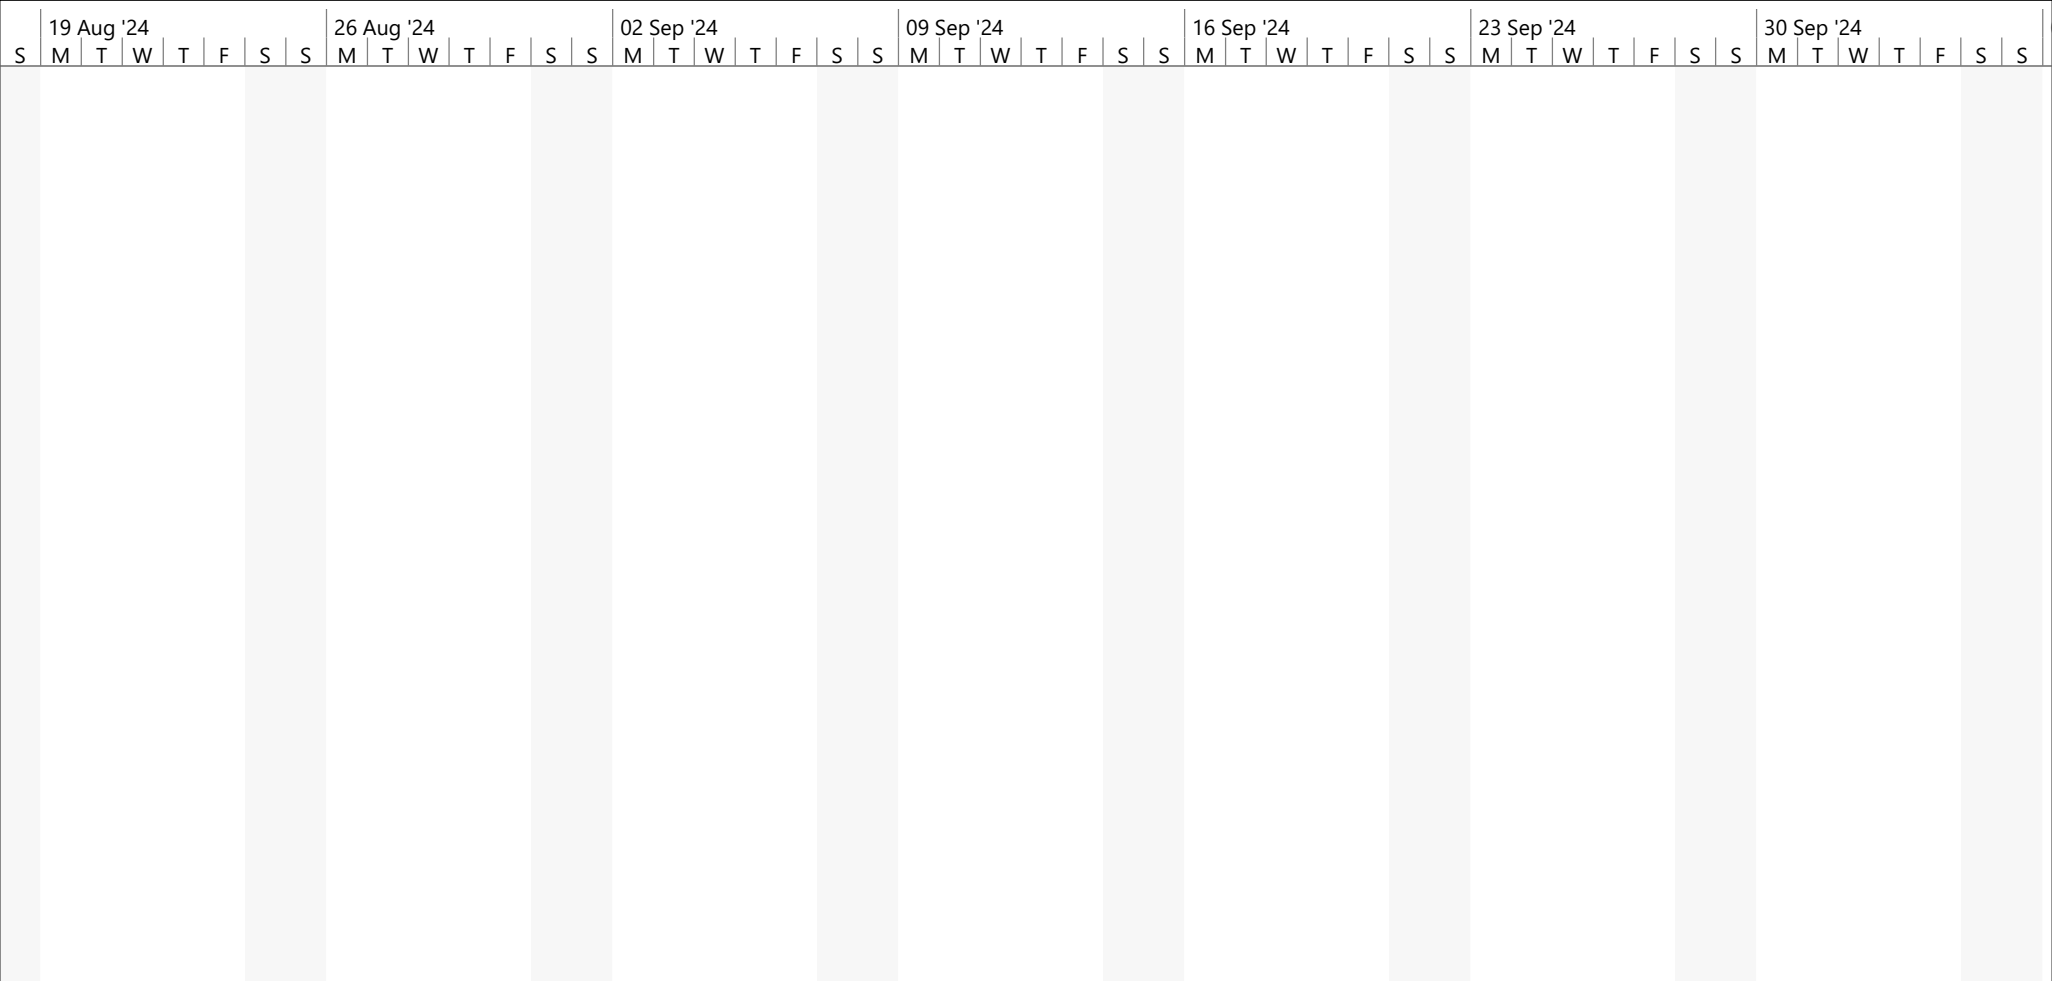


Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

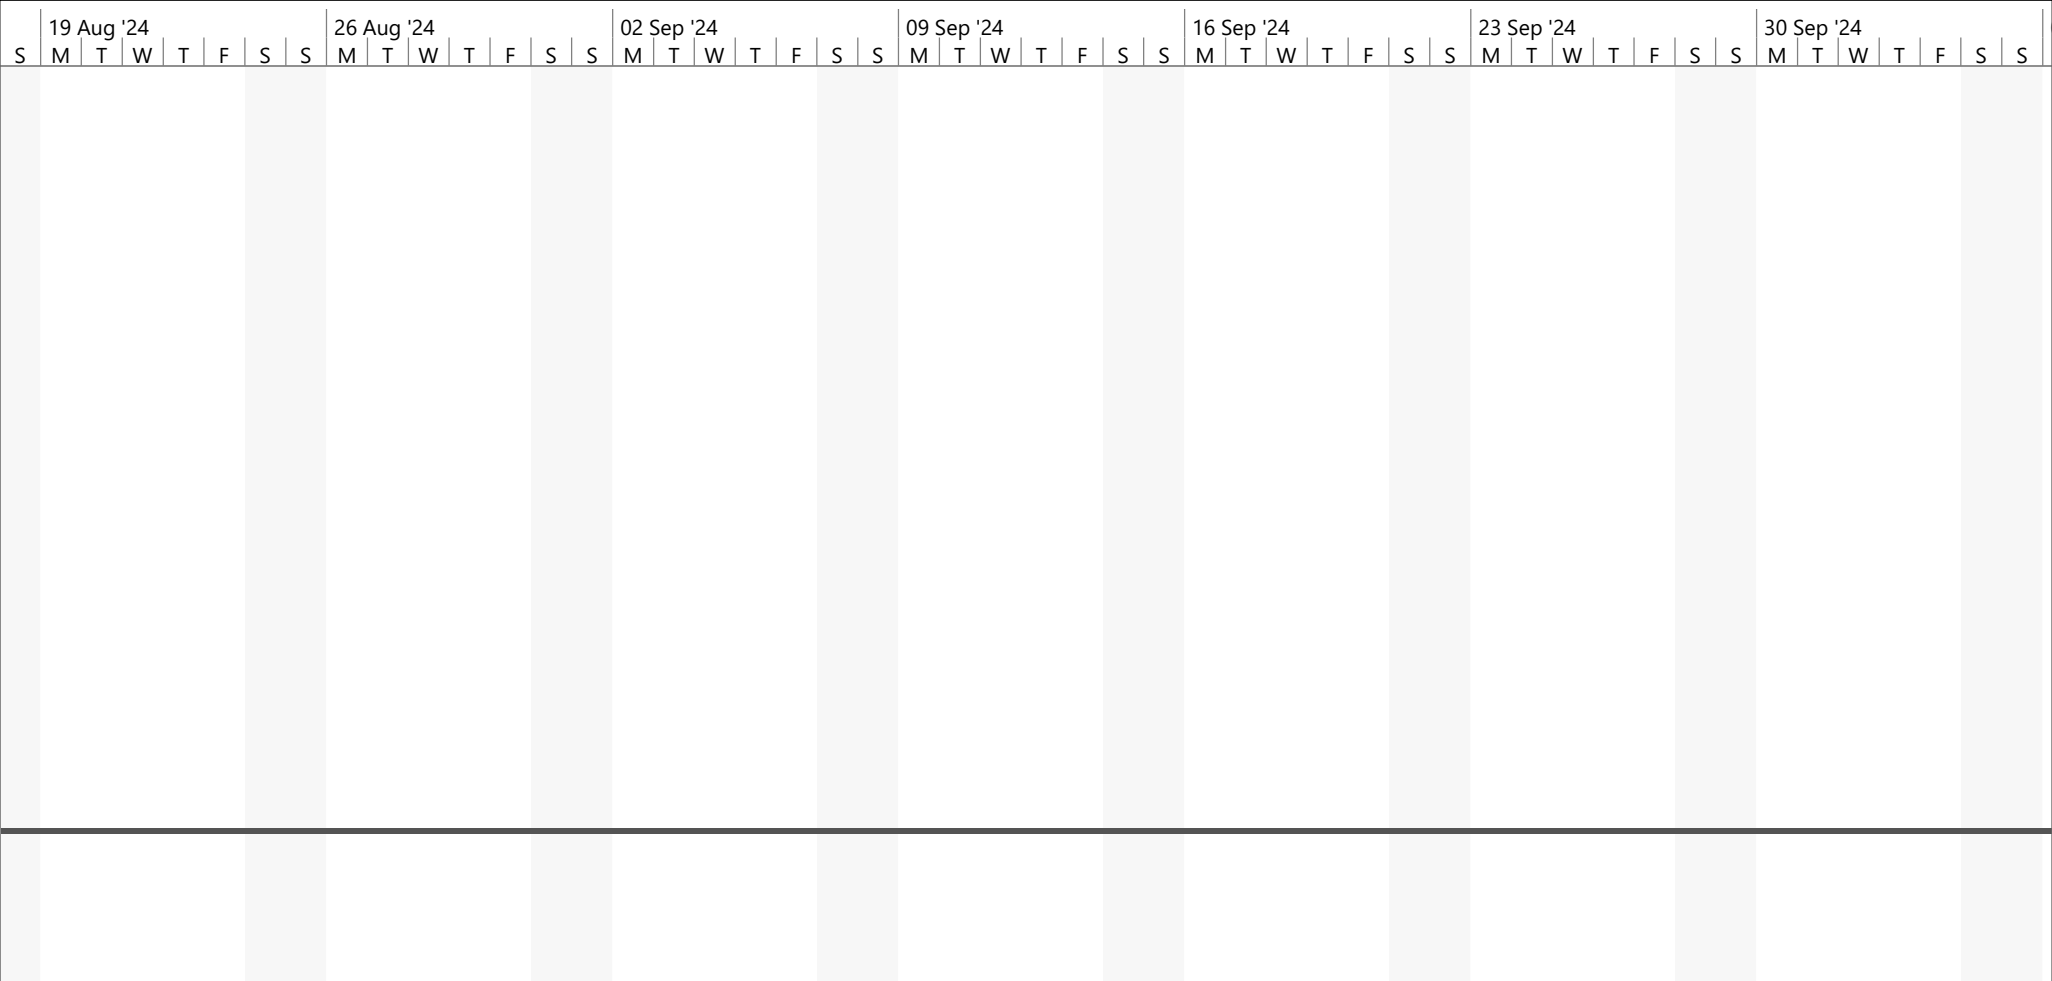


Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

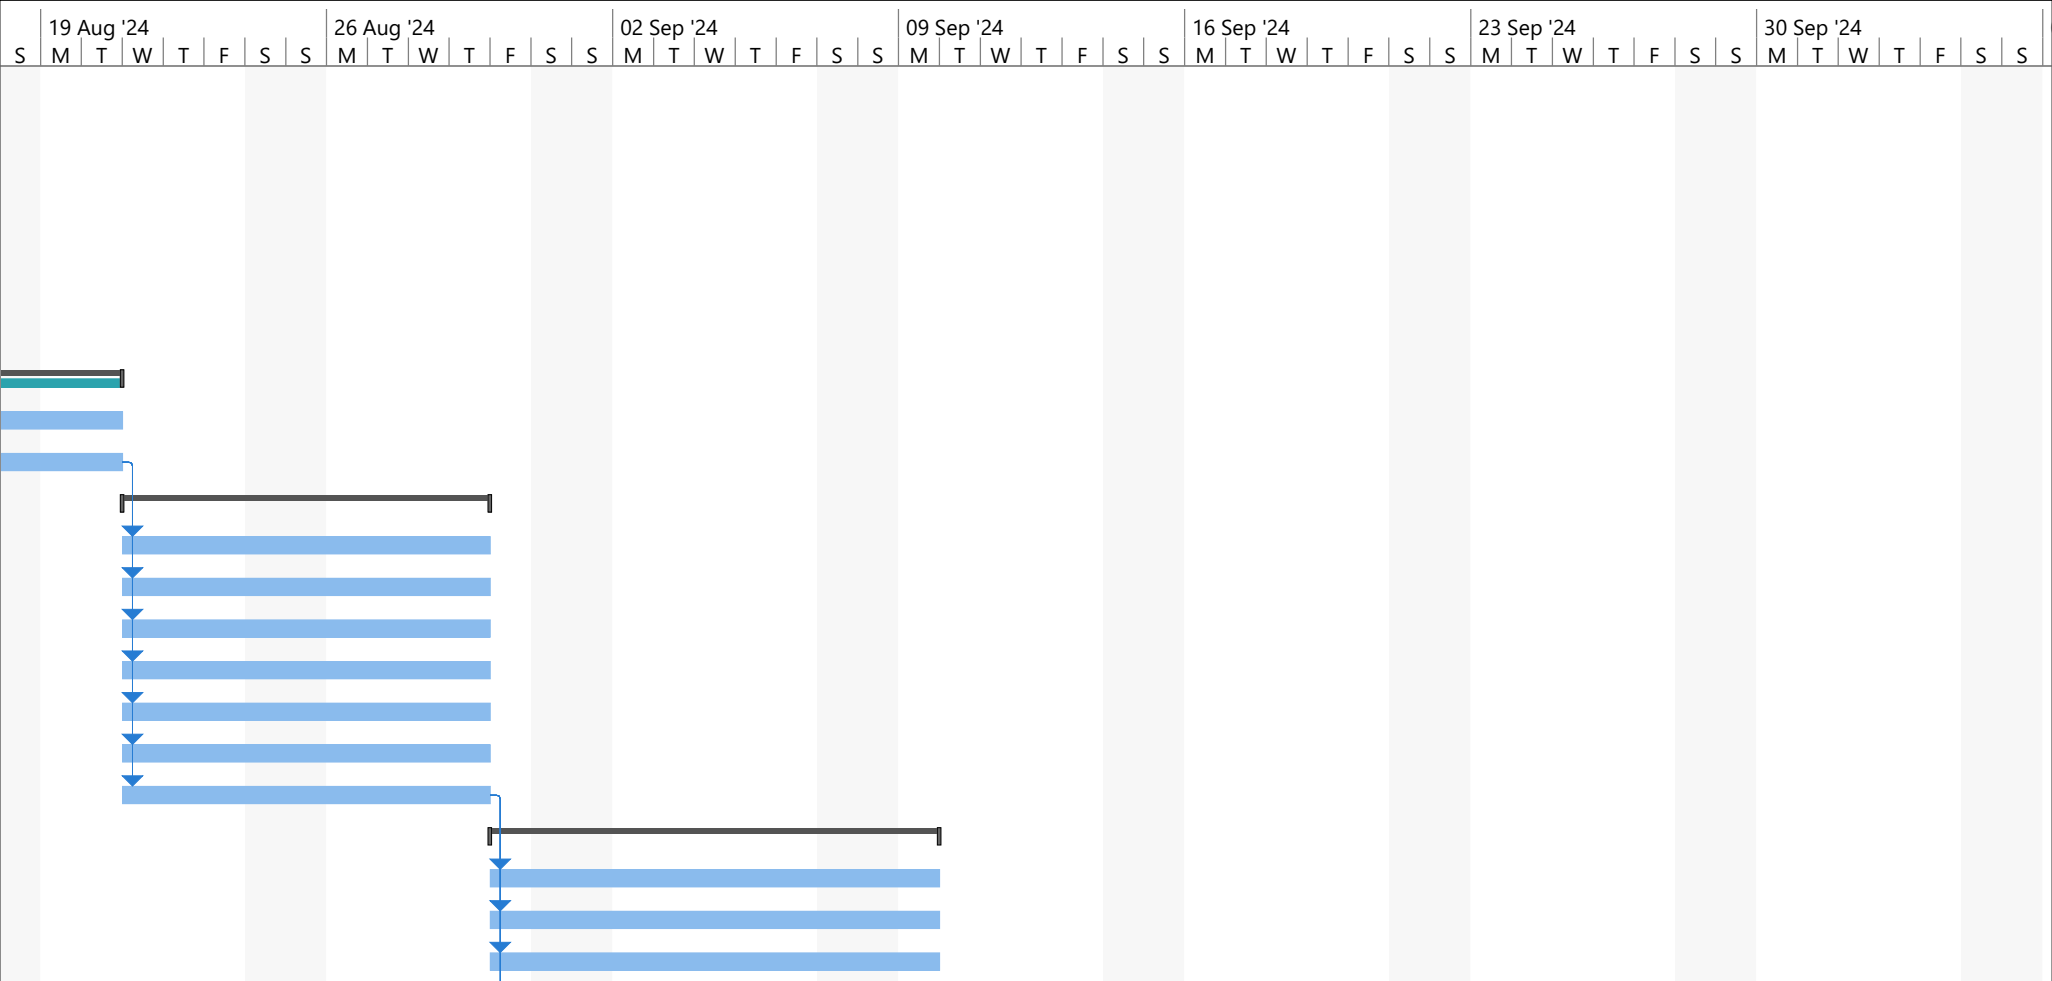

Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

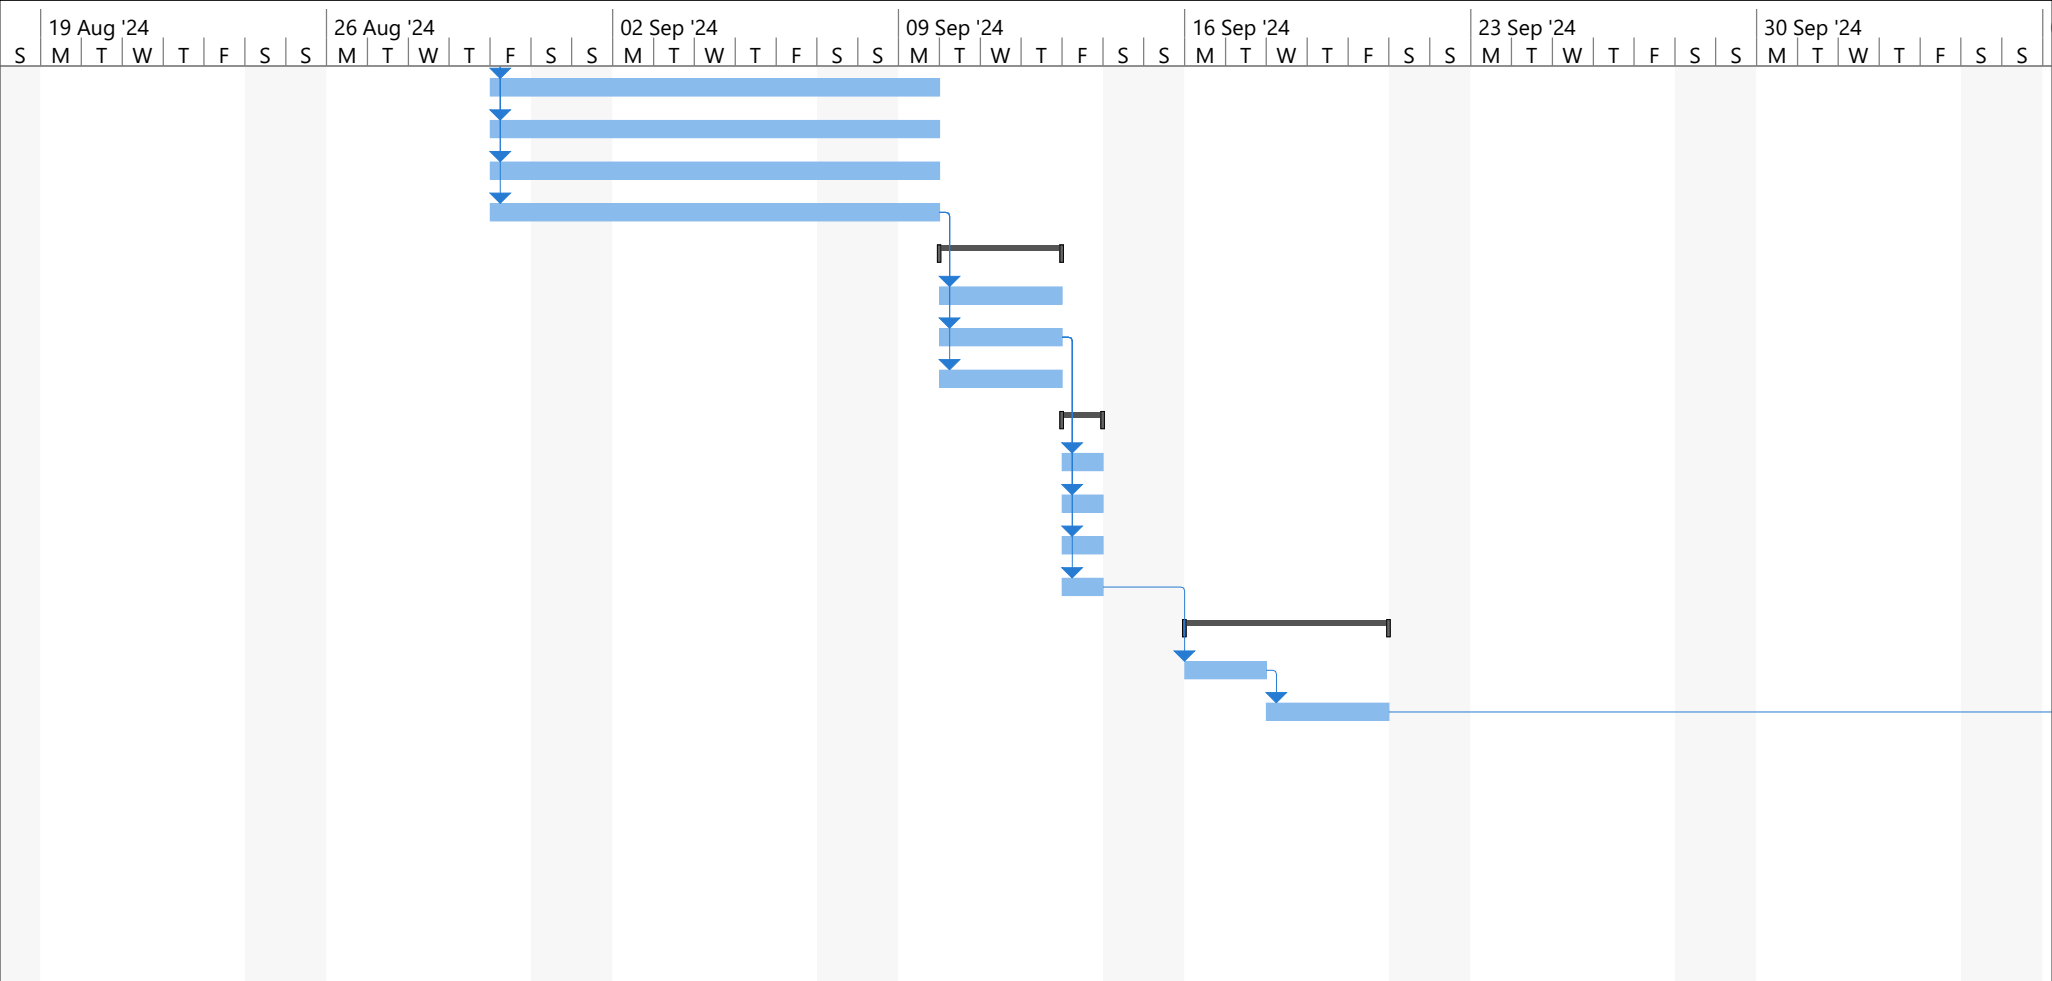



Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


19 Aug '24							26 Aug '24							02 Sep '24							09 Sep '24							16 Sep '24							23 Sep '24							30 Sep '24						
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S						




Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

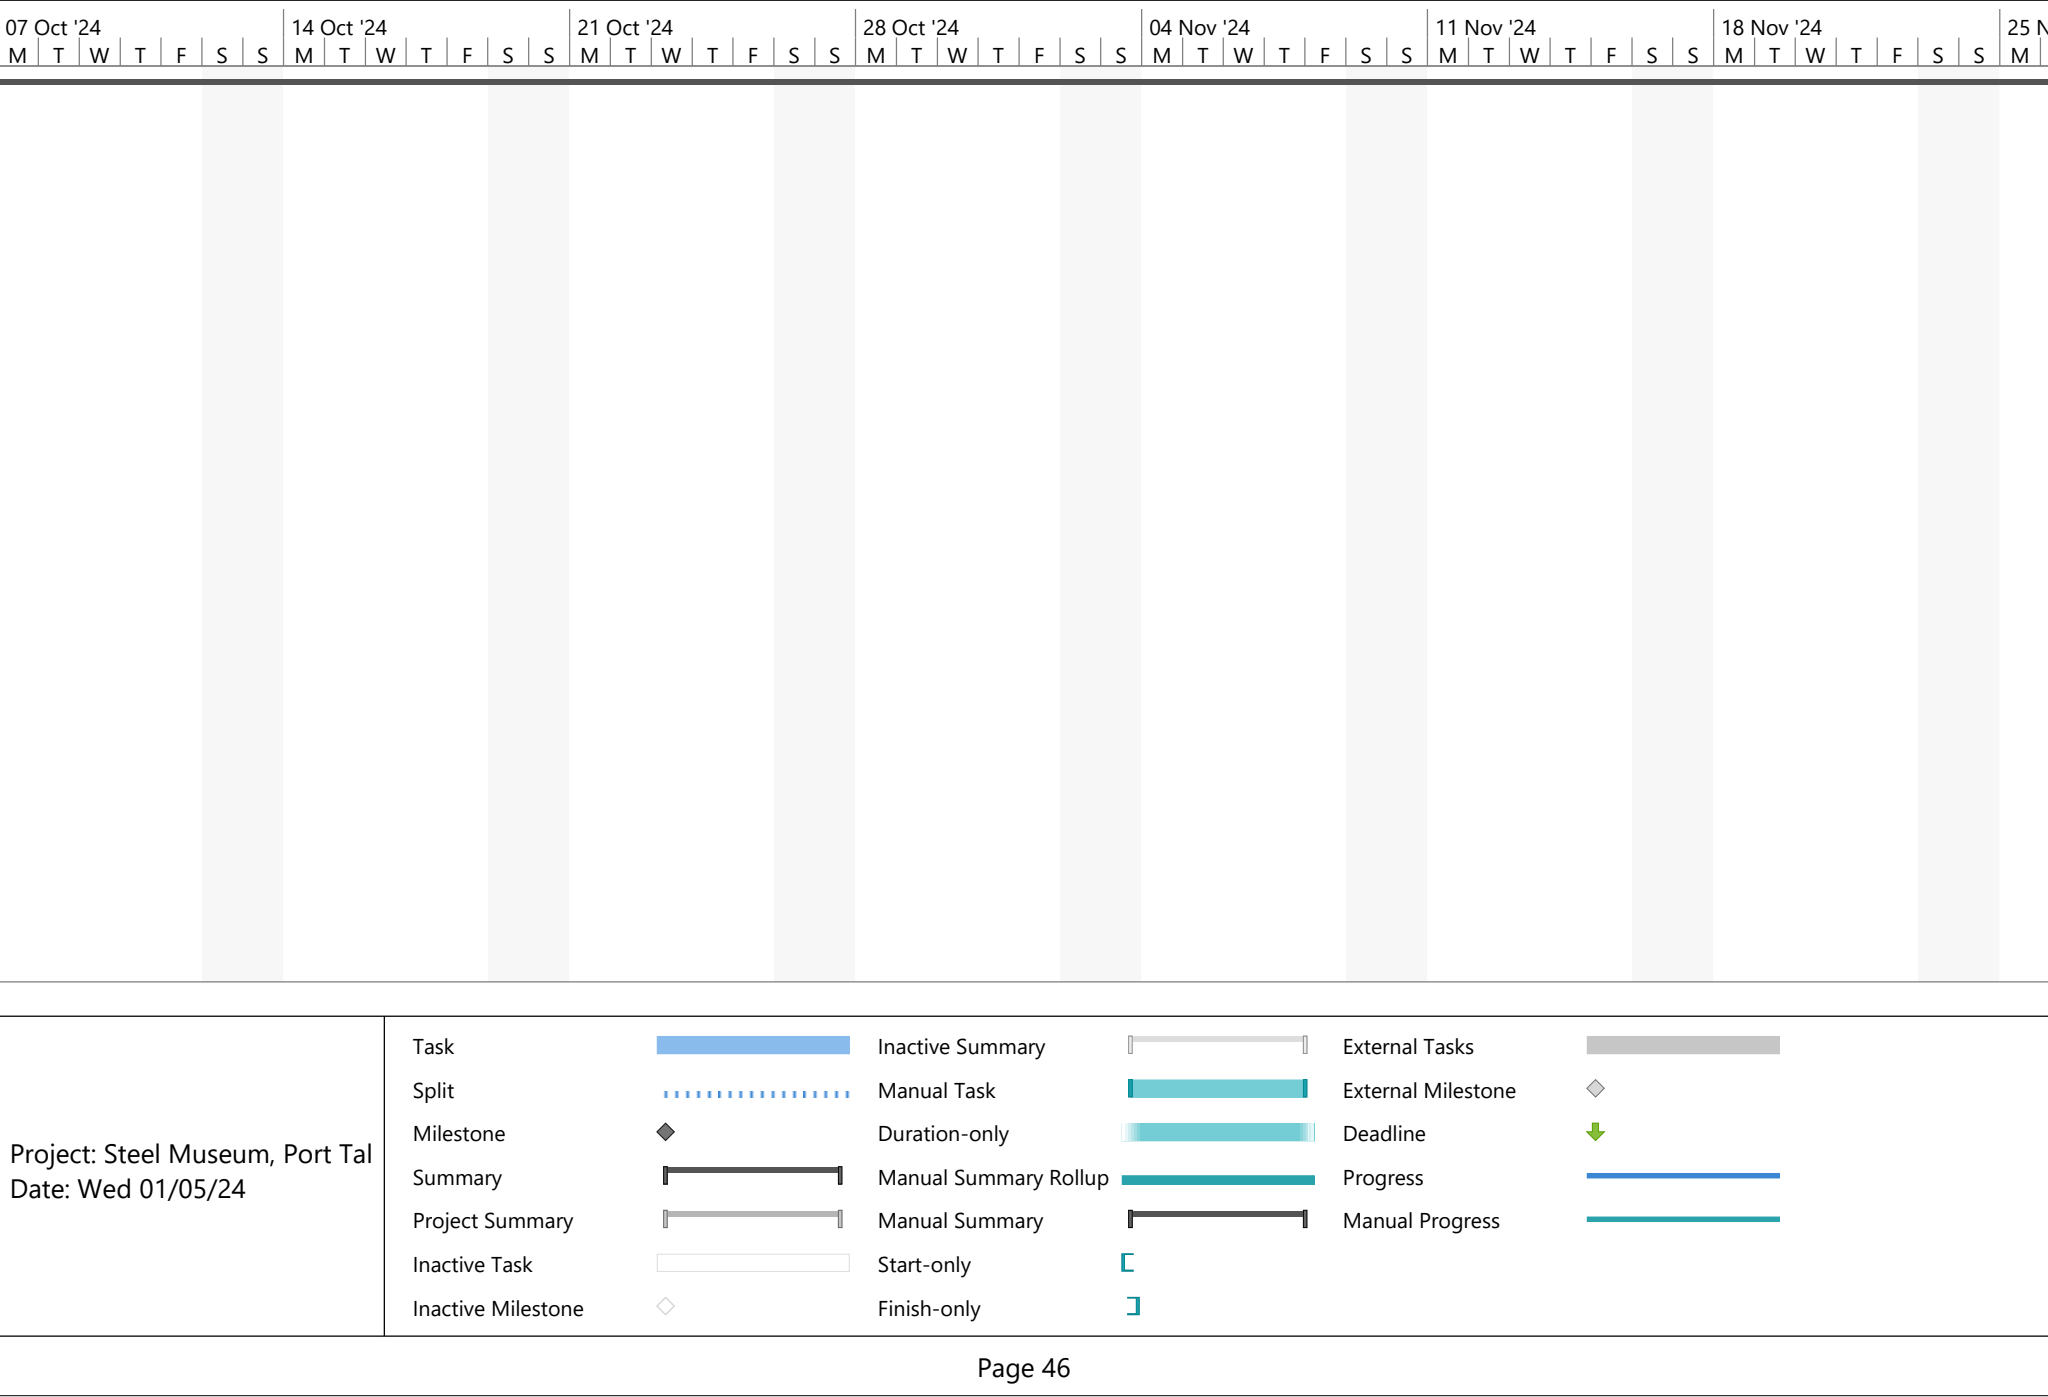

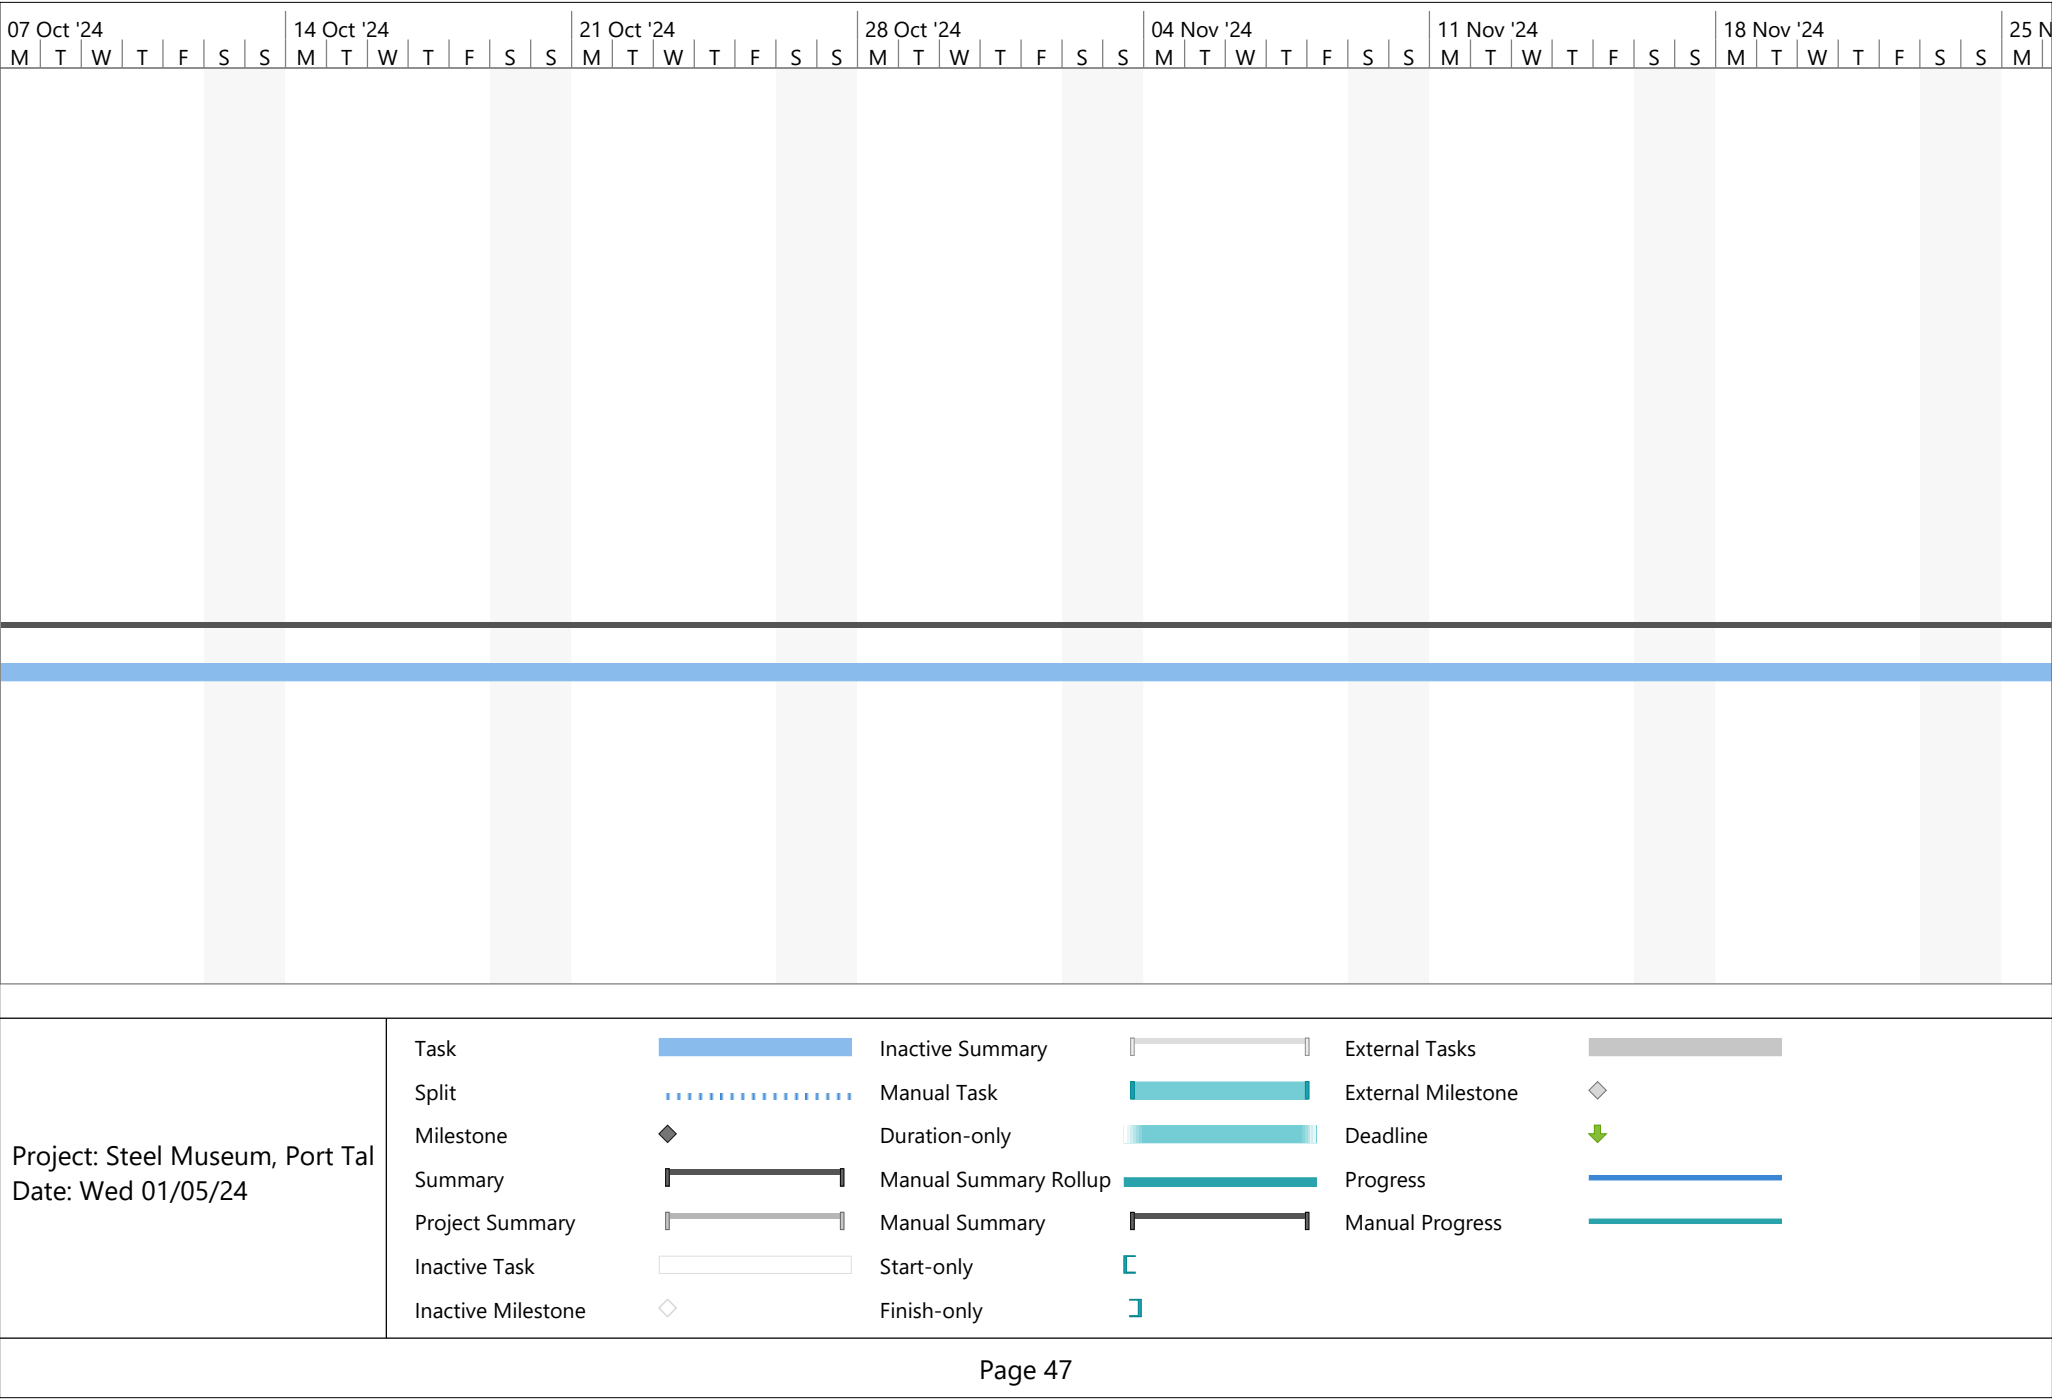

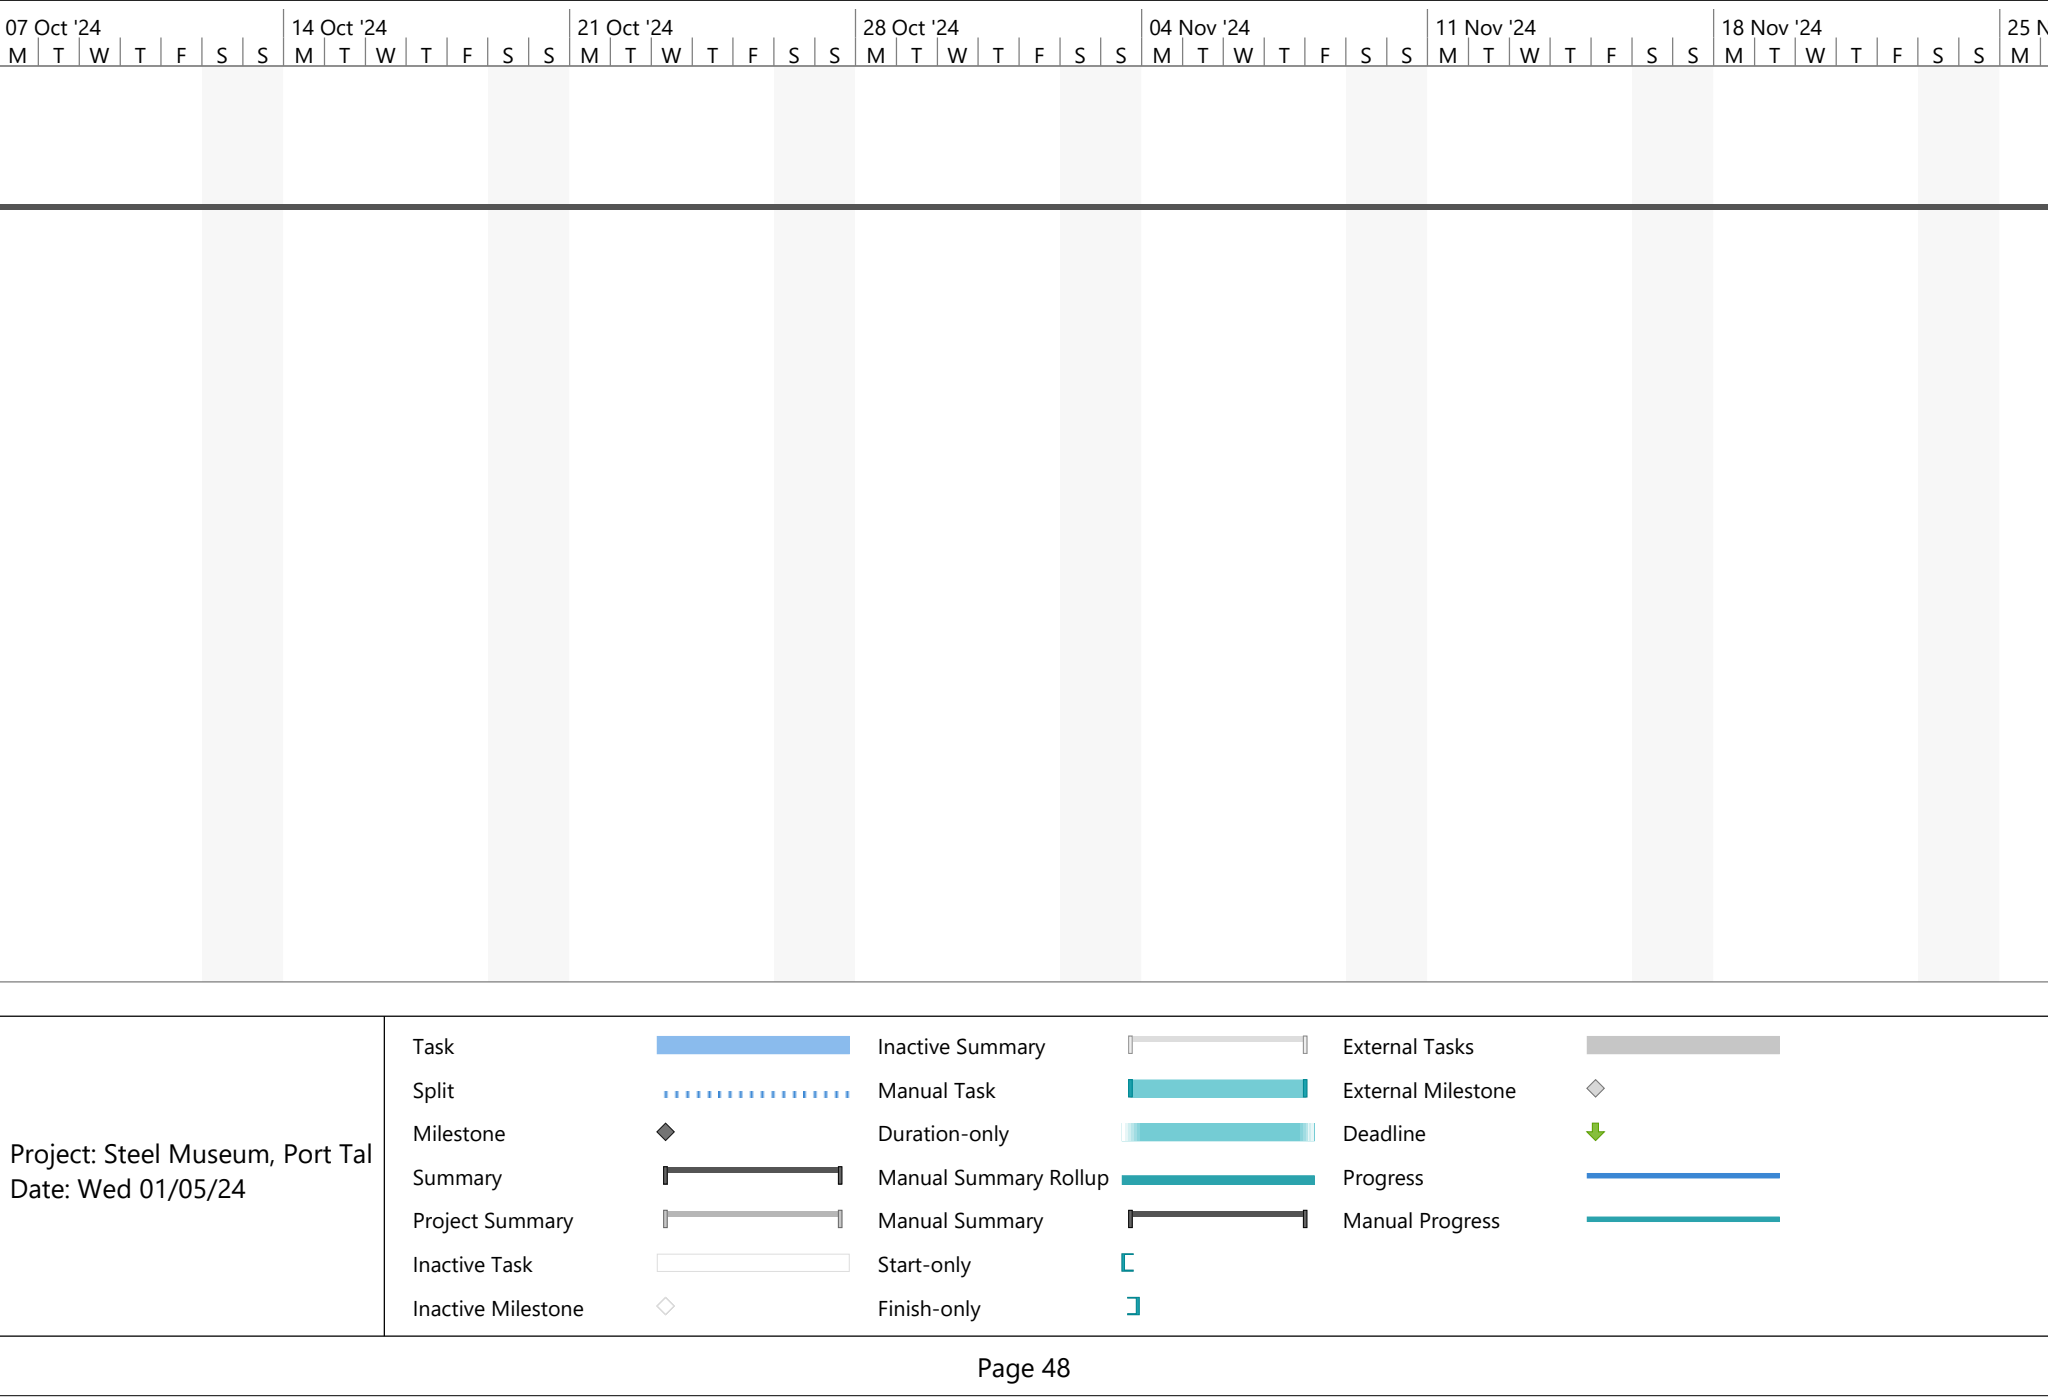

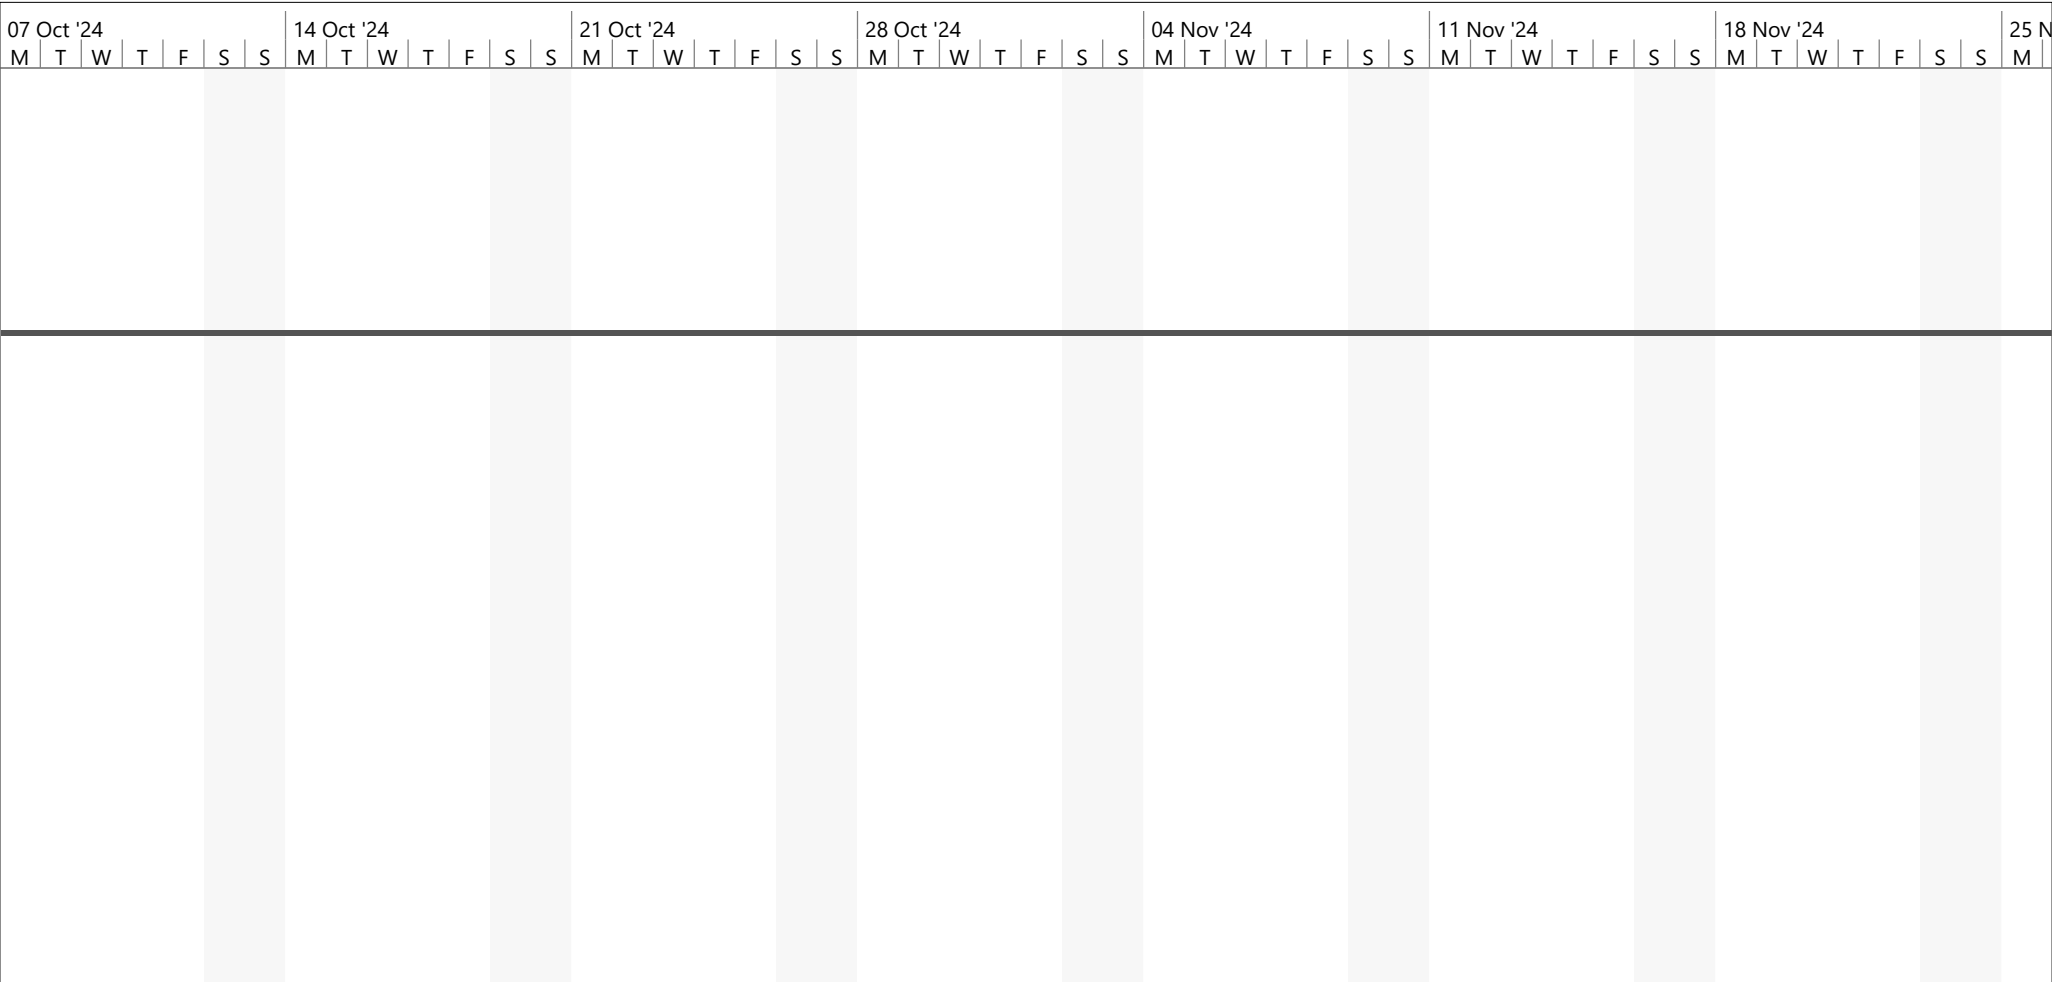

Project: Steel Museum, Port Talbot
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 49

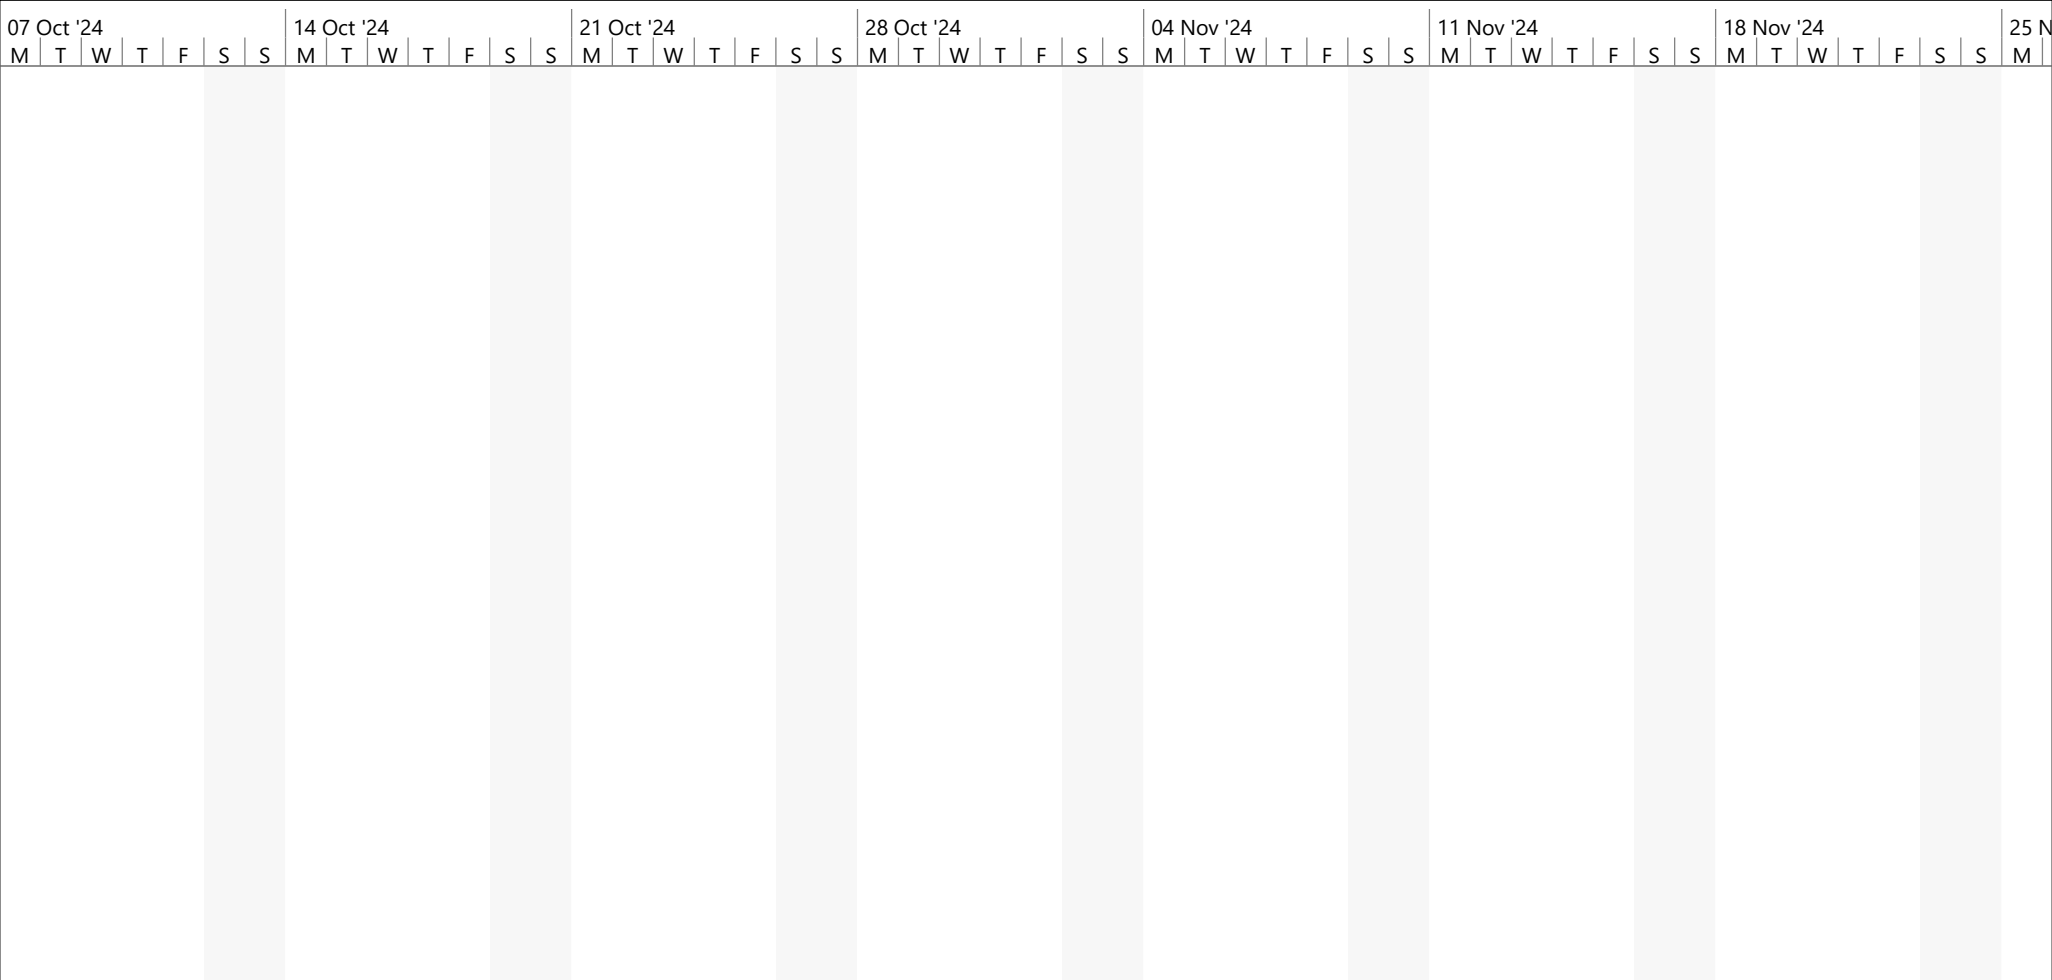

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone


Deadline

Progress

Manual Progress

Page 50

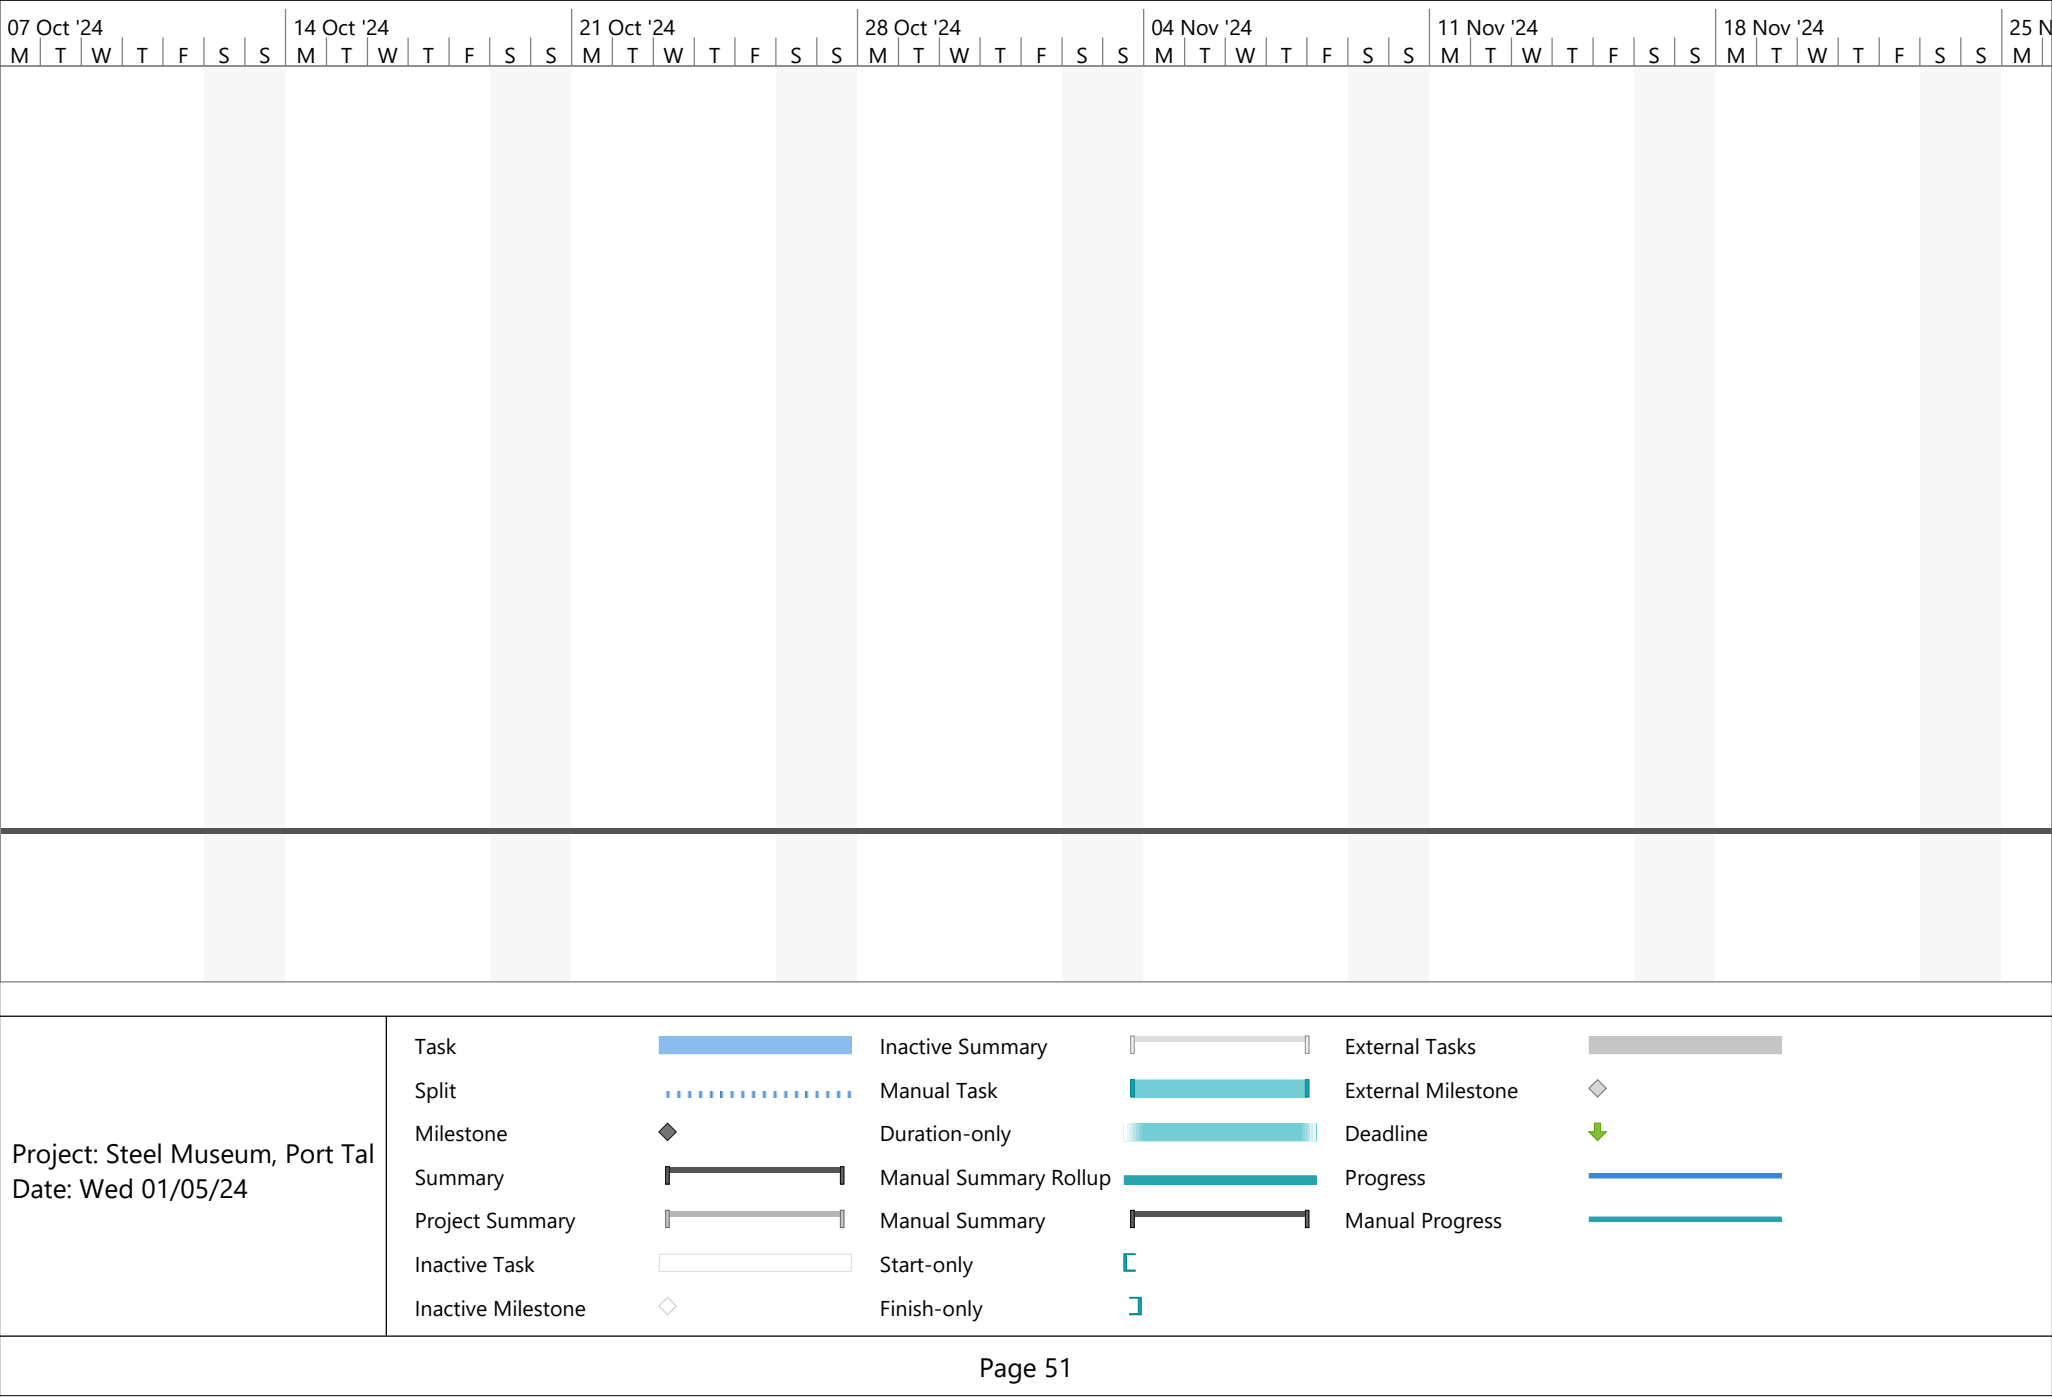

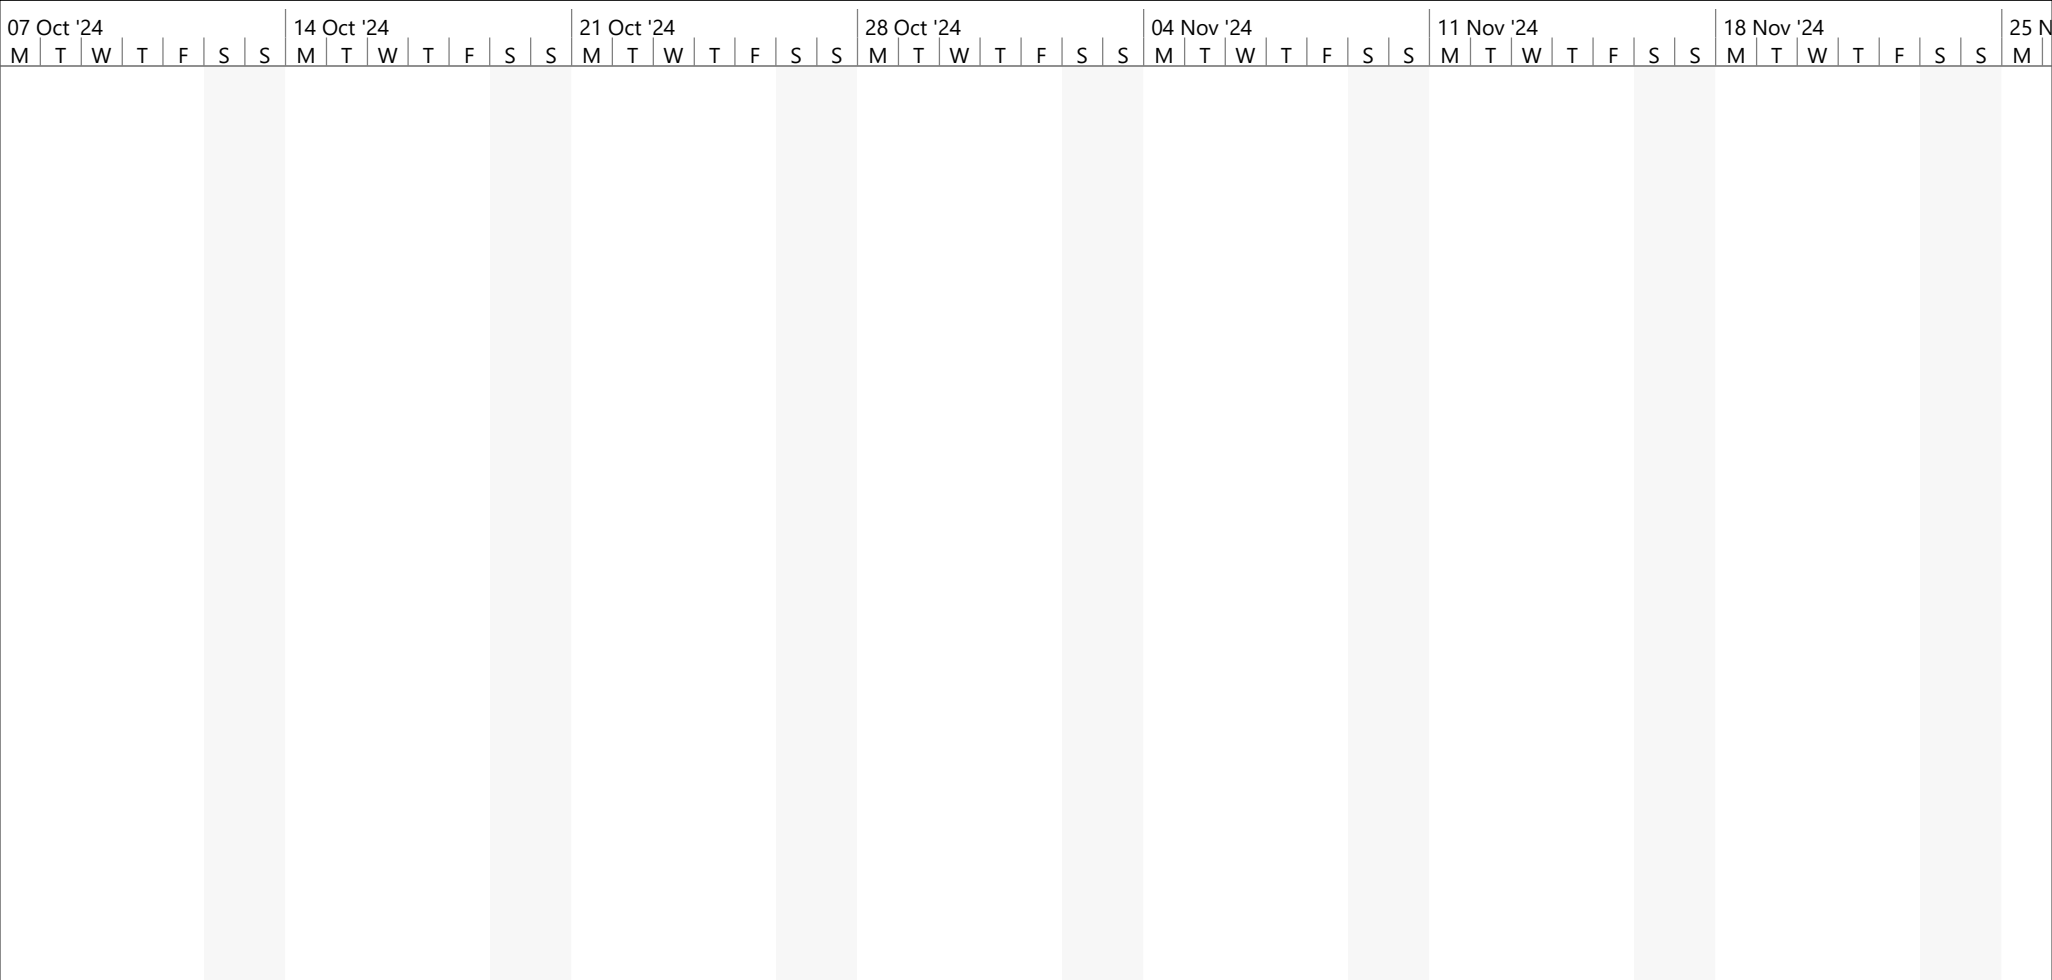

Project: Steel Museum, Port Tal

Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Nov '24

T

W

T

F

S

S

02 Dec '24

M

T

W

T

F

S

S

09 Dec '24

M

T

W

T

F

S

S

16 Dec '24

M

T

W

T

F

S

S

23 Dec '24

M

T

W

T

F

S

S

30 Dec '24

M

T

W

T

F

S

S

06 Jan '25

M

T

W

T

F

S

S

13 Jan '25

M

T

Project: Steel Museum, Port Talbot

Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 55

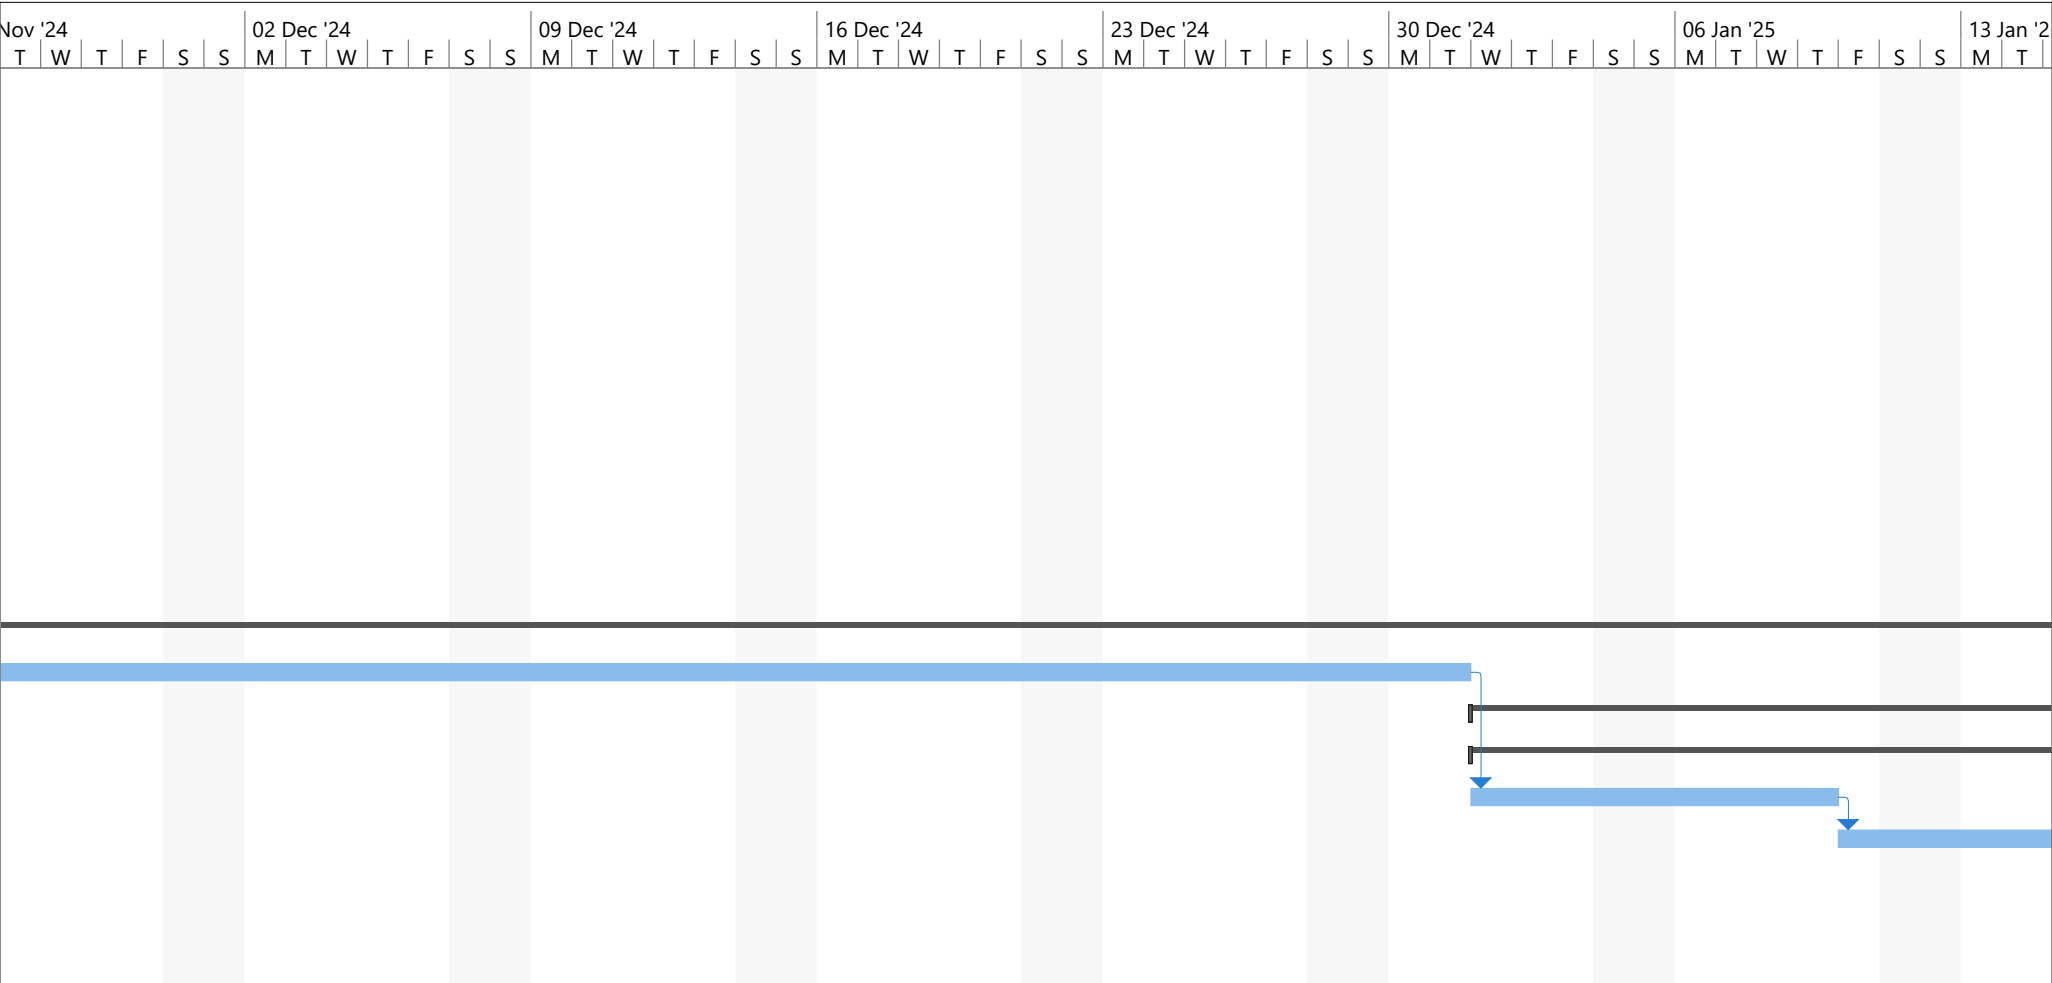

Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Nov '24

T

W

T

F

S

S

02 Dec '24

M

T

W

T

F

S

S

09 Dec '24

M

T

W

T

F

S

S

16 Dec '24

M

T

W

T

F

S

S

23 Dec '24

M

T

W

T

F

S

S

30 Dec '24

M

T

W

T

F

S

S

06 Jan '25

M

T

W

T

F

S

S

13 Jan '25

M

T

Project: Steel Museum, Port Talbot

Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 57

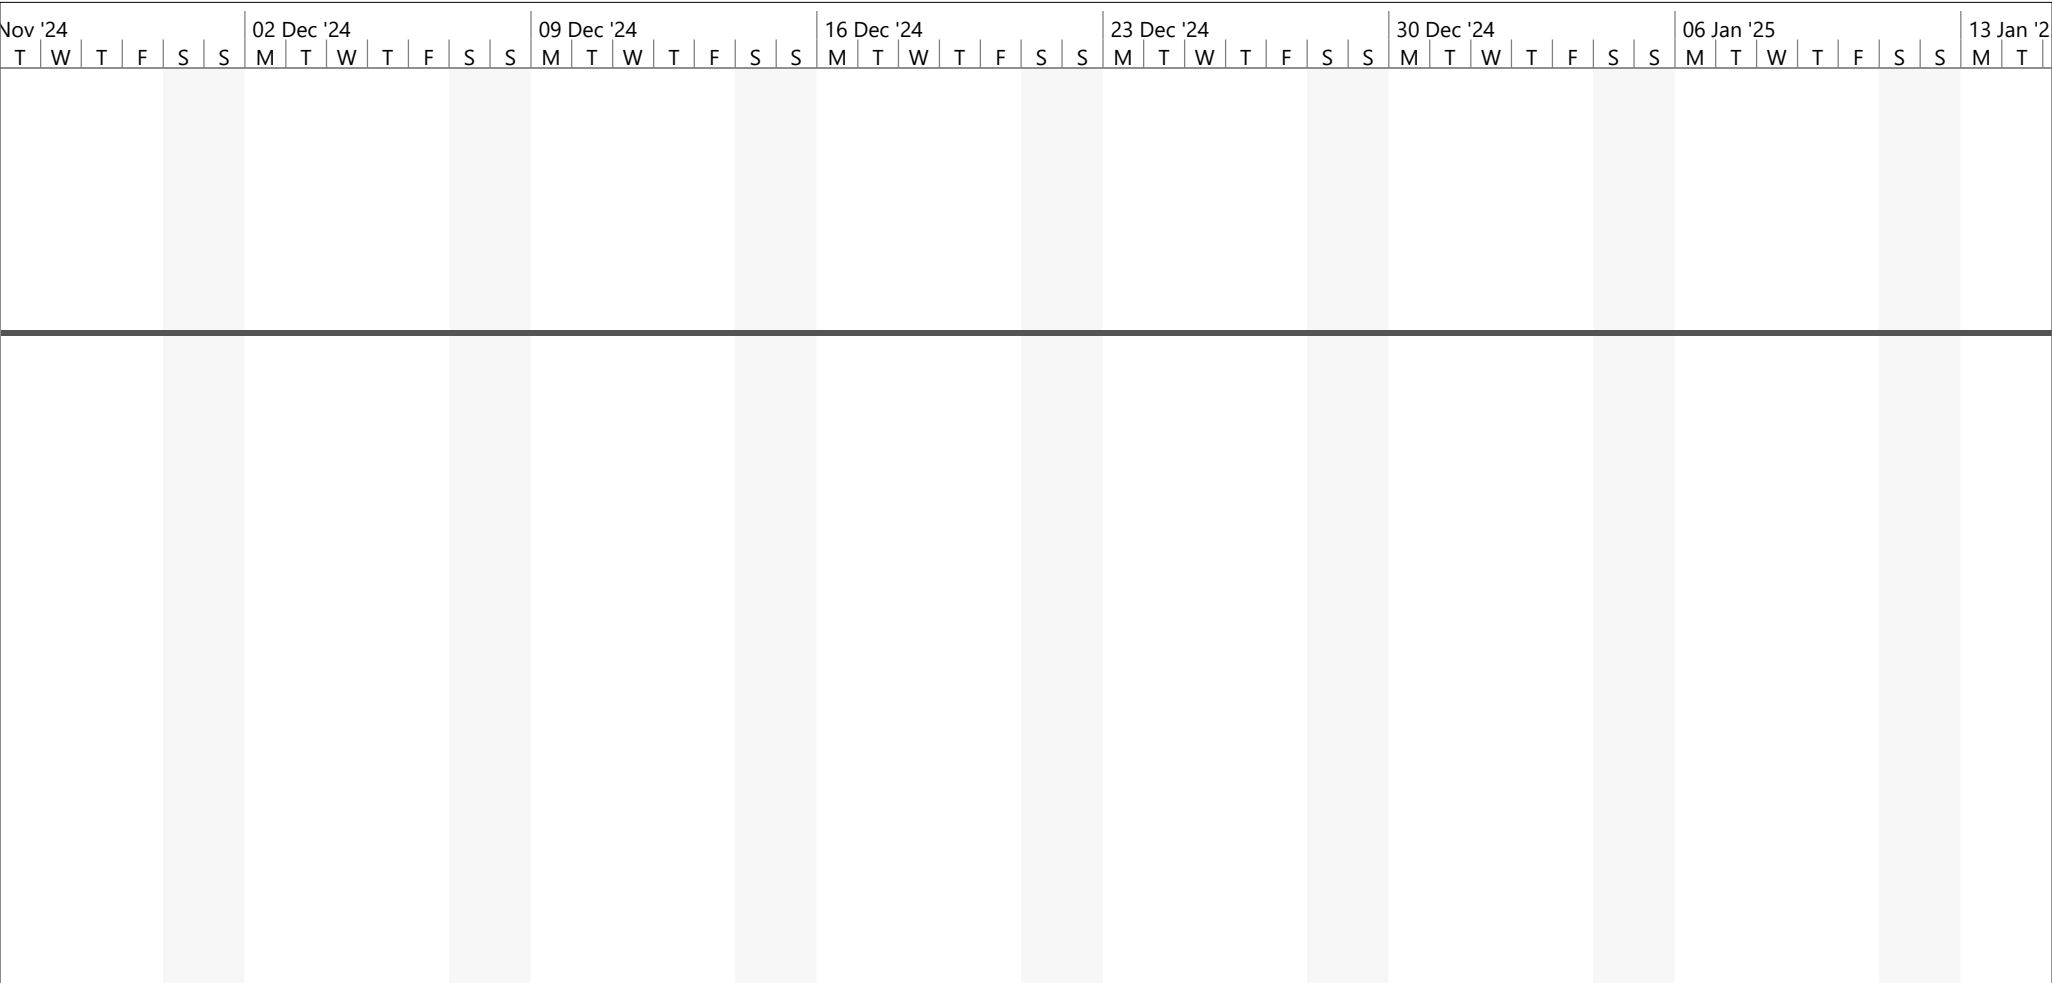

Project: Steel Museum, Port Talbot
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline


Progress

Manual Progress

Page 58

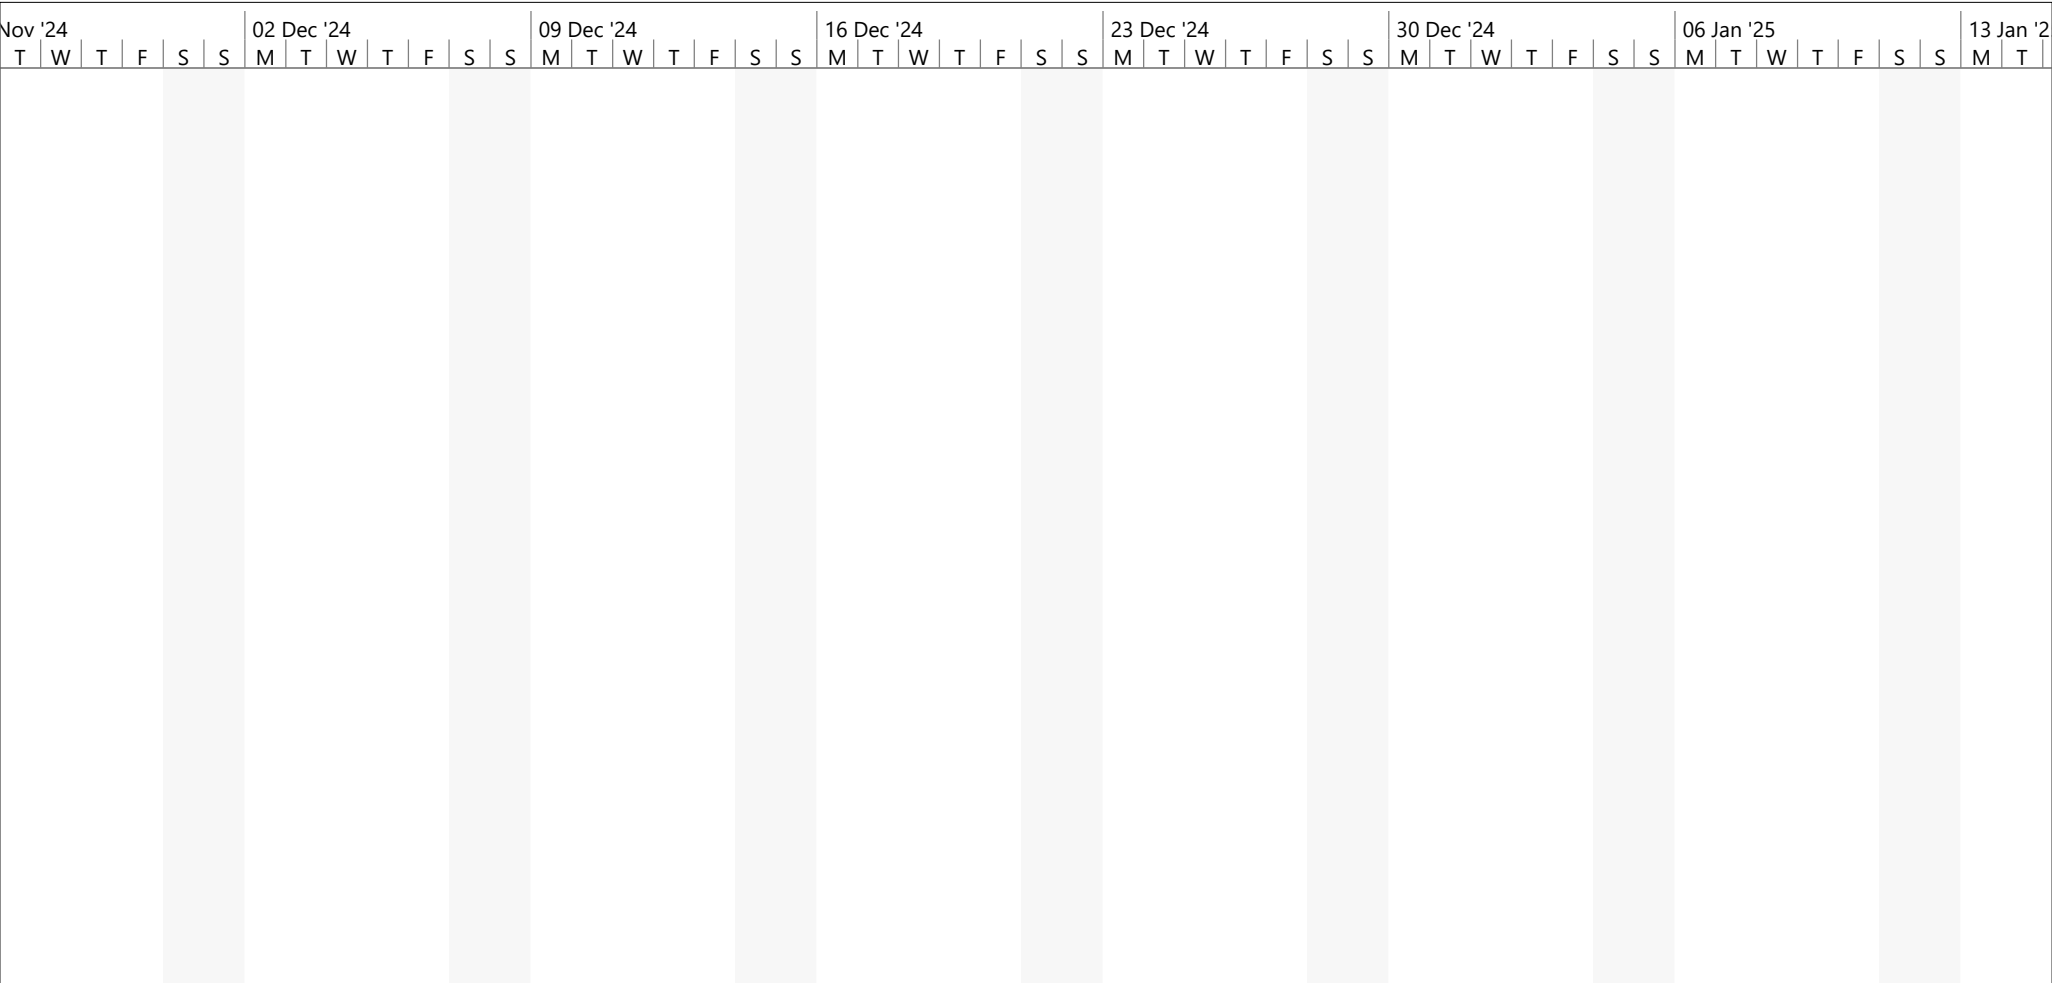

Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

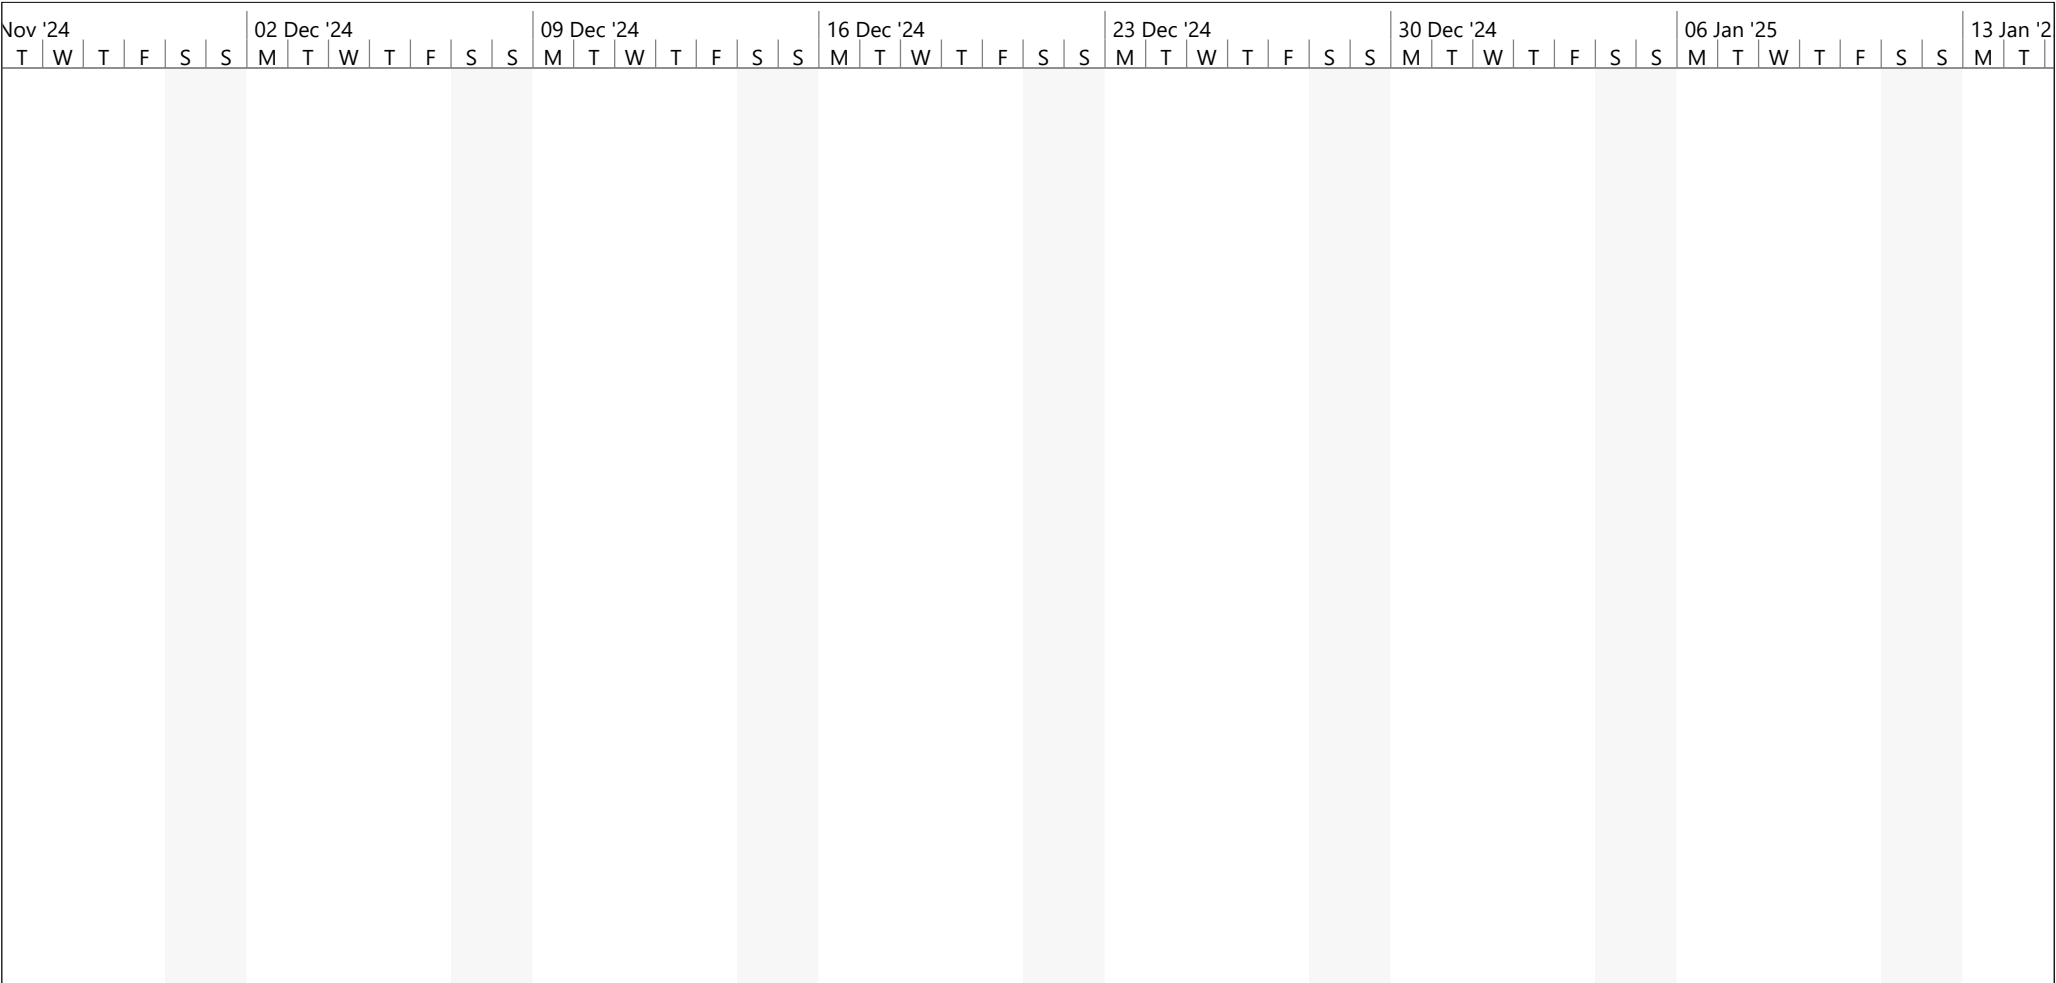

Project: Steel Museum, Port Talbot

Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone


Deadline

Progress


Manual Progress

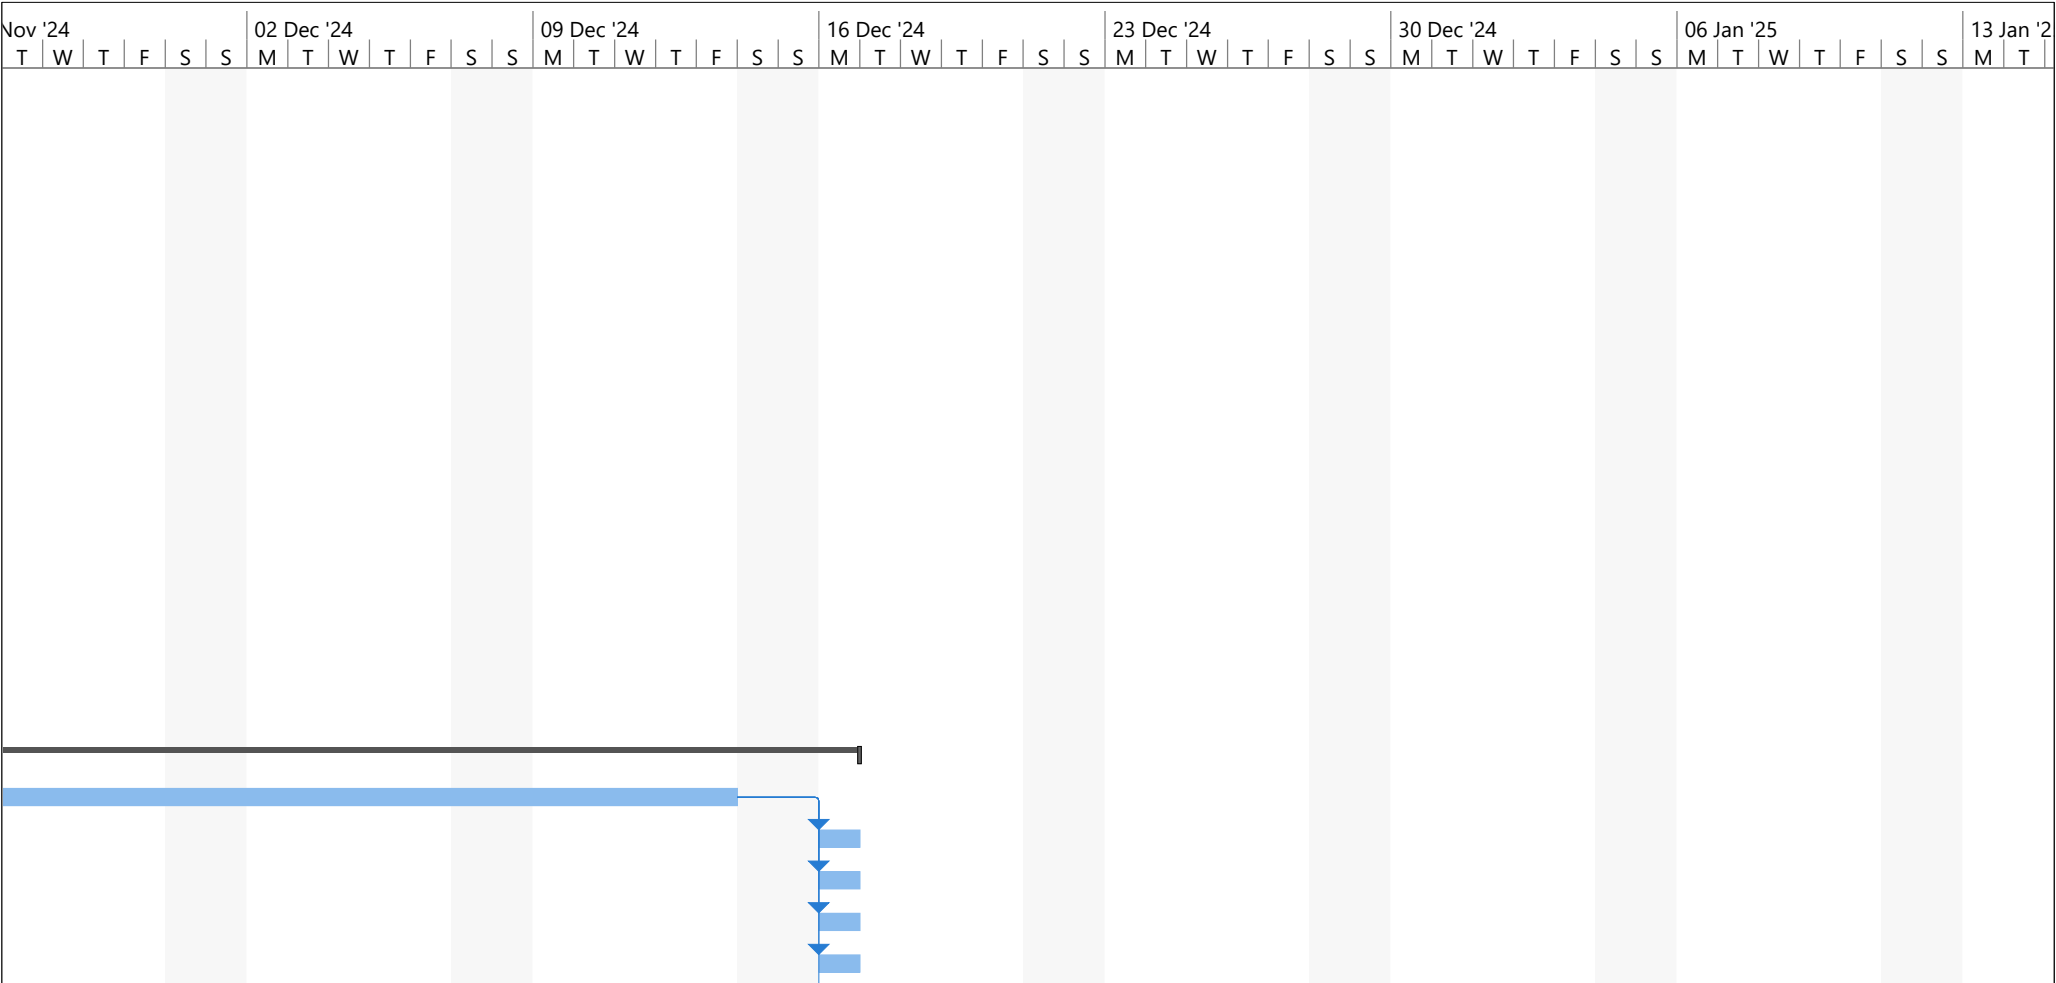

Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

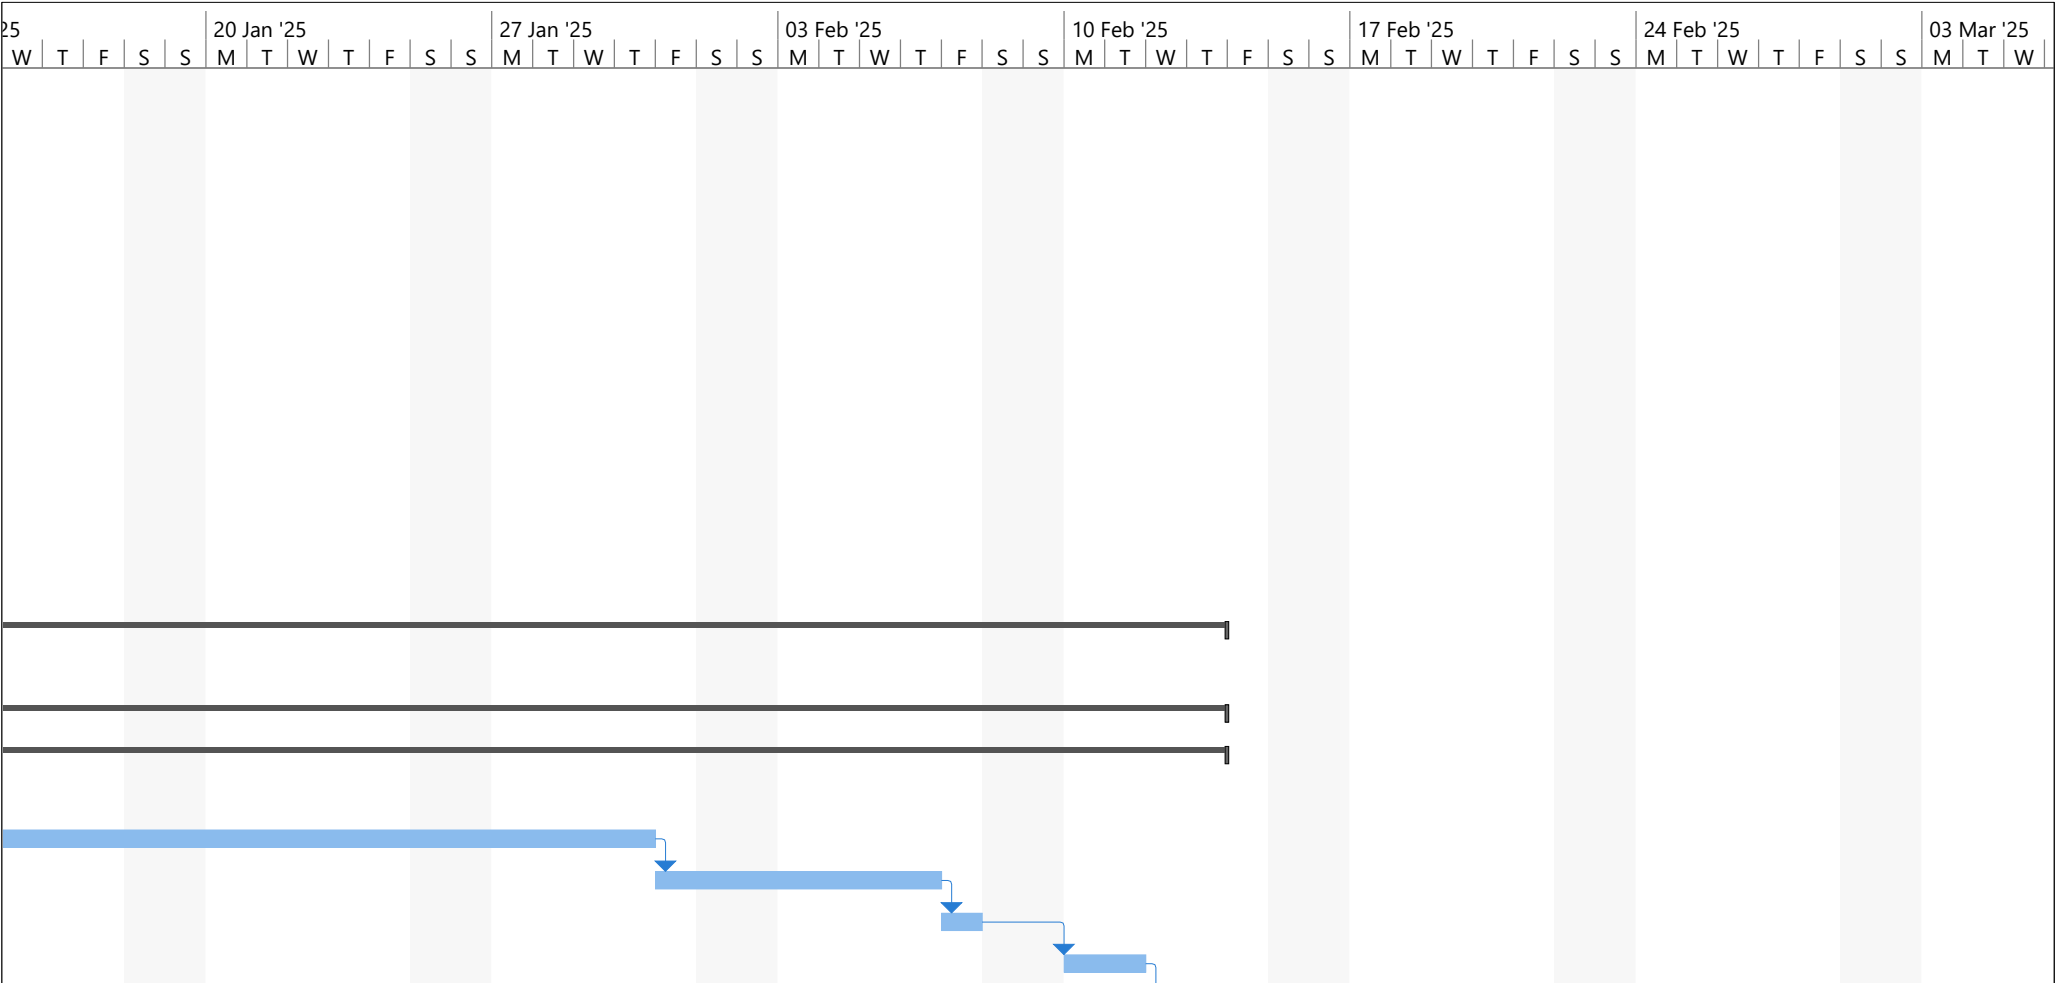


Project: Steel Museum, Port Talbot Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

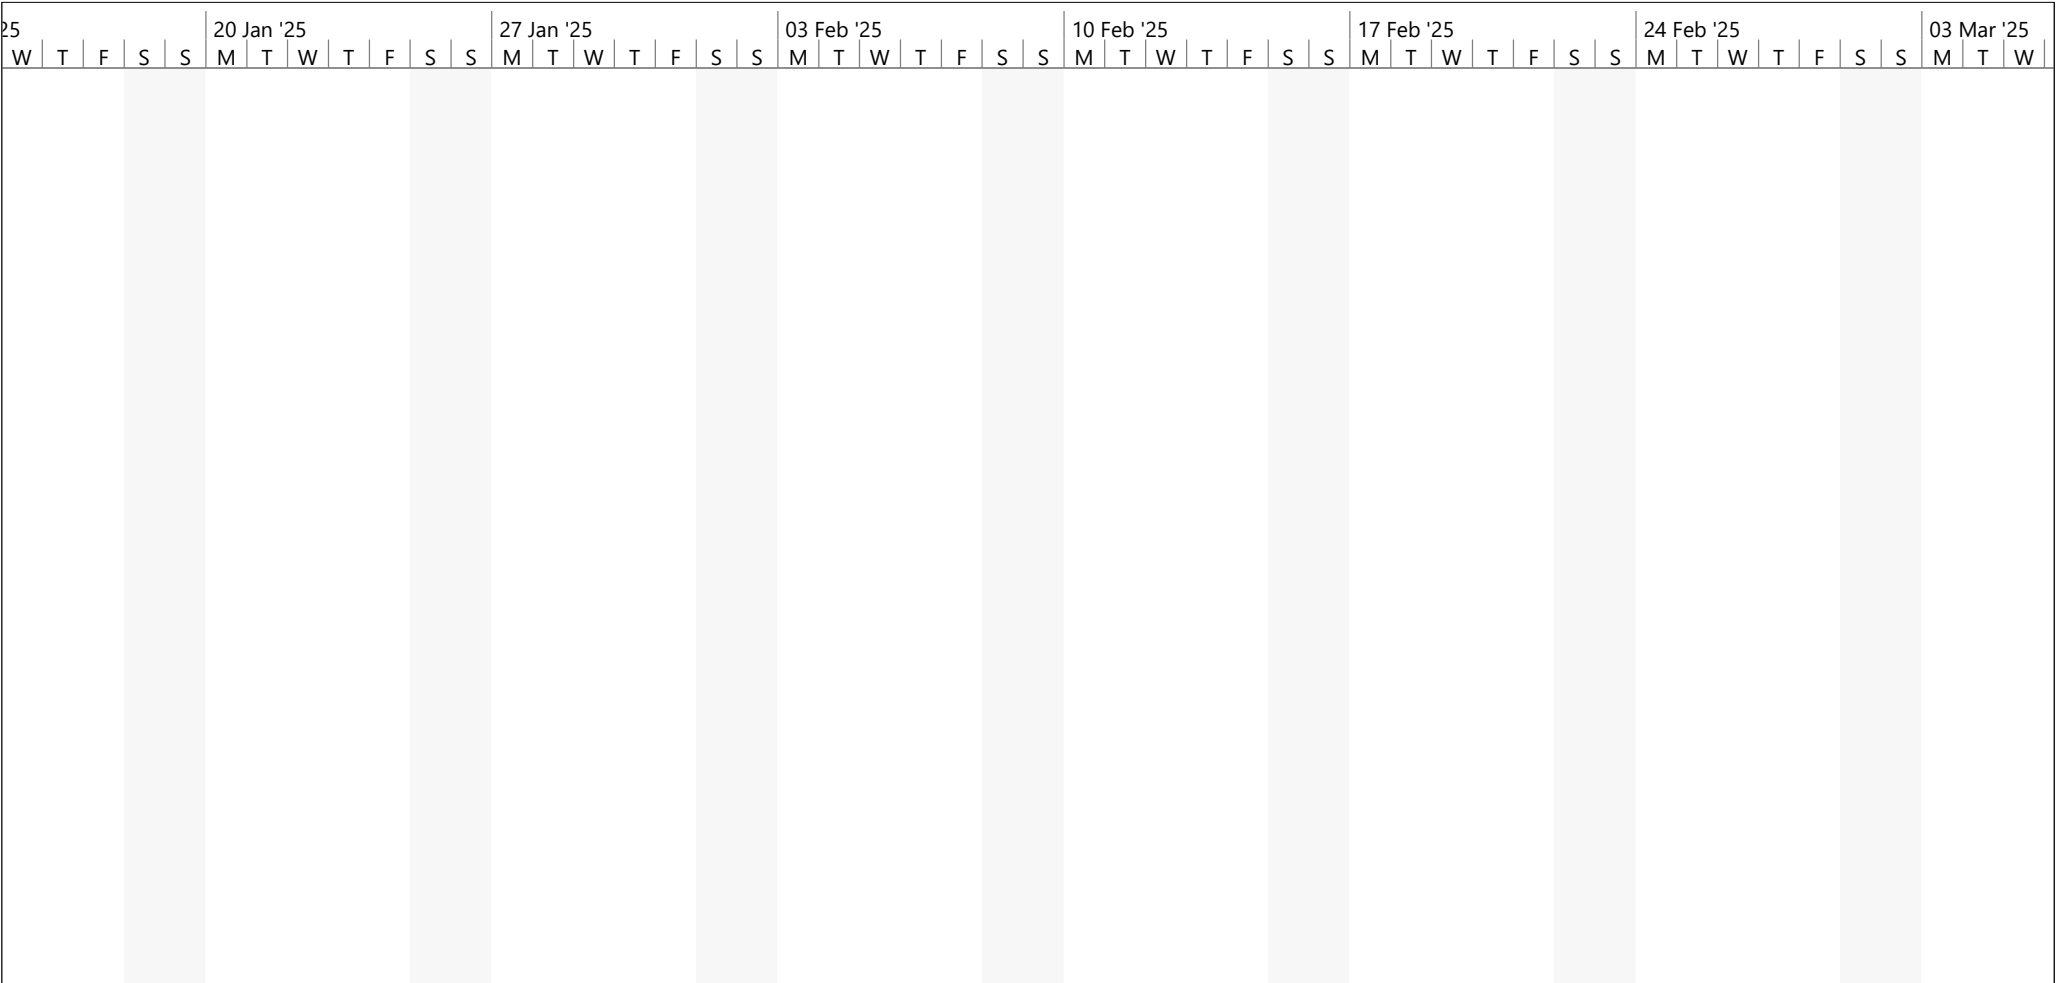


Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

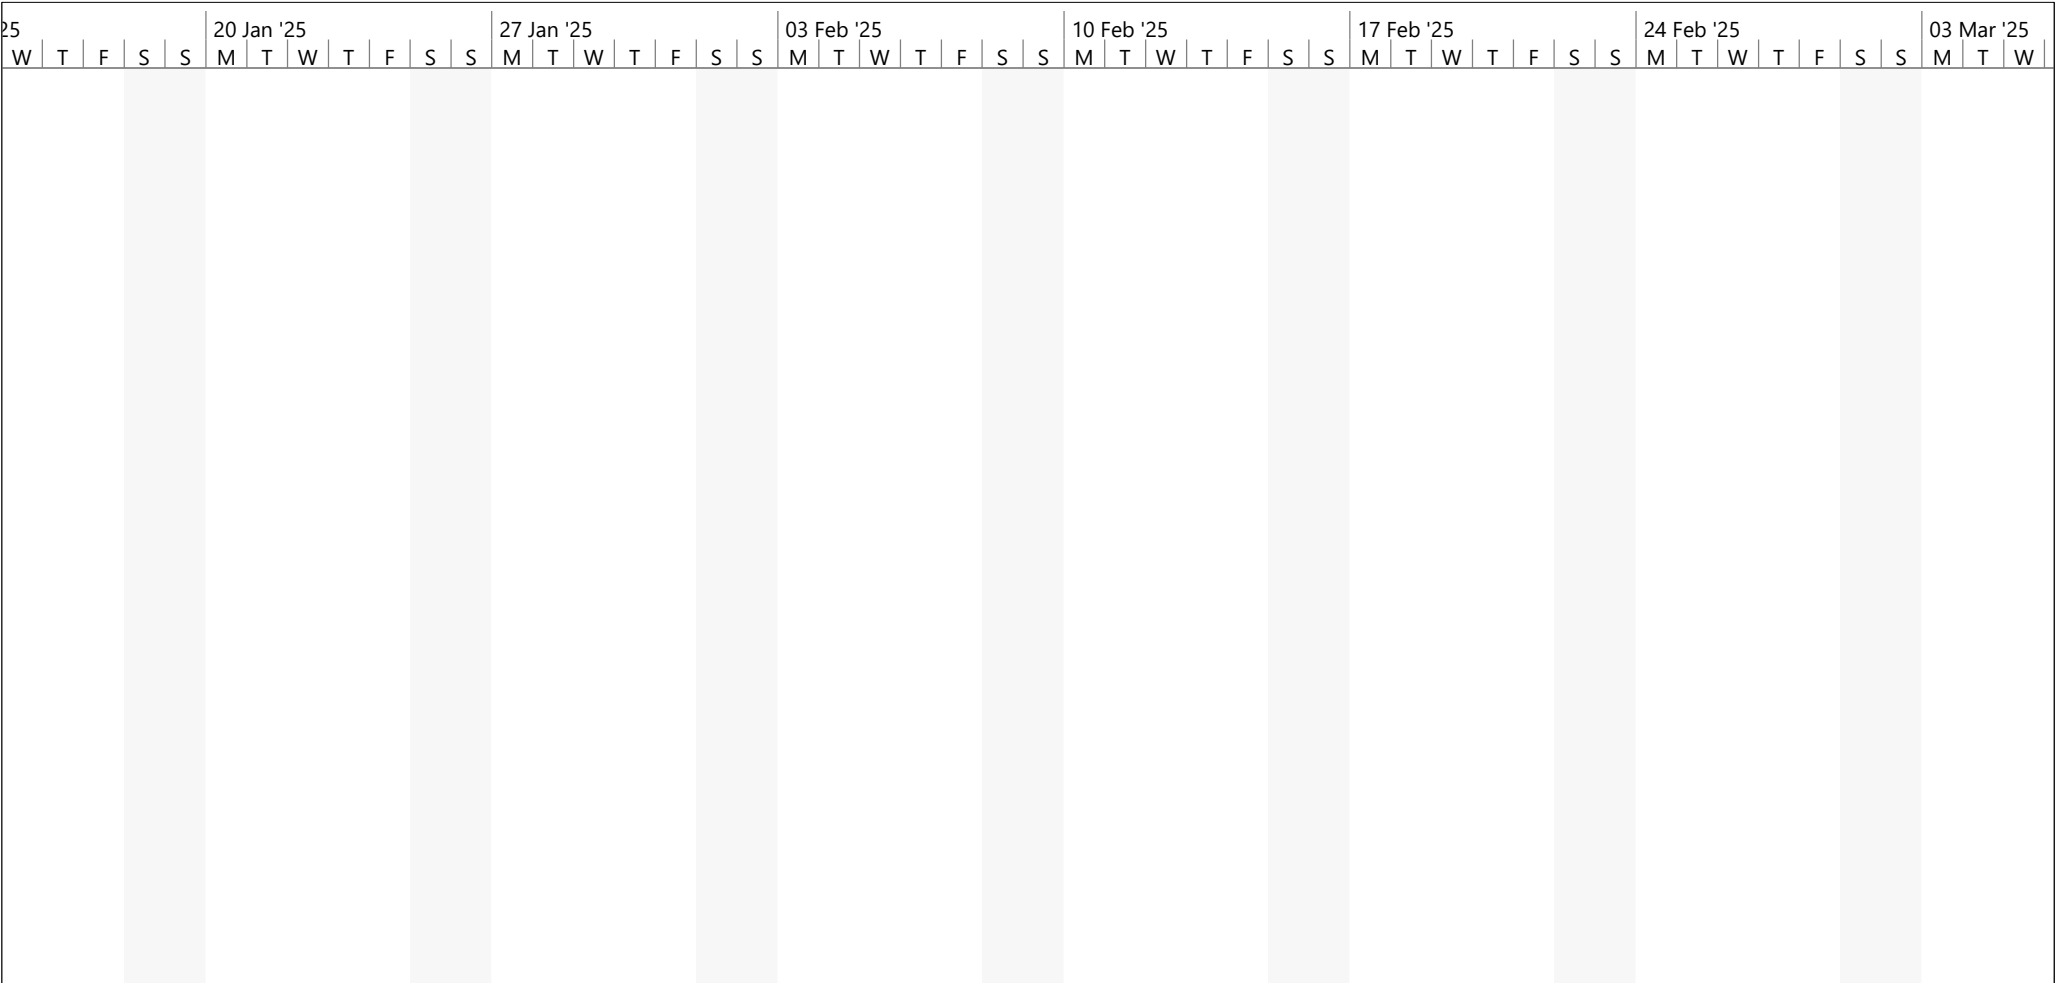

Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

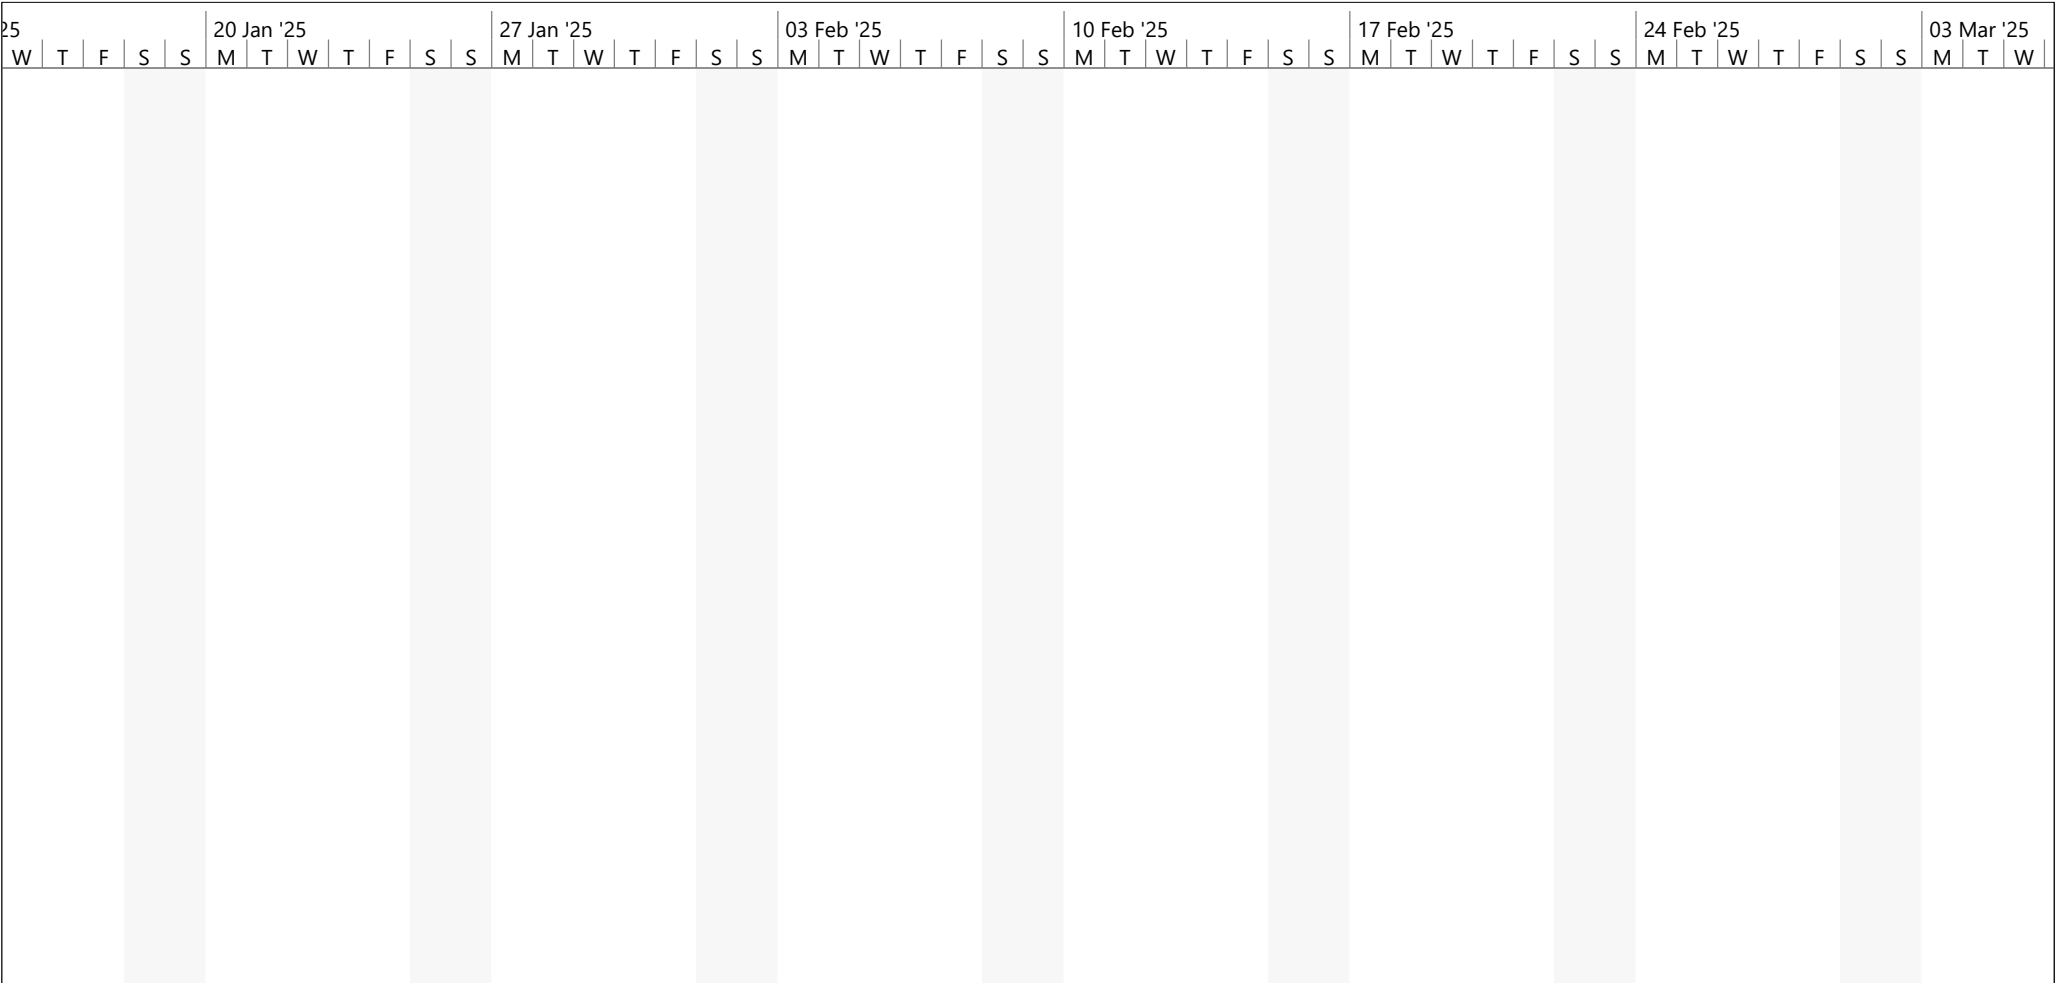

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone

Deadline

Progress


Manual Progress

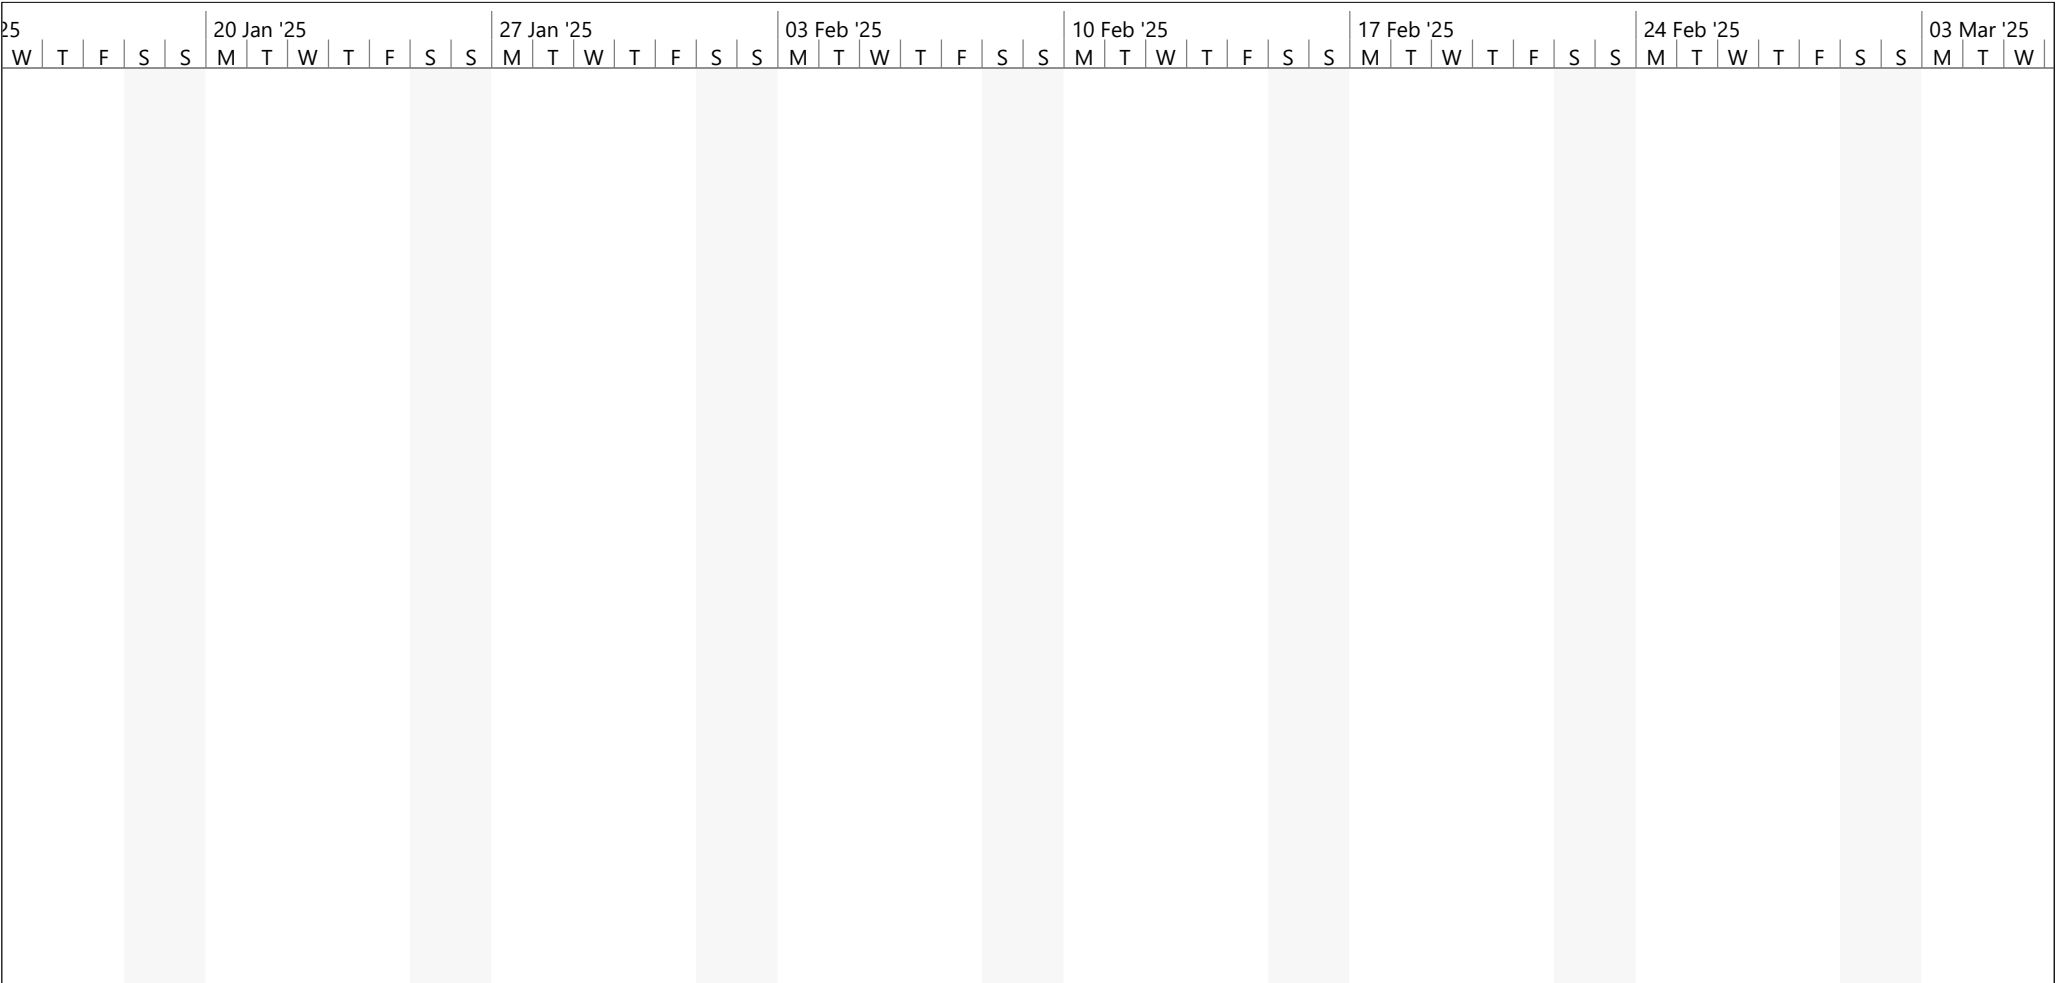


Project: Steel Museum, Port Tal

Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

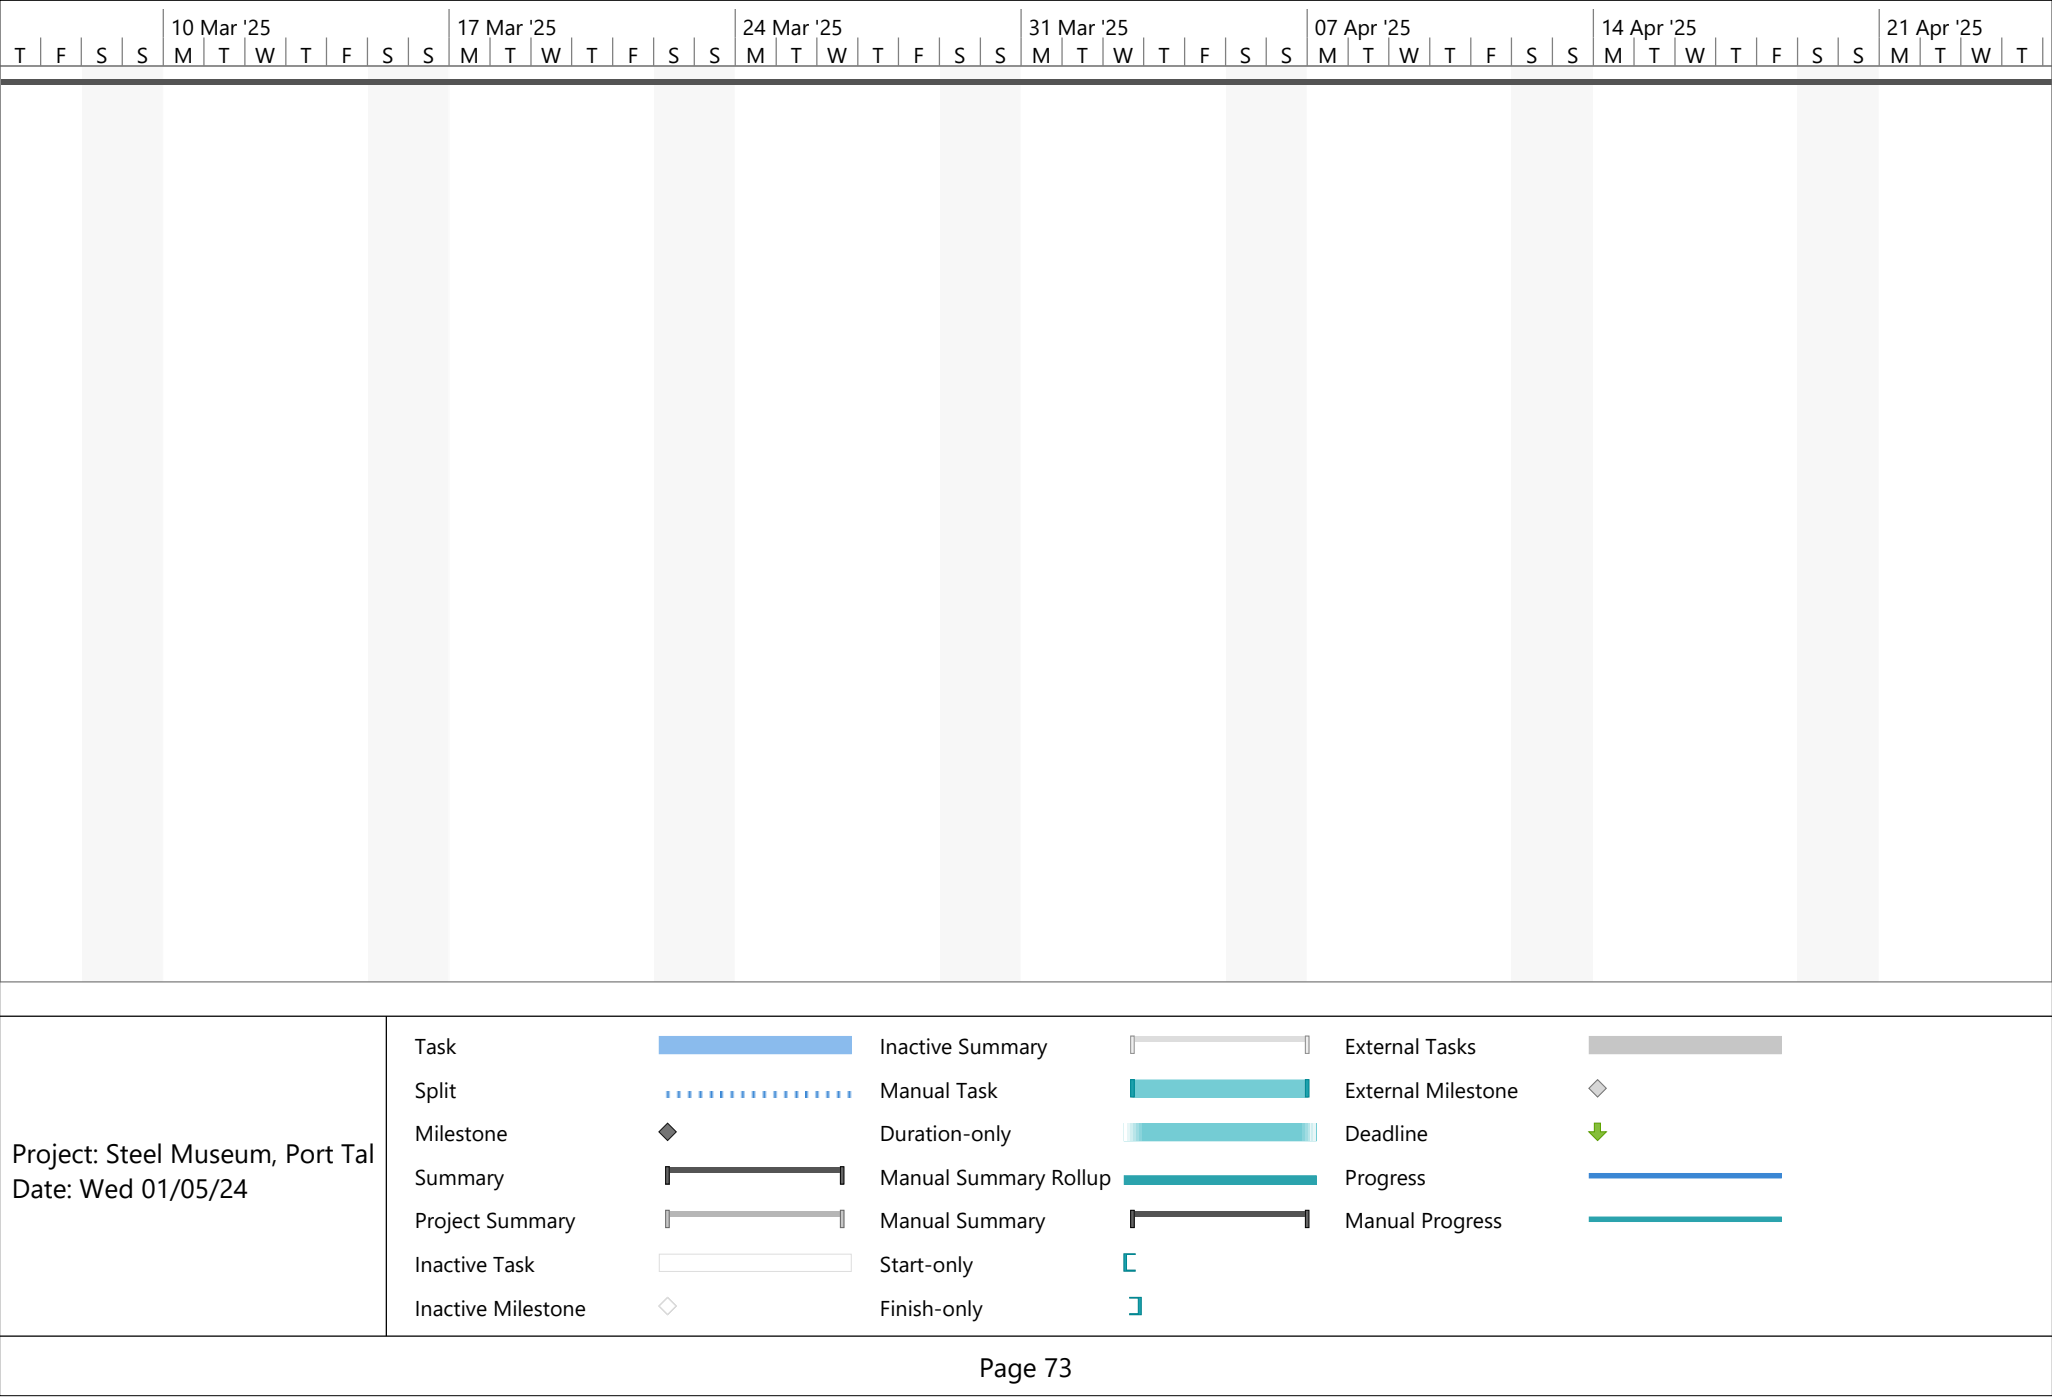

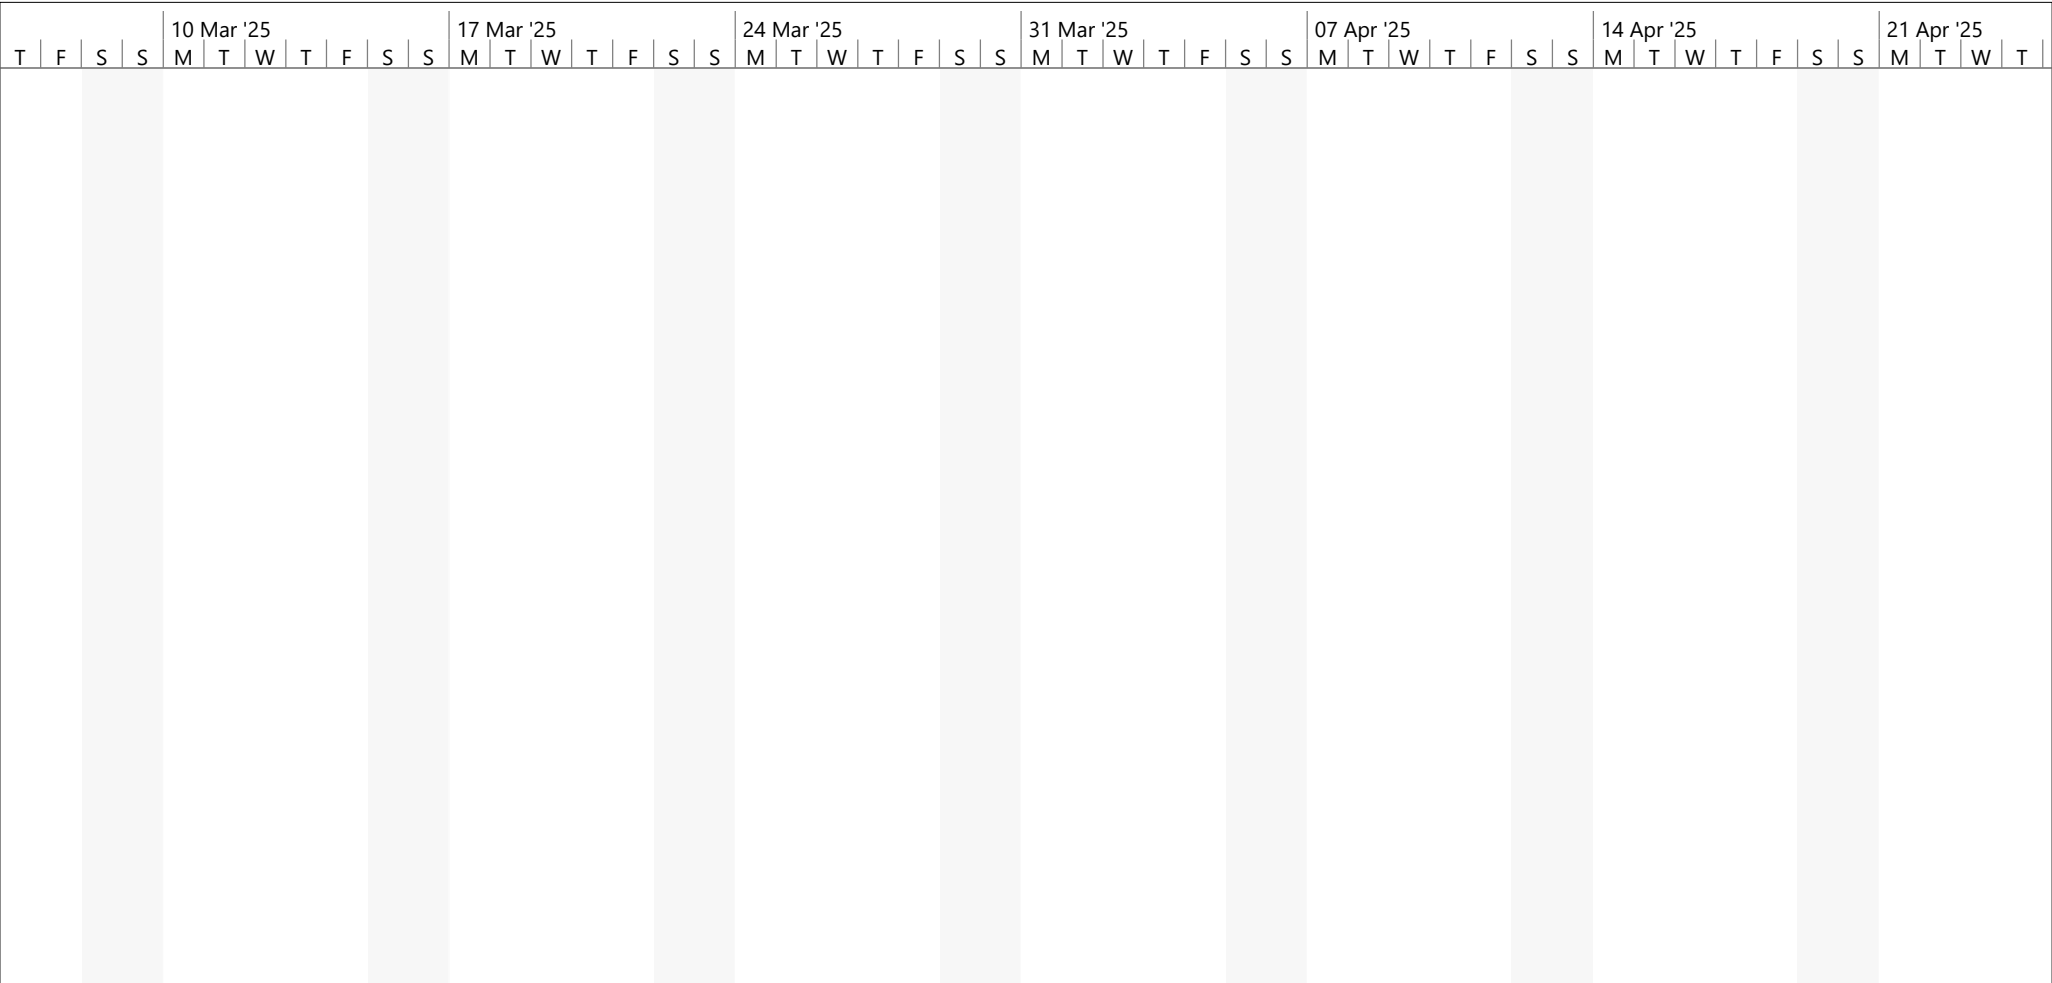

Project: Steel Museum, Port Talbot
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone


Deadline

Progress

Manual Progress

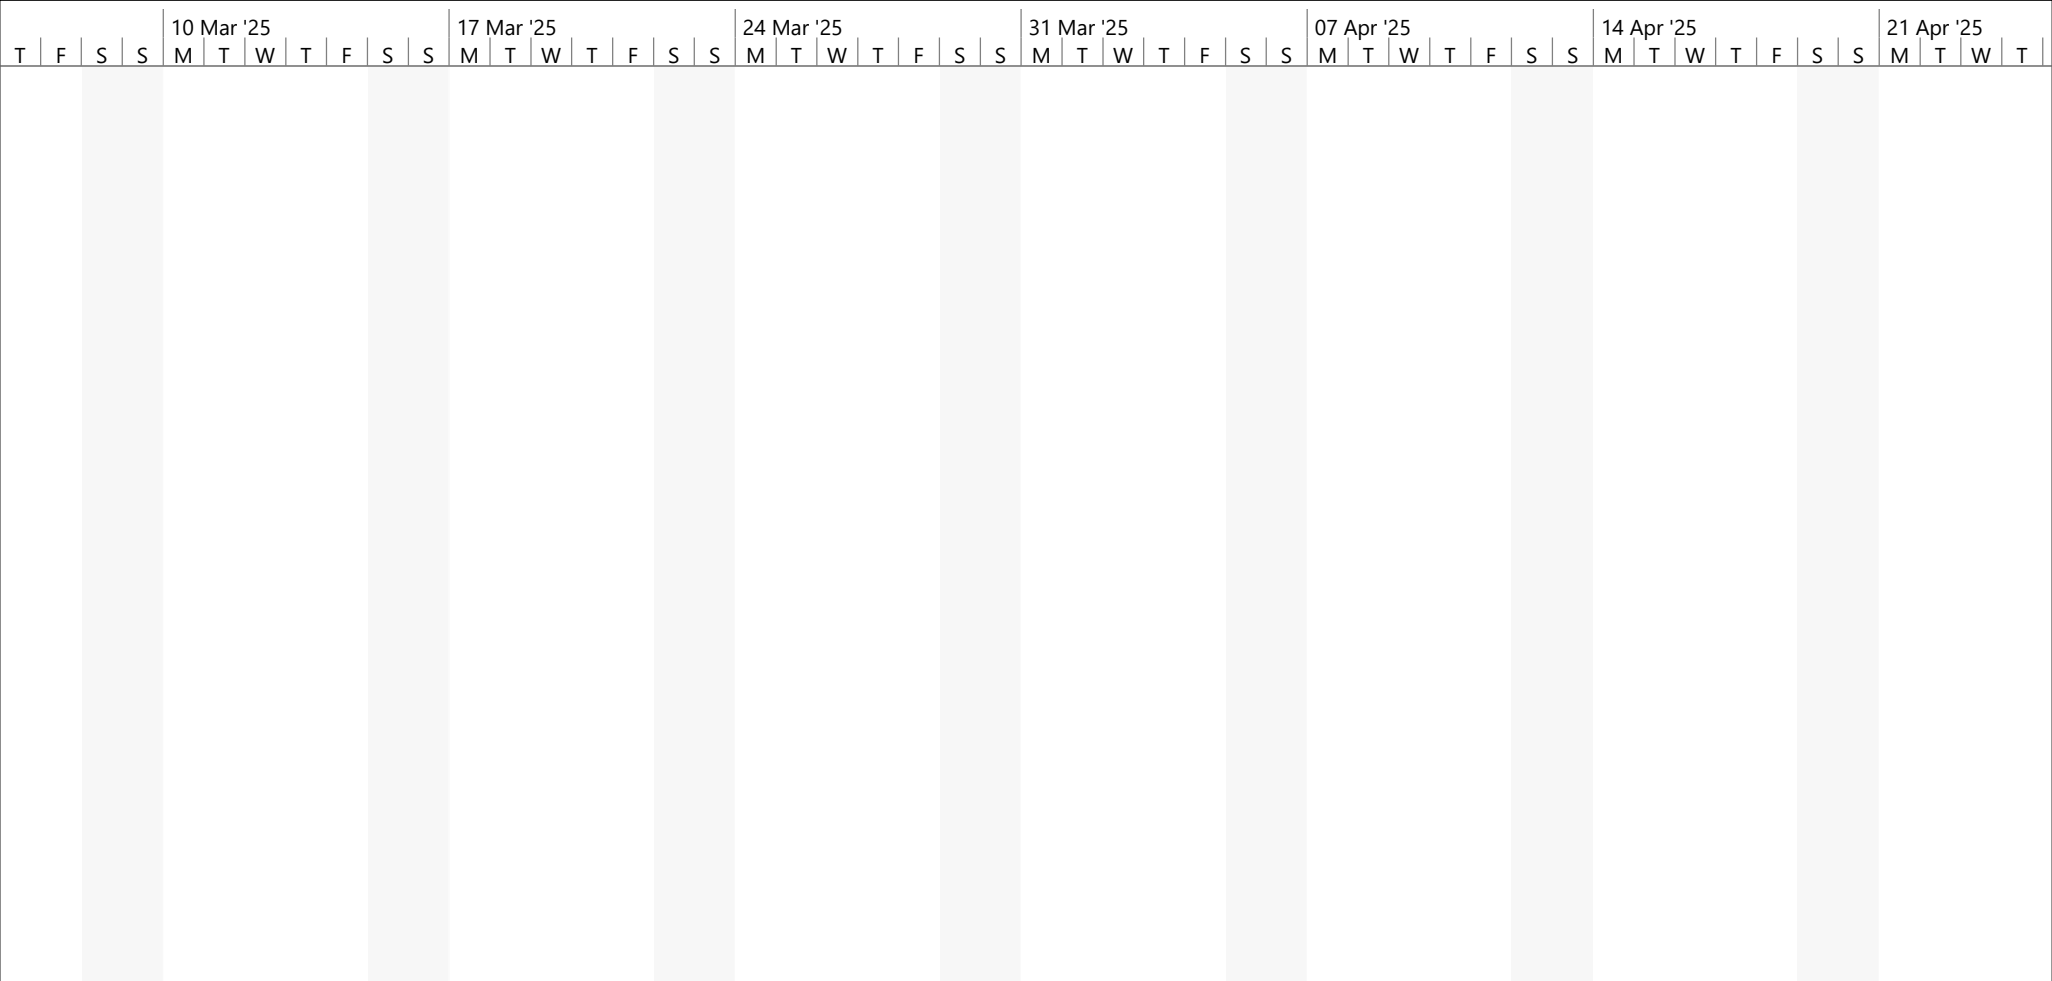

Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

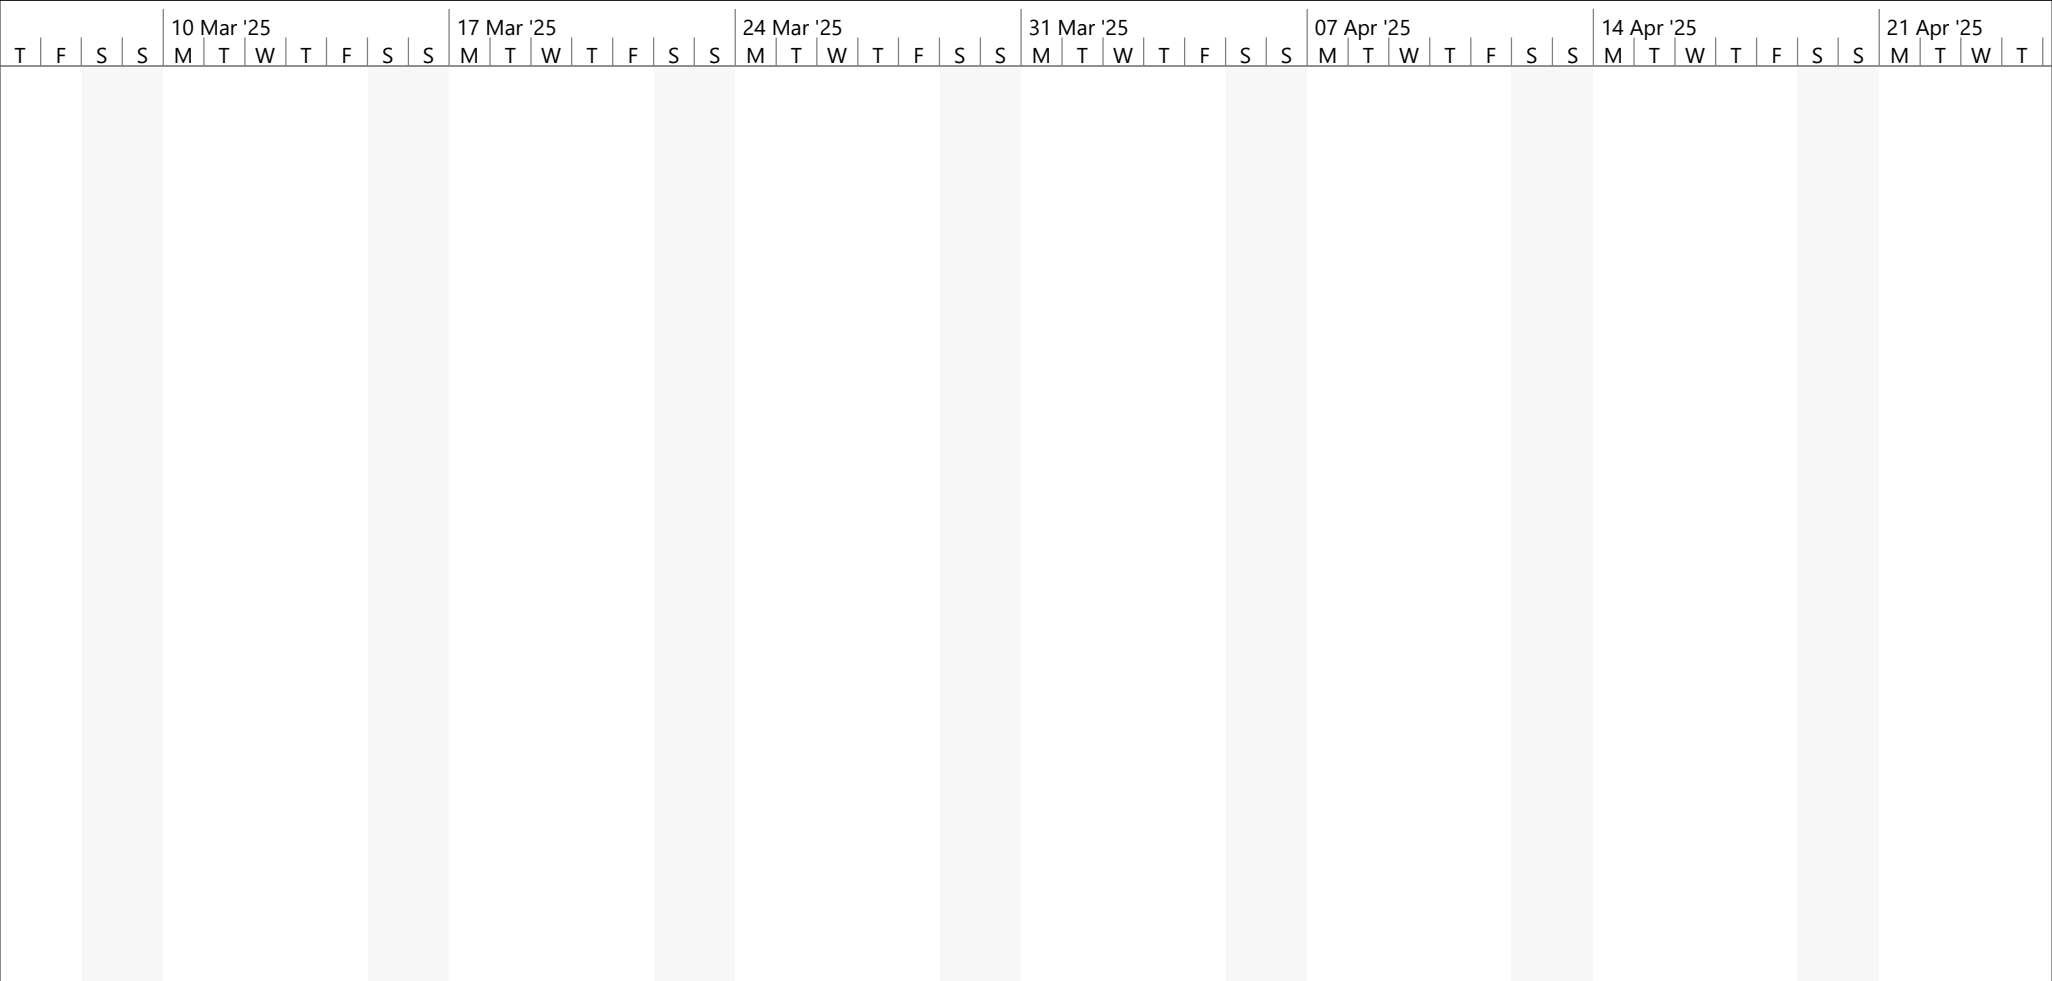

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone

Deadline


Progress

Manual Progress

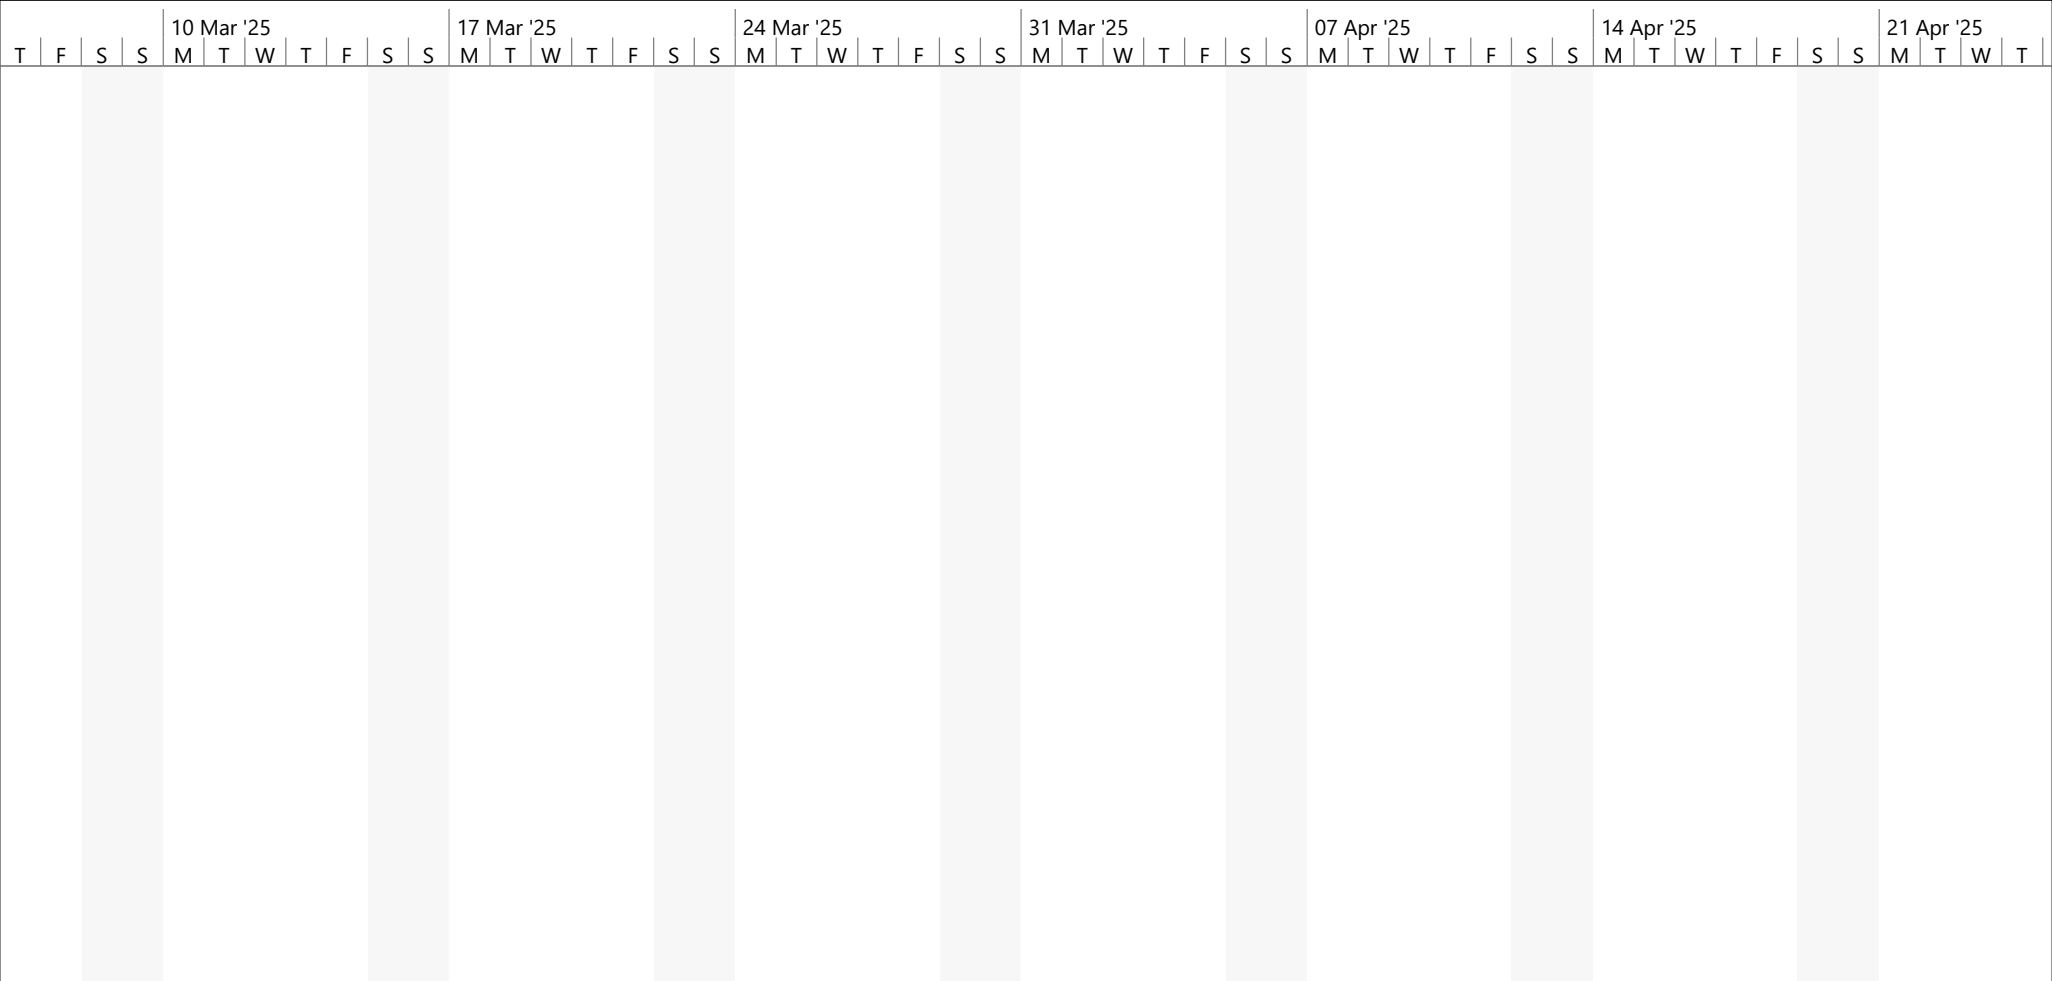


Project: Steel Museum, Port Tal
Date: Wed 01/05/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

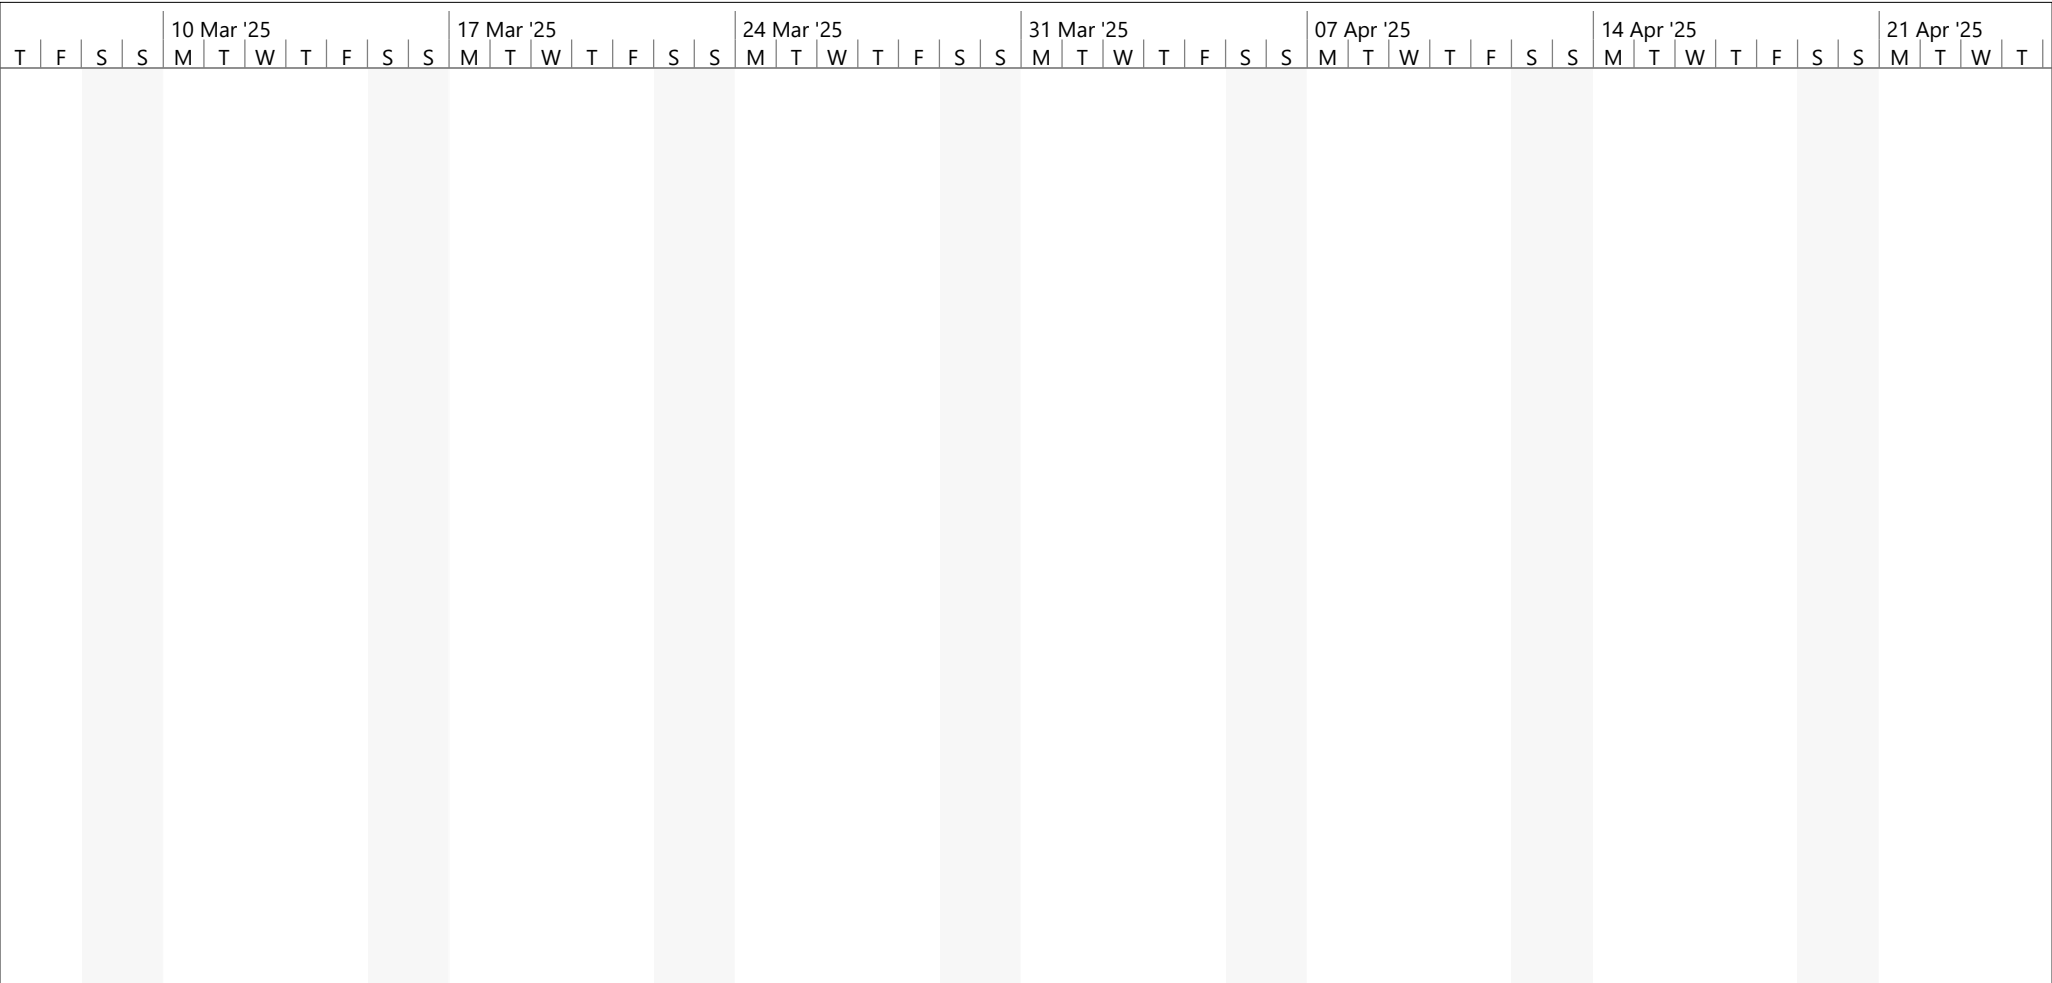

Project: Steel Museum, Port Tal
Date: Wed 01/05/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

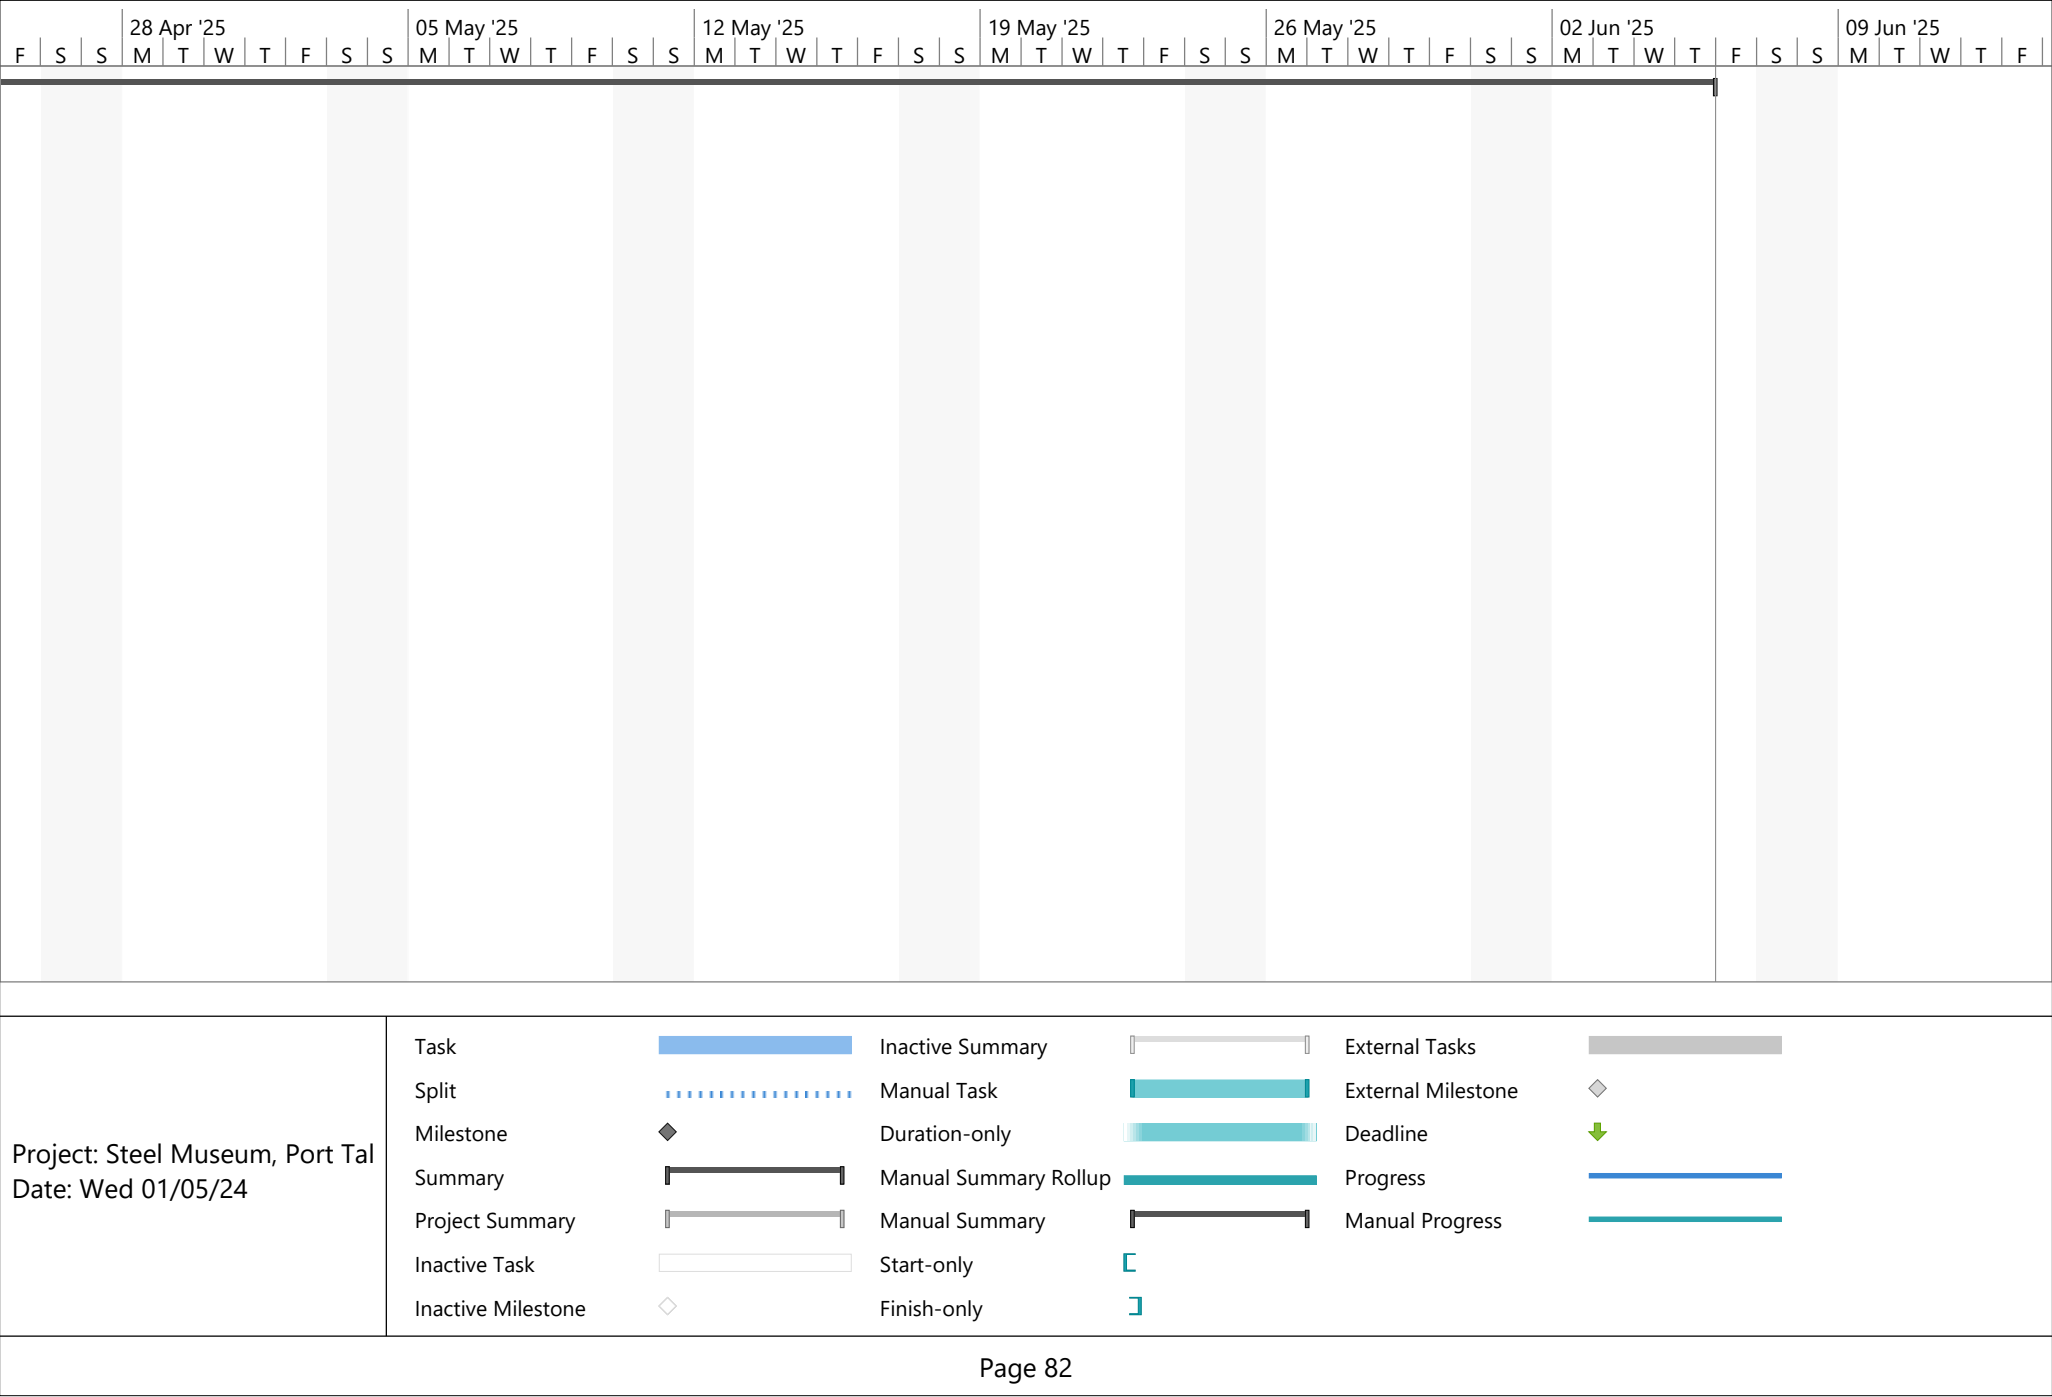

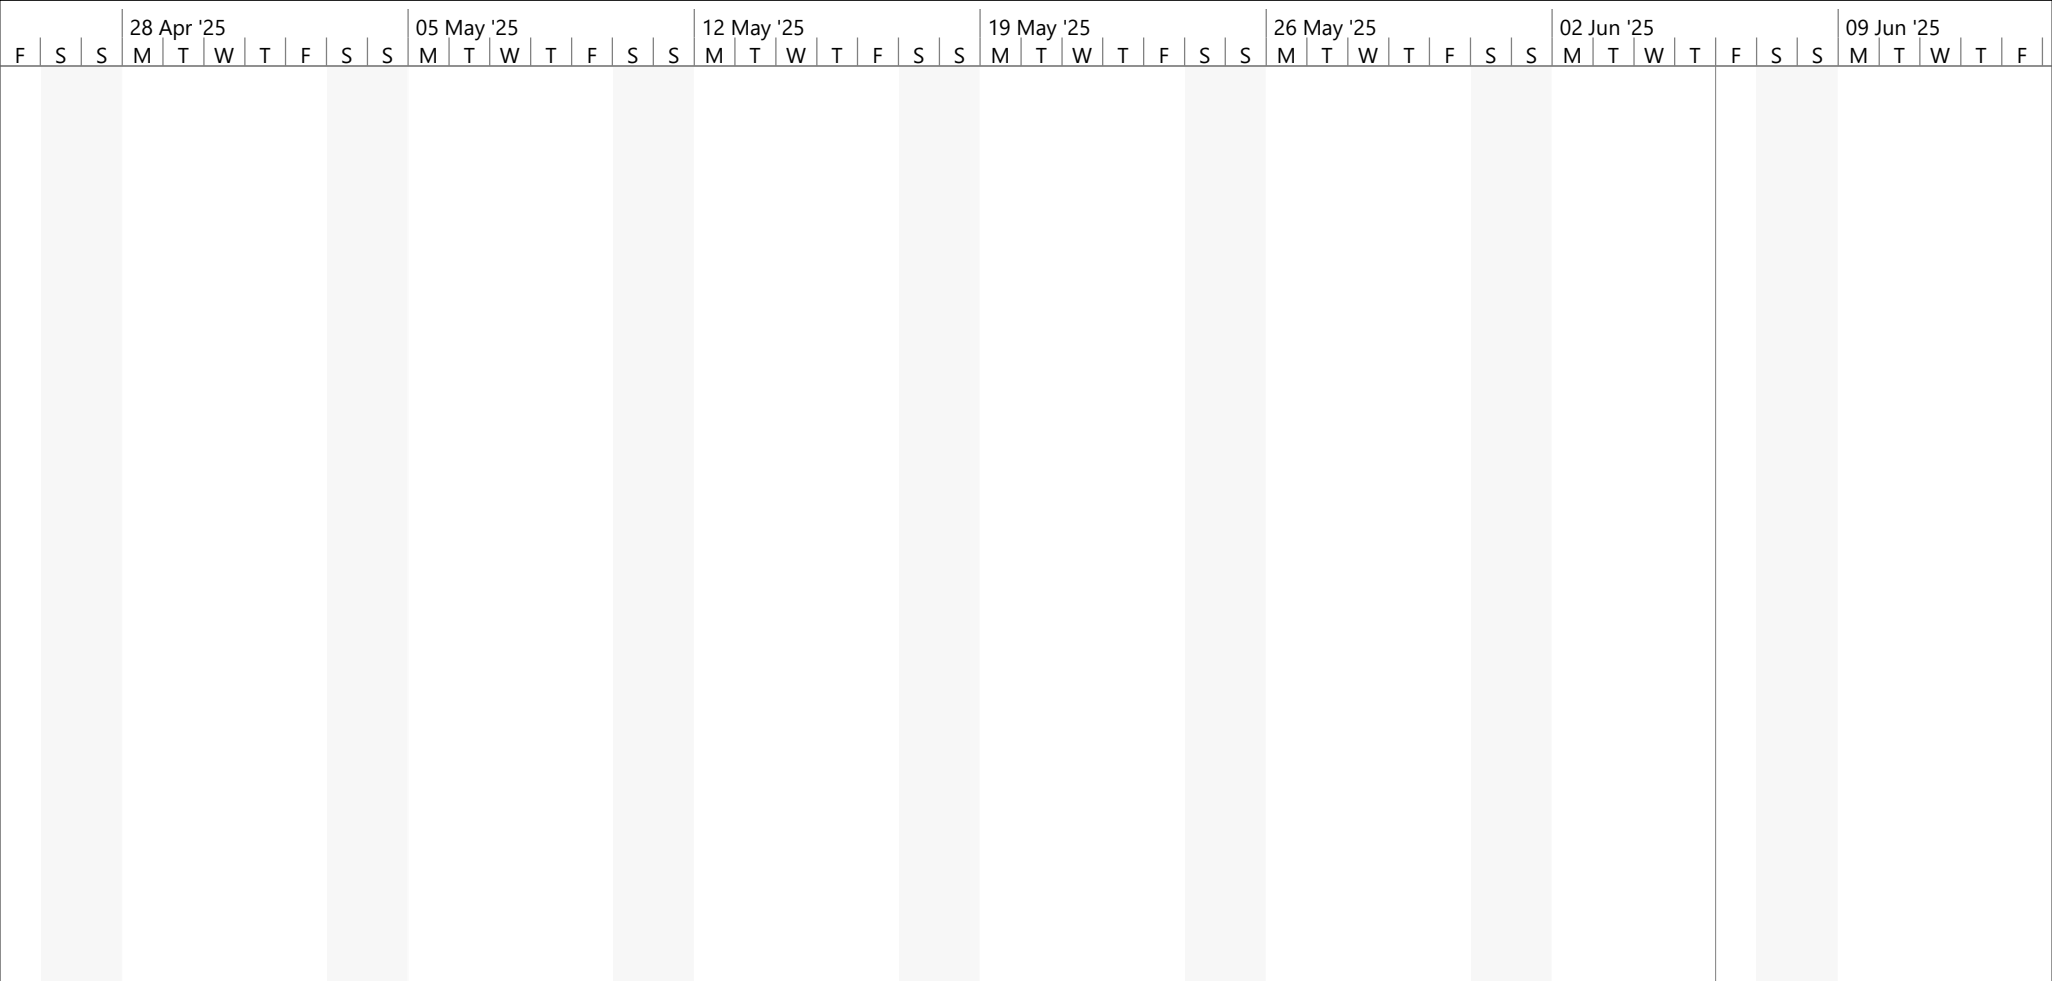

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

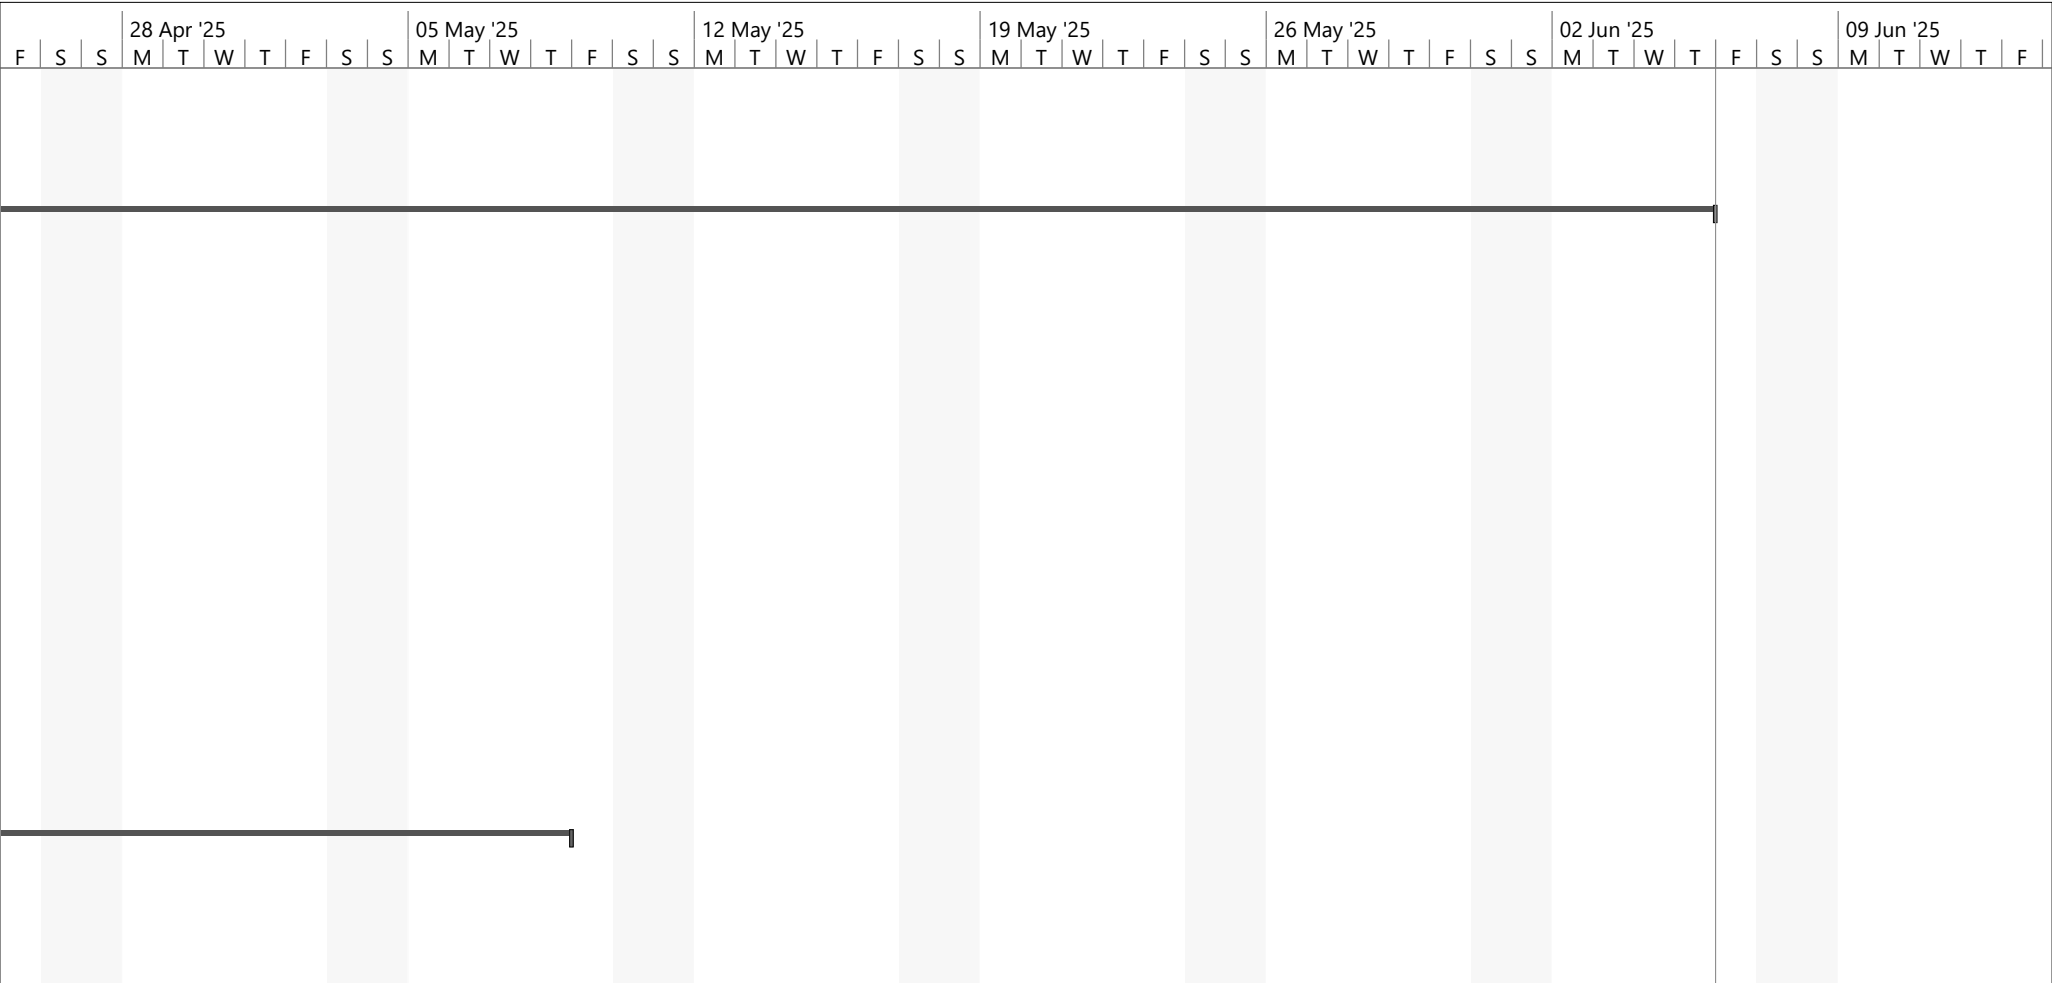

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

Page 84

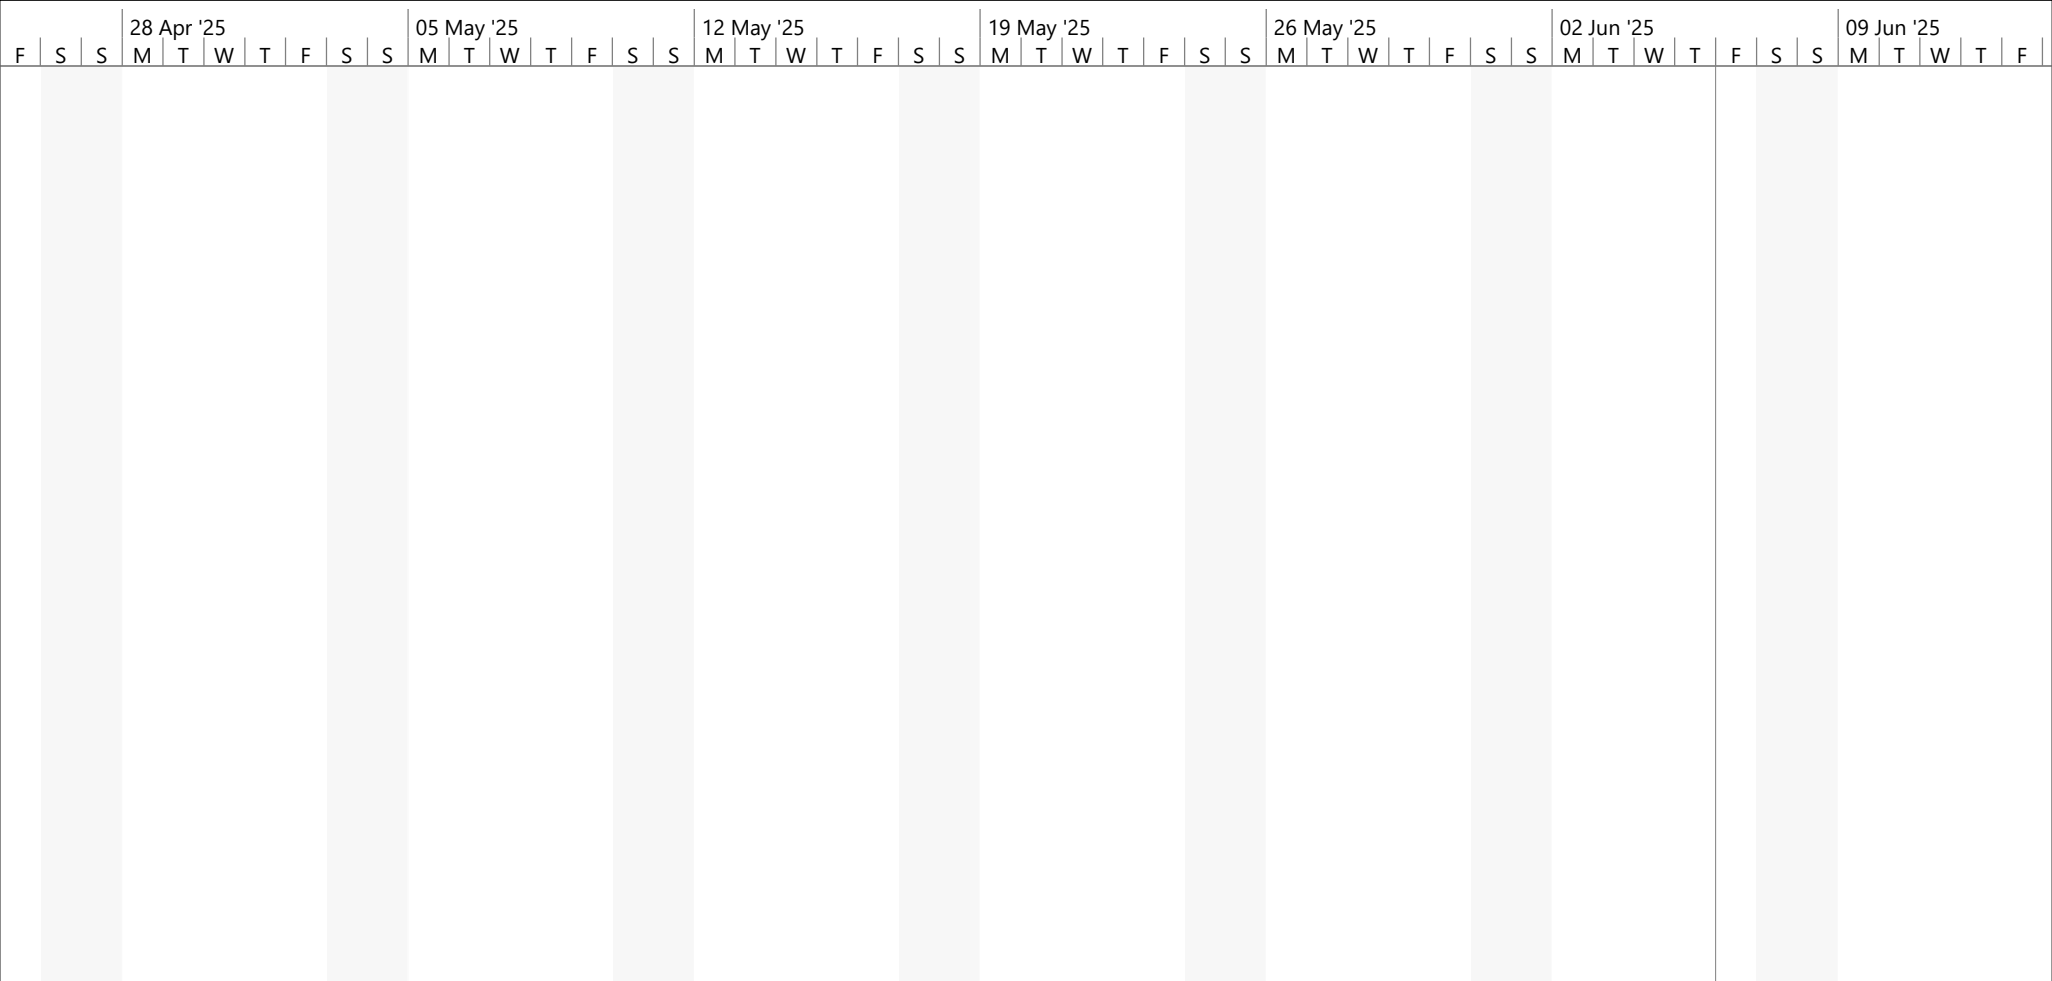

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only


External Tasks

External Milestone

Deadline

Progress

Manual Progress

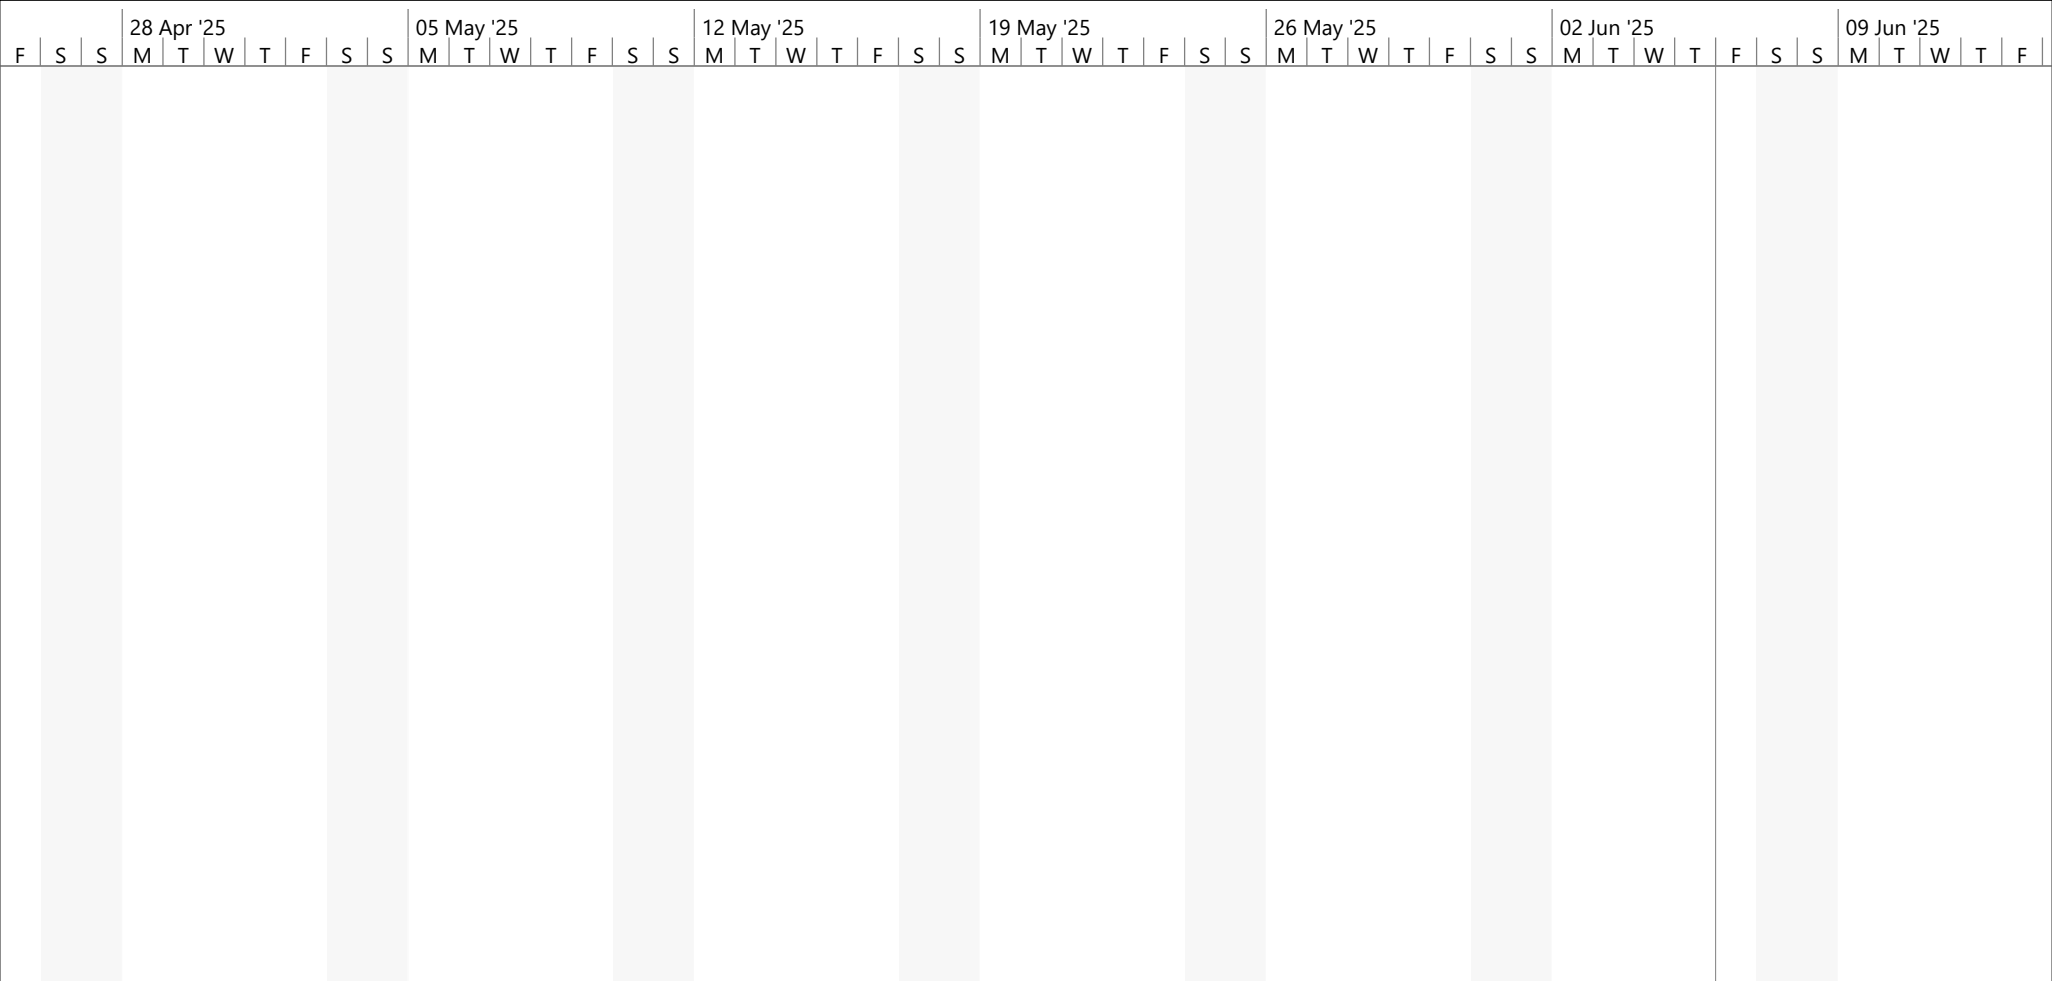

Project: Steel Museum, Port Tal
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

			28 Apr '25							05 May '25							12 May '25							19 May '25							26 May '25							02 Jun '25							09 Jun '25						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F									



Project: Steel Museum, Port Tal Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
