

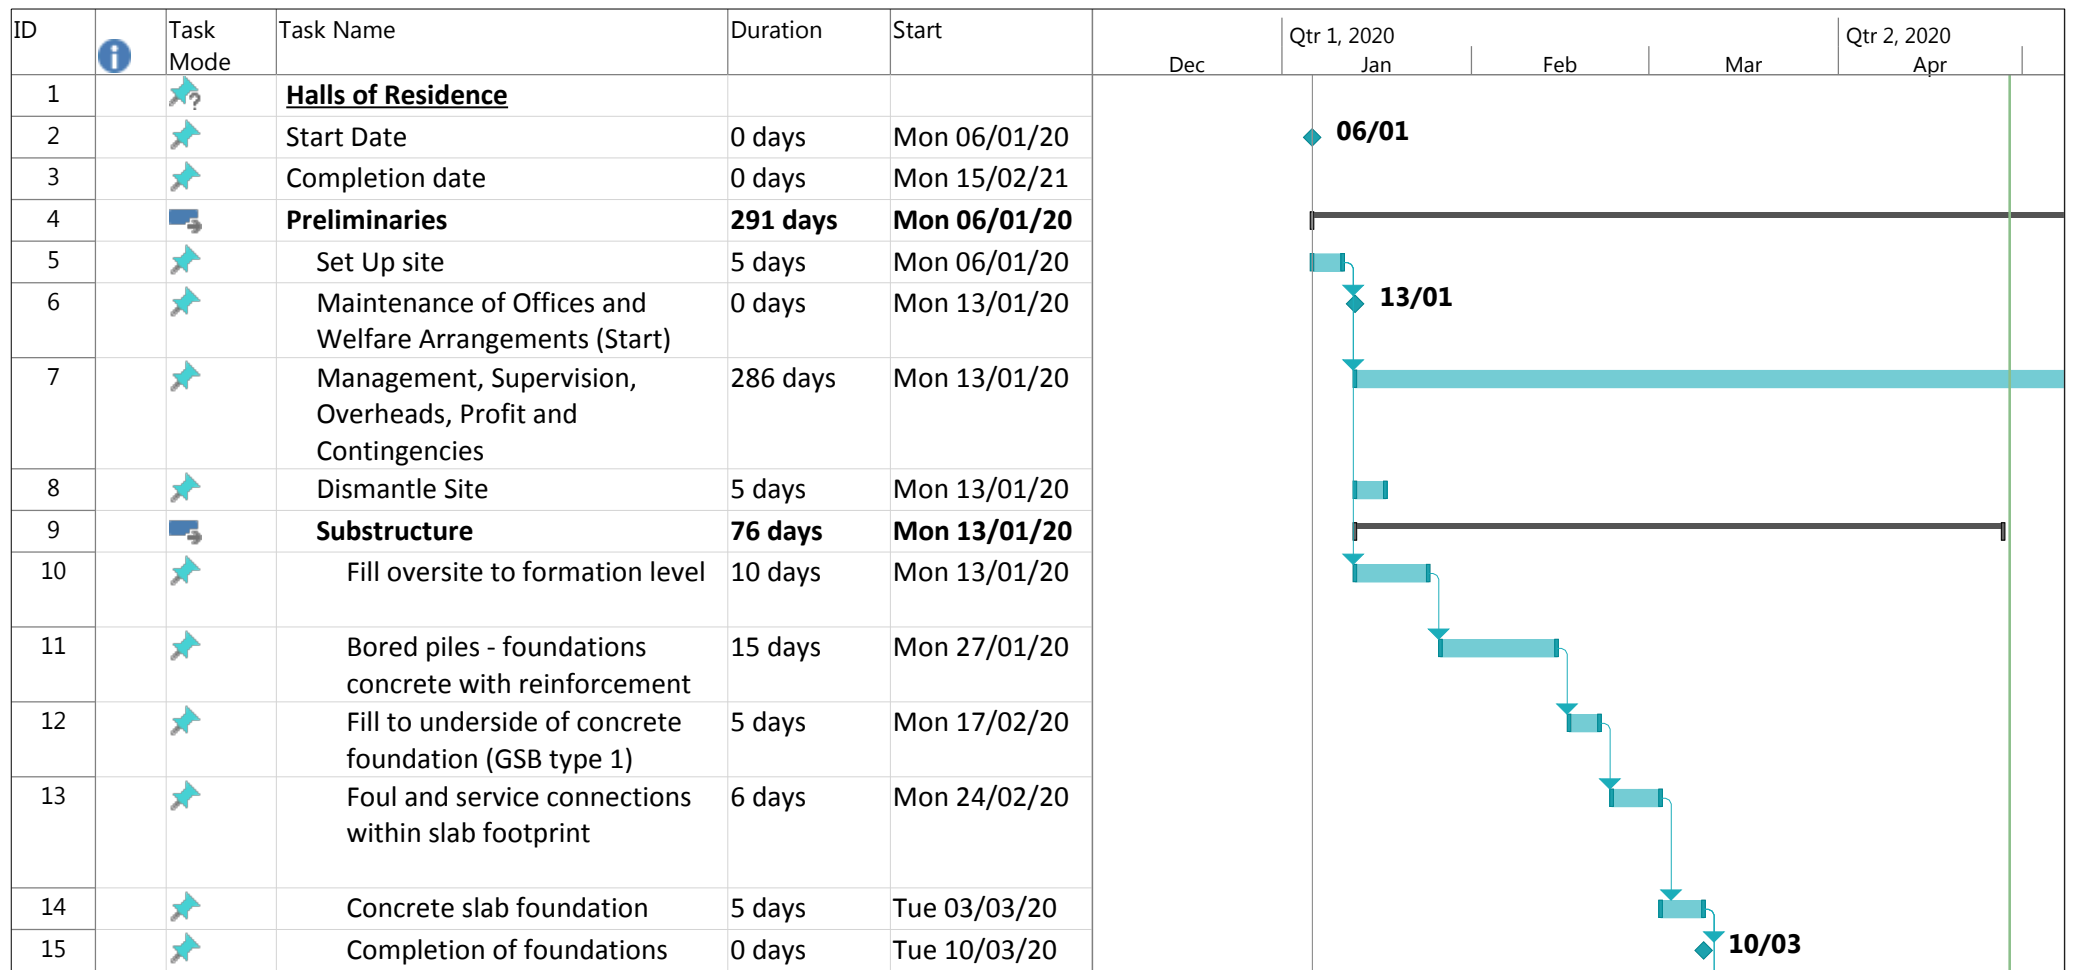






Project: Construction Programm
Date: Wed 29/04/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

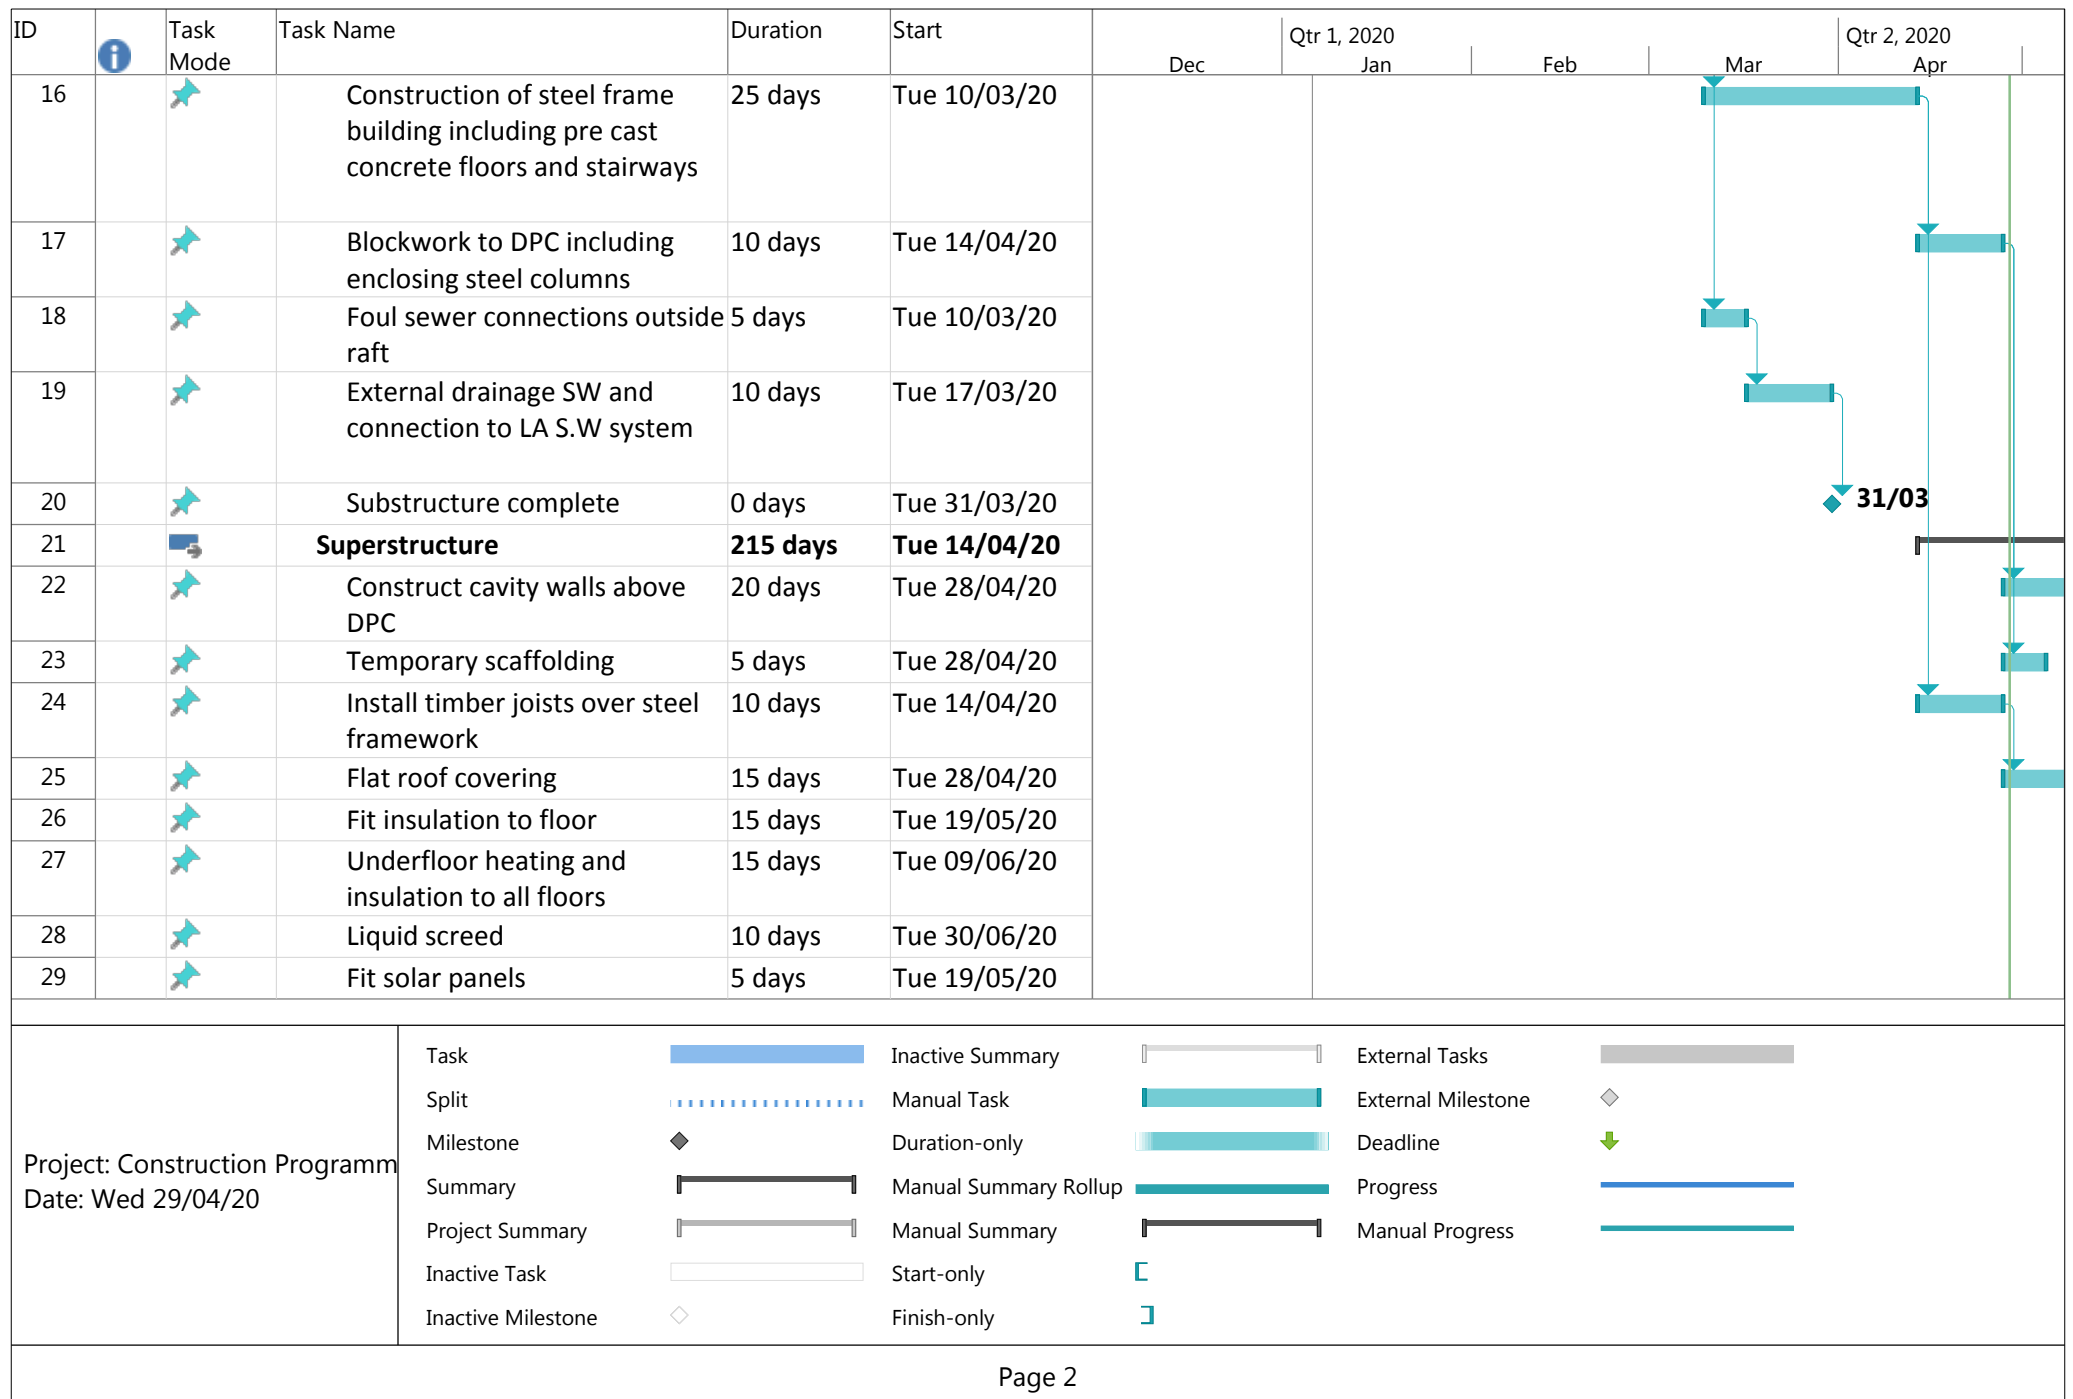

ID		Task Mode	Task Name	Duration	Start	Dec	Qtr 1, 2020 Jan	Feb	Mar	Qtr 2, 2020 Apr
30			Fit external windows and doors	15 days	Tue 26/05/20					
31			Building is now water tight	0 days	Tue 16/06/20					
32			External render and paint	10 days	Tue 16/06/20					
33			Tarmac wearing course can be applied	0 days	Tue 30/06/20					
34			First fix plumbing	40 days	Tue 19/05/20					
35			First fix electrics	40 days	Tue 19/05/20					
36			First fix carpentry (partitions, linings, plasterboard, insulation (etc)	50 days	Tue 19/05/20					
37			Plaster internal walls and ceilings	50 days	Tue 28/07/20					
38			Second fix carpentry (doors architraves and skirting)	50 days	Tue 06/10/20					
39			Second fix plumbing	20 days	Tue 06/10/20					
40			Second fix electrics	20 days	Tue 06/10/20					
41			Decoration can now begin	0 days	Tue 03/11/20					
42			Finishing (tiling, fitting kitchens and interior painting)	70 days	Tue 03/11/20					
43			Carriageway surfacing and kerbing	20 days	Tue 30/06/20					


Project: Construction Programm
Date: Wed 29/04/20


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Dec	Qtr 1, 2020 Jan	Feb	Mar	Qtr 2, 2020 Apr	
44			External paving	10 days	Tue 28/07/20						
45											



Project: Construction Programm Date: Wed 29/04/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

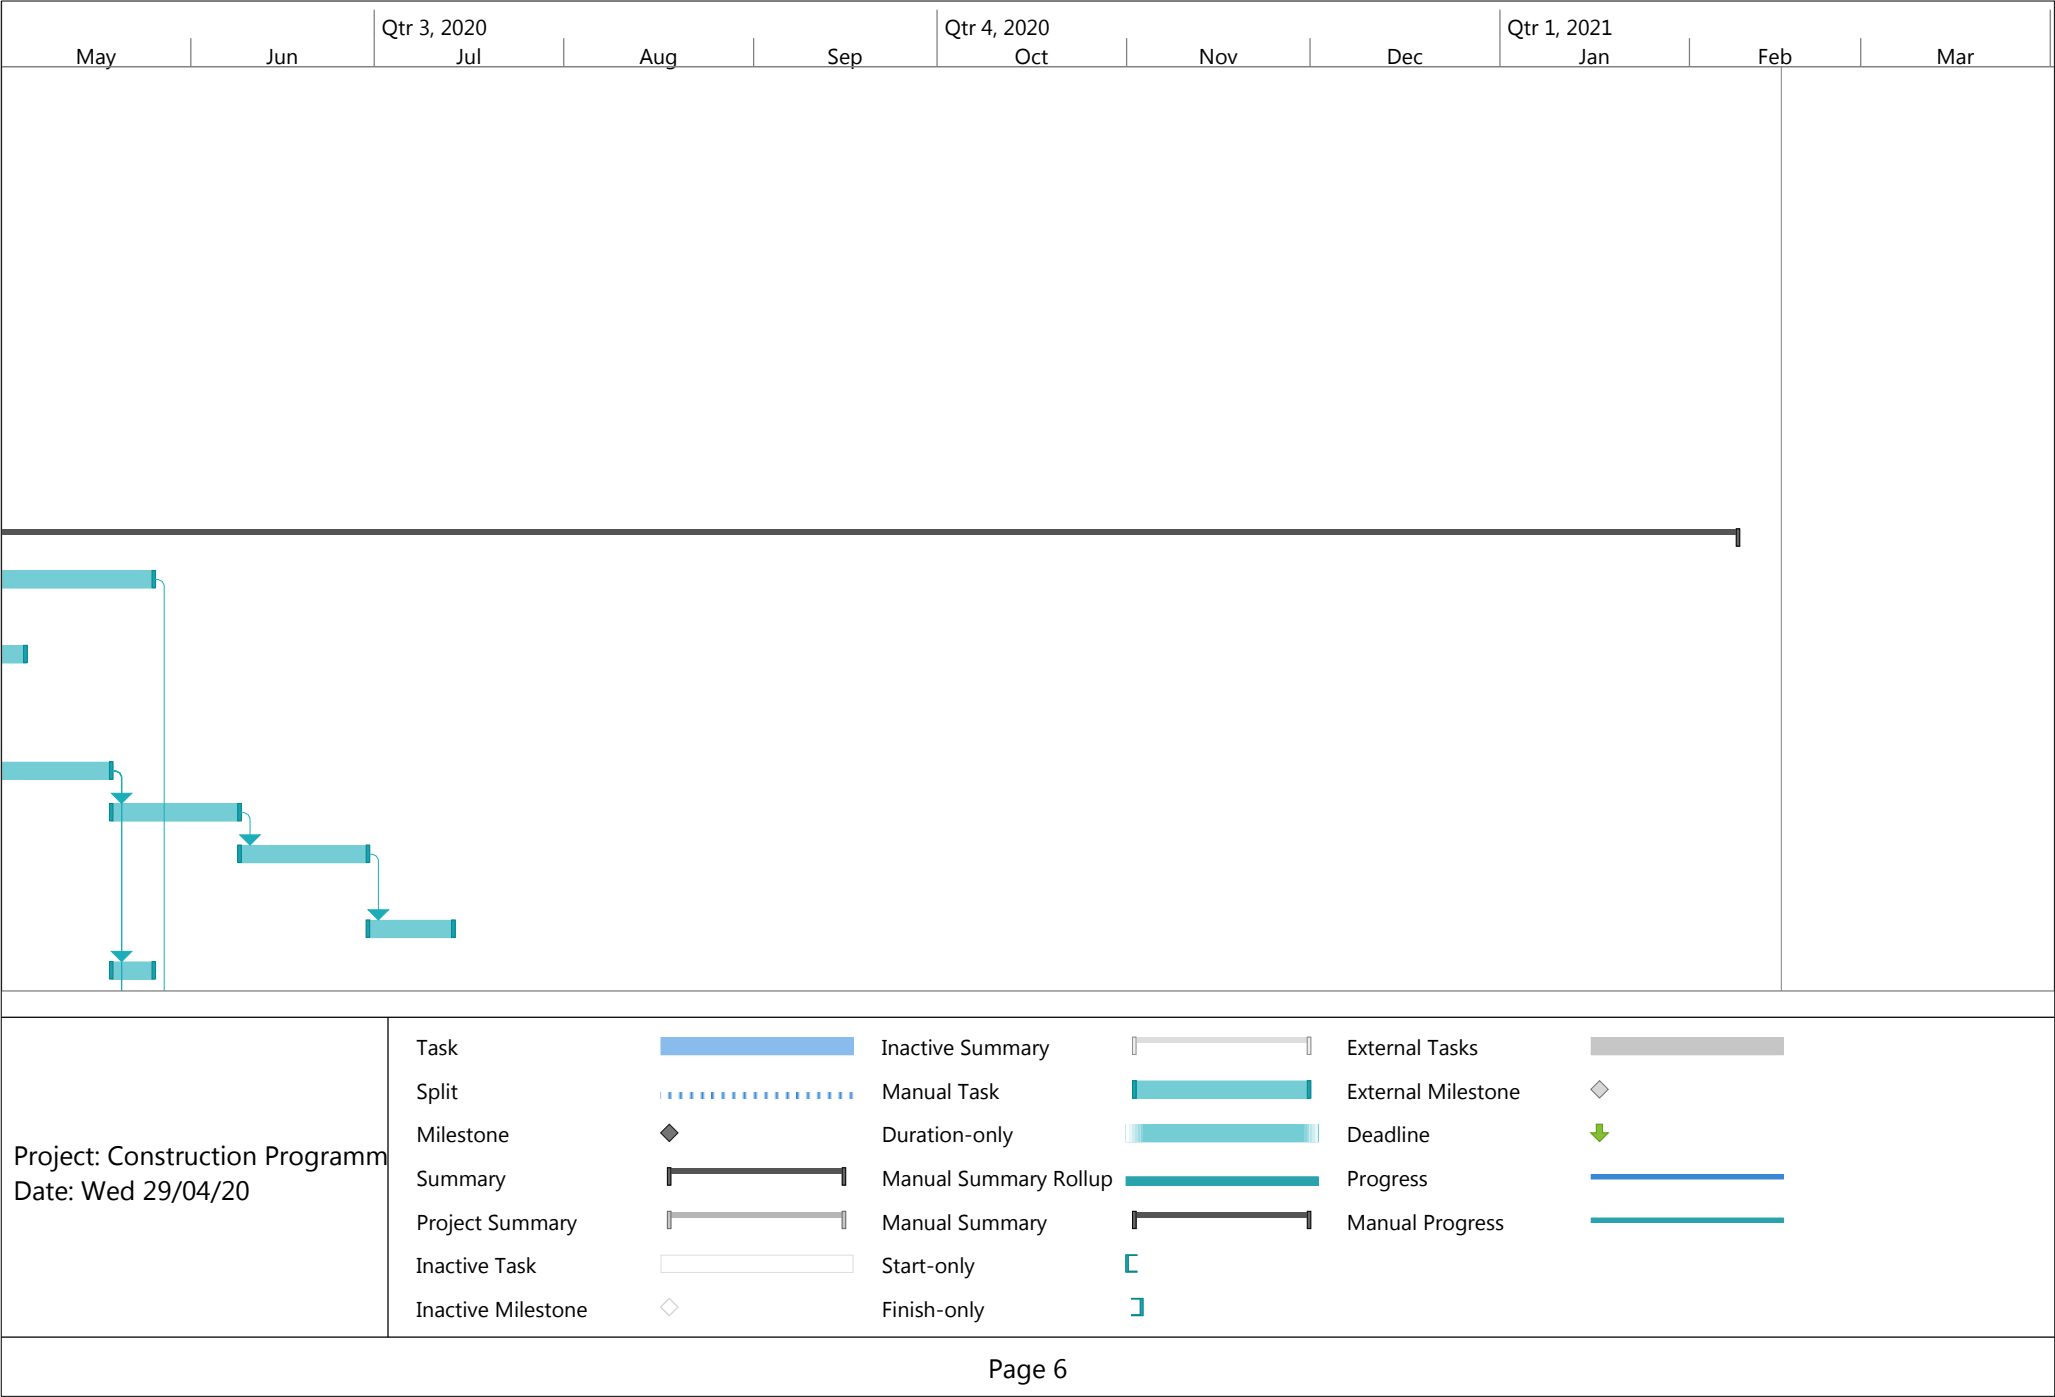

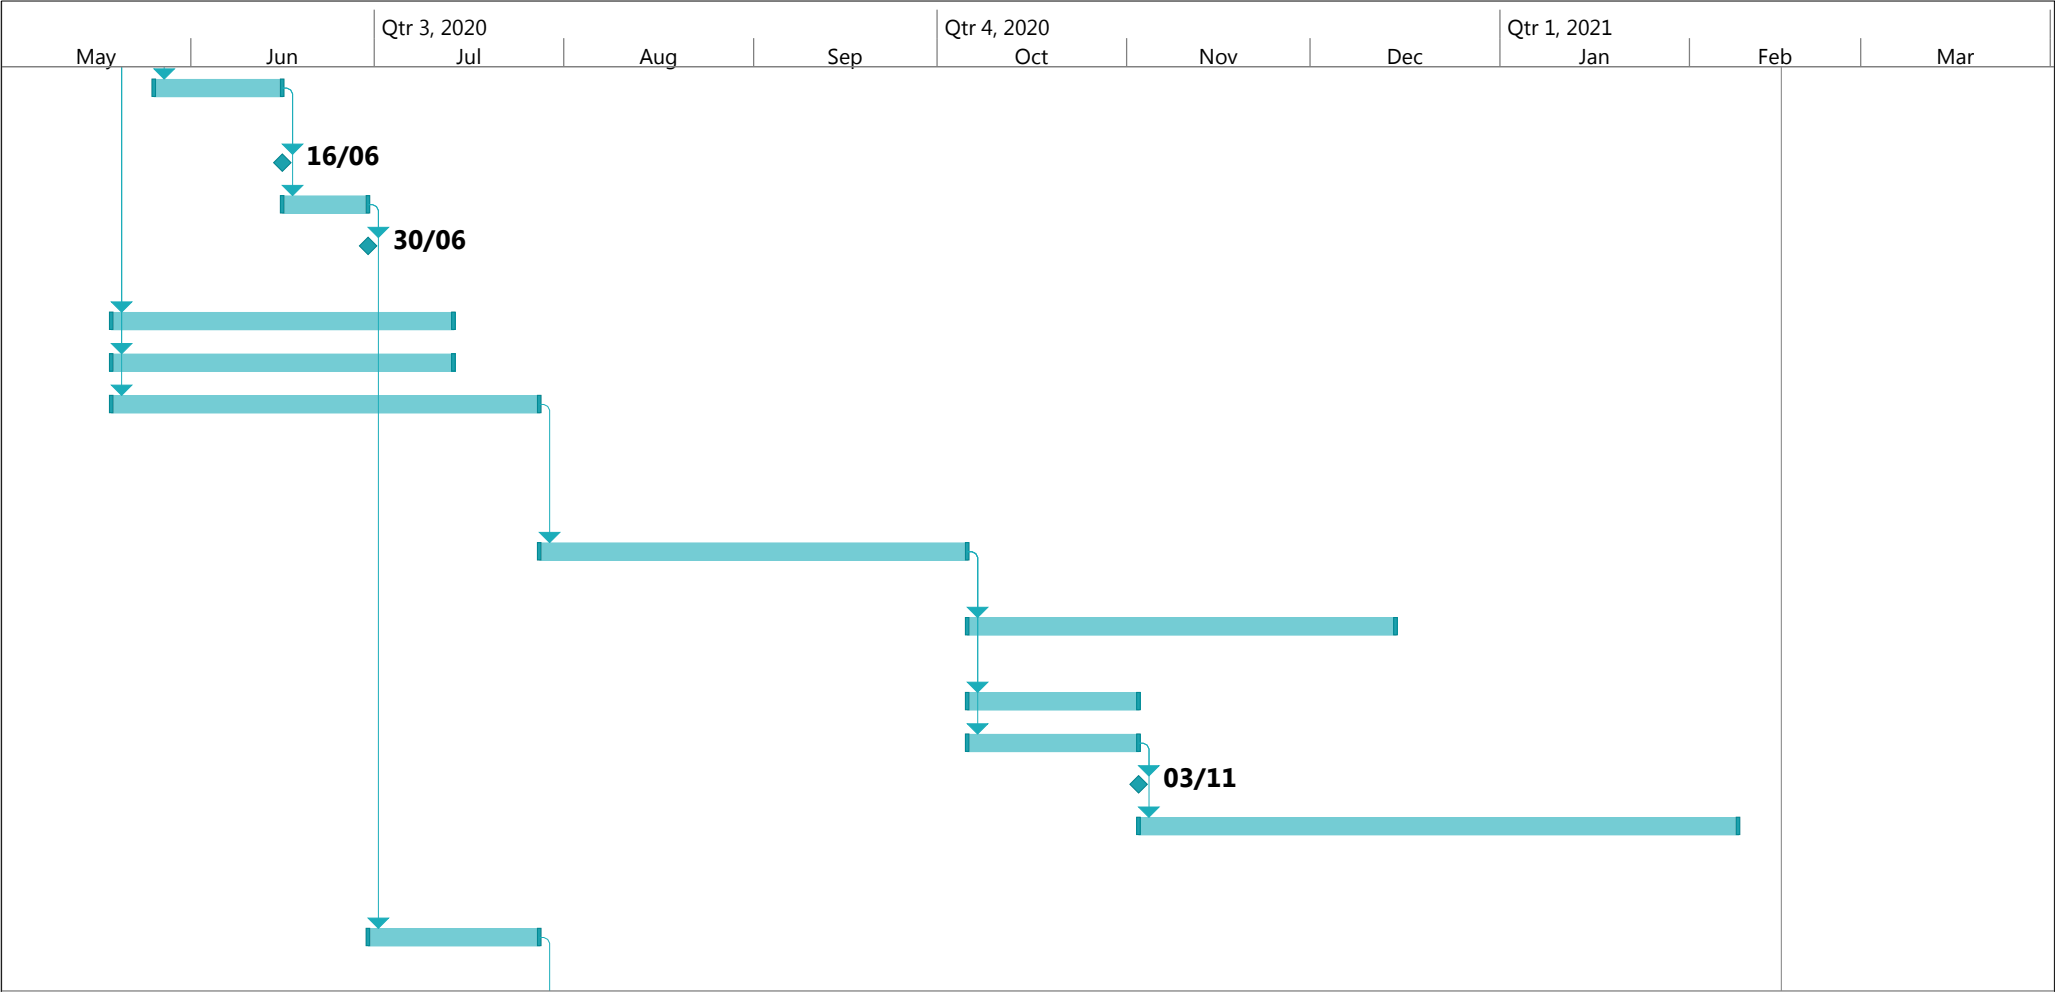

Project: Construction Programm Date: Wed 29/04/20	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: Construction Programm

Date: Wed 29/04/20

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Halls of Residence

Start: ID: 1

Finish: Dur:

Res:

Start Date

Milestone Date: Mon 06/01/20

ID: 2

Completion date

Milestone Date: Mon 15/02/21

ID: 3

Preliminaries

Start: Mon 06/01/20 ID: 4

Finish: Mon 15/02/20 Dur: 291 days

Comp: 0%

Set Up site

Start: Mon 06/01/20 ID: 5

Finish: Fri 10/01/20 Dur: 5 days

Res:

Dismantle Site

Start: Mon 13/01/2020 ID: 8

Finish: Fri 17/01/2020 Dur: 5 days

Res:

Substructure

Start: Mon 13/01/2020 ID: 9

Finish: Mon 27/04/2020 Dur: 76 days



Comp: 0%


Superstructure

Start: Tue 14/04/2020 ID: 21


Finish: Mon 08/02/2021 Dur: 215 days

Comp: 0%








Start:	ID: 45
Finish:	Dur:
Res:	

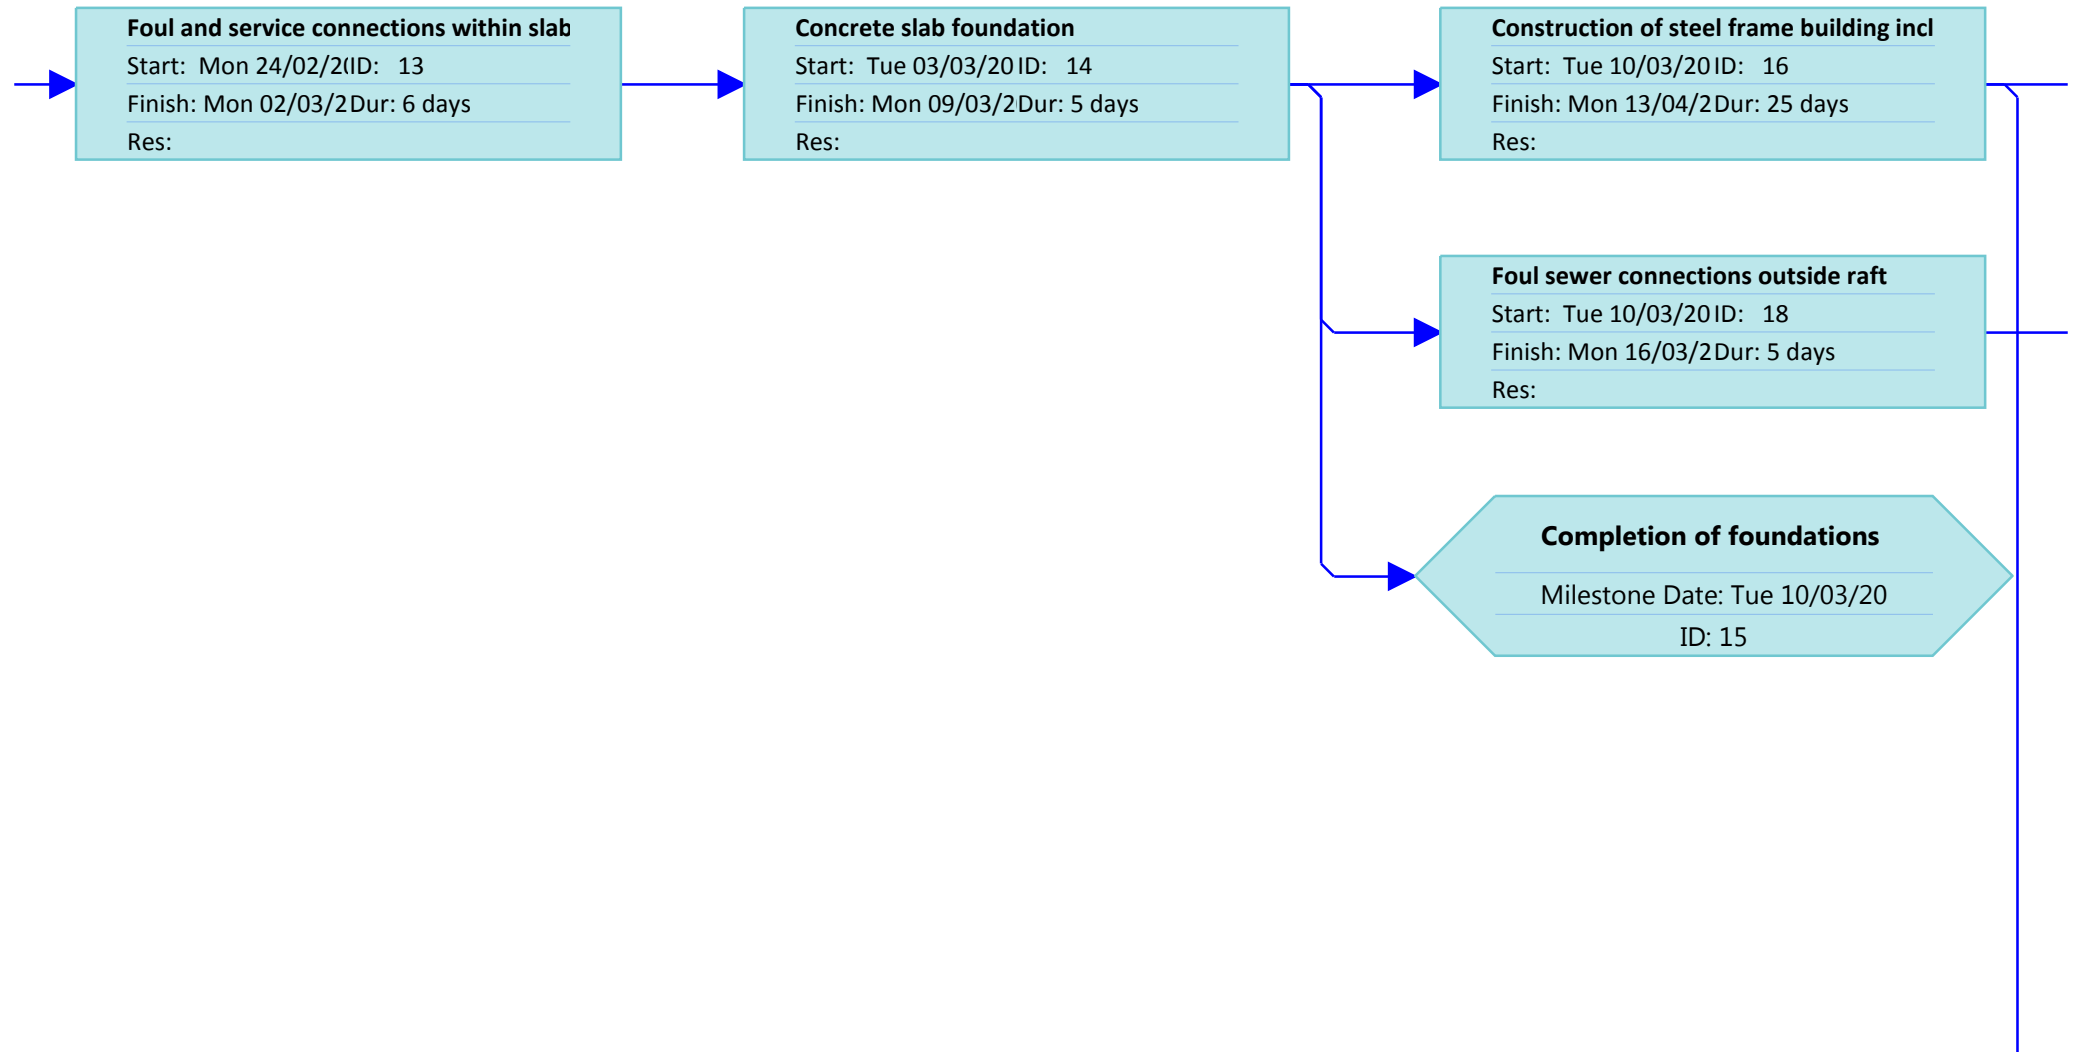





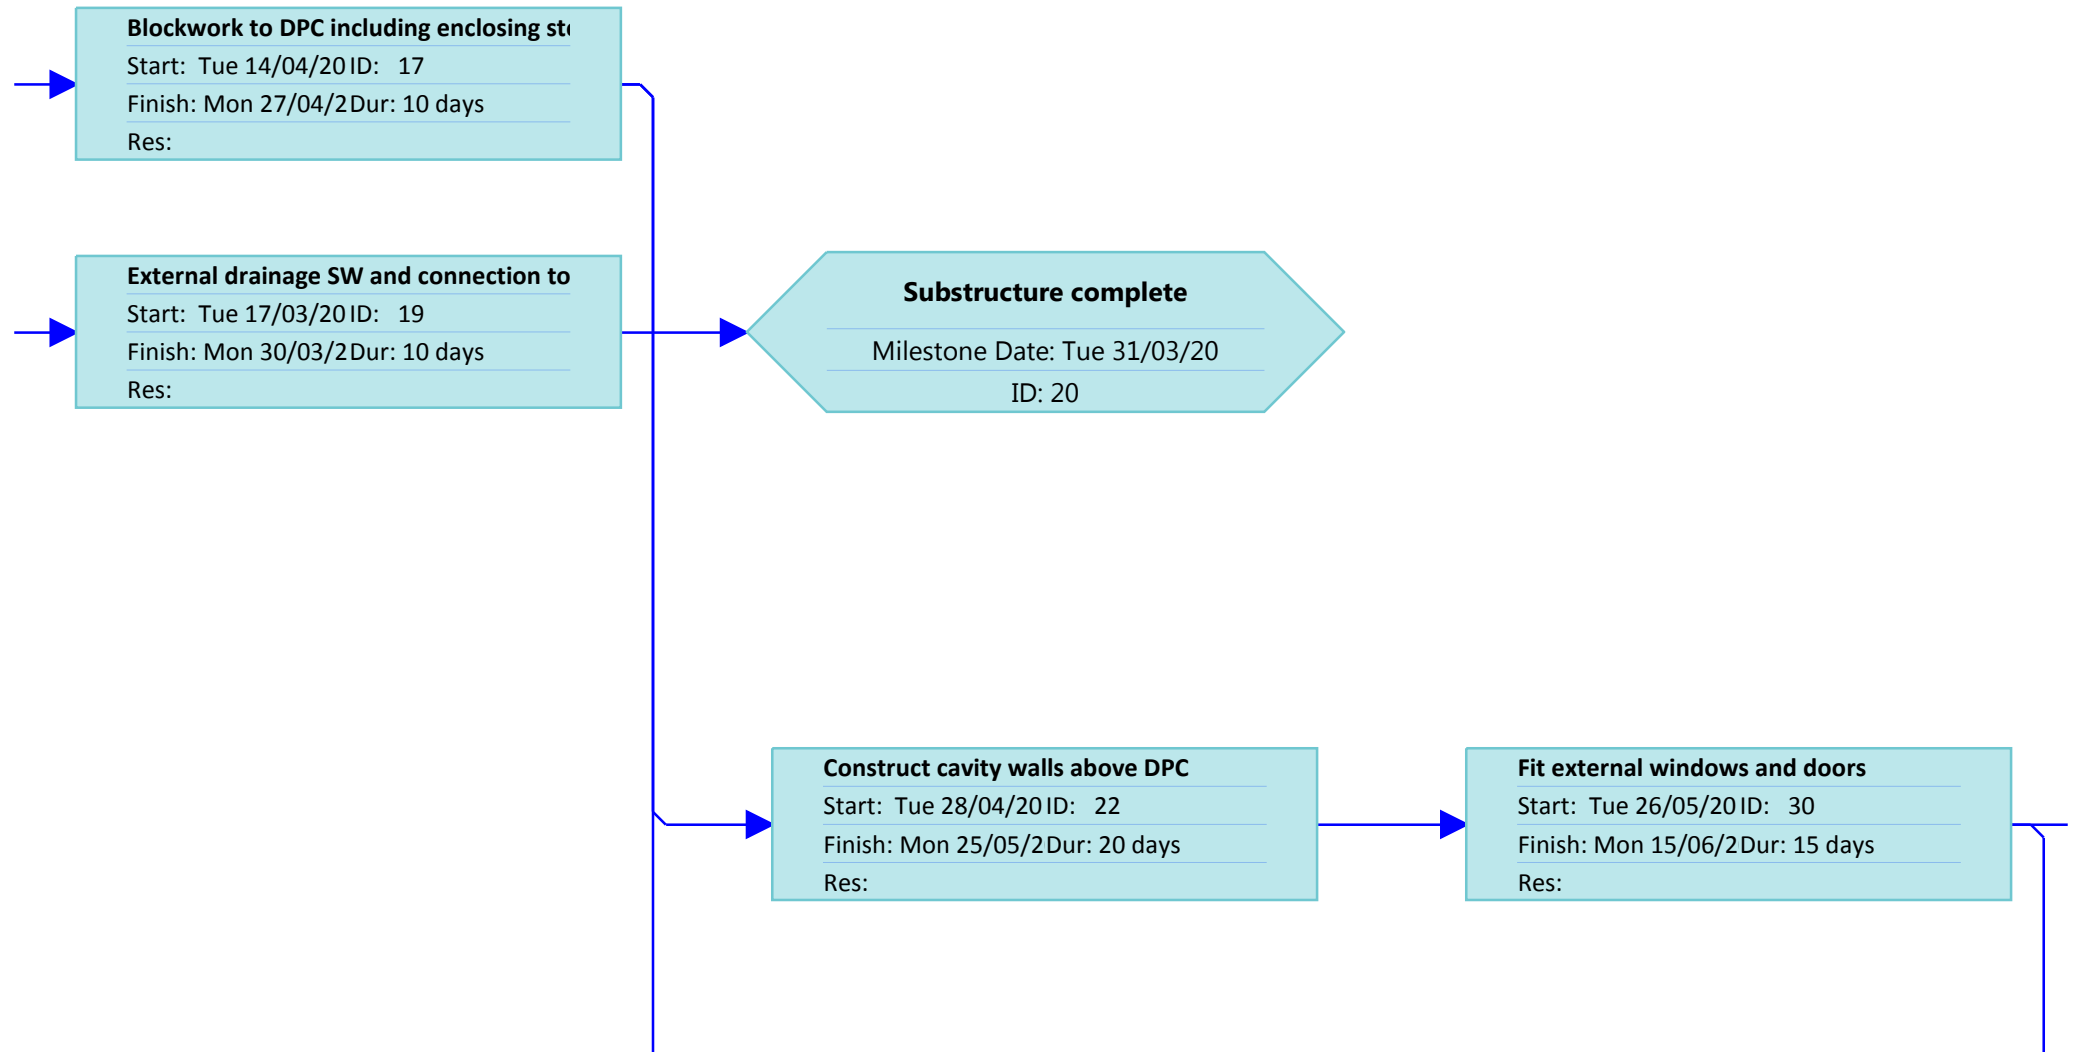


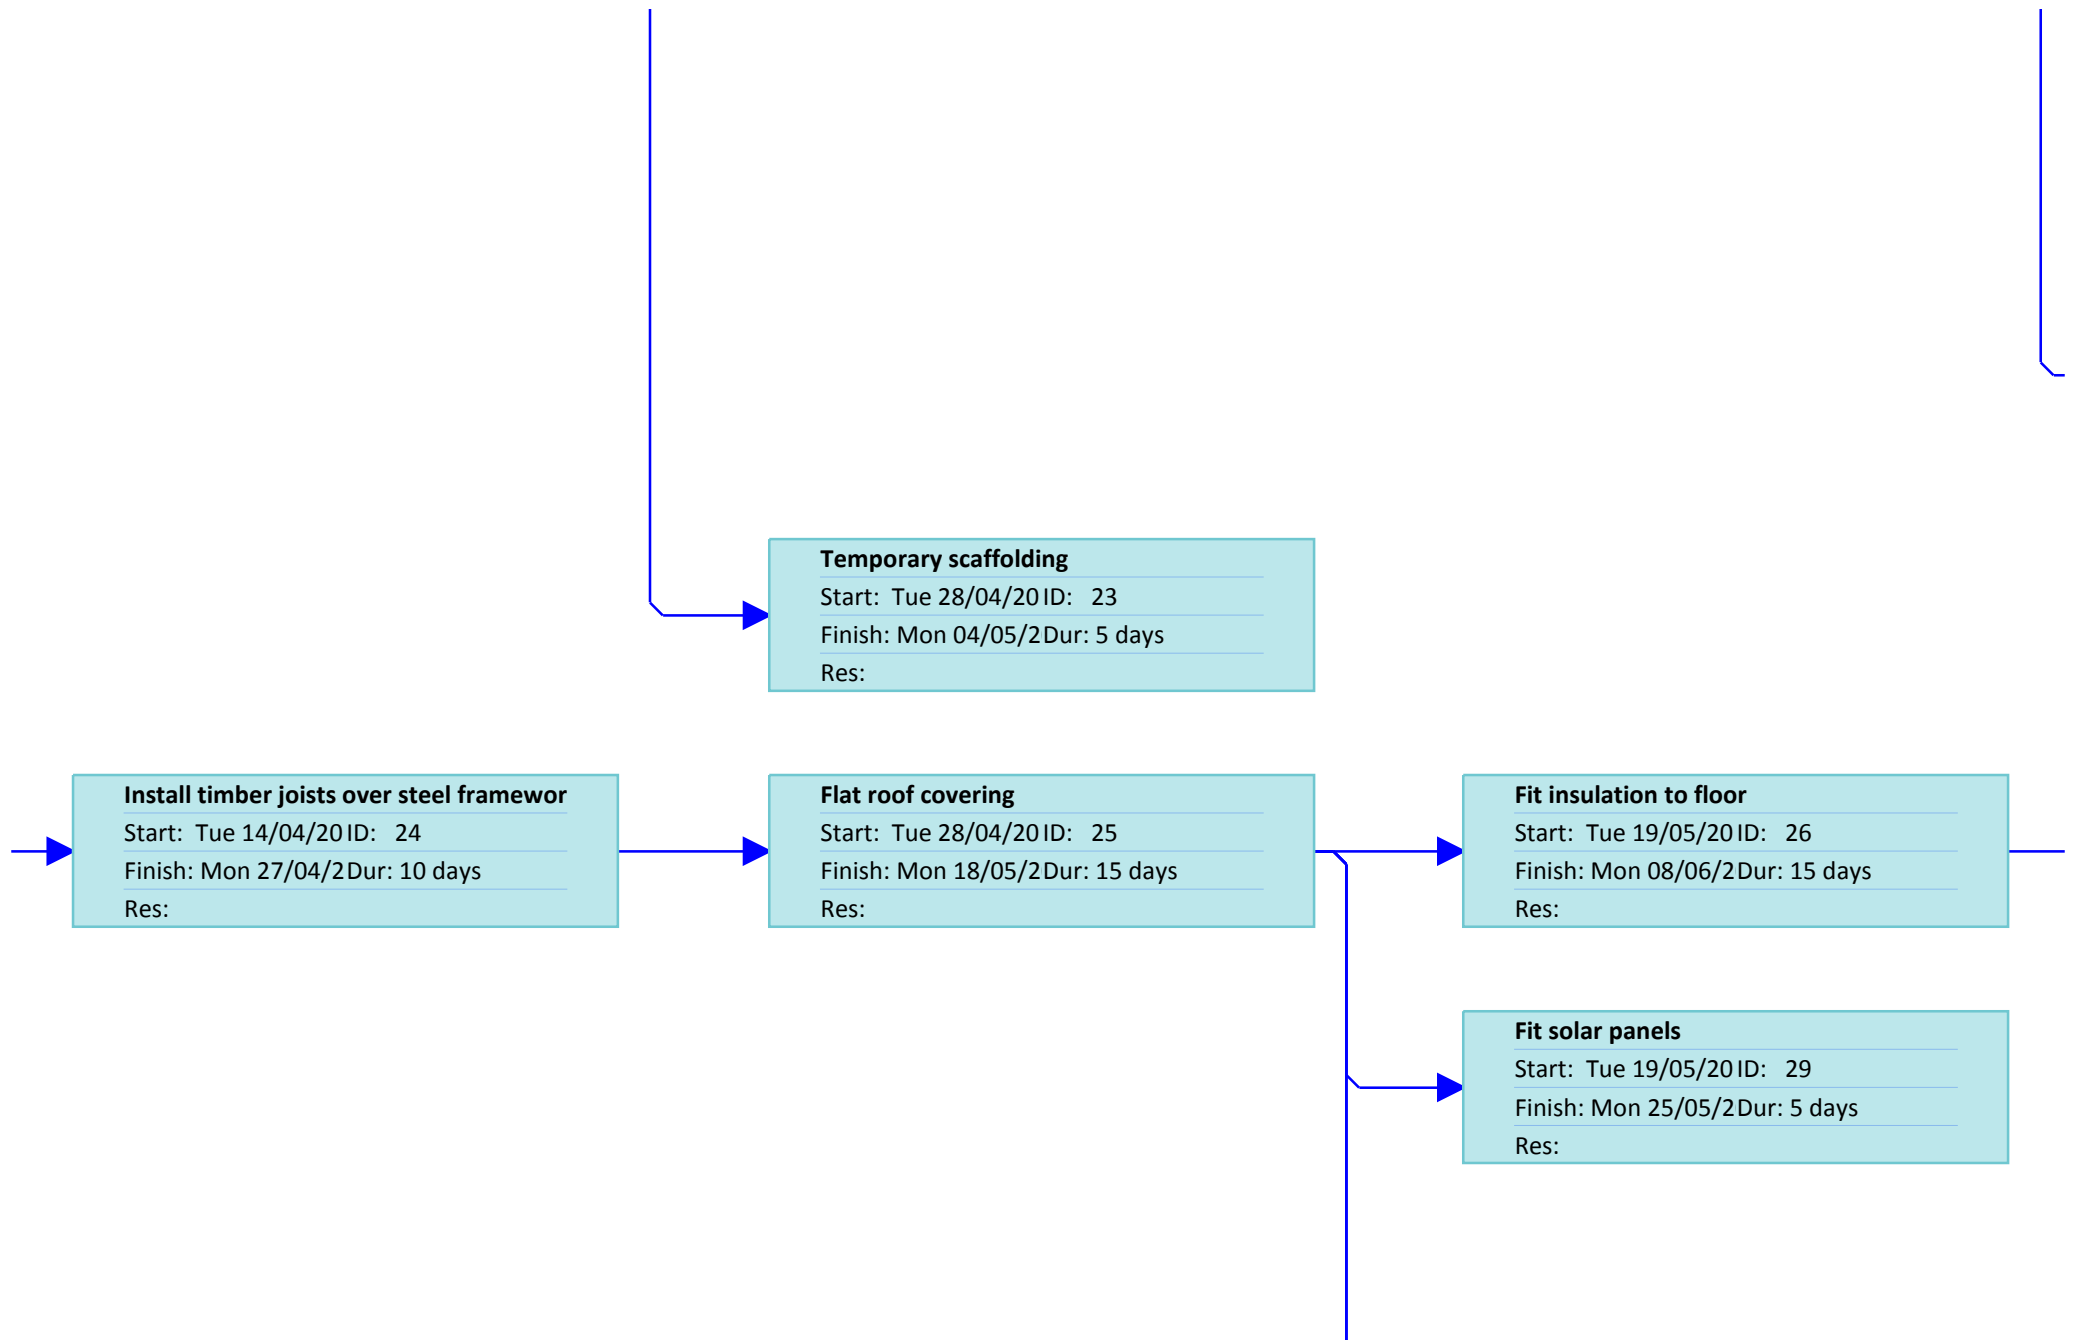

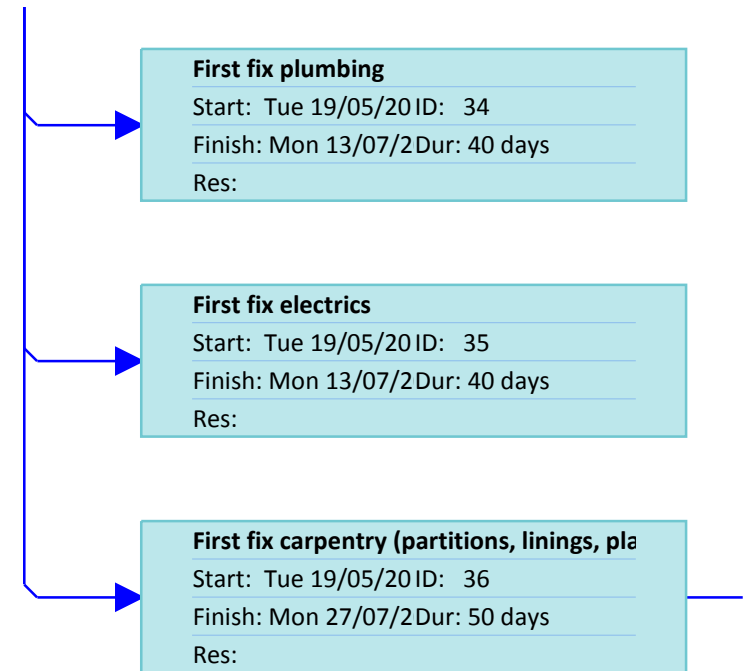

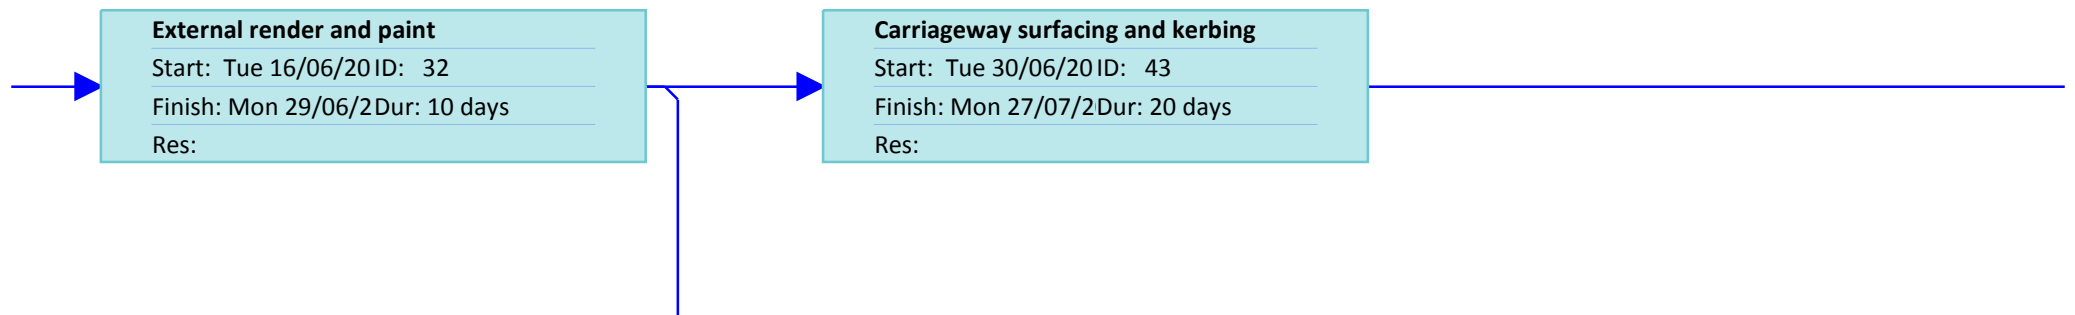

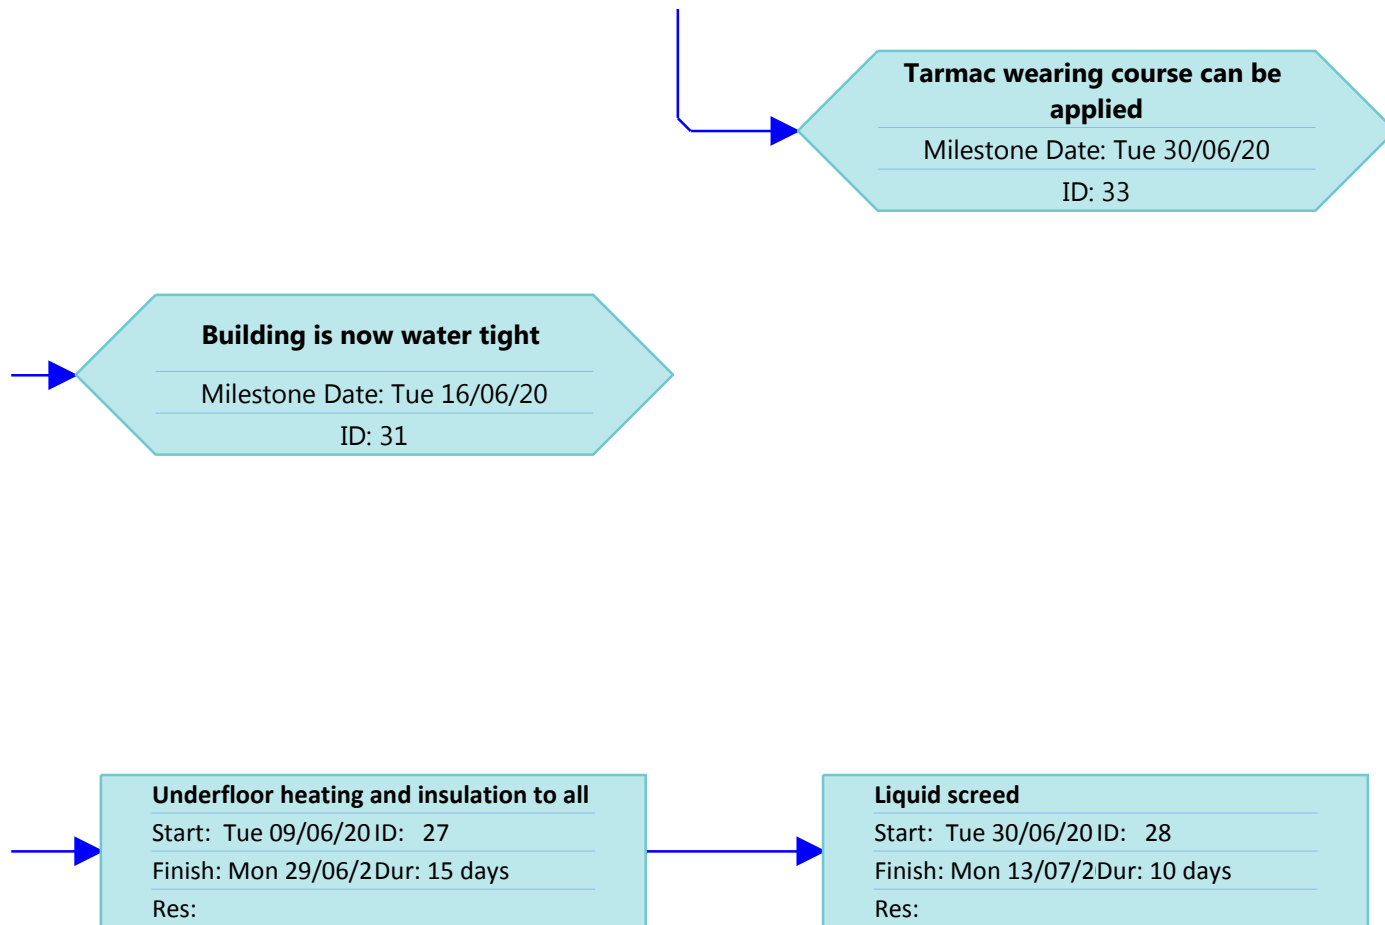

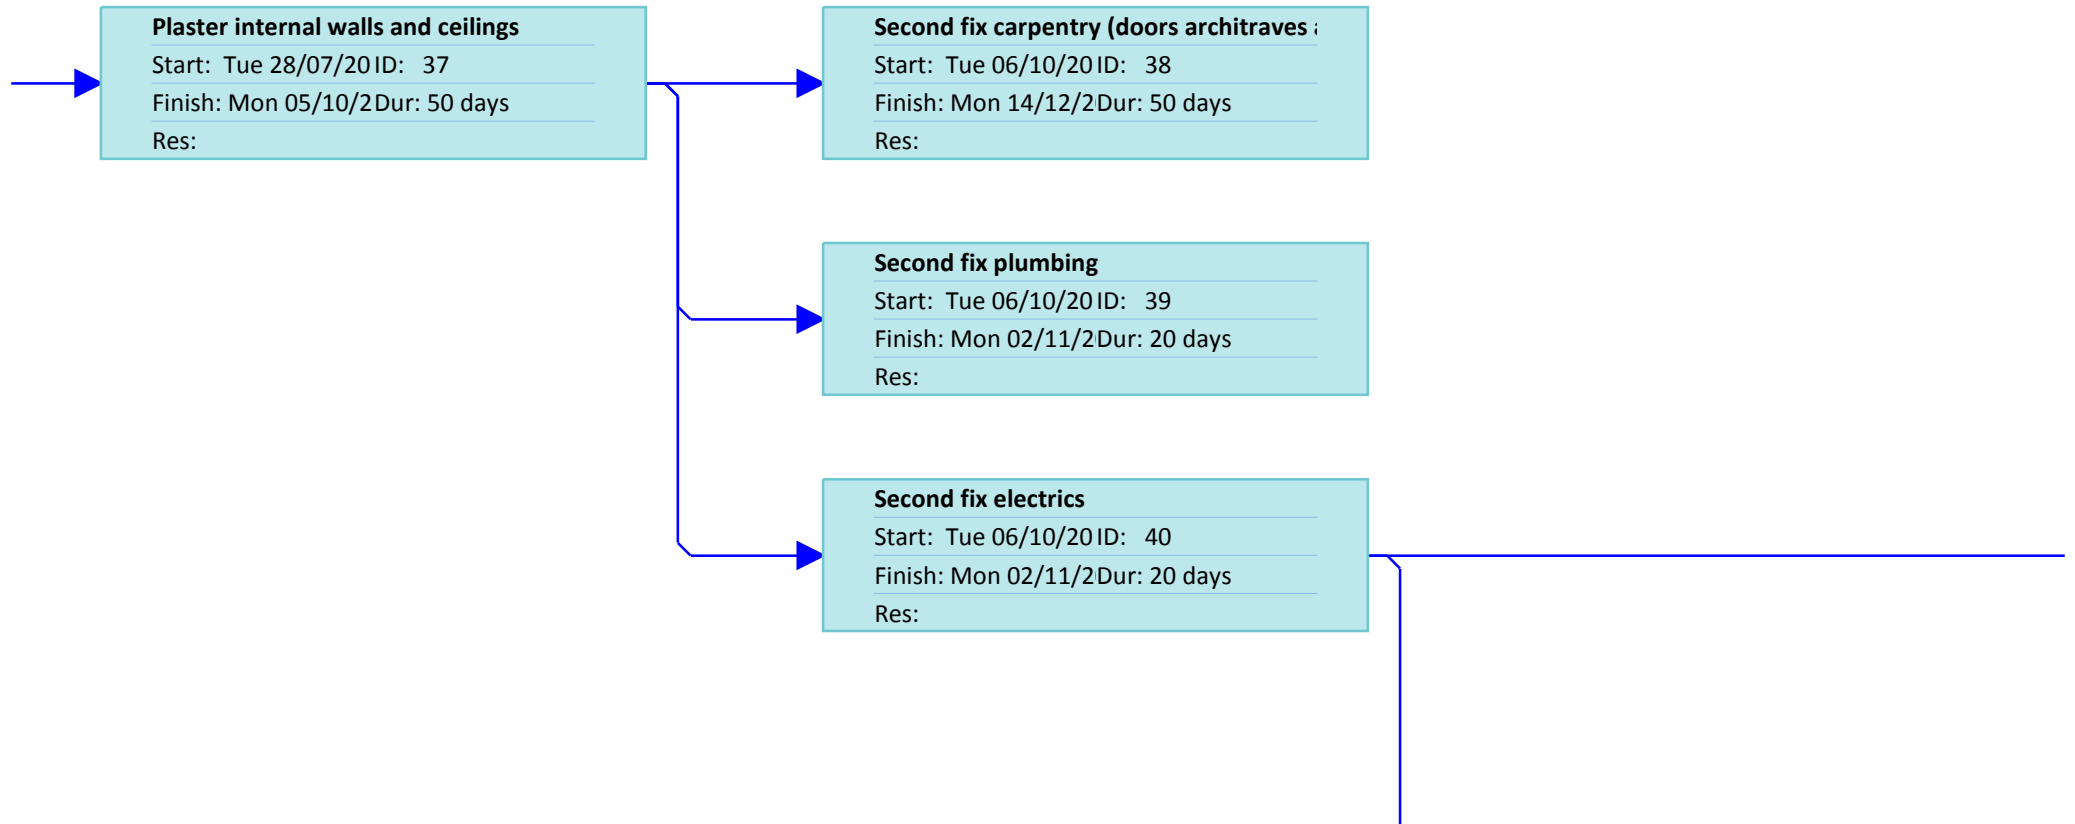





External paving

Start: Tue 28/07/20 ID: 44

Finish: Mon 10/08/2 Dur: 10 days

Res:




Finishing (tiling, fitting kitchens and inte








Start: Tue 03/11/20 ID: 42

Finish: Mon 08/02/2 Dur: 70 days

Res:





Project: Construction Programm Date: Wed 29/04/20	Critical		Critical Summary		Critical Marked		Project Summary	
	Noncritical		Summary		Marked		Highlighted Critical	
	Critical Milestone		Critical Inserted		Critical External		Highlighted Noncritical	
	Milestone		Inserted		External	
