




[illegible]

Trades Contractor, Procurement Stages, Build Stages

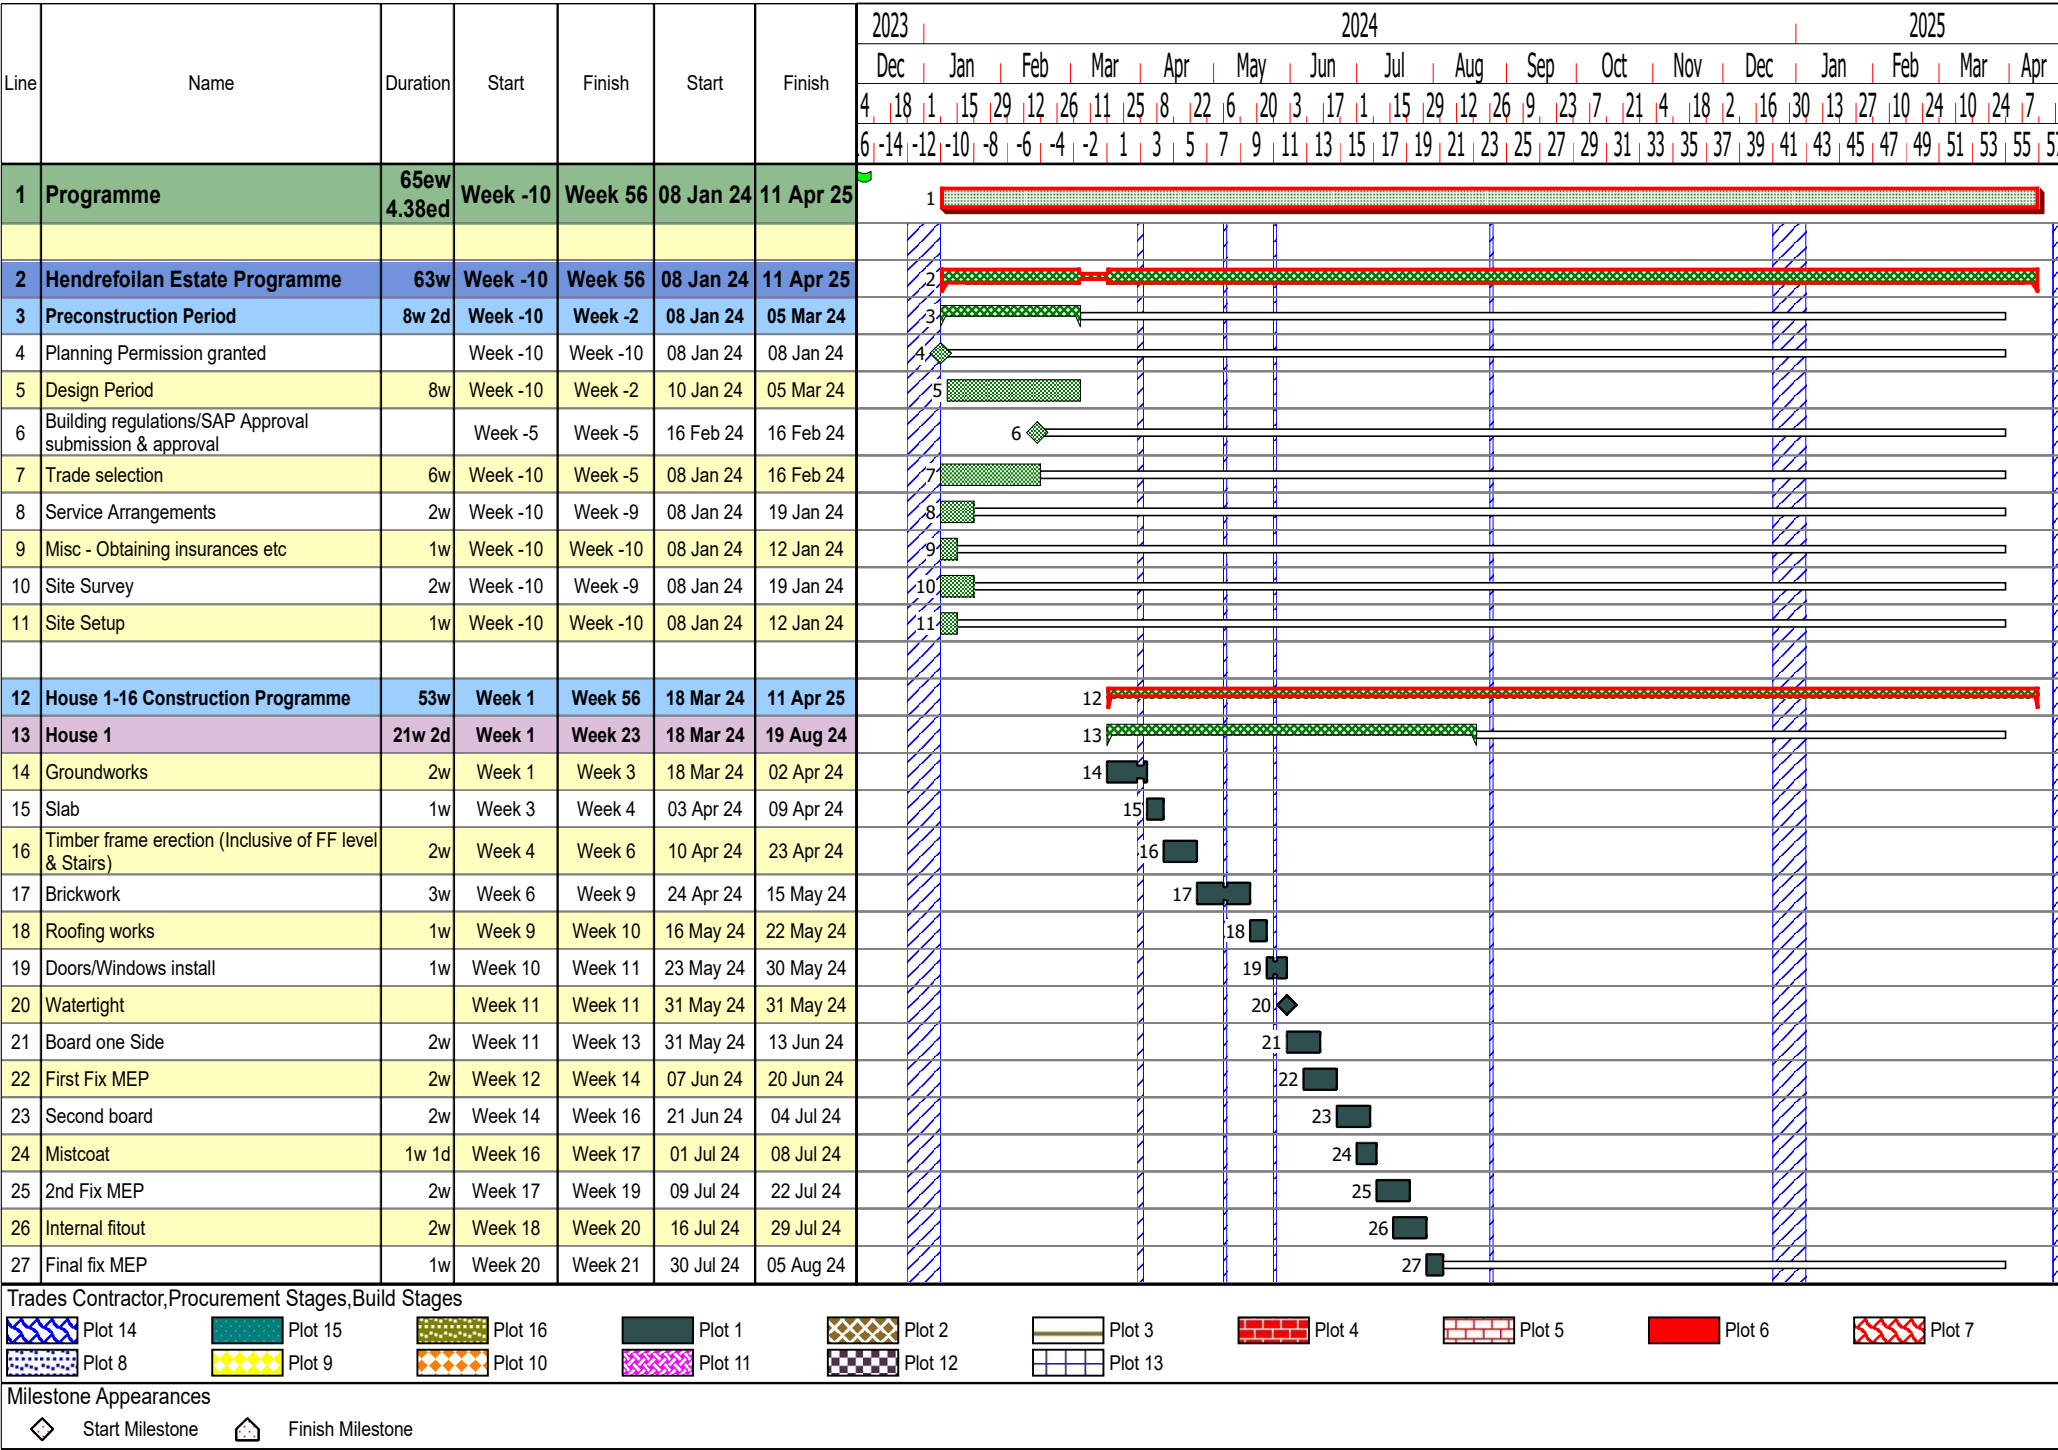

Planned by Powerproject

Line	Name	Duration	Start	Finish	Start	Finish	2023 2024 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
							2023 2024 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
							2023 2024 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
							2023 2024 2025																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
86	Roofing works	1w	Week 17	Week 18	11 Jul 24	17 Jul 24																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	

Trades Contractor,Procurement Stages,Build Stages

Plot 14

Plot 15

Plot 16

Plot 1

Plot 2

Plot 3

Plot 4

Plot 5

Plot 6

Plot 7

Plot 8

Plot 9

Plot 10

Plot 11

Plot 12

Plot 13

Milestone Appearances

Start Milestone

Finish Milestone

[illegible][illegible]

Milestone Appearances	
1990	First appearance in a major film role
1995	First appearance in a major television series
2000	First appearance in a major award-winning film
2005	First appearance in a major award-winning television series
2010	First appearance in a major award-winning film
2015	First appearance in a major award-winning television series
2020	First appearance in a major award-winning film
2025	First appearance in a major award-winning television series



Planned by Powerproject

Line	Name	Duration	Start	Finish	Start	Finish	2023																							
							2024																							
							2025																							
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
							4	18	1	15	29	12	26	11	25	8	22	6	20	3	17	1	15	29	12	26	9	23	7	21
							6	-14	-12	-10	-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31
173	Watertight		Week 29	Week 29	04 Oct 24	04 Oct 24																					173			
174	Board one Side	2w	Week 29	Week 31	04 Oct 24	17 Oct 24																						174		
175	First Fix MEP	2w	Week 30	Week 32	11 Oct 24	24 Oct 24																						175		
176	Second board	2w	Week 32	Week 34	25 Oct 24	07 Nov 24																						176		
177	Mistcoat	1w 1d	Week 34	Week 35	04 Nov 24	11 Nov 24																						177		
178	2nd Fix MEP	2w	Week 35	Week 37	12 Nov 24	25 Nov 24																						178		
179	Internal fitout	2w	Week 36	Week 38	19 Nov 24	02 Dec 24																						179		
180	Final fix MEP	1w	Week 38	Week 39	03 Dec 24	09 Dec 24																						180		
181	Finishes	2w	Week 38	Week 40	03 Dec 24	16 Dec 24																						181		
182	Snagging	1w	Week 40	Week 43	17 Dec 24	06 Jan 25																						182		
183	House 11	21w 2d	Week 21	Week 45	08 Aug 24	20 Jan 25																						183		
184	Groundworks	2w	Week 21	Week 23	08 Aug 24	21 Aug 24																						184		
185	Slab	1w	Week 23	Week 24	22 Aug 24	29 Aug 24																						185		
186	Timber frame erection (Inclusive of FF level & Stairs)	2w	Week 24	Week 26	30 Aug 24	12 Sep 24																						186		
187	Brickwork	3w	Week 26	Week 29	13 Sep 24	03 Oct 24																						187		
188	Roofing works	1w	Week 29	Week 30	04 Oct 24	10 Oct 24																						188		
189	Doors/Windows install	1w	Week 30	Week 31	11 Oct 24	17 Oct 24																						189		
190	Watertight		Week 31	Week 31	18 Oct 24	18 Oct 24																						190		
191	Board one Side	2w	Week 31	Week 33	18 Oct 24	31 Oct 24																						191		
192	First Fix MEP	2w	Week 32	Week 34	25 Oct 24	07 Nov 24																						192		
193	Second board	2w	Week 34	Week 36	08 Nov 24	21 Nov 24																						193		
194	Mistcoat	1w 1d	Week 36	Week 37	18 Nov 24	25 Nov 24																						194		
195	2nd Fix MEP	2w	Week 37	Week 39	26 Nov 24	09 Dec 24																						195		
196	Internal fitout	2w	Week 38	Week 40	03 Dec 24	16 Dec 24																						196		
197	Final fix MEP	1w	Week 40	Week 43	17 Dec 24	06 Jan 25																						197		
198	Finishes	2w	Week 40	Week 44	17 Dec 24	13 Jan 25																						198		
199	Snagging	1w	Week 44	Week 45	14 Jan 25	20 Jan 25																						199		
200	House 12	21w 2d	Week 23	Week 47	22 Aug 24	03 Feb 25																						200		
201	Groundworks	2w	Week 23	Week 25	22 Aug 24	05 Sep 24																						201		

Trades Contractor,Procurement Stages,Build Stages

Plot 14

Plot 8

Plot 15

Plot 9

Plot 16

Plot 10

Plot 1

Plot 11

Plot 2

Plot 12

Plot 3

Plot 13

Plot 4

Plot 5

Plot 6

Plot 7

Milestone Appearances

Start Milestone

Finish Milestone

Planned by Powerproject

Line	Name	Duration	Start	Finish	Start	Finish	2023																							
							2024																							
							2025																							
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
							4	18	1	15	29	12	26	11	25	8	22	6	20	3	17	1	15	29	12	26	9	23	7	21
							6	-14	-12	-10	-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31
202	Slab	1w	Week 25	Week 26	06 Sep 24	12 Sep 24																								
203	Timber frame erection (Inclusive of FF level & Stairs)	2w	Week 26	Week 28	13 Sep 24	26 Sep 24																								
204	Brickwork	3w	Week 28	Week 31	27 Sep 24	17 Oct 24																								
205	Roofing works	1w	Week 31	Week 32	18 Oct 24	24 Oct 24																								
206	Doors/Windows install	1w	Week 32	Week 33	25 Oct 24	31 Oct 24																								
207	Watertight		Week 33	Week 33	01 Nov 24	01 Nov 24																								
208	Board one Side	2w	Week 33	Week 35	01 Nov 24	14 Nov 24																								
209	First Fix MEP	2w	Week 34	Week 36	08 Nov 24	21 Nov 24																								
210	Second board	2w	Week 36	Week 38	22 Nov 24	05 Dec 24																								
211	Mistcoat	1w 1d	Week 38	Week 39	02 Dec 24	09 Dec 24																								
212	2nd Fix MEP	2w	Week 39	Week 43	10 Dec 24	06 Jan 25																								
213	Internal fitout	2w	Week 40	Week 44	17 Dec 24	13 Jan 25																								
214	Final fix MEP	1w	Week 44	Week 45	14 Jan 25	20 Jan 25																								
215	Finishes	2w	Week 44	Week 46	14 Jan 25	27 Jan 25																								
216	Snagging	1w	Week 46	Week 47	28 Jan 25	03 Feb 25																								
217	House 13	21w 2d	Week 25	Week 48	05 Sep 24	14 Feb 25																								
218	Groundworks	2w	Week 25	Week 27	05 Sep 24	18 Sep 24																								
219	Slab	1w	Week 27	Week 28	19 Sep 24	25 Sep 24																								
220	Timber frame erection (Inclusive of FF level & Stairs)	2w	Week 28	Week 30	26 Sep 24	09 Oct 24																								
221	Brickwork	3w	Week 30	Week 33	10 Oct 24	30 Oct 24																								
222	Roofing works	1w	Week 33	Week 34	31 Oct 24	06 Nov 24																								
223	Doors/Windows install	1w	Week 34	Week 35	07 Nov 24	13 Nov 24																								
224	Watertight		Week 35	Week 35	14 Nov 24	14 Nov 24																								
225	Board one Side	2w	Week 35	Week 37	14 Nov 24	27 Nov 24																								
226	First Fix MEP	2w	Week 36	Week 38	21 Nov 24	04 Dec 24																								
227	Second board	2w	Week 38	Week 40	05 Dec 24	18 Dec 24																								
228	Mistcoat	1w 1d	Week 39	Week 40	13 Dec 24	20 Dec 24																								
229	2nd Fix MEP	2w	Week 43	Week 44	06 Jan 25	17 Jan 25																								
230	Internal fitout	2w	Week 44	Week 45	13 Jan 25	24 Jan 25																								

Trades Contractor,Procurement Stages,Build Stages

 Plot 14

 Plot 15

 Plot 16

 Plot 1

 Plot 2

 Plot 3

 Plot 4

 Plot 5

 Plot 6

 Plot 7

 Plot 8

 Plot 9

 Plot 10

 Plot 11

 Plot 12

 Plot 13

Milestone Appearances

 Start Milestone

 Finish Milestone

Line	Name	Duration	Start	Finish	Start	Finish	2023																							
							2024																							
							2025																							
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
							4	18	1	15	29	12	26	11	25	8	22	6	20	3	17	1	15	29	12	26	9	23	7	21
							6	-14	-12	-10	-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31
231	Final fix MEP	1w	Week 46	Week 46	27 Jan 25	31 Jan 25																								
232	Finishes	2w	Week 46	Week 47	27 Jan 25	07 Feb 25																								
233	Snagging	1w	Week 48	Week 48	10 Feb 25	14 Feb 25																								
234	House 14	21w 2d	Week 27	Week 50	19 Sep 24	28 Feb 25																								
235	Groundworks	2w	Week 27	Week 29	19 Sep 24	02 Oct 24																								
236	Slab	1w	Week 29	Week 30	03 Oct 24	09 Oct 24																								
237	Timber frame erection (Inclusive of FF level & Stairs)	2w	Week 30	Week 32	10 Oct 24	23 Oct 24																								
238	Brickwork	3w	Week 32	Week 35	24 Oct 24	13 Nov 24																								
239	Roofing works	1w	Week 35	Week 36	14 Nov 24	20 Nov 24																								
240	Doors/Windows install	1w	Week 36	Week 37	21 Nov 24	27 Nov 24																								
241	Watertight		Week 37	Week 37	28 Nov 24	28 Nov 24																								
242	Board one Side	2w	Week 37	Week 39	28 Nov 24	11 Dec 24																								
243	First Fix MEP	2w	Week 38	Week 40	05 Dec 24	18 Dec 24																								
244	Second board	2w	Week 40	Week 44	19 Dec 24	15 Jan 25																								
245	Mistcoat	1w 1d	Week 43	Week 44	10 Jan 25	17 Jan 25																								
246	2nd Fix MEP	2w	Week 45	Week 46	20 Jan 25	31 Jan 25																								
247	Internal fitout	2w	Week 46	Week 47	27 Jan 25	07 Feb 25																								
248	Final fix MEP	1w	Week 48	Week 48	10 Feb 25	14 Feb 25																								
249	Finishes	2w	Week 48	Week 49	10 Feb 25	21 Feb 25																								
250	Snagging	1w	Week 50	Week 50	24 Feb 25	28 Feb 25																								
251	House 15	21w 2d	Week 29	Week 52	03 Oct 24	14 Mar 25																								
252	Groundworks	2w	Week 29	Week 31	03 Oct 24	16 Oct 24																								
253	Slab	1w	Week 31	Week 32	17 Oct 24	23 Oct 24																								
254	Timber frame erection (Inclusive of FF level & Stairs)	2w	Week 32	Week 34	24 Oct 24	06 Nov 24																								
255	Brickwork	3w	Week 34	Week 37	07 Nov 24	27 Nov 24																								
256	Roofing works	1w	Week 37	Week 38	28 Nov 24	04 Dec 24																								
257	Doors/Windows install	1w	Week 38	Week 39	05 Dec 24	11 Dec 24																								
258	Watertight		Week 39	Week 39	12 Dec 24	12 Dec 24																								
259	Board one Side	2w	Week 39	Week 43	12 Dec 24	08 Jan 25																								

Trades Contractor,Procurement Stages,Build Stages

 Plot 14

 Plot 15

 Plot 16

 Plot 1

 Plot 2

 Plot 3

 Plot 4

 Plot 5

 Plot 6

 Plot 7

 Plot 8

 Plot 9

 Plot 10

 Plot 11

 Plot 12

 Plot 13

Milestone Appearances

 Start Milestone

 Finish Milestone

Line	Name	Duration	Start	Finish	Start	Finish	2023																							
							2024																							
							2025																							
							Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
							4	18	1	15	29	12	26	11	25	8	22	6	20	3	17	1	15	29	12	26	9	23	7	21
							6	-14	-12	-10	-8	-6	-4	-2	1	3	5	7	9	11	13	15	17	19	21	23	25	27	29	31
260	First Fix MEP	2w	Week 40	Week 44	19 Dec 24	15 Jan 25																								
261	Second board	2w	Week 44	Week 46	16 Jan 25	29 Jan 25																								
262	Mistcoat	1w 1d	Week 45	Week 46	24 Jan 25	31 Jan 25																								
263	2nd Fix MEP	2w	Week 47	Week 48	03 Feb 25	14 Feb 25																								
264	Internal fitout	2w	Week 48	Week 49	10 Feb 25	21 Feb 25																								
265	Final fix MEP	1w	Week 50	Week 50	24 Feb 25	28 Feb 25																								
266	Finishes	2w	Week 50	Week 51	24 Feb 25	07 Mar 25																								
267	Snagging	1w	Week 52	Week 52	10 Mar 25	14 Mar 25																								
268	House 16	23w 2d	Week 31	Week 56	17 Oct 24	11 Apr 25																								
269	Groundworks	2w	Week 31	Week 33	17 Oct 24	30 Oct 24																								
270	Slab	1w	Week 33	Week 34	31 Oct 24	06 Nov 24																								
271	Timber frame erection (Inclusive of FF level & Stairs)	2w	Week 34	Week 36	07 Nov 24	20 Nov 24																								
272	Brickwork	3w	Week 36	Week 39	21 Nov 24	11 Dec 24																								
273	Roofing works	1w	Week 39	Week 40	12 Dec 24	18 Dec 24																								
274	Doors/Windows install	1w	Week 40	Week 43	19 Dec 24	08 Jan 25																								
275	Watertight		Week 43	Week 43	09 Jan 25	09 Jan 25																								
276	Board one Side	2w	Week 43	Week 45	09 Jan 25	22 Jan 25																								
277	First Fix MEP	2w	Week 44	Week 46	16 Jan 25	29 Jan 25																								
278	Second board	2w	Week 46	Week 48	30 Jan 25	12 Feb 25																								
279	Mistcoat	1w 1d	Week 47	Week 48	07 Feb 25	14 Feb 25																								
280	2nd Fix MEP	2w	Week 49	Week 50	17 Feb 25	28 Feb 25																								
281	Internal fitout	2w	Week 50	Week 51	24 Feb 25	07 Mar 25																								
282	Final fix MEP	1w	Week 52	Week 52	10 Mar 25	14 Mar 25																								
283	Finishes	2w	Week 52	Week 53	10 Mar 25	21 Mar 25																								
284	Snagging	1w	Week 54	Week 54	24 Mar 25	28 Mar 25																								
285	Handover		Week 56	Week 56	11 Apr 25	11 Apr 25																								
286	Final Snag of houses 1-16	2w	Week 55	Week 56	31 Mar 25	11 Apr 25																								

Trades Contractor,Procurement Stages,Build Stages

 Plot 14

 Plot 15

 Plot 16

 Plot 1

 Plot 2

 Plot 3

 Plot 4

 Plot 5

 Plot 6

 Plot 7

 Plot 8

 Plot 9

 Plot 10

 Plot 11

 Plot 12

 Plot 13

Milestone Appearances

 Start Milestone

 Finish Milestone
