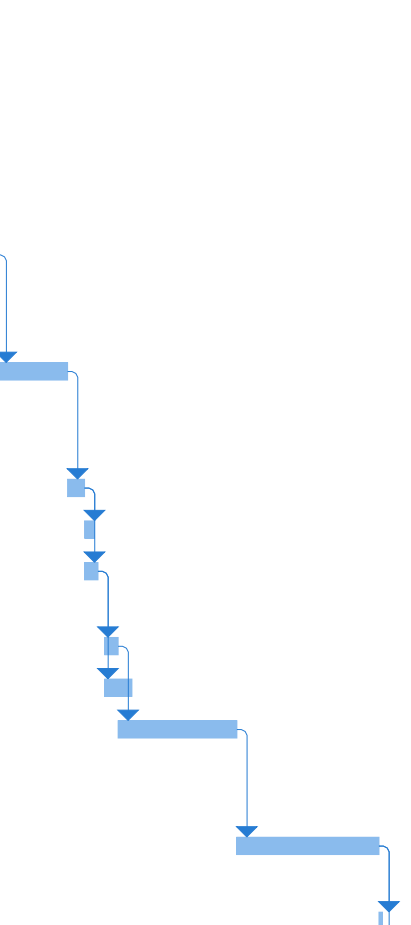


ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023							Half 1, 2024					
					J	A	S	O	N	D	J									
1			Theatre building	1 day	Mon 10/07/23	Mon 10/07/23														
2			RIBA STAGE 0																	
3			Project starts	1 day	Wed 12/07/23	Wed 12/07/23	1													
4			client meetings for requirements	2 days	Mon 22/07/23	Tue 23/07/23	2													
5			risk assessments	10 days	Thu 13/07/23	Wed 26/07/23														
6			project cost plan	10 days	Thu 27/07/23	Wed 09/08/23														
7			information about site surveys & what is needed	10 days	Thu 27/07/23	Wed 09/08/23	5													
8			work out and sort out a project programme	15 days	Thu 10/08/23	Wed 30/08/23	6													
9			RIBA STAGE 1																	
10			objective and brief for project	3 days	Thu 31/08/23	Mon 04/09/23														
11			gather information on the site	3 days	Tue 05/09/23	Thu 07/09/23	10													
12			understand the outcome of the project	4 days	Tue 05/09/23	Fri 08/09/23	10													
13			sustainability expectations	4 days	Mon 11/09/23	Thu 14/09/23	12													
14			project execution plan	6 days	Mon 11/09/23	Mon 18/09/23	12													
15			site information gathered and reviewed	25 days	Fri 15/09/23	Thu 19/10/23	13													
16			RIBA STAGES 2				15													
17			concept design and cost plans presented	30 days	Fri 20/10/23	Thu 30/11/23	15													
18			consult the planning authority	1 day	Fri 01/12/23	Fri 01/12/23	17													

Project: intergrated programme

Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone

Deadline

Progress

Manual Progress

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023							Half 1, 2024
					J	A	S	O	N	D	J				
19			reviewal and approval of the design	5 days	Fri 01/12/23	Thu 07/12/23	17								
20			specifications outlined	4 days	Fri 08/12/23	Wed 13/12/23	19								
21			finalised project brief	4 days	Thu 14/12/23	Tue 19/12/23	20								
22			RIBA STAGE 3		Wed 20/12/23										
23			Develop structural and architectural design	14 days	Wed 20/12/23	Mon 08/01/24	21								
24			design programme	6 days	Wed 20/12/23	Wed 27/12/23	21								
25			RIBA STAGE 4	1 day	Thu 28/12/23	Thu 28/12/23	24								
26			BIM review	10 days	Thu 28/12/23	Wed 10/01/24	24								
27			developing technical design	15 days	Thu 11/01/24	Wed 31/01/24	26								
28			building regulations	10 days	Thu 11/01/24	Wed 24/01/24	26								
29			RIBA STAGE 5												
30			pre construction												
31			set up site entrance	1 day	Thu 25/01/24	Thu 25/01/24	28								
32			set up site perimeter	1 day	Fri 26/01/24	Fri 26/01/24	31								
33			ecology survey	10 days?	Mon 04/03/24	Fri 15/03/24	32								
34			Service diversions	80 days?	Mon 11/12/23	Fri 29/03/24	16								
35			Demolitions	15 days	Mon 01/04/24	Fri 19/04/24	33								
36			Site clearance	4 days	Mon 22/04/24	Thu 25/04/24	35								
37			Compound set up	1 day	Fri 26/04/24	Fri 26/04/24	36								
38			parking facilities	1 day	Fri 26/04/24	Fri 26/04/24	36								
39			material stores	1 day	Fri 26/04/24	Fri 26/04/24	36								

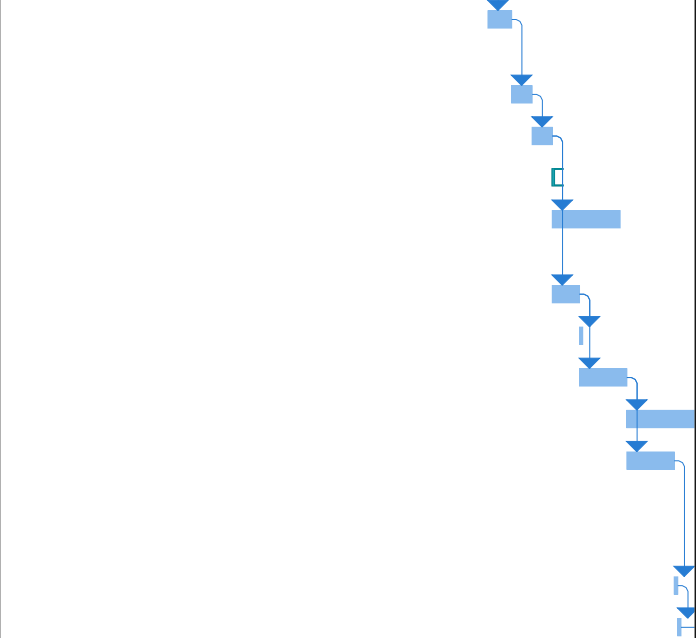

Project: intergrated programme

Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023						Half 1, 2024
					J	A	S	O	N	D	J			
40			Access/haul roads	2 days	Fri 26/04/24	Mon 29/04/24	36							
41			Temporary Services											
42			Temporary Water Supply	2 days	Tue 30/04/24	Wed 01/05/24	40							
43			Temporary Gas Supply	2 days	Tue 30/04/24	Wed 01/05/24	40							
44			Temporary Electricity Supply	2 days	Thu 02/05/24	Fri 03/05/24	43							
45			Temporary Drainage	4 days	Thu 02/05/24	Tue 07/05/24	43							
46			Security											
47			Security Equipment	2 days	Wed 08/05/24	Thu 09/05/24	45							
48			Fences and Gates	2 days	Wed 08/05/24	Thu 09/05/24	45							
49			Setting out											
50			Marking out	1 day	Fri 10/05/24	Fri 10/05/24	48							
51			Setting levels	3 days	Mon 13/05/24	Wed 15/05/24	50							
52			Excavators in	2 days	Thu 16/05/24	Fri 17/05/24	51							
53			Foundations											
54			excavate for foundations	4 days	Mon 20/05/24	Thu 23/05/24	52							
55			piles installed	4 days	Fri 24/05/24	Wed 29/05/24	54							
56			pile caps	2 days	Thu 30/05/24	Fri 31/05/24	55							
57			pour foundations	2 days	Mon 03/06/24	Tue 04/06/24	56							
58			final inspection	1 day	Wed 05/06/24	Wed 05/06/24	57							
59			install service connections	12 days	Thu 06/06/24	Fri 21/06/24	58							
60			drainage installation, run test, backfill	5 days	Mon 24/06/24	Fri 28/06/24	59							
61			Superstructure											

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline

Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023						Half 1, 2024			
					J	A	S	O	N	D	J						
62			erect shutter for concrete	4 days	Mon 01/07/24	Thu 04/07/24	60										
63			put in structural steel	3 days	Fri 05/07/24	Tue 09/07/24	62										
64			pour concrete	10 days	Wed 10/07/24	Tue 23/07/24	63										
65			remover shutters	2 days	Wed 24/07/24	Thu 25/07/24	64										
66			Scaffolding	2 days	Fri 26/07/24	Mon 29/07/24	65										
67			internal columns poured	3 days	Wed 24/07/24	Fri 26/07/24	64										
68			inspections	1 day	Tue 30/07/24	Tue 30/07/24	66										
69			balcony railings fitted	4 days	Wed 31/07/24	Mon 05/08/24	68										
70			roof trusses	2 days	Tue 06/08/24	Wed 07/08/24	69										
71			Roof construction	8 days	Thu 08/08/24	Mon 19/08/24	70										
72			Roof covering	2 days	Tue 20/08/24	Wed 21/08/24	71										
73			gutter installation	3 days	Thu 22/08/24	Mon 26/08/24	72										
74			roof inspection	1 day	Tue 27/08/24	Tue 27/08/24	73										
75			external Windows & doors	21 days	Wed 28/08/24	Wed 25/09/24	74										
76			External mastic/sealant	6 days	Thu 26/09/24	Thu 03/10/24	75										
77			external light fought	3 days	Thu 26/09/24	Mon 30/09/24	75										
78			fire inspection	1 day	Tue 01/10/24	Tue 01/10/24	77										
79			health and safety inspection	1 day	Tue 01/10/24	Tue 01/10/24	77										
80			client inspection	1 day	Wed 02/10/24	Wed 02/10/24	79										
81			Scaffold dismantle	3 days	Thu 03/10/24	Mon 07/10/24	80										
82			Internal work														
83			stair installation	4 days	Tue 08/10/24	Fri 11/10/24	81										

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 4

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023						Half 1, 2024
					J	A	S	O	N	D	J			
84			First fix carpentry	14 days	Mon 14/10/24	Thu 31/10/24	83							
85			stage construction	7 days	Fri 01/11/24	Mon 11/11/24	84							
86			First fix plumbing	7 days	Fri 01/11/24	Mon 11/11/24	84							
87			First fix electrics	13 days	Fri 01/11/24	Tue 19/11/24	84							
88			Drylining/wall finishes	10 days	Wed 20/11/24	Tue 03/12/24	87							
89			service installation	8 days	Wed 20/11/24	Fri 29/11/24	87							
90			inspection	1 day	Mon 02/12/24	Mon 02/12/24	89							
91			plaster	10 days	Tue 03/12/24	Mon 16/12/24	90							
92			Second fix carpentry	12 days	Tue 17/12/24	Wed 01/01/25	91							
93			Second fix plumbing	10 days	Thu 02/01/25	Wed 15/01/25	92							
94			Second fix electrical	9 days	Thu 02/01/25	Tue 14/01/25	92							
95			health & safety inspection	1 day	Wed 15/01/25	Wed 15/01/25	94							
96			lift installation	7 days	Thu 16/01/25	Fri 24/01/25	95							
97			lighting fixtures	10 days	Thu 16/01/25	Wed 29/01/25	95							
98			acoustic ceiling panels	5 days	Mon 27/01/25	Fri 31/01/25	96							
99			fitting the seating for the theatre	5 days	Mon 03/02/25	Fri 07/02/25	98							
100			Bathroom fixings	7 days	Mon 03/02/25	Tue 11/02/25	98							
101			bar/kitchen fit out	5 days	Mon 10/02/25	Fri 14/02/25	99							
102			Painting and Decorating	20 days	Mon 17/02/25	Fri 14/03/25	101							
103			flooring and carpet	11 days	Mon 17/03/25	Mon 31/03/25	102							
104			Internal fittings	10 days	Tue 01/04/25	Mon 14/04/25	103							

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone















Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only















External Tasks

External Milestone

Deadline


Progress

Manual Progress











ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023						Half 1, 2024
					J	A	S	O	N	D	J			
105			flood light fixtures for the stages	1 day	Tue 15/04/25	Tue 15/04/25	104							
106			PA system	1 day	Tue 15/04/25	Tue 15/04/25	104							
107			COMMS fittings	1 day	Tue 15/04/25	Tue 15/04/25	104							
108			curtains fitted & chain drive system	2 days	Wed 16/04/25	Thu 17/04/25	107							
109			sound system	2 days	Wed 16/04/25	Thu 17/04/25	107							
110			internal snagging and clean	10 days	Fri 18/04/25	Thu 01/05/25	109							
111			acoustic/air pressure tests	1 day	Fri 02/05/25	Fri 02/05/25	110							
112			final snagging and cleaning	1 day	Mon 05/05/25	Mon 05/05/25	111							
113			final inspection on everything	1 day	Tue 06/05/25	Tue 06/05/25	112							
114			Externals											
115			ground leveled	3 days	Wed 07/05/25	Fri 09/05/25	113							
116			area of footpaths measured out	1 day	Mon 12/05/25	Mon 12/05/25	115							
117			stoned and compacted to height	4 days	Tue 13/05/25	Fri 16/05/25	116							
118			brick pavings laid	10 days	Mon 19/05/25	Fri 30/05/25	117							
119			marbal slabs laid	12 days	Mon 19/05/25	Tue 03/06/25	117							
120			Open air amphitheatre construction	10 days	Wed 04/06/25	Tue 17/06/25	119							
121			trees planted	3 days	Wed 18/06/25	Fri 20/06/25	120							
122			topsoil laid to level	2 days	Mon 23/06/25	Tue 24/06/25	121							

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 6

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Half 2, 2023						Half 1, 2024
								J	A	S	O	N	D	J
123			grass for bethany gardens	2 days	Wed 25/06/2	Thu 26/06/2	122							
124			bethany gardens complete	1 day	Fri 27/06/25	Fri 27/06/25	123							
125			final landsacpe inspection	1 day	Mon 30/06/2	Mon 30/06/2	124							
126			internal furnishings comple	14 days	Mon 30/06/2	Thu 17/07/2	124							
127			RIBA Stage 6				126							
128			final inspection	1 day?	Fri 18/07/25	Fri 18/07/25	126							
129			Handover	1 day?	Mon 21/07/2	Mon 21/07/2	128							
130			RIBA Stage 7											
131			after occupancy evaluation	1 day	Tue 22/07/2	Tue 22/07/2	129							
132			Aftercare plan	3 days	Wed 23/07/2	Fri 25/07/25	131							
133			sustainability outcome	1 day	Mon 28/07/2	Mon 28/07/2	132							
134			project outcome report	5 days	Tue 29/07/2	Mon 04/08/2	133							

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks


External Milestone


Deadline

Progress


Manual Progress


Page 7


Project: intergrated programme Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

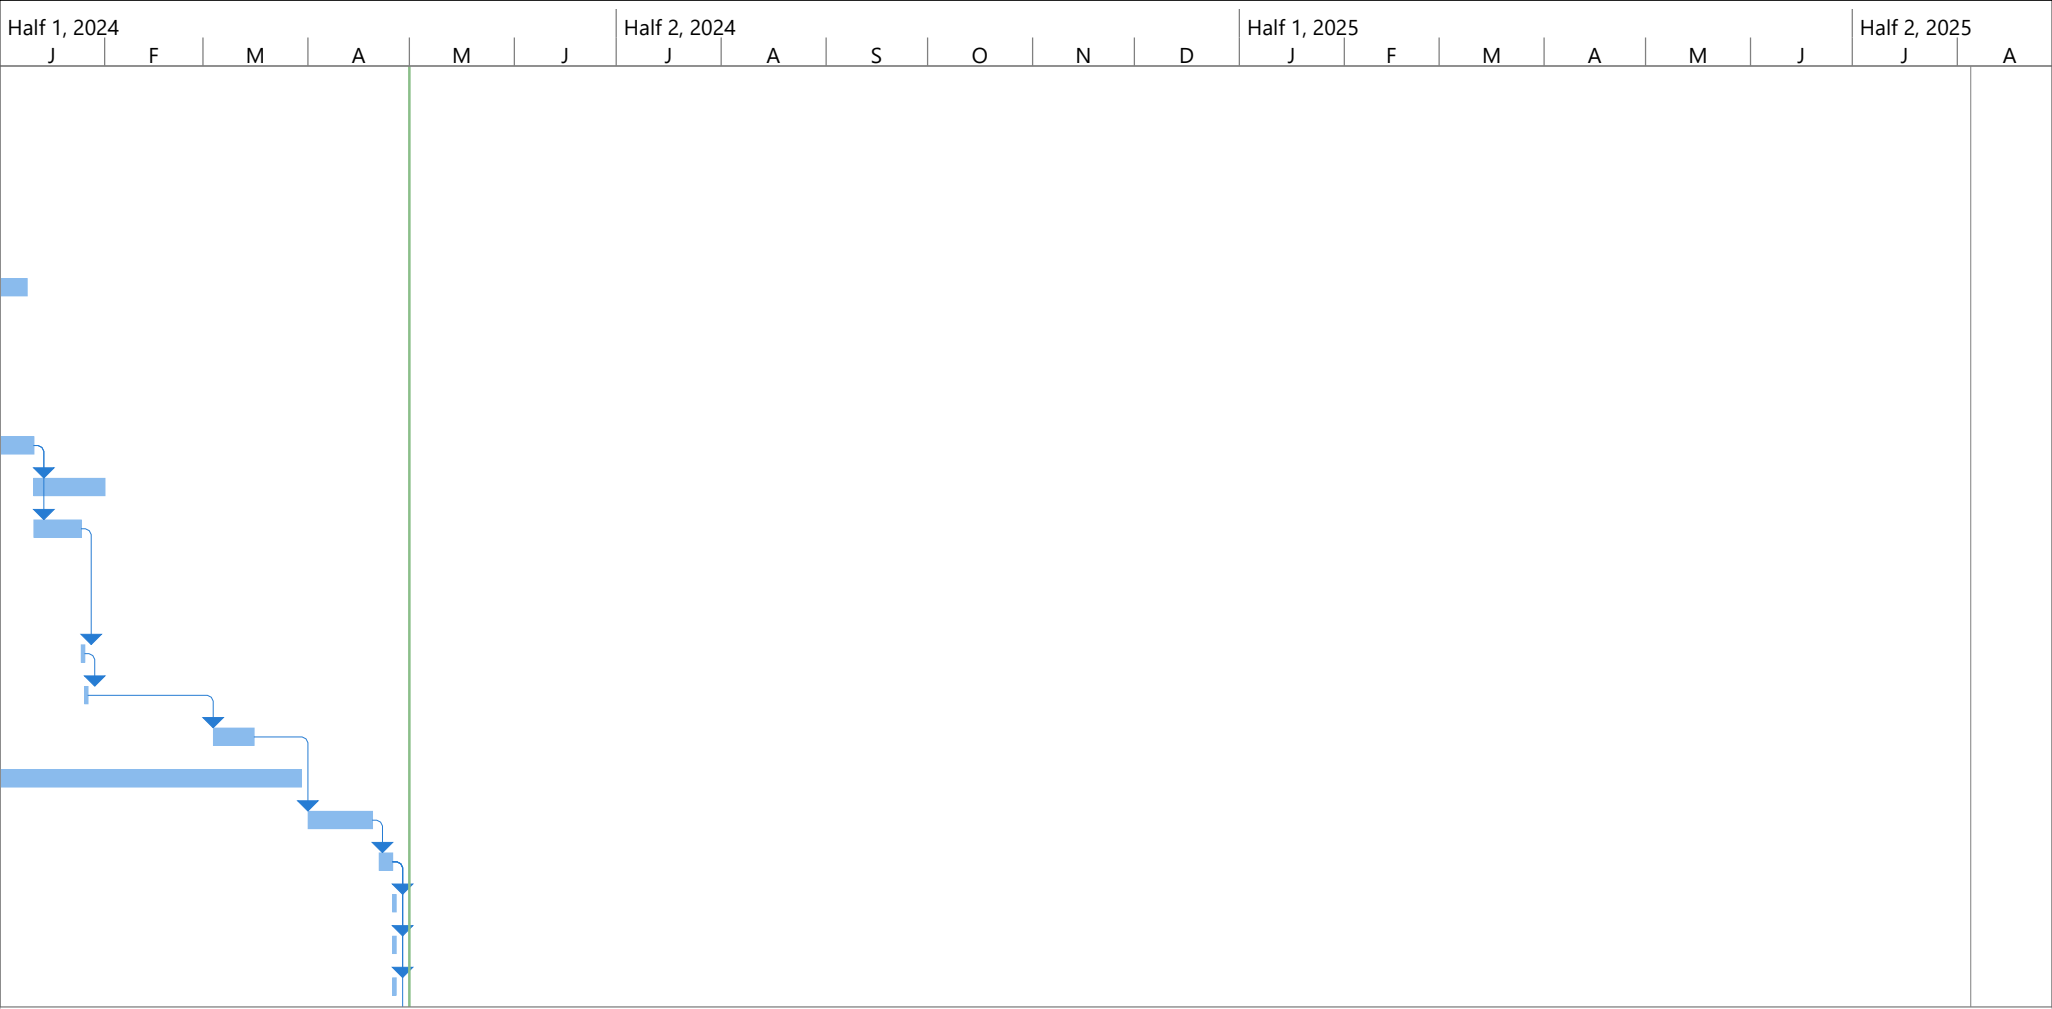



Project: intergrated programme Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

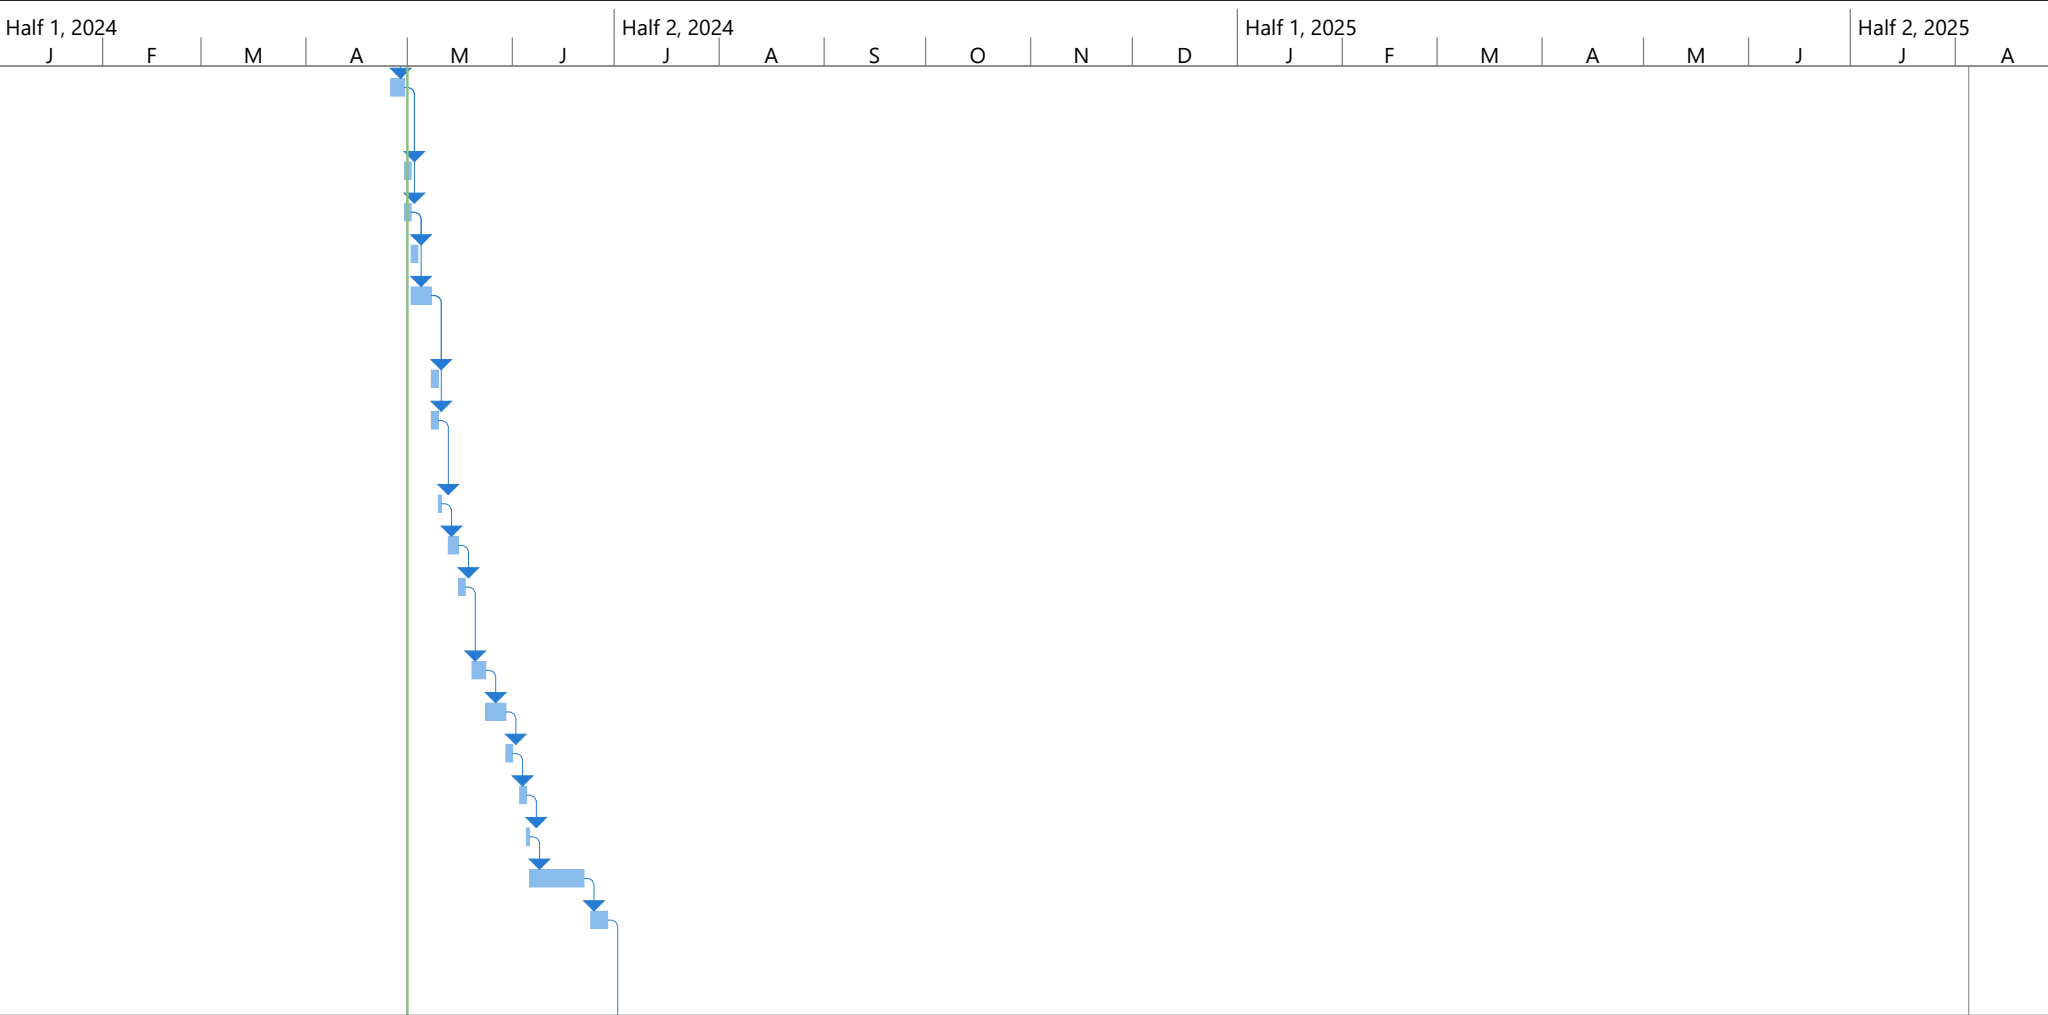

Project: intergrated programme Date: Wed 01/05/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

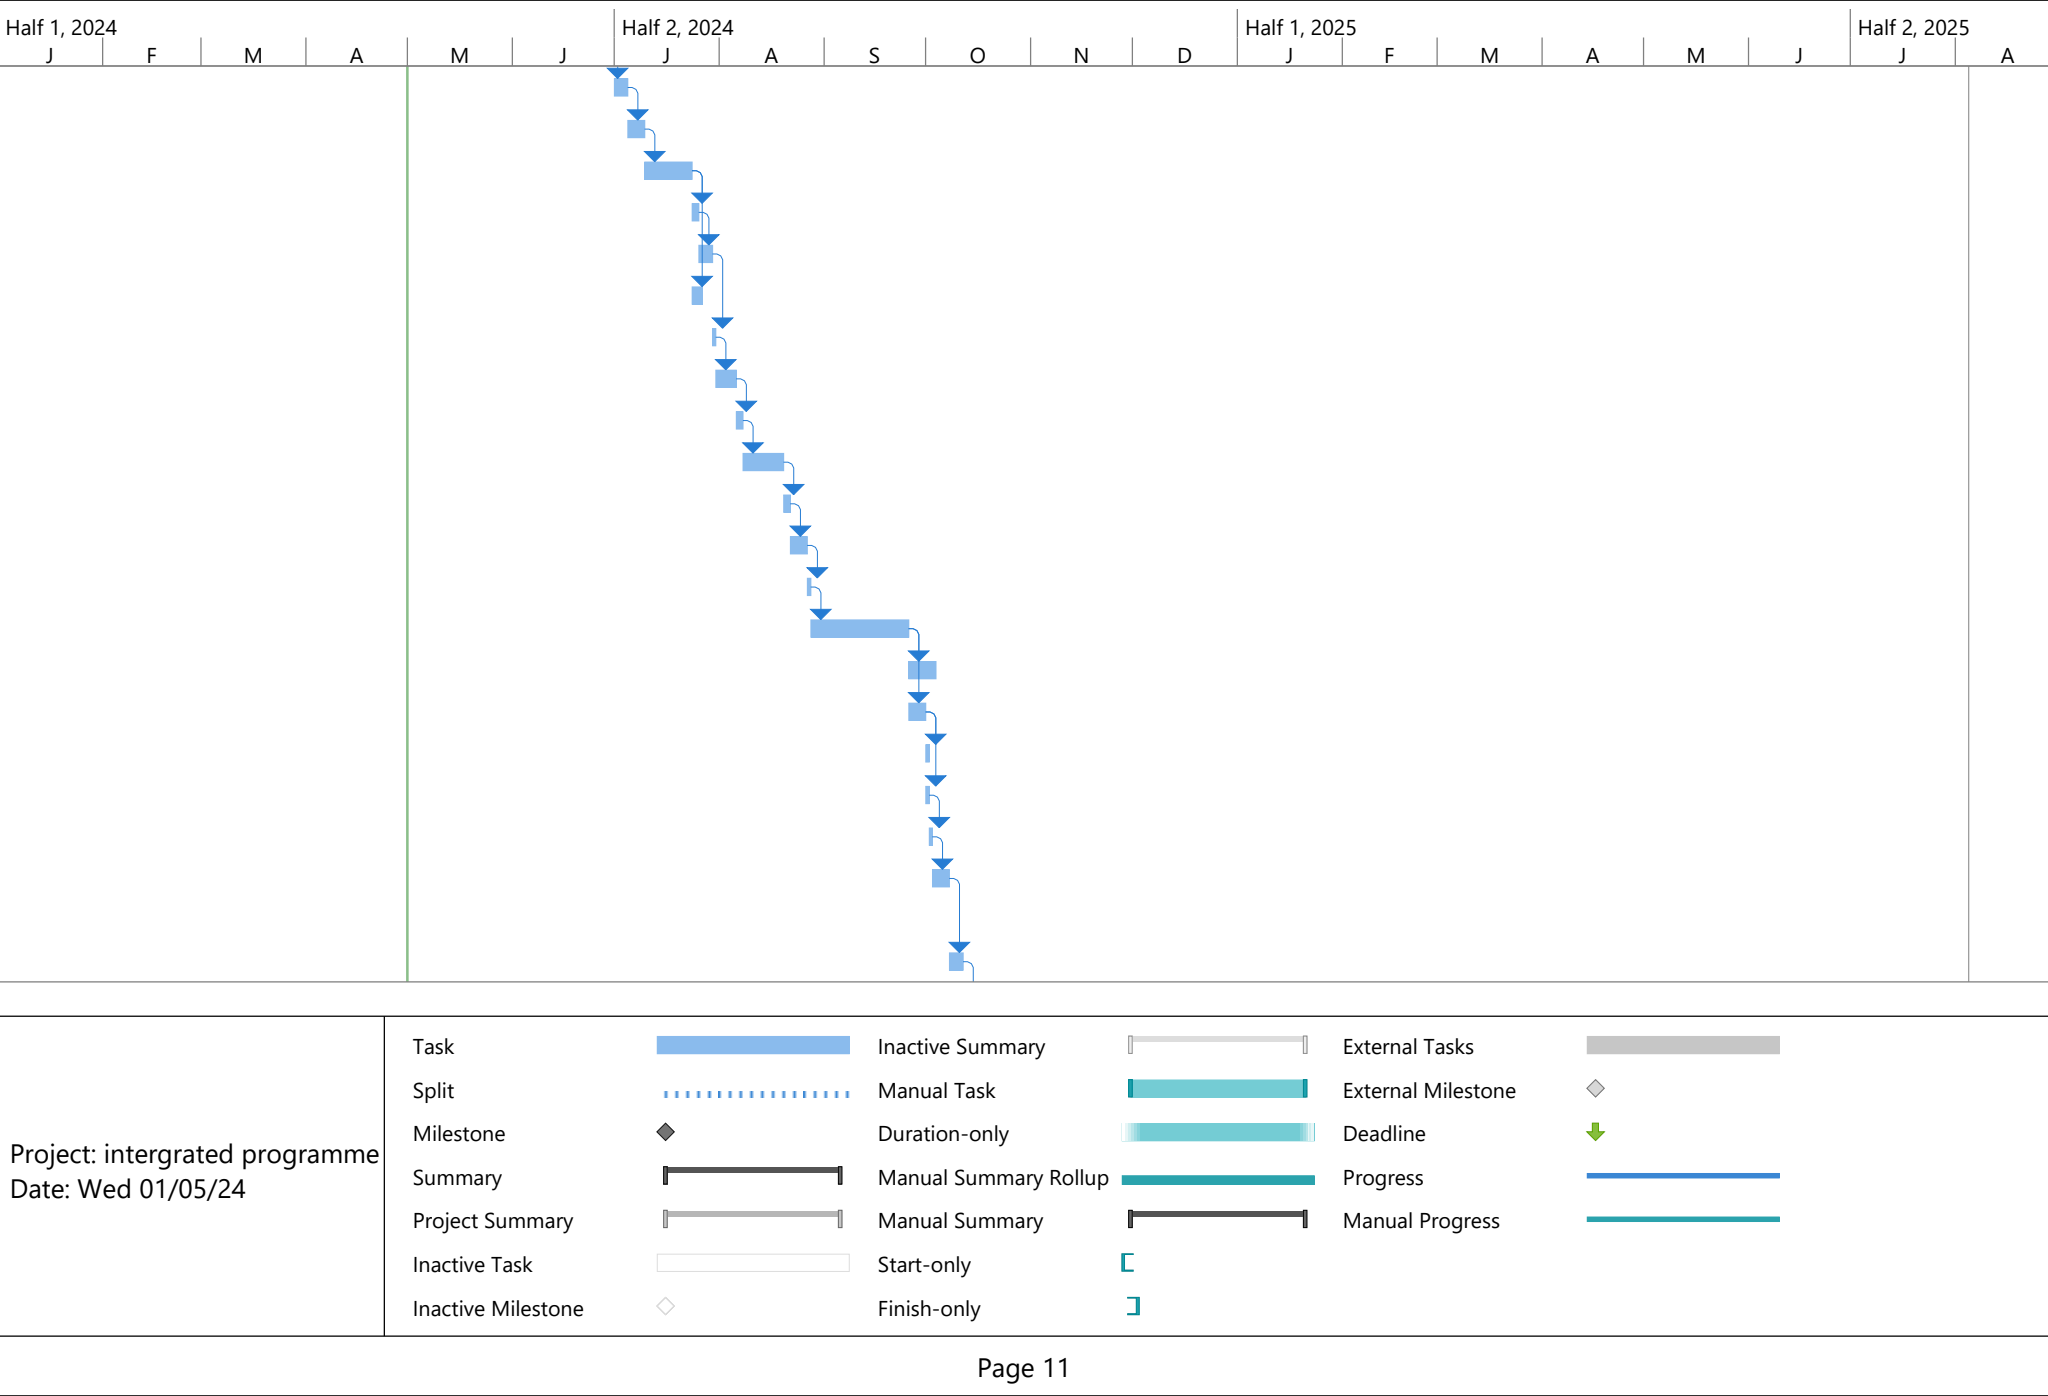

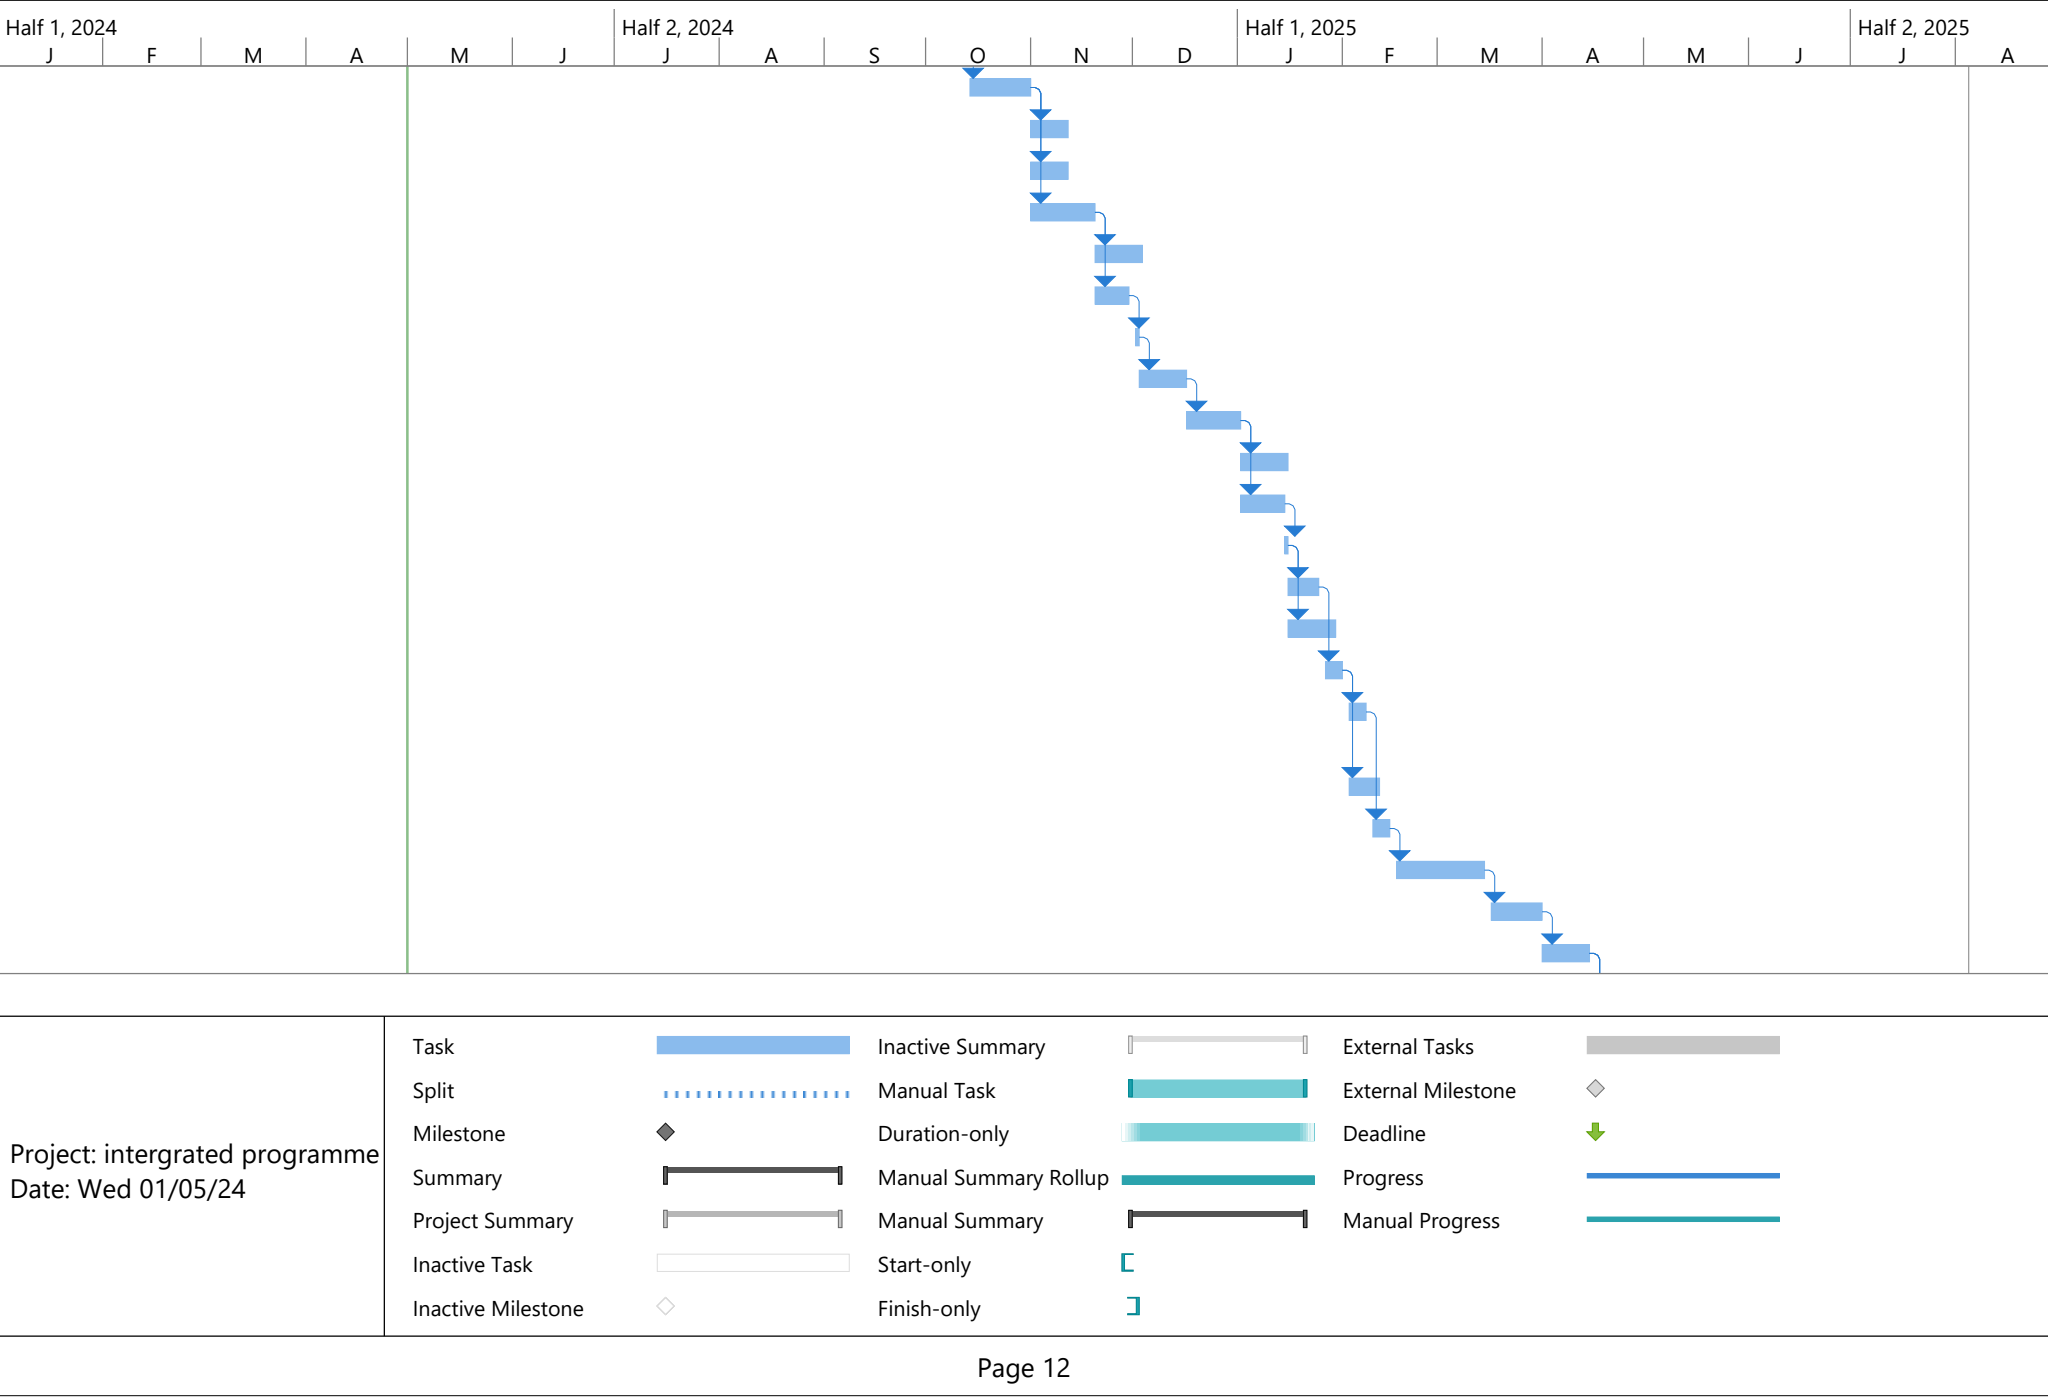

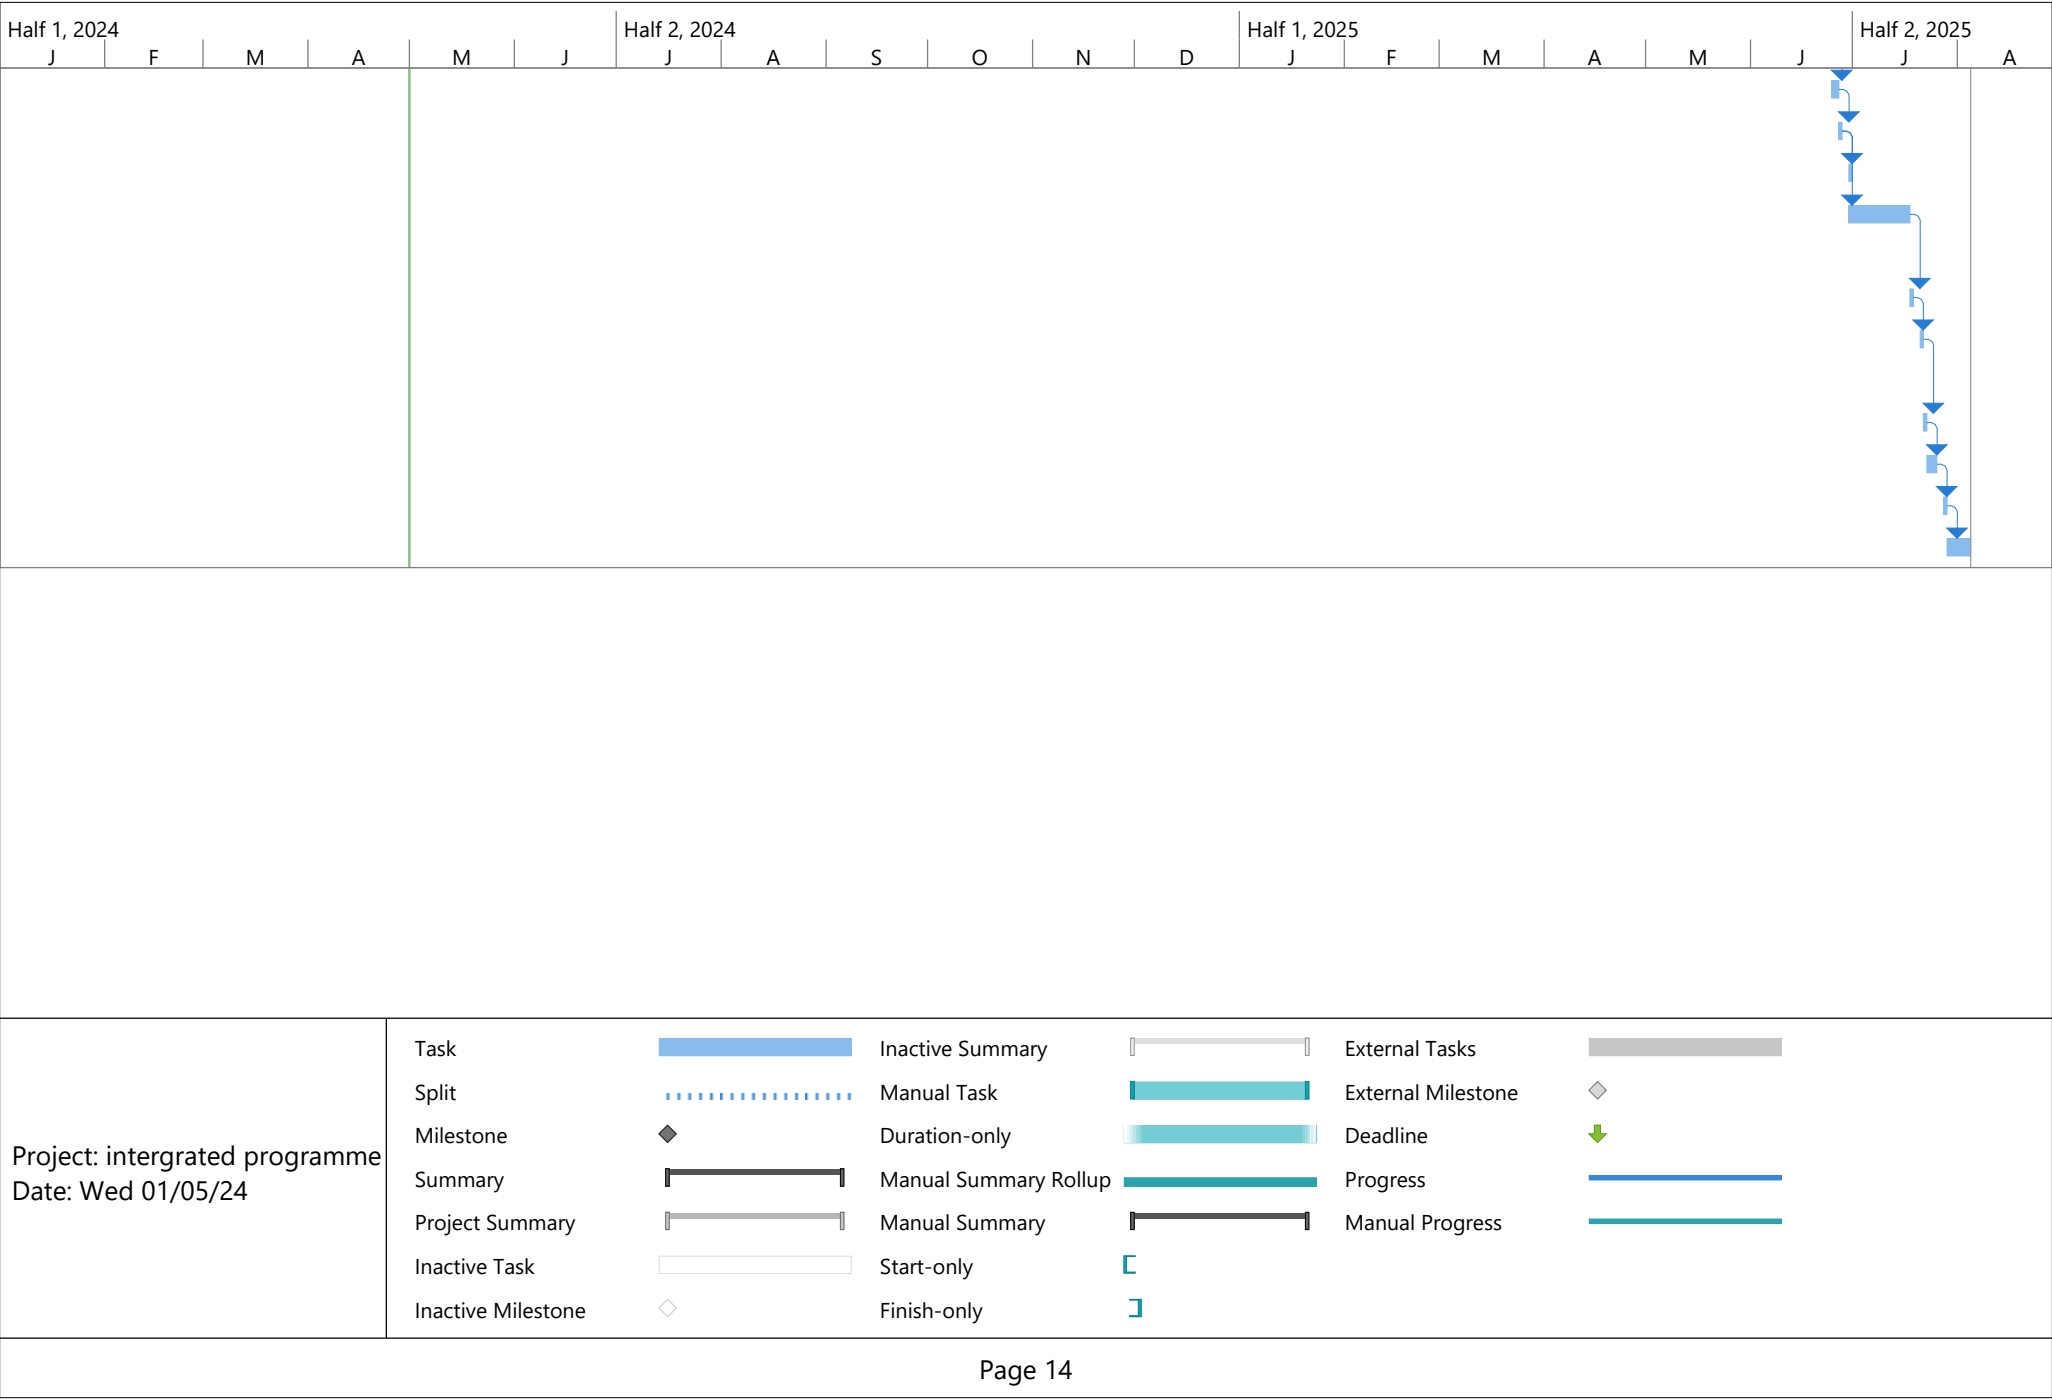

5

A

S

O

N

D

Half 1, 2026

J

F

M

A

M

J

Half 2, 2026

J

A

S

O

N

D

Half 1, 2027

J

F

M

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 15

5

A

S

O

N

D

Half 1, 2026

J

F

M

A

M

J

Half 2, 2026

J

A

S

O

N

D

Half 1, 2027

J

F

M

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 16

5

A

S

O

N

D

Half 1, 2026

J

F

M

A

M

J

Half 2, 2026

J

A

S

O

N

D

Half 1, 2027

J

F

M

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 17

5

A

S

O

N

D

Half 1, 2026

J

F

M

A

M

J

Half 2, 2026

J

A

S

O

N

D

Half 1, 2027

J

F

M

Project: intergrated programme
Date: Wed 01/05/24

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 18

