


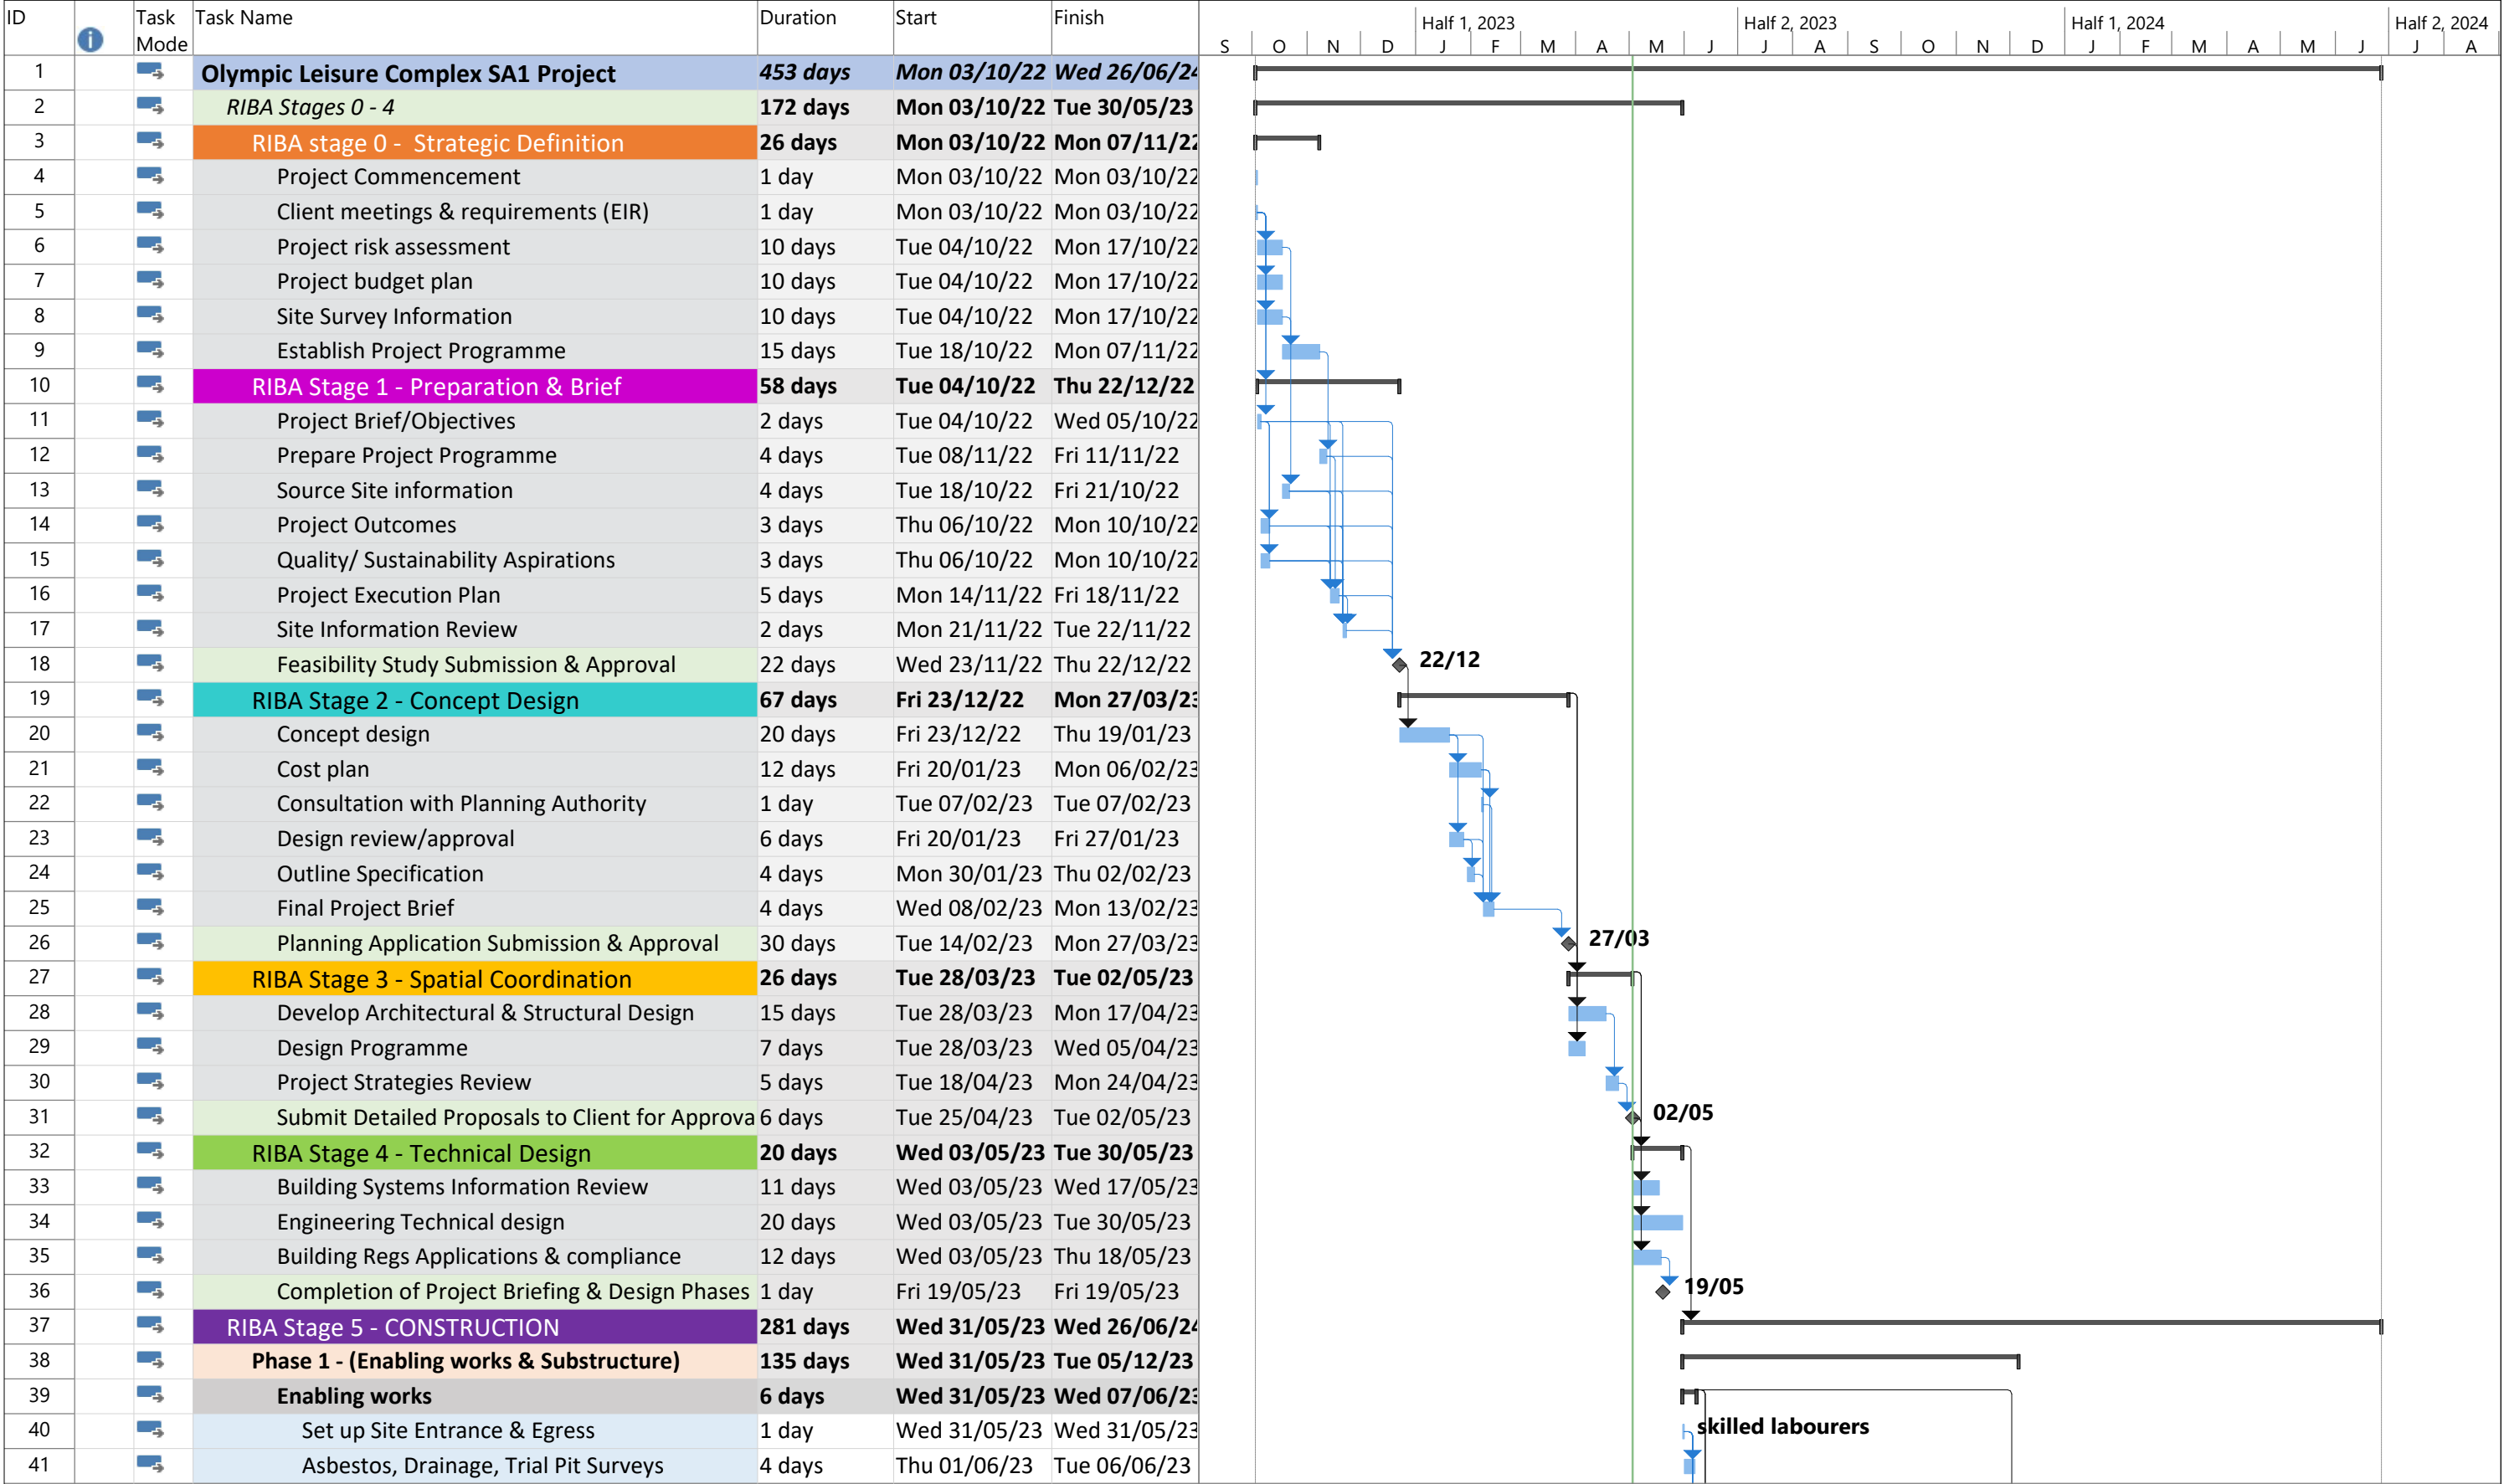

ID	Task Mode	Task Name	Duration	Start	Finish	Half 1, 2023														Half 2, 2023							Half 1, 2024							Half 2, 2024	
						S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A						
42			Form Compound (Office, Welfare, Materials)	2 days	Thu 01/06/23	Fri 02/06/23	</																												

Project: SA1 Olympic Leisure Co Date: Wed 03/05/23	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish															Half 1, 2023				Half 2, 2023				Half 1, 2024				Half 2, 2024			
						S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A						
117		Decorations (painting etc)	18 days	Wed 08/05/24	Fri 31/05/24																														
118		General Tiling	10 days	Wed 05/06/24	Tue 18/06/24																														
119		Welfare/Kitchen facilities Install	7 days	Wed 08/05/24	Thu 16/05/24																														
120		Internal Snagging & Cleaning	8 days	Fri 17/05/24	Tue 28/05/24																														
121		Flooring & Carpet finishing	15 days	Fri 17/05/24	Thu 06/06/24																														
122		Furnishing Delivery & Install	6 days	Fri 07/06/24	Fri 14/06/24																														
123		Air pressure Test	1 day	Mon 17/06/24	Mon 17/06/24																														
124		Acoustic tests	1 day	Mon 17/06/24	Mon 17/06/24																														
125		Final clean & Snag	1 day	Mon 17/06/24	Mon 17/06/24																														
126		Full Inspection , Test & Commission by Client & Contractor	1 day	Mon 24/06/24	Mon 24/06/24																														
127		Final BREAMM insepction	1 day	Tue 18/06/24	Tue 18/06/24																														
128		Internal works Completion	1 day	Tue 25/06/24	Tue 25/06/24																														
129		Construction Phase 2 Completion	1 day	Wed 26/06/24	Wed 26/06/24																														
130		Phase 3 - (Outdoor sports pitch, Tennis courts & Landscape)	24 days	Wed 08/05/24	Mon 10/06/24																														
131		General Landscaping	8 days	Wed 08/05/24	Fri 17/05/24																														
132		Football/Rugby sports Pitch Full Construction	8 days	Mon 20/05/24	Wed 29/05/24																														
133		Outdoor Tennis Court Construction	8 days	Mon 20/05/24	Wed 29/05/24																														
134		Fencing Perimeters (Tennis courts and Sports Pitch)	5 days	Thu 30/05/24	Wed 05/06/24																														
135		Fencing to Carpark Entrance	3 days	Mon 20/05/24	Wed 22/05/24																														
136		Road finishes	5 days	Thu 23/05/24	Wed 29/05/24																														
137		Paving and Slabbing	10 days	Mon 20/05/24	Fri 31/05/24																														
138		Landscape Snagging	4 days	Mon 03/06/24	Thu 06/06/24																														
139		Completion of Entire Construction Phases 1 - 3	2 days	Fri 07/06/24	Mon 10/06/24																														
140		RIBA Stage 6 - Handover	6 days	Tue 11/06/24	Tue 18/06/24																														
141		Practical Completion & Official Handover to Client	1 day	Tue 11/06/24	Tue 11/06/24																														
142		Plan For Use Strategy Documentation	4 days	Tue 11/06/24	Fri 14/06/24																														
143		BREAMM Final inspection & Assessment Certificate	1 day	Tue 11/06/24	Tue 11/06/24																														
144		Local Authority, Building control, & Client inspection of Complete Asset	1 day	Tue 11/06/24	Tue 11/06/24																														
145		Removal of Welfare facilities & Hoarding & Snagging	5 days	Tue 11/06/24	Mon 17/06/24																														
146		Complete Asset Handover	1 day	Tue 18/06/24	Tue 18/06/24																														
147		RIBA stage 7 - Use	1 day	Wed 19/06/24	Wed 19/06/24																														
148		Post occupancy evaluation	1 day	Wed 19/06/24	Wed 19/06/24																														
149		Aftercare Plan	1 day	Wed 19/06/24	Wed 19/06/24																														
150		Equipment commissioning	1 day	Wed 19/06/24	Wed 19/06/24																														
151		Sustainability Outcomes	1 day	Wed 19/06/24	Wed 19/06/24																														
152		Project Outcomes Report/Review	1 day	Wed 19/06/24	Wed 19/06/24																														

Project: SA1 Olympic Leisure Co
Date: Wed 03/05/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Progress

Manual Progress

Page 4
