

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**Project timeline**	**846 days**	**Tue 12/03/24**	**Tue 08/06/27**	
2		**RIBA Stages 0-4**	**846 days**	**Tue 12/03/24**	**Tue 08/06/27**	
3		**RIBA Stage 0 - Strategic Definition**	**32 days**	**Tue 12/03/24**	**Wed 24/04/24**	
4		Project Commencement	4 days	Tue 12/03/24	Fri 15/03/24	
5		Client Meetings	3 days	Mon 18/03/24	Wed 20/03/24	4
6		Internal Team Meetings	4 days	Thu 21/03/24	Tue 26/03/24	5
7		Project Risk Assessments	7 days	Wed 27/03/24	Thu 04/04/24	6
8		Project Budget Plans	7 days	Fri 05/04/24	Mon 15/04/24	7
9		Establish Project Programme	7 days	Tue 16/04/24	Wed 24/04/24	8
10		**RIBA Stage 1 - Preperation & Brief**	**50 days**	**Thu 25/04/24**	**Wed 03/07/24**	**3,9**
11		Project Objectives/Brief	3 days	Thu 25/04/24	Mon 29/04/24	9
12		Prepare Project Programme	3 days	Tue 30/04/24	Thu 02/05/24	11
13		Site Information	4 days	Fri 03/05/24	Wed 08/05/24	12
14		Project Deliverables & Outcomes	5 days	Thu 09/05/24	Wed 15/05/24	13
15		Quality Goals	5 days	Thu 16/05/24	Wed 22/05/24	14
16		Sustainibility Goals	4 days	Thu 23/05/24	Tue 28/05/24	15
17		Project Execution Plan	5 days	Wed 29/05/24	Tue 04/06/24	16
18		Site Investigation	4 days	Wed 05/06/24	Mon 10/06/24	17
19		Site Information Review	5 days	Tue 11/06/24	Mon 17/06/24	18
20		Feasibility Study Report	36 days	Thu 25/04/24	Thu 13/06/24	8
21		Feasibility Study Submission	1 day	Tue 18/06/24	Tue 18/06/24	19
22		Feasibility Study Client Approval	10 days	Wed 19/06/24	Tue 02/07/24	21

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
23		Feasibility Review	1 day	Wed 03/07/24	Wed 03/07/24	22
24		**RIBA Stage 2 - Concept Design**	**102 days**	**Thu 04/07/24**	**Fri 22/11/24**	**10,23**
25		Concept Design	15 days	Thu 04/07/24	Wed 24/07/24	23
26		Cost Plan	14 days	Thu 25/07/24	Tue 13/08/24	25
27		Consultation with Planning Authority (NPT)	1 day	Wed 14/08/24	Wed 14/08/24	26
28		Design Review/Approval	7 days	Thu 15/08/24	Fri 23/08/24	27
29		Outline Specification	3 days	Mon 26/08/24	Wed 28/08/24	28
30		Final Project Prief	2 days	Thu 29/08/24	Fri 30/08/24	29
31		Planning Application Submission & Approval	60 days	Mon 02/09/24	Fri 22/11/24	30
32		**RIBA Stage 3 - Spatial Coordination**	**29 days**	**Mon 02/09/24**	**Thu 10/10/24**	**30**
33		Architectural & Structural Design Drawings	14 days	Mon 02/09/24	Thu 19/09/24	30
34		Design Programme	7 days	Fri 20/09/24	Mon 30/09/24	33
35		Project Strategies Review	4 days	Tue 01/10/24	Fri 04/10/24	34
36		Submit Detailed Proposals to Client for Approval	3 days	Mon 07/10/24	Wed 09/10/24	35
37		Client Approval	1 day	Thu 10/10/24	Thu 10/10/24	36
38		**RIBA Stage 4 - Technical Design**	**53 days**	**Fri 11/10/24**	**Tue 24/12/24**	**37**
39		Building System Information Reviews	13 days	Fri 11/10/24	Tue 29/10/24	37
40		Engineering Technical Design	20 days	Wed 30/10/24	Tue 26/11/24	39
41		Building Regulations Application & Compliance	15 days	Wed 27/11/24	Tue 17/12/24	40
42		Completion of Project Briefing and Design Stages	5 days	Wed 18/12/24	Tue 24/12/24	41
43		**RIBA Stage 5 - Construction**	**271 days**	**Wed 25/12/24**	**Wed 07/01/26**	**42**
44		Phase 1 - Enabling Works	1 day	Wed 25/12/24	Wed 25/12/24	42

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
45		**Site Set Up**	**43 days**	**Wed 25/12/24**	**Fri 21/02/25**	**42**
46		Access to Site	1 day	Wed 25/12/24	Wed 25/12/24	42
47		Perimeter hoarding	3 days	Thu 26/12/24	Mon 30/12/24	46
48		Site Compound Setup	2 days	Tue 31/12/24	Wed 01/01/25	47
49		Welfare facilities Delivery	2 days	Thu 02/01/25	Fri 03/01/25	48
50		Electrical supply	2 days	Mon 06/01/25	Tue 07/01/25	49
51		Water supply	2 days	Wed 08/01/25	Thu 09/01/25	50
52		Portable site Office Delivery	1 day	Fri 10/01/25	Fri 10/01/25	51
53		Idetification of Services	1 day	Mon 13/01/25	Mon 13/01/25	52
54		Protection measures of services	1 day	Tue 14/01/25	Tue 14/01/25	53
55		Gridlines & Datums	1 day	Wed 15/01/25	Wed 15/01/25	54
56		Temporary access route	3 days	Thu 16/01/25	Mon 20/01/25	55
57		Install temporary signage	1 day	Tue 21/01/25	Tue 21/01/25	56
58		Setup Crane Location Ground Test (Stoning)	7 days	Wed 22/01/25	Thu 30/01/25	57
59		Delivery of Crane	2 days	Fri 31/01/25	Mon 03/02/25	58
60		Material Delivery	7 days	Tue 04/02/25	Wed 12/02/25	59
61		Plant Delivery	2 days	Thu 13/02/25	Fri 14/02/25	60
62		Site Investigation Surveys	5 days	Mon 17/02/25	Fri 21/02/25	61
63		**Execution of Building Site**	**34 days**	**Mon 24/02/25**	**Thu 10/04/25**	**45,62**
64		Site clearing and cleaning	3 days	Mon 24/02/25	Wed 26/02/25	62
65		Levelling of Site	21 days	Thu 27/02/25	Thu 27/03/25	64
66		Marking on site as per drawings (layout)	7 days	Fri 28/03/25	Mon 07/04/25	65

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
67		Establish access & Safety signage	3 days	Tue 08/04/25	Thu 10/04/25	66
68		**New Road Layout Construction**	**17 days**	**Wed 22/01/25**	**Thu 13/02/25**	**57**
69		TM Installation	1 day	Wed 22/01/25	Wed 22/01/25	57
70		Mobilise Plant	2 days	Thu 23/01/25	Fri 24/01/25	69
71		Plane off existing roundabout and road 100mm deep	2 days	Mon 27/01/25	Tue 28/01/25	70
72		Excavate surrounding ground for surfacing	3 days	Wed 29/01/25	Fri 31/01/25	71
73		Install Binder Course 60mm (Surfacing)	3 days	Mon 03/02/25	Wed 05/02/25	72
74		Bond Coat	1 day	Thu 06/02/25	Thu 06/02/25	73
75		Install Surface Course 40mm (Surfacing)	3 days	Thu 06/02/25	Mon 10/02/25	73
76		Lining	1 day	Tue 11/02/25	Tue 11/02/25	75
77		Demobilise Plant	2 days	Wed 12/02/25	Thu 13/02/25	76
78		Remove TM	1 day	Wed 12/02/25	Wed 12/02/25	76
79		Re-open new road layout	1 day	Thu 13/02/25	Thu 13/02/25	78
80		**Sub-Structure**	**91 days**	**Fri 11/04/25**	**Fri 15/08/25**	**63,67**
81		Excavate to locate services	1 day	Fri 11/04/25	Fri 11/04/25	67
82		Relocate Services	1 day	Mon 14/04/25	Mon 14/04/25	81
83		Cap-off dis-used service end points	1 day	Tue 15/04/25	Tue 15/04/25	82
84		Install new service ducts	1 day	Wed 16/04/25	Wed 16/04/25	83
85		Excavation for foundations	1 day	Thu 17/04/25	Thu 17/04/25	84
86		Level Site	1 day	Fri 18/04/25	Fri 18/04/25	85
87		**Phase 1 Piling East Side - Health Centre**	**55 days**	**Mon 21/04/25**	**Fri 04/07/25**	**86**
88		Construct Piling Mats	3 days	Mon 21/04/25	Wed 23/04/25	86

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
89		Mobilise Pile Rig	1 day	Thu 24/04/25	Thu 24/04/25	88
90		Driven Piles	14 days	Fri 25/04/25	Wed 14/05/25	89
91		Install Reinforcement for Piles	5 days	Thu 15/05/25	Wed 21/05/25	90
92		Concrete Pour on Piles	5 days	Thu 22/05/25	Wed 28/05/25	91
93		Concrete Curing	7 days	Thu 29/05/25	Fri 06/06/25	92
94		Crop (Cut) Piles to correct level	1 day	Mon 09/06/25	Mon 09/06/25	93
95		Steel Reinforcement on top of Piles	4 days	Tue 10/06/25	Fri 13/06/25	94
96		Shutter Piles for pile cap	4 days	Mon 16/06/25	Thu 19/06/25	95
97		Pour concrete to pile cap	5 days	Fri 20/06/25	Thu 26/06/25	96
98		Concrete Curing	5 days	Fri 27/06/25	Thu 03/07/25	97
99		Remove/Strike Shutters	1 day	Fri 04/07/25	Fri 04/07/25	98
100		**Phase 2 Piling West - Health Centre**	**67 days**	**Thu 24/04/25**	**Fri 25/07/25**	**88**
101		Construct Piling Mats	3 days	Thu 24/04/25	Mon 28/04/25	88
102		Mobilise Pile Rig	1 day	Thu 15/05/25	Thu 15/05/25	90
103		Driven Piles	14 days	Fri 16/05/25	Wed 04/06/25	102
104		Install Reinforcement for Piles	5 days	Thu 05/06/25	Wed 11/06/25	103
105		Concrete Pour on Piles	5 days	Thu 12/06/25	Wed 18/06/25	104
106		Concrete Curing	7 days	Thu 19/06/25	Fri 27/06/25	105
107		Crop (Cut) Piles to correct level	1 day	Mon 30/06/25	Mon 30/06/25	106
108		Steel Reinforcement on top of Piles	4 days	Tue 01/07/25	Fri 04/07/25	107
109		Shutter Piles for pile cap	4 days	Mon 07/07/25	Thu 10/07/25	108
110		Pour concrete to pile cap	5 days	Fri 11/07/25	Thu 17/07/25	109

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
111		Concrete Curing	5 days	Fri 18/07/25	Thu 24/07/25	110
112		Remove/Strike Shutters	1 day	Fri 25/07/25	Fri 25/07/25	111
113		**Phase 3 Piling Buildings behind Health Centre**	**79 days**	**Tue 29/04/25**	**Fri 15/08/25**	**101**
114		Construct Piling Mats	3 days	Tue 29/04/25	Thu 01/05/25	101
115		Mobilise Pile Rig	1 day	Thu 05/06/25	Thu 05/06/25	103
116		Driven Piles	14 days	Fri 06/06/25	Wed 25/06/25	115
117		Install Reinforcement for Piles	5 days	Thu 26/06/25	Wed 02/07/25	116
118		Concrete Pour on Piles	5 days	Thu 03/07/25	Wed 09/07/25	117
119		Concrete Curing	7 days	Thu 10/07/25	Fri 18/07/25	118
120		Crop (Cut) Piles to correct level	1 day	Mon 21/07/25	Mon 21/07/25	119
121		Steel Reinforcement on top of Piles	4 days	Tue 22/07/25	Fri 25/07/25	120
122		Shutter Piles for pile cap	4 days	Mon 28/07/25	Thu 31/07/25	121
123		Pour concrete to pile cap	5 days	Fri 01/08/25	Thu 07/08/25	122
124		Concrete Curing	5 days	Fri 08/08/25	Thu 14/08/25	123
125		Remove/Strike Shutters	1 day	Fri 15/08/25	Fri 15/08/25	124
126		**Foundation Works**	**14 days**	**Mon 28/07/25**	**Thu 14/08/25**	**112**
127		300mm Compacted Hardcore	4 days	Mon 28/07/25	Thu 31/07/25	112
128		100mm Compacted Hardcore	2 days	Fri 01/08/25	Mon 04/08/25	127
129		100mm sand lining	2 days	Tue 05/08/25	Wed 06/08/25	128
130		500mm concrete slab with reinforced 60mm rebar	4 days	Thu 07/08/25	Tue 12/08/25	129
131		215mm x 140mm concrete block	2 days	Wed 13/08/25	Thu 14/08/25	130
132		Foundation Inspection by Project Team	1 day	Fri 15/08/25	Fri 15/08/25	131

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
133		Final Prep Works ready for superstructure	1 day	Fri 15/08/25	Fri 15/08/25	131
134		**Phase 4 - Superstructure**	**88 days**	**Mon 18/08/25**	**Wed 17/12/25**	**133**
135		Mechanical Services First Fix (Piping)	2 days	Mon 18/08/25	Tue 19/08/25	133
136		Install DPM	2 days	Wed 20/08/25	Thu 21/08/25	135
137		Crane installed into position	1 day	Mon 18/08/25	Mon 18/08/25	133
138		215mm concrete blocks to DPC	3 days	Fri 22/08/25	Tue 26/08/25	136
139		240mm Steel Structural Columns to 1st Floor	7 days	Wed 27/08/25	Thu 04/09/25	138
140		460mm Structural beams to 2nd floor	7 days	Fri 05/09/25	Mon 15/09/25	139
141		Alutech Solutions ALT F50TT Boxing to 1st floor	3 days	Tue 16/09/25	Thu 18/09/25	140
142		Alutech Solutions F50 Curtain Wall Transom	3 days	Fri 19/09/25	Tue 23/09/25	141
143		Alutech Solutions F50 Curtain Wall Mullion	3 days	Wed 24/09/25	Fri 26/09/25	142
144		200mm concrete deck first floor	5 days	Fri 05/09/25	Thu 11/09/25	139
145		Alutech Solutions ALT F50TT Boxing to 2nd floor	2 days	Mon 29/09/25	Tue 30/09/25	143
146		200mm Tata Steel D46 Roof Deck	2 days	Wed 01/10/25	Thu 02/10/25	145
147		Vapour Control Layer	1 day	Fri 03/10/25	Fri 03/10/25	146
148		Rigid Taper Insulation	2 days	Mon 06/10/25	Tue 07/10/25	147
149		TATA Steel mild C channel	1 day	Wed 08/10/25	Wed 08/10/25	148
150		Rockwood Hardrock multifix tapered insulation 2nd floor	2 days	Thu 09/10/25	Fri 10/10/25	149
151		Rockwool wall insulation	2 days	Mon 13/10/25	Tue 14/10/25	150
152		20mm Plywood board	1 day	Wed 15/10/25	Wed 15/10/25	151
153		Alumasc Harer Large Sump Cast Iron Roof Outlet	1 day	Thu 16/10/25	Thu 16/10/25	152

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
154		EPDM Layer	1 day	Fri 17/10/25	Fri 17/10/25	153
155		Grey Stone External Tiling	3 days	Mon 20/10/25	Wed 22/10/25	154
156		Vadania Support Steel Triangle Support Brackets	1 day	Thu 23/10/25	Thu 23/10/25	155
157		Curtain Wall Double Glazing 1st & 2nd Floor	5 days	Fri 24/10/25	Thu 30/10/25	156
158		Tata Steel Colorcoat primsa steel frame	2 days	Fri 31/10/25	Mon 03/11/25	157
159		Tata Steel Ympress Steel Fins	2 days	Tue 04/11/25	Wed 05/11/25	158
160		12.5mm Knauf Aquapanel Exterior Cement Board	1 day	Thu 06/11/25	Thu 06/11/25	159
161		DuPont Tyvek UV Facade Protective Breathable Membrane	1 day	Fri 07/11/25	Fri 07/11/25	160
162		RHS Vertical Support to FINS	2 days	Mon 10/11/25	Tue 11/11/25	161
163		RHS Facade Frame	3 days	Wed 12/11/25	Fri 14/11/25	162
164		Argeton Terracotta Rainscreen Cladding System	3 days	Mon 17/11/25	Wed 19/11/25	163
165		Skyline Aluminium Coping	3 days	Thu 20/11/25	Mon 24/11/25	164
166		Geo Dark Grey 600 x 400 x 20mm Outdoor Stone Paving	3 days	Thu 23/10/25	Mon 27/10/25	155
167		Innowood Vertical Sol'art Operable Louvers	3 days	Tue 25/11/25	Thu 27/11/25	165
168		Steel Cladding Frame System	3 days	Fri 28/11/25	Tue 02/12/25	167
169		Perforated Galvanised Steel Cladding Panels	3 days	Wed 03/12/25	Fri 05/12/25	168
170		**Bridge Installation**	**7 days**	**Tue 16/09/25**	**Wed 24/09/25**	**140**
171		Install steel beams	3 days	Tue 16/09/25	Thu 18/09/25	140
172		Install Decking Panels	2 days	Fri 19/09/25	Mon 22/09/25	171

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
173		Install Handrails & Safety Features	2 days	Tue 23/09/25	Wed 24/09/25	172
174		Install Anti-Slip Coatings	1 day	Tue 23/09/25	Tue 23/09/25	172
175		**Finishings**	**1 day**	**Wed 24/09/25**	**Wed 24/09/25**	**174**
176		Install Flashing and cladding around joints	1 day	Wed 24/09/25	Wed 24/09/25	174
177		Paint Surfaces	1 day	Wed 24/09/25	Wed 24/09/25	174
178		**Rooftop Pool Installation**	**17 days**	**Tue 16/09/25**	**Wed 08/10/25**	**140**
179		Formwork & Reinforcement	3 days	Tue 16/09/25	Thu 18/09/25	140
180		**Plumping & Electrical Fix**	**2 days**	**Fri 19/09/25**	**Mon 22/09/25**	**179**
181		Filtration Systems	2 days	Fri 19/09/25	Mon 22/09/25	179
182		Pumps	2 days	Fri 19/09/25	Mon 22/09/25	179
183		Lighting	2 days	Fri 19/09/25	Mon 22/09/25	179
184		Heating Elements	2 days	Fri 19/09/25	Mon 22/09/25	179
185		Shell Construction of Pool	2 days	Tue 23/09/25	Wed 24/09/25	180
186		Pour Concrete	3 days	Thu 25/09/25	Mon 29/09/25	185
187		Tile Pool	4 days	Tue 30/09/25	Fri 03/10/25	186
188		Apply Waterproof Coatings	2 days	Mon 06/10/25	Tue 07/10/25	187
189		2nd Fix Plumbing & Electrical	1 day	Wed 08/10/25	Wed 08/10/25	188
190		**Roofing**	**8 days**	**Mon 08/12/25**	**Wed 17/12/25**	**169**
191		Erect Scaffolding	3 days	Mon 08/12/25	Wed 10/12/25	169
192		Insulation & Topsheet	5 days	Thu 11/12/25	Wed 17/12/25	191
193		Gutters	2 days	Thu 11/12/25	Fri 12/12/25	191
194		**Phase 5 - Internal Finishes**	**34 days**	**Fri 31/10/25**	**Wed 17/12/25**	**157**

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
195		**Ground floor**	**27 days**	**Fri 31/10/25**	**Mon 08/12/25**	**157**
196		150mm underfloor insulation	1 day	Fri 31/10/25	Fri 31/10/25	157
197		85mm screed with underfloor heating (Rayotech Webtech 150w/m2)	2 days	Mon 03/11/25	Tue 04/11/25	196
198		Polished screed Finish	1 day	Wed 05/11/25	Wed 05/11/25	197
199		Rockfon Eclipse Rectangle Kit (Ceiling Fixing)	1 day	Thu 06/11/25	Thu 06/11/25	198
200		Suspended Framing Ceiling	1 day	Fri 07/11/25	Fri 07/11/25	199
201		Suspended LED Lighting Fix	1 day	Mon 10/11/25	Mon 10/11/25	200
202		Handrail to stairs and walkways	2 days	Tue 11/11/25	Wed 12/11/25	201
203		Internal Walls	4 days	Thu 06/11/25	Tue 11/11/25	198
204		Knauf Fireproof tapered edge plasterboard	4 days	Wed 12/11/25	Mon 17/11/25	203
205		Dry Lining	2 days	Tue 18/11/25	Wed 19/11/25	204
206		Electrical 1st Fix	2 days	Tue 18/11/25	Wed 19/11/25	204
207		Mechanical 1st Fix	2 days	Tue 18/11/25	Wed 19/11/25	204
208		Door Installation & Stair to FF	2 days	Wed 12/11/25	Thu 13/11/25	203
209		Skirting Board Installation	1 day	Tue 18/11/25	Tue 18/11/25	204
210		Internal Window Installations	2 days	Wed 12/11/25	Thu 13/11/25	203
211		Electrical 2nd Fix	1 day	Thu 20/11/25	Thu 20/11/25	206
212		Mechanical 2nd Fix	1 day	Thu 20/11/25	Thu 20/11/25	207
213		Decoration	7 days	Wed 19/11/25	Thu 27/11/25	209
214		Flooring to toilets	1 day	Thu 06/11/25	Thu 06/11/25	198
215		Toilet cubicle installations	2 days	Fri 07/11/25	Mon 10/11/25	214
216		Flooring to coridors	2 days	Fri 28/11/25	Mon 01/12/25	213

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
217		Clean site	1 day	Tue 02/12/25	Tue 02/12/25	216
218		Mastic Works	1 day	Wed 03/12/25	Wed 03/12/25	217
219		Install Loose Furniture & Fittings	3 days	Thu 04/12/25	Mon 08/12/25	218
220		**1st Floor**	**25 days**	**Thu 06/11/25**	**Wed 10/12/25**	**198**
221		65mm Screed Flooring	1 day	Thu 06/11/25	Thu 06/11/25	198
222		Rockfon Eclipse Rectangle Kit (Ceiling Fixing)	1 day	Fri 07/11/25	Fri 07/11/25	199
223		Suspended Framing Ceiling	1 day	Mon 10/11/25	Mon 10/11/25	200
224		Suspended LED Lighting Fix	1 day	Tue 11/11/25	Tue 11/11/25	201
225		Suspended Ceiling	2 days	Tue 11/11/25	Wed 12/11/25	201
226		Handrail to stairs and walkways	4 days	Thu 13/11/25	Tue 18/11/25	202
227		Internal Walls	4 days	Wed 12/11/25	Mon 17/11/25	203
228		Knauf Fireproof tapered edge plasterboard	2 days	Tue 18/11/25	Wed 19/11/25	204
229		Dry Lining	2 days	Thu 20/11/25	Fri 21/11/25	205
230		Electrical 1st Fix	2 days	Thu 20/11/25	Fri 21/11/25	206
231		Mechanical 1st Fix	2 days	Thu 20/11/25	Fri 21/11/25	207
232		Door Installation & Stair to SF	1 day	Fri 14/11/25	Fri 14/11/25	208
233		Skirting Board Installation	2 days	Wed 19/11/25	Thu 20/11/25	209
234		Internal Window Installations	1 day	Fri 14/11/25	Fri 14/11/25	210
235		Electrical 2nd Fix	1 day	Fri 21/11/25	Fri 21/11/25	211
236		Mechanical 2nd Fix	7 days	Fri 21/11/25	Mon 01/12/25	212
237		Decoration	1 day	Fri 28/11/25	Fri 28/11/25	213
238		Flooring to toilets	2 days	Fri 07/11/25	Mon 10/11/25	214

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
239		Toilet cubicle installations	2 days	Tue 11/11/25	Wed 12/11/25	215
240		Flooring to coridors	1 day	Tue 02/12/25	Tue 02/12/25	216
241		Clean site	1 day	Wed 03/12/25	Wed 03/12/25	217
242		Mastic Works	3 days	Thu 04/12/25	Mon 08/12/25	218
243		Install Loose Furniture & Fittings	1 day	Tue 09/12/25	Tue 09/12/25	219
244		Install Gym equipment	1 day	Wed 10/12/25	Wed 10/12/25	243
245		**2nd Floor**	**25 days**	**Mon 10/11/25**	**Fri 12/12/25**	**222**
246		Rockfon Eclipse Rectangle Kit (Ceiling Fixing)	1 day	Mon 10/11/25	Mon 10/11/25	222
247		Suspended Framing Ceiling	1 day	Tue 11/11/25	Tue 11/11/25	223
248		Suspended LED Lighting Fix	1 day	Wed 12/11/25	Wed 12/11/25	224
249		Suspended Ceiling	2 days	Thu 13/11/25	Fri 14/11/25	225
250		Handrail to stairs and walkways	4 days	Wed 19/11/25	Mon 24/11/25	226
251		Internal Walls	4 days	Tue 18/11/25	Fri 21/11/25	227
252		Knauf Fireproof tapered edge plasterboard	2 days	Thu 20/11/25	Fri 21/11/25	228
253		Dry Lining	2 days	Mon 24/11/25	Tue 25/11/25	229
254		Electrical 1st Fix	2 days	Mon 24/11/25	Tue 25/11/25	230
255		Mechanical 1st Fix	2 days	Mon 24/11/25	Tue 25/11/25	231
256		Door Installation	1 day	Mon 17/11/25	Mon 17/11/25	232
257		Skirting Board Installation	2 days	Fri 21/11/25	Mon 24/11/25	233
258		Internal Window Installations	1 day	Mon 17/11/25	Mon 17/11/25	234
259		Electrical 2nd Fix	1 day	Mon 24/11/25	Mon 24/11/25	235
260		Mechanical 2nd Fix	7 days	Tue 02/12/25	Wed 10/12/25	236

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
261		Decoration	1 day	Mon 01/12/25	Mon 01/12/25	237
262		Flooring to toilets	2 days	Tue 11/11/25	Wed 12/11/25	238
263		Toilet cubicle installations	2 days	Thu 13/11/25	Fri 14/11/25	239
264		Flooring to coridors	1 day	Wed 03/12/25	Wed 03/12/25	240
265		Clean site	1 day	Thu 04/12/25	Thu 04/12/25	241
266		Mastic Works	3 days	Tue 09/12/25	Thu 11/12/25	242
267		Install Loose Furniture & Fittings	1 day	Wed 10/12/25	Wed 10/12/25	243
268		Install Cryo chamber	2 days	Thu 11/12/25	Fri 12/12/25	267
269		Final Clean & Snag	1 day	Mon 15/12/25	Mon 15/12/25	268
270		Full Inspection of Internal Finishing	1 day	Tue 16/12/25	Tue 16/12/25	269
271		Test & commission by Client	1 day	Wed 17/12/25	Wed 17/12/25	270
272		Full BREAMM Inspection	1 day	Tue 16/12/25	Tue 16/12/25	269
273		Internal Works Completion	1 day	Wed 17/12/25	Wed 17/12/25	272
274		Construction Phase Complete of Structure	1 day	Thu 18/12/25	Thu 18/12/25	44,80,134,194
275		**Phase 6 - External Works**	**22 days**	**Mon 08/12/25**	**Tue 06/01/26**	**169**
276		External Lighting Installation	2 days	Mon 08/12/25	Tue 09/12/25	169
277		Install Solar Shading	3 days	Mon 08/12/25	Wed 10/12/25	169
278		Level stoning works	5 days	Thu 11/12/25	Wed 17/12/25	277
279		Path Edgings	3 days	Thu 18/12/25	Mon 22/12/25	278
280		Tarmac to footpaths	2 days	Tue 23/12/25	Wed 24/12/25	279
281		Lay Block work outside building	7 days	Thu 25/12/25	Fri 02/01/26	280
282		Landscaping	5 days	Tue 23/12/25	Mon 29/12/25	279

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
283		Site Clearance	2 days	Mon 05/01/26	Tue 06/01/26	281
284		Completion of Entire Construction phase	1 day	Wed 07/01/26	Wed 07/01/26	44,45,63,68,80,87
285		**RIBA Stage 6 - Handover**	**4 days**	**Thu 08/01/26**	**Tue 13/01/26**	**284,43**
286		Official Handover to Client	1 day	Thu 08/01/26	Thu 08/01/26	284
287		Plan for use Strategy documentation	1 day	Fri 09/01/26	Fri 09/01/26	286
288		BREAMM Inspection & Certificate	2 days	Fri 09/01/26	Mon 12/01/26	286
289		Building control, local authority & Client inspections Complete	2 days	Fri 09/01/26	Mon 12/01/26	286
290		Inspection of Building and external works	2 days	Fri 09/01/26	Mon 12/01/26	286
291		Removal of Welfare Facilities	1 day	Fri 09/01/26	Fri 09/01/26	286
292		Remove Hoarding around Health and wellness centre	2 days	Fri 09/01/26	Mon 12/01/26	286
293		Leave Hoarding in situ around other building site	0 days	Mon 12/01/26	Mon 12/01/26	292
294		Complete Handover	1 day	Tue 13/01/26	Tue 13/01/26	292
295		**RIBA Stage 7 - Use**	**365 days**	**Wed 14/01/26**	**Tue 08/06/27**	**294**
296		Equipment commissioning	3 days	Wed 14/01/26	Fri 16/01/26	294
297		Sustainability Review	2 days	Mon 19/01/26	Tue 20/01/26	296
298		Post occupancy evaluations	3 days	Mon 19/01/26	Wed 21/01/26	296
299		**Aftercare Plan**	**365 days**	**Wed 14/01/26**	**Tue 08/06/27**	**294**
300		3 months defects meeting	90 days	Wed 14/01/26	Tue 19/05/26	294
301		3 month snagging	90 days	Wed 14/01/26	Tue 19/05/26	294
302		12 month review	365 days	Wed 14/01/26	Tue 08/06/27	294
303		12 month snagging	365 days	Wed 14/01/26	Tue 08/06/27	294

Project: Riverside Health Centre
Date: Tue 30/04/24




ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
304		Project Reviews	5 days	Wed 14/01/26	Tue 20/01/26	294
305		Project completion	5 days	Wed 14/01/26	Tue 20/01/26	294

Project: Riverside Health Centre
Date: Tue 30/04/24




Resource Names
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team,Engineer,Quantity Surveyor
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team

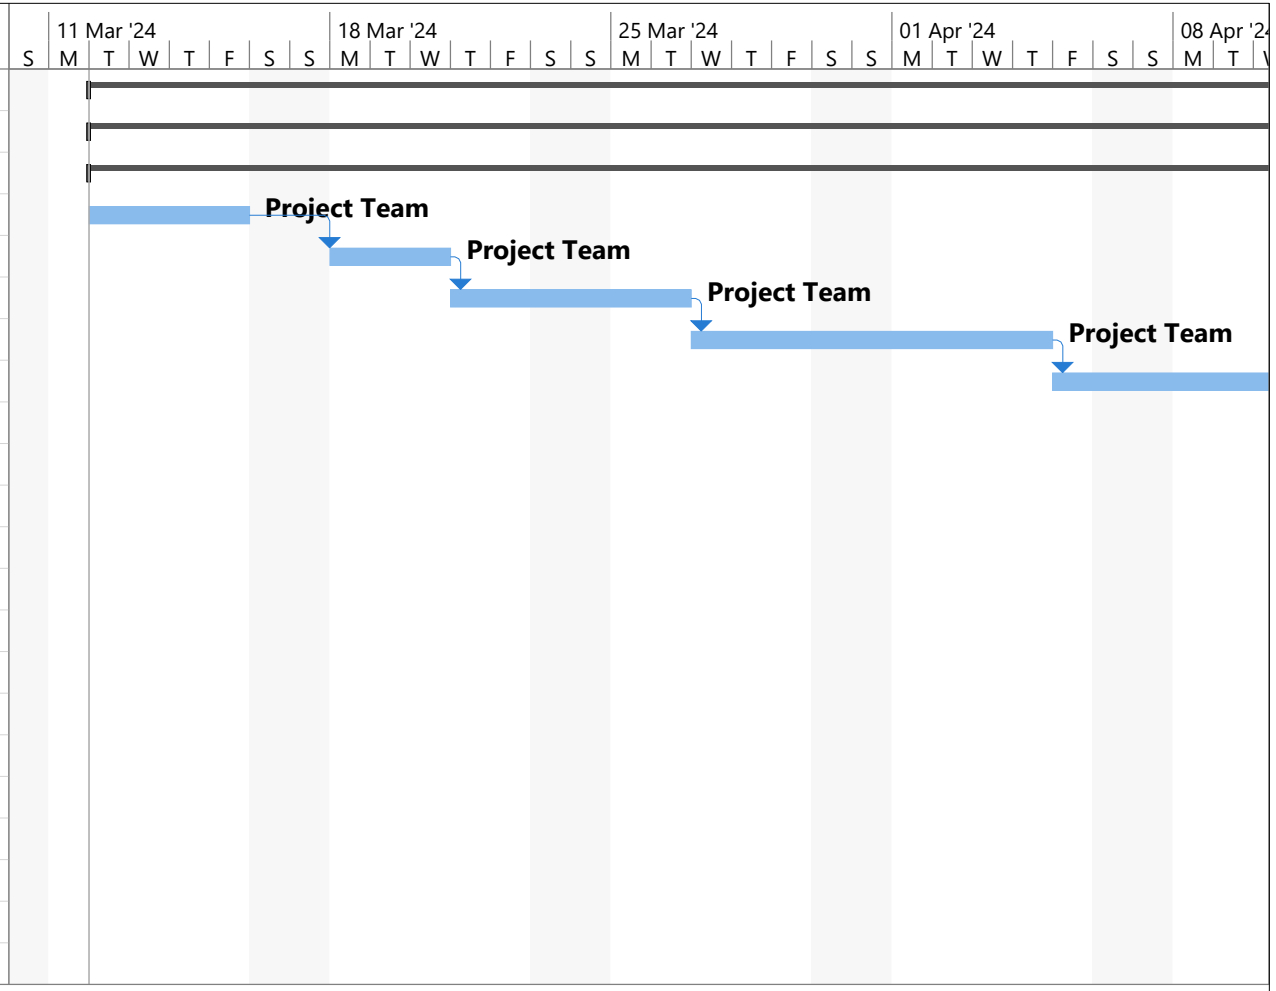

Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


Resource Names
Project Team
Project Team
Project Team,Quantity Surveyor
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team,Engineer
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team,Engineer
Project Team
Project Team

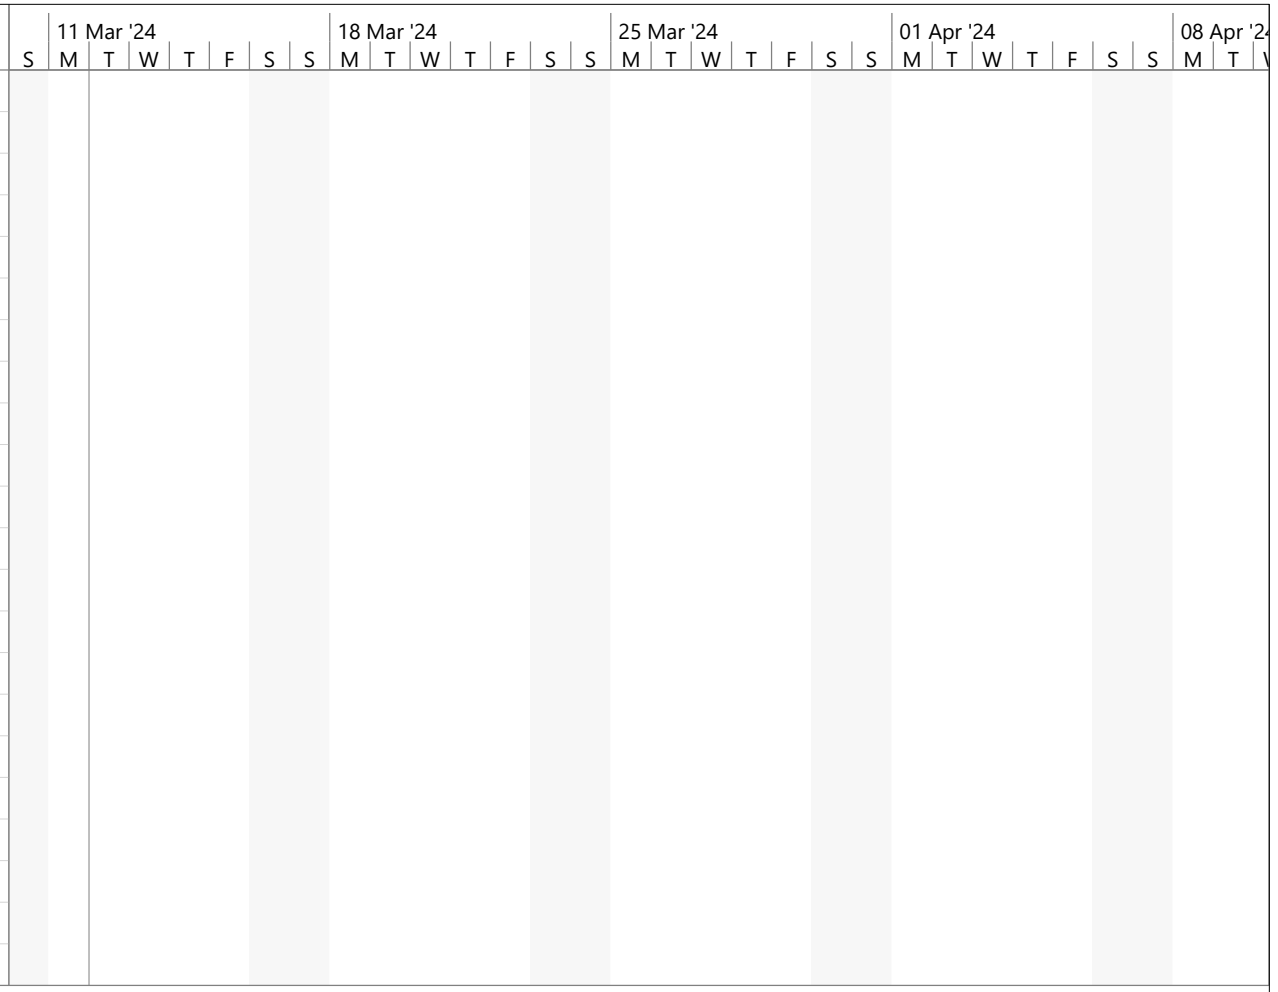

Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Resource Names
Labourer,Supervisor
Labourer,Supervisor,Perimeter Hoarding (Lm)[1]
Labourer,Supervisor,Site Manager
Labourer,Supervisor,Site Manager,Welfare Facilities
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Engineer,Labourer,Site Manager
Engineer,Labourer,Site Manager,Dumper & Driver
Engineer,Labourer,Site Manager

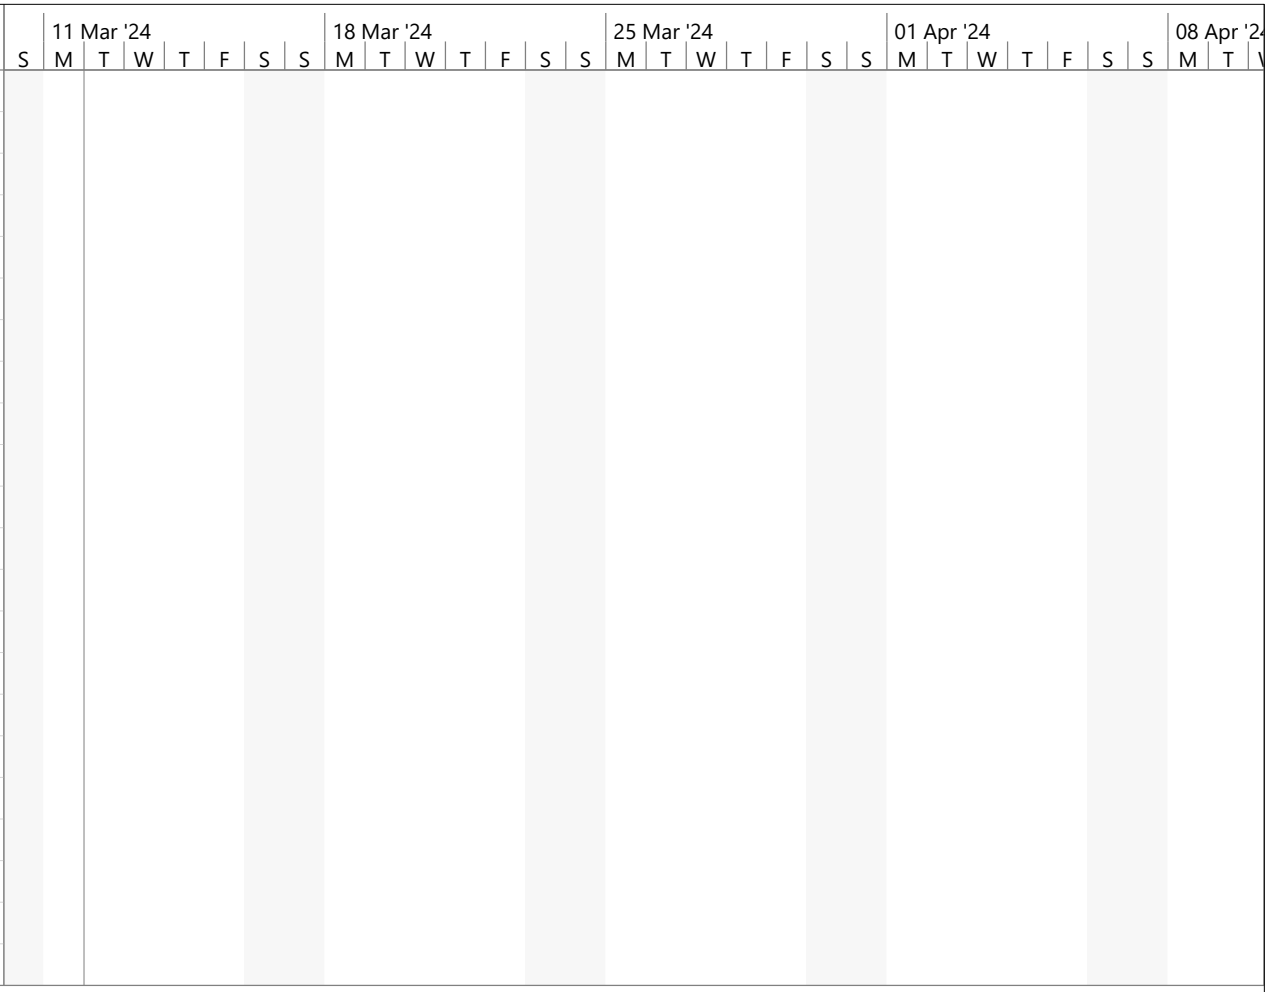

Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


Resource Names
Labourer,Site Manager
Traffic Management
Engineer,Labourer,Dumper & Driver
Engineer,Labourer,Perimeter Hoarding (Lm)[1],Planer (Surfacing)
Engineer,Labourer,Perimeter Hoarding (Lm)[1],Planer (Surfacing)
Engineer,Labourer,Perimeter Hoarding (Lm)[1],AC20 Dense Binde
Engineer,Labourer
AC 10 Surf 40/60[1]
Labourer
Labourer
Labourer
Assisstant Site Manager,Labourer
Dumper & Driver,Labourer,Supervisor
Dumper & Driver,Labourer,Supervisor
Labourer,Engineer
Labourer,Engineer
Dumper & Driver,Labourer,Supervisor
Dumper & Driver,Labourer,Supervisor
Engineer,Labourer



Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


Resource Names
Labourer,Pile rig
300mm Piles (9m Depth)[1],Engineer,Labourer,Supervisor
Engineer,Groundworker,Labourer,Pile Rebar[1],Piling Grout Mix[1
C20/20 Concrete (M3)[1],Engineer,Labourer,Supervisor
Labourer
Labourer,Supervisor
Labourer,Steel Reinforcement (M)[1],Supervisor
Labourer
C20/20 Concrete (M3)[1],Engineer,Labourer
Labourer
Engineer,Labourer
Engineer,Labourer
Labourer,Pile rig
300mm Piles (9m Depth)[1],Engineer,Labourer,Supervisor
Engineer,Groundworker,Labourer,Pile Rebar[1],Piling Grout Mix[1
C20/20 Concrete (M3)[1],Engineer,Labourer,Supervisor
Labourer
Labourer,Supervisor
Labourer,Steel Reinforcement (M)[1],Supervisor
Labourer
C20/20 Concrete (M3)[1],Engineer,Labourer

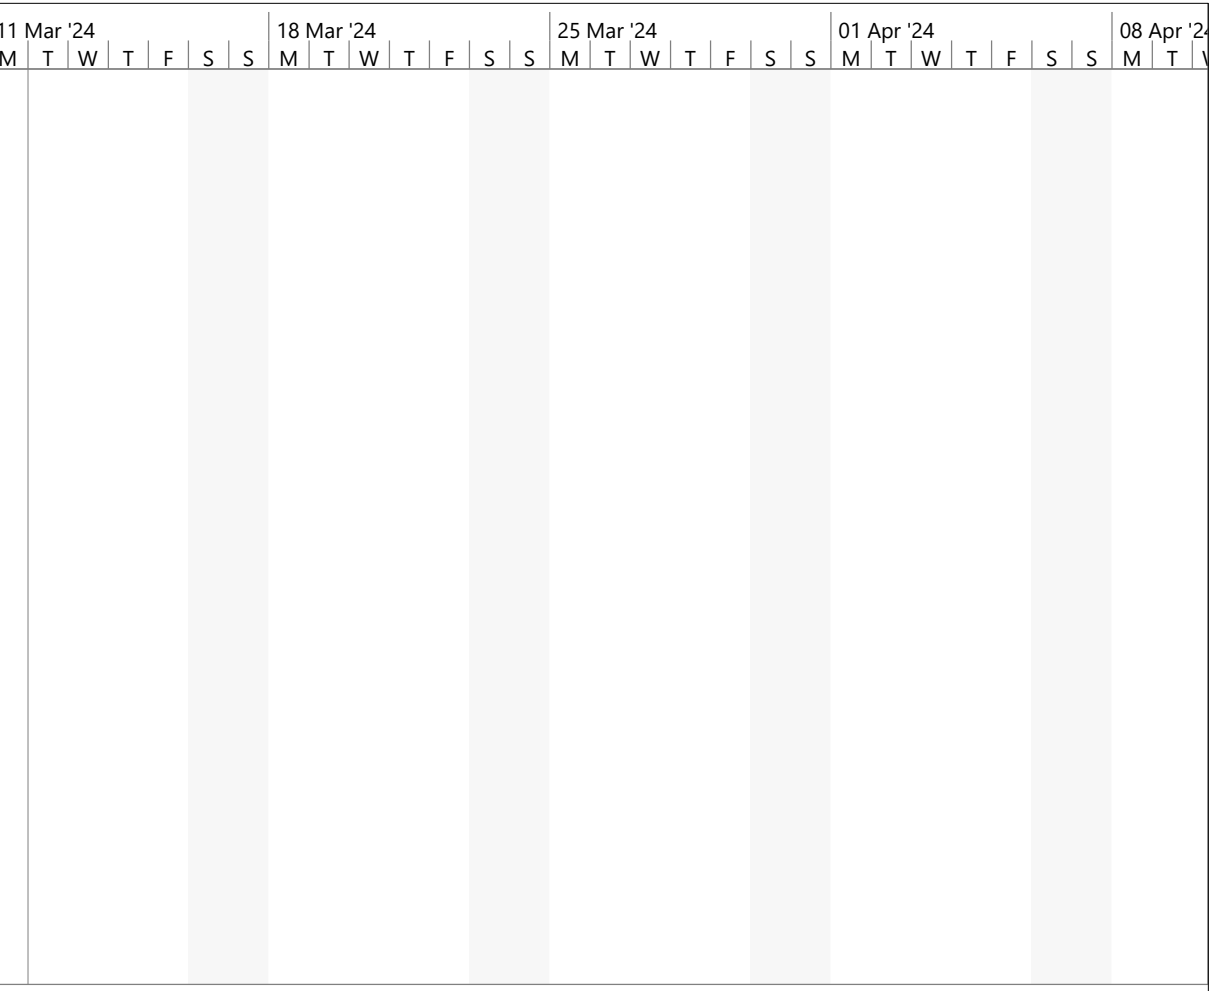

Project: Riverside Health Centre
Date: Tue 30/04/24


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Resource Names
Labourer
Engineer,Labourer
Engineer,Labourer
Labourer,Pile rig
300mm Piles (9m Depth)[1],Engineer,Labourer,Supervisor
Engineer,Groundworker,Labourer,Pile Rebar[1],Piling Grout Mix[1
C20/20 Concrete (M3)[1],Engineer,Labourer,Supervisor
Labourer
Labourer,Supervisor
Labourer,Steel Reinforcement (M)[1],Supervisor
Labourer
C20/20 Concrete (M3)[1],Engineer,Labourer
Labourer
Engineer,Labourer
Hardcore[1],Labourer,Supervisor,Engineer
Engineer,Hardcore[1],Labourer,Supervisor
Engineer,Labourer,Sand Lining[1]
C20/20 Concrete (M3)[1],Engineer,Labourer,Steel Reinforcement (M)[1]
215mm x 140mm Concrete Block[1],Labourer,Supervisor
Engineer,Project Team,Site Manager,Supervisor



Project: Riverside Health Centre
Date: Tue 30/04/24

Resource Names
Engineer,Project Team,Site Manager,Supervisor
Electrician,Engineer,Labourer
DPM (m2)[1],Labourer,Supervisor
Engineer,Labourer,Site Manager,Supervisor
215mm x 140mm Concrete Block[1],Labourer,Supervisor
240mm Steel Structural Column[1],Engineer,Labourer,Supervisor
460mm Structural Beams[1],Engineer,Labourer,Supervisor
ALT F50TT Boxing[1],Labourer,Supervisor
Engineer,Labourer,Tramsom[1],Supervisor
Supervisor,Engineer,Mullion[1],Labourer
Engineer,Labourer,Supervisor
ALT F50TT Boxing[1],Labourer,Supervisor
200mm TataSteel D46 Roof Deck[1],Engineer,Labourer,Supervisor
Labourer,Supervisor,Vapour Control Layer (m2)[1]
Labourer,Rigid Taper Insulation[1],Supervisor
Labourer,Supervisor,Tata Steel Mild C-channel[1]
Labourer,Rockwood Insulation[1],Supervisor
Labourer,Rockwood Insulation[1],Supervisor
20mm Plywood Board[1],Labourer,Supervisor
Alumasc Harer Large Sump Cast Iron Roof Outlet[1],Engineer,Labourer,Supervisor



Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Resource Names
EPDM Layer[1],Labourer,Supervisor
Grey Stone External Tiling[1],Labourer,Supervisor
Labourer,Supervisor,Vadania Triangle Support Brackets[1]
Curtain Walling[1],Engineer,Labourer,Supervisor
Labourer,Supervisor,Tata Steel Colorcoat Primsa Steel Frame[1]
Labourer,Engineer,Tata Steel Ympress Steel Fins[1]
12.5mm Knauf Aquapanel Cement Board[1],Labourer,Supervisor
Dupont Tyvek UV Faceade Protective breathable membrane[1],Labourer,Supervisor
Engineer,Labourer,RHS Vertical Supports[1],Supervisor
Engineer,Labourer,RHS Façade Frame[1],Supervisor
Argeton Terracotta Rainscreen Cladding system[1],Labourer,Super
Labourer,Skyline Aluminium Coping[1],Supervisor
600x 400 x 200mm outdoor stone paving[1],Labourer,Supervisor
Innowood Vertical Sol'art Operable Louvers[1],Labourer,Supervisc
Engineer,Labourer,Steel Cladding Frame System[1]
Labourer,Perforated Galvanised Steel Cladding Panels[1],Supervisc
Engineer,Labourer,Steel Beams[1],Supervisor
Decking Panels[1],Labourer,Supervisor,Engineer




Project: Riverside Health Centre
Date: Tue 30/04/24


Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

Resource Names	11 Mar '24							18 Mar '24							25 Mar '24							01 Apr '24							08 Apr '24
	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M
Handrail [1],Labourer,Supervisor,Engineer																													
Labourer,Supervisor,Pmb Waterproof Bridge Deck (m2)[1]																													
Engineer,Labourer,Supervisor																													
Painter																													
Engineer,Labourer,Steel Reinforcement (M)[1]																													
Electrician,Engineer,Labourer																													
Electrician,Engineer,Labourer																													
Electrician,Engineer,Labourer																													
Electrician,Engineer,Labourer																													
Engineer,Labourer,Site Manager,Supervisor																													
Engineer,Labourer,C20/20 Concrete (M3)[1],Supervisor																													
Labourer																													
Painter																													
Electrician,Engineer,Supervisor																													
Engineer,Labourer,Scaffolding,Supervisor																													
Labourer,Supervisor																													
Gutters (Lm)[1],Labourer,Supervisor																													

Project: Riverside Health Centre
Date: Tue 30/04/24




Resource Names
Labourer,Supervisor,150mm Underfloor Insulation[1]
Labourer,Supervisor,85mm Screed [1],Rayotech Webtech 150w/m2 Underfloor heating[1]
Labourer,Supervisor,Polished Screed[1]
Labourer,Supervisor,Rockfon Eclipse Rectangle Kit (Ceiling fixing)[1
Labourer,Supervisor
Labourer,Supervisor,Electrician,Light Fitting[1]
Labourer,Supervisor,Handrail [1]
Labourer,Supervisor,Internal Walls [1]
Labourer,Supervisor,Knauf Fireproof Tapered edge plasterboard[1
Labourer,Supervisor,Dry Liner
Supervisor,Electrician,Engineer,Sockets [1],Switches [1]
Supervisor,Electrician,Engineer
Labourer,Supervisor,Doors [1],Stairs (m2)[1]
Labourer,Supervisor,Skirting [1]
Labourer,Supervisor,Window Fitter
Supervisor,Electrician,Engineer
Supervisor,Electrician,Engineer
Labourer,Painter,Supervisor
Labourer,Supervisor
Labourer,Supervisor,Toilet[1],Toilet Cubicles [1],WH Basin [1]
Labourer,Supervisor

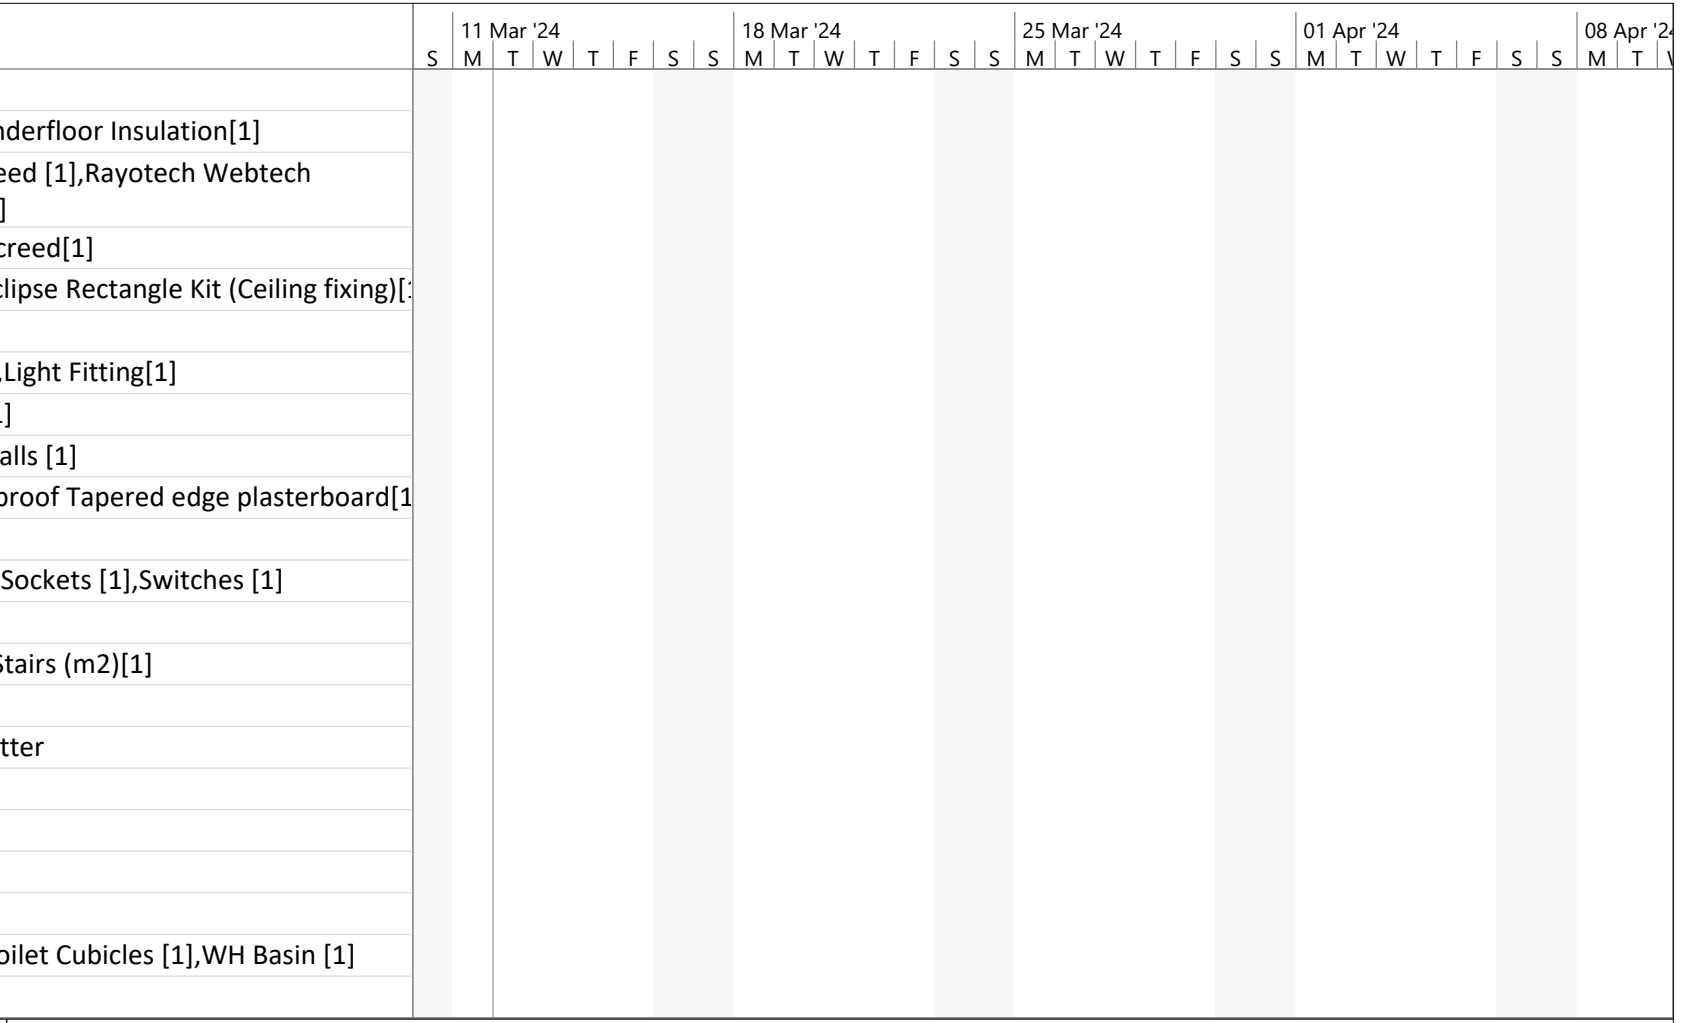

Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	


Resource Names
Labourer,Supervisor,Cleaner
Labourer,Supervisor
Labourer,Supervisor
65mm screed flooring[1],Labourer,Supervisor
Labourer,Supervisor,Polished Screed[1]
Labourer,Supervisor,Rockfon Eclipse Rectangle Kit (Ceiling fixing)[1
Labourer,Supervisor
Labourer,Supervisor,Electrician,Light Fitting[1]
Labourer,Supervisor,Handrail [1]
Labourer,Supervisor,Internal Walls [1]
Labourer,Supervisor,Knauf Fireproof Tapered edge plasterboard[1
Labourer,Supervisor,Dry Liner
Supervisor,Electrician,Engineer,Sockets [1],Switches [1]
Supervisor,Electrician,Engineer
Labourer,Supervisor,Doors [1],Stairs (m2)[1]
Labourer,Supervisor,Skirting [1]
Labourer,Supervisor,Window Fitter
Supervisor,Electrician,Engineer
Supervisor,Electrician,Engineer
Labourer,Painter,Supervisor
Labourer,Supervisor



Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Resource Names
Labourer,Supervisor,Toilet[1],Toilet Cubicles [1],WH Basin [1]
Labourer,Supervisor
Labourer,Supervisor,Cleaner
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor,Polished Screed[1]
Labourer,Supervisor,Rockfon Eclipse Rectangle Kit (Ceiling fixing)[1
Labourer,Supervisor
Labourer,Supervisor,Electrician,Light Fitting[1]
Labourer,Supervisor,Handrail [1]
Labourer,Supervisor,Internal Walls [1]
Labourer,Supervisor,Knauf Fireproof Tapered edge plasterboard[1
Labourer,Supervisor,Dry Liner
Supervisor,Electrician,Engineer,Sockets [1],Switches [1]
Supervisor,Electrician,Engineer
Labourer,Supervisor,Doors [1],Stairs (m2)[1]
Labourer,Supervisor,Skirting [1]
Labourer,Supervisor,Window Fitter
Supervisor,Electrician,Engineer
Supervisor,Electrician,Engineer



Project: Riverside Health Centre
Date: Tue 30/04/24


Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

Resource Names	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T
		11 Mar '24							18 Mar '24							25 Mar '24							01 Apr '24							08 Apr '24	
Labourer,Painter,Supervisor																															
Labourer,Supervisor																															
Labourer,Supervisor,Toilet[1],Toilet Cubicles [1],WH Basin [1]																															
Labourer,Supervisor																															
Labourer,Supervisor,Cleaner																															
Labourer,Supervisor																															
Labourer,Supervisor																															
Labourer,Supervisor																															
Cleaner,Labourer,Project Team,Site Manager,Supervisor																															
Cleaner,Labourer,Project Team,Site Manager,Supervisor																															
Project Team,Site Manager,Supervisor																															
Project Team,Site Manager,Supervisor																															
Project Team,Site Manager,Supervisor																															
Project Team,Site Manager,Supervisor																															
Electrician,Engineer,Labourer,Light Fitting[1],Supervisor																															
Engineer,Labourer,Solar shading[1],Supervisor																															
Dumper & Driver,Engineer,Labourer,Supervisor																															
Labourer,Supervisor																															
AC 10 Surf 40/60[1],Engineer,Labourer																															
Labourer,Supervisor																															
Labourer,Supervisor																															

Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

Resource Names
Labourer,Supervisor,Cleaner
Project Team,Site Manager,Supervisor
Project Team,Site Manager
Project Team,Site Manager
Project Team,Site Manager
Project Team,Site Manager
Project Team,Site Manager
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor
Labourer,Supervisor,Project Team,Quantity Surveyor,Site Manage
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team
Project Team




Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

Resource Names	S	11 Mar '24 M	T	W	T	F	S	S	18 Mar '24 M	T	W	T	F	S	S	25 Mar '24 M	T	W	T	F	S	S	01 Apr '24 M	T	W	T	F	S	S	08 Apr '24 M	T
Project Team																													
Project Team																													


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

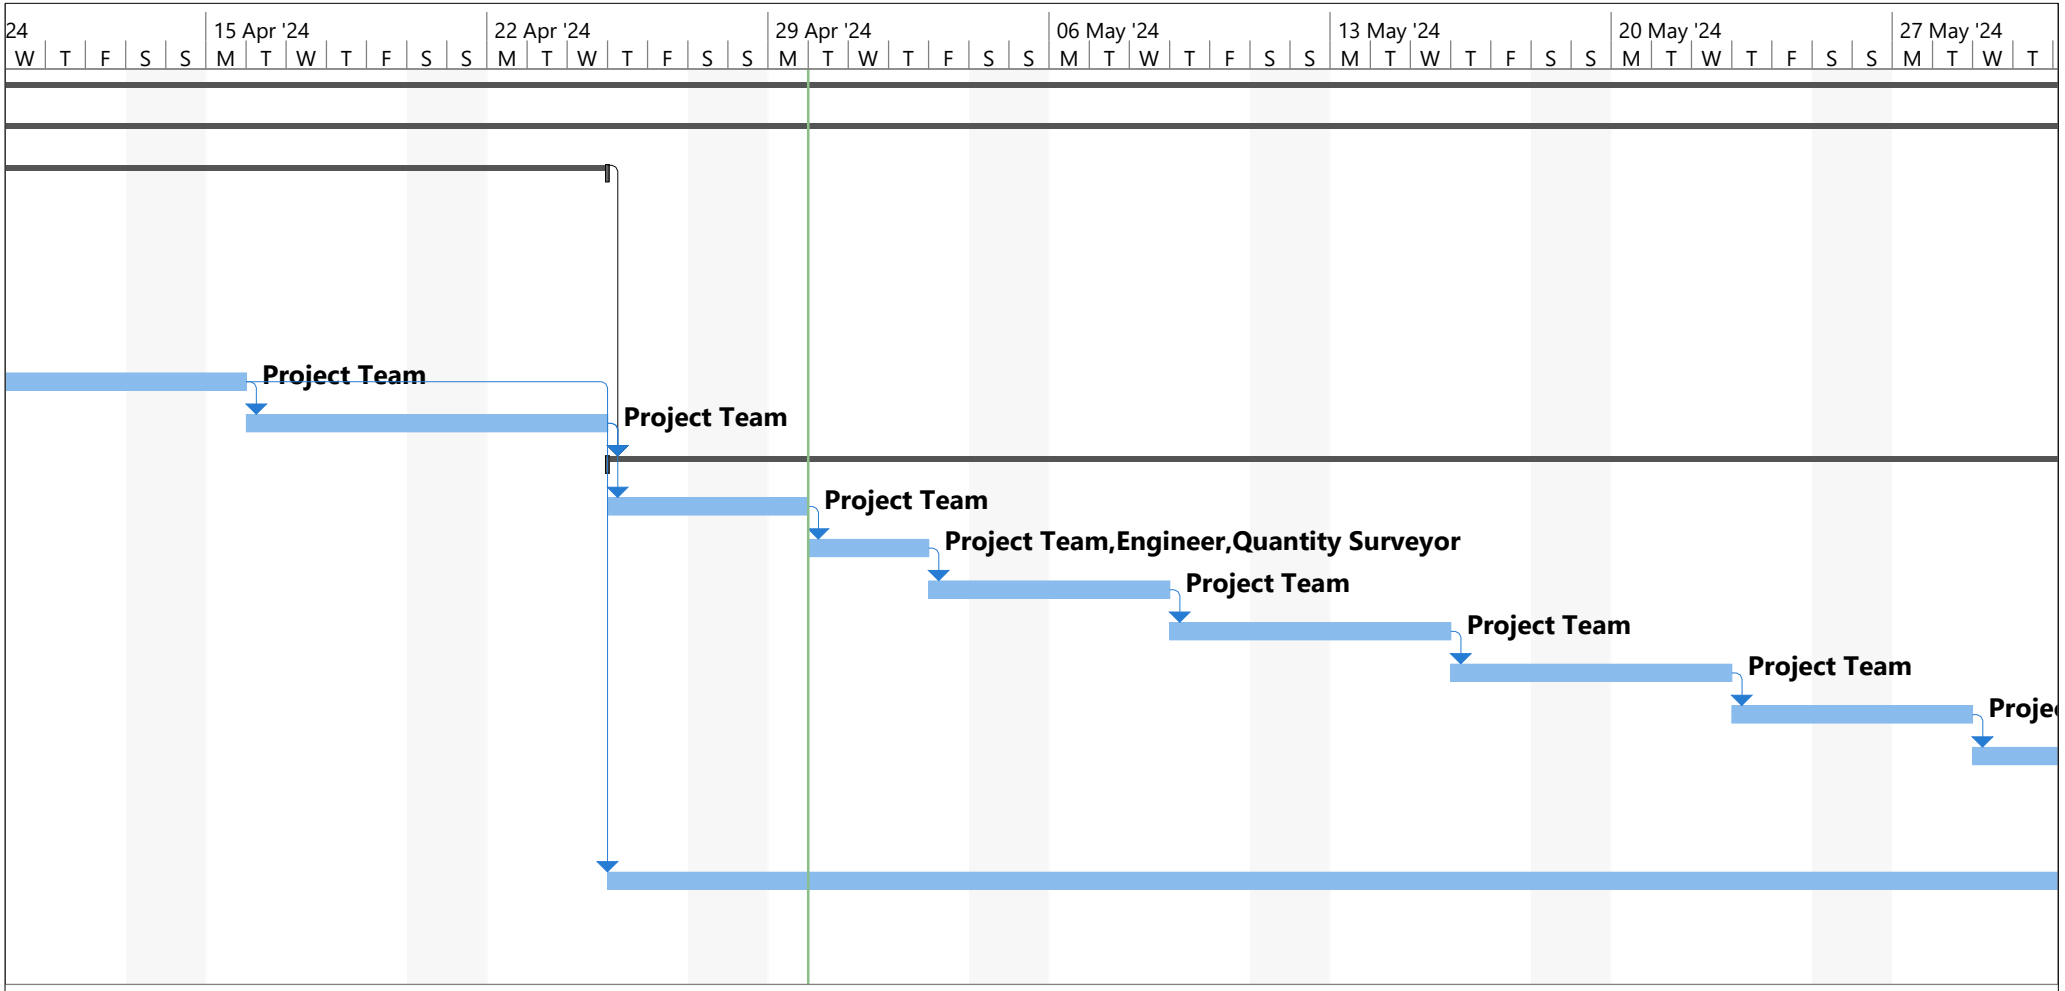


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

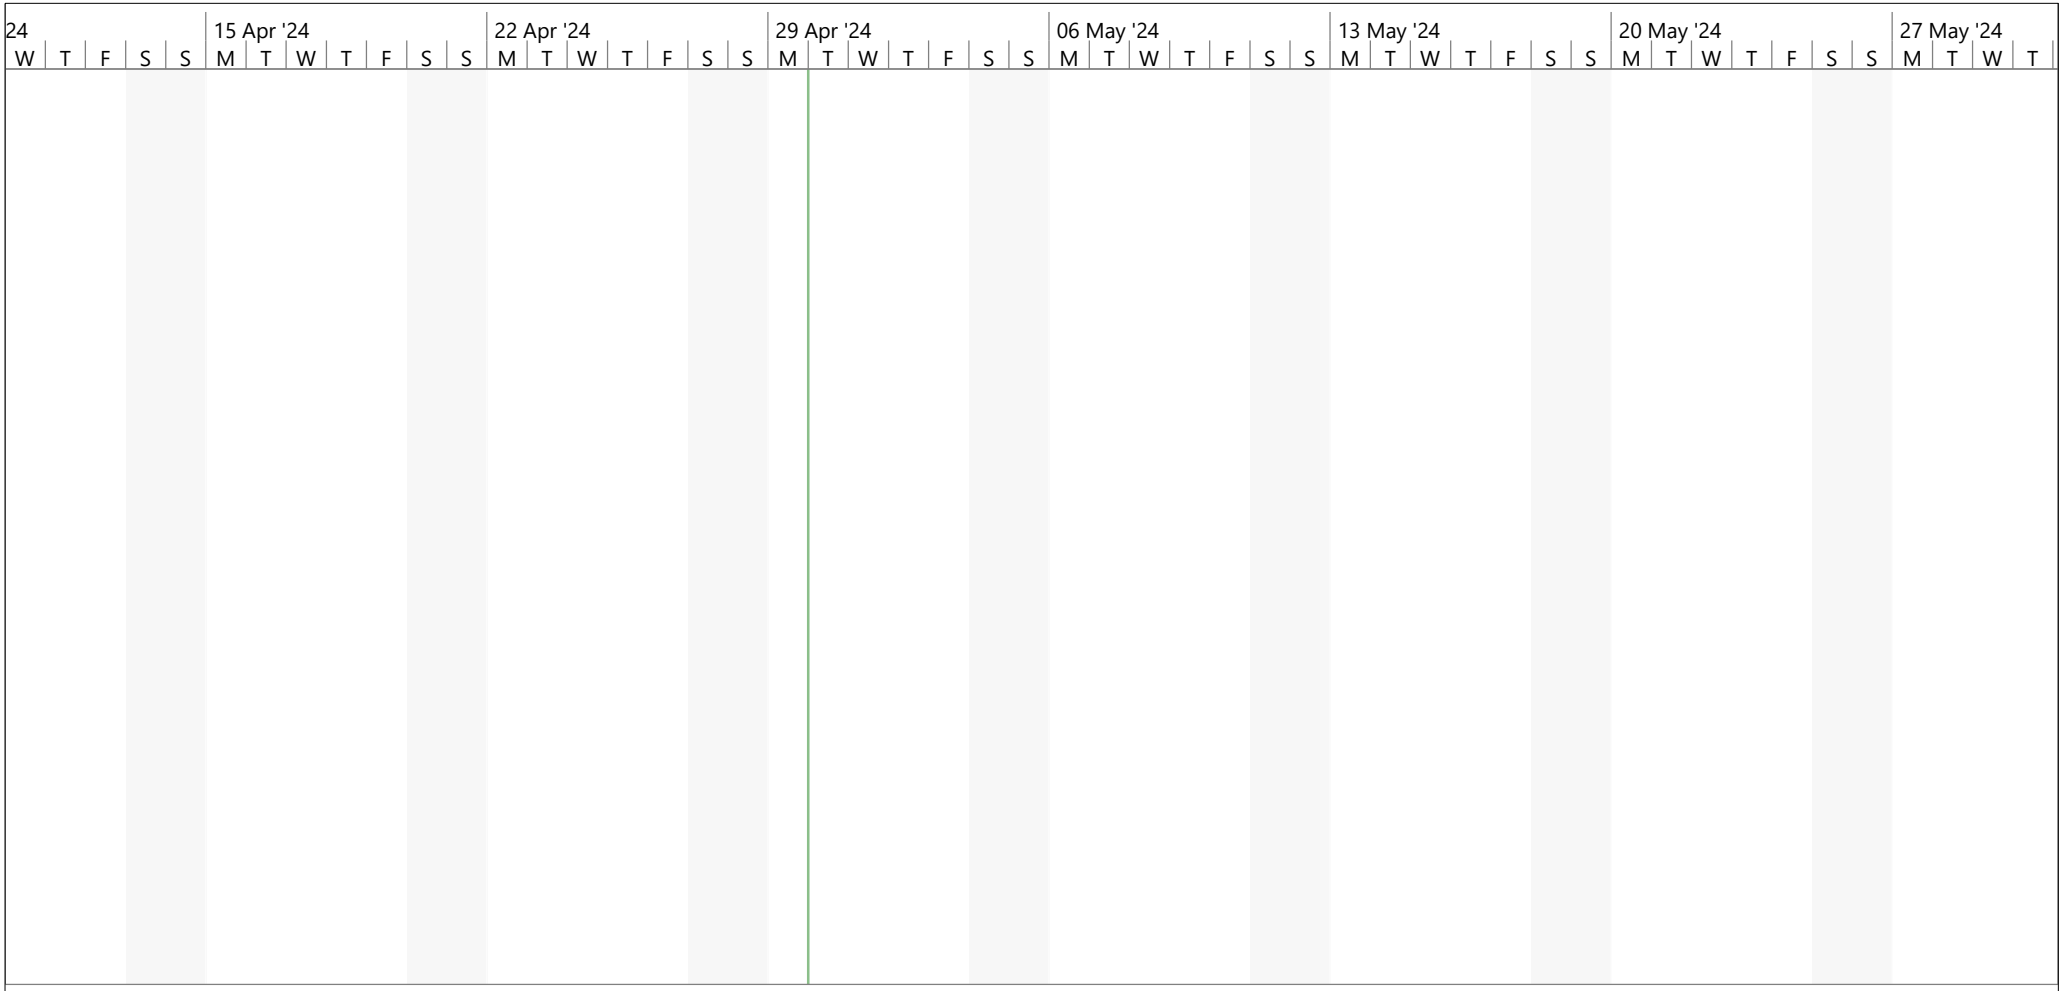


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

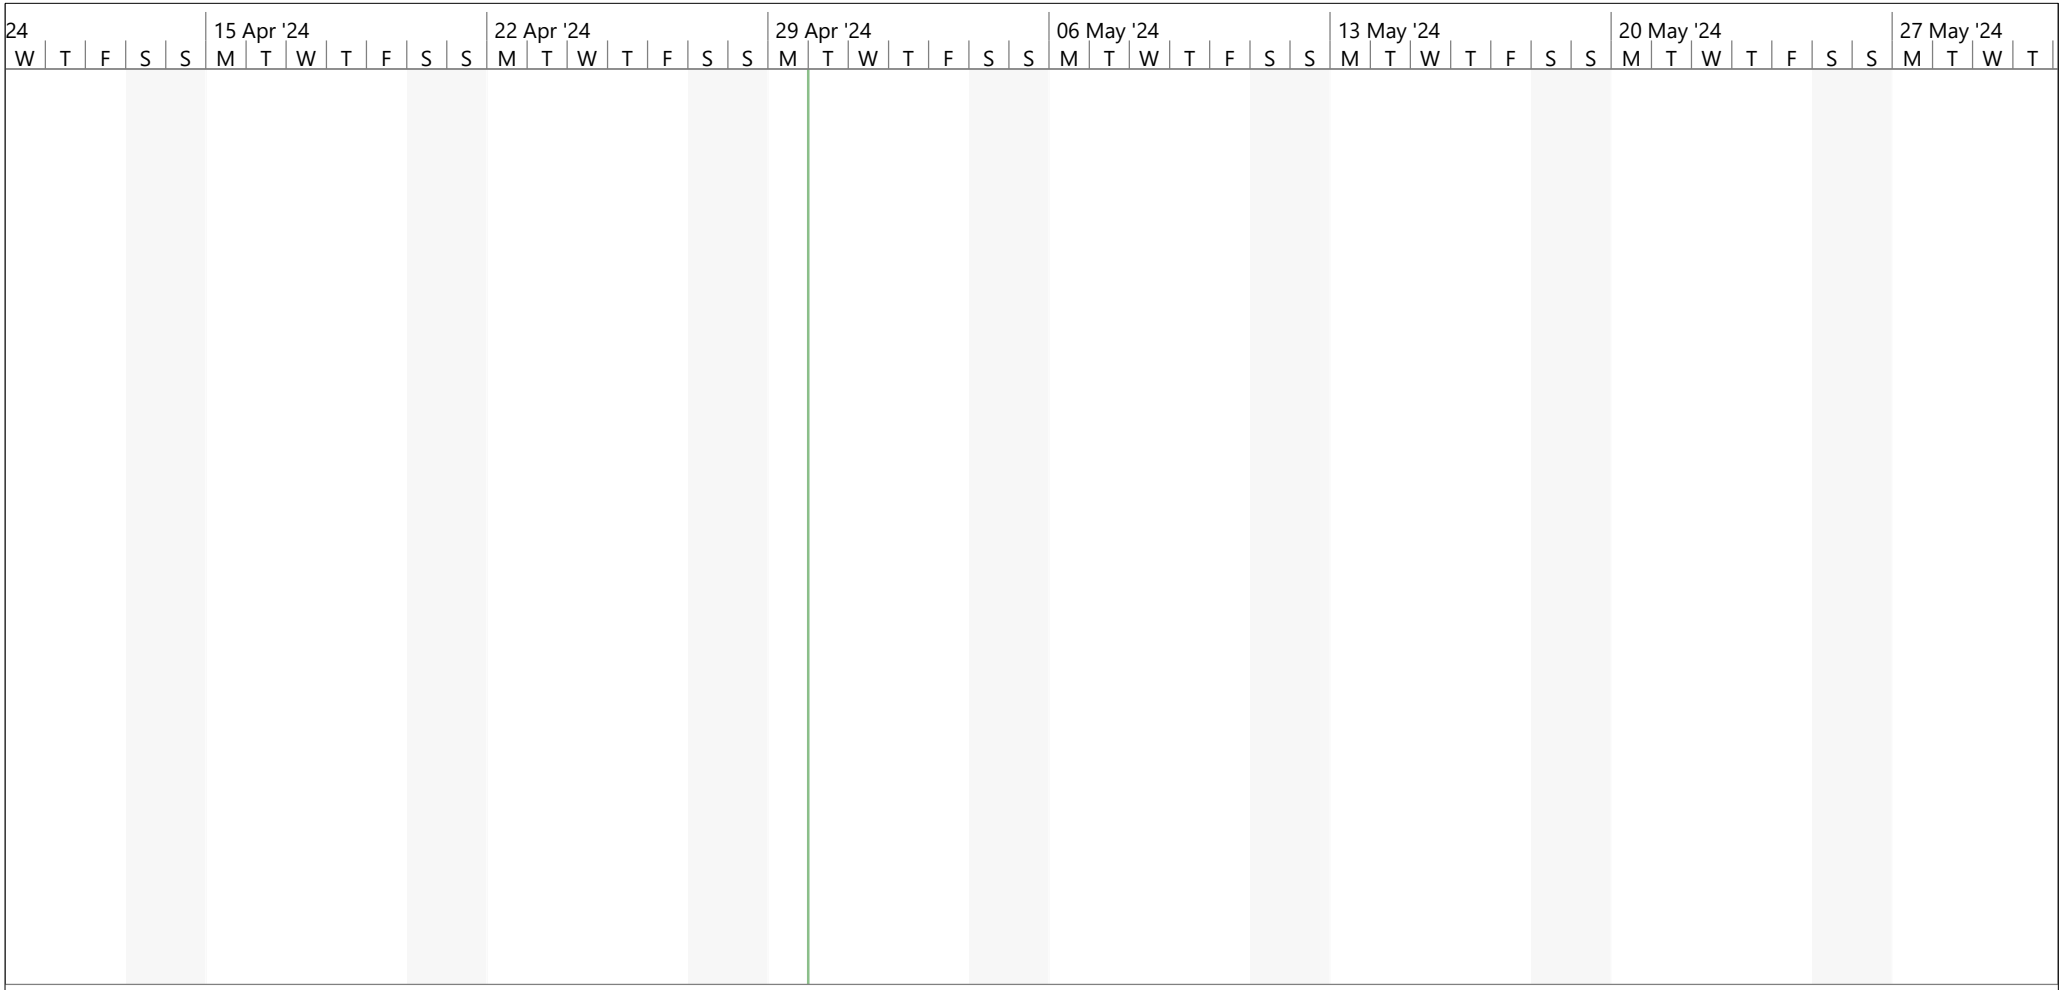


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

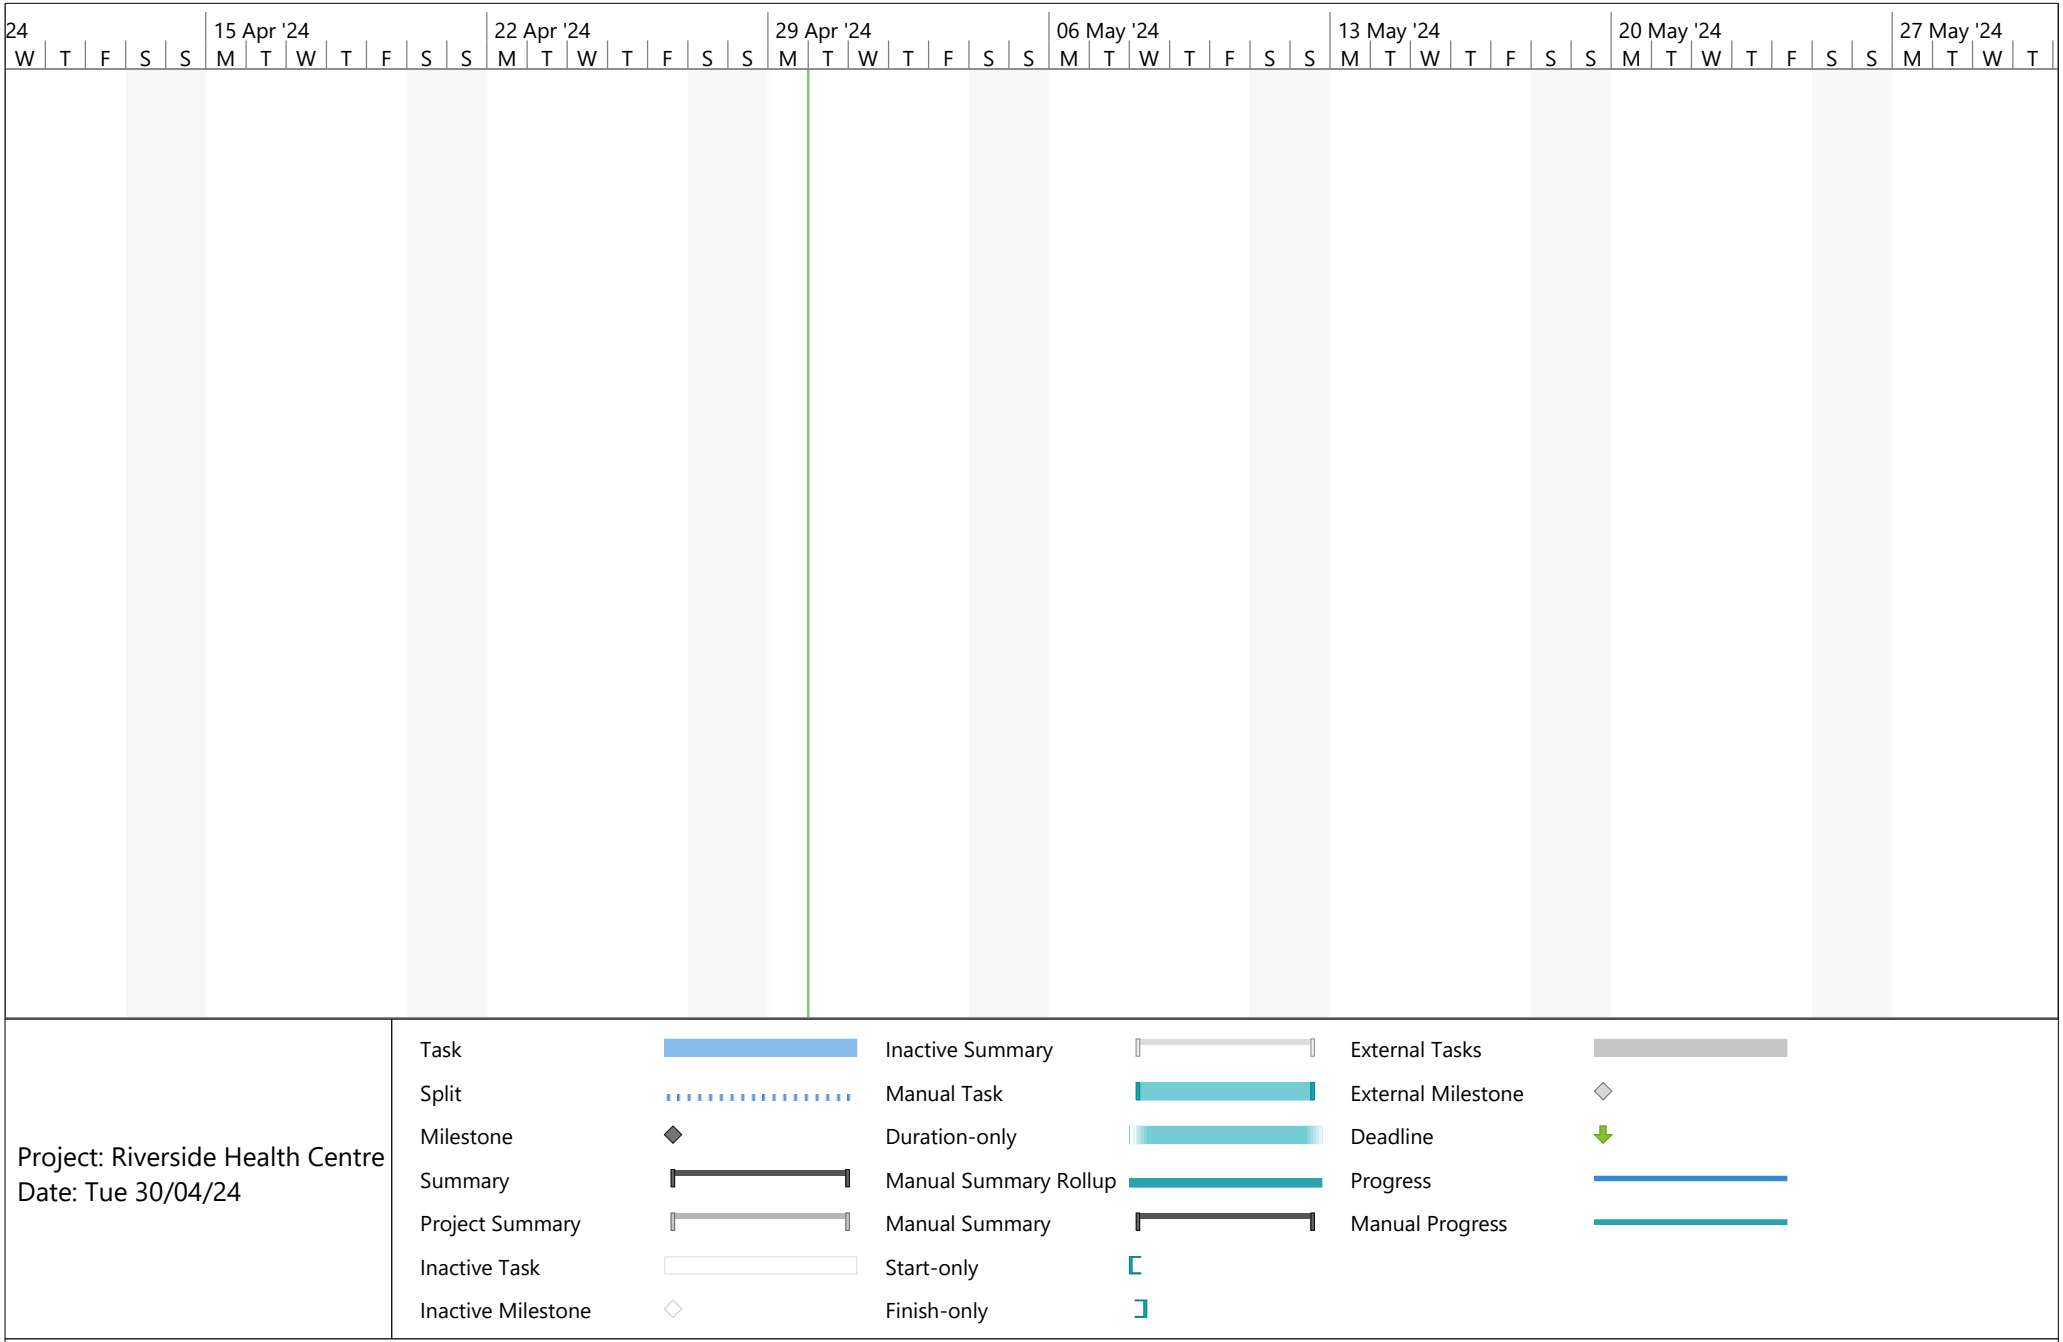


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

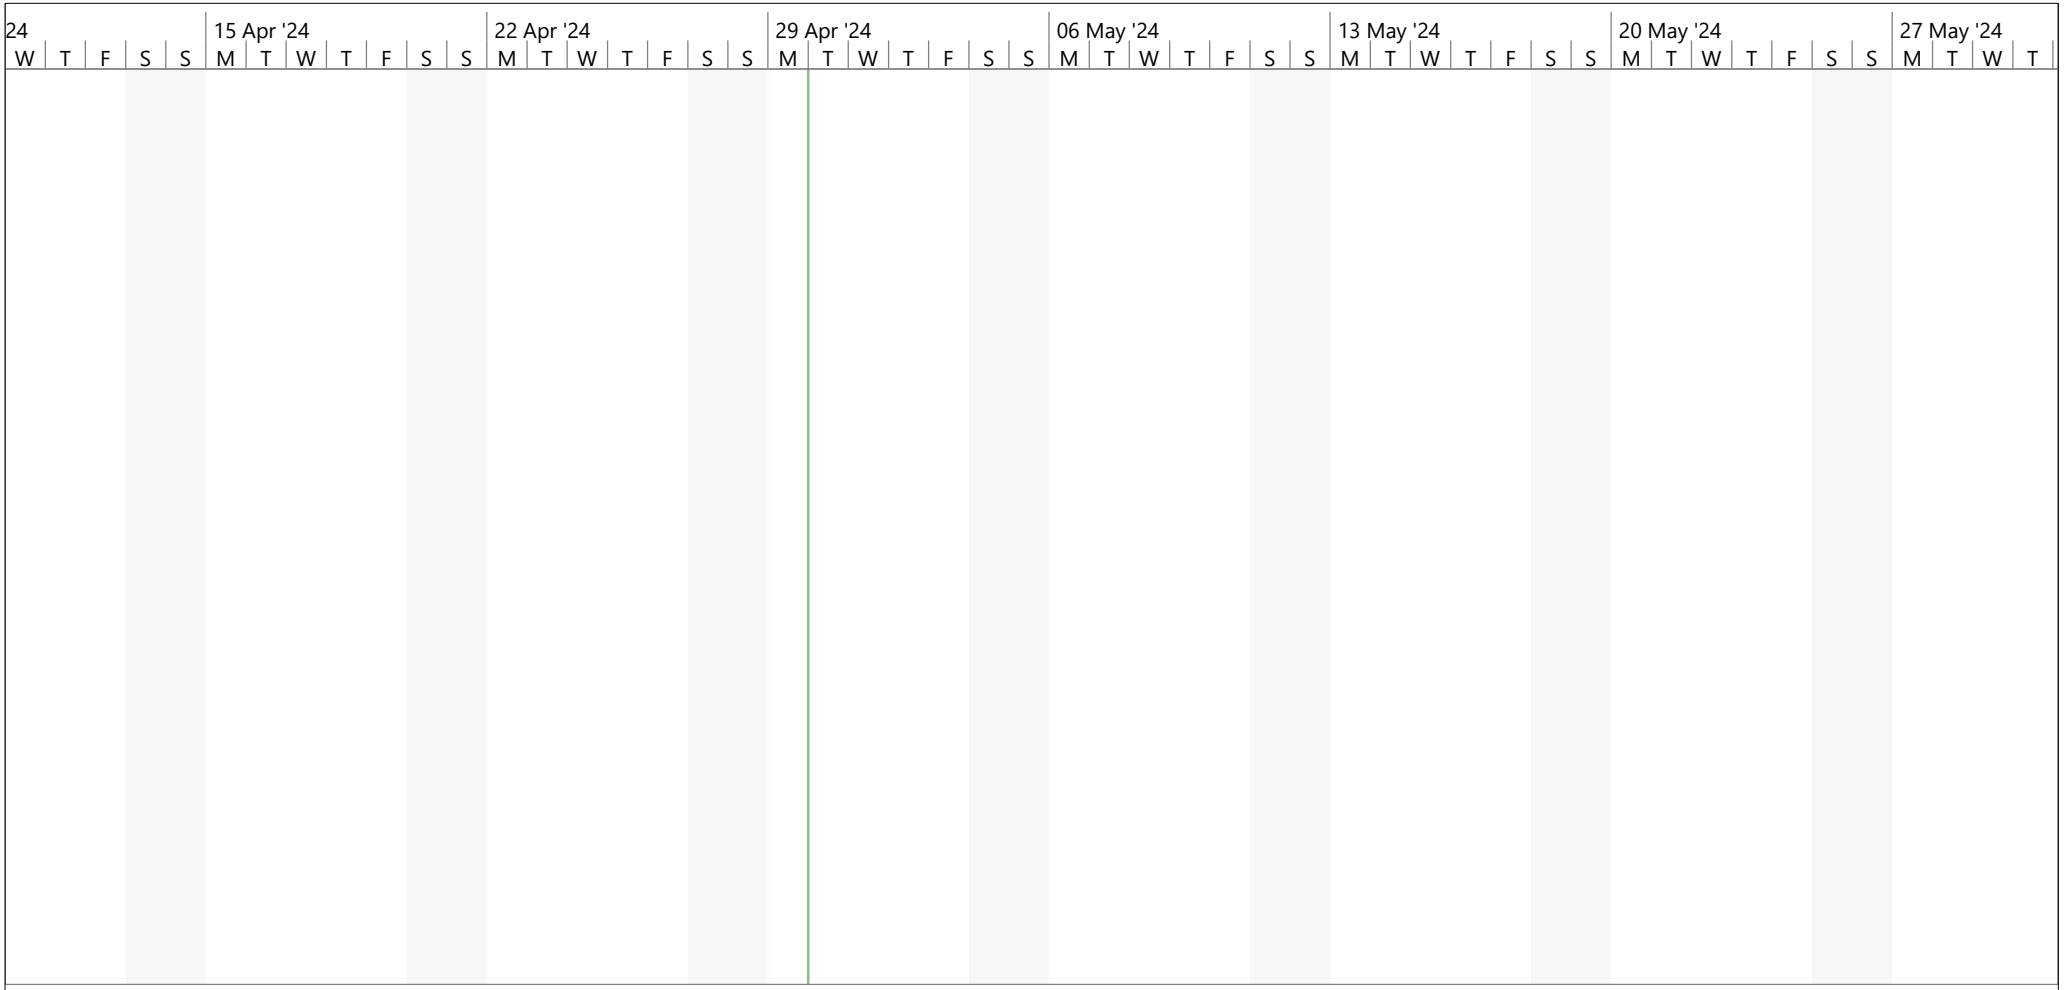

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

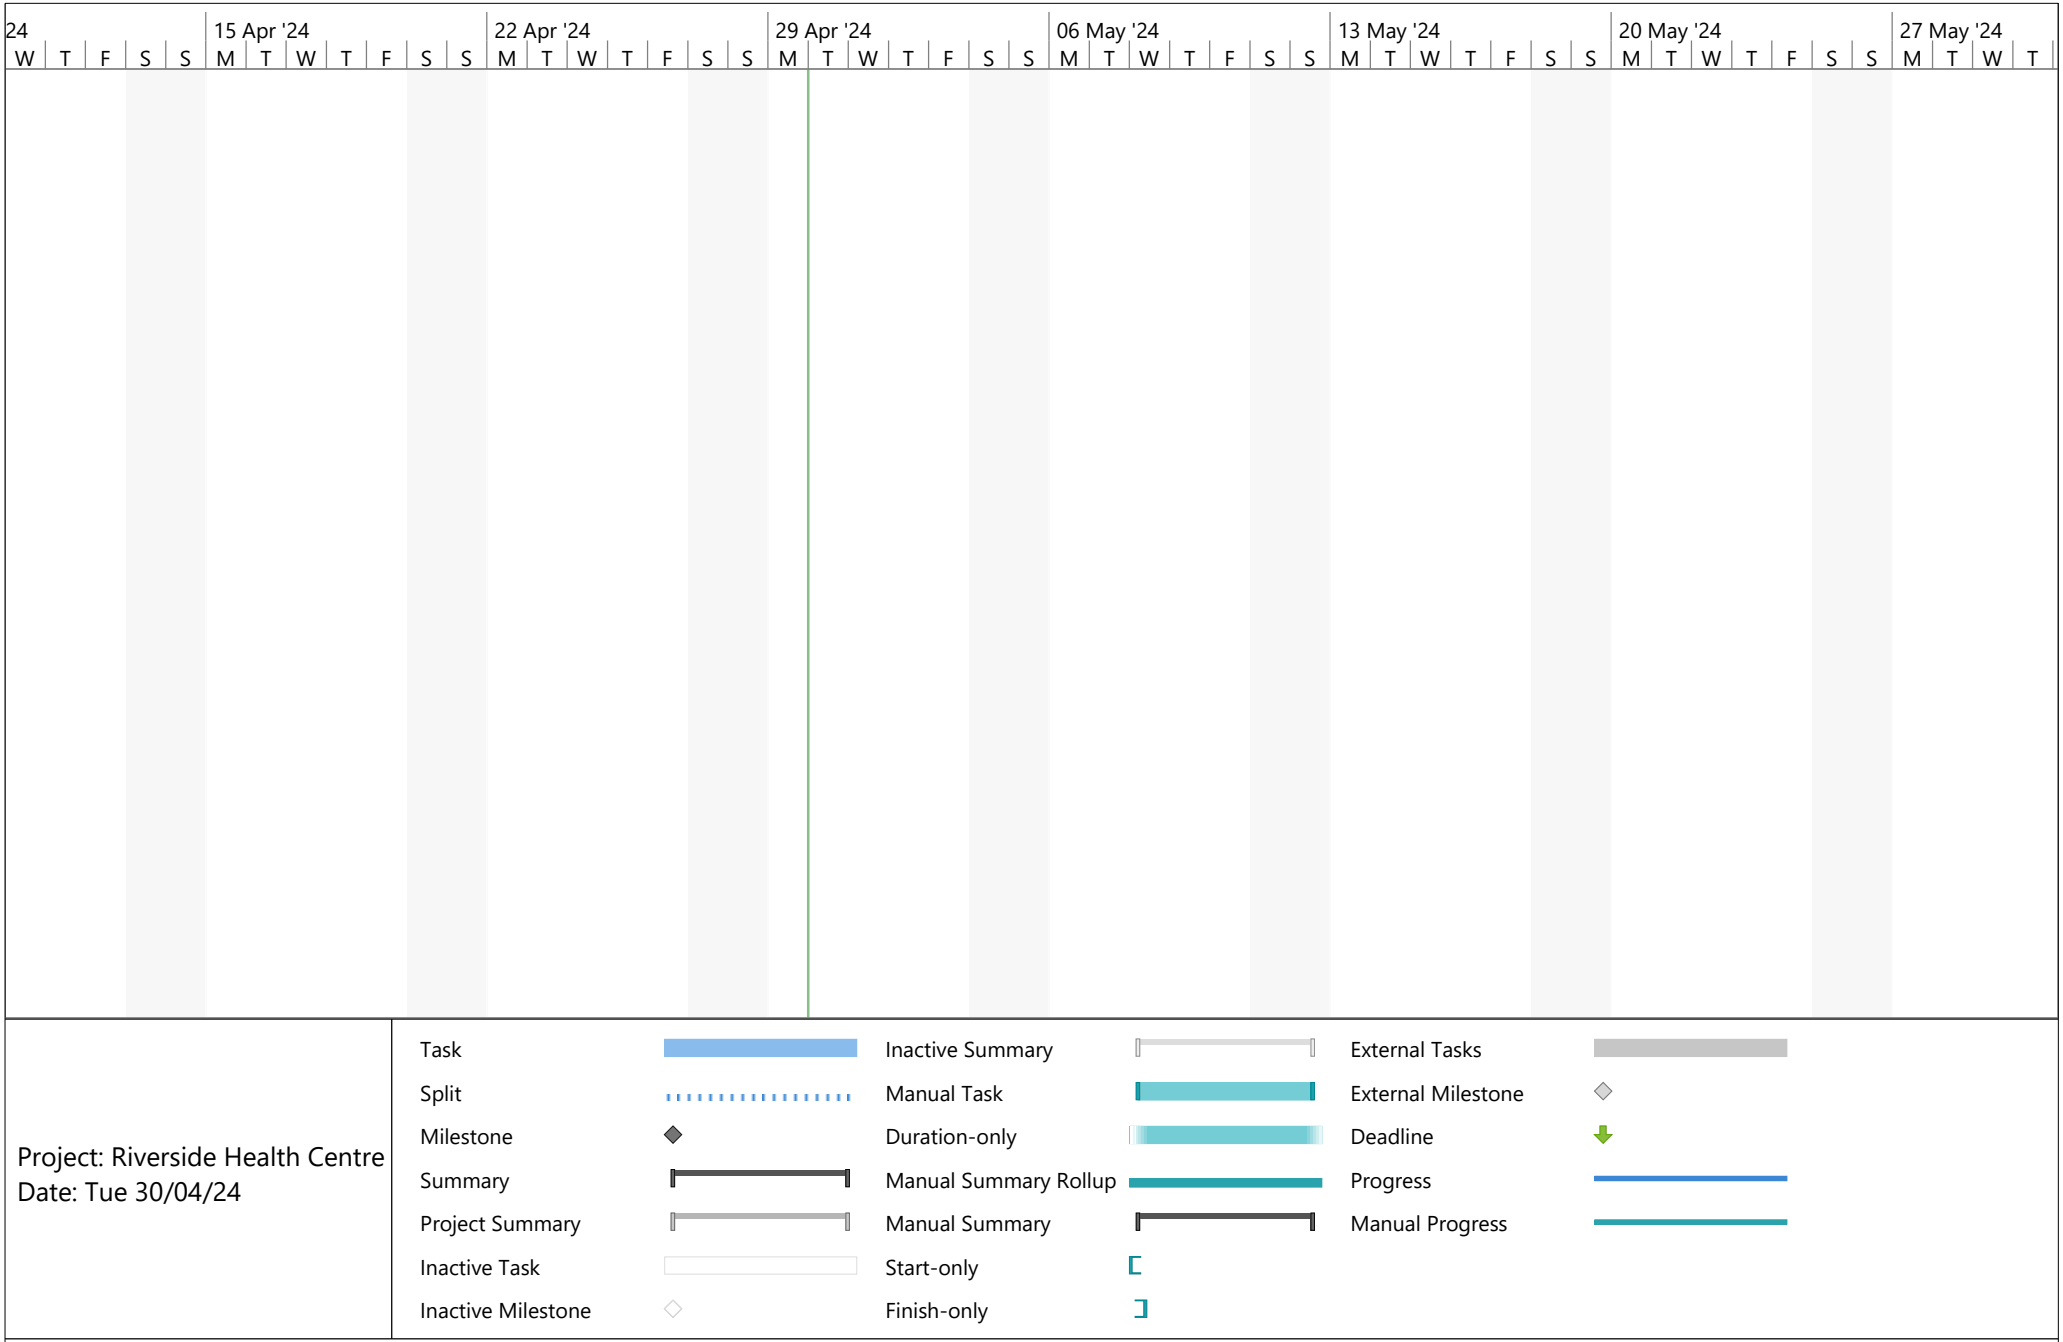


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

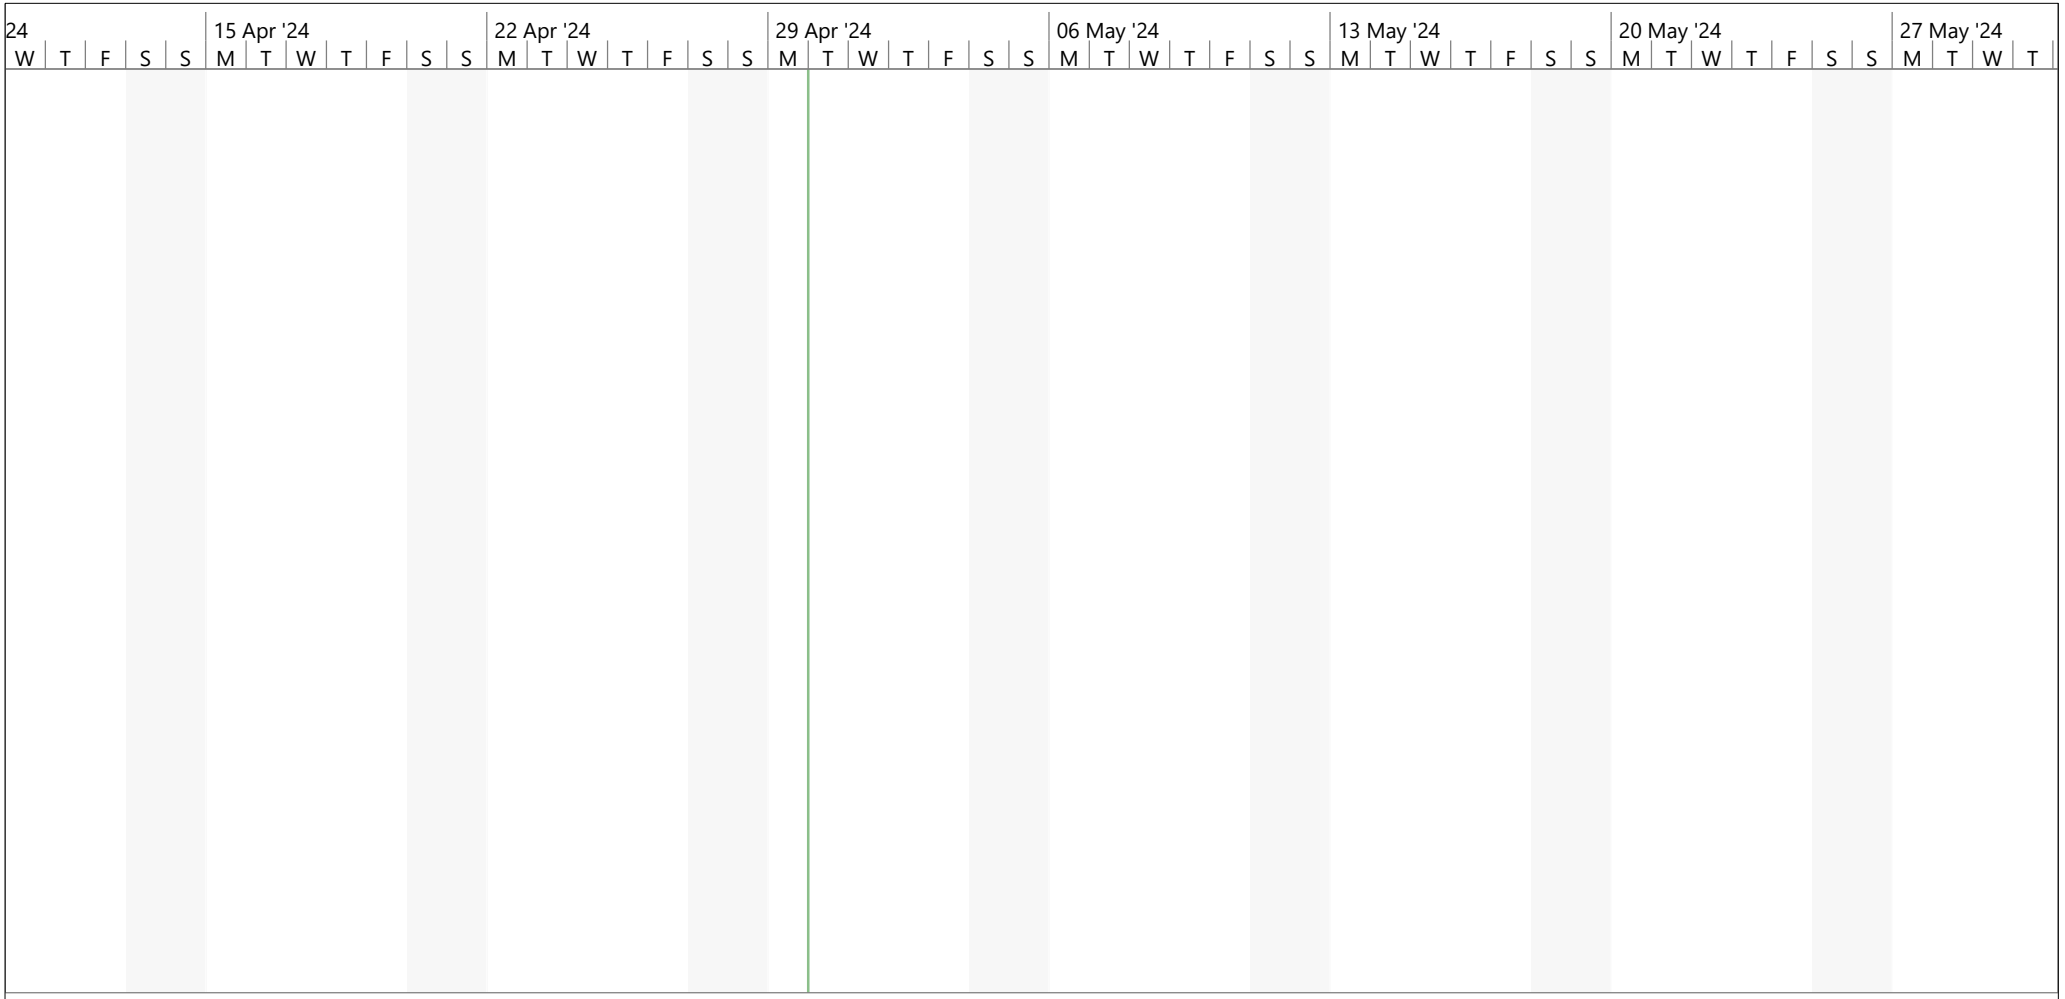


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

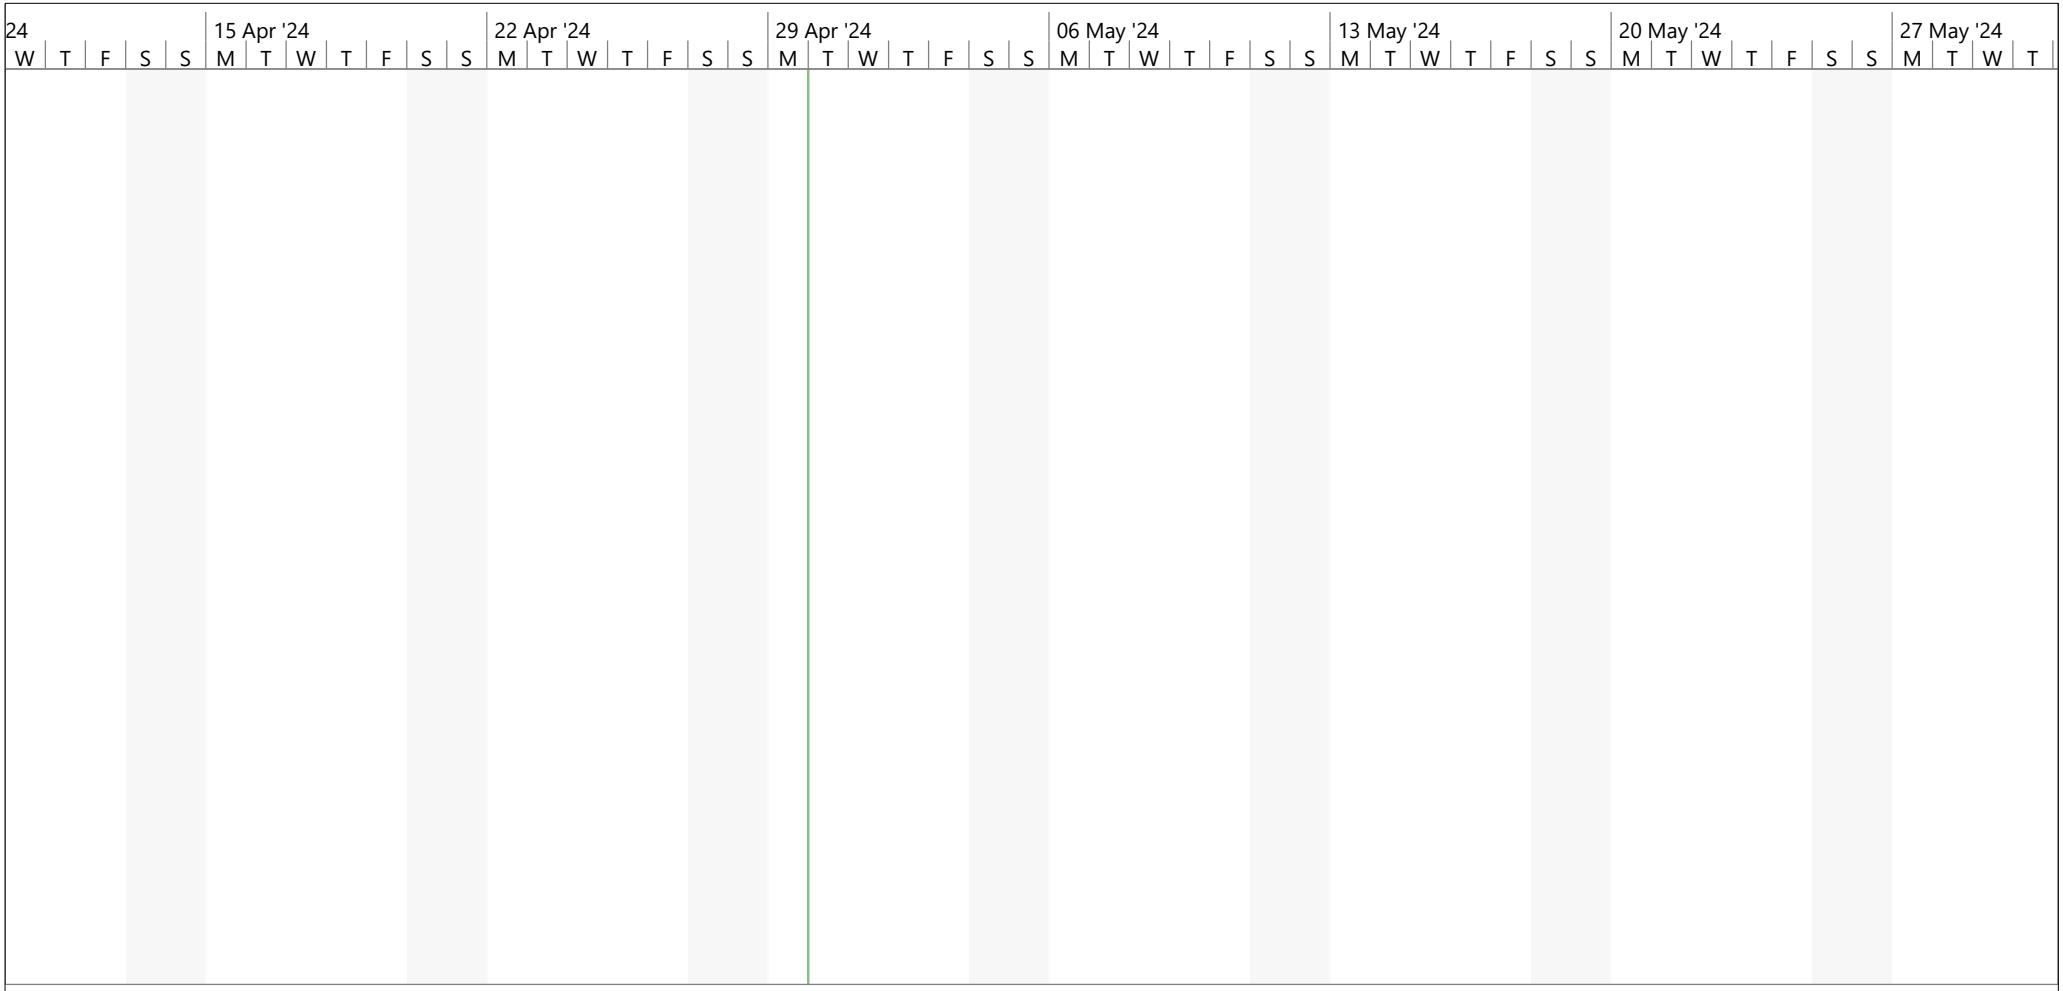


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

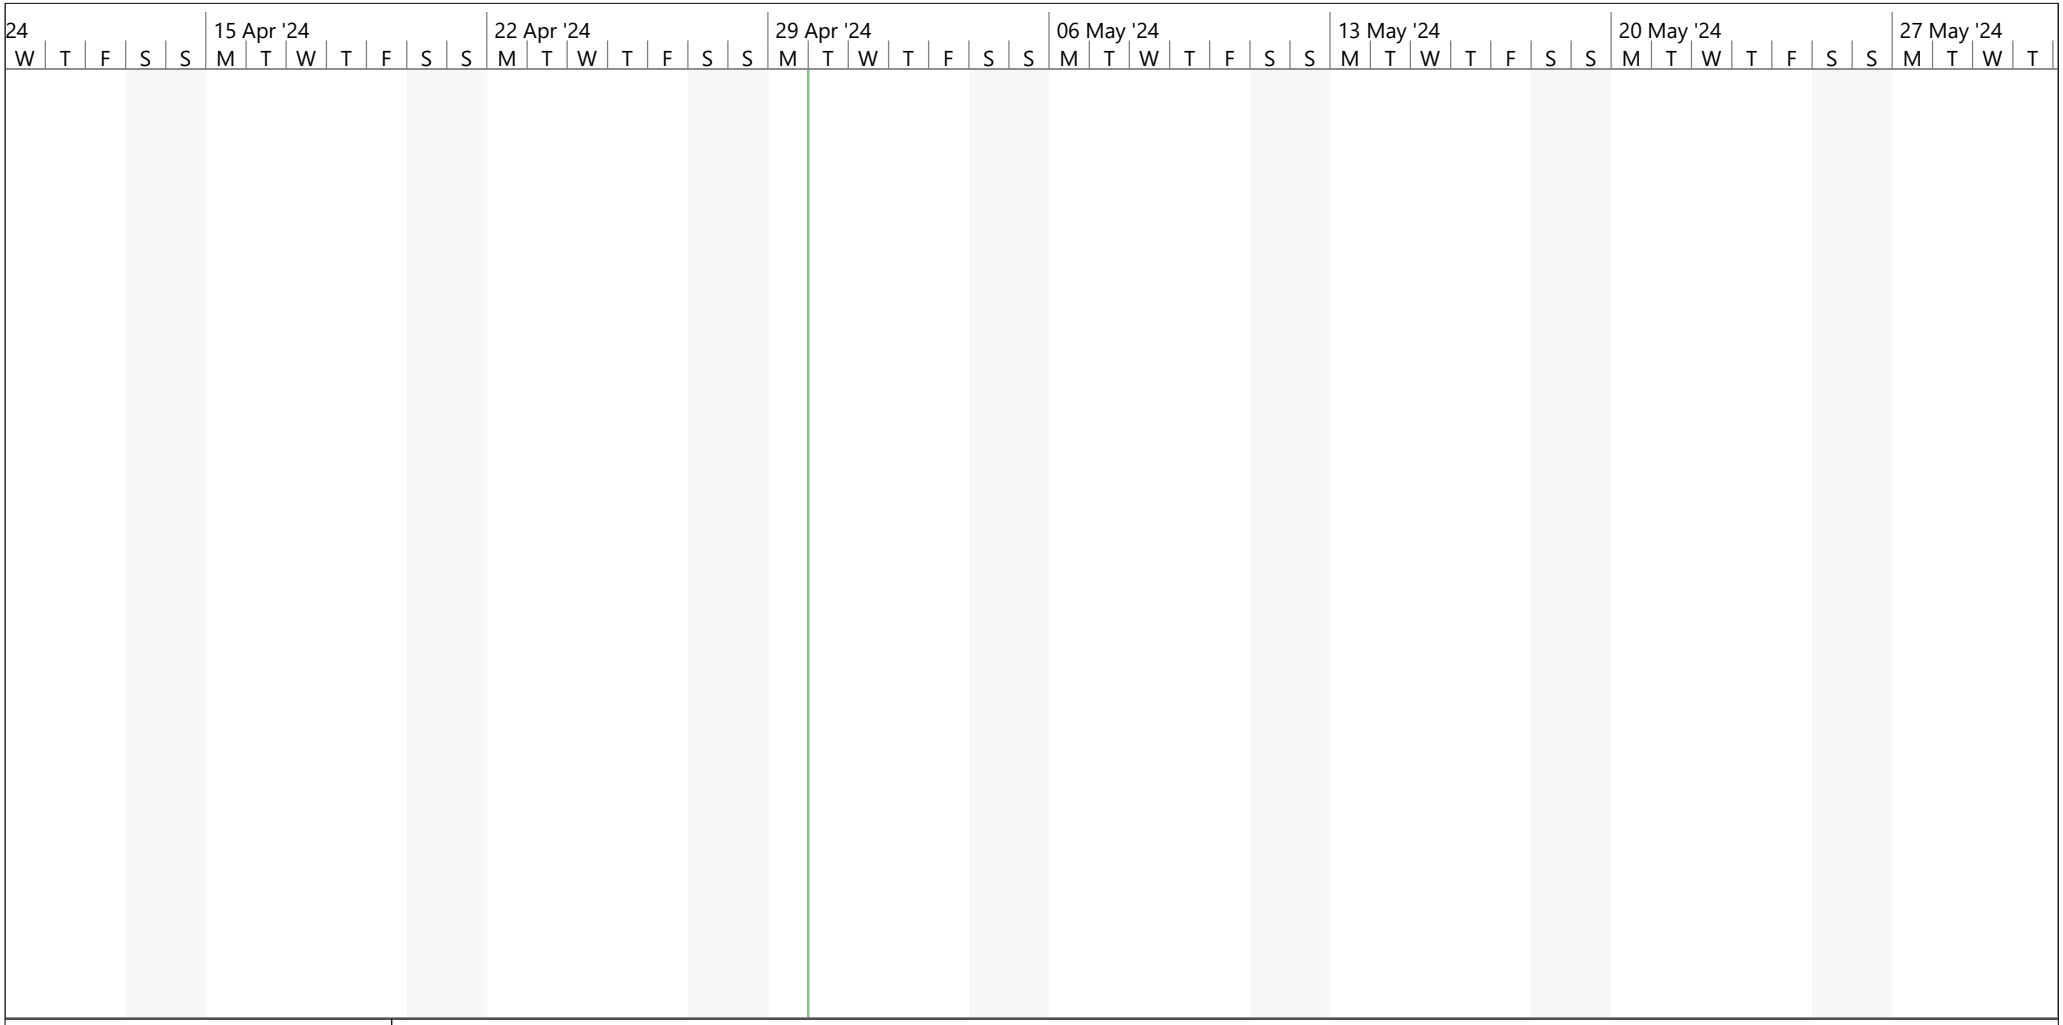


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

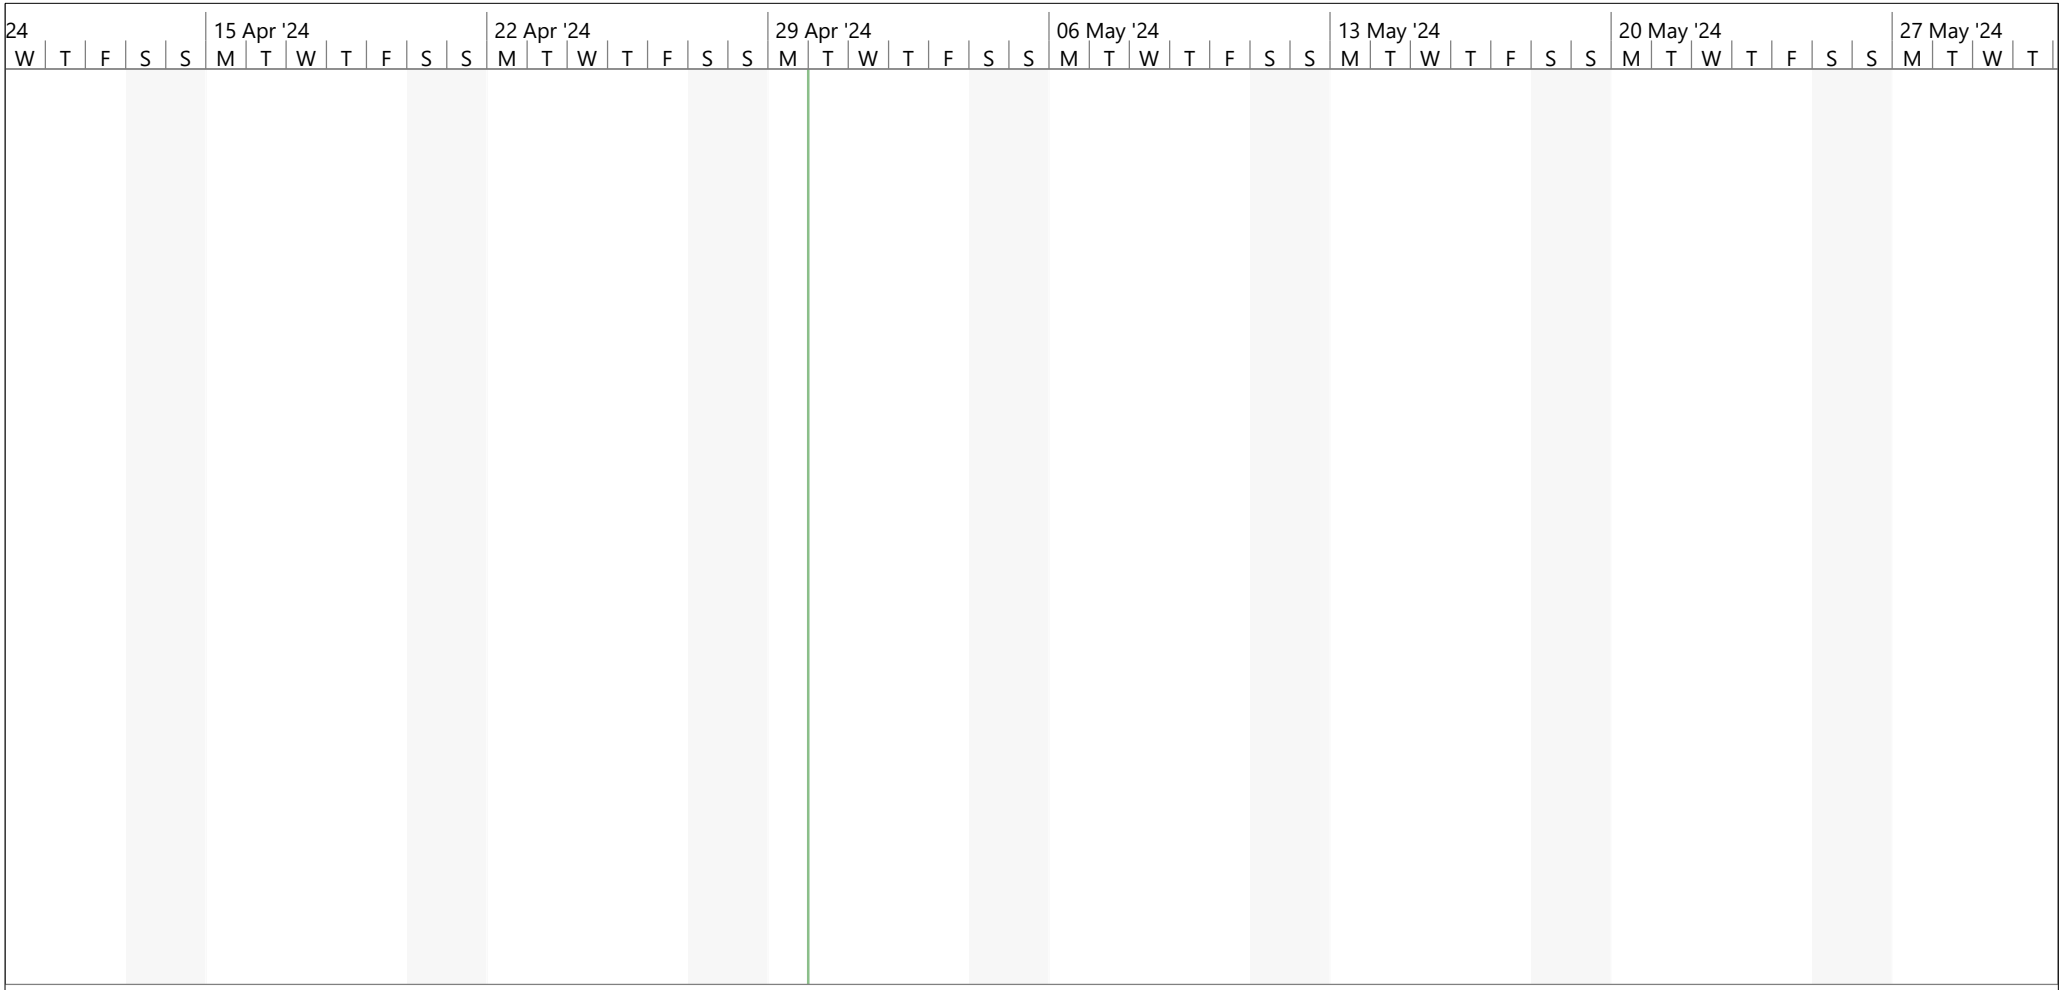


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

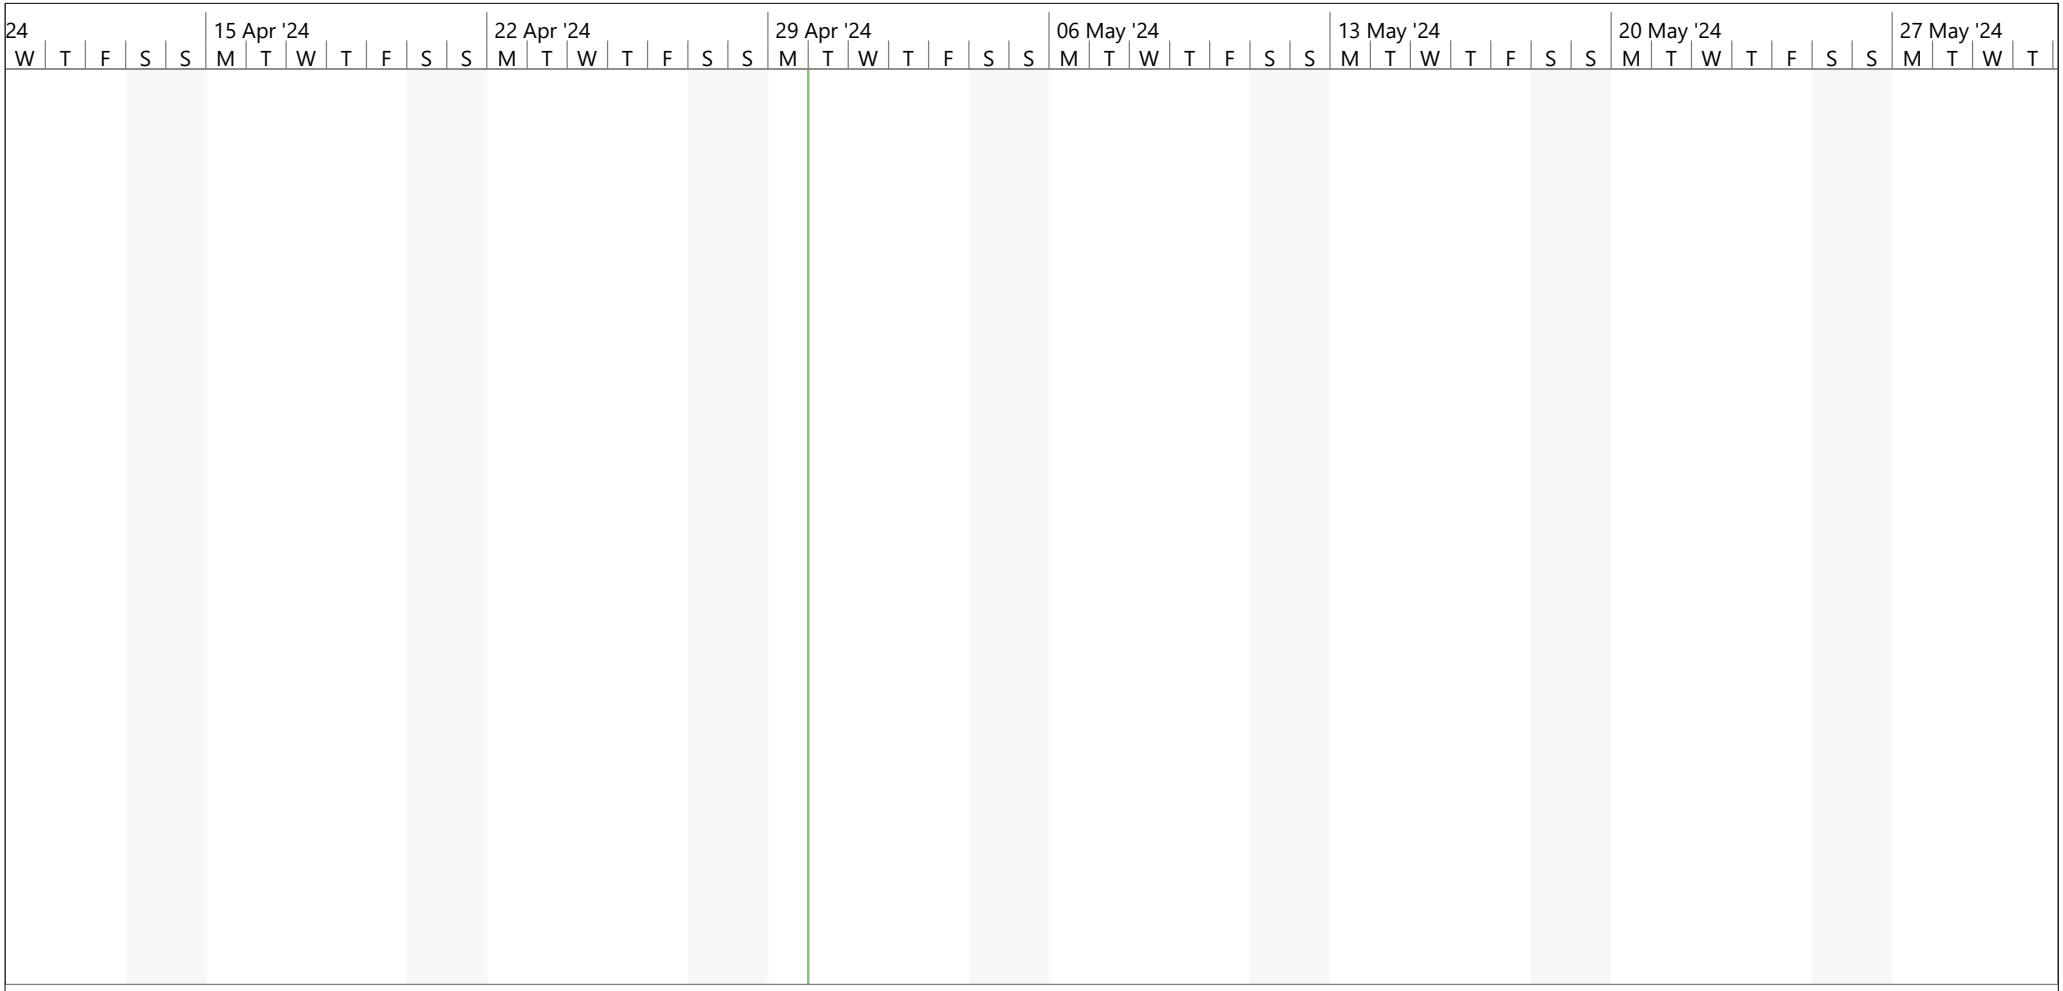

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

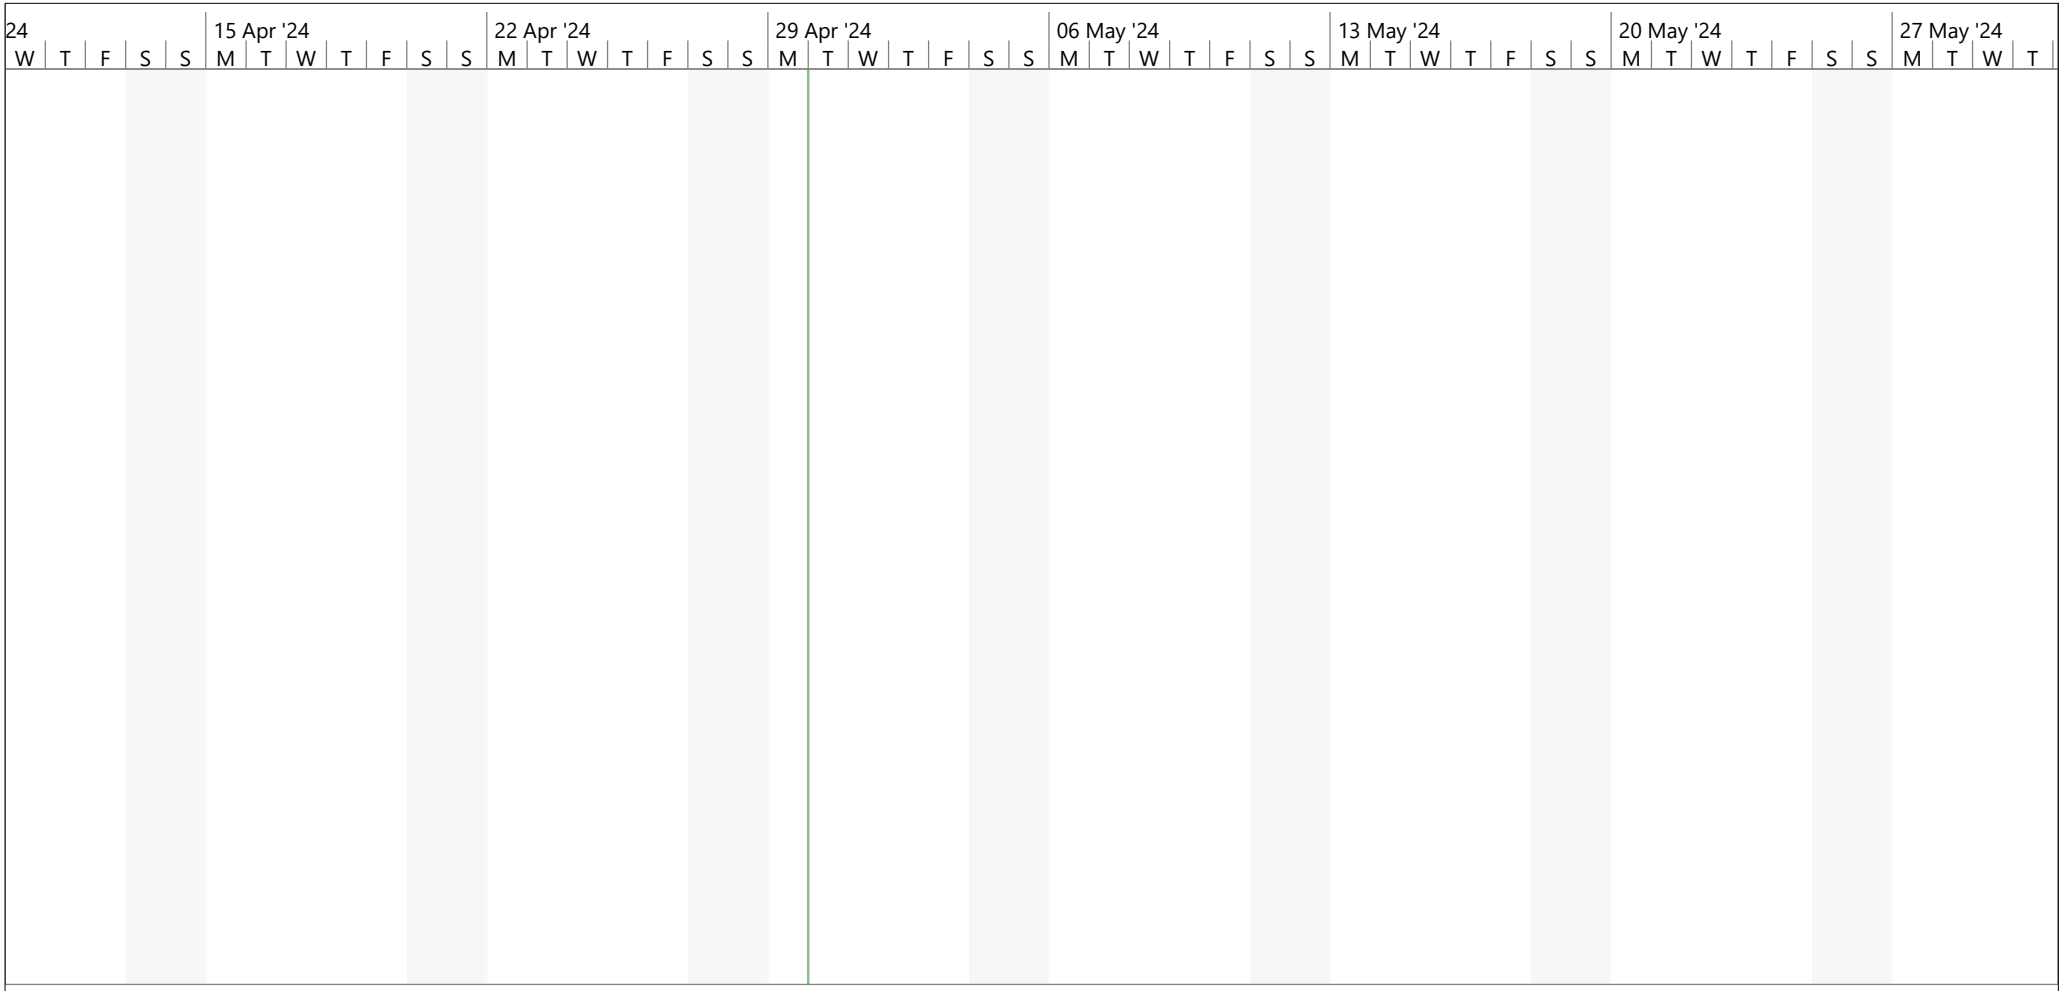


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

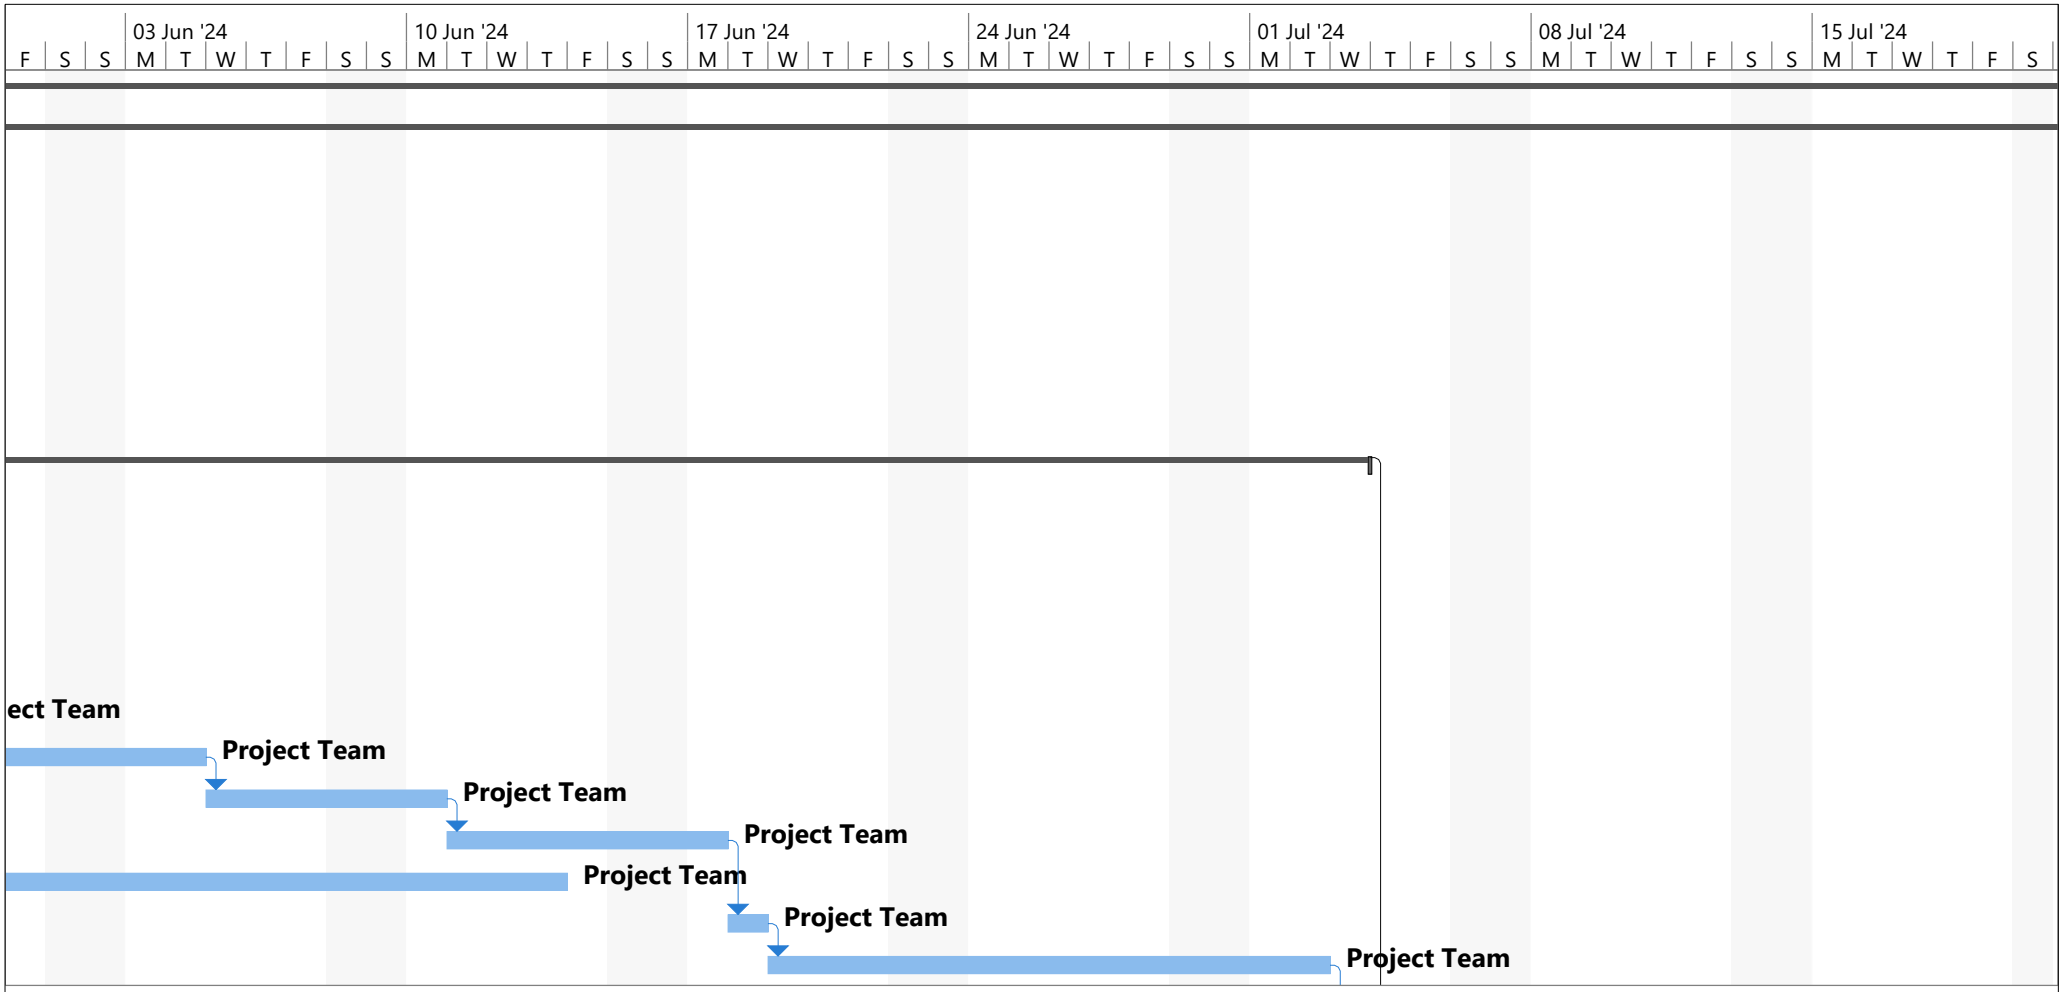


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

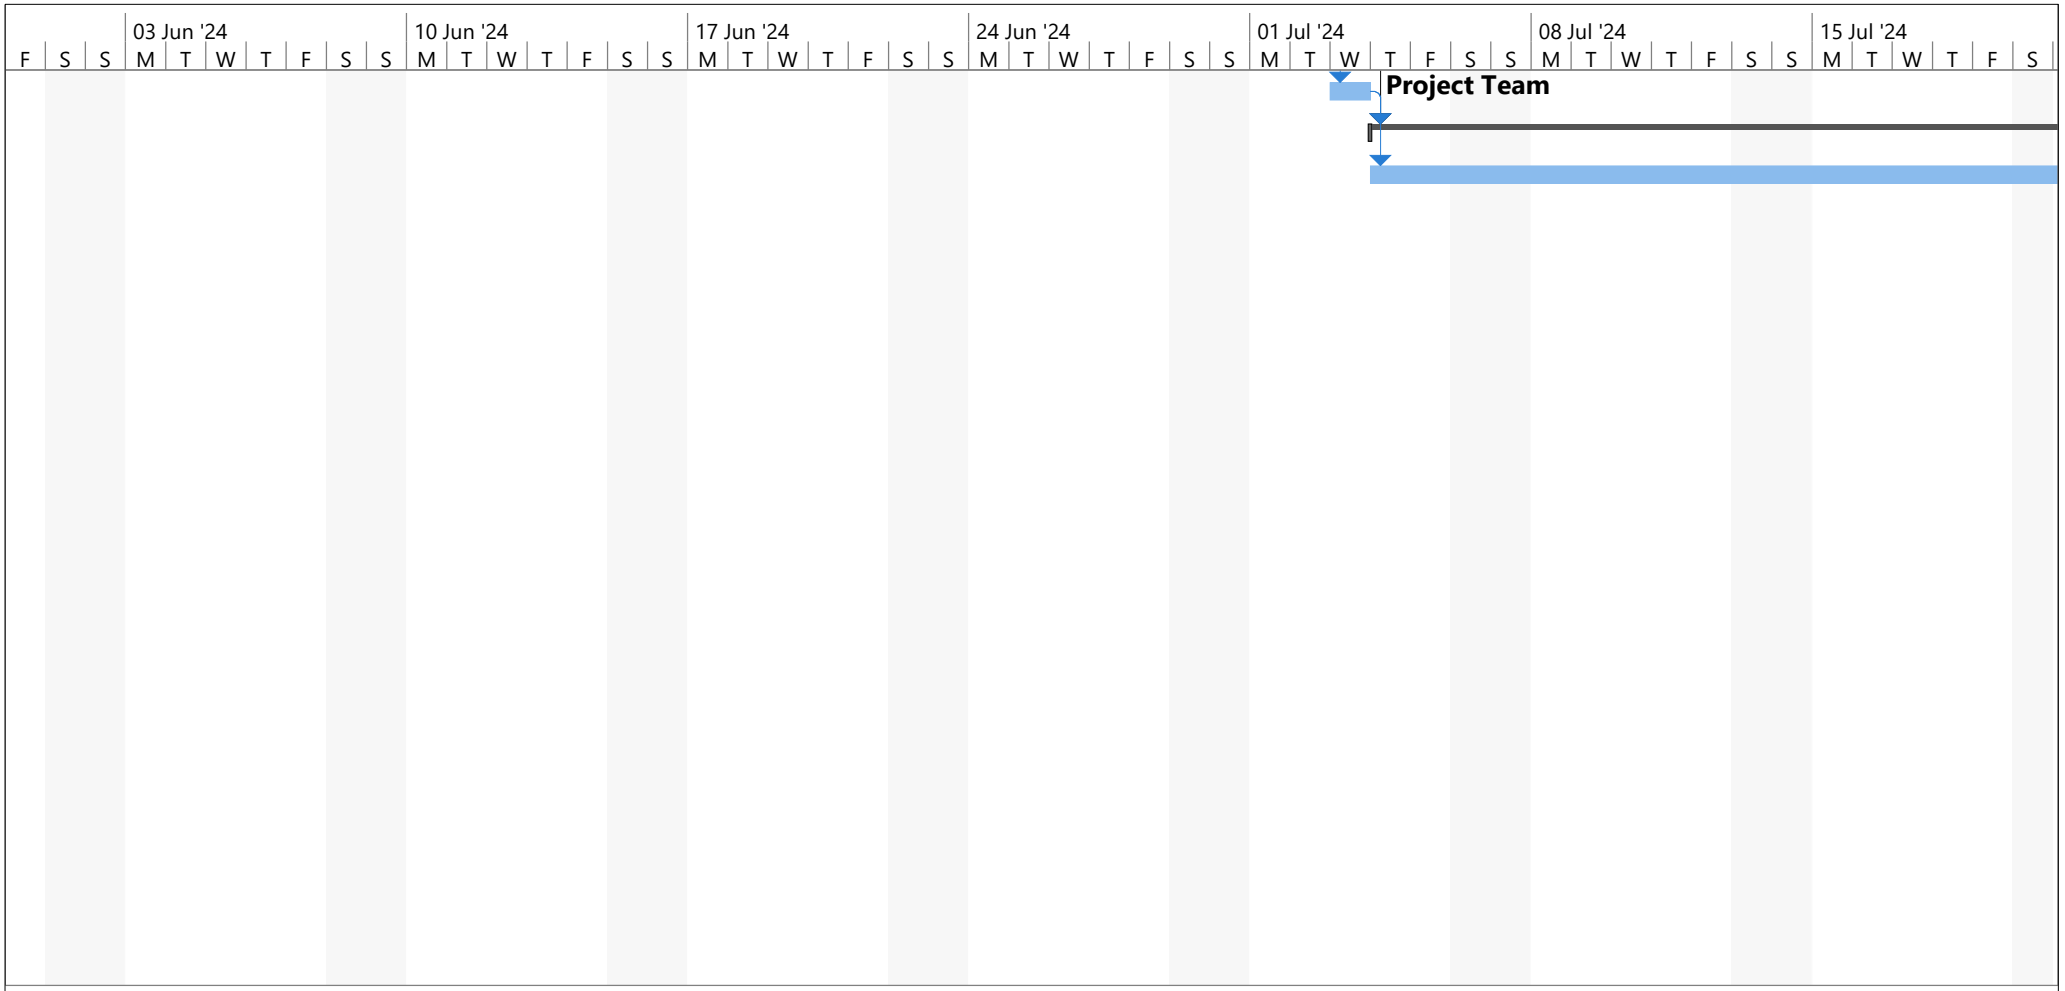


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

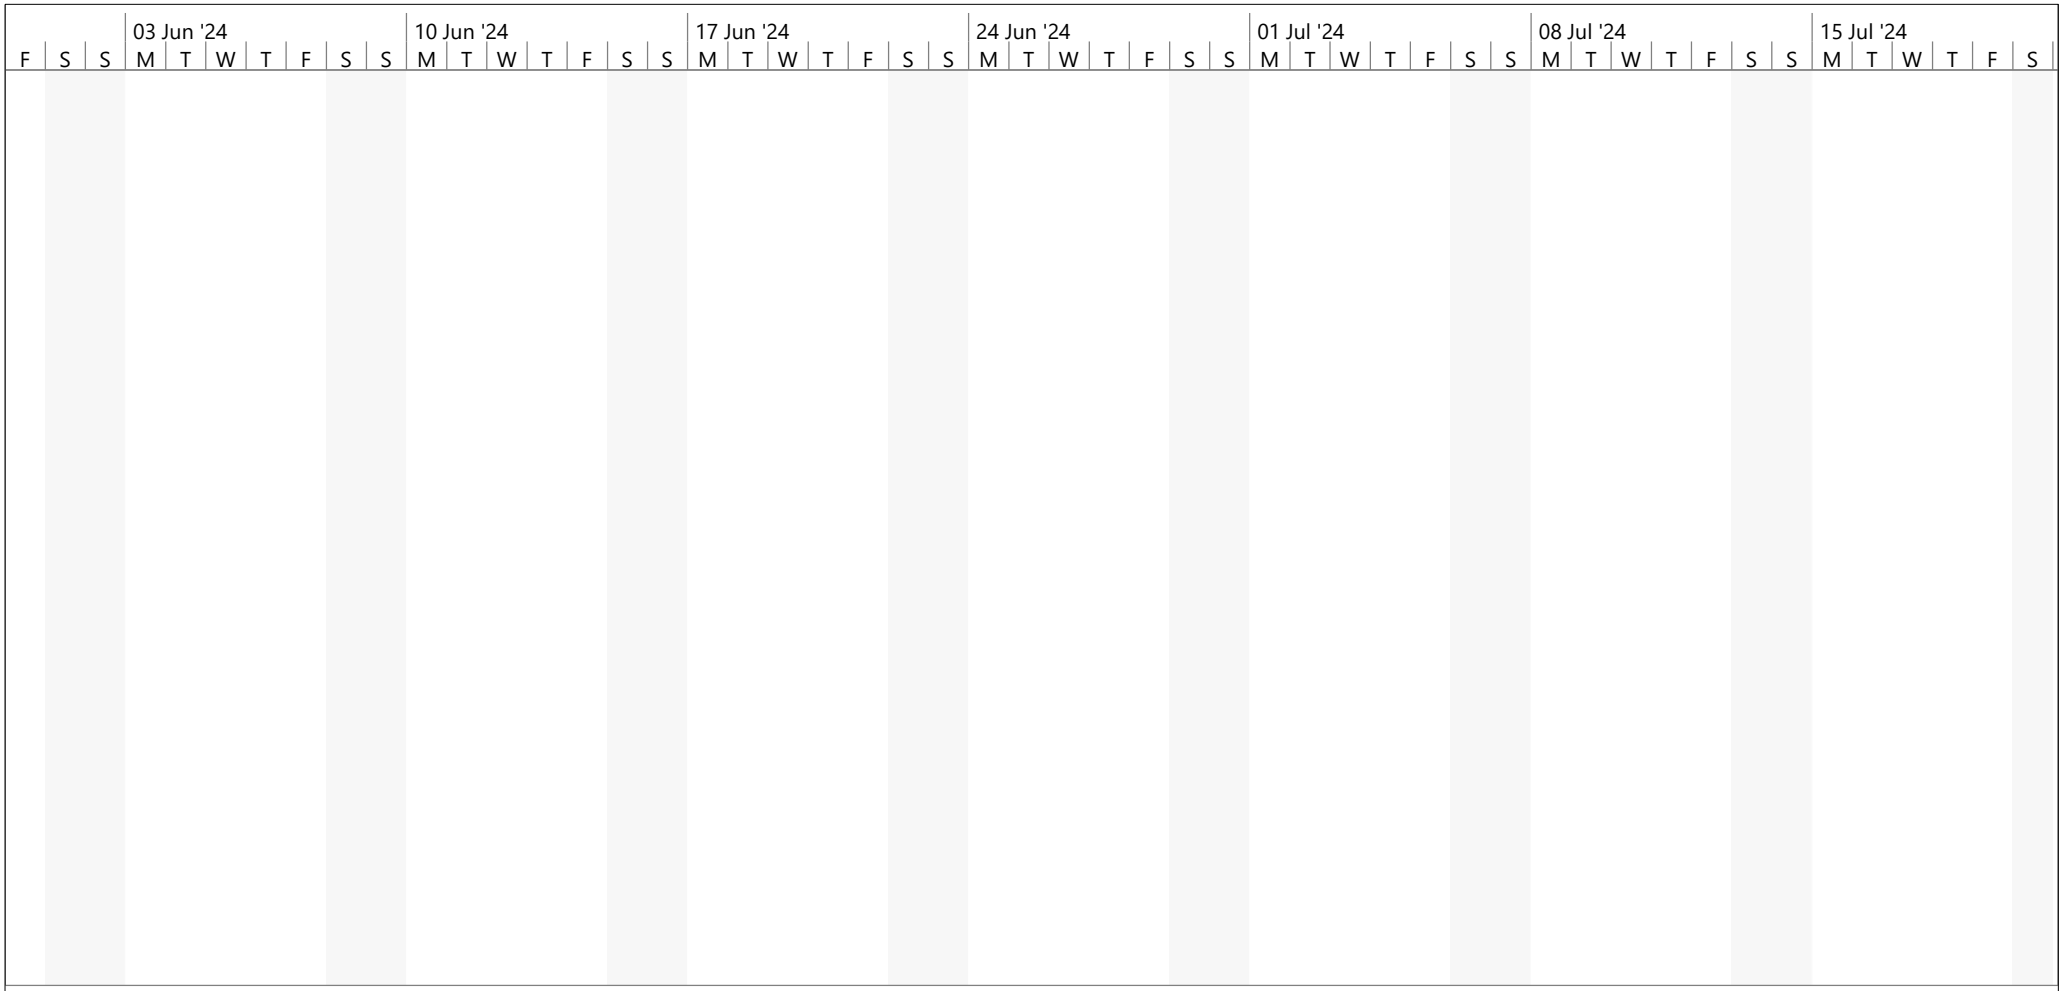


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

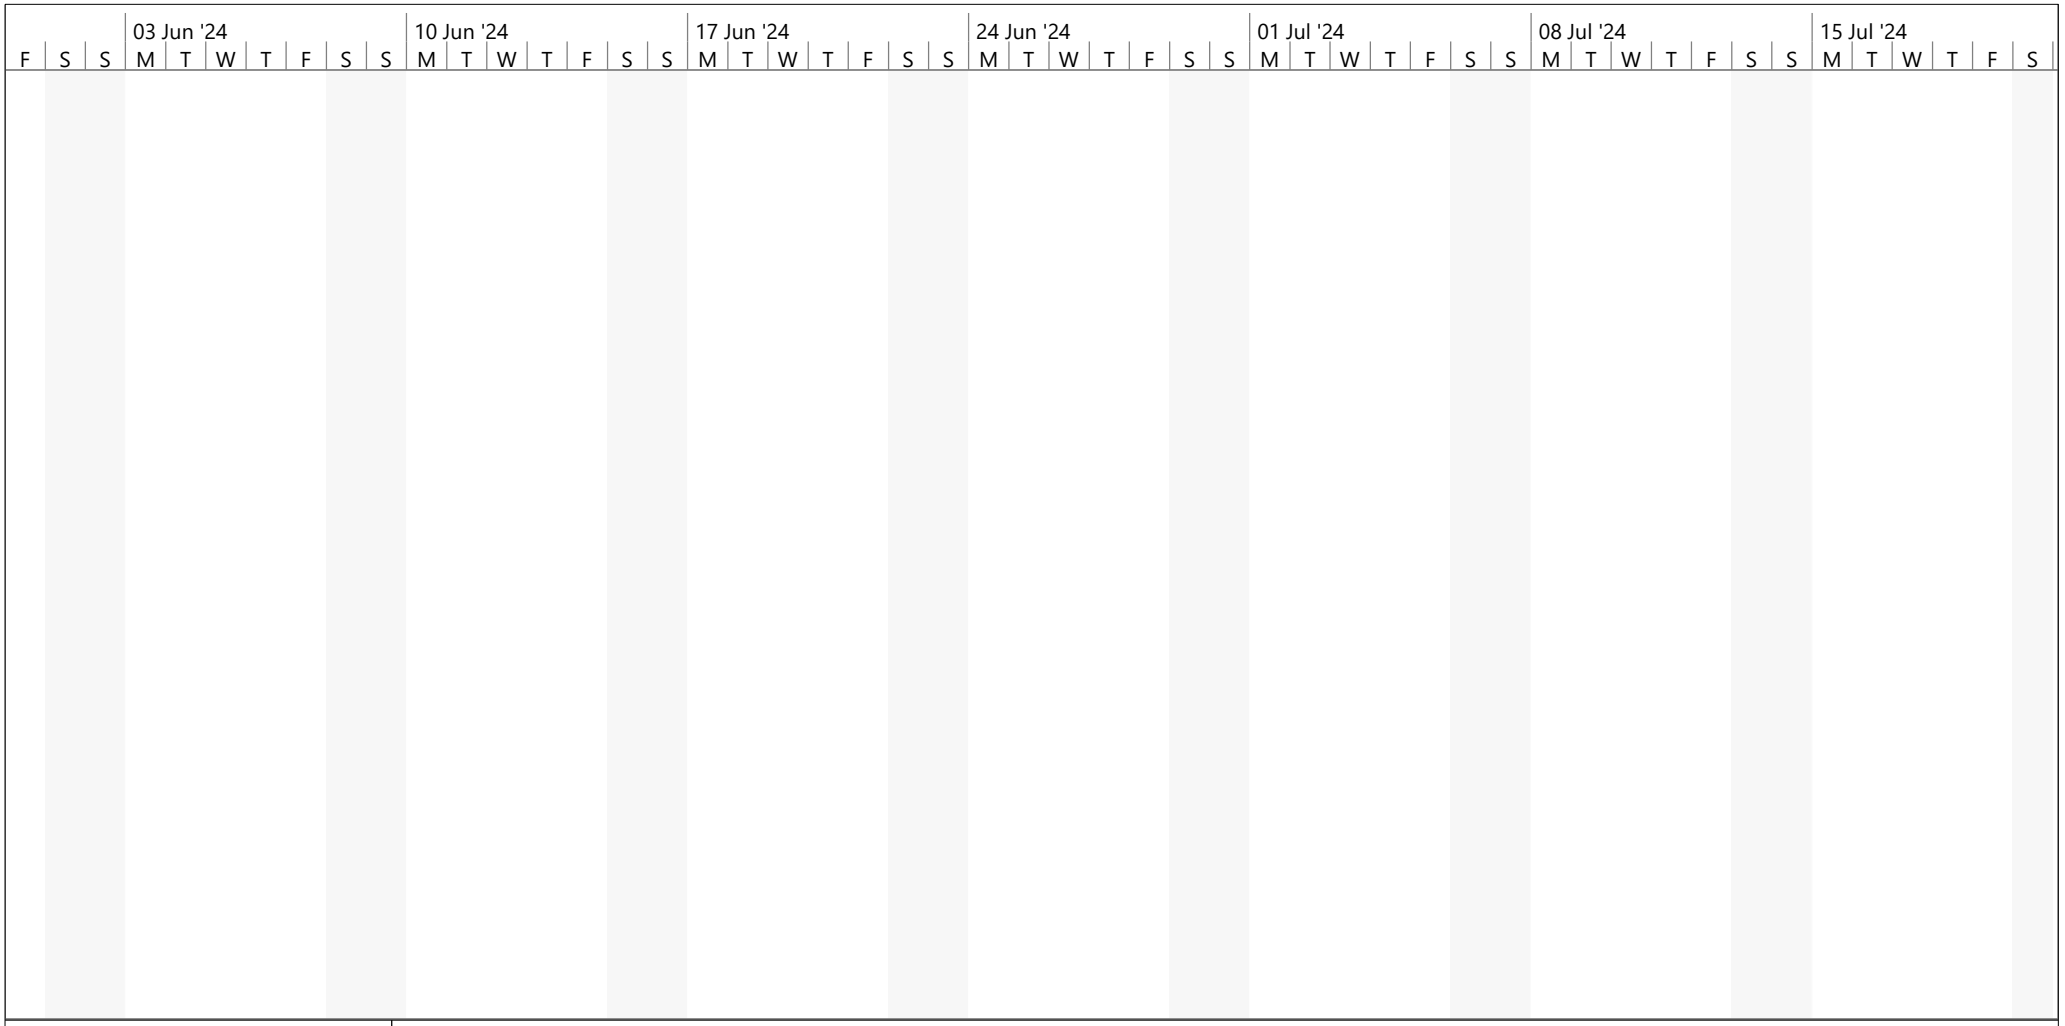


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

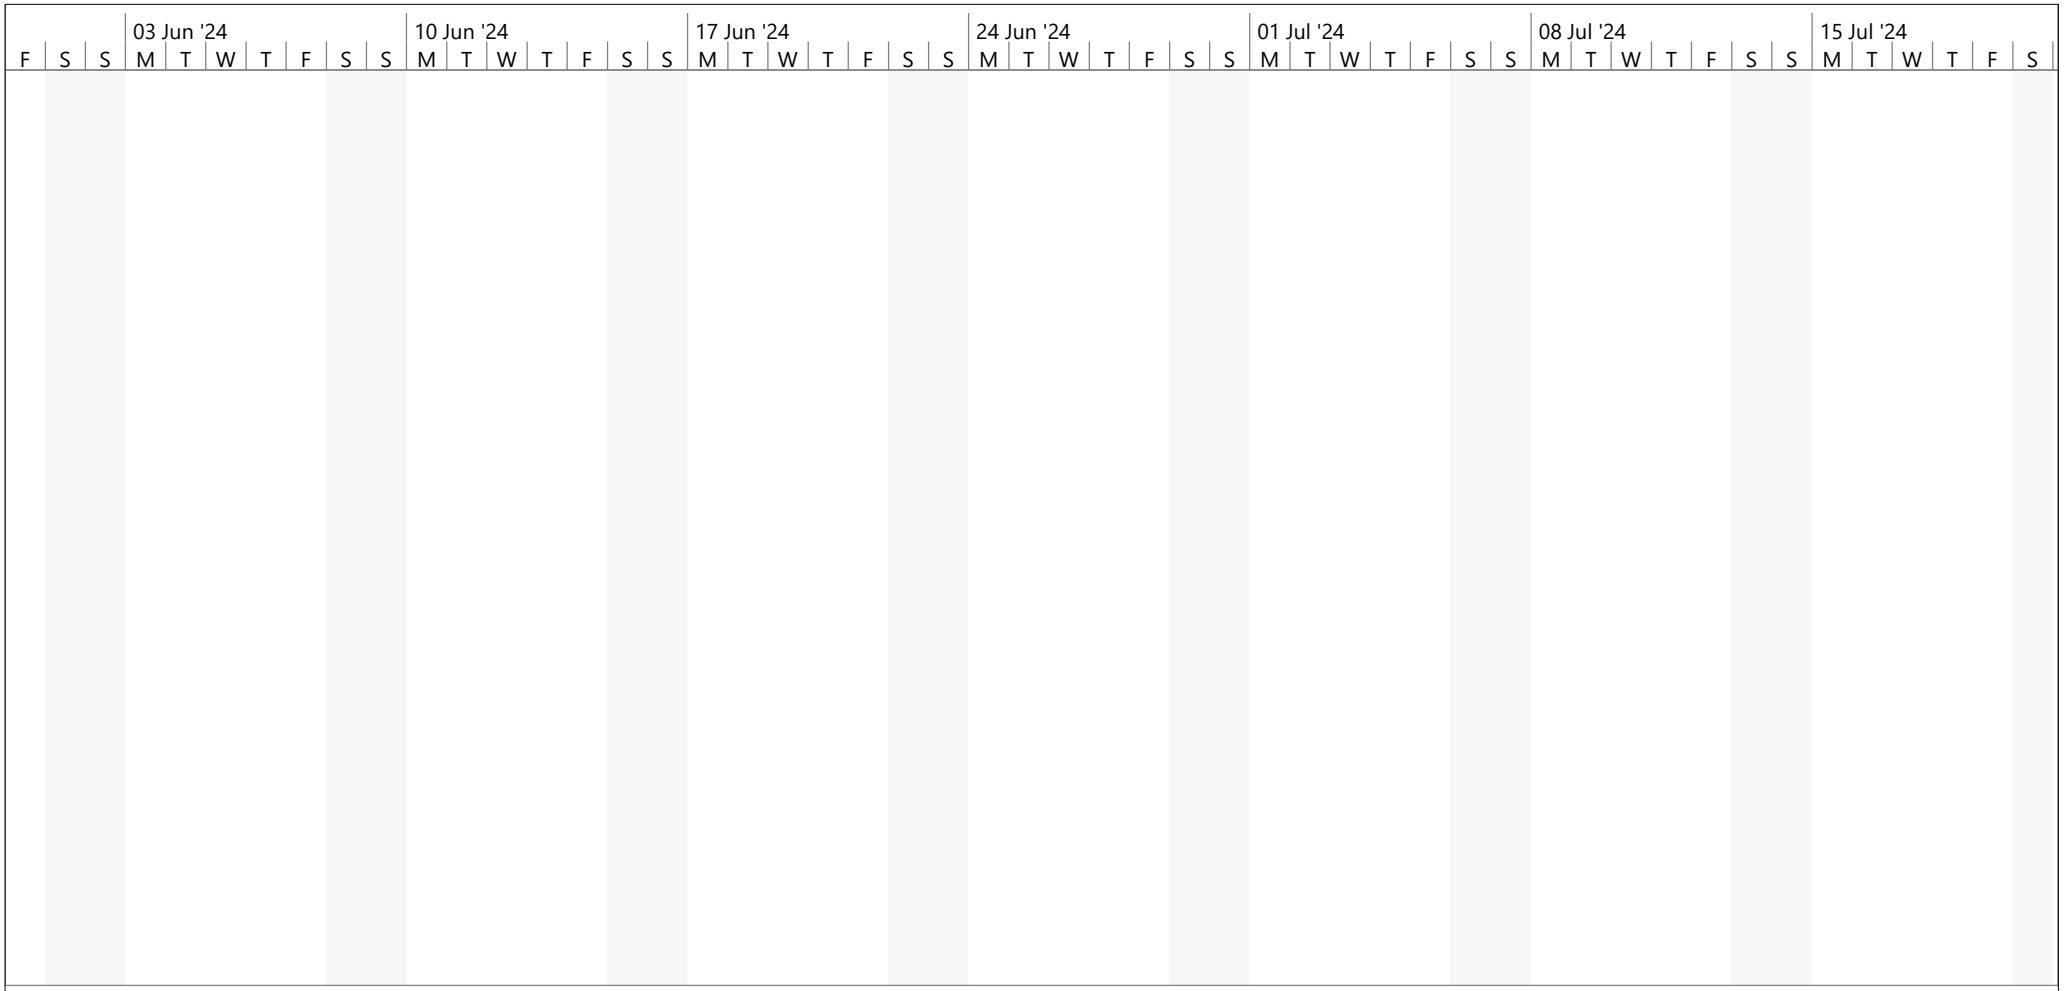


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

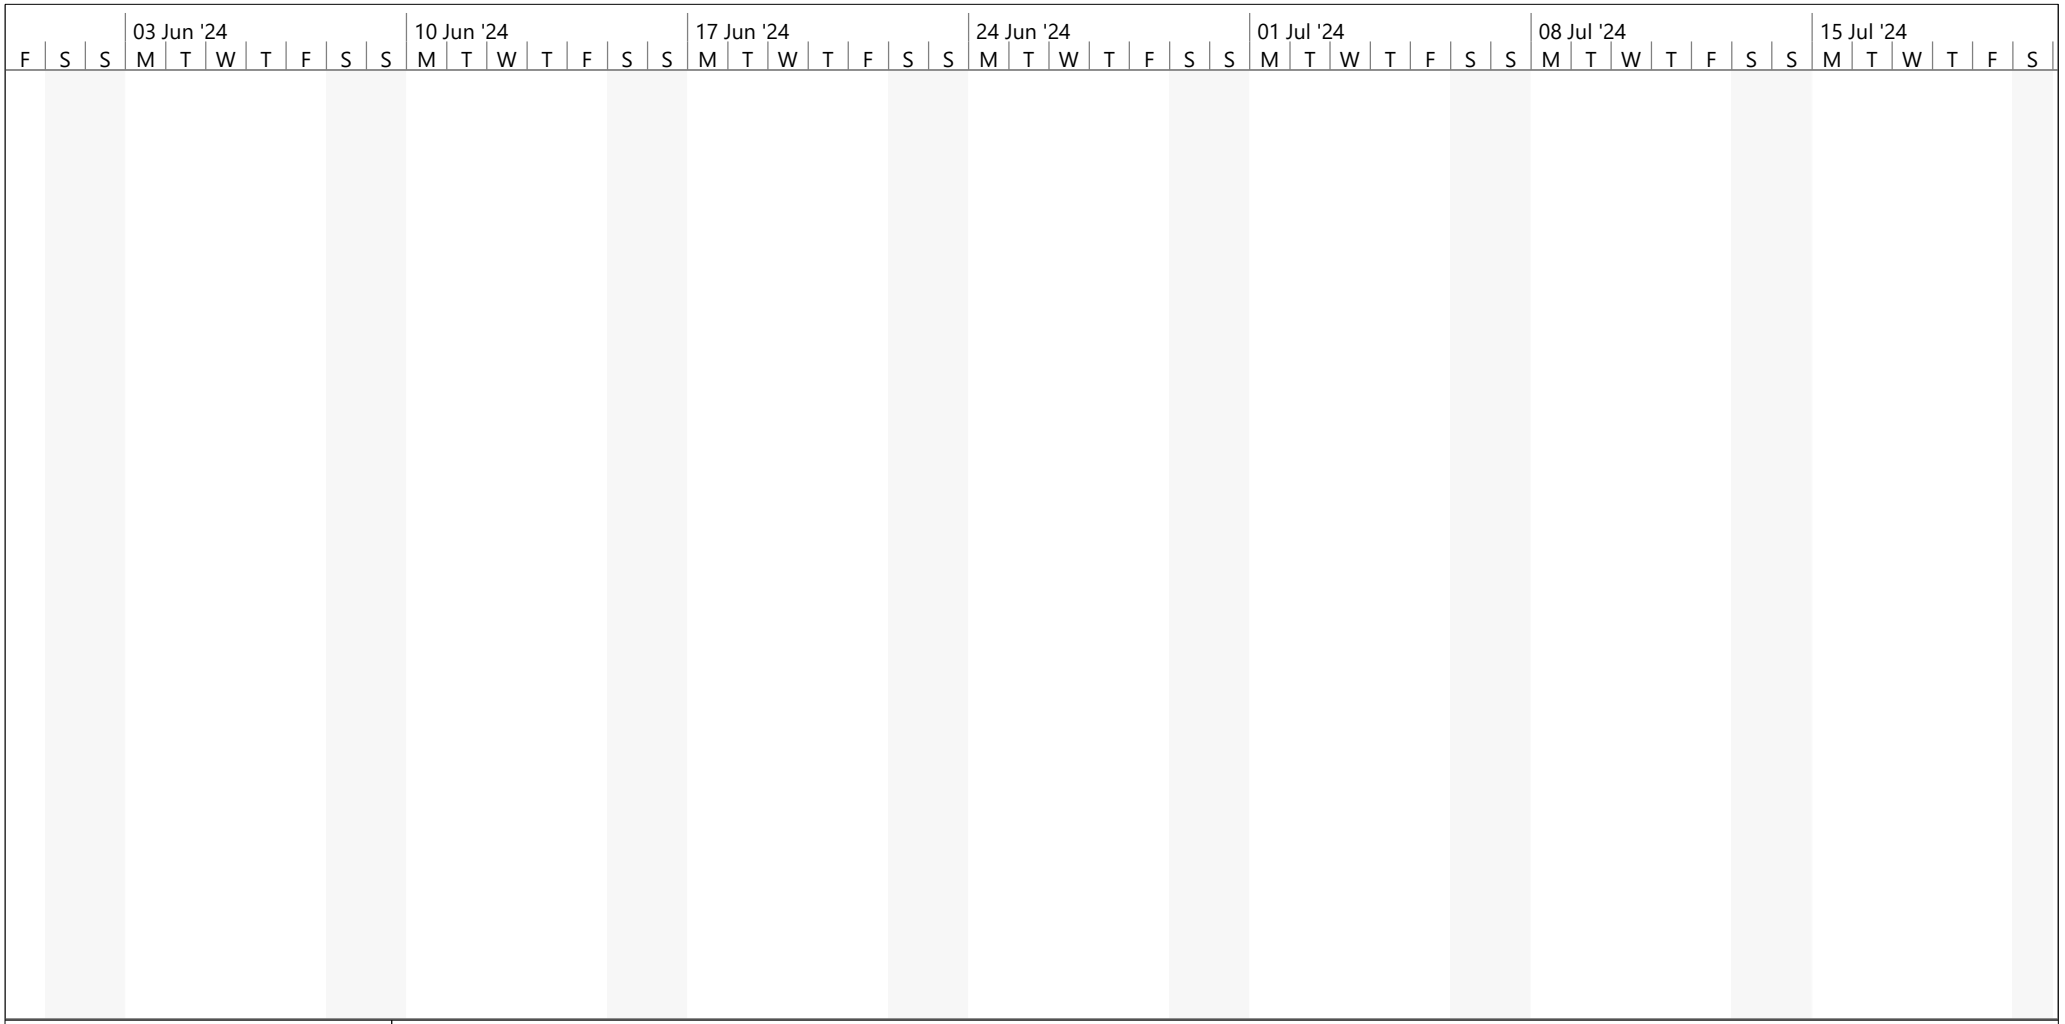


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

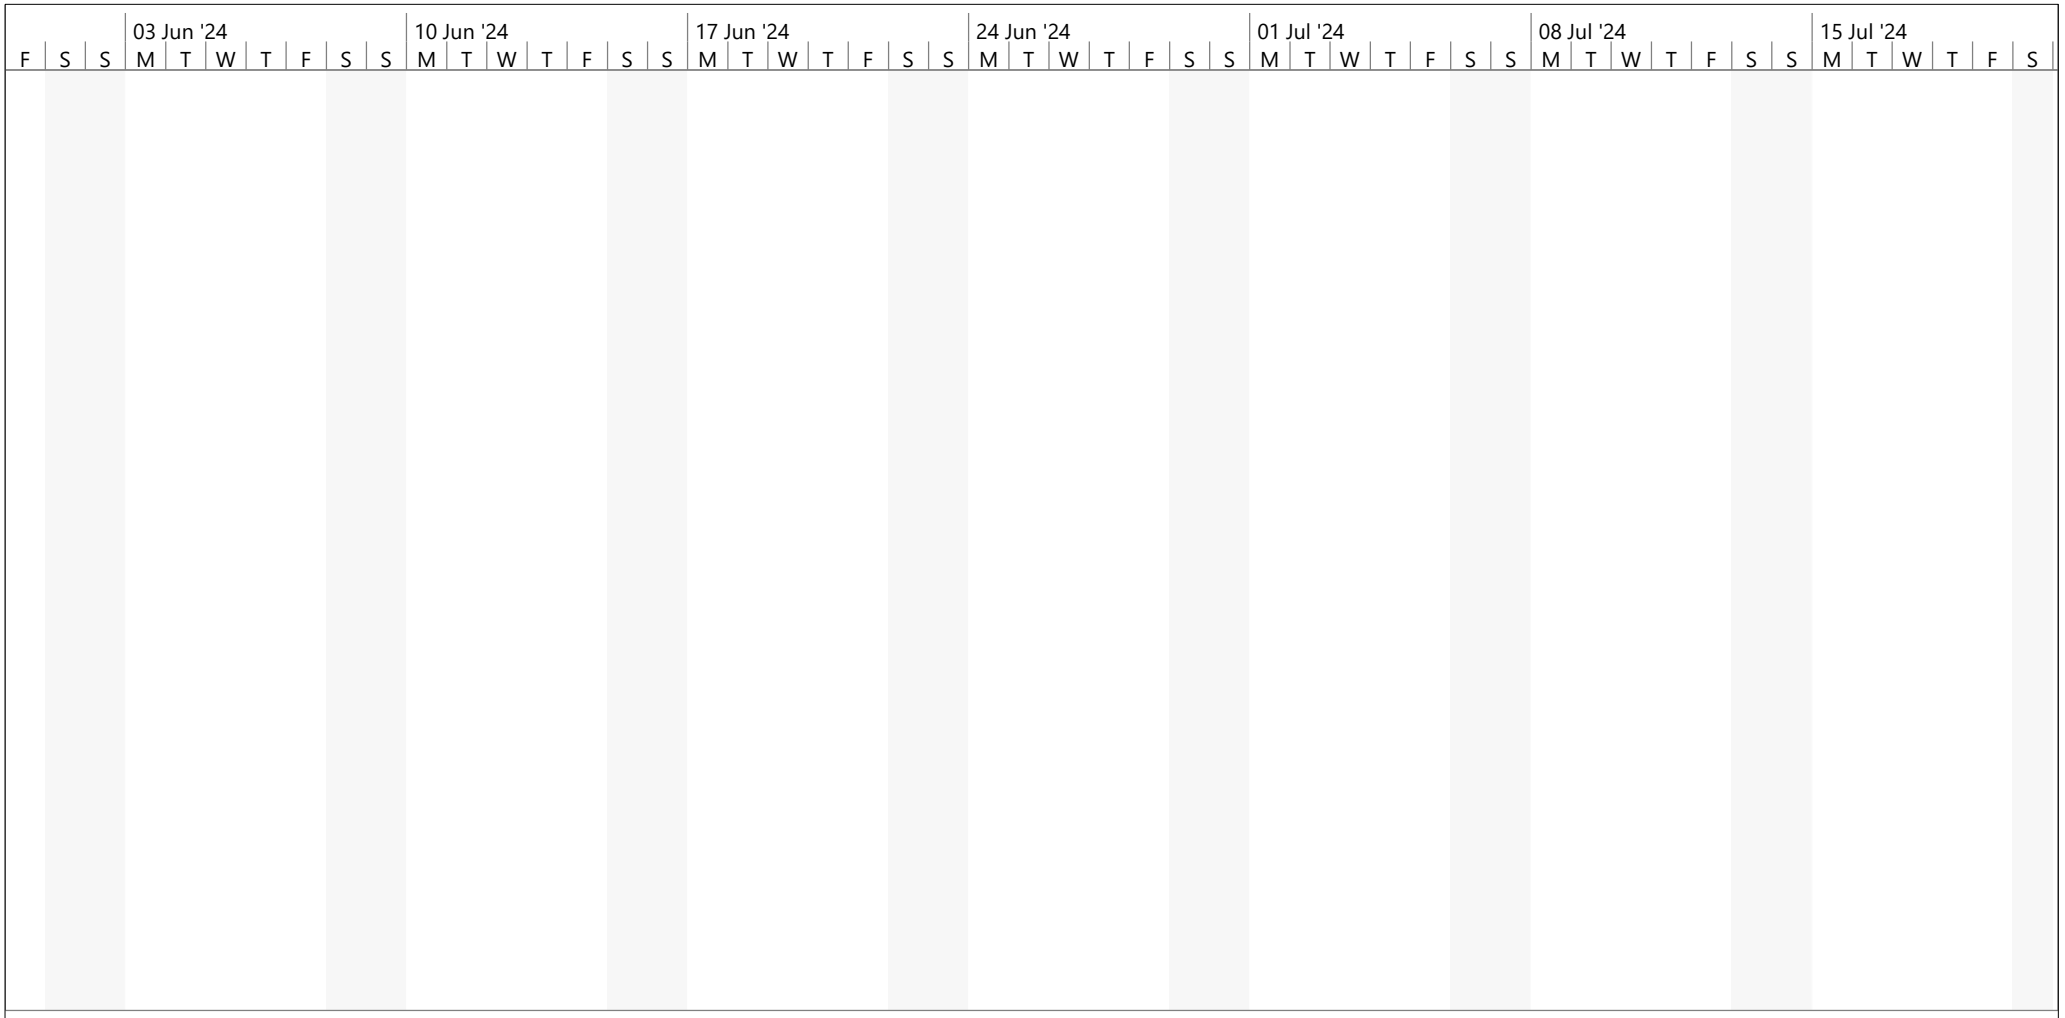


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

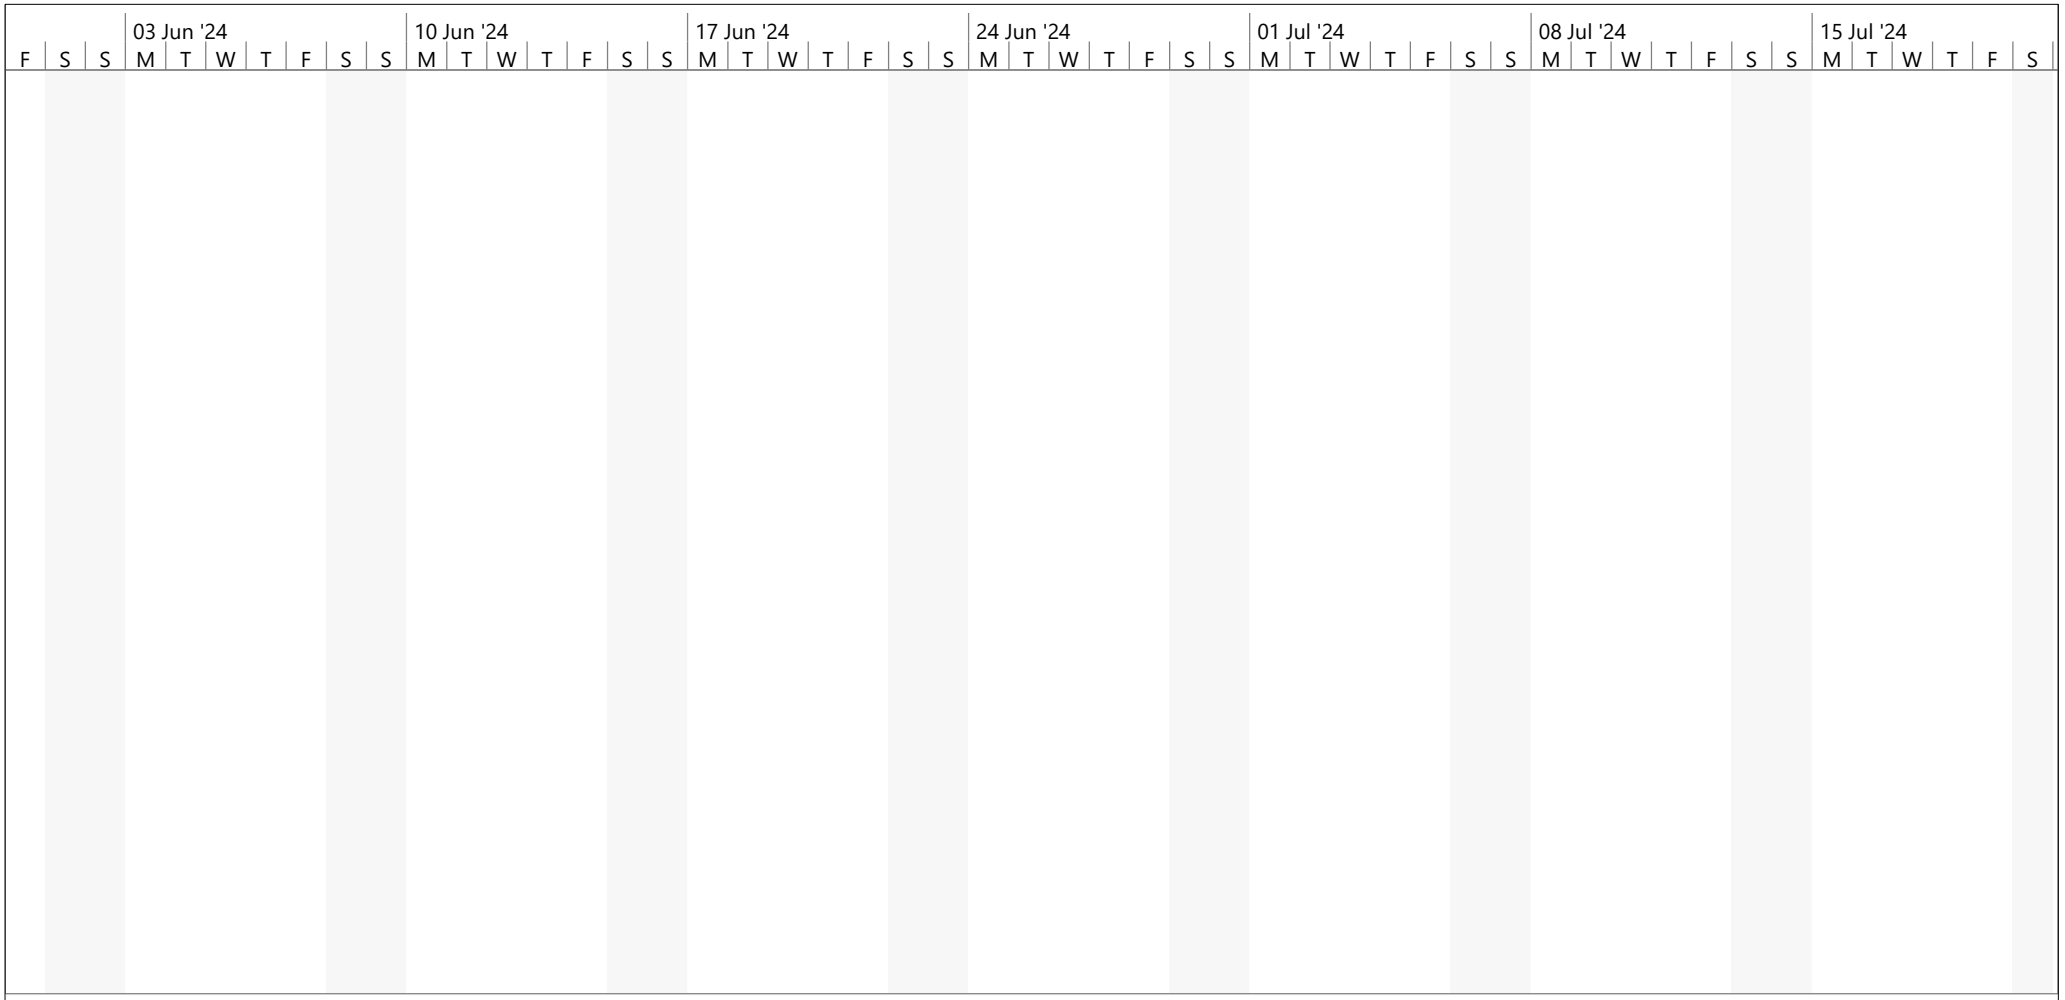


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

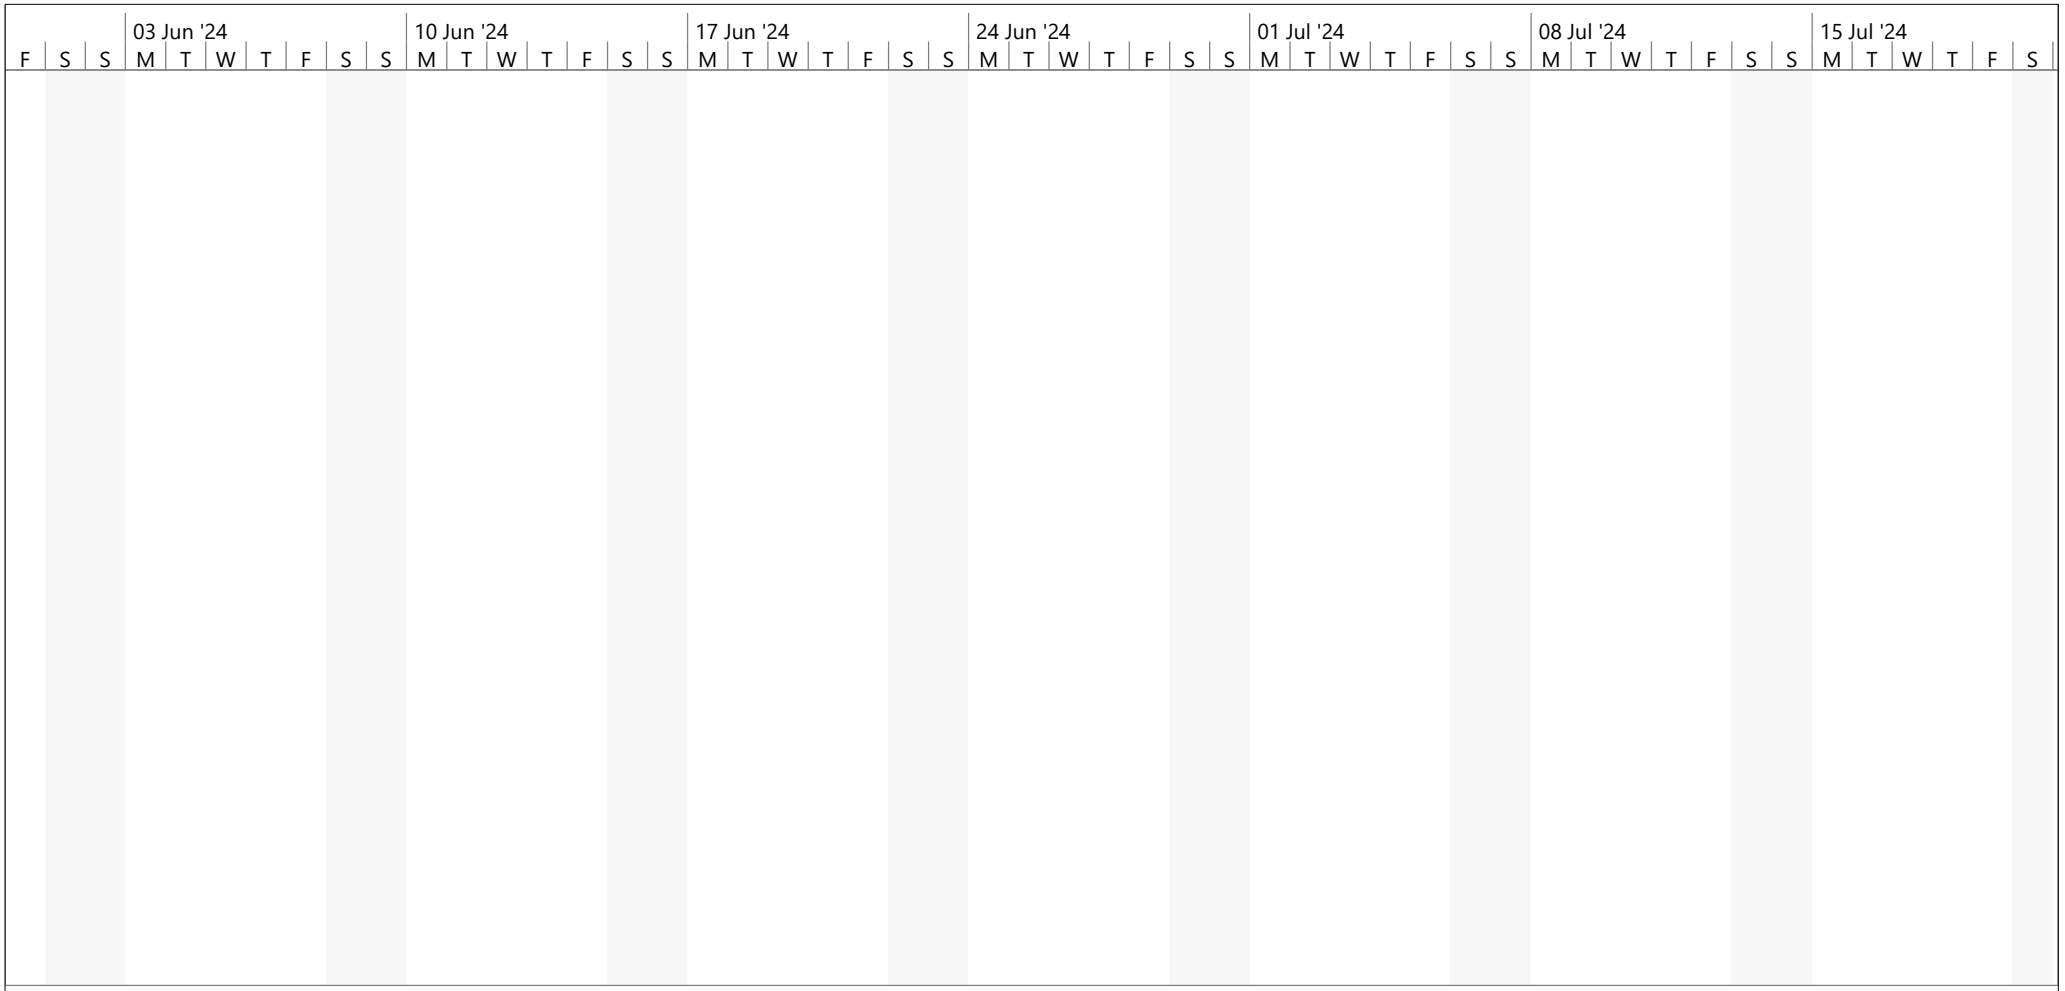

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

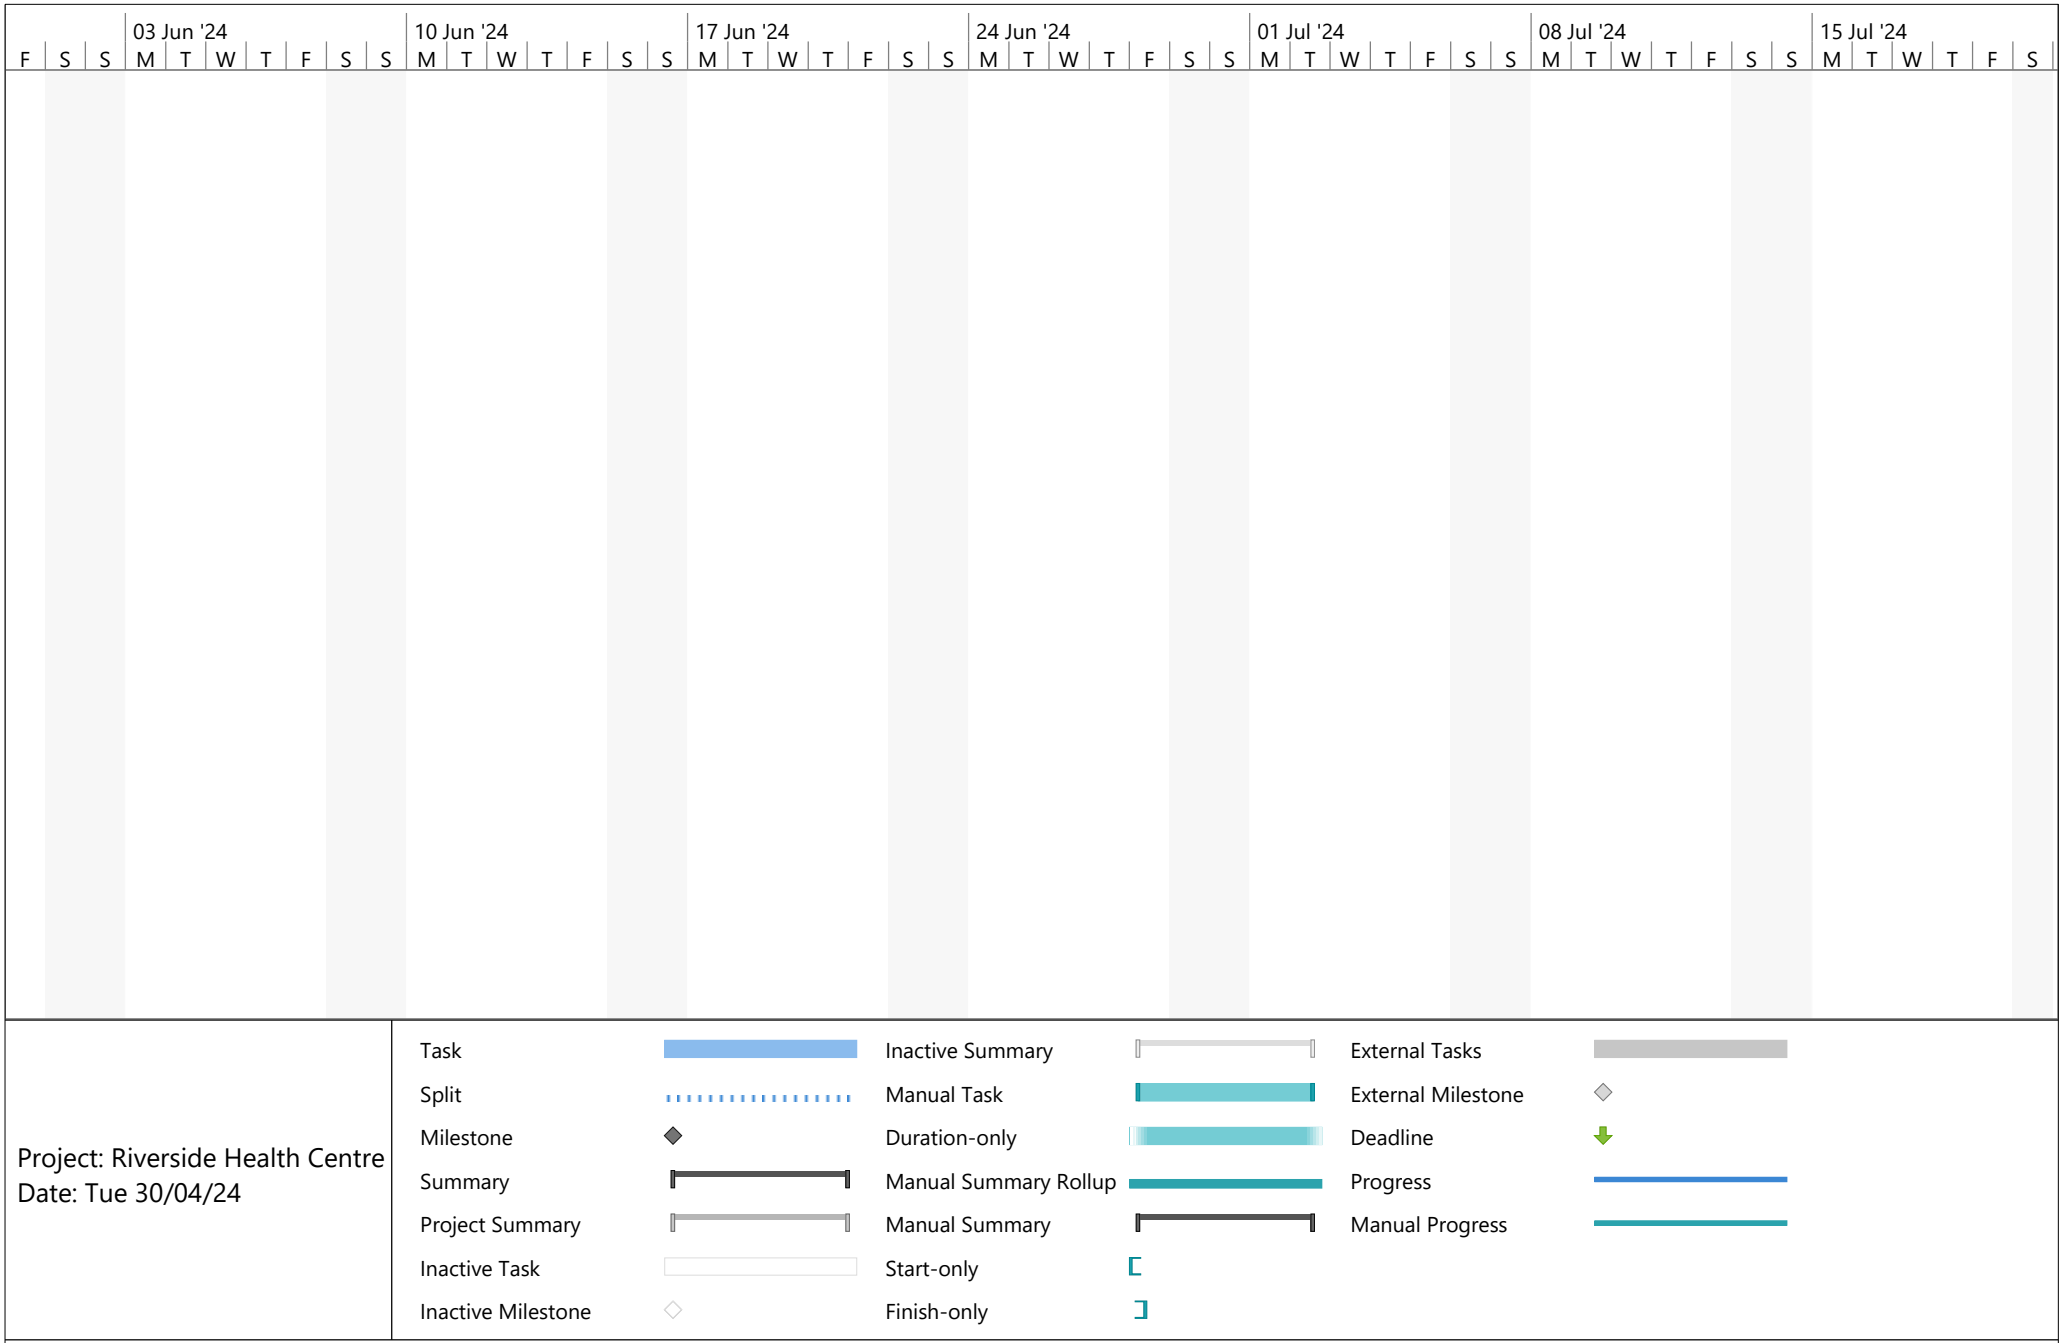
03 Jun '24
10 Jun '24
17 Jun '24
24 Jun '24
01 Jul '24
08 Jul '24
15 Jul '24
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

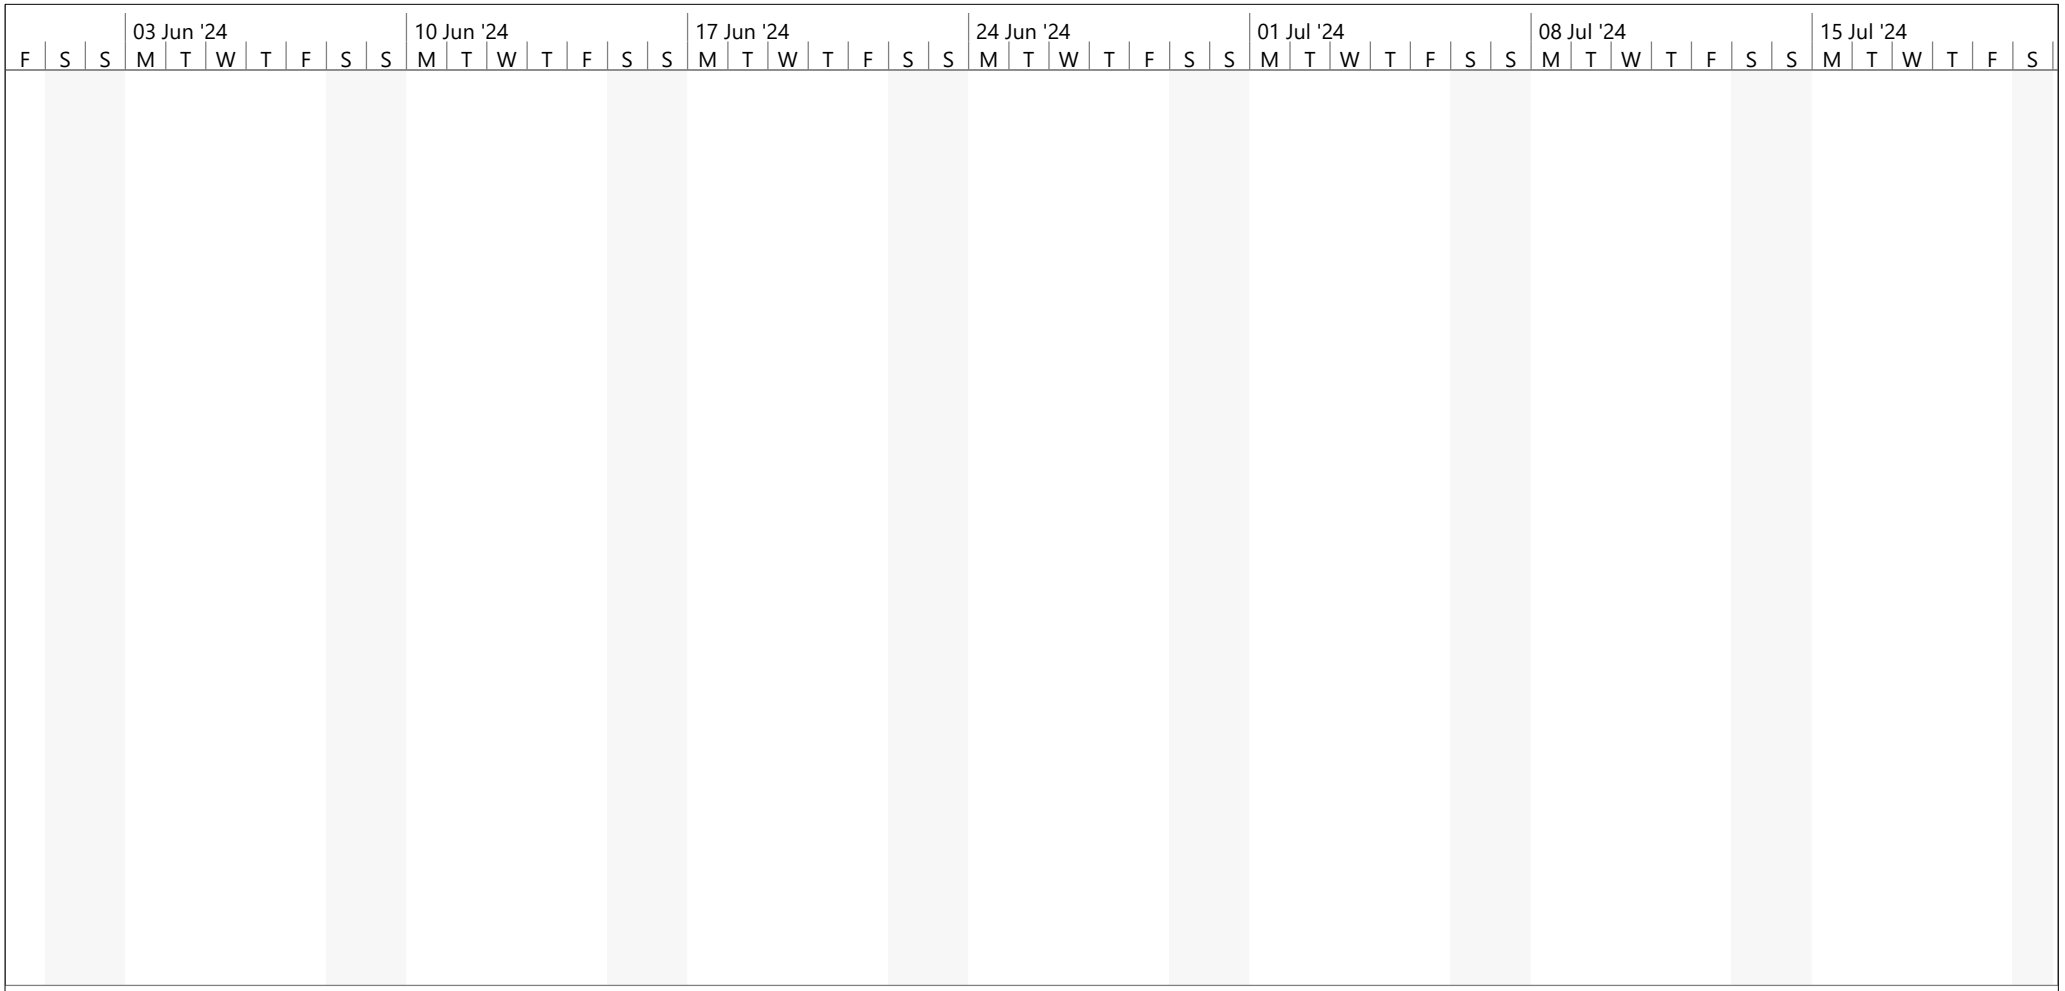


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

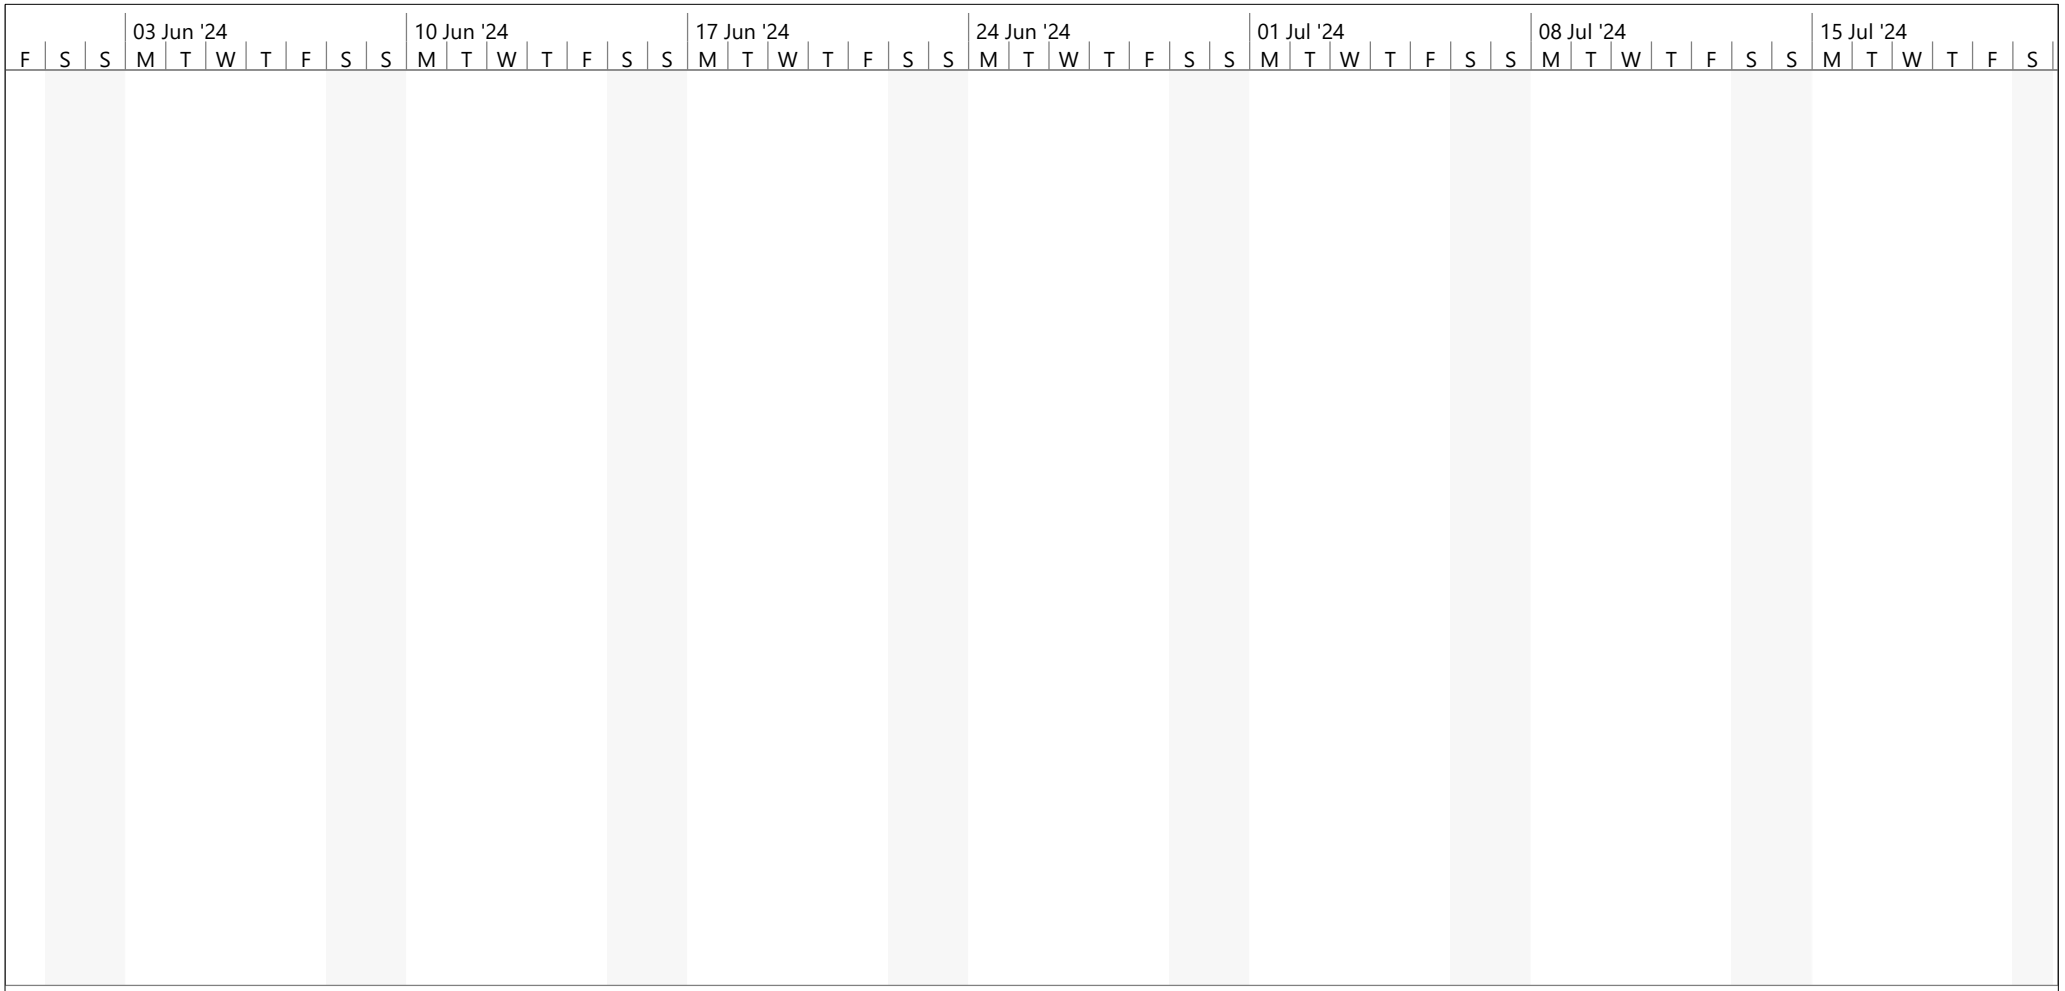


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

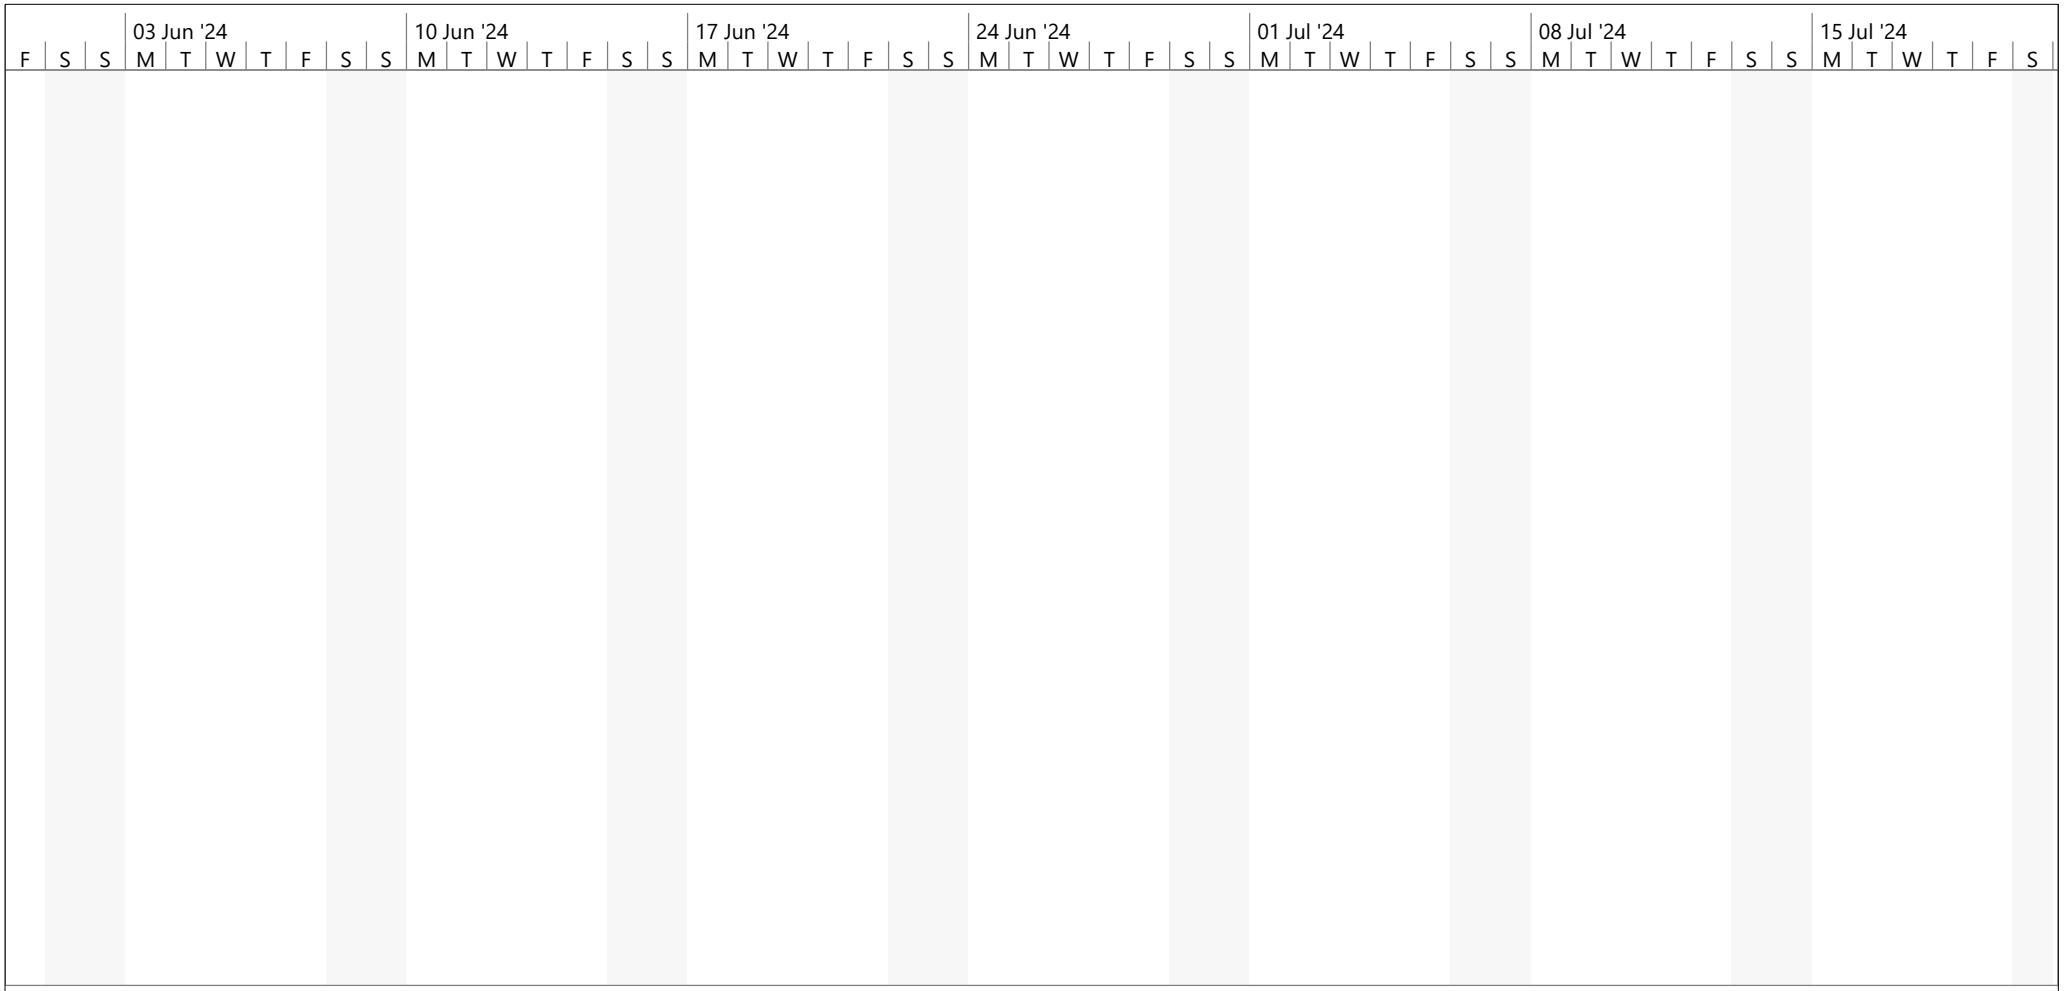


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

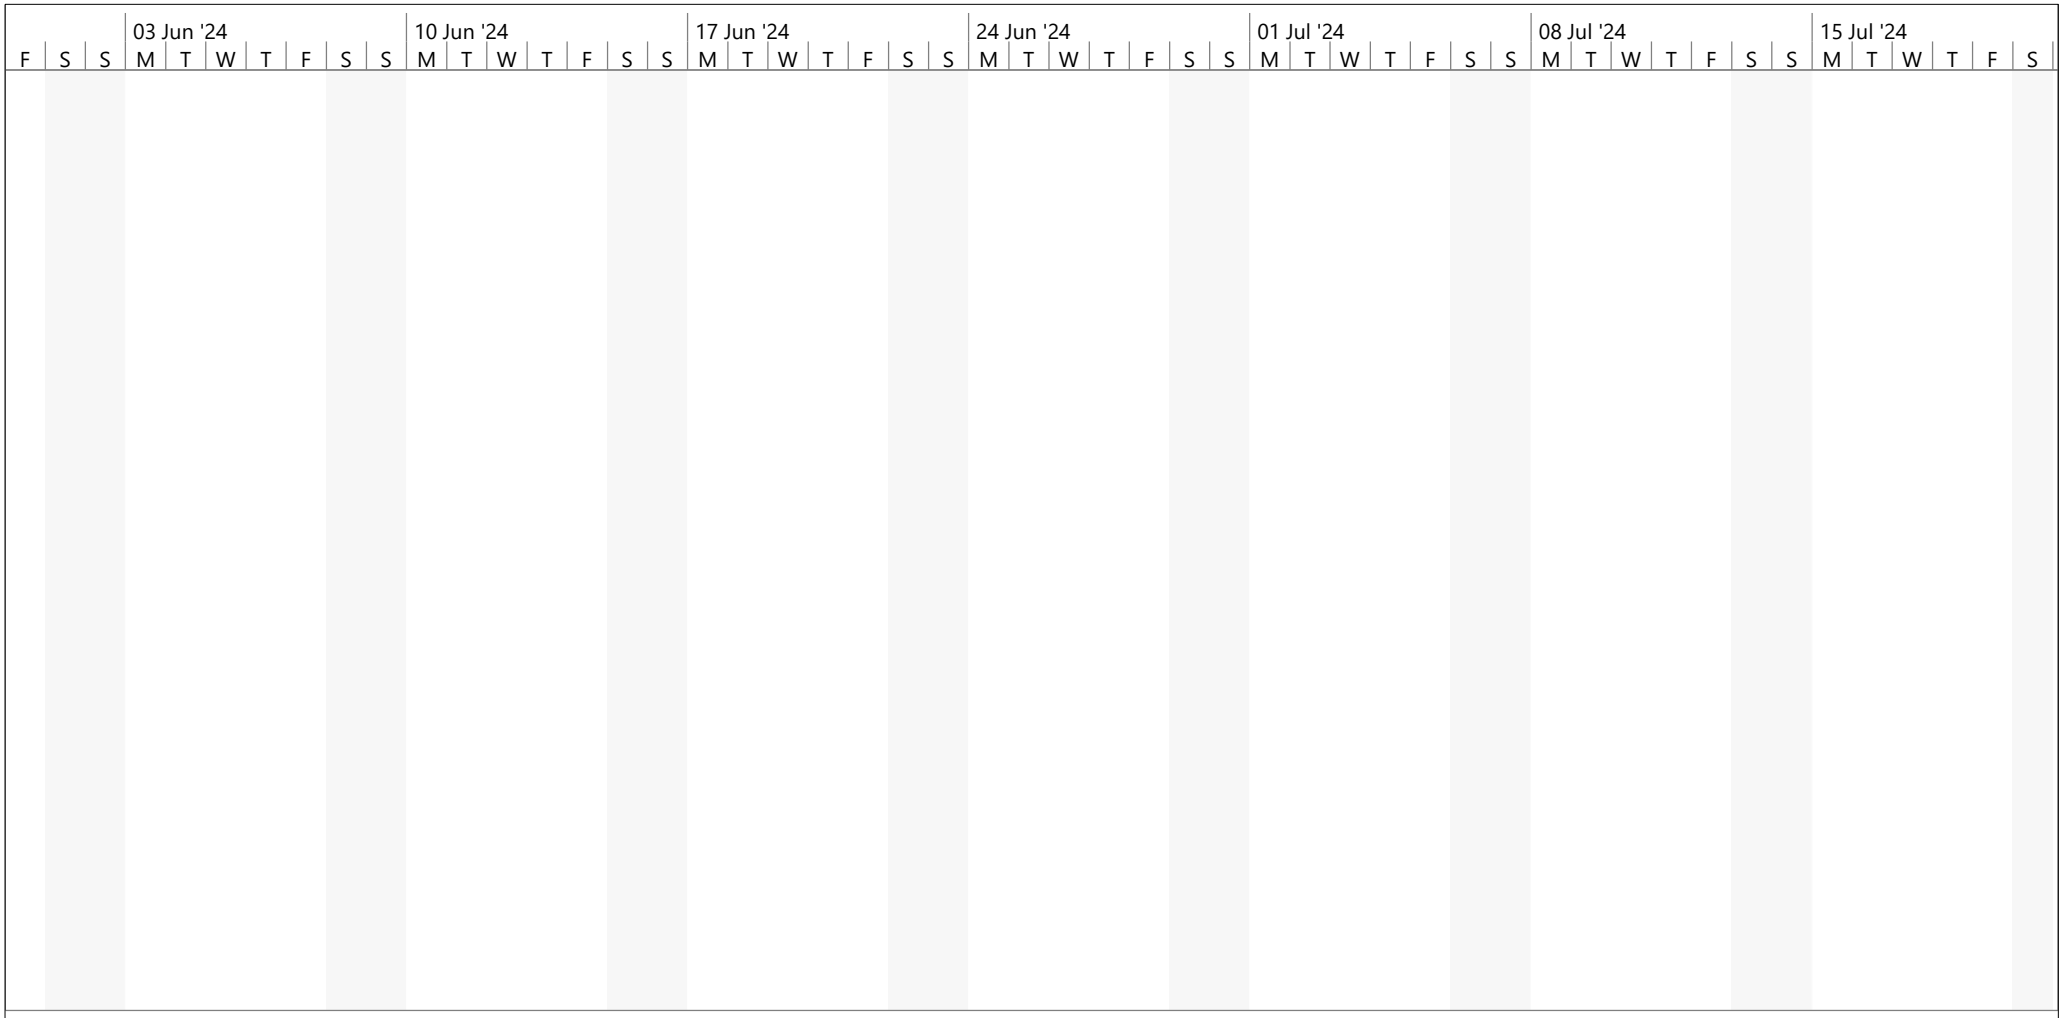

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

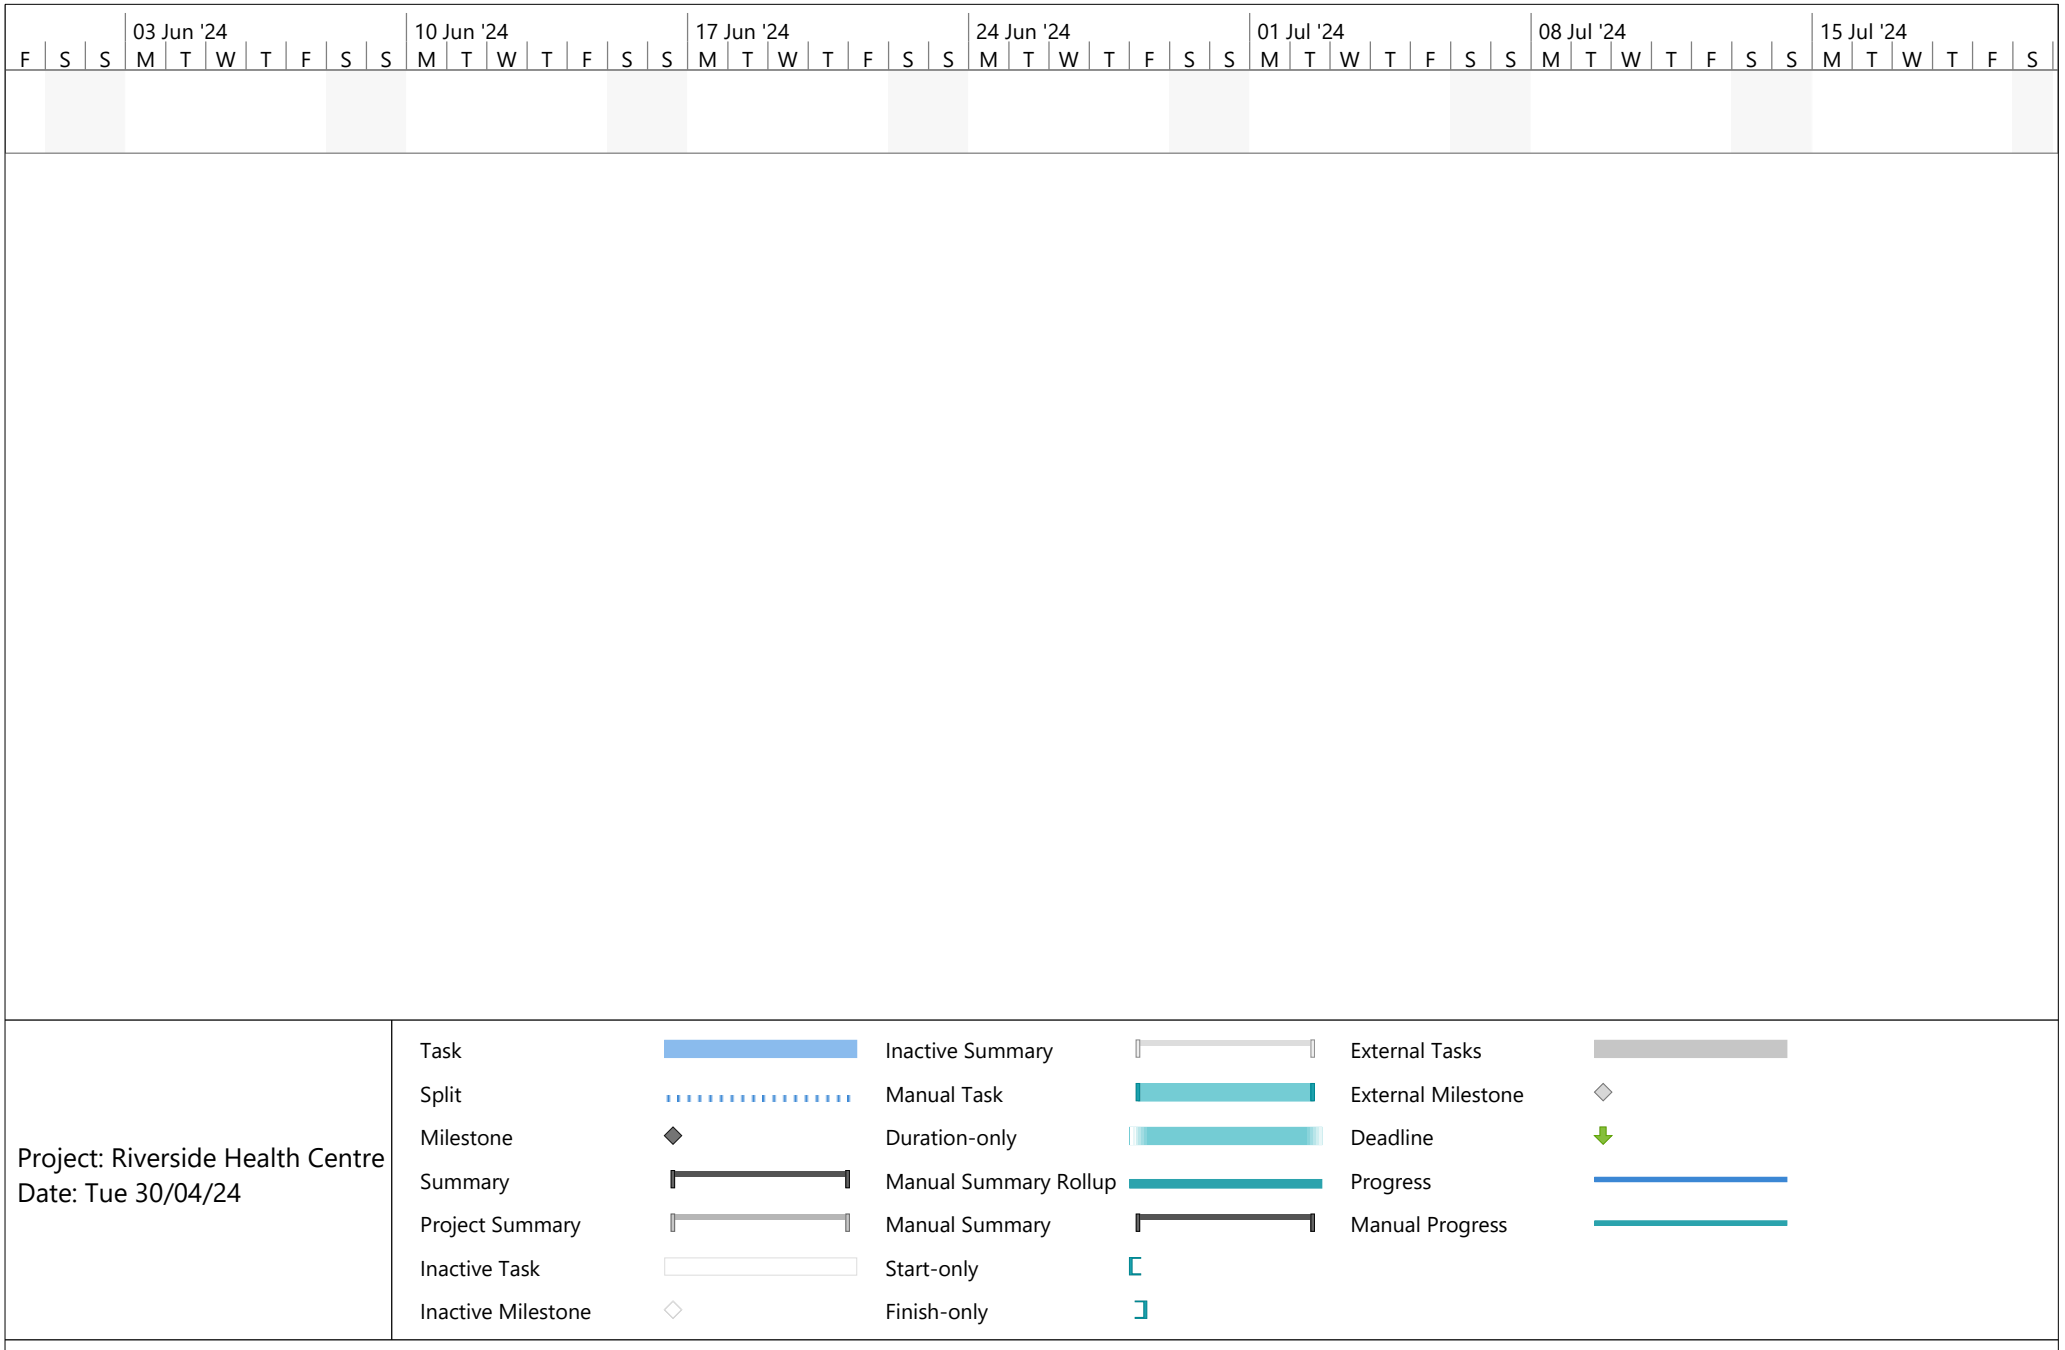
03 Jun '24
10 Jun '24
17 Jun '24
24 Jun '24
01 Jul '24
08 Jul '24
15 Jul '24
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

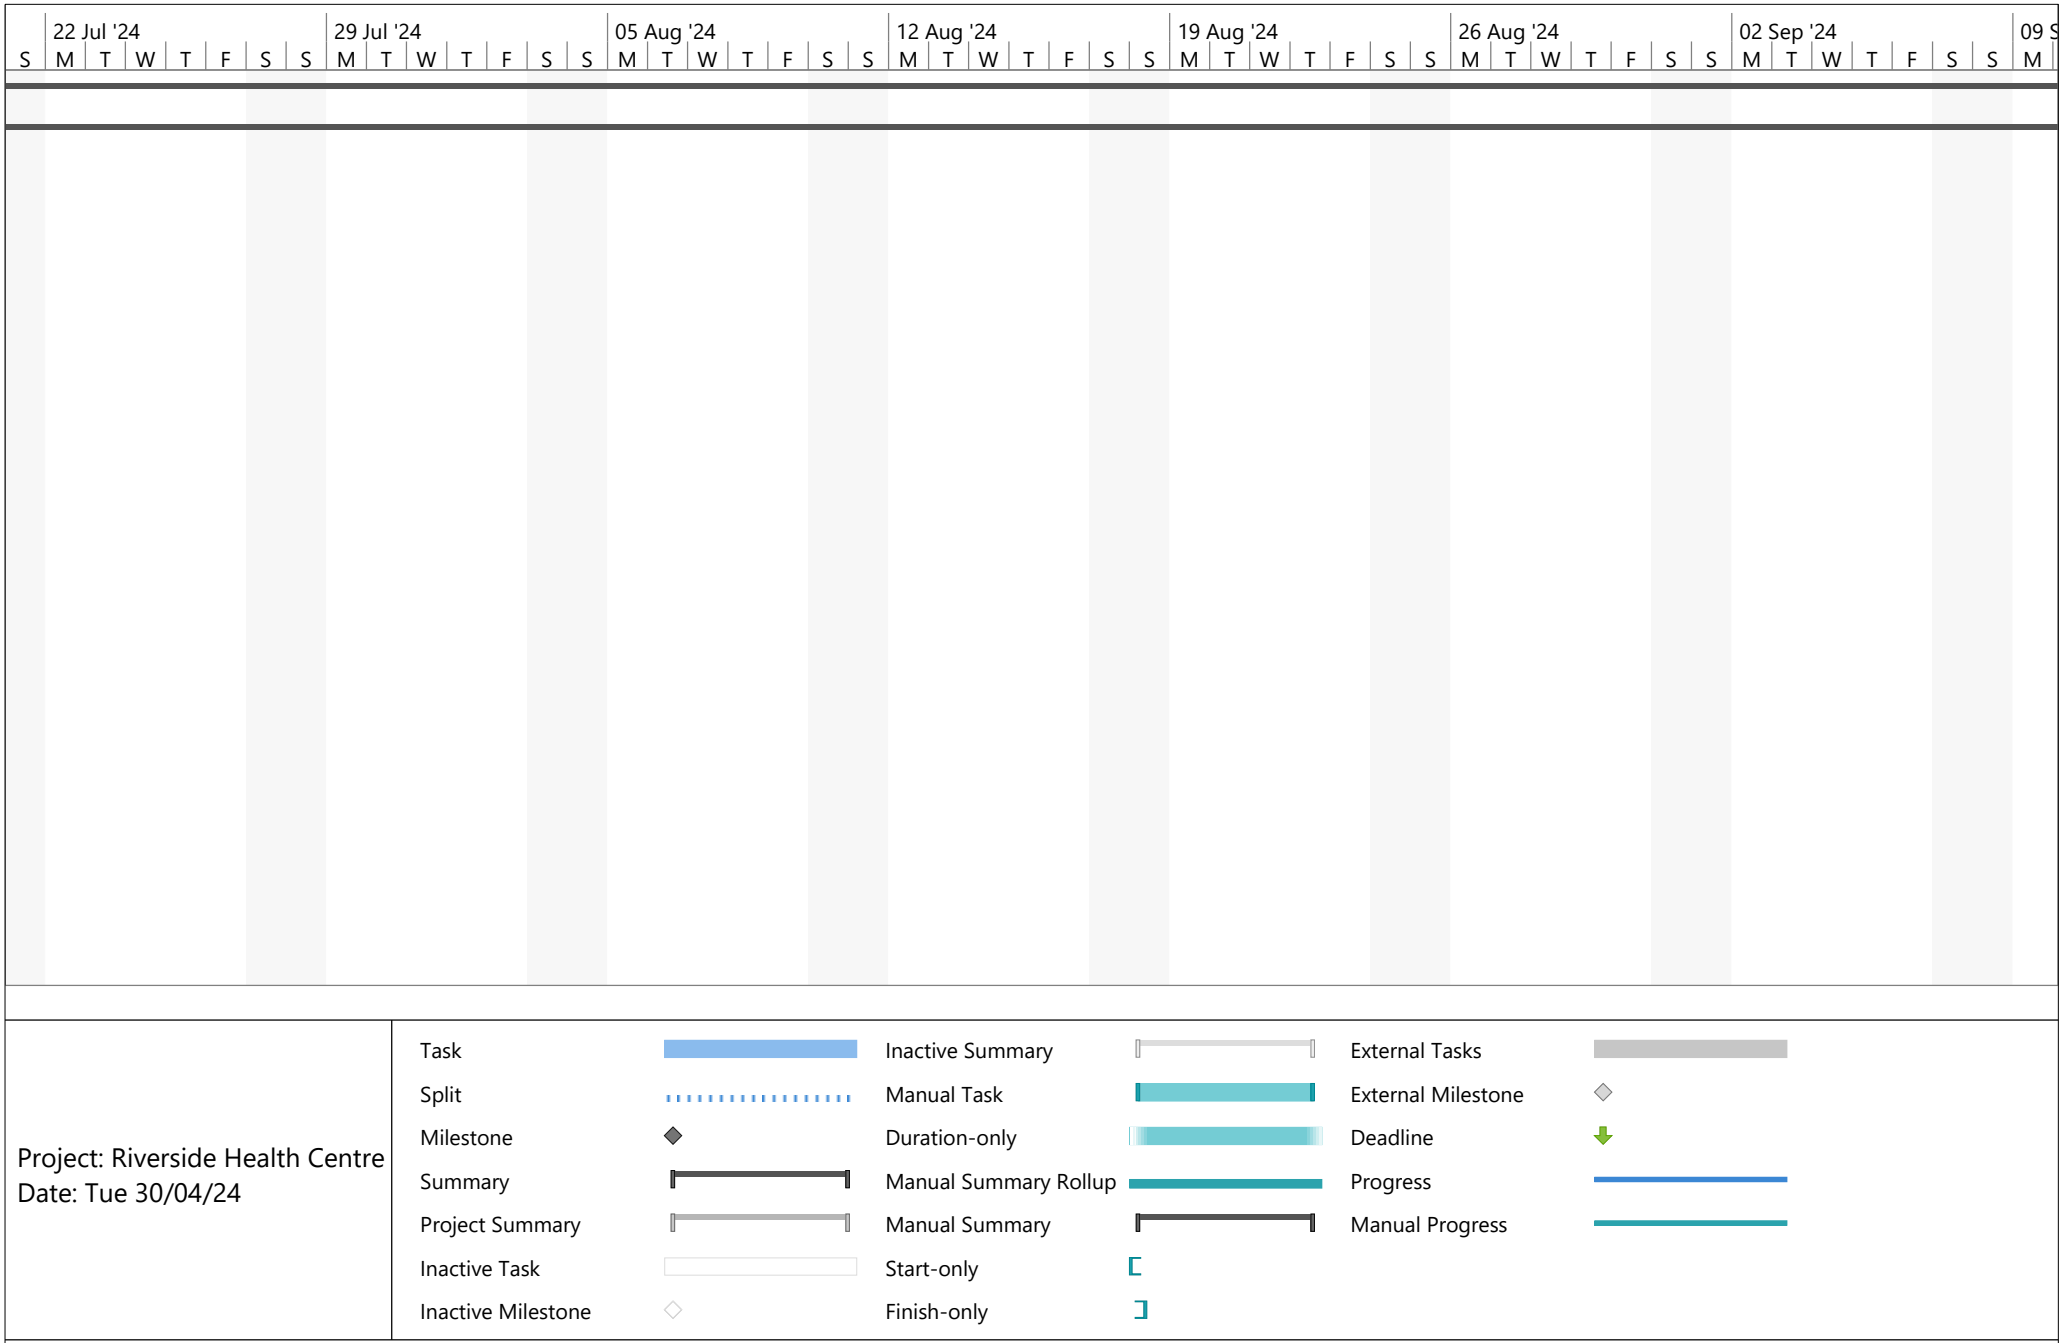


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

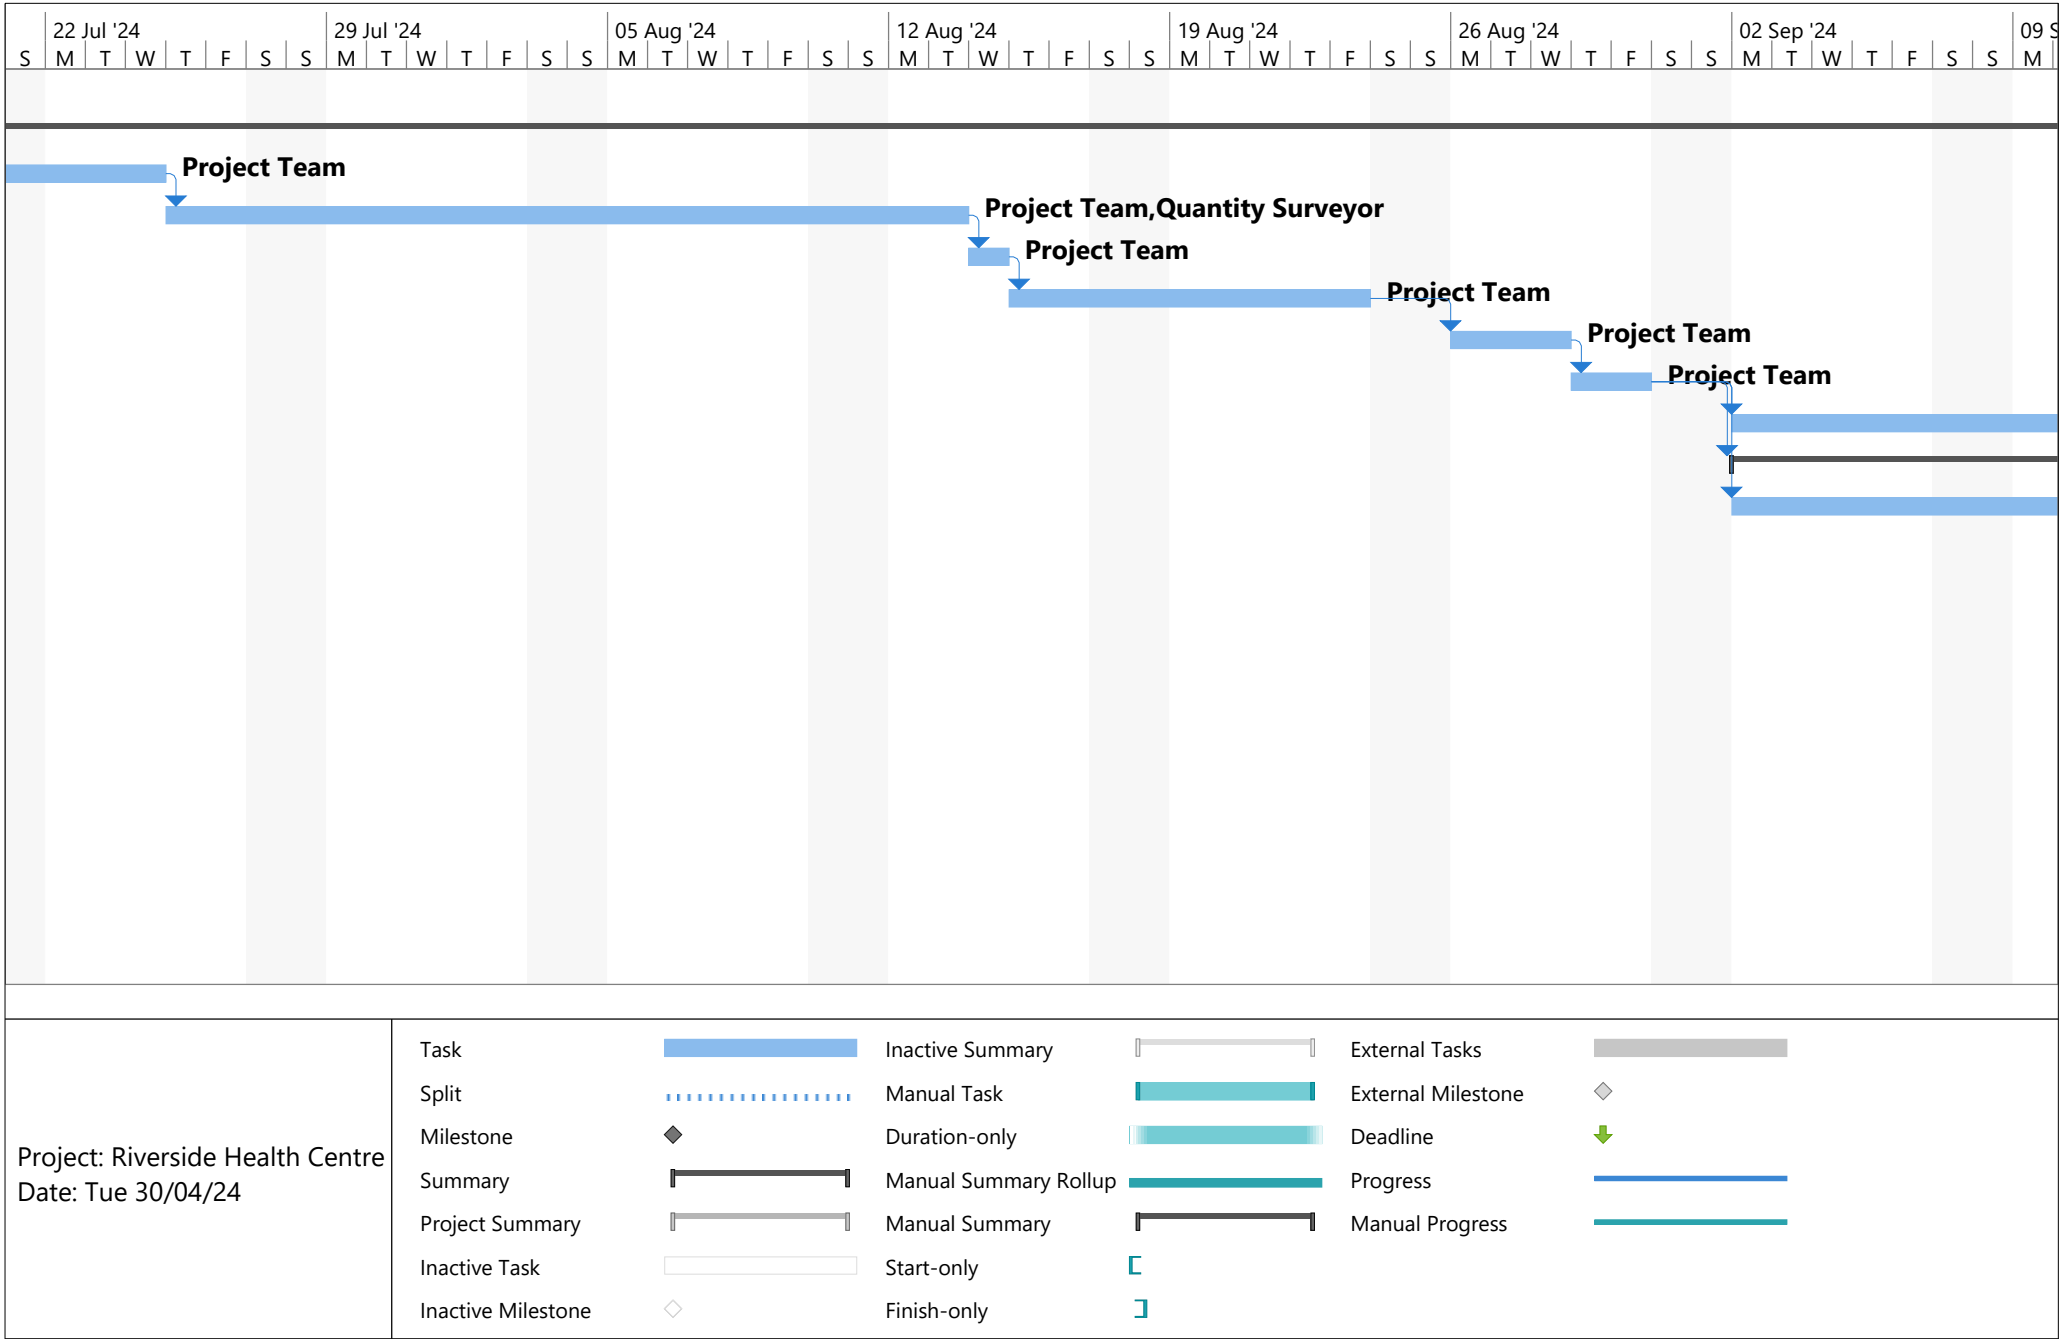


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

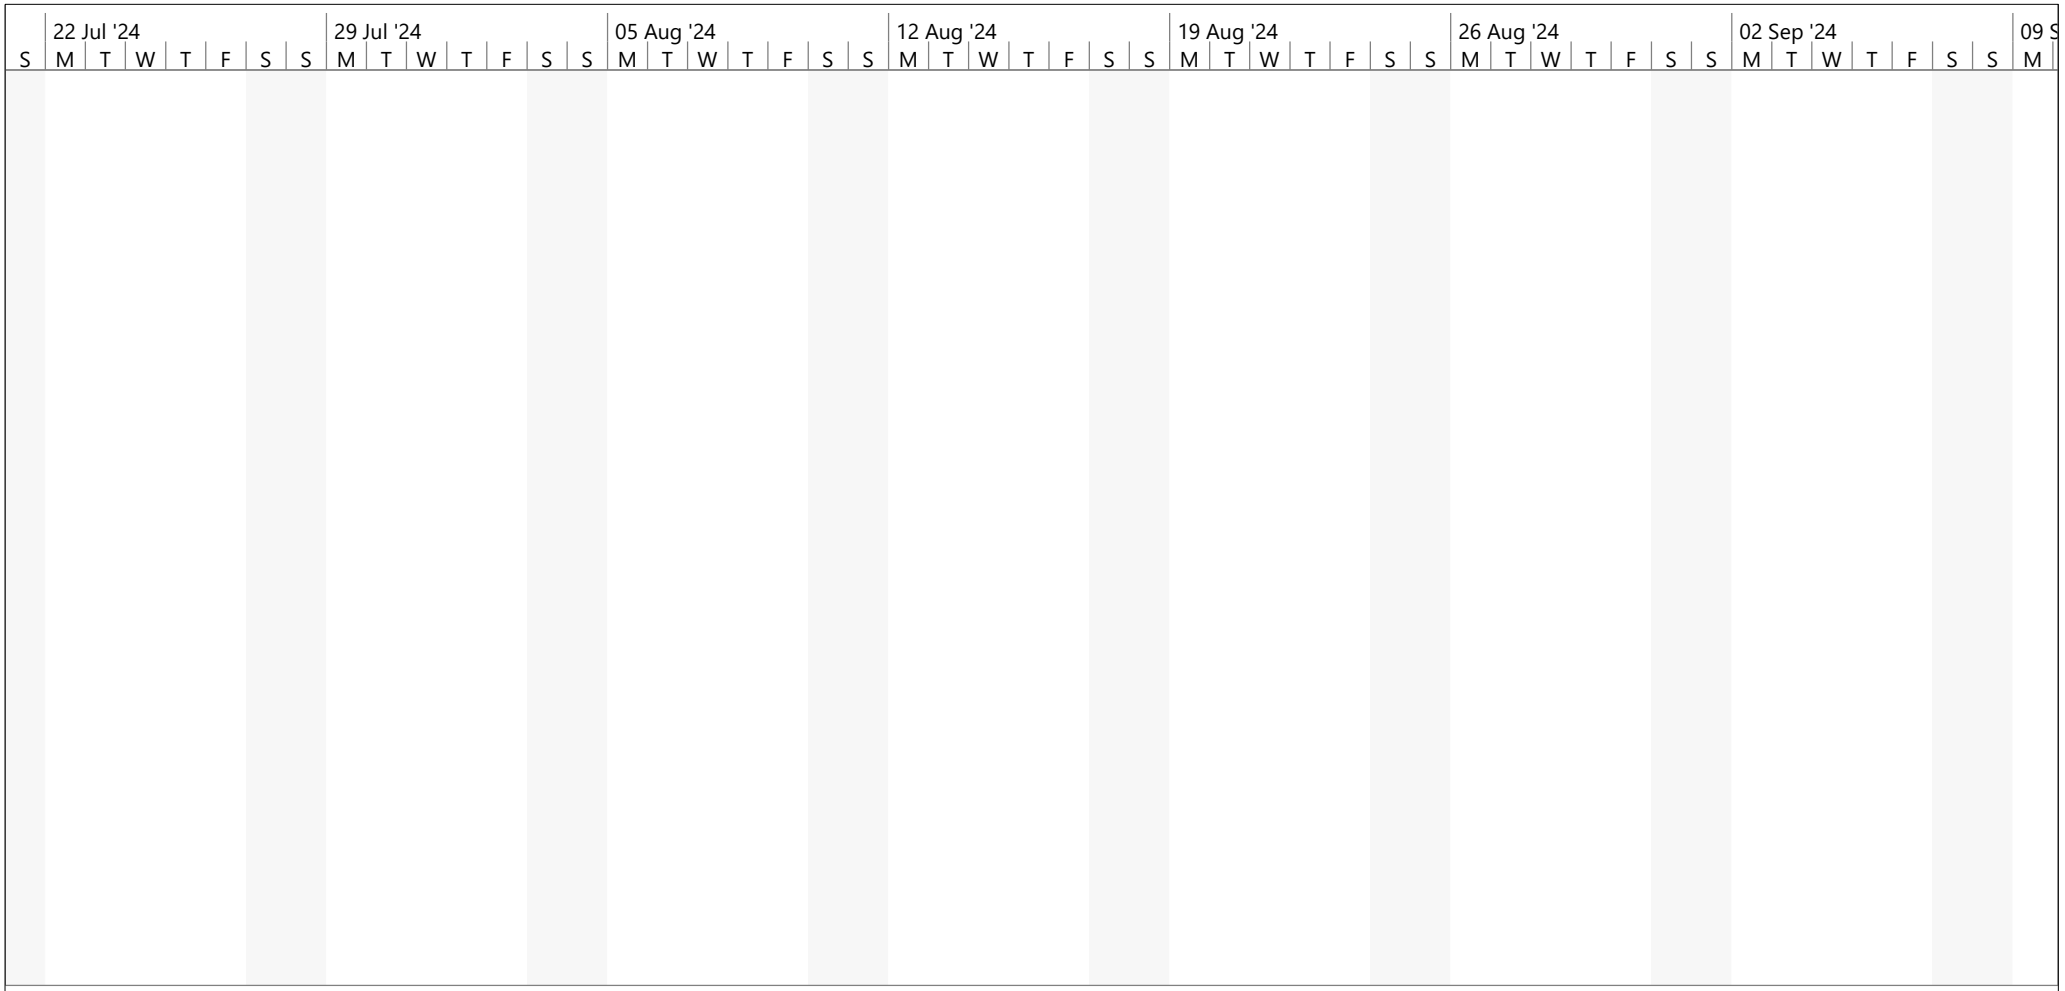


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

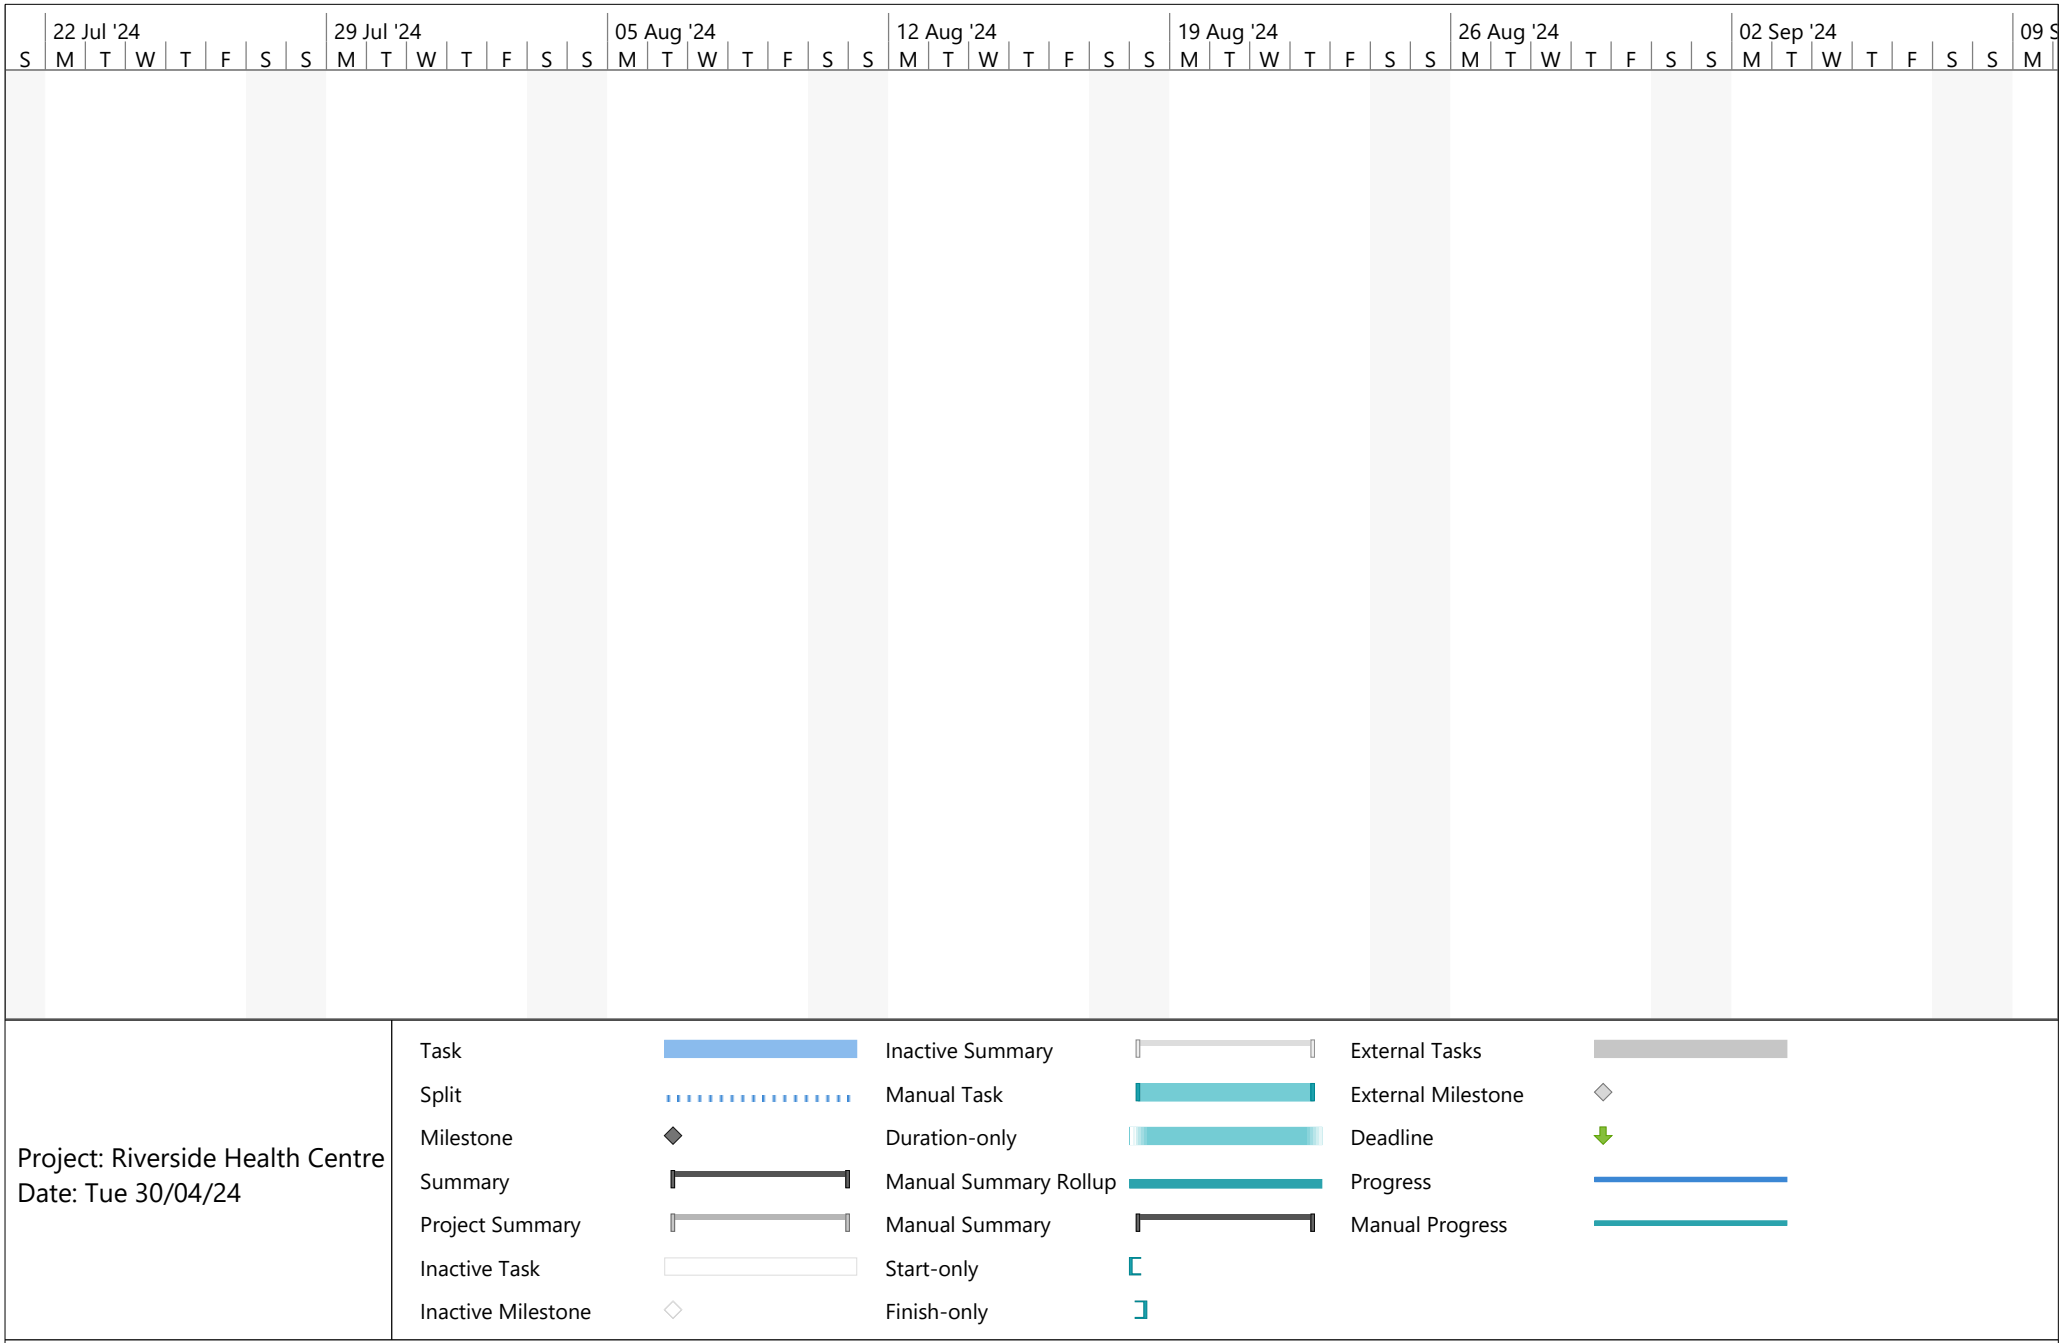


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

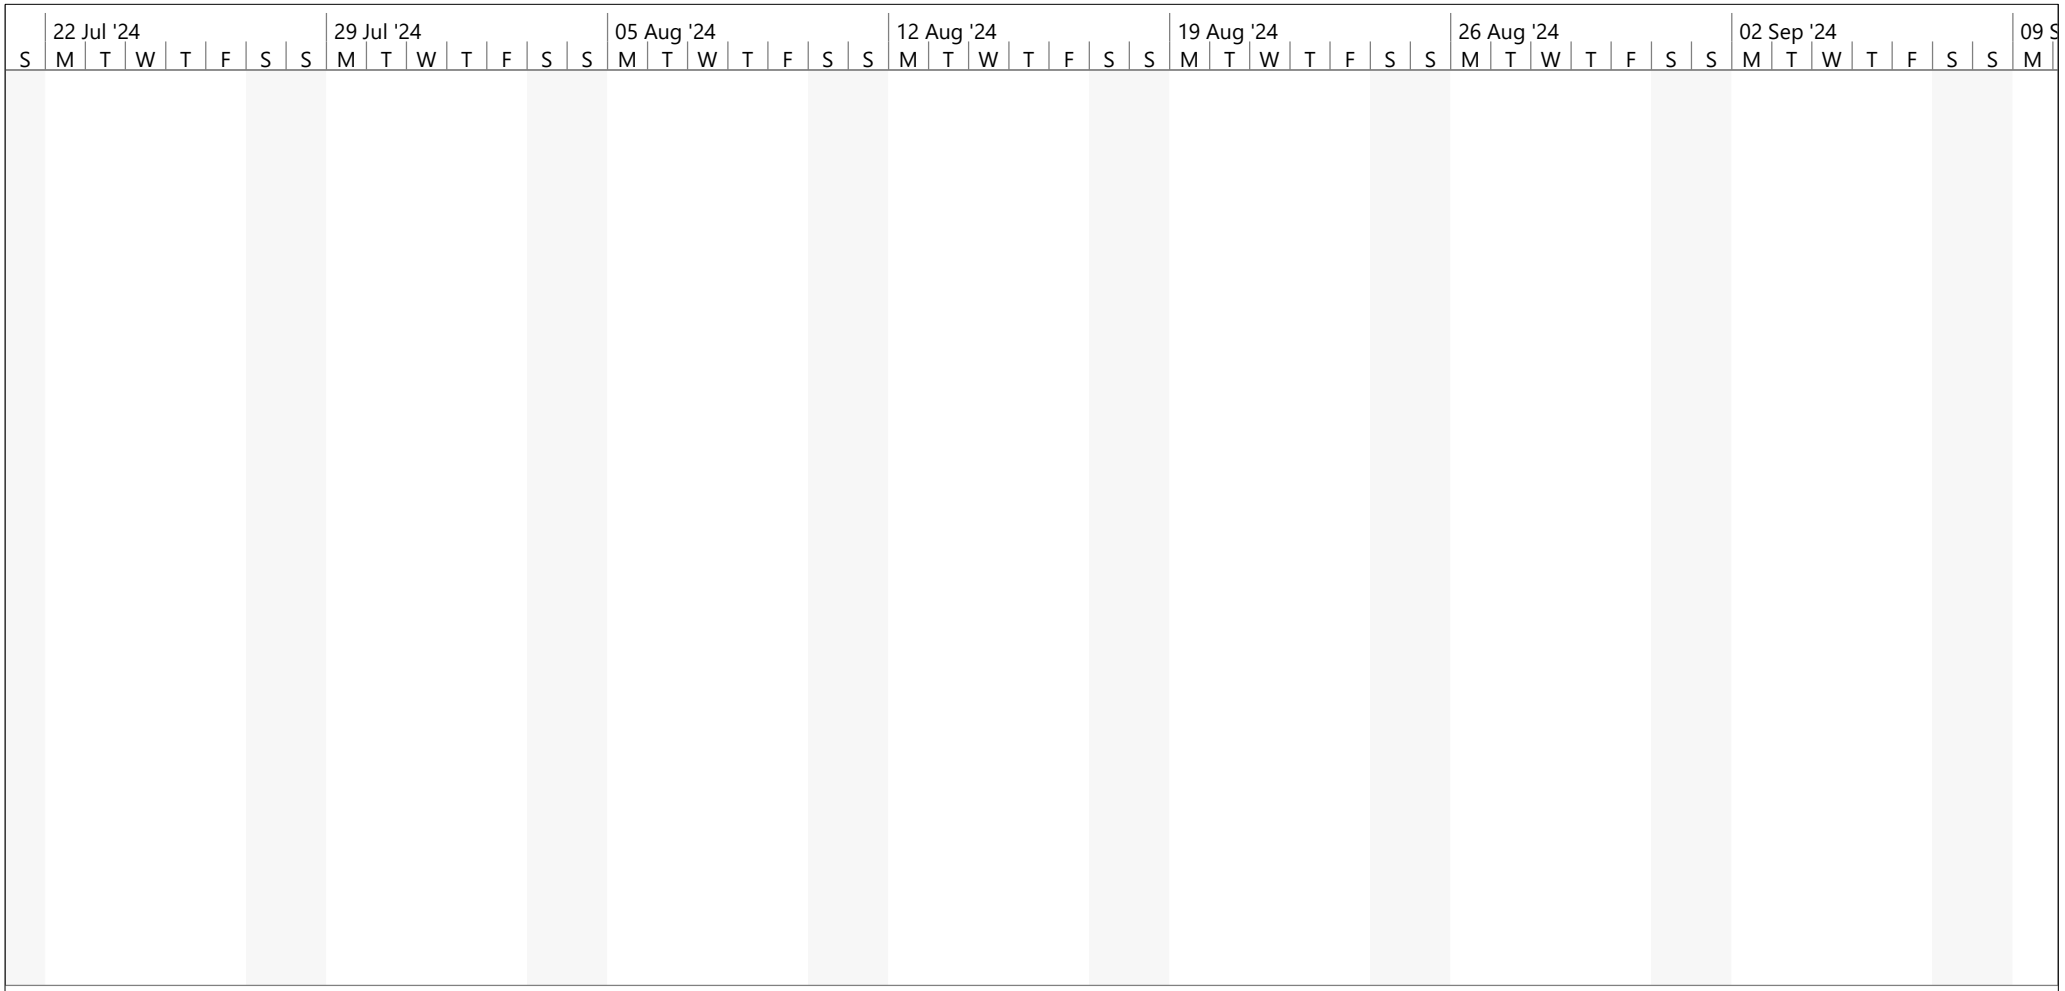


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

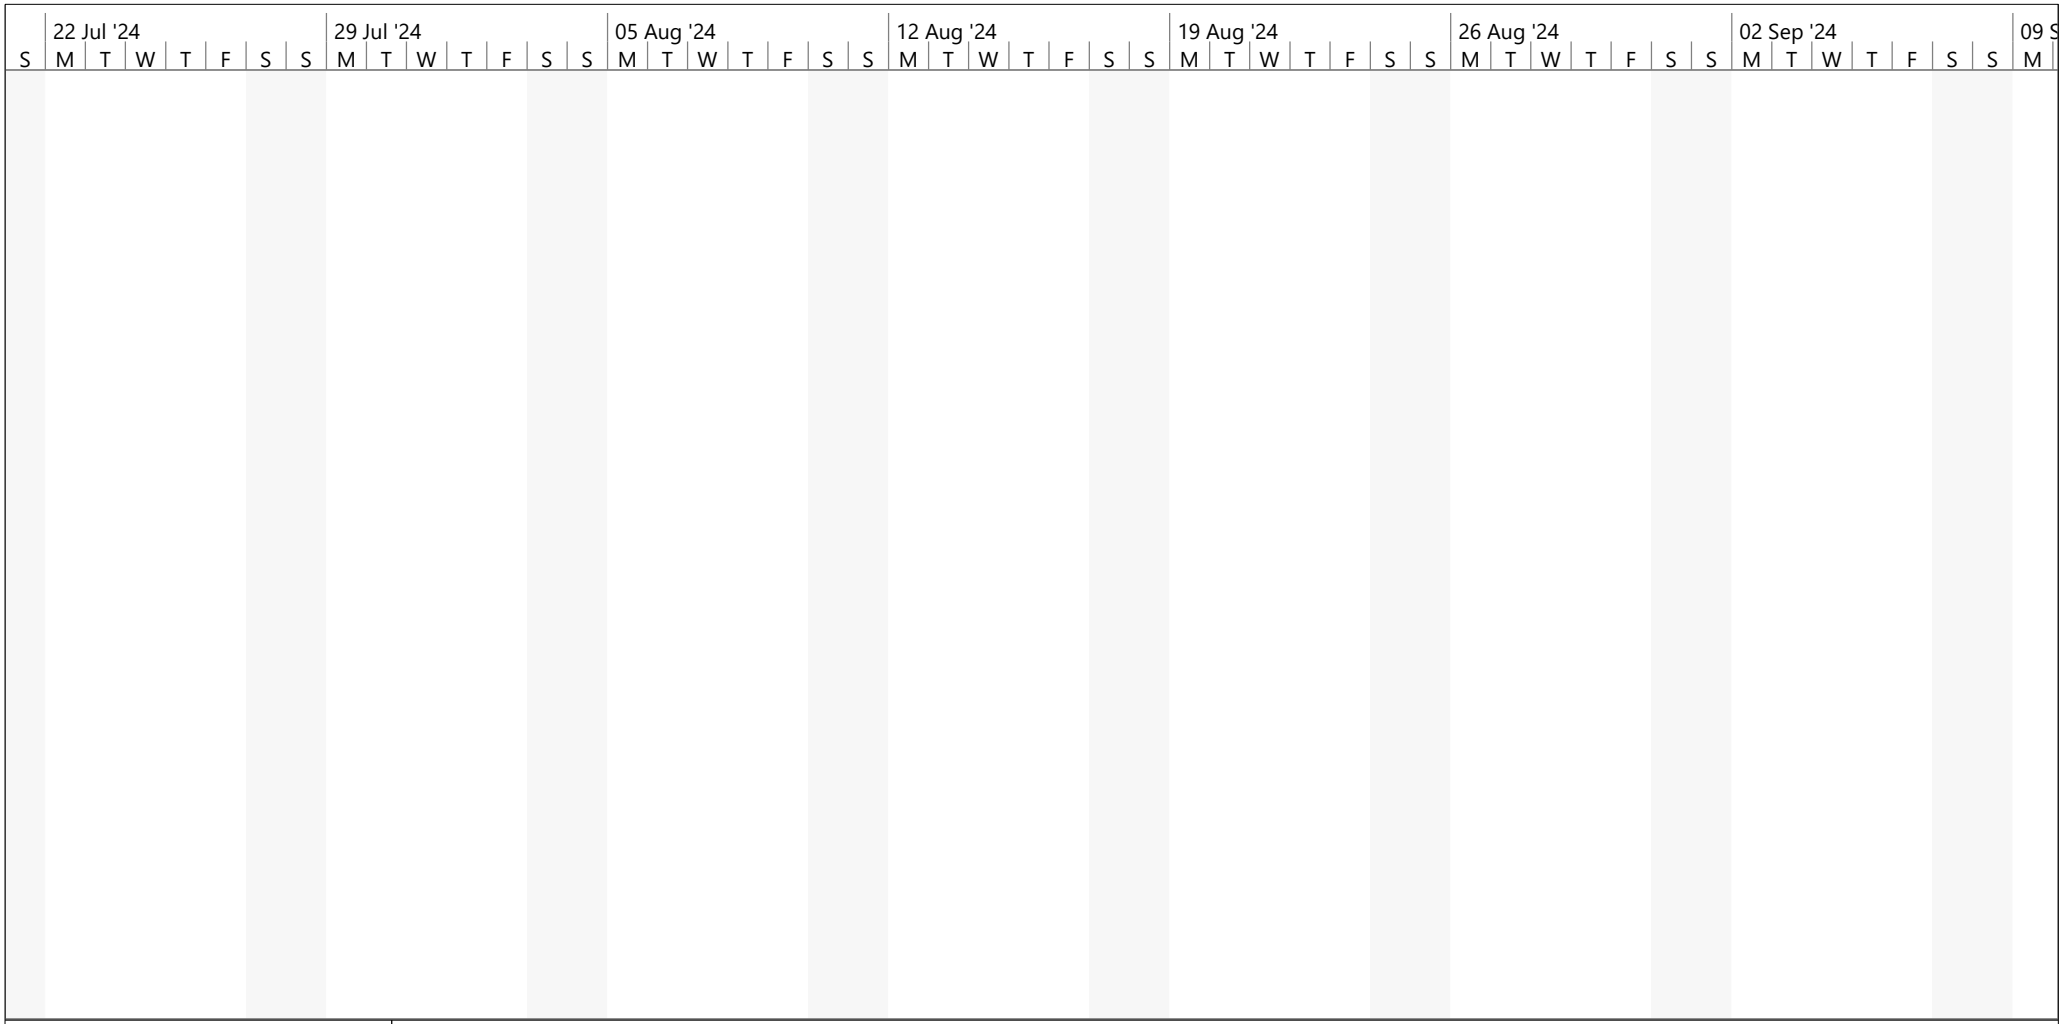


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

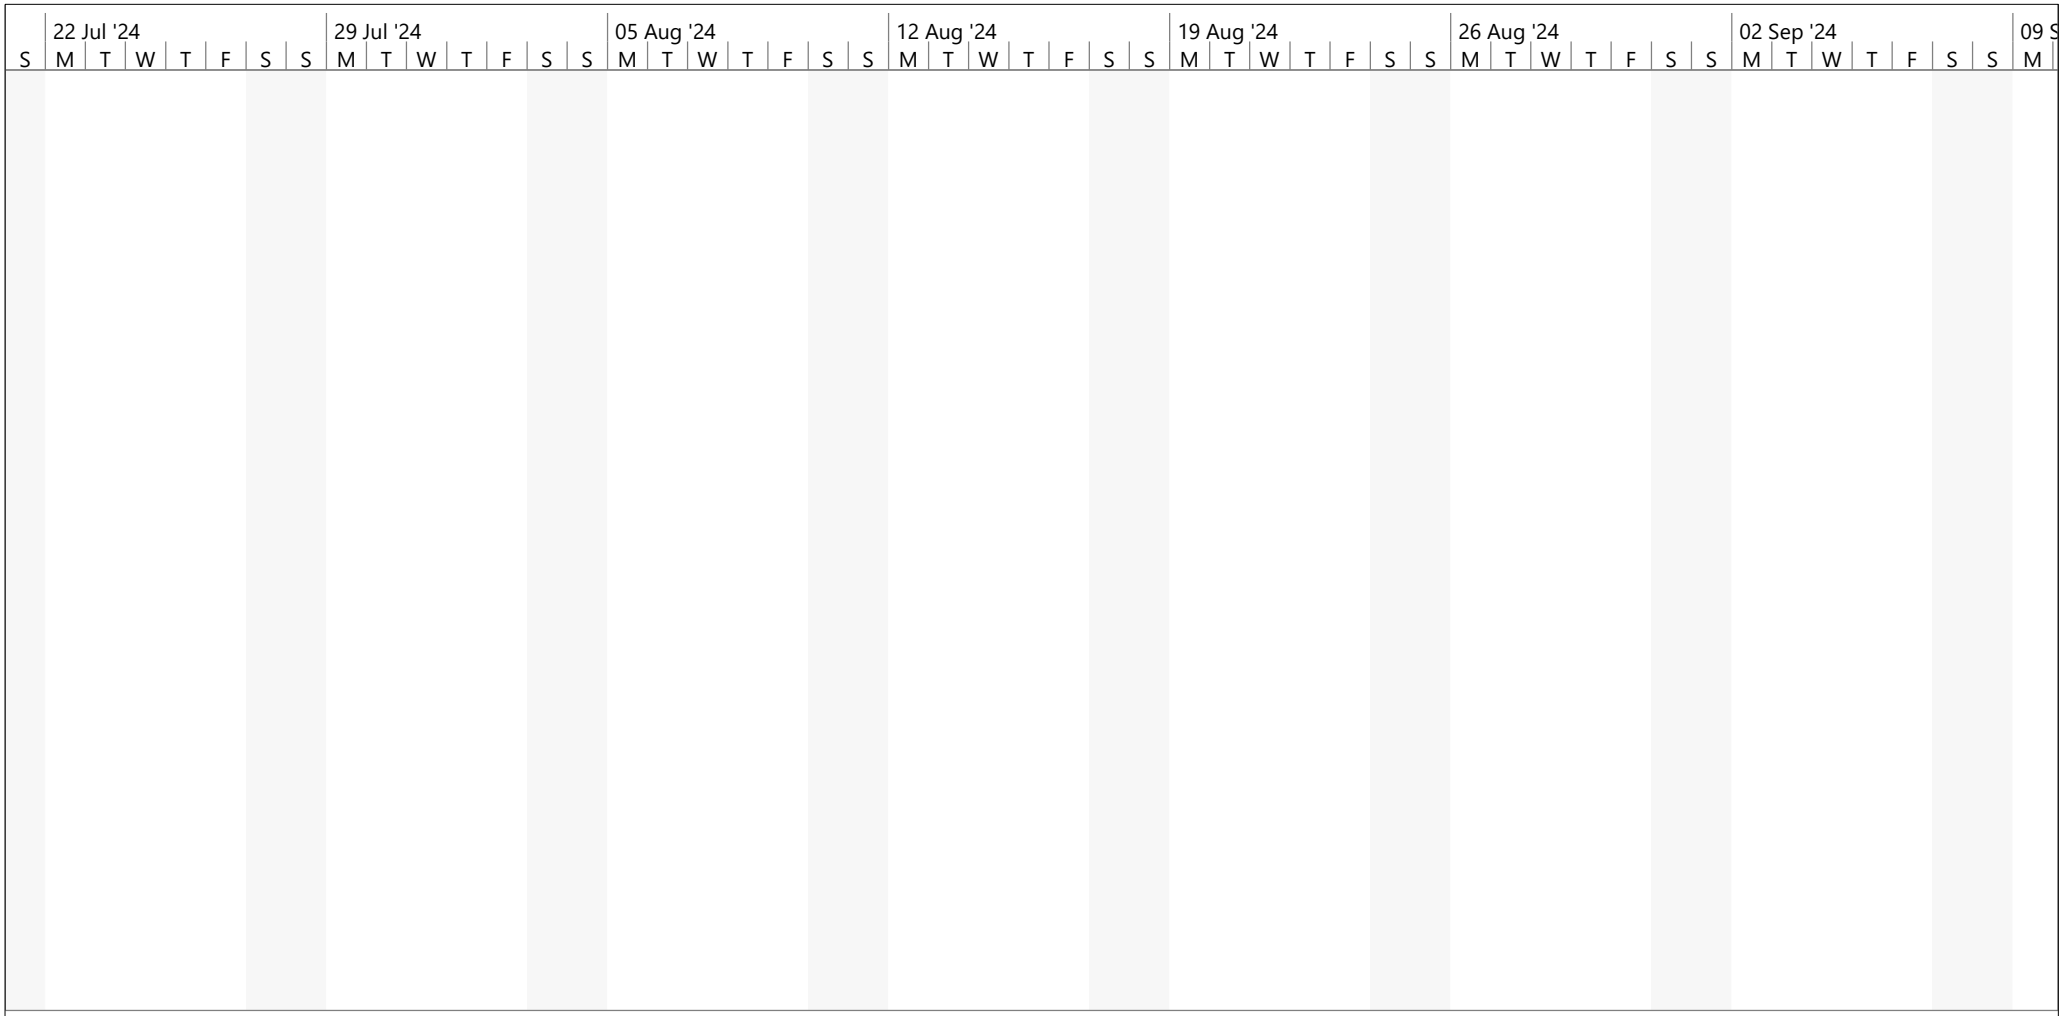


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

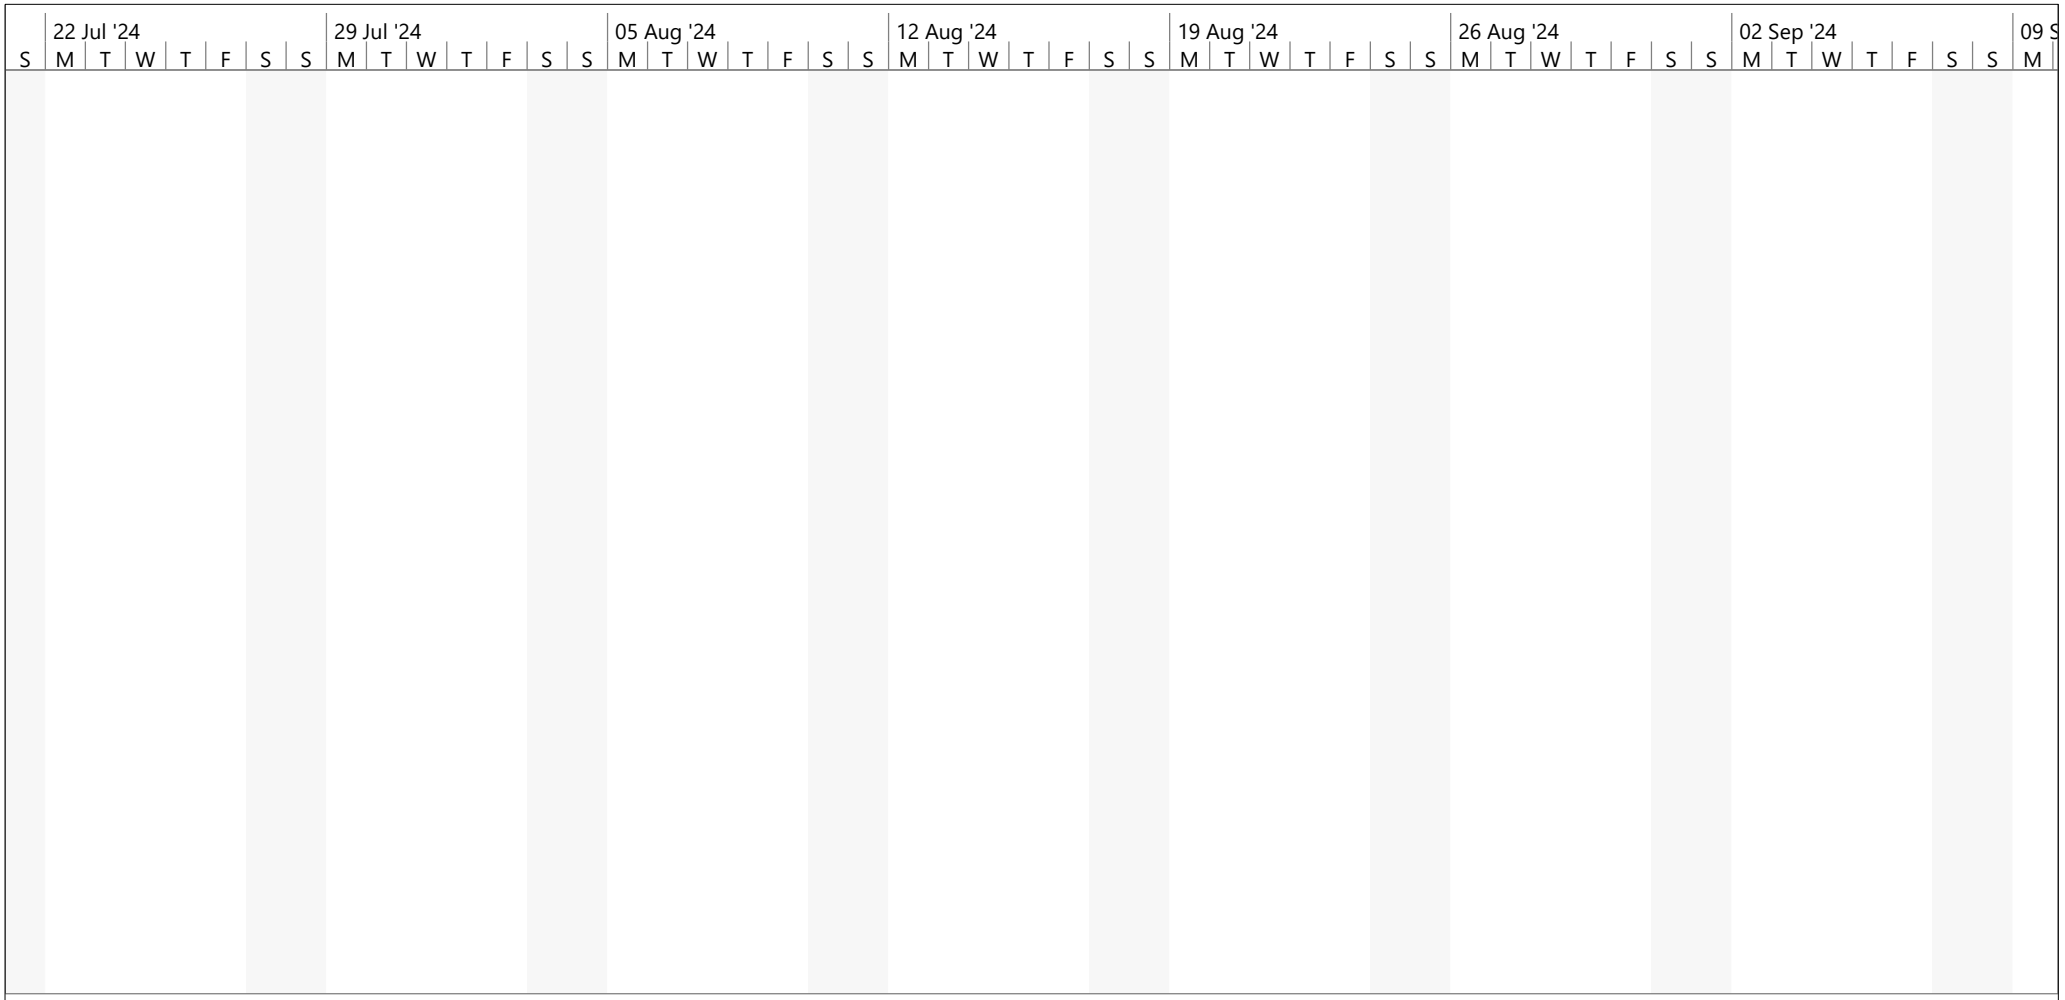


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

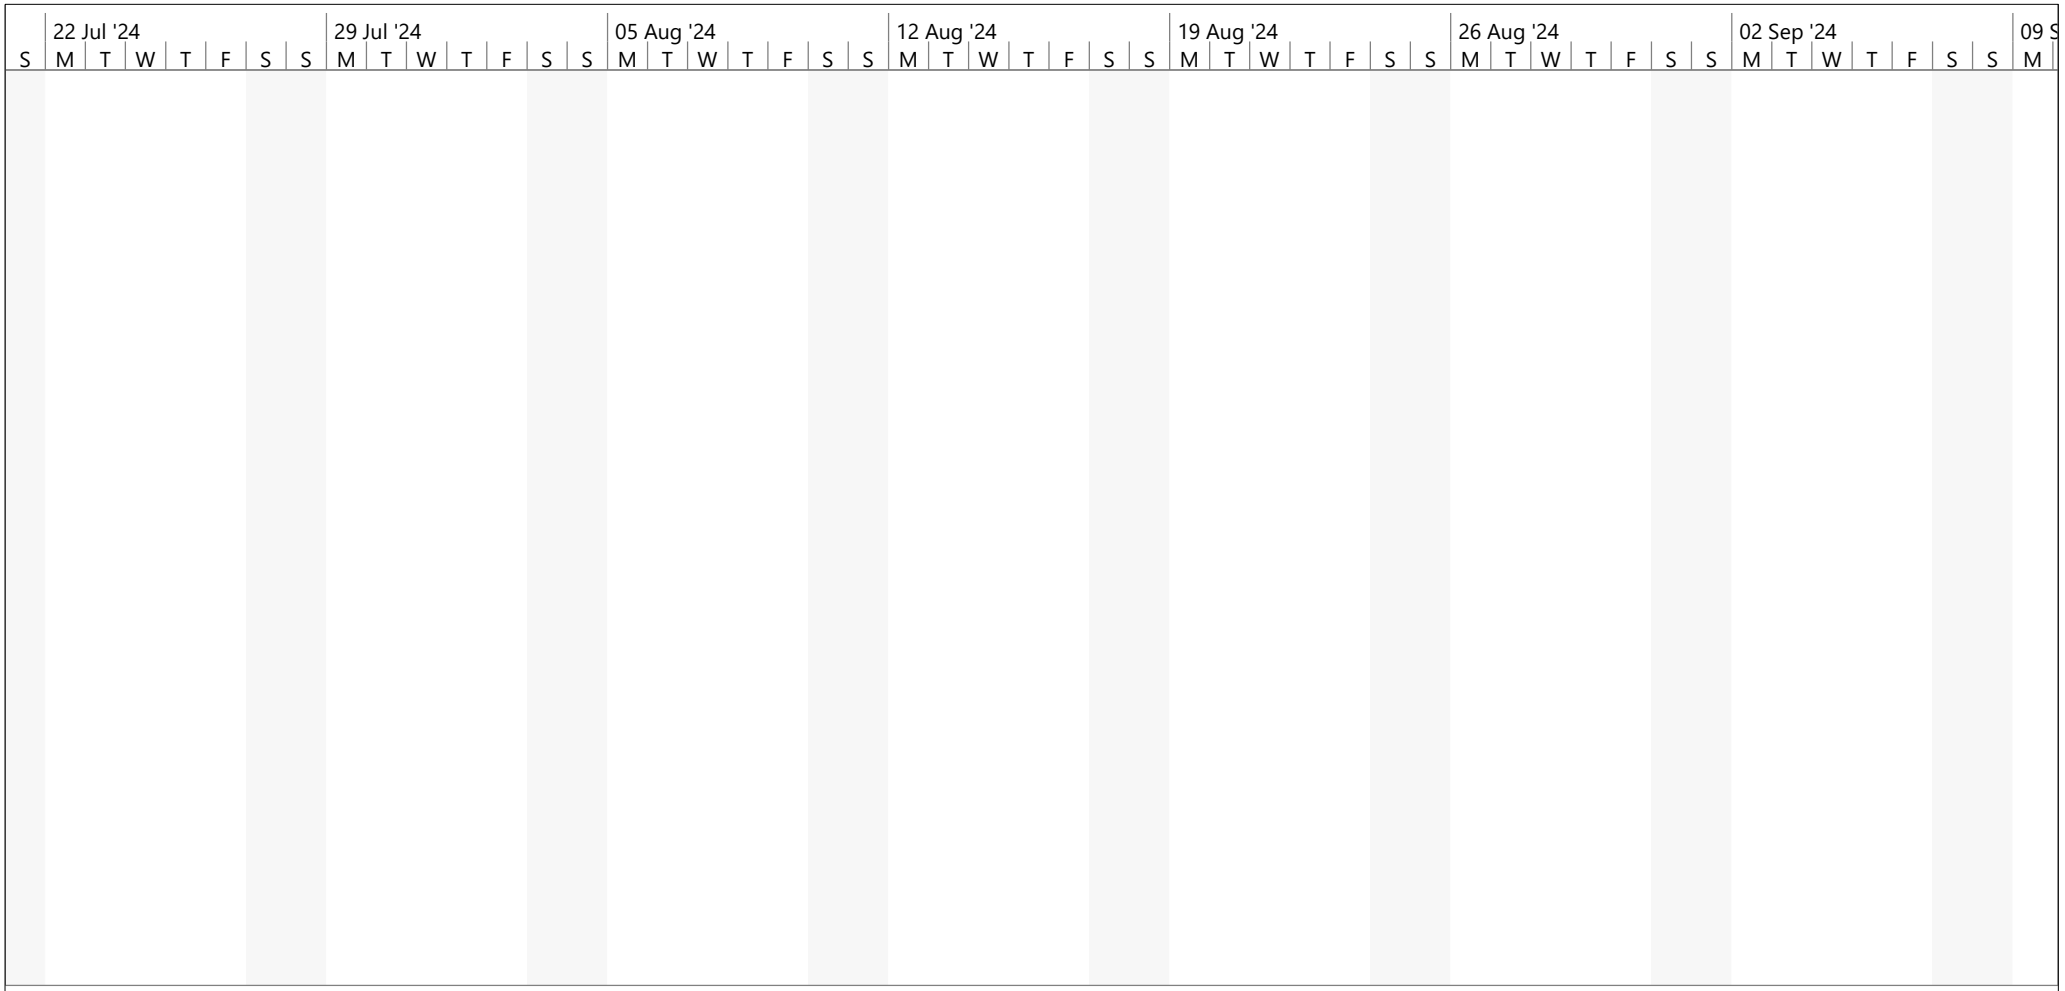


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

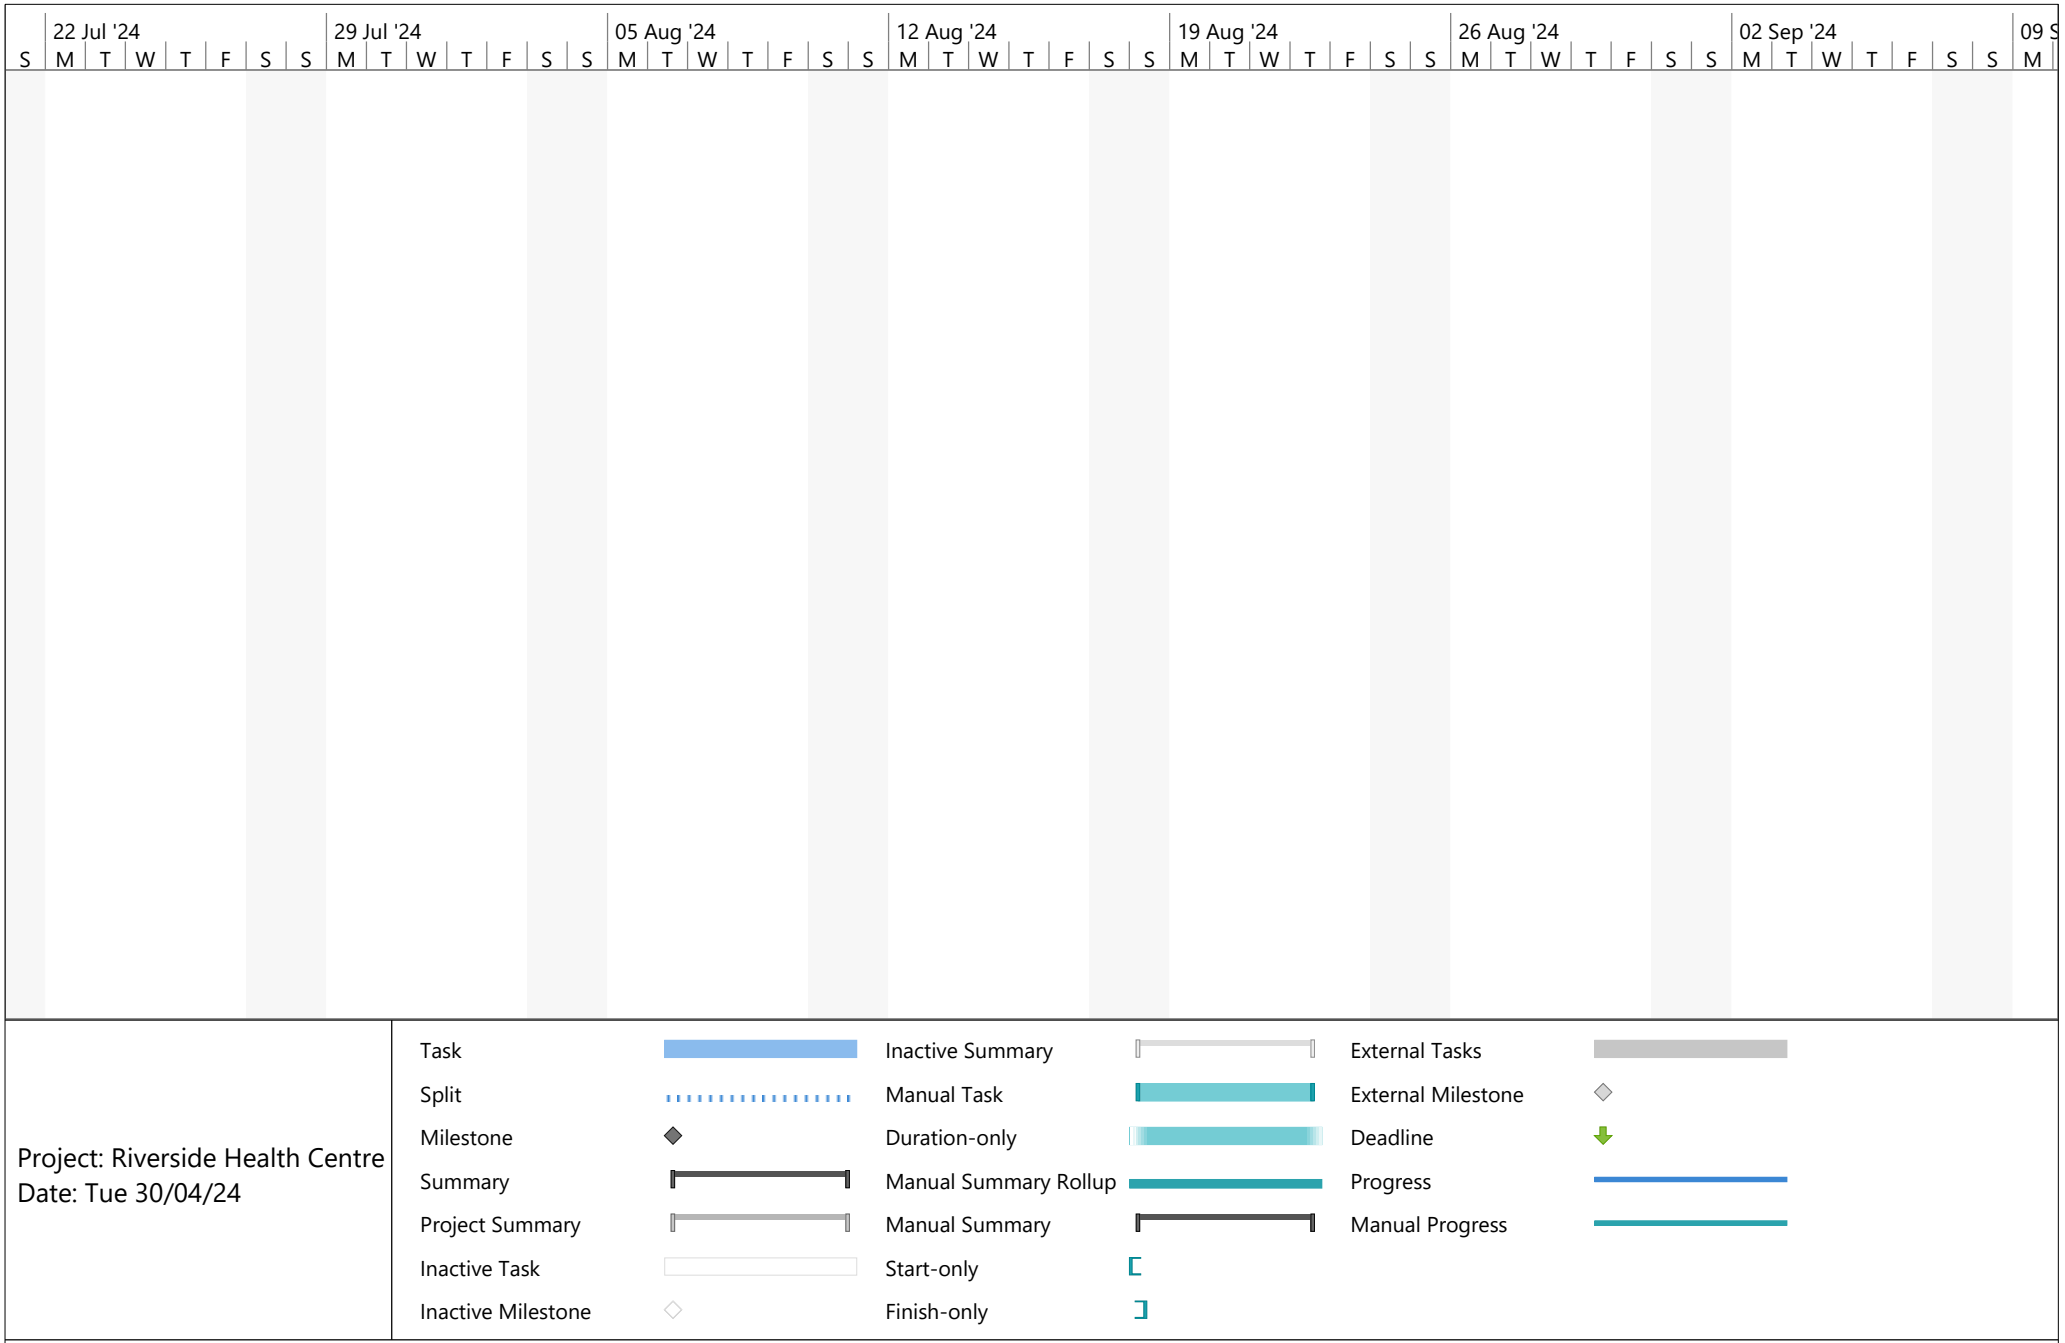


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

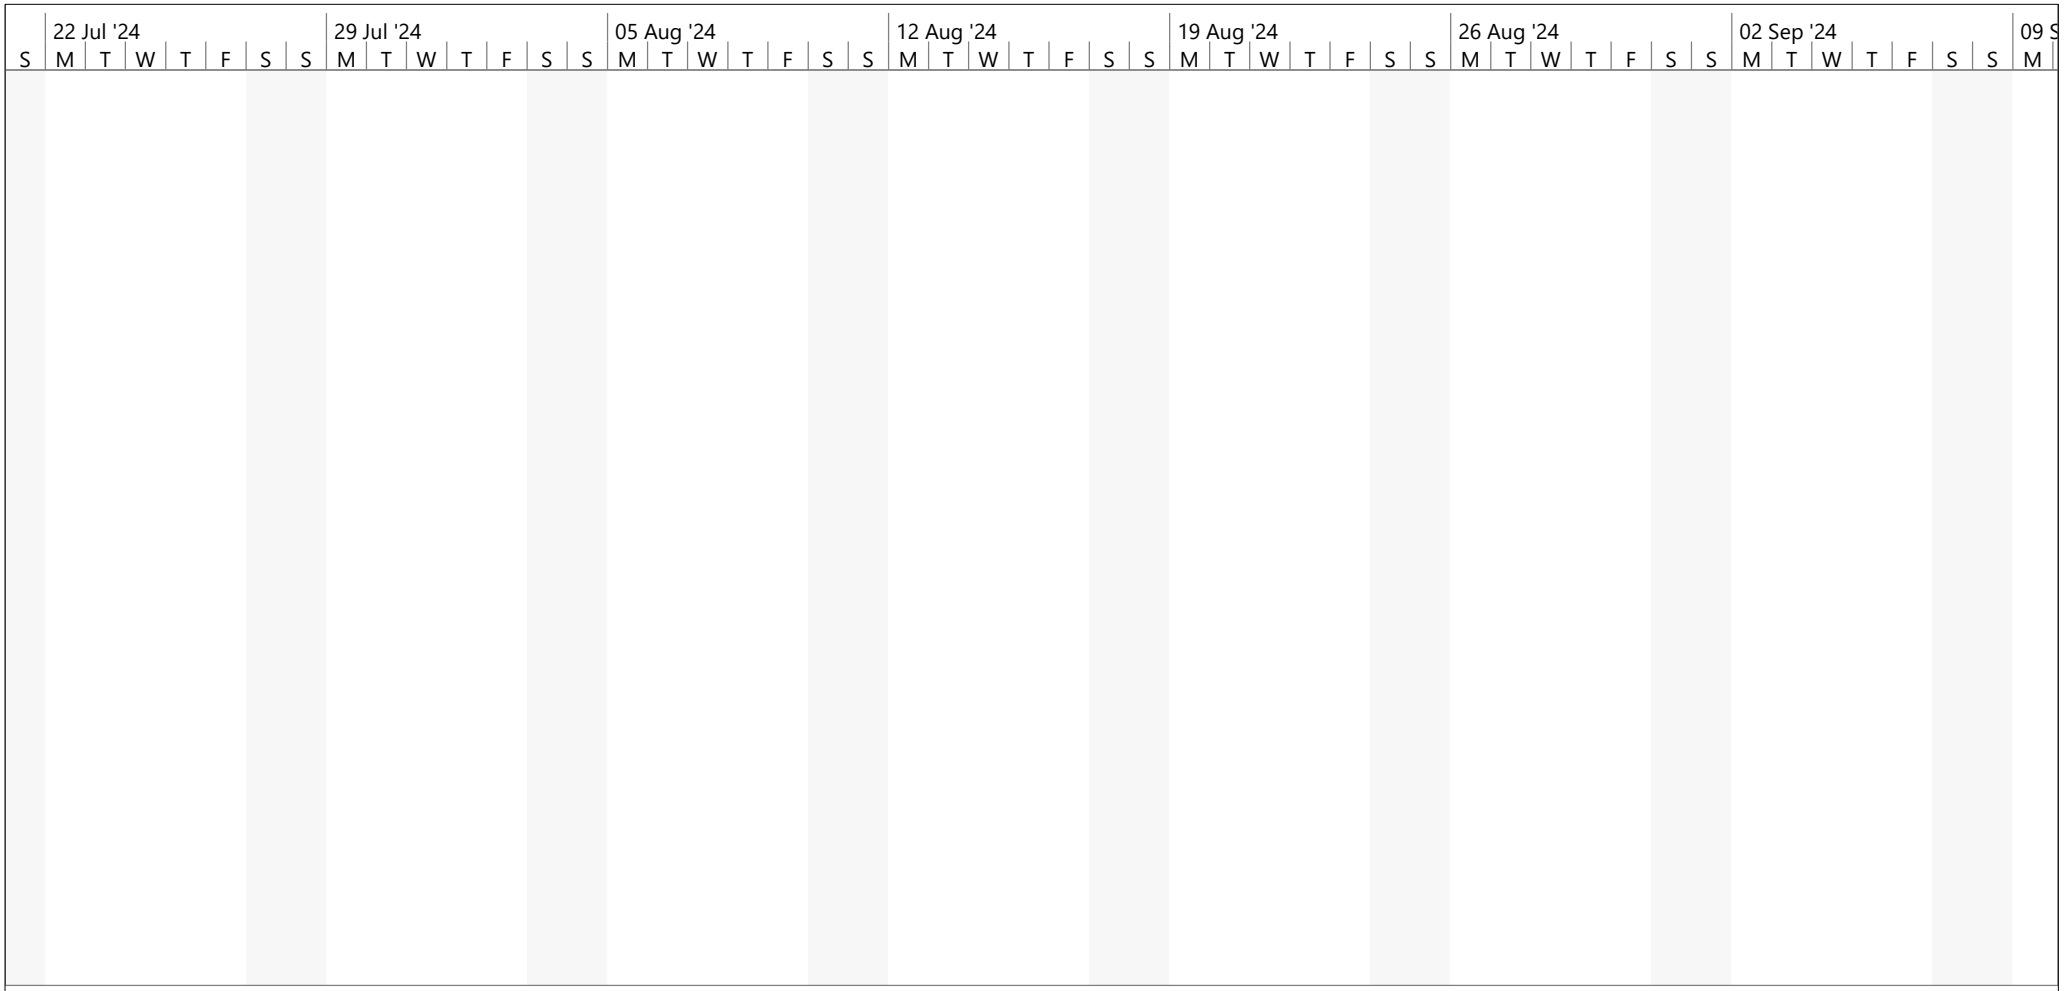


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

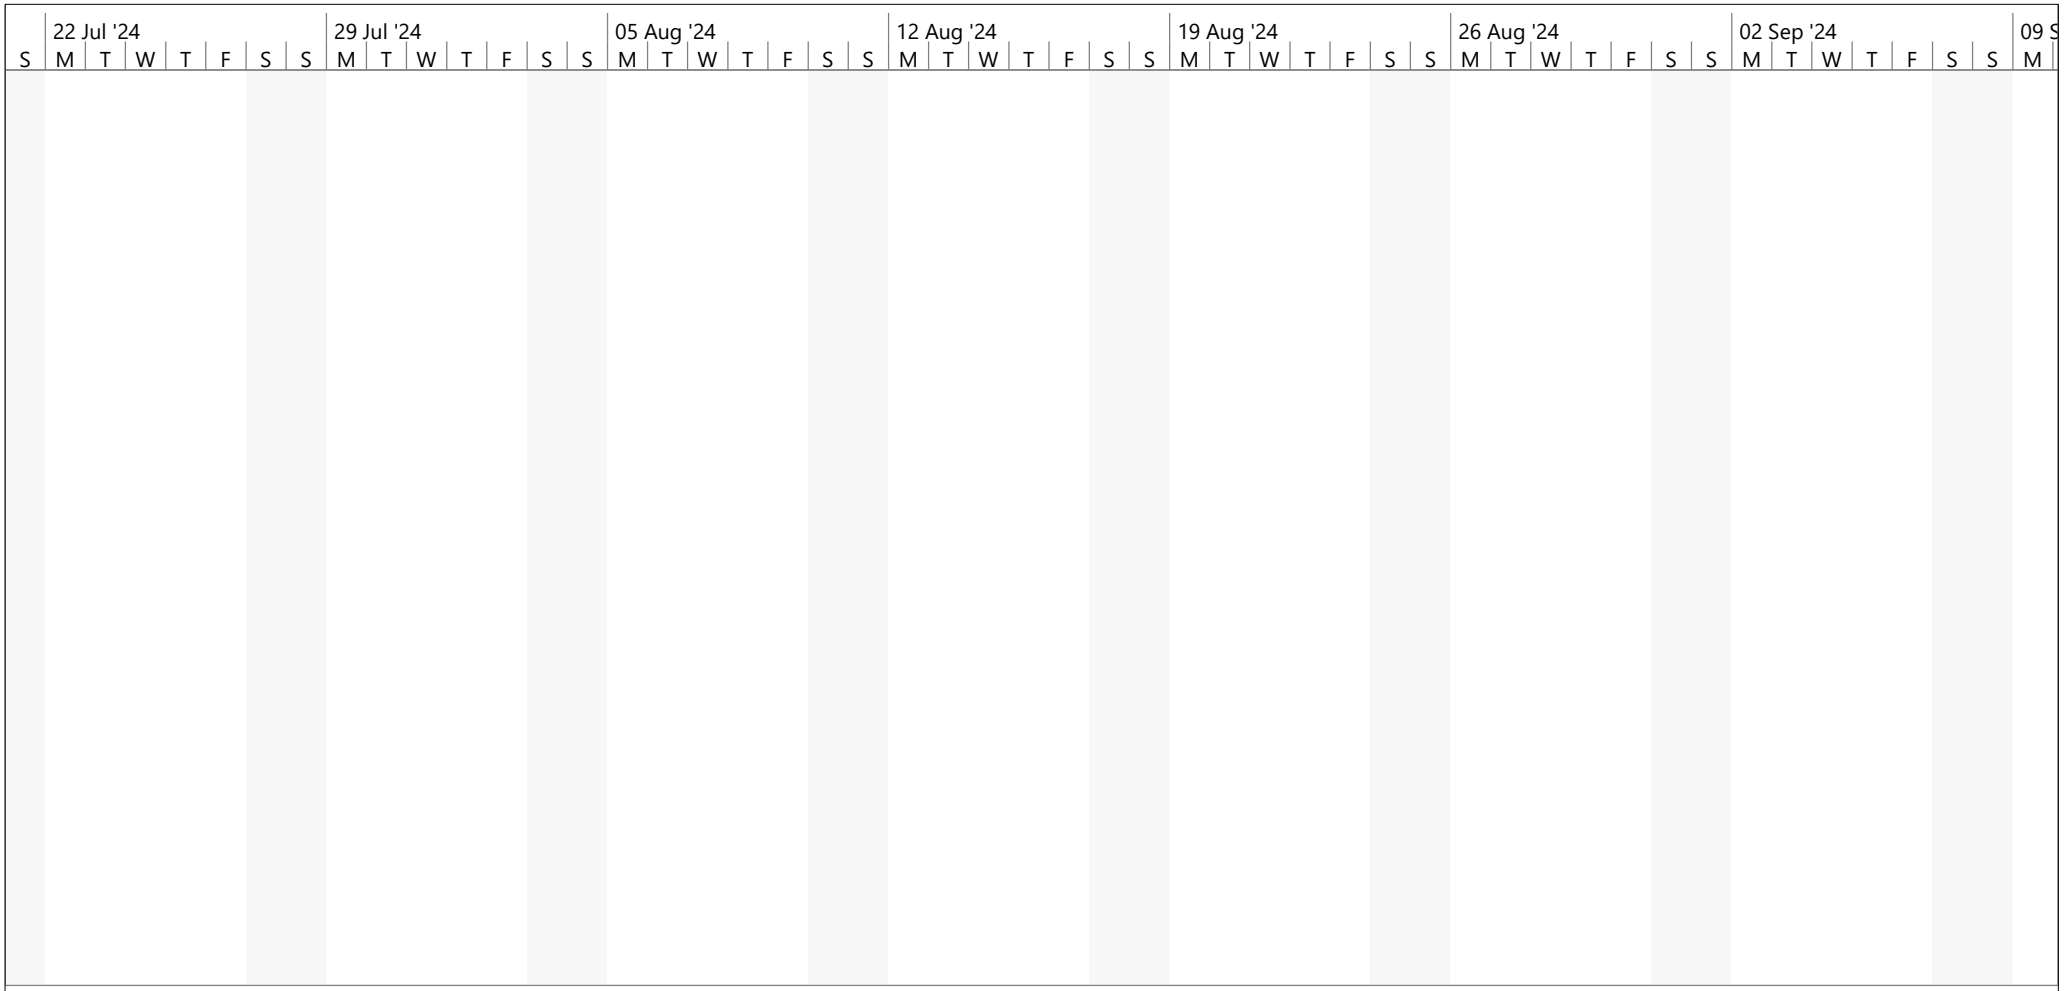


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

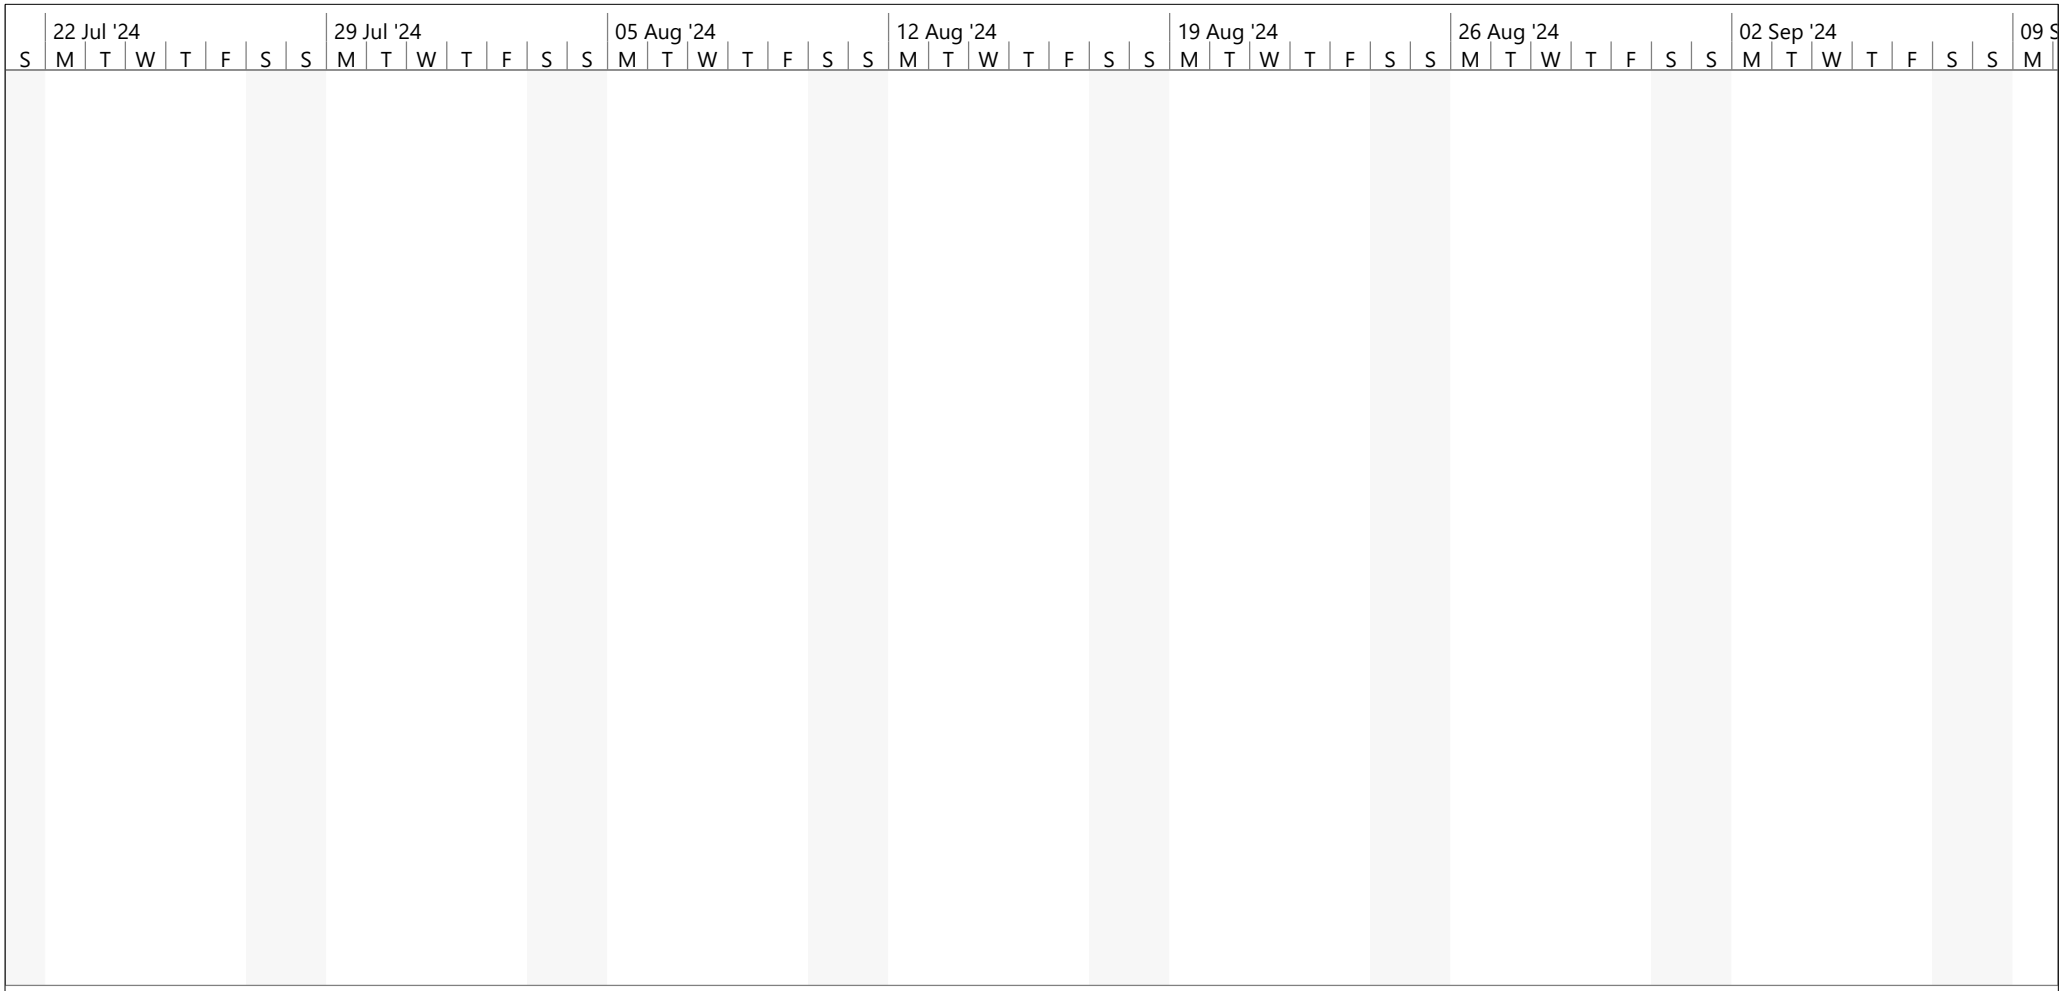


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

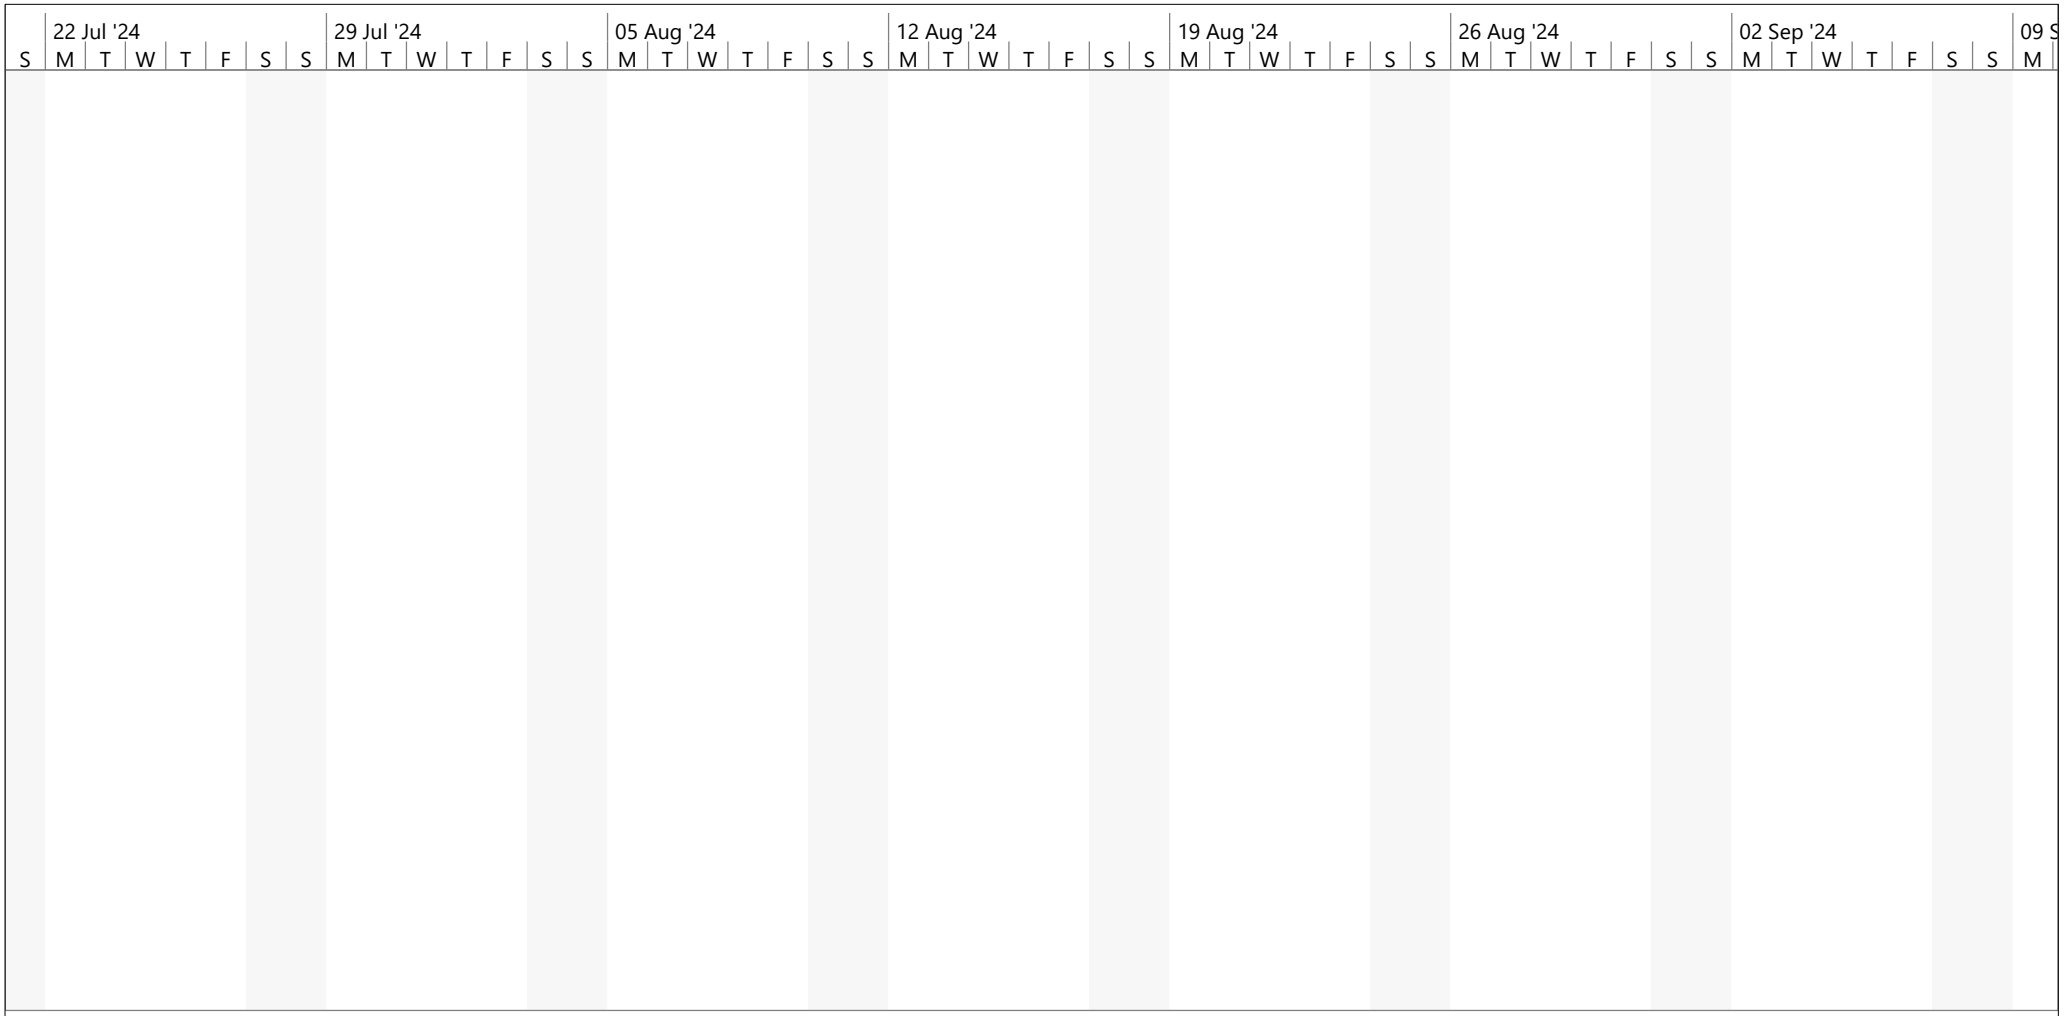


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

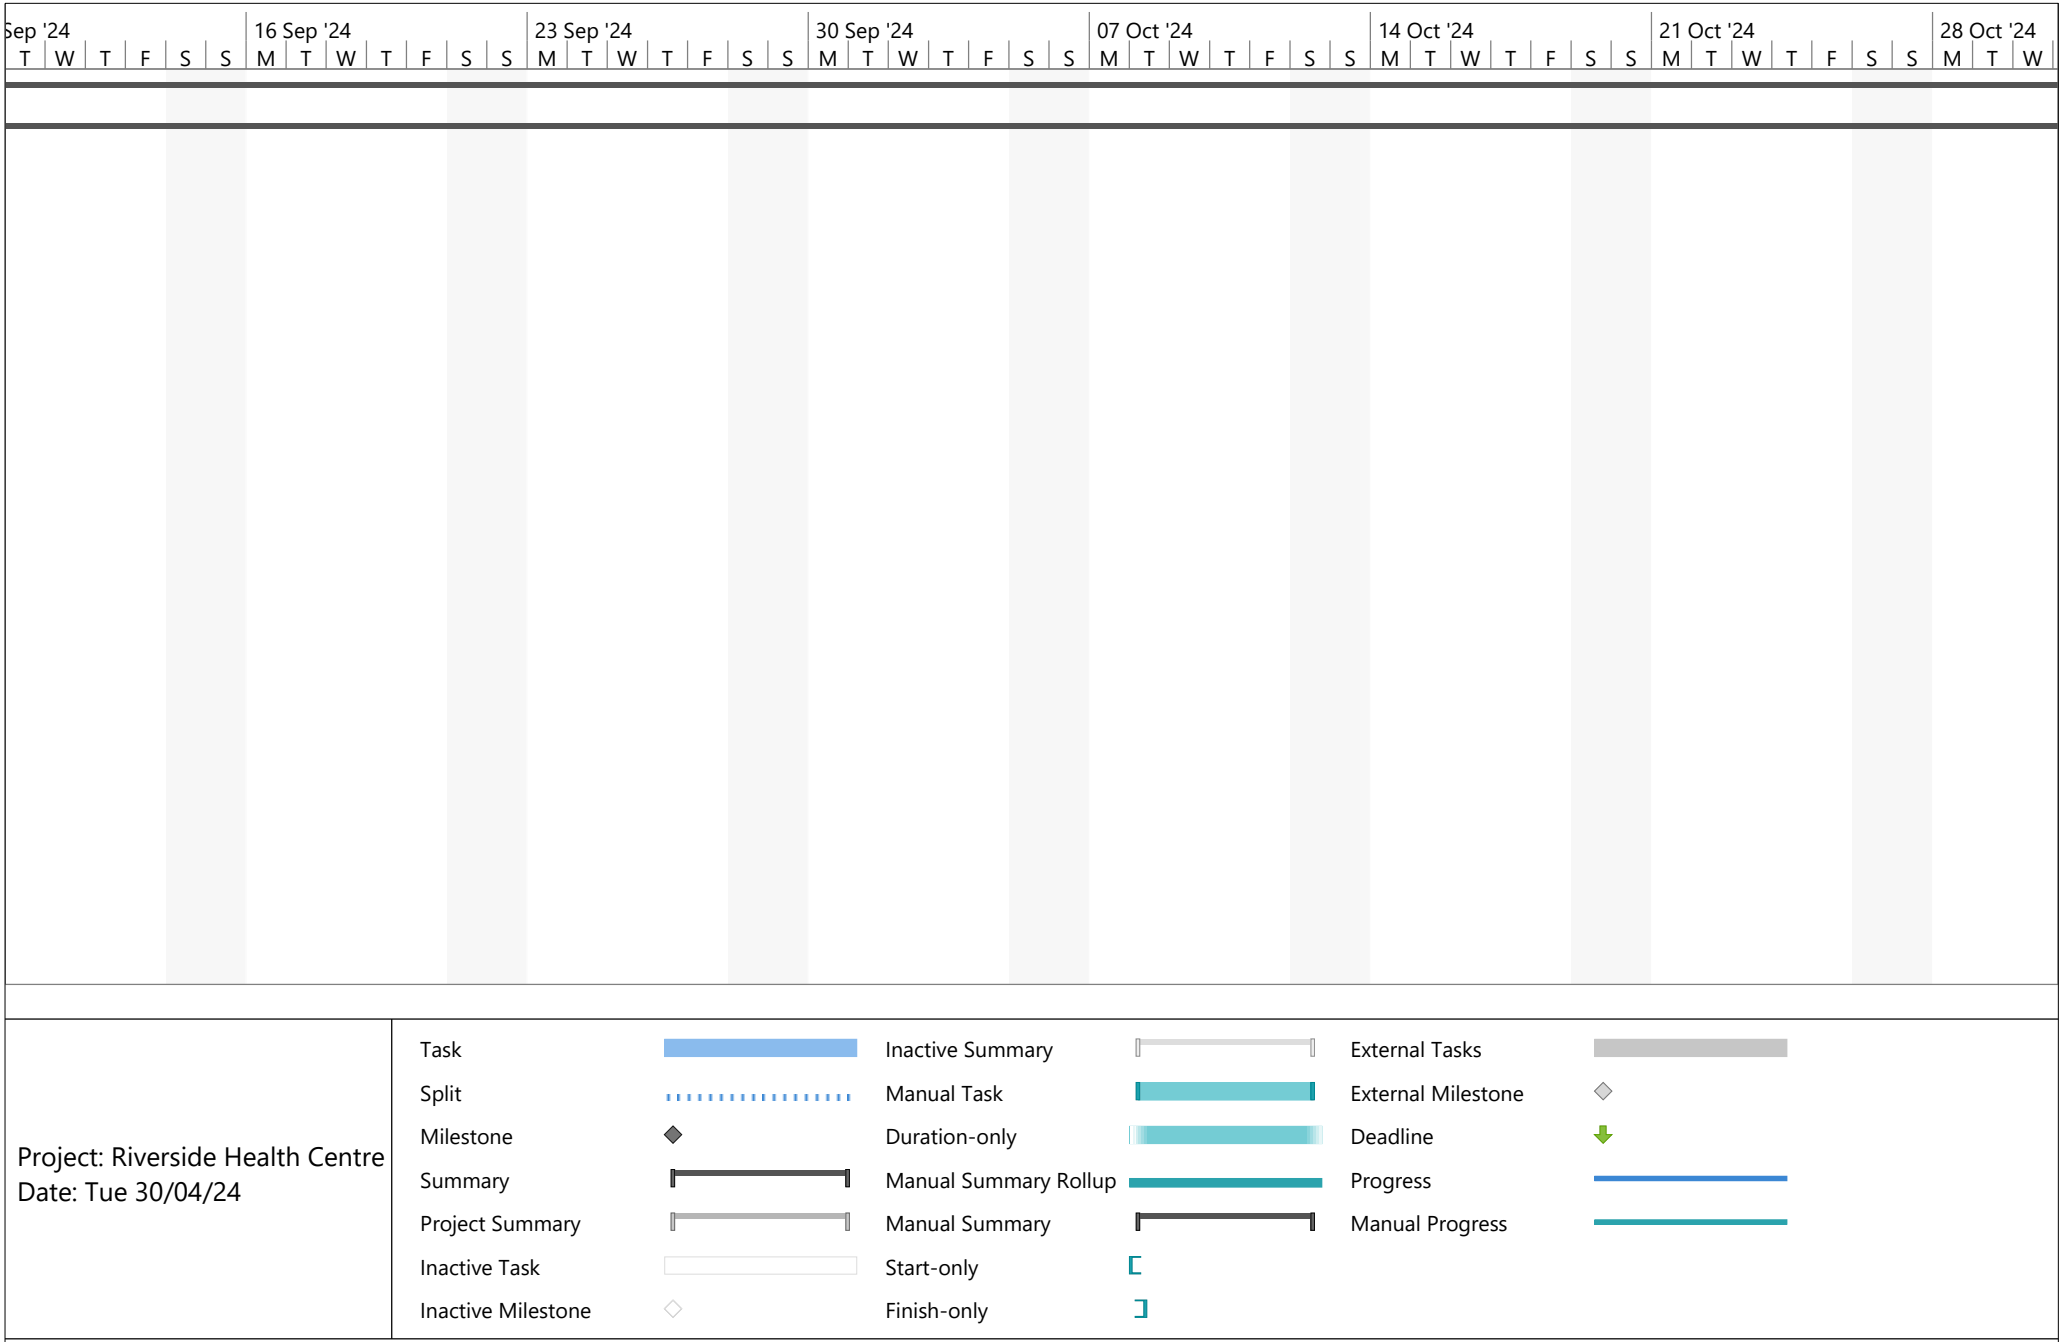
Sep '24
16 Sep '24
23 Sep '24
30 Sep '24
07 Oct '24
14 Oct '24
21 Oct '24
28 Oct '24
T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

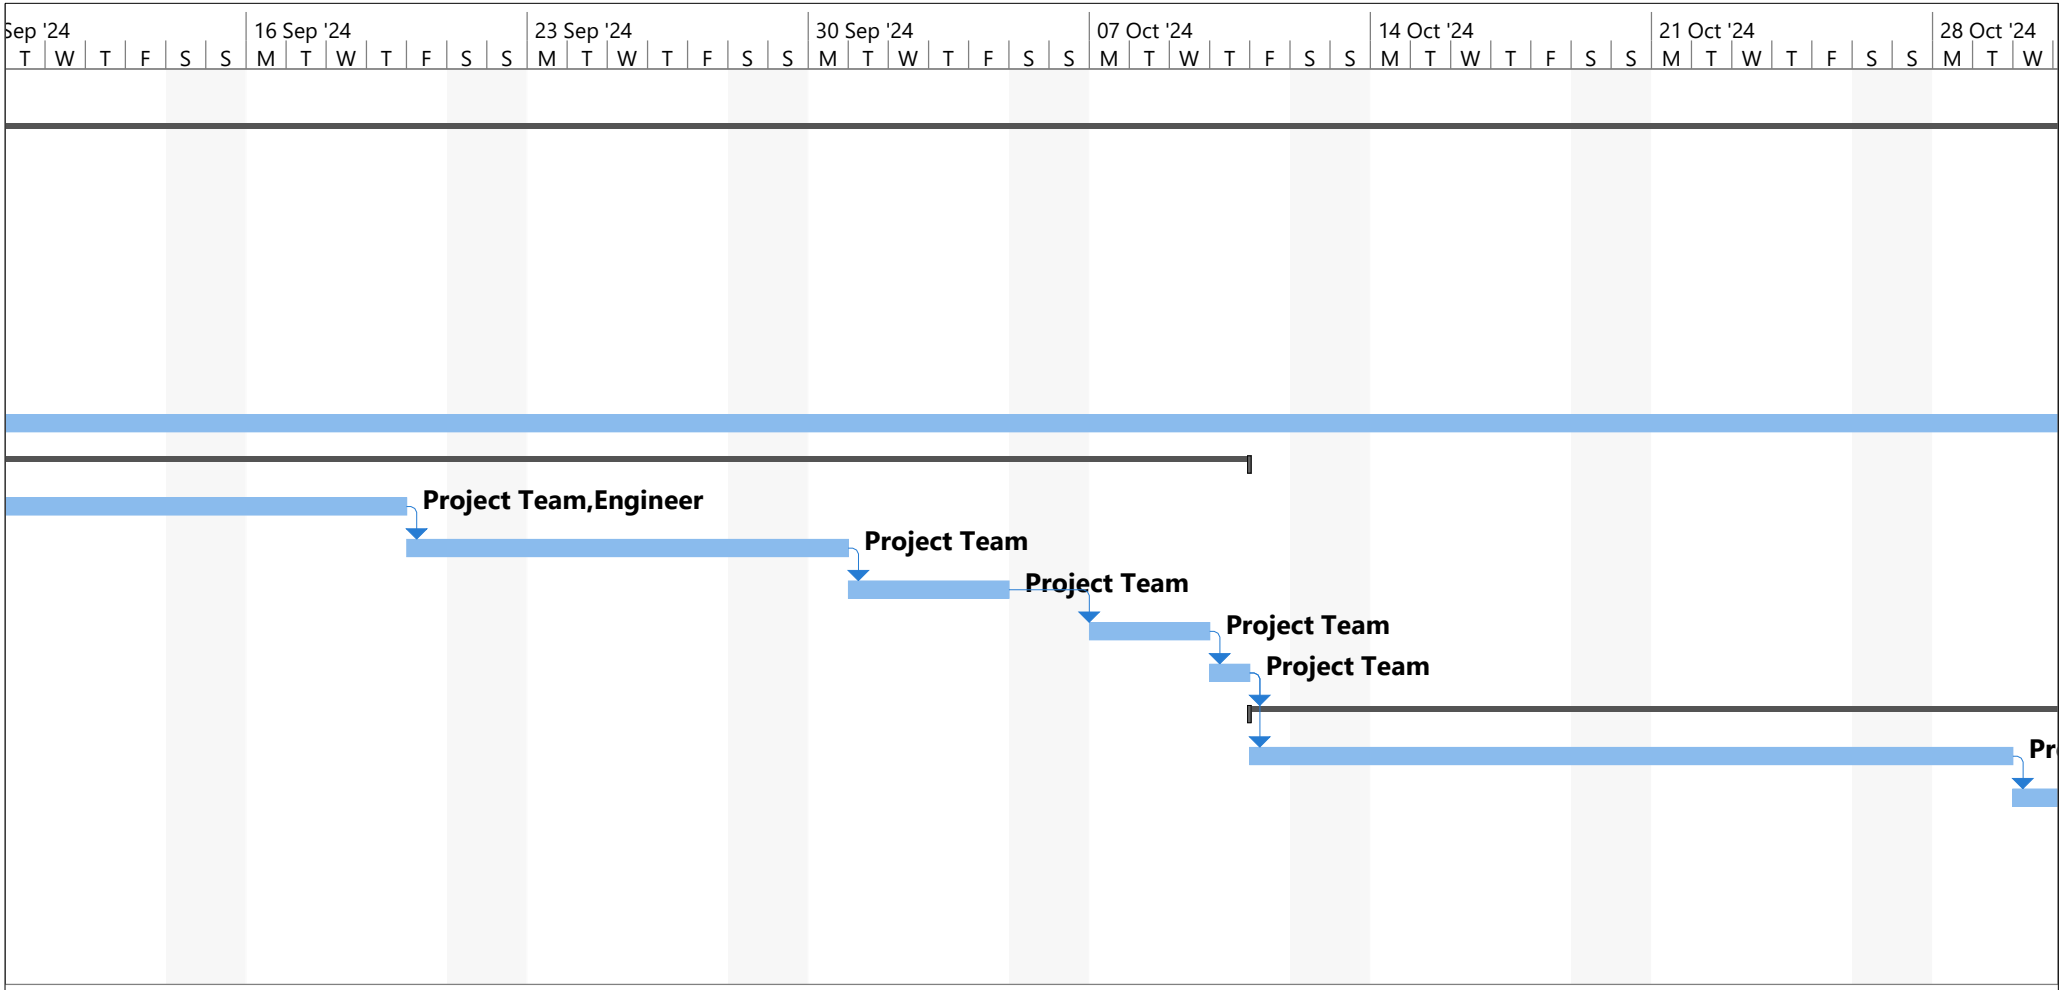


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

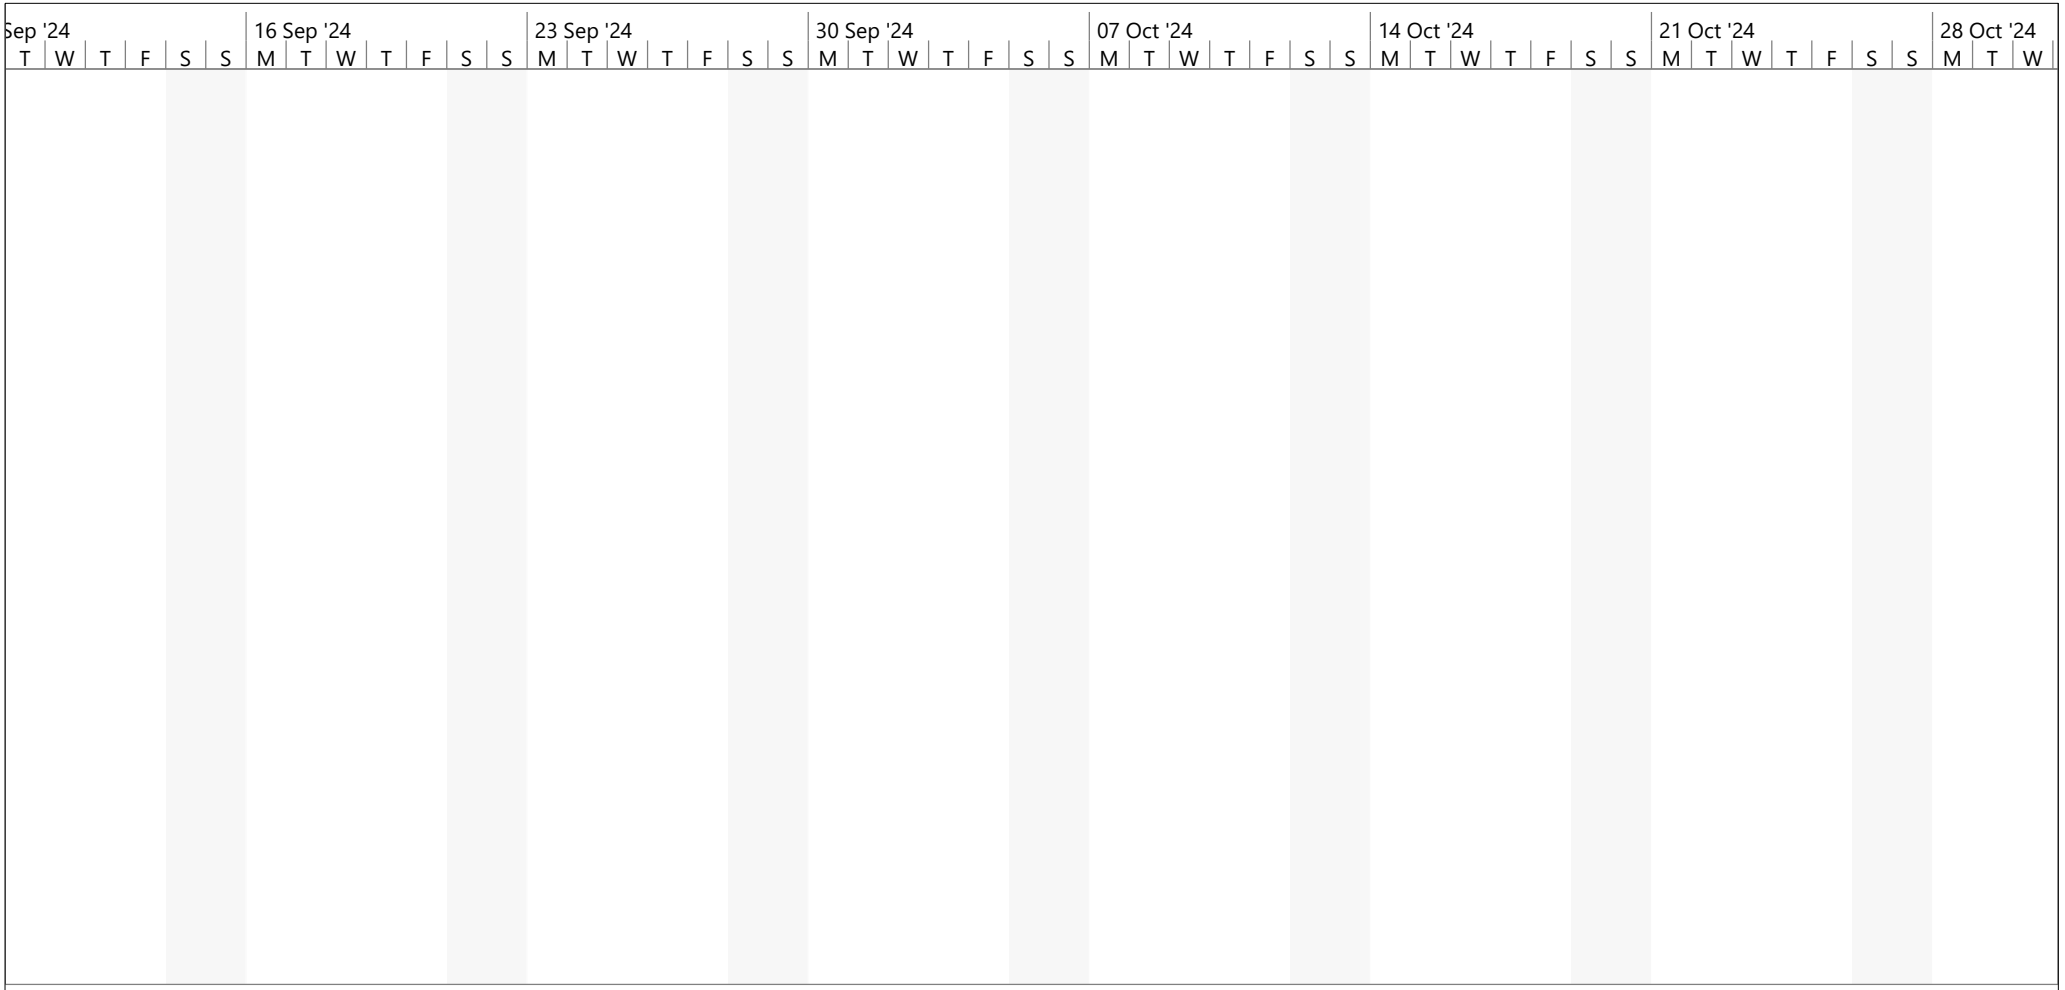


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

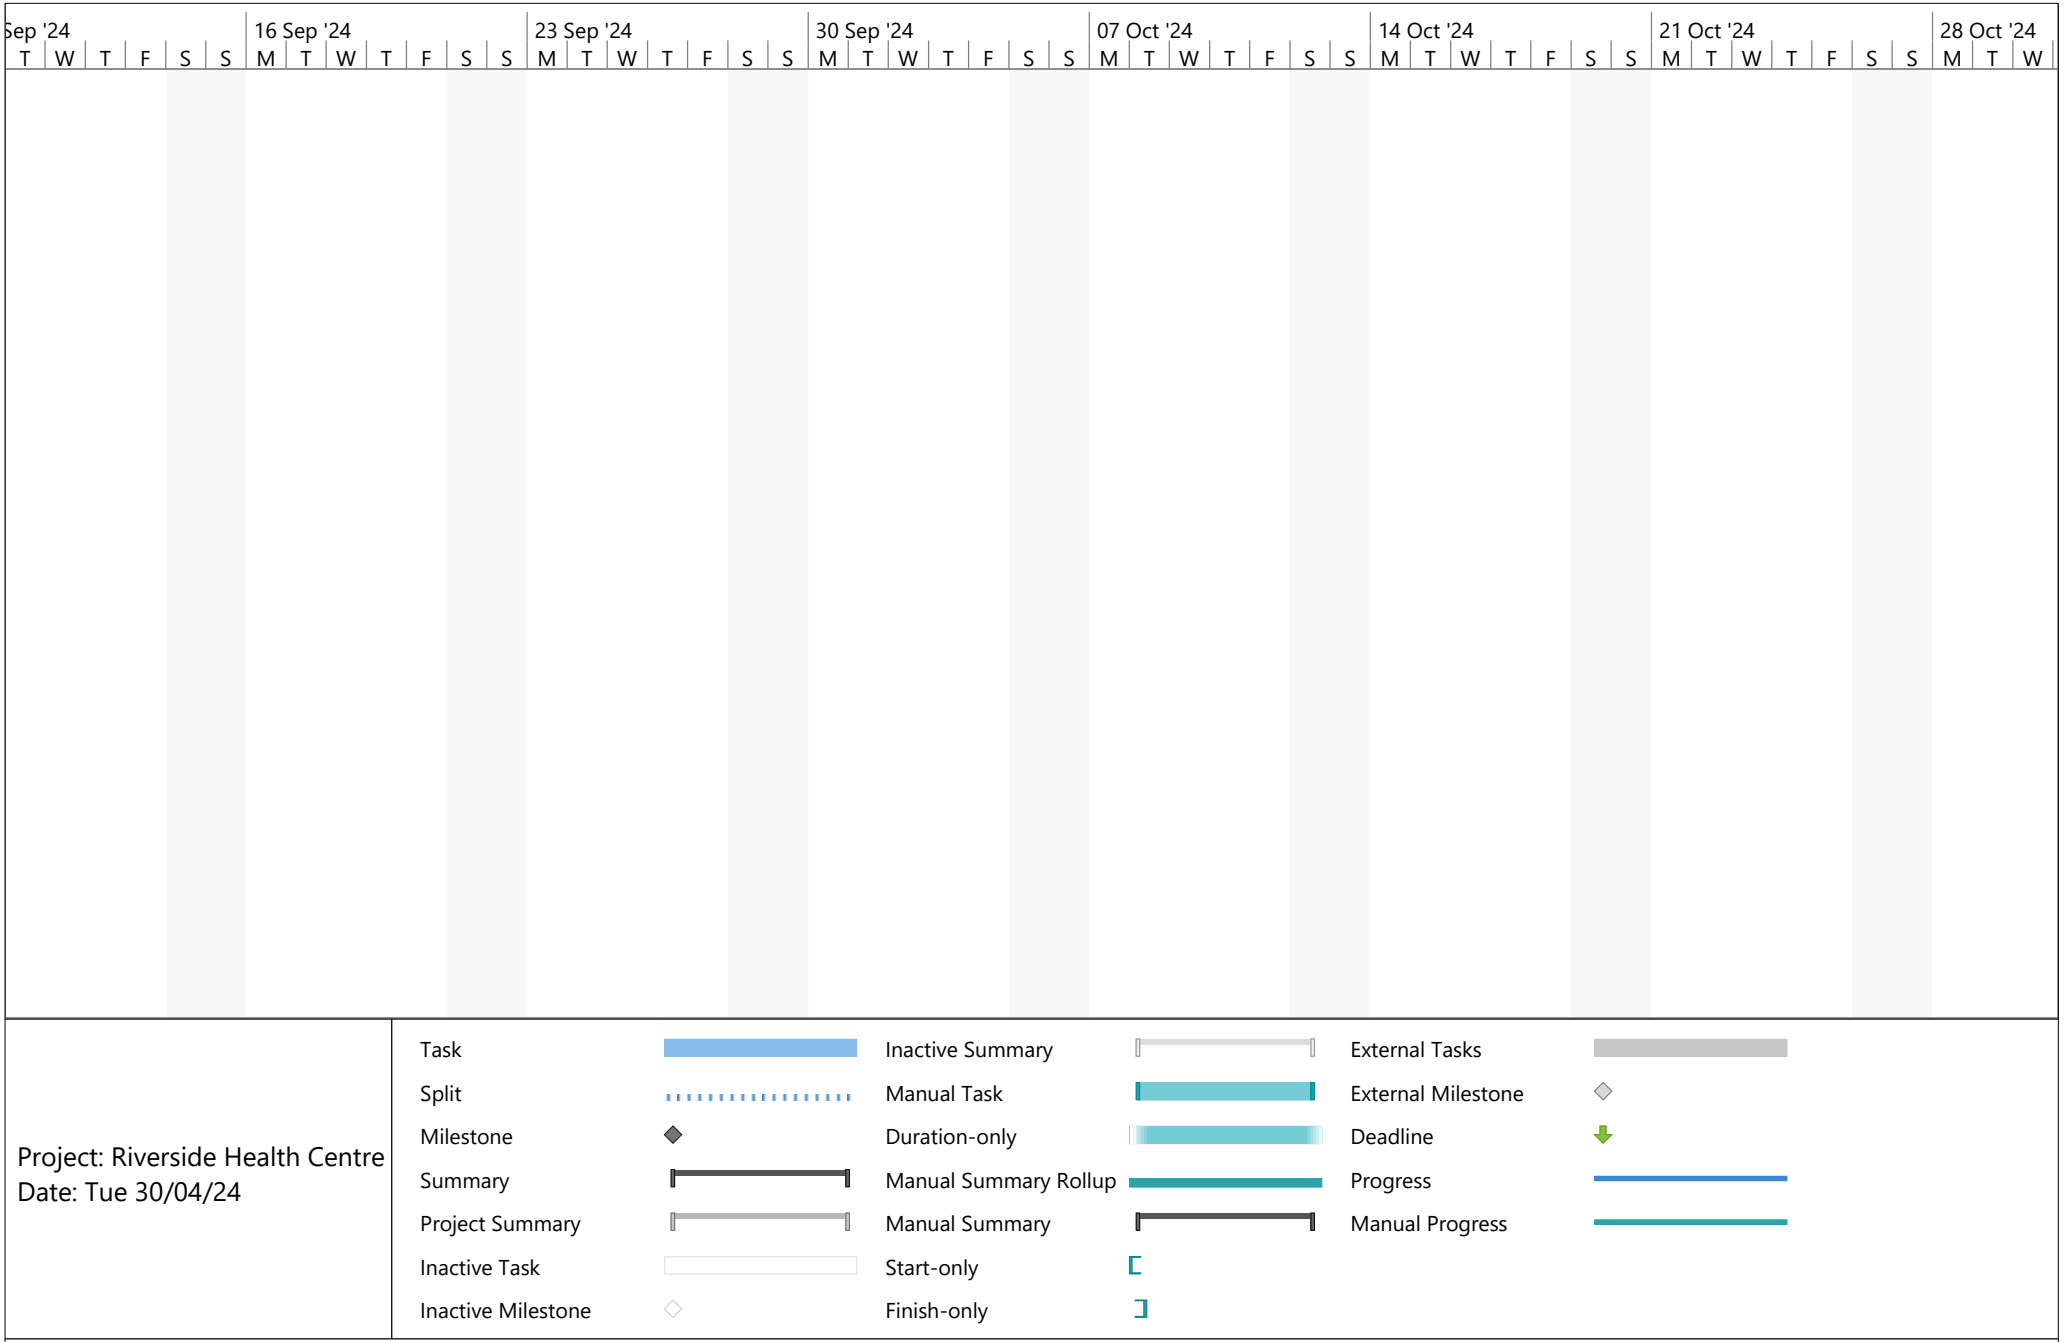


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

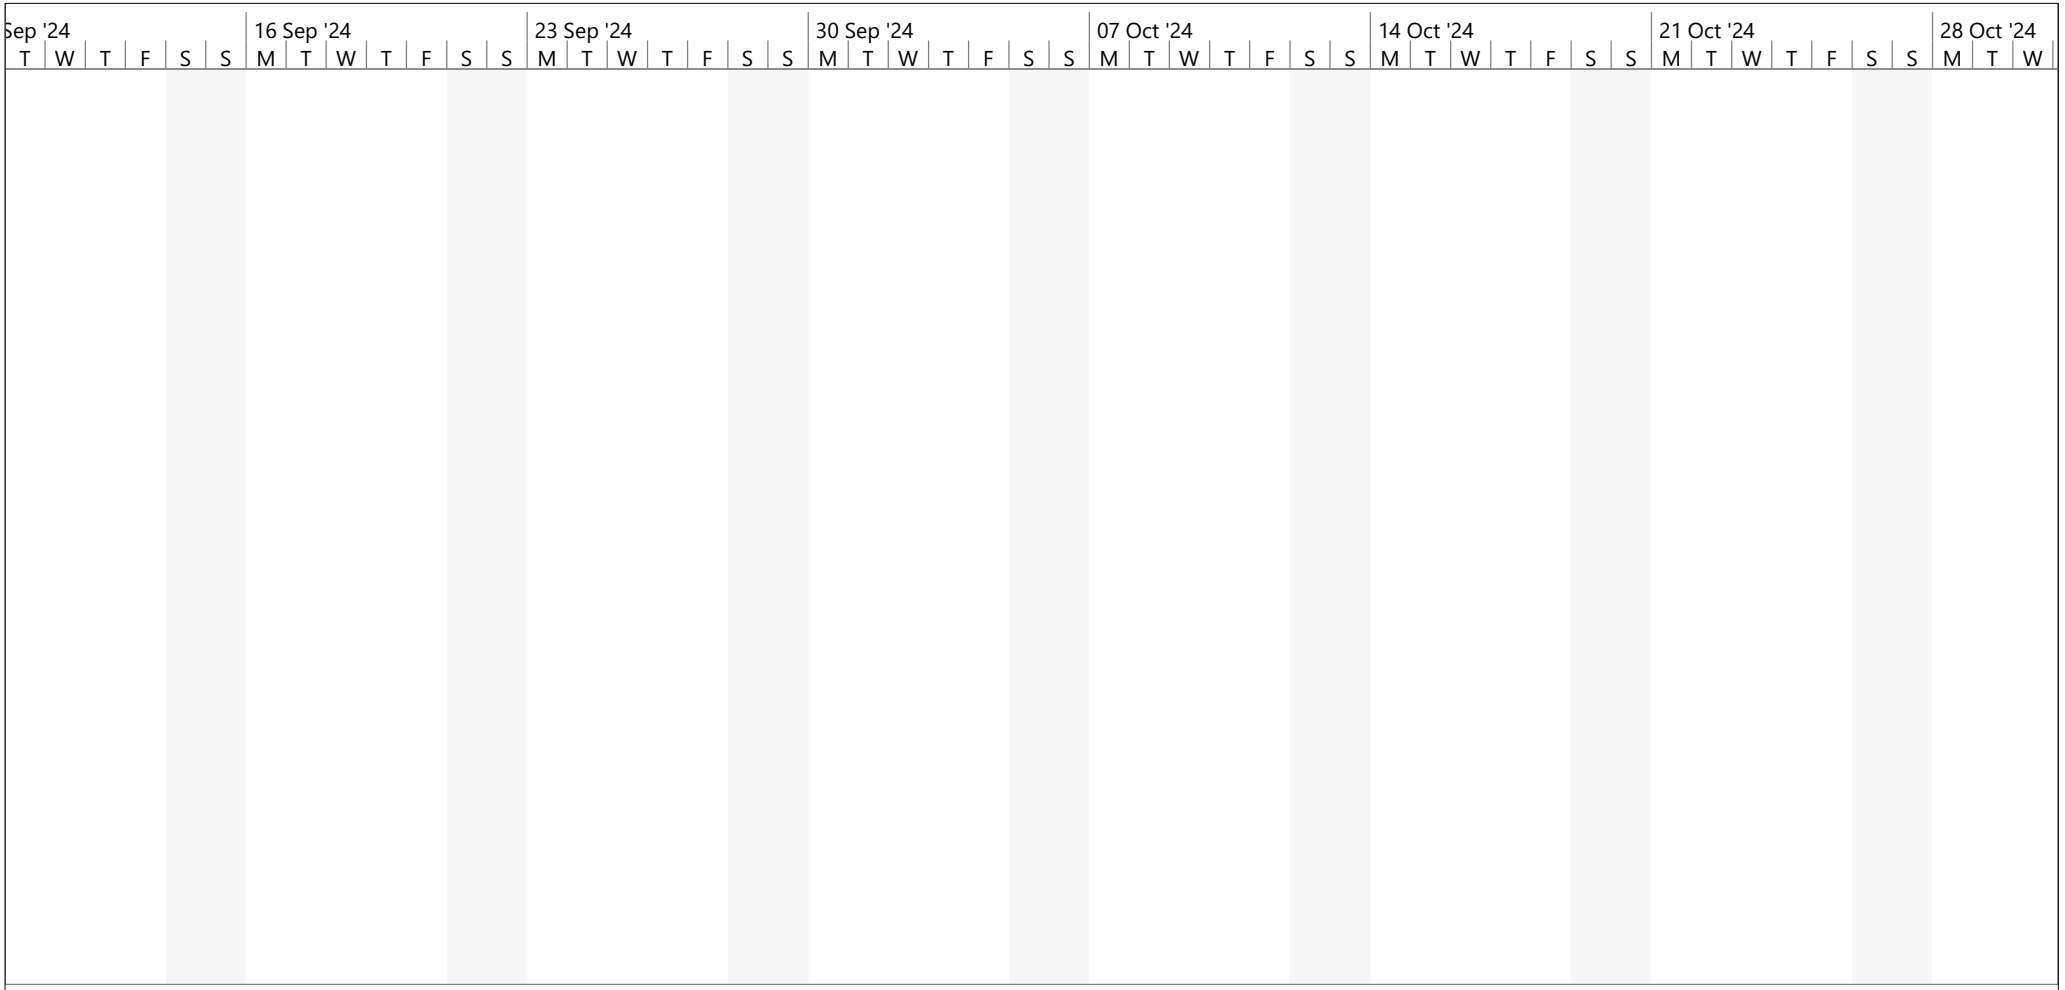


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

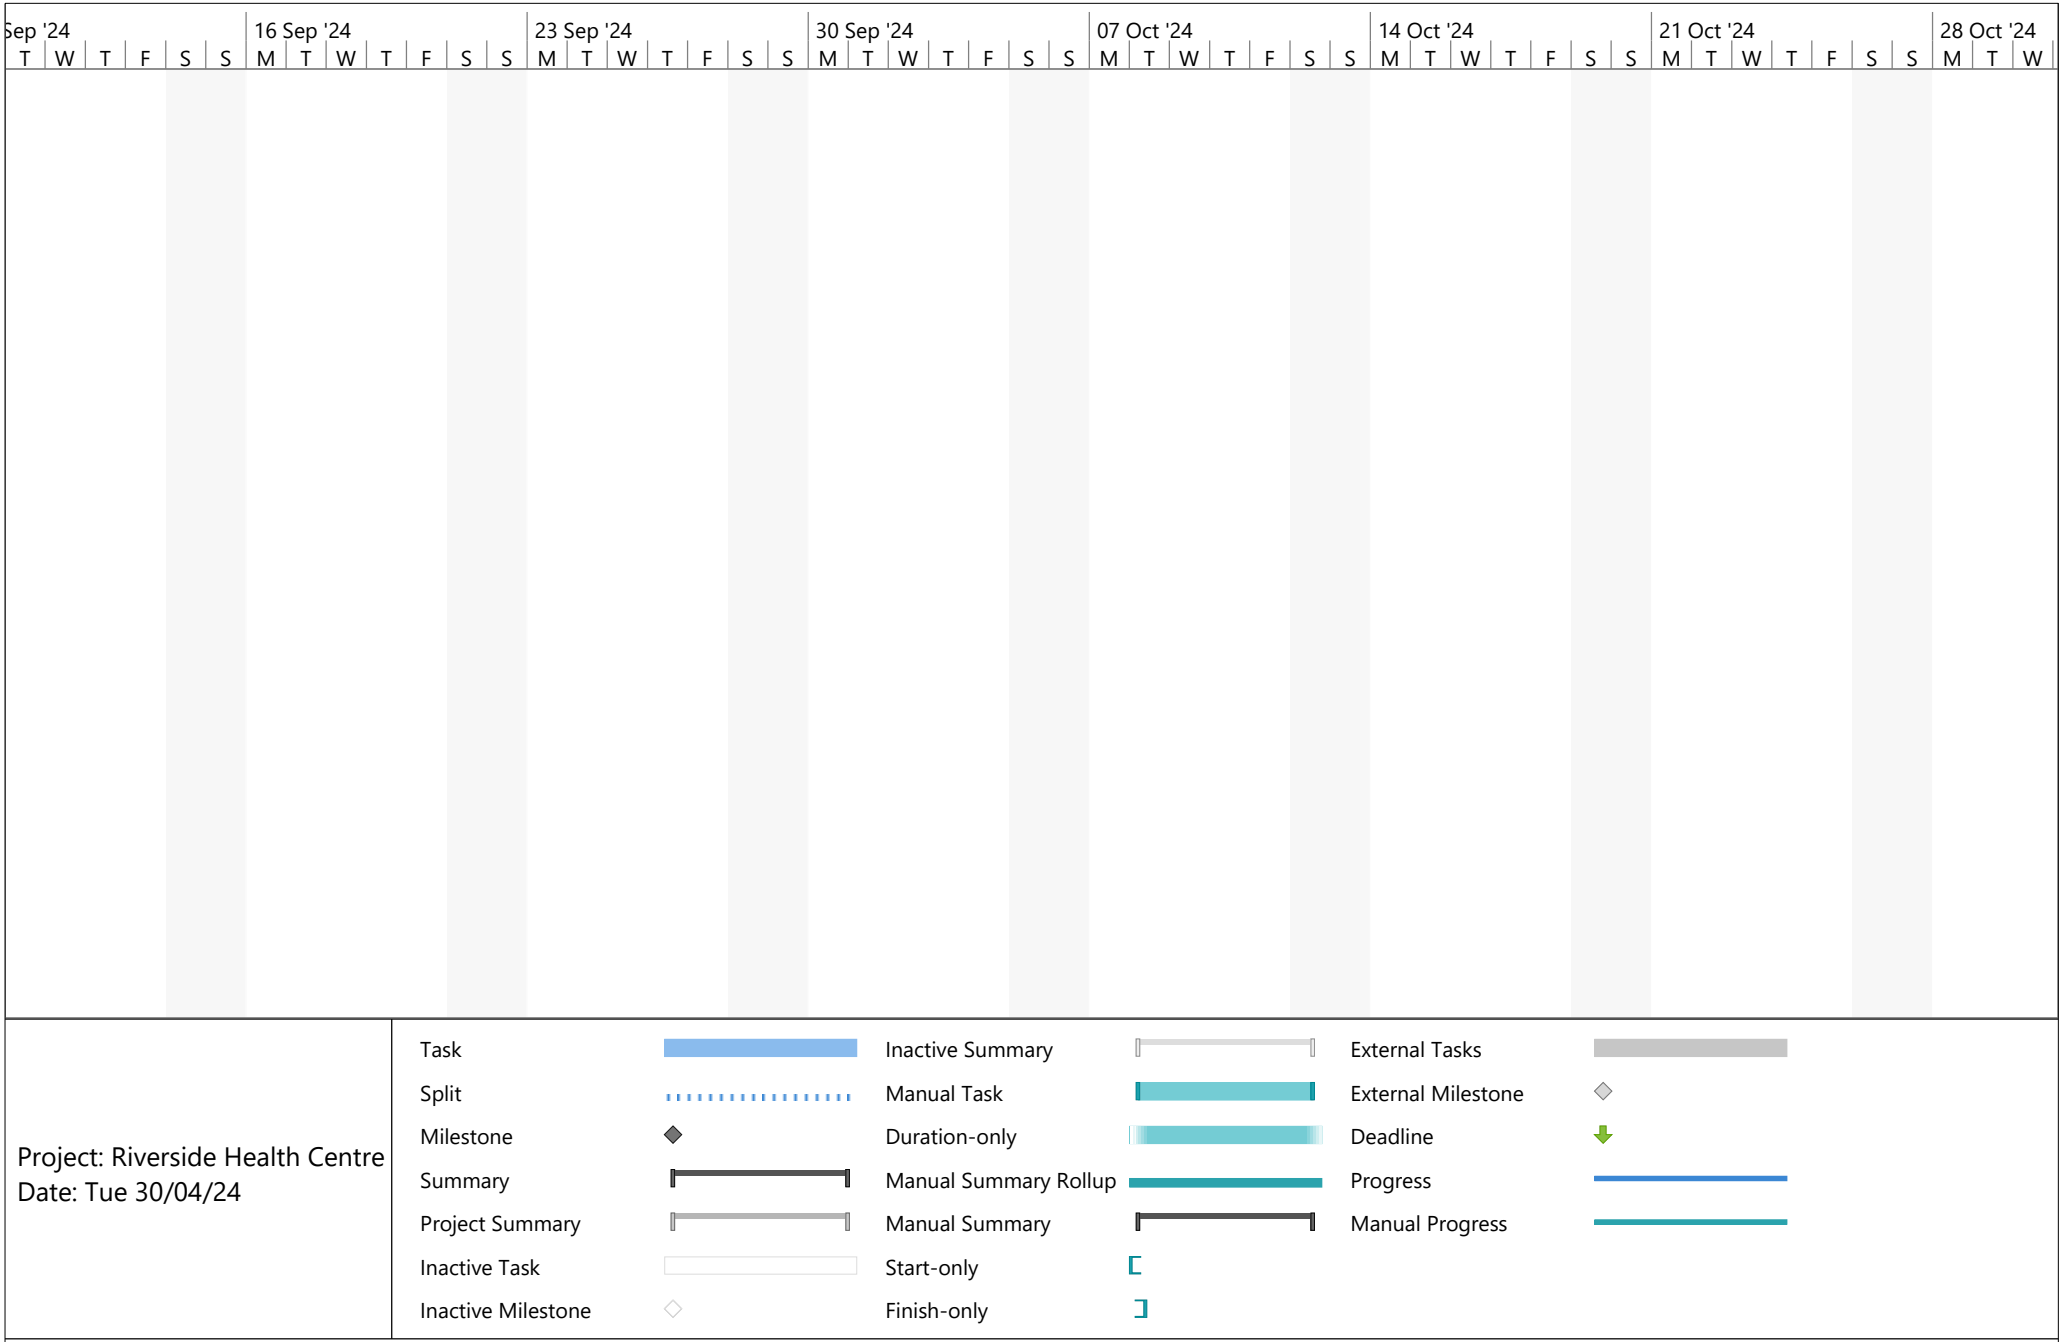


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

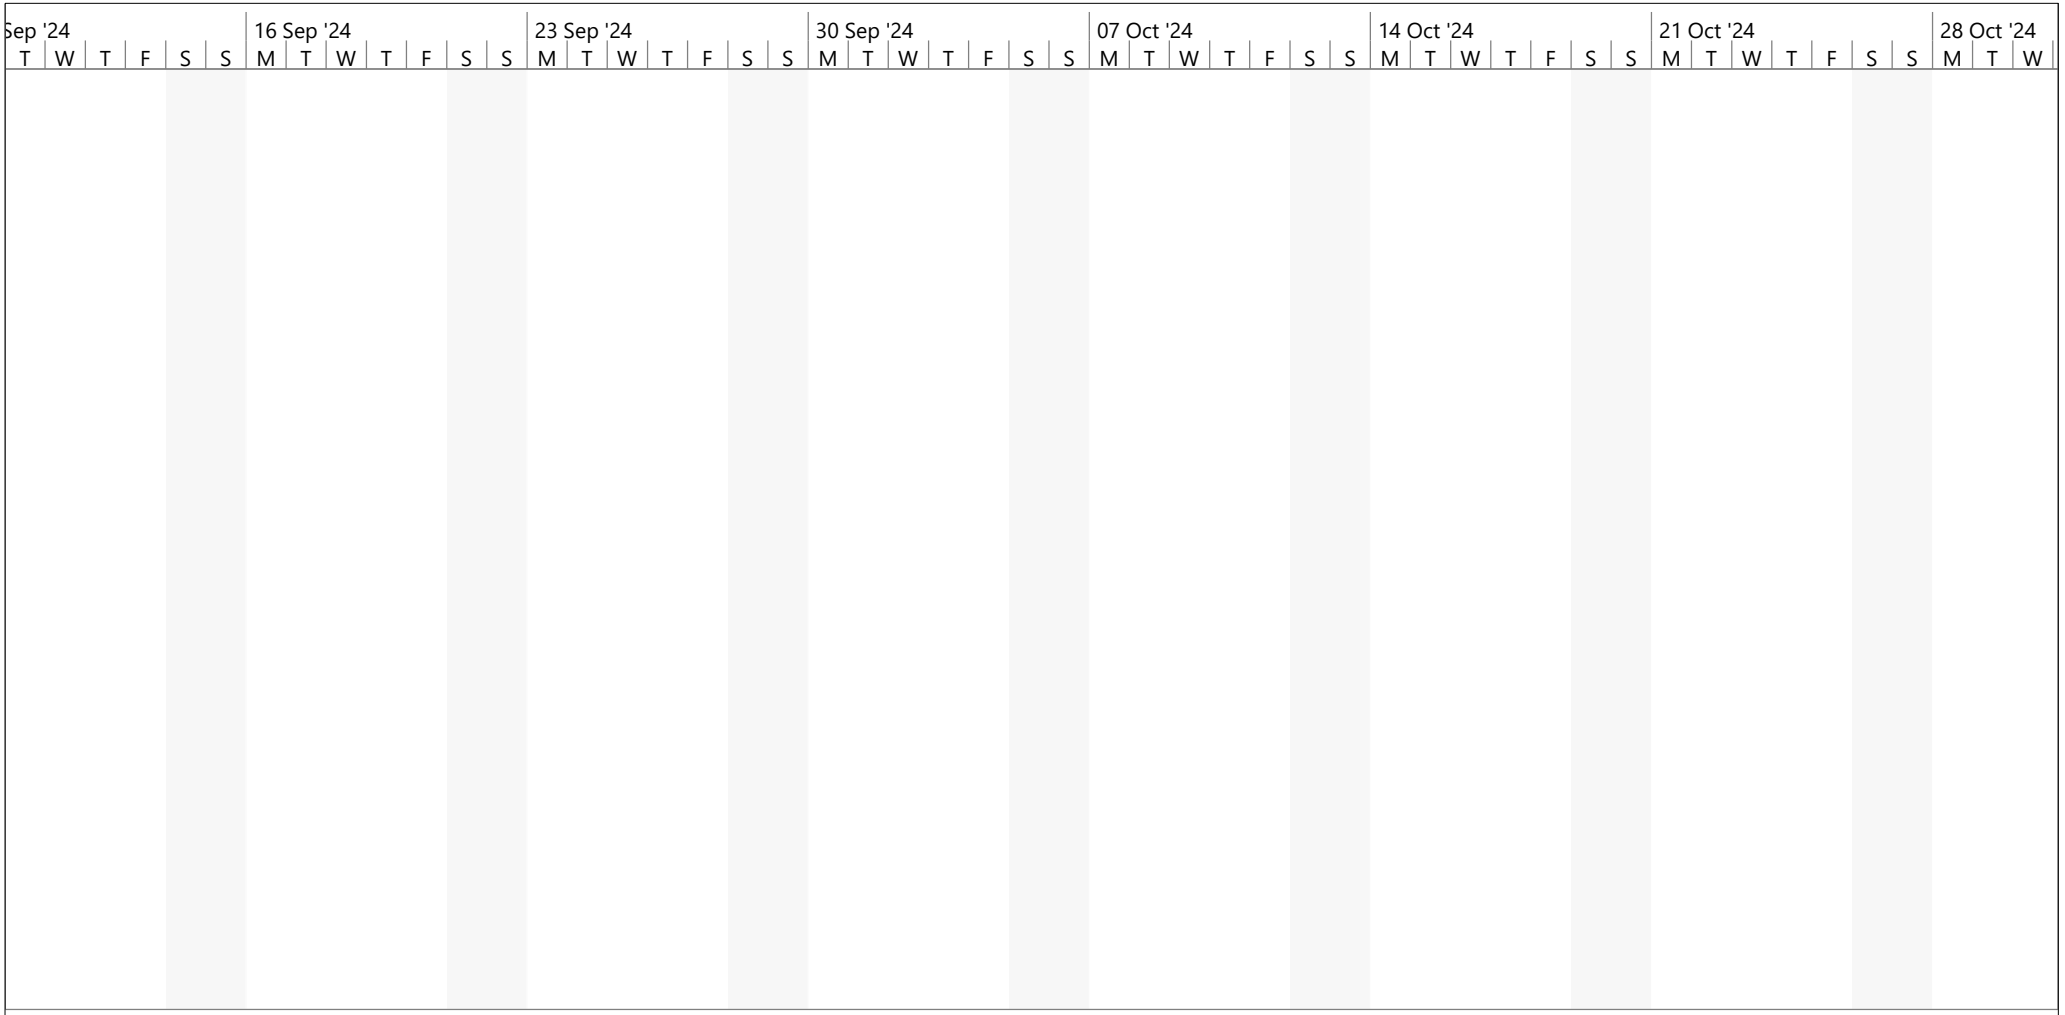


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

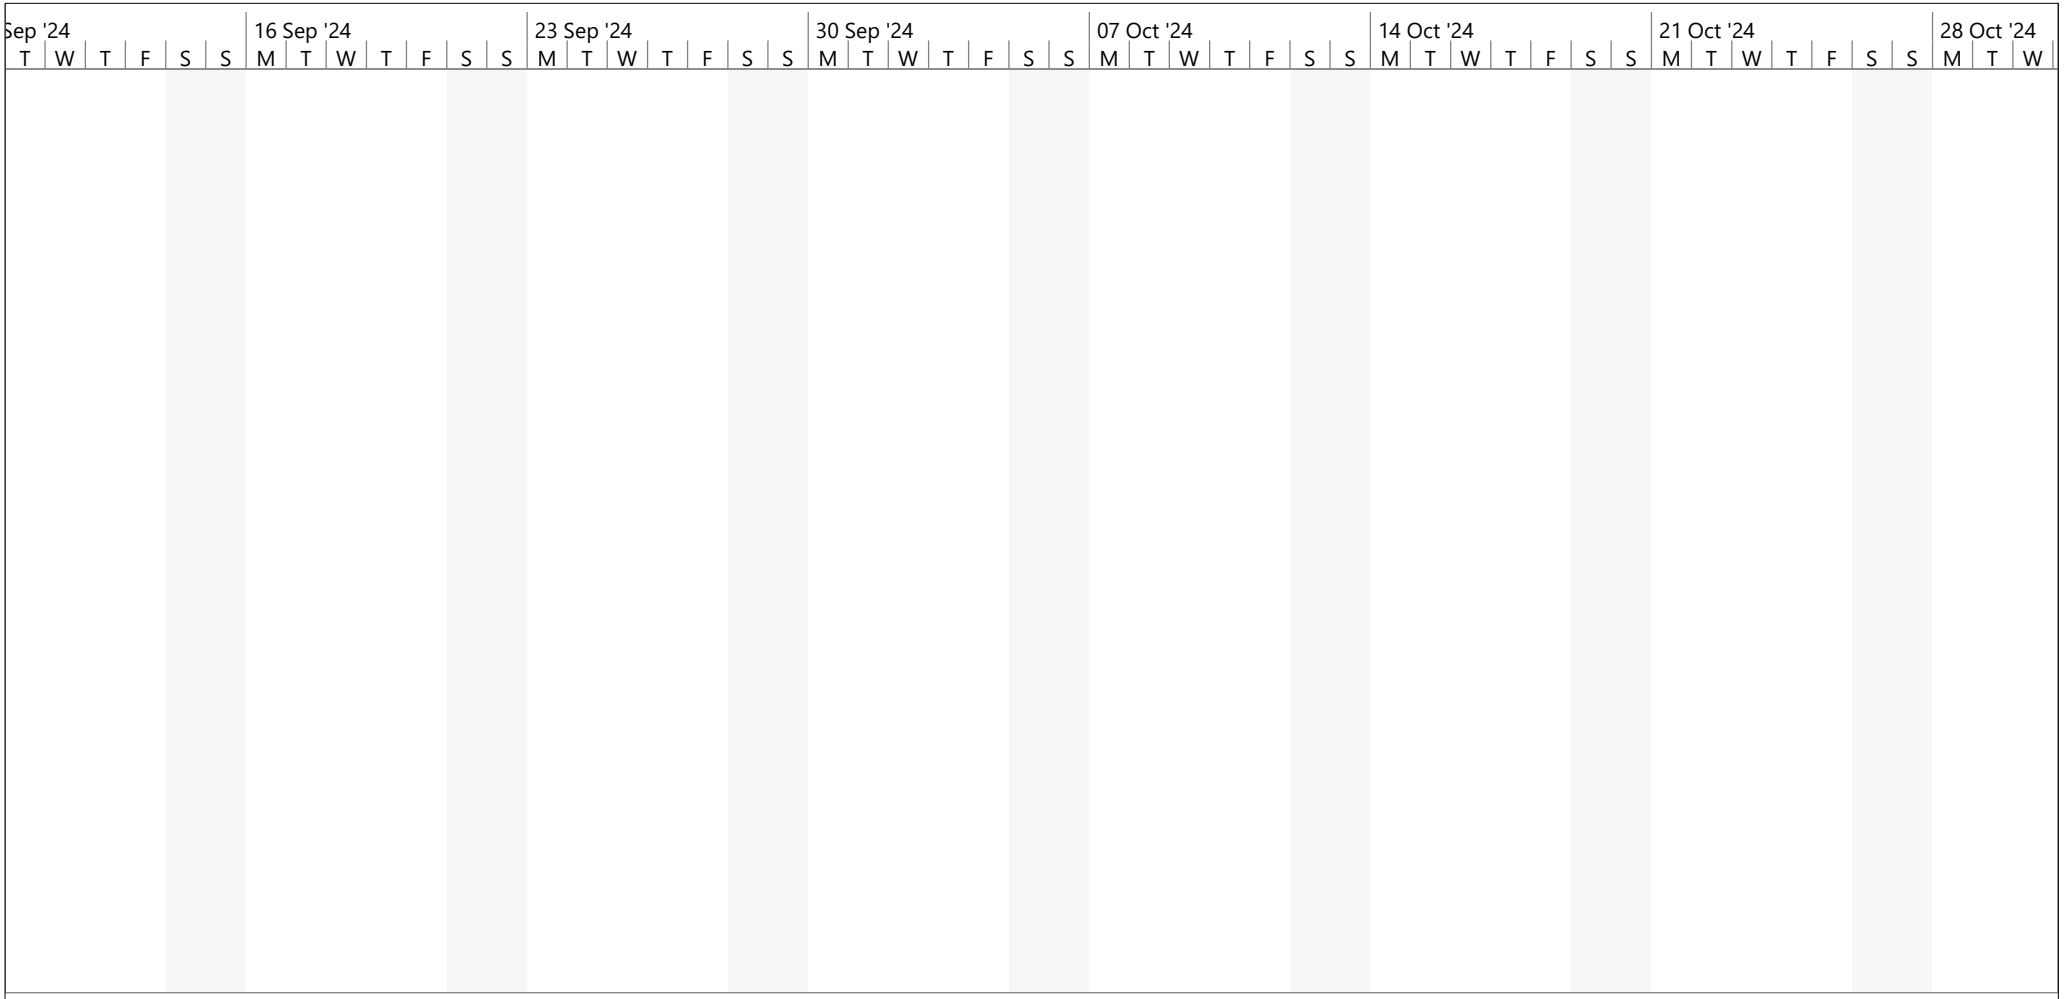


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

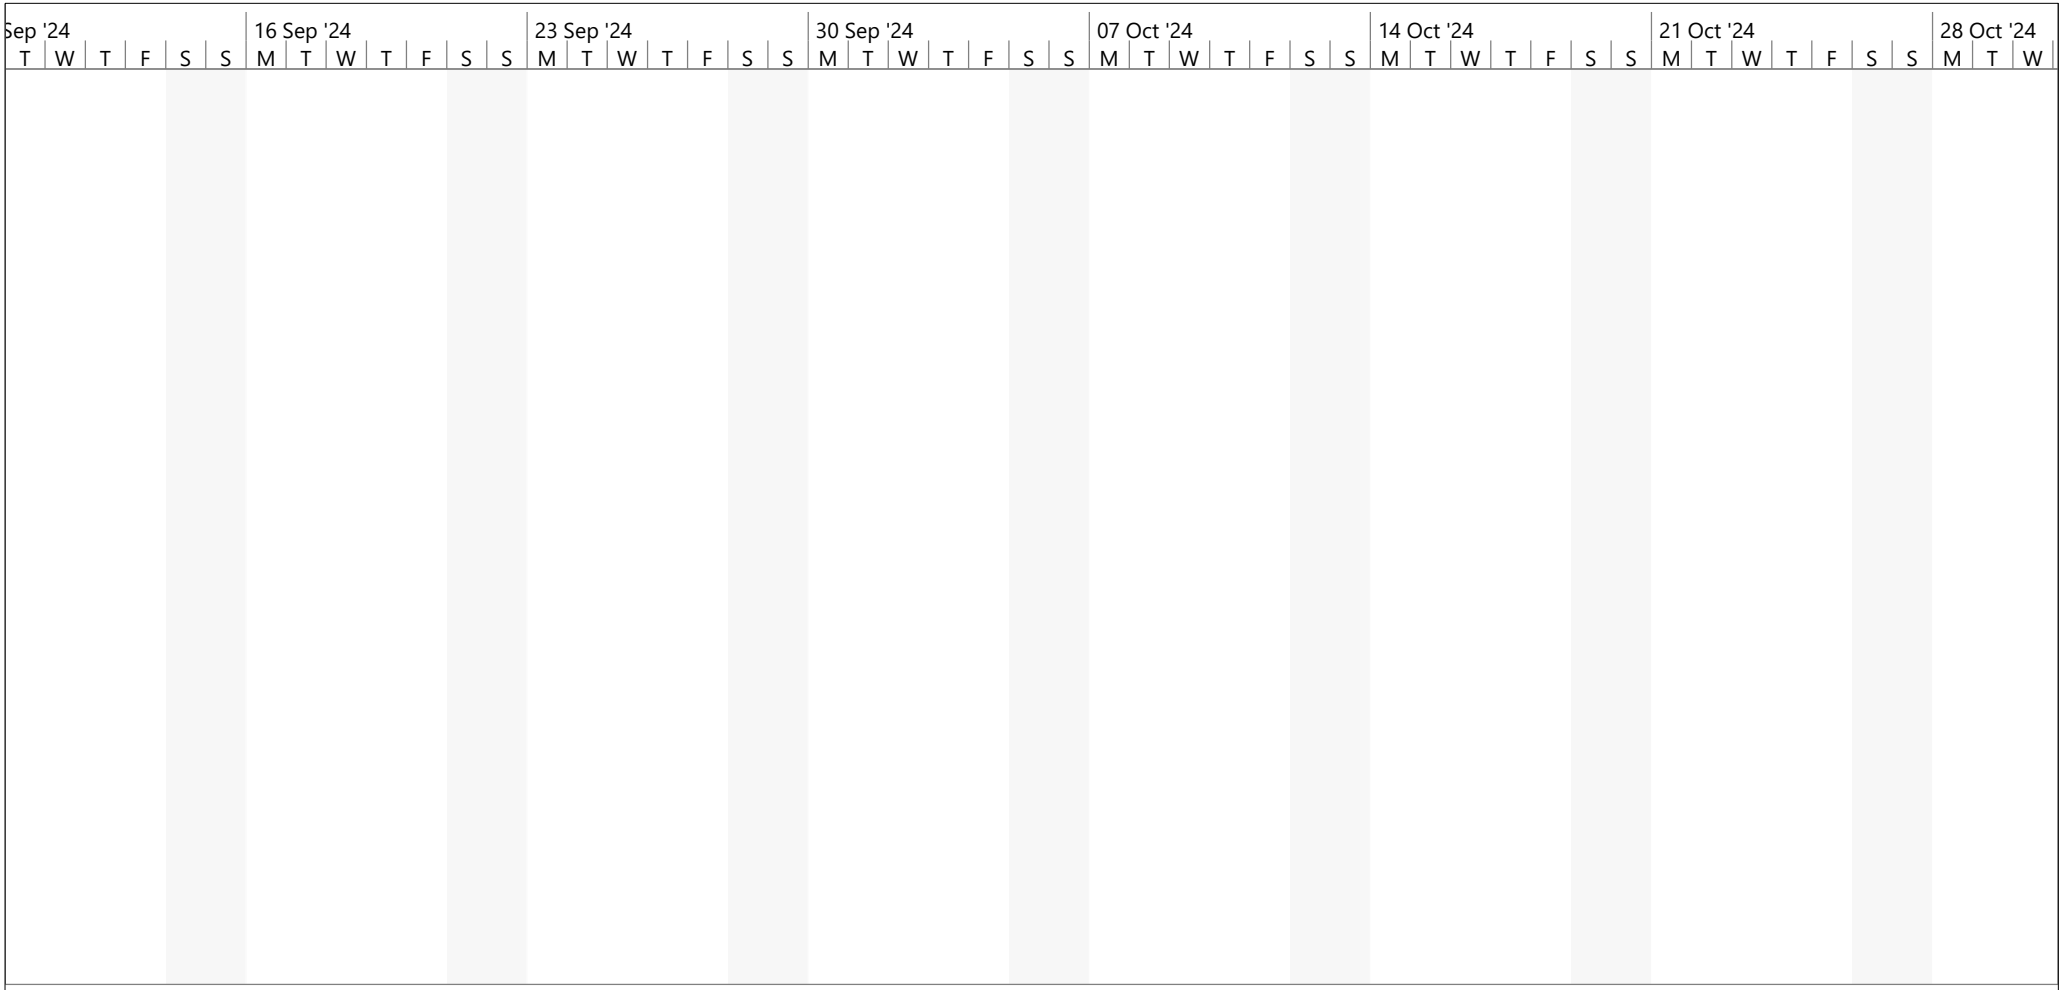


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

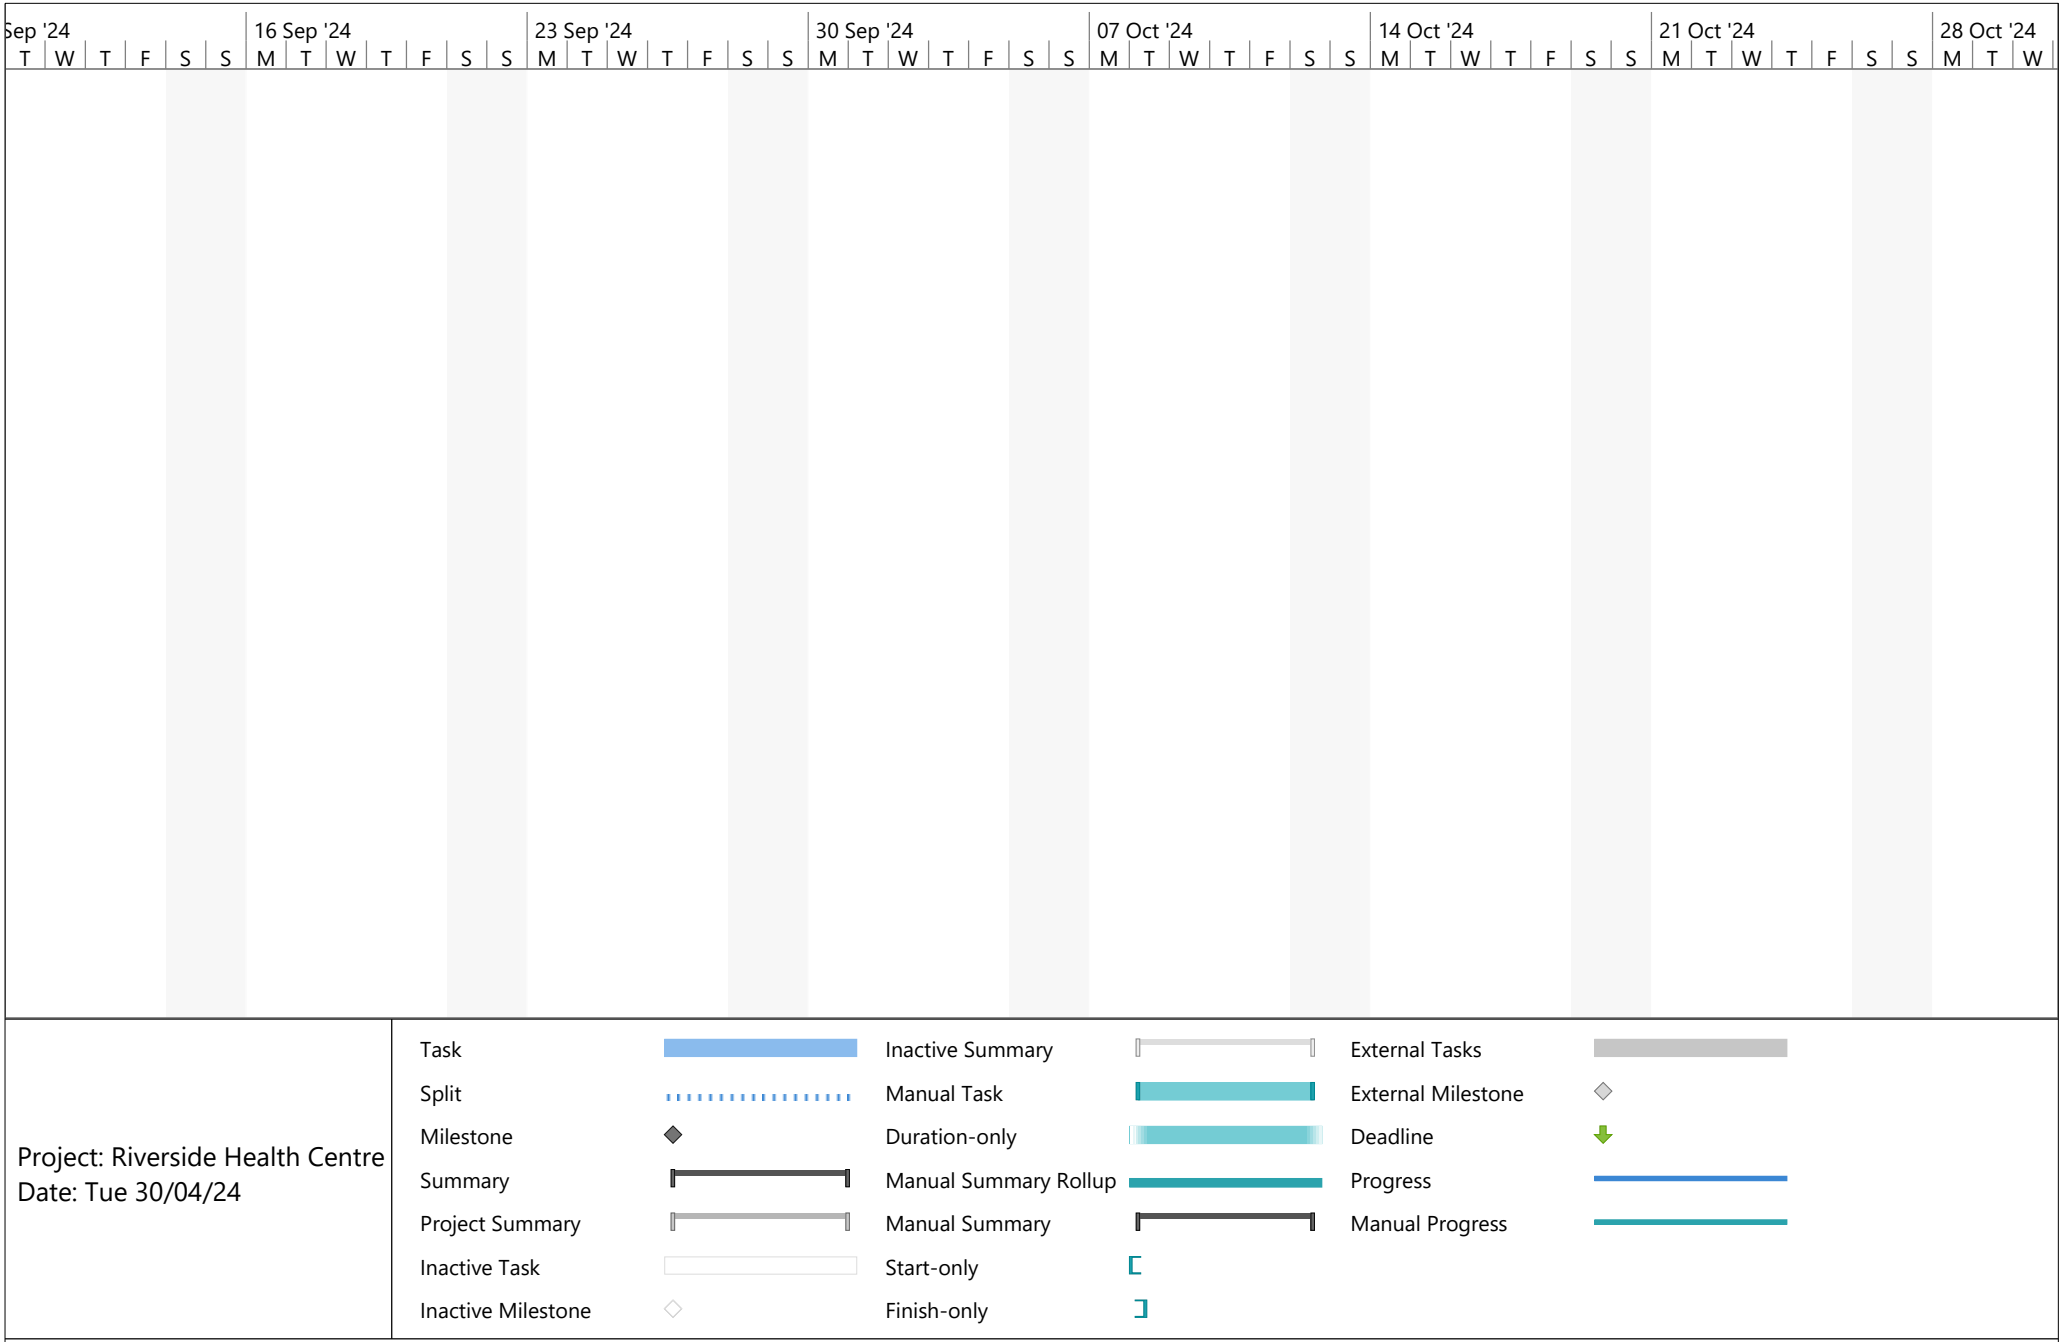


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

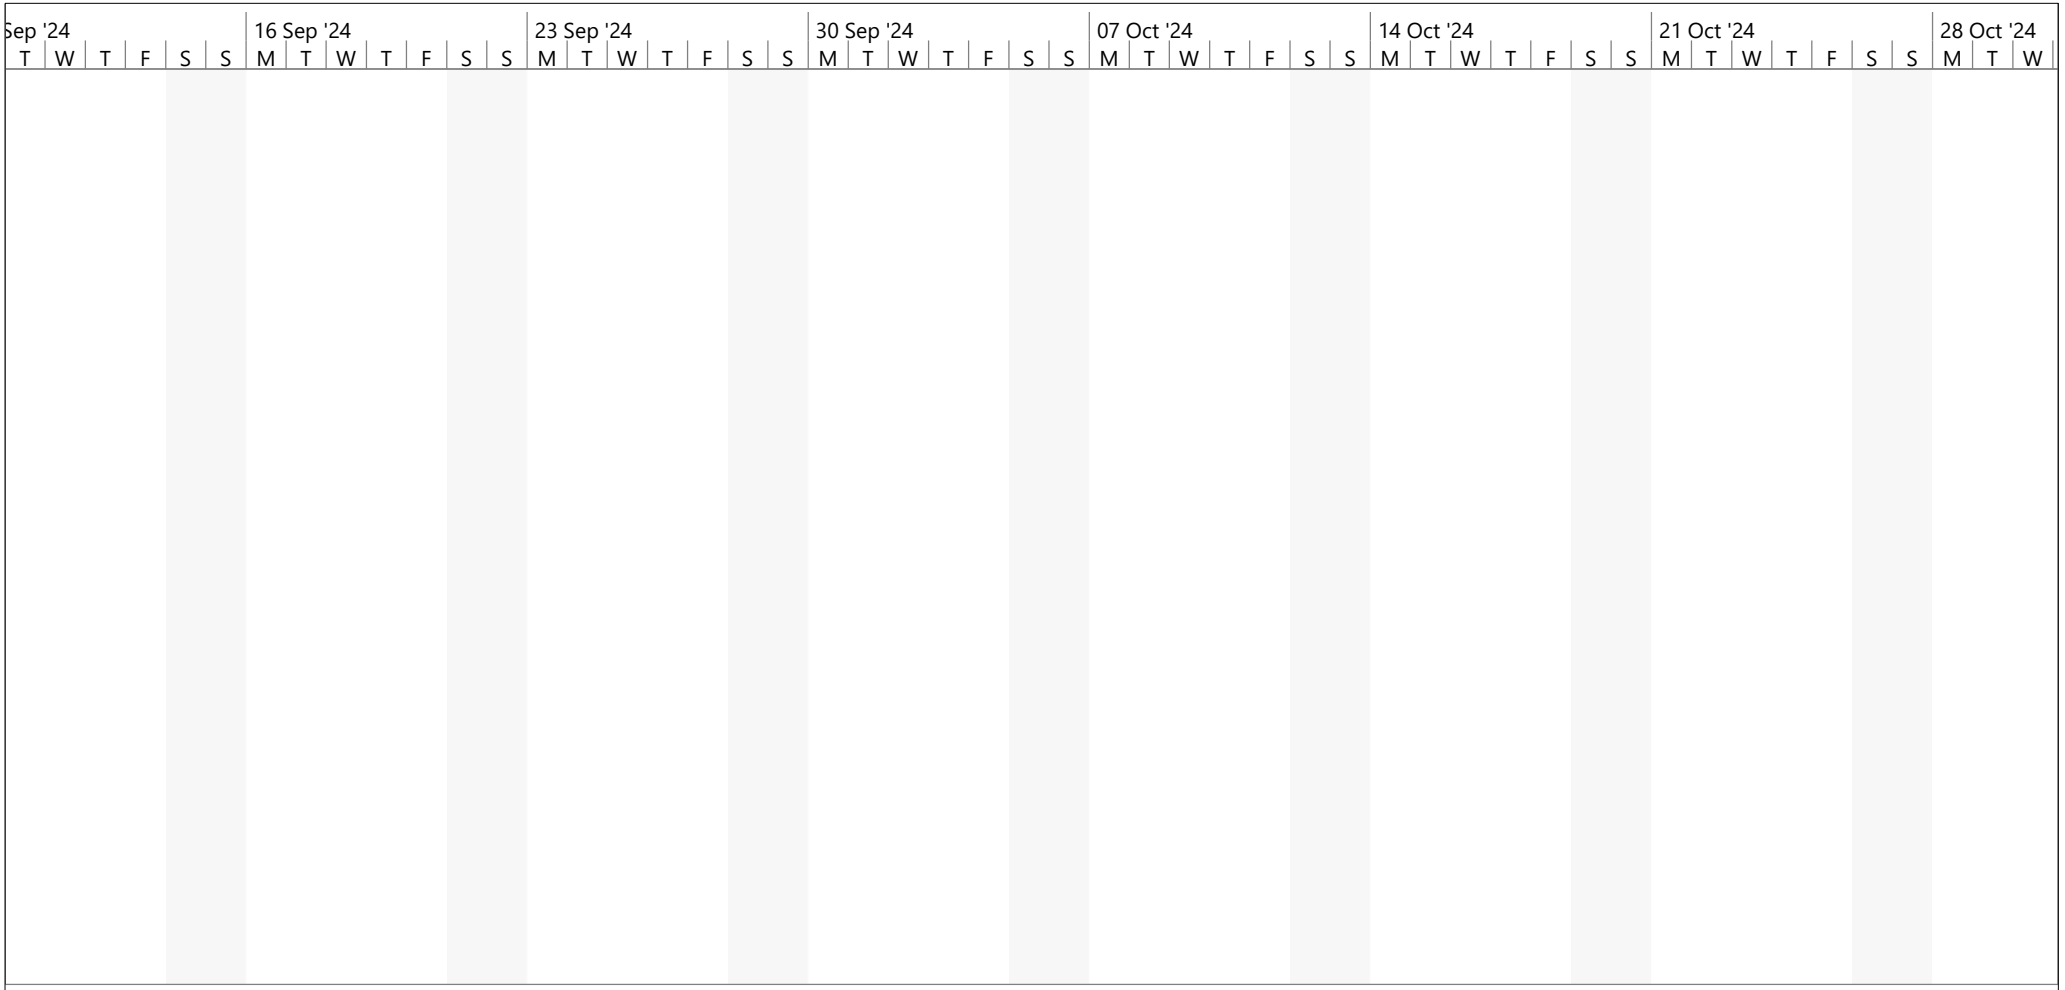


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

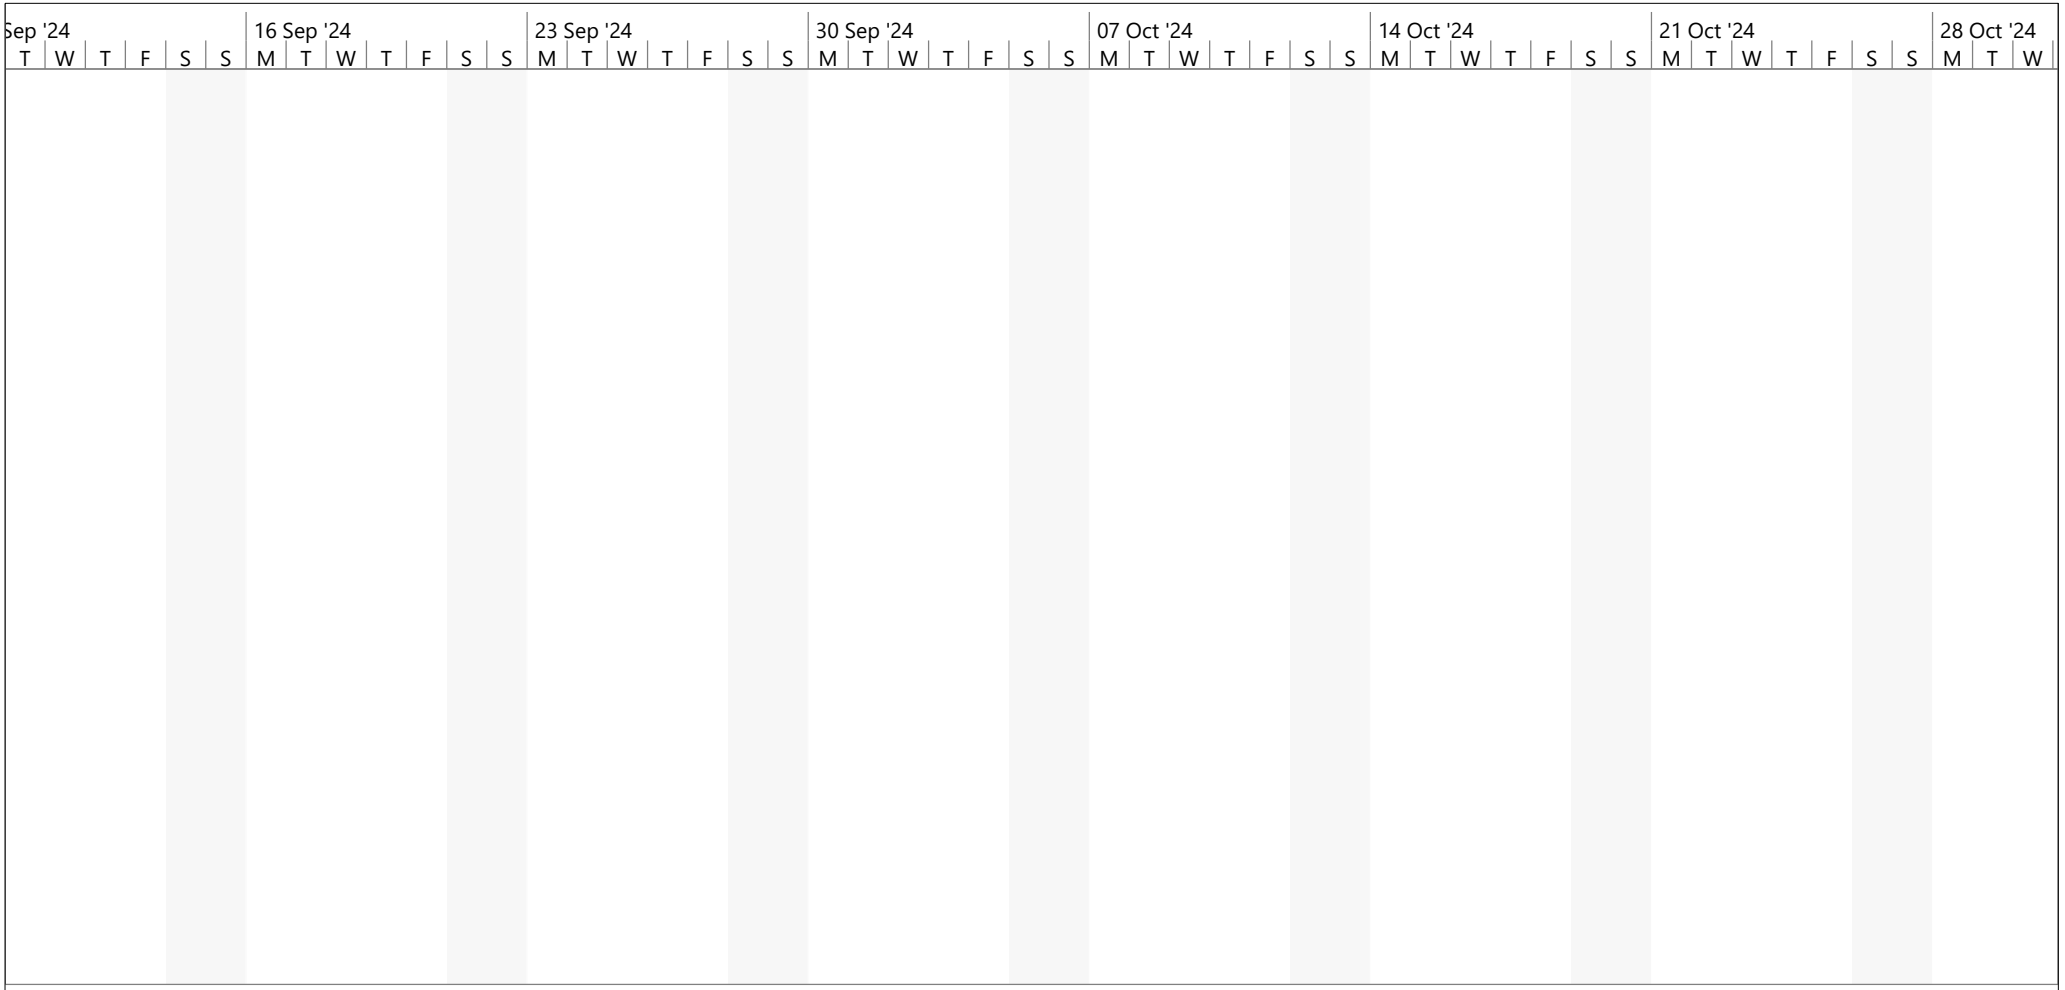


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

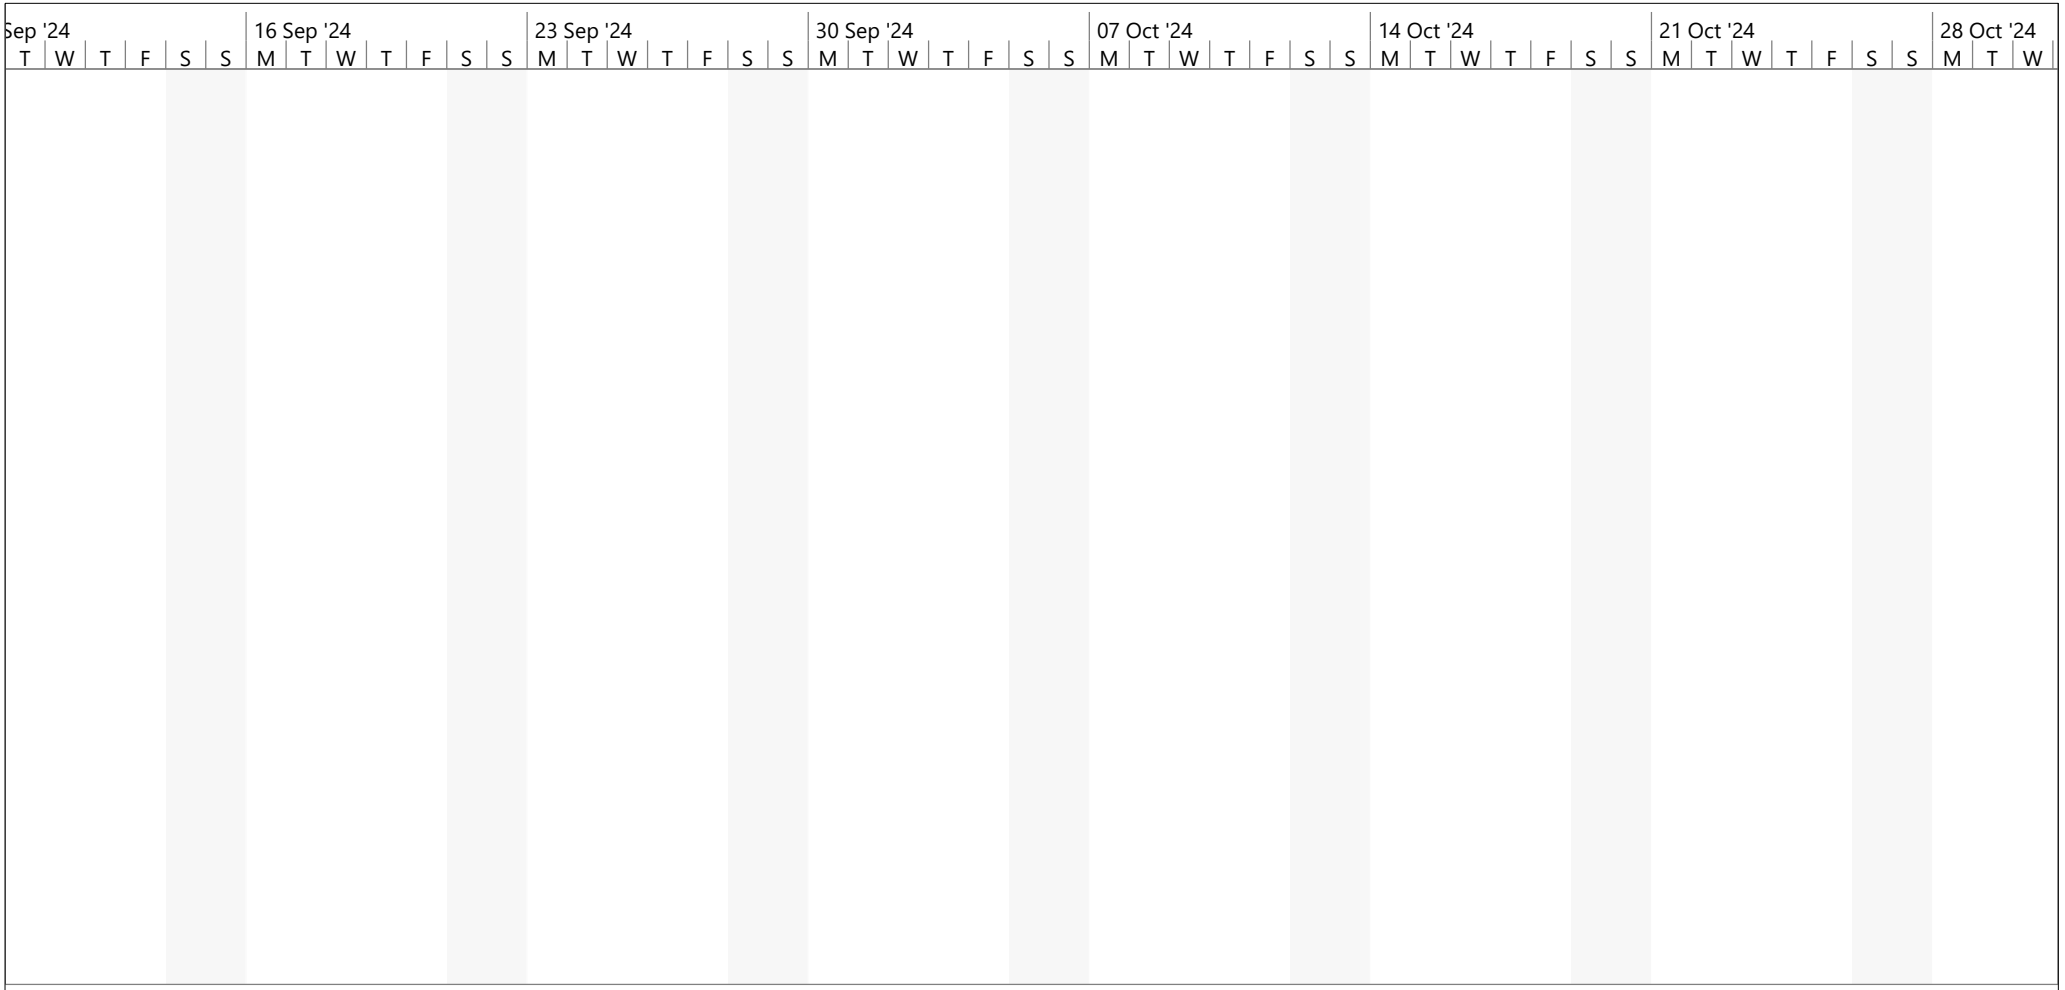


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

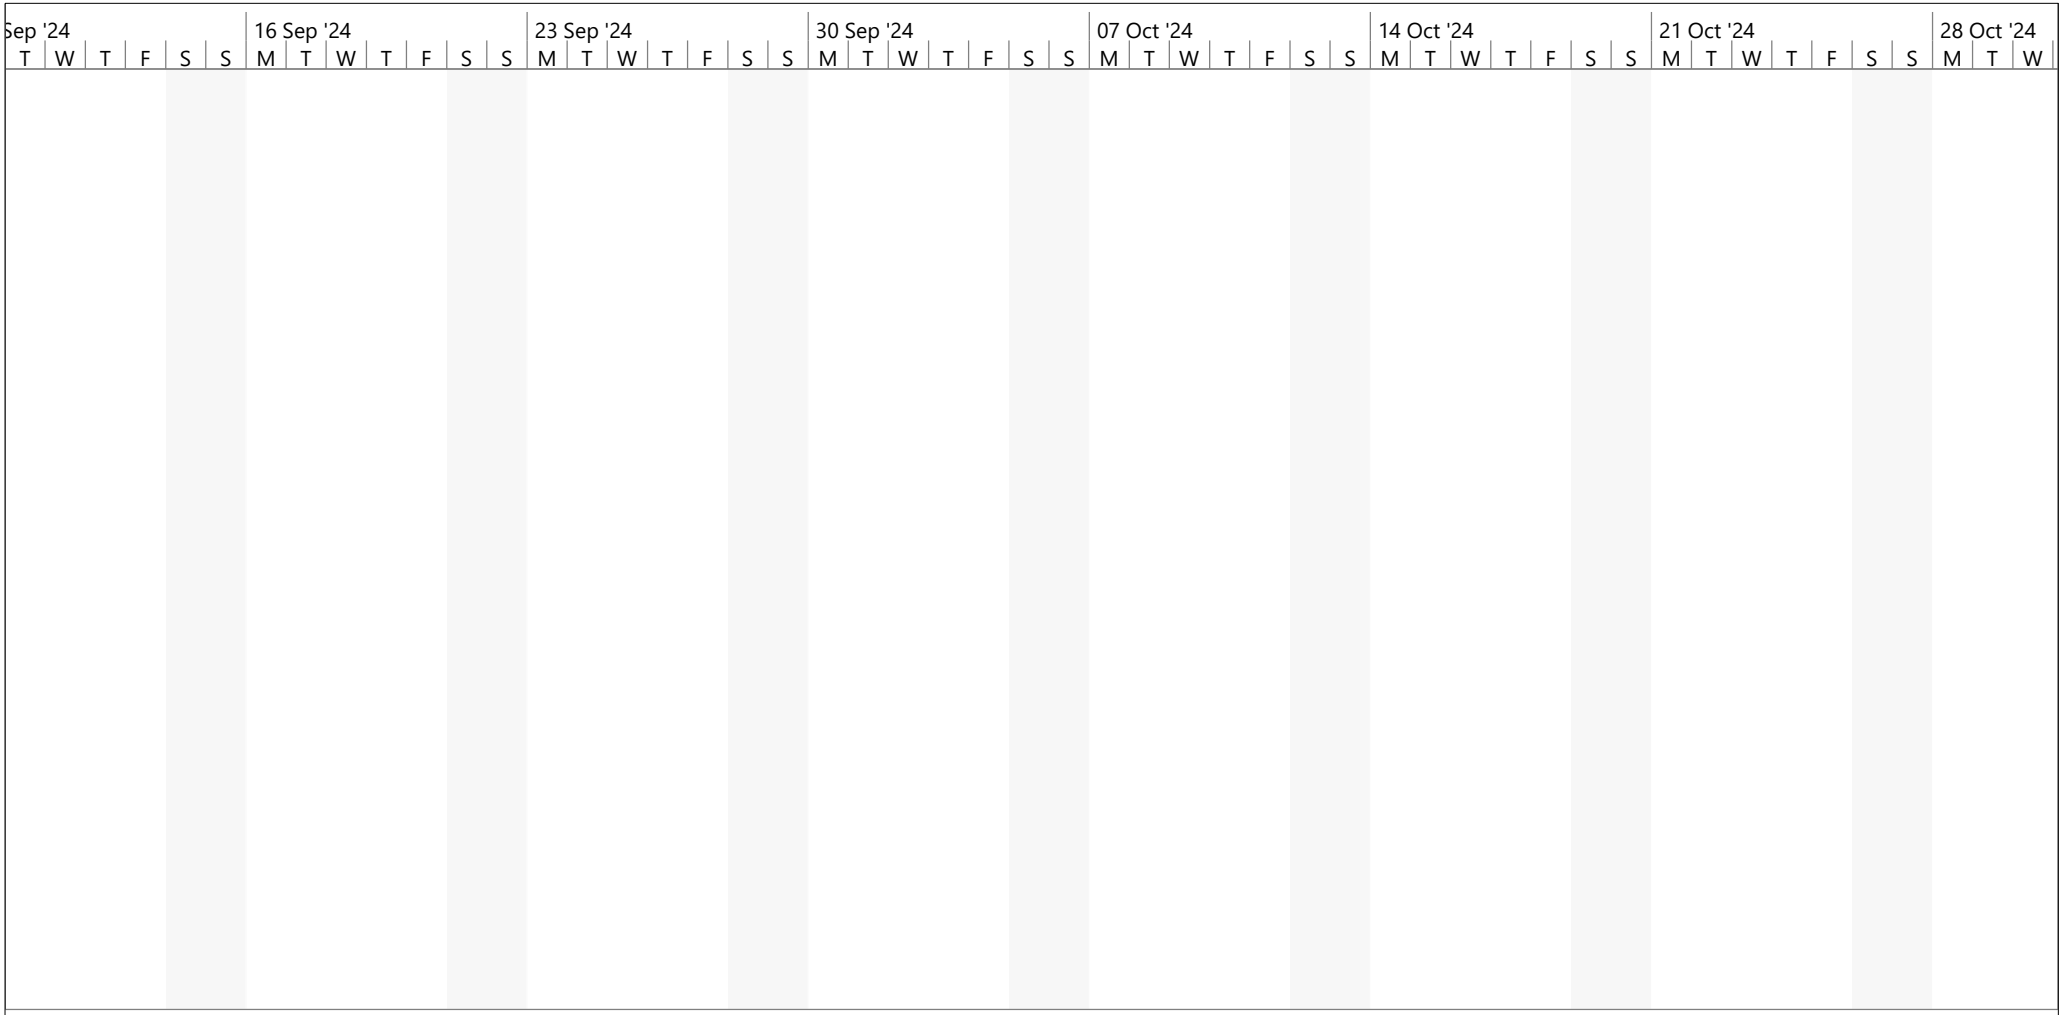


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

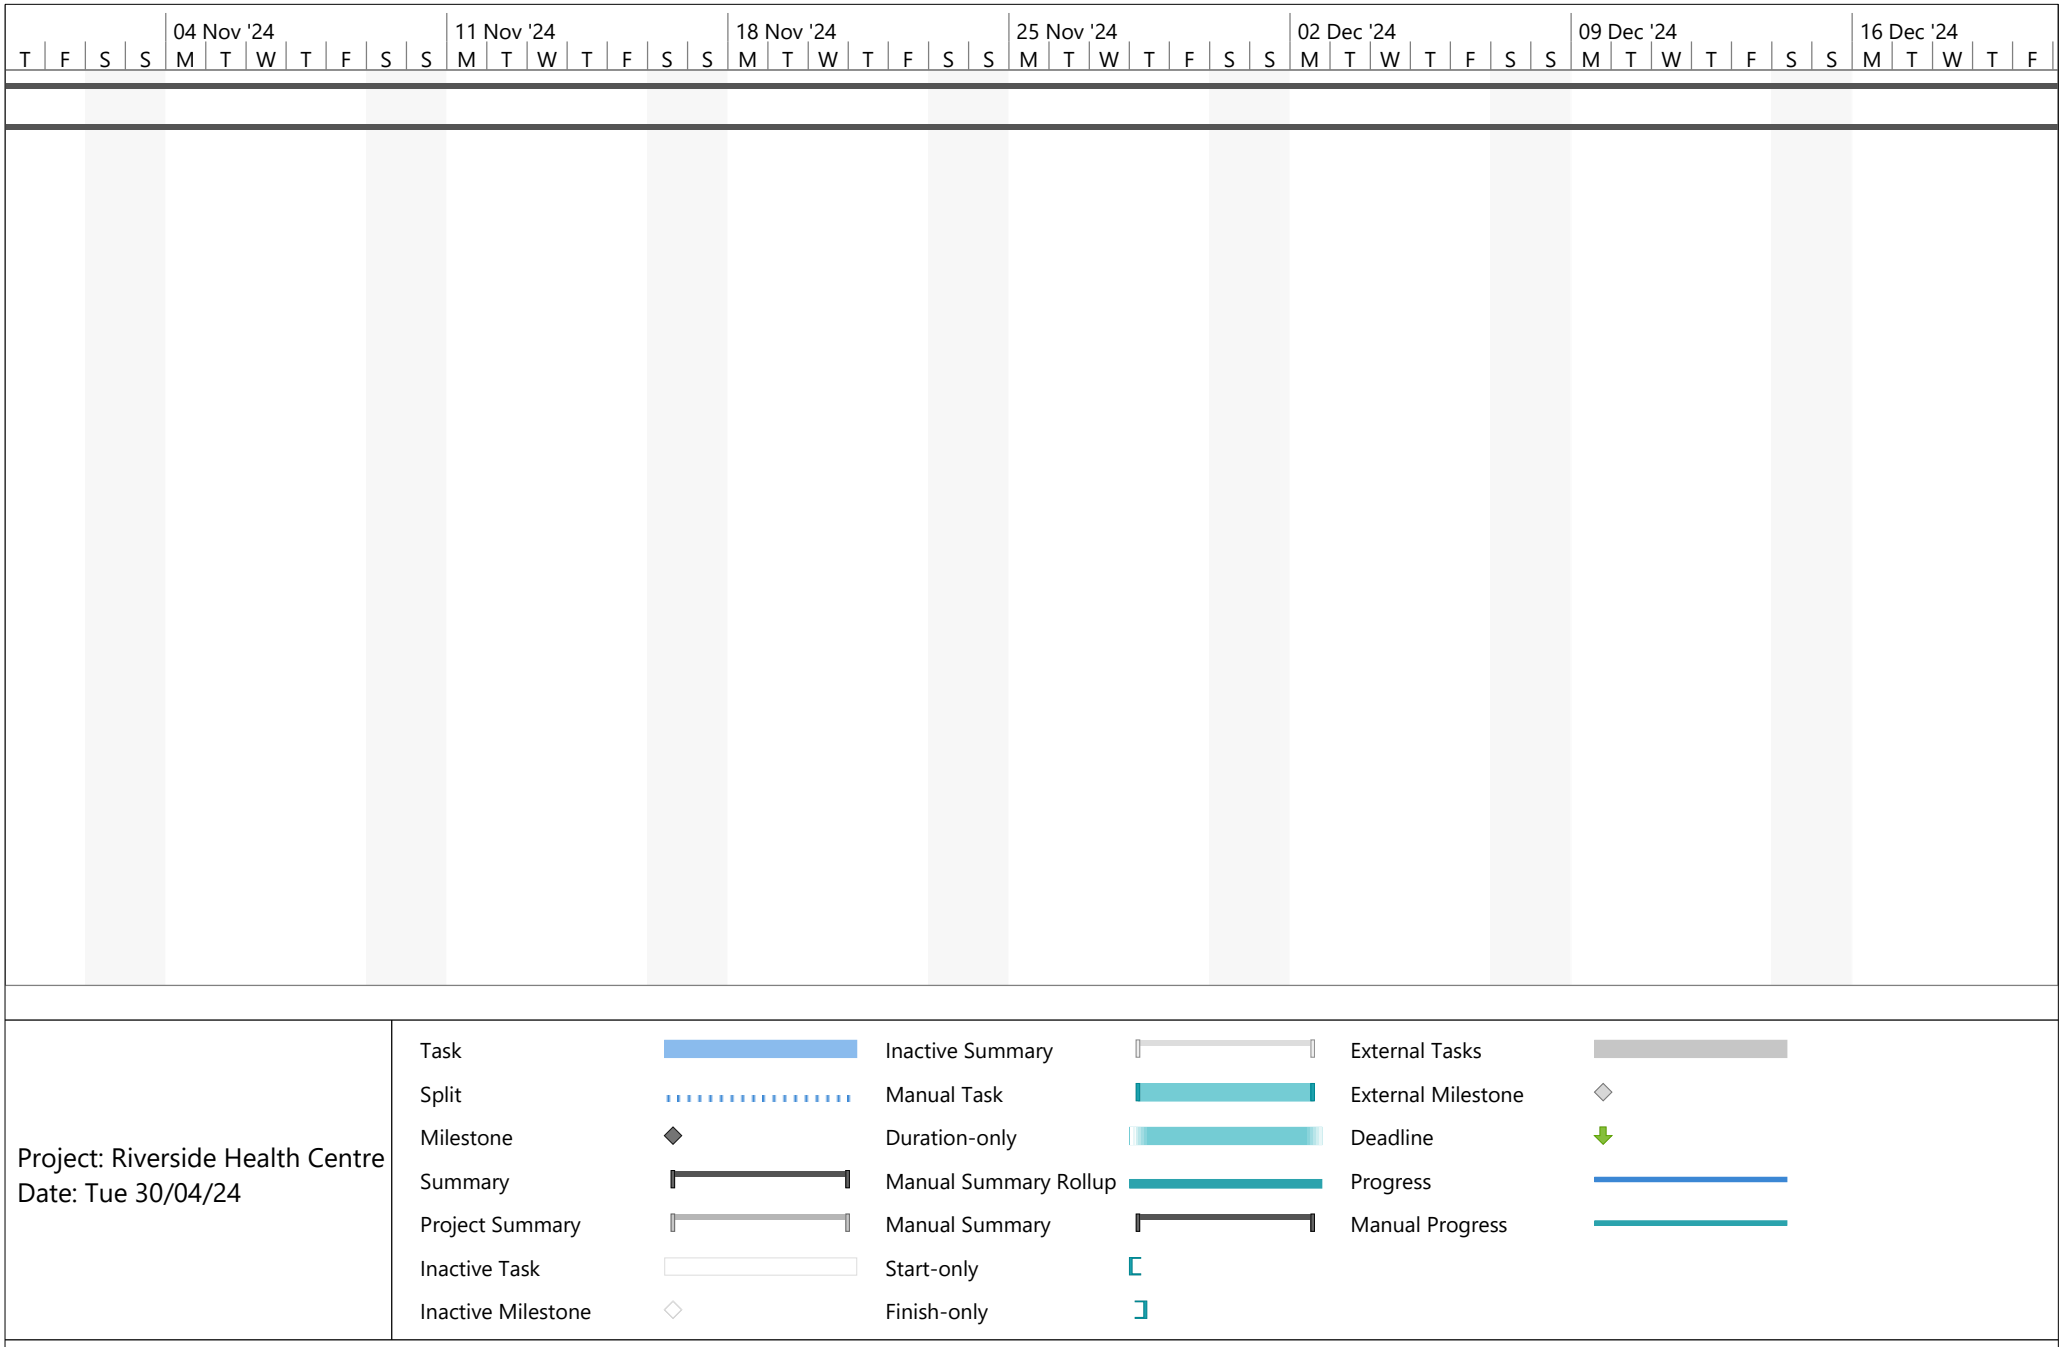


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

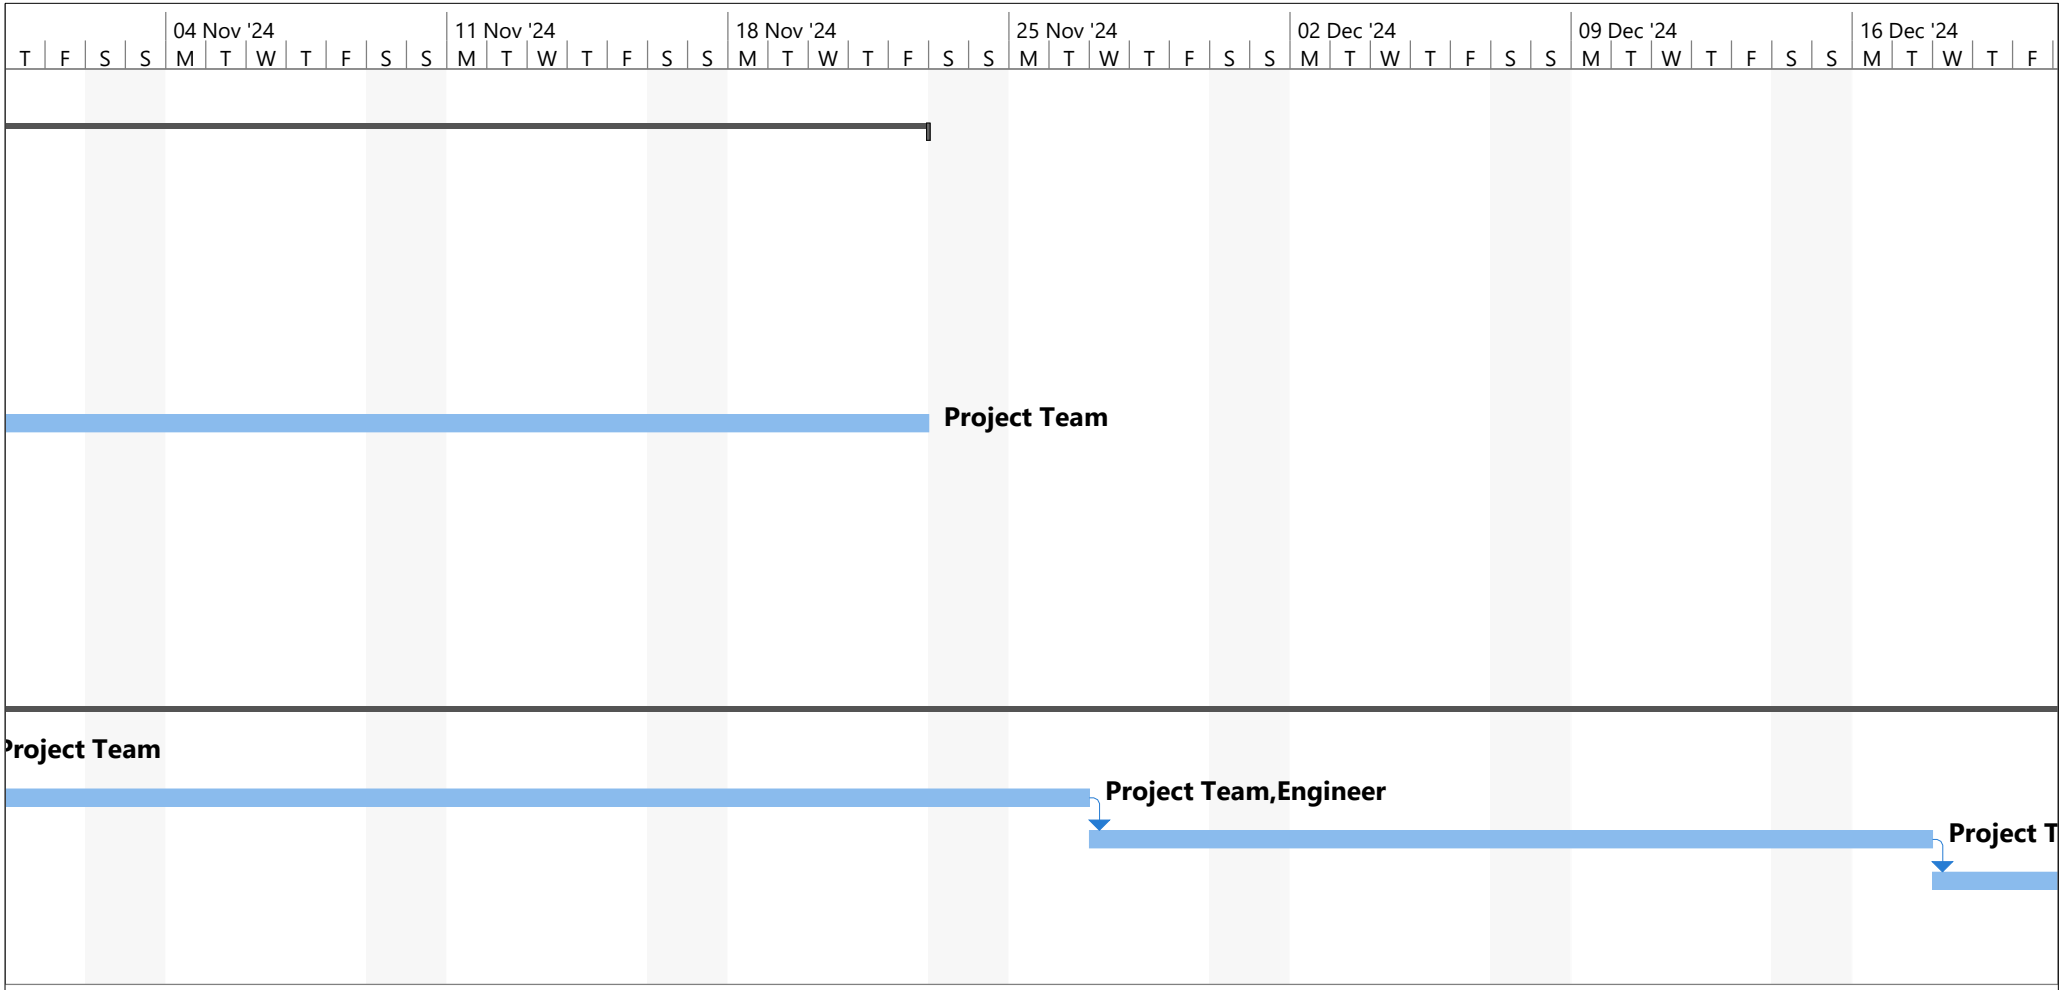


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

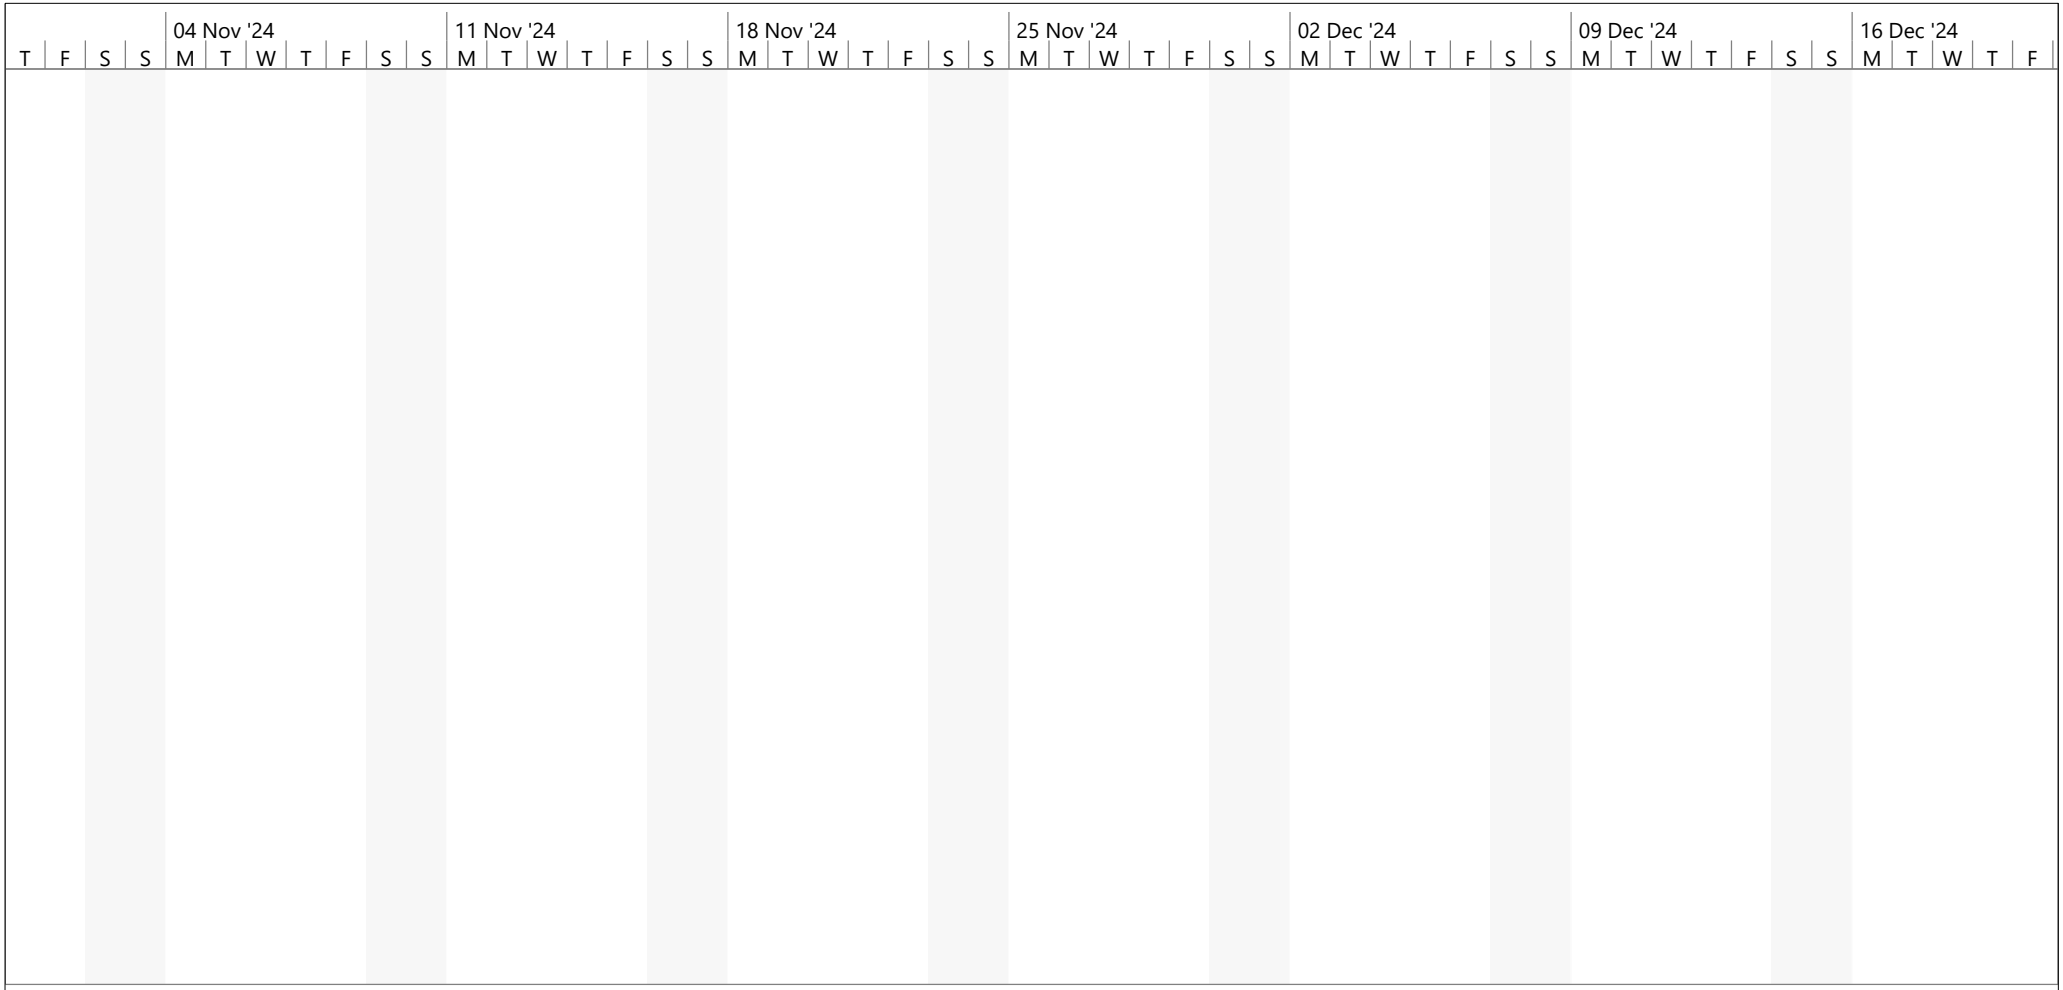


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

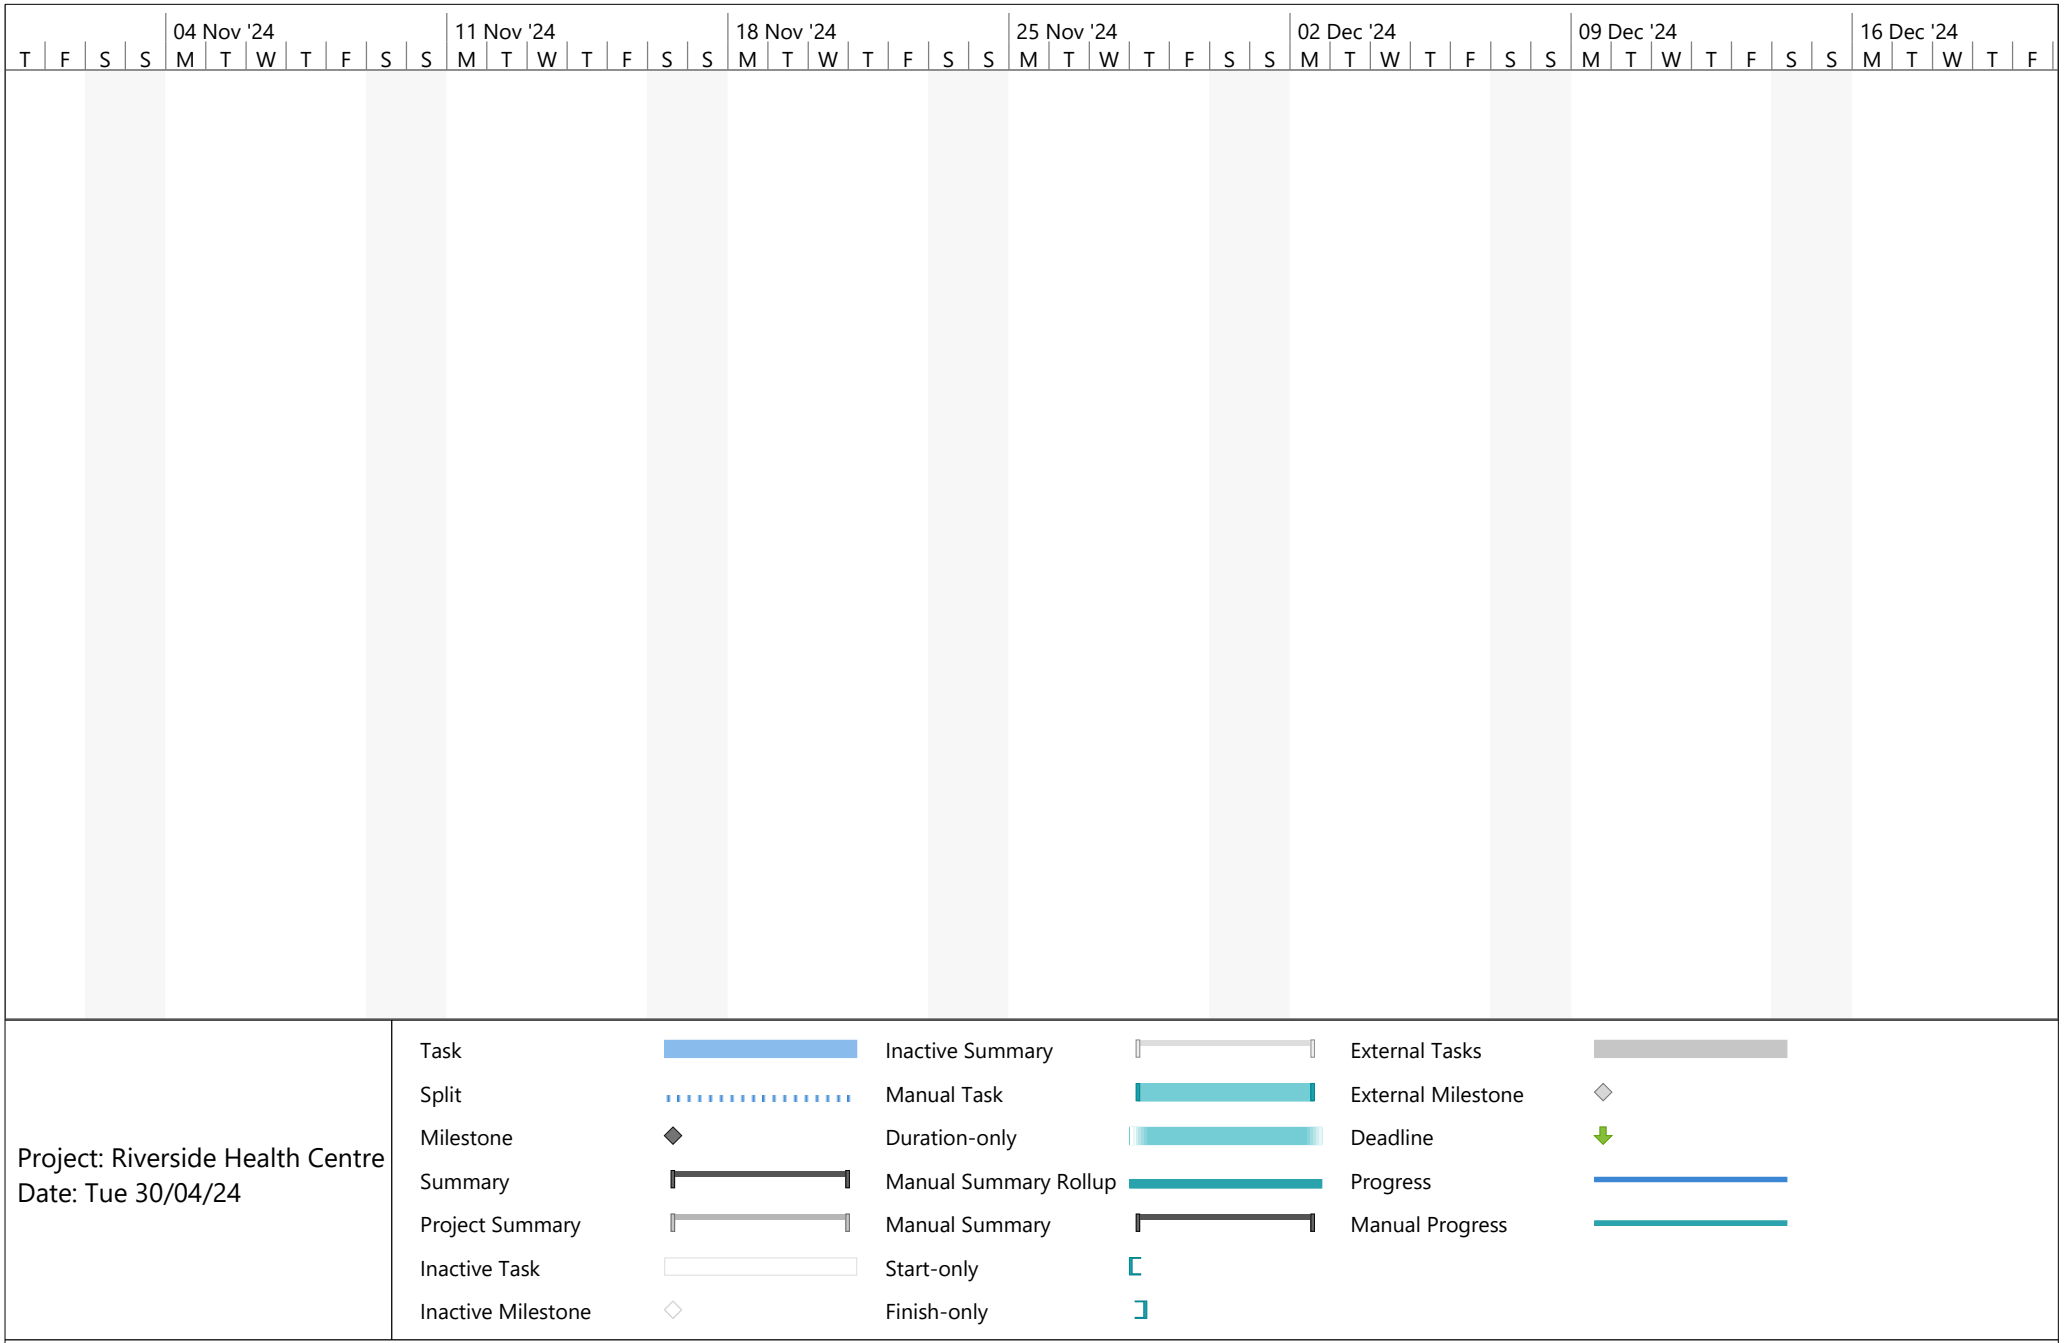


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

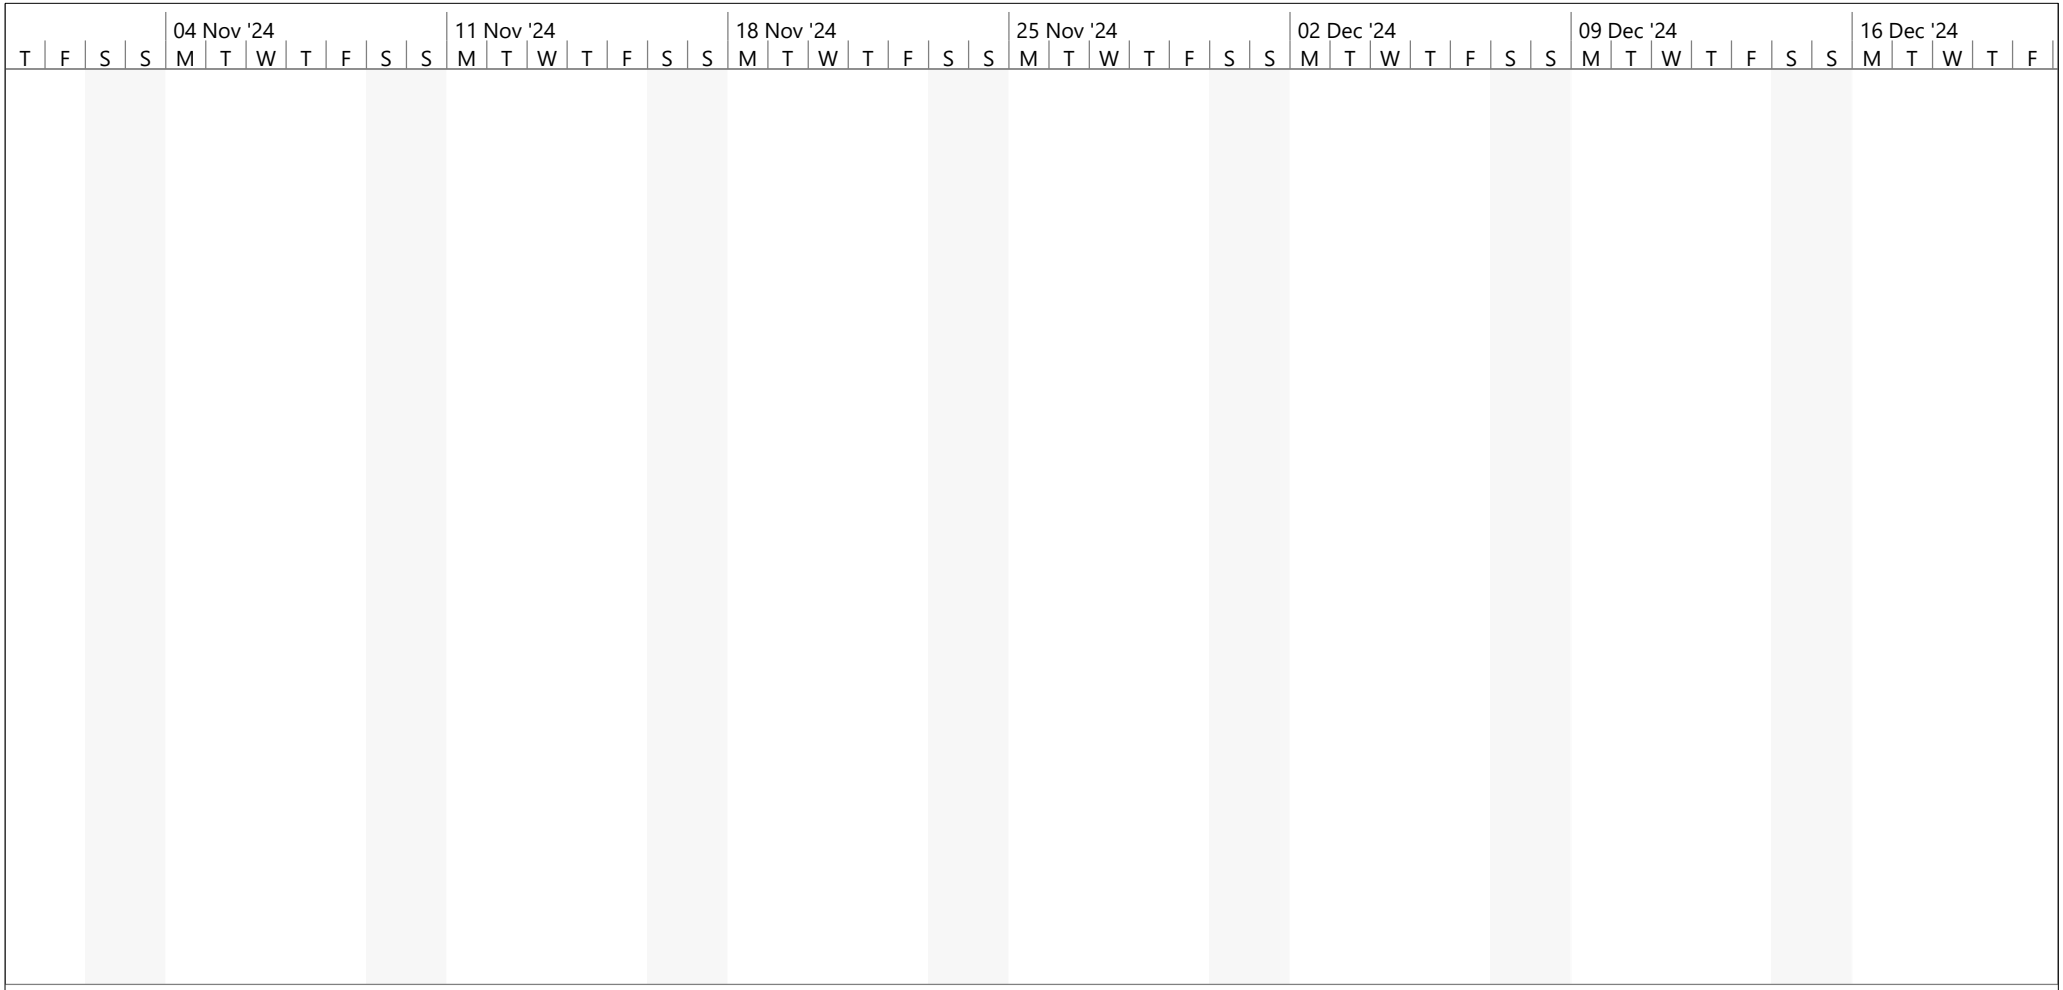


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

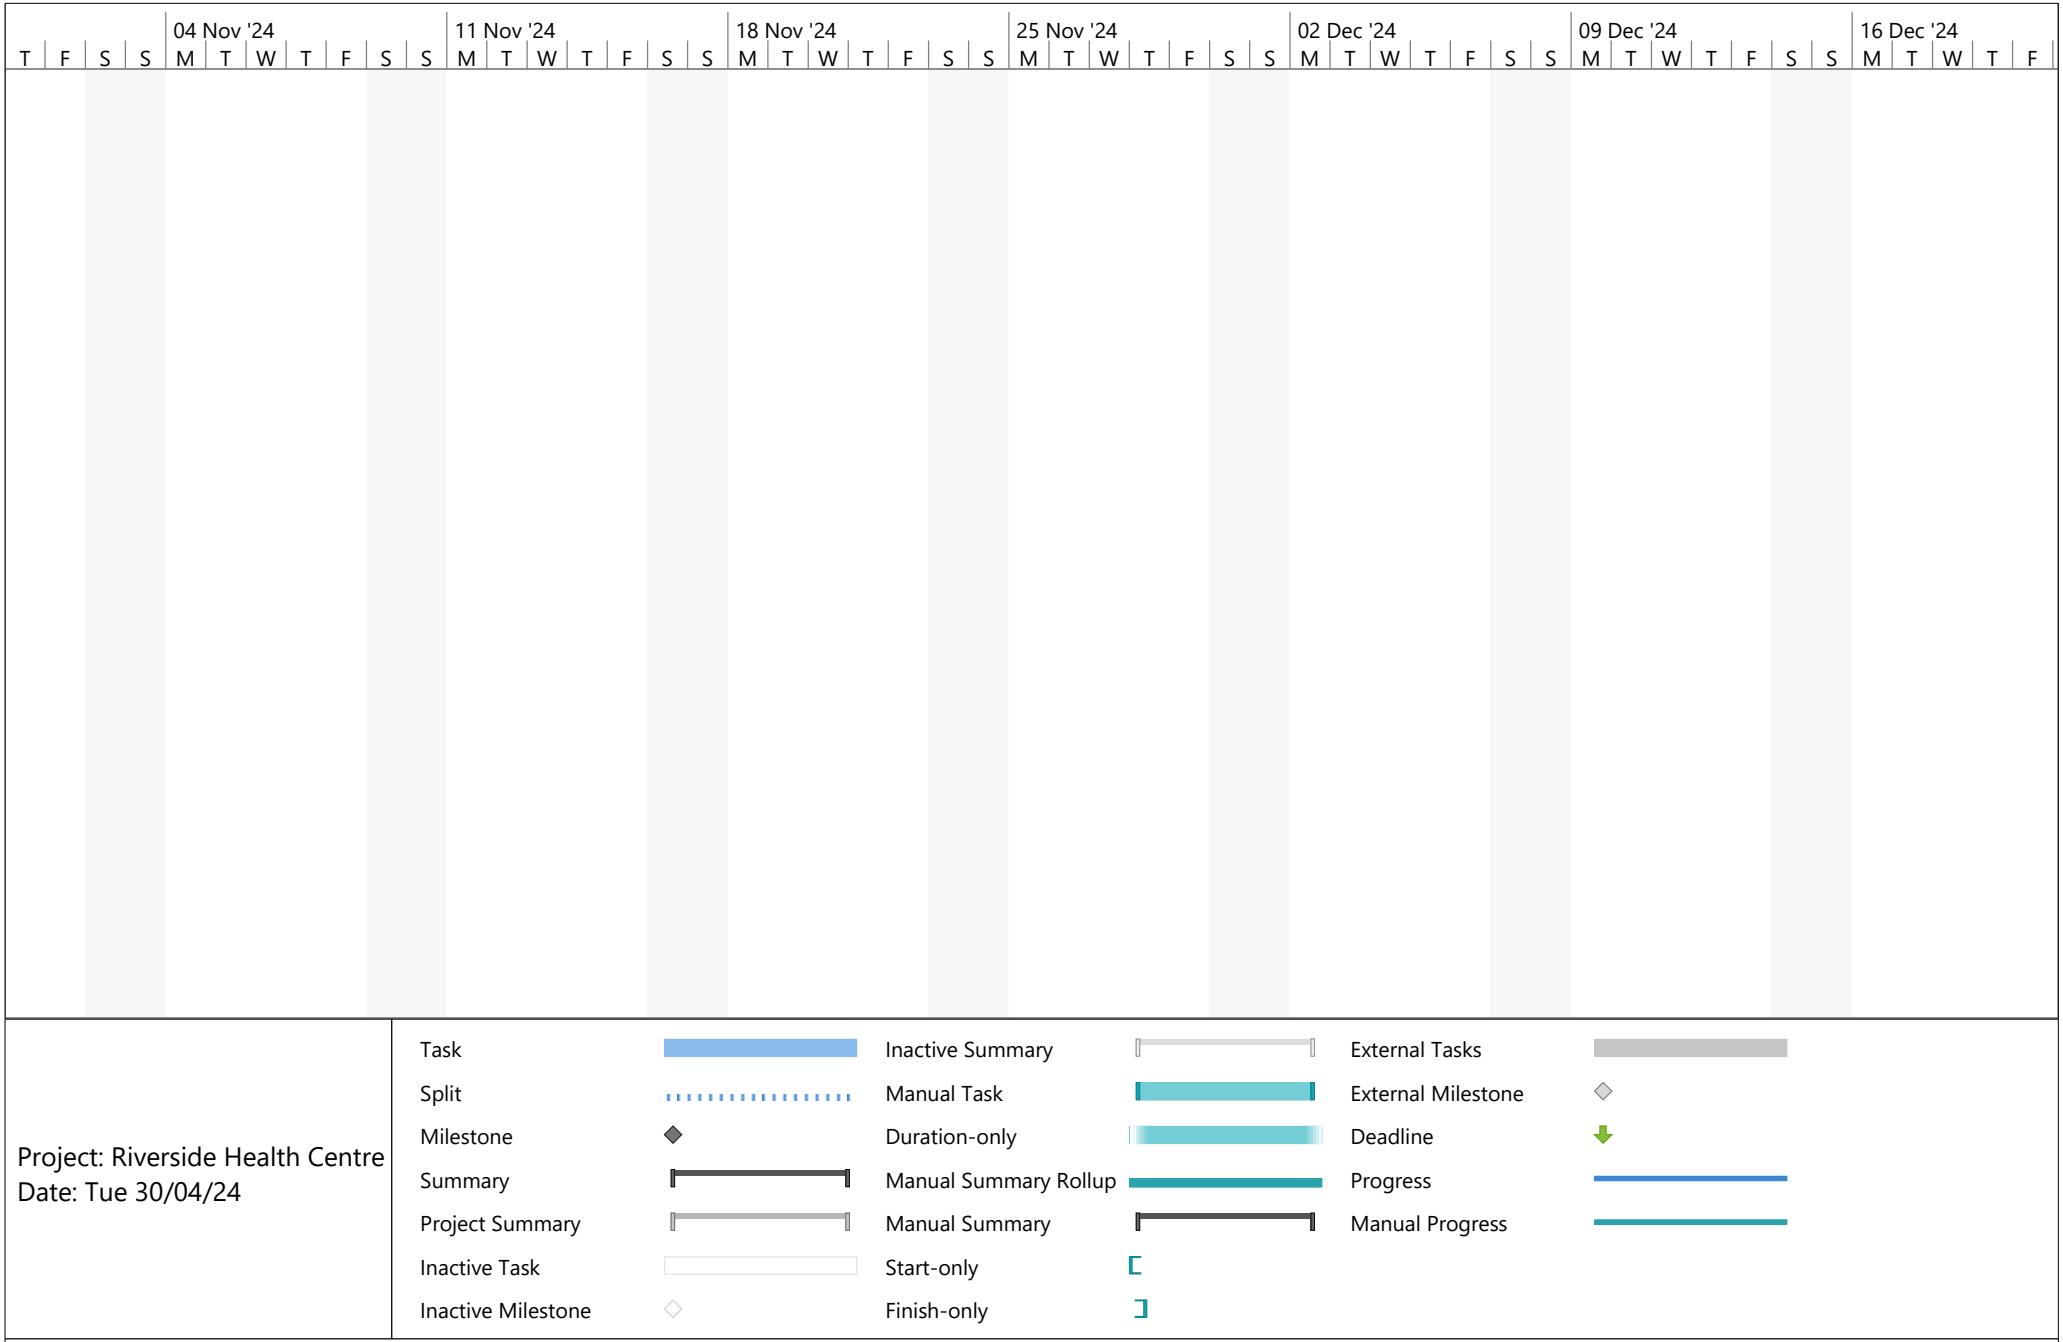

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

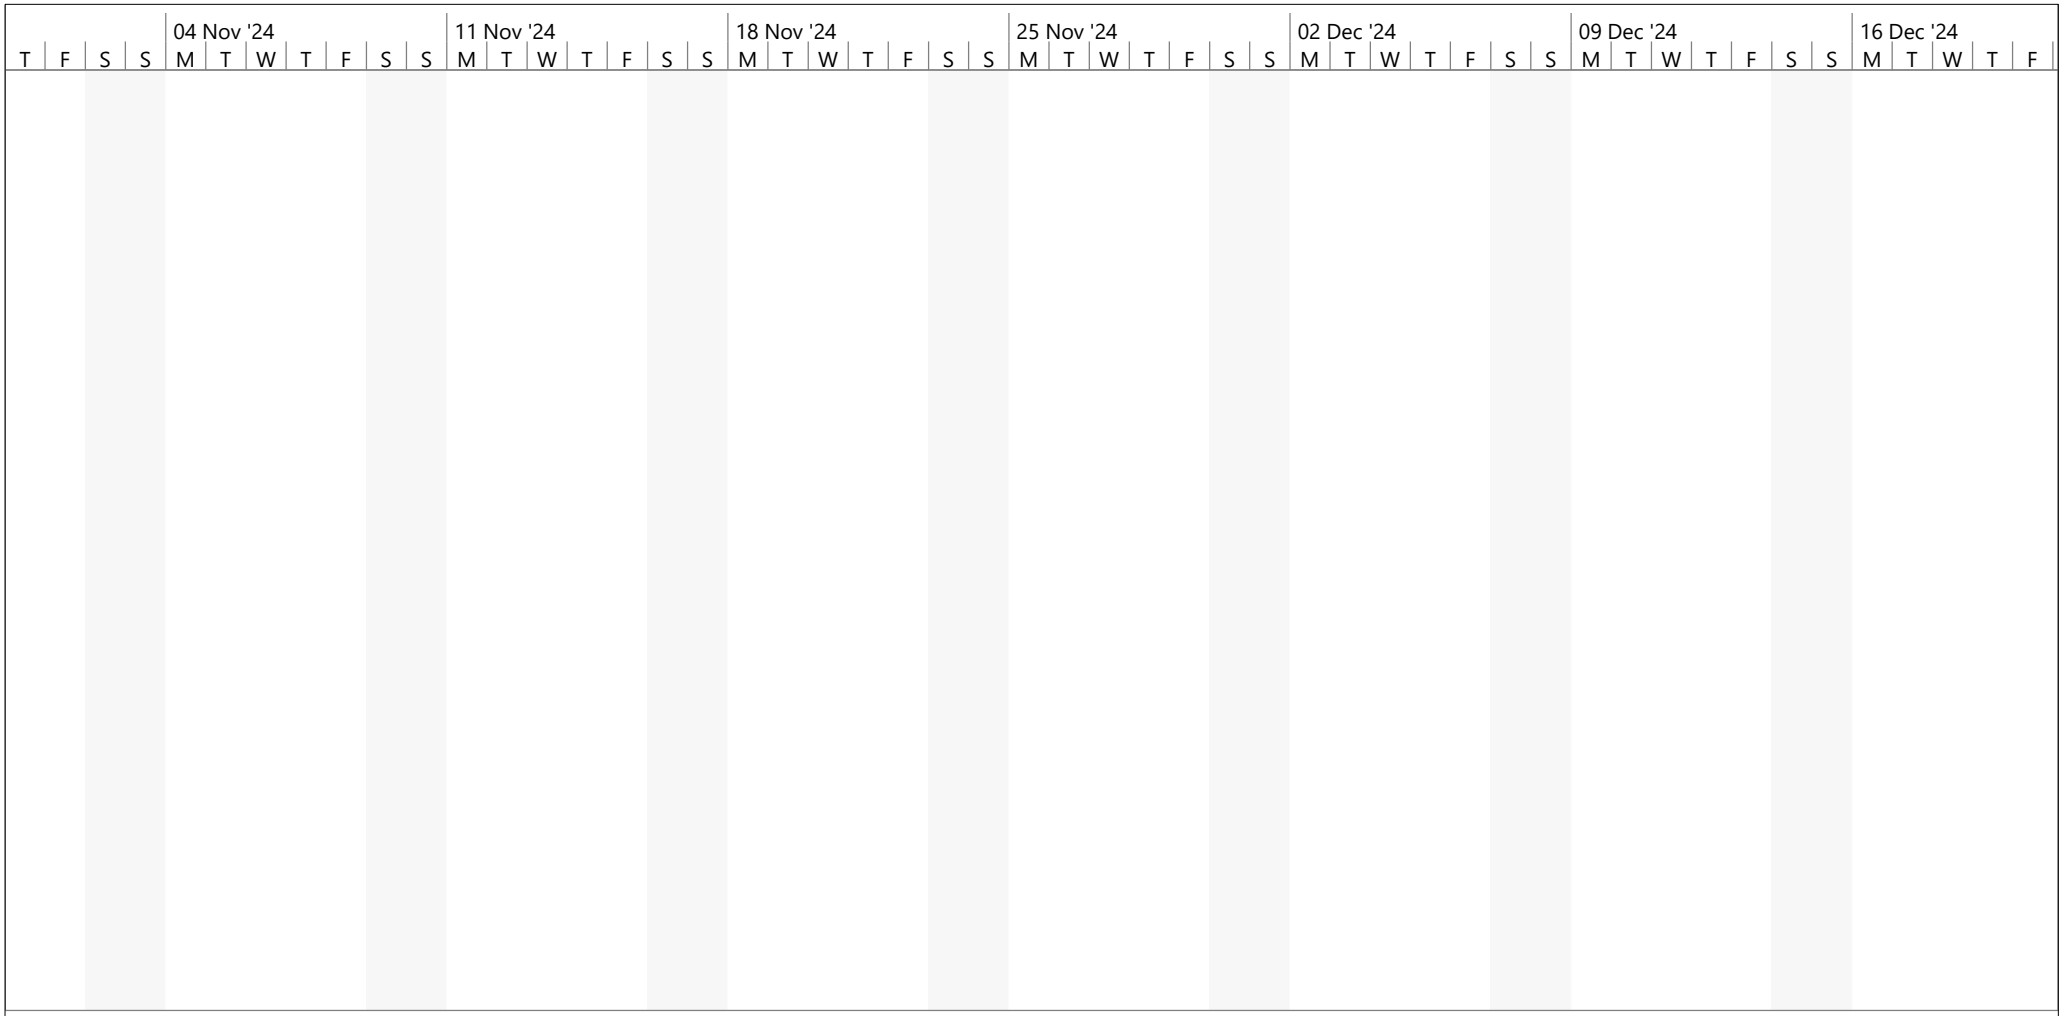


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

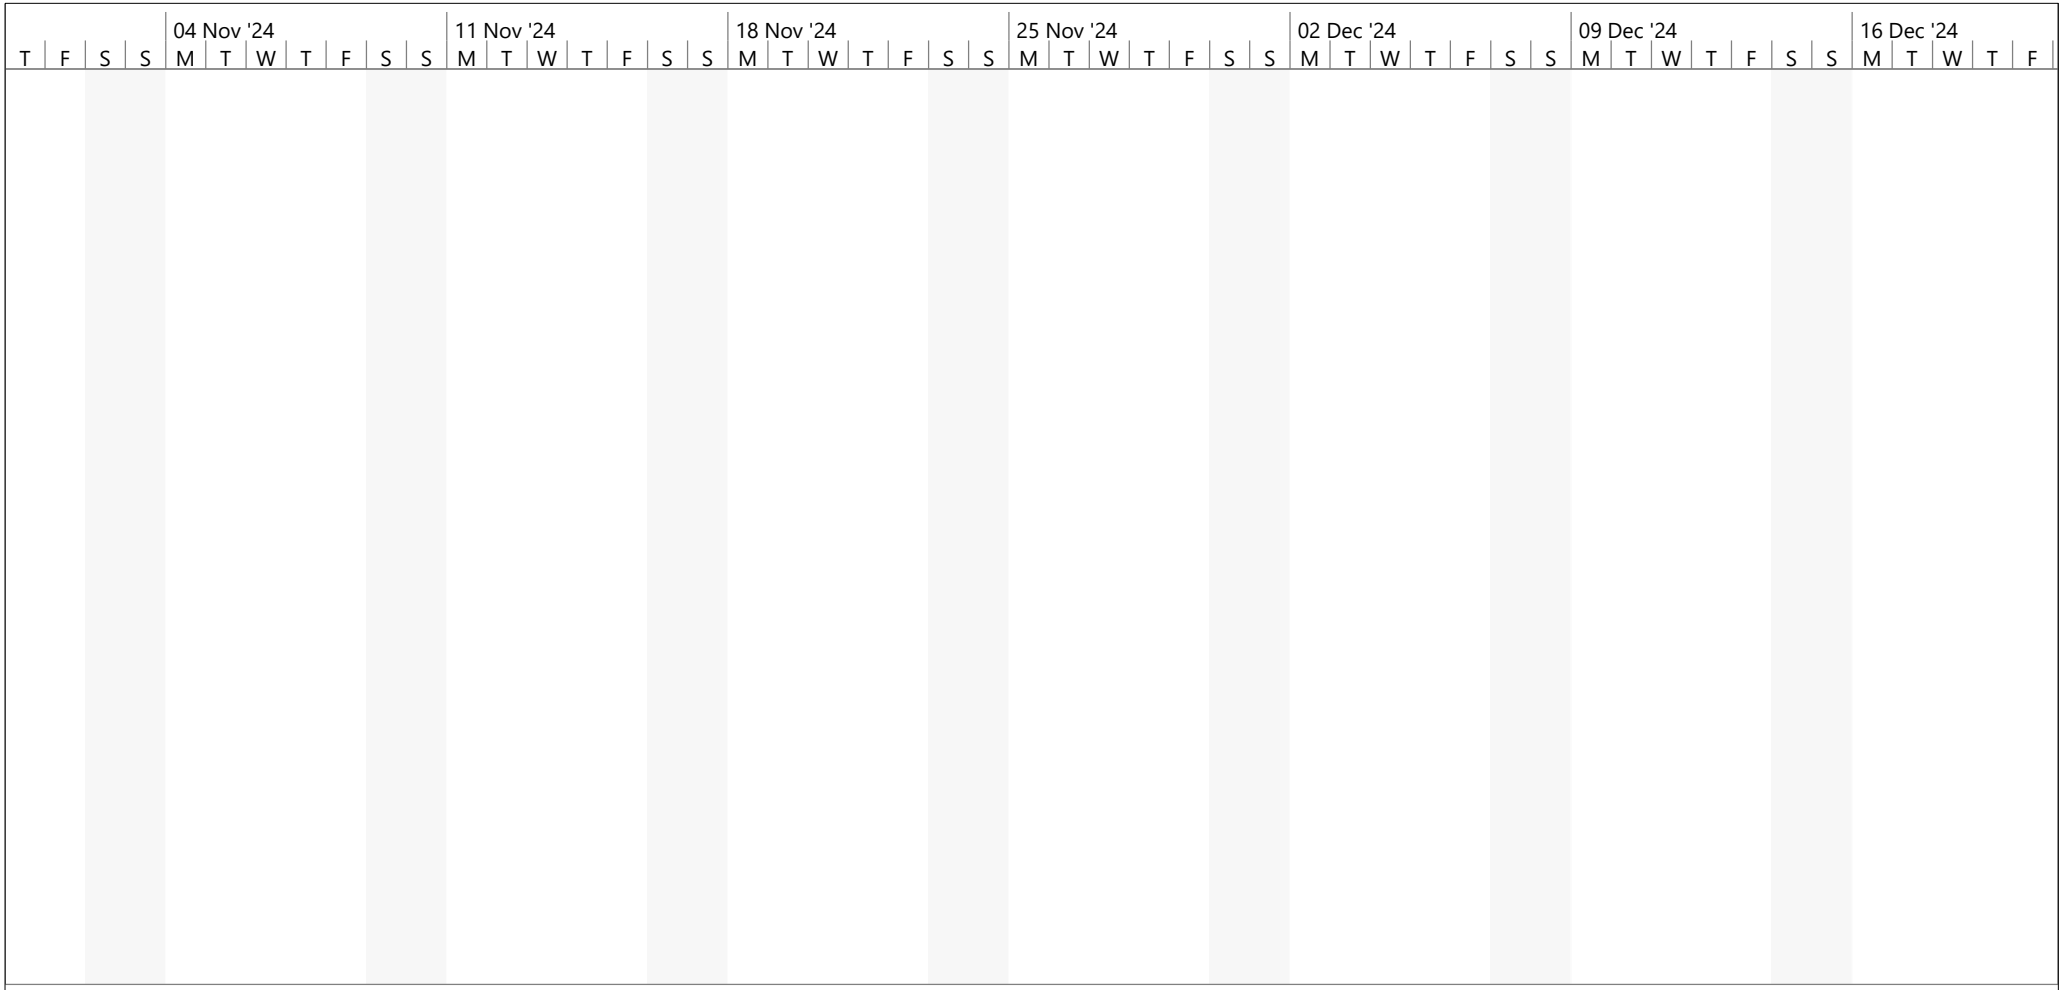

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

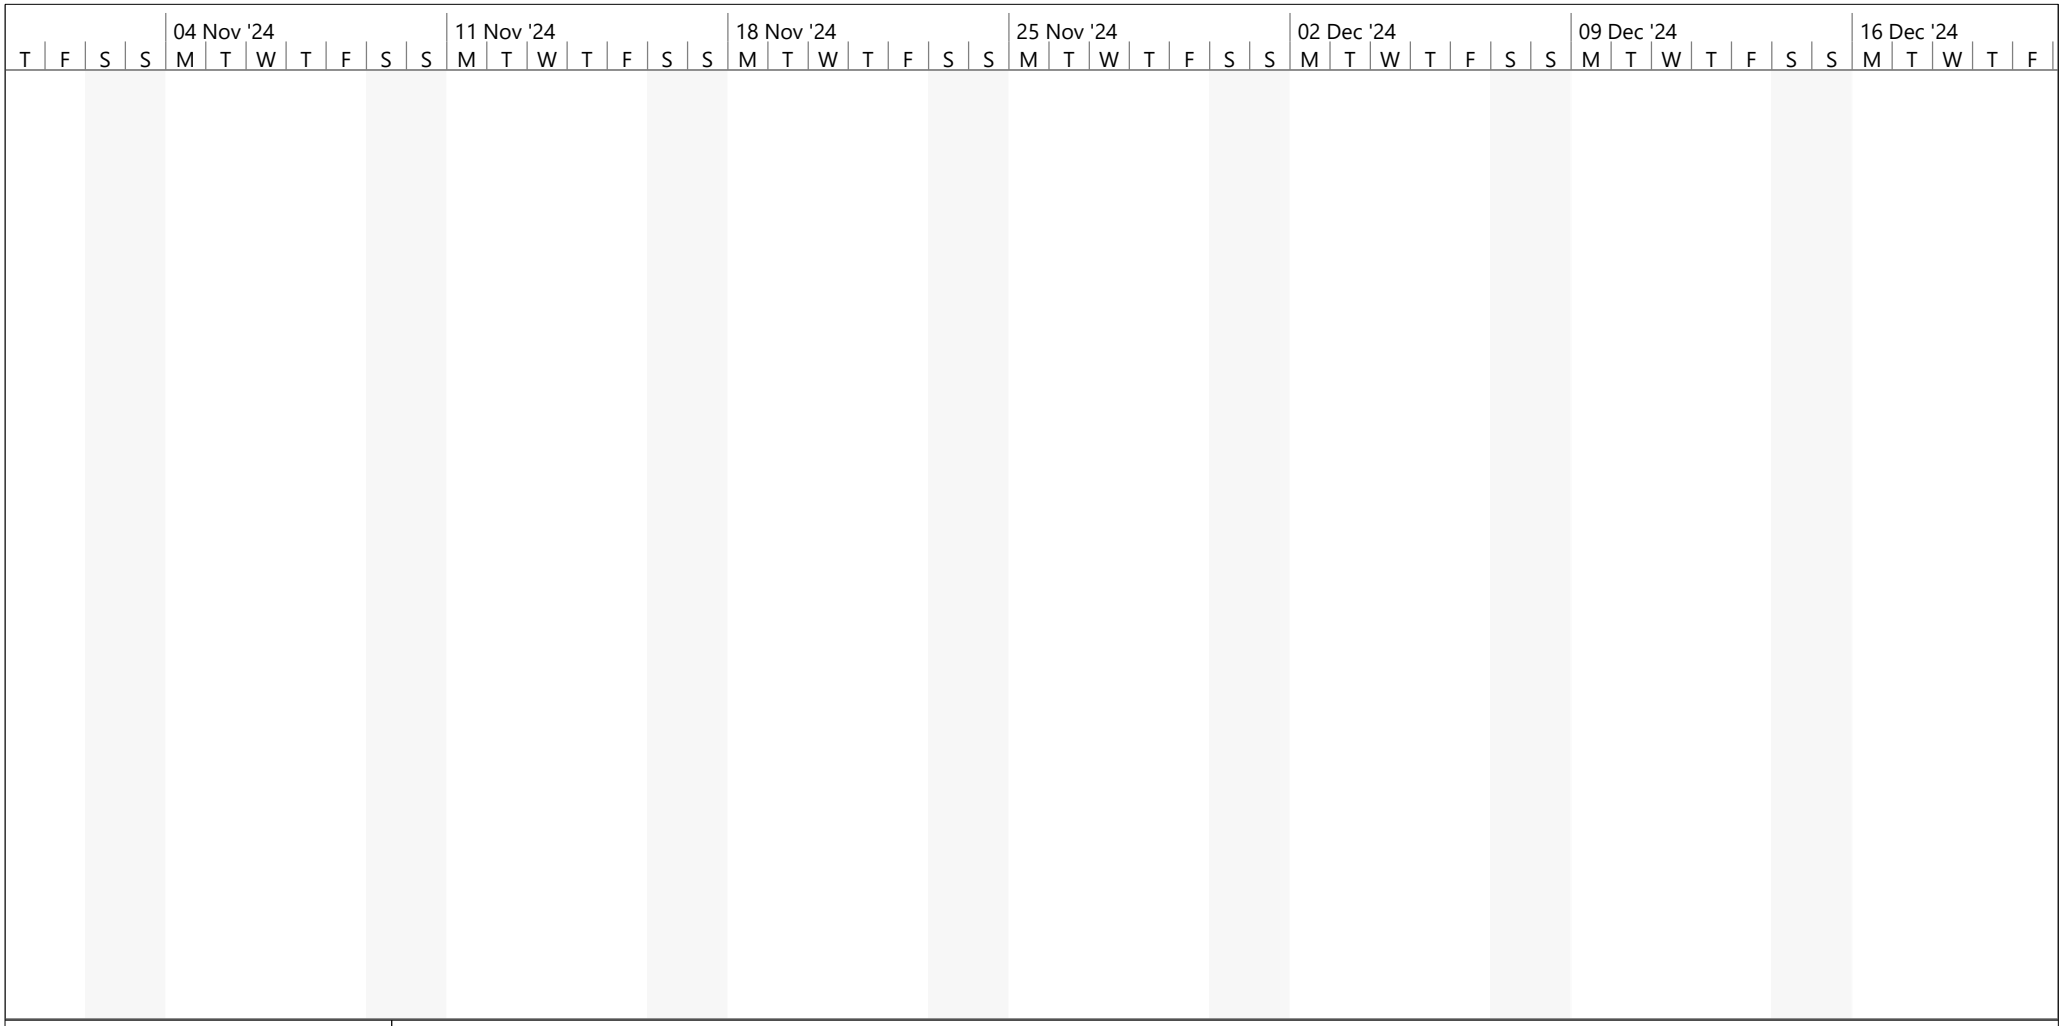


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

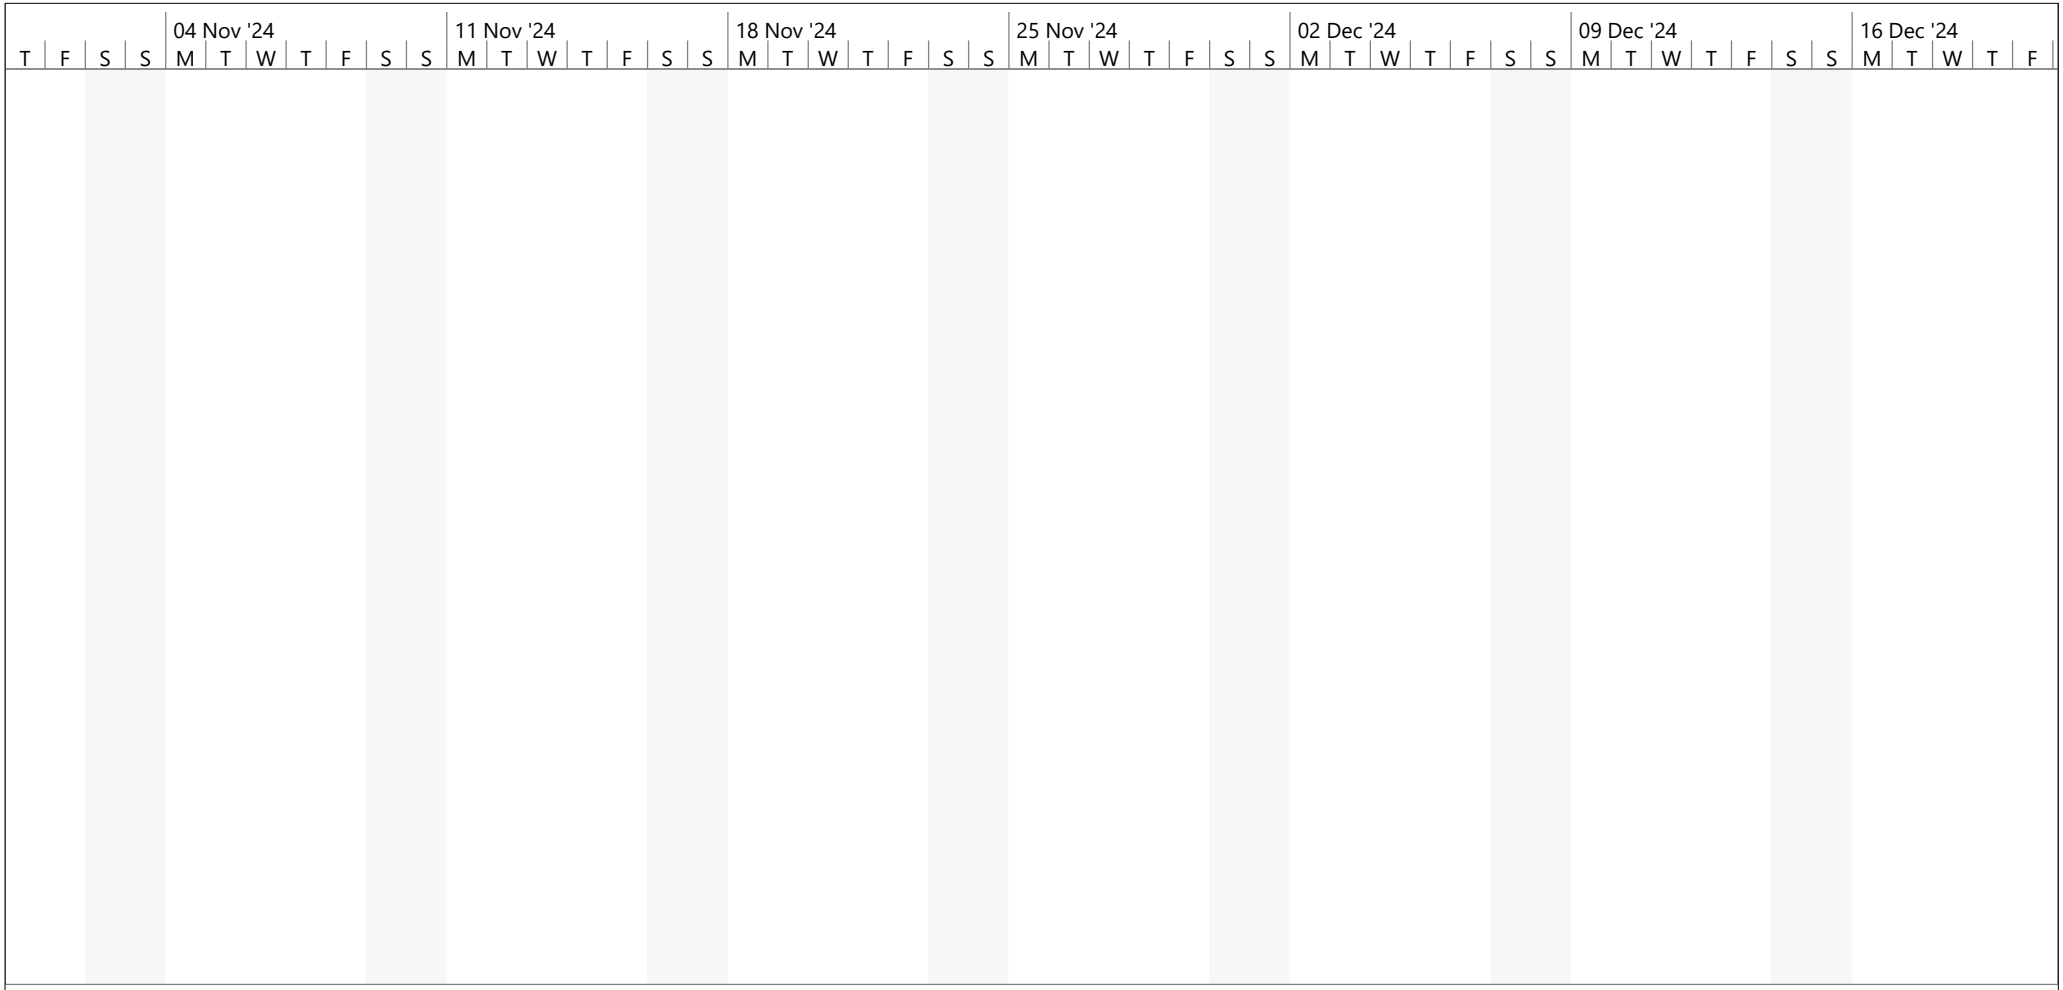


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

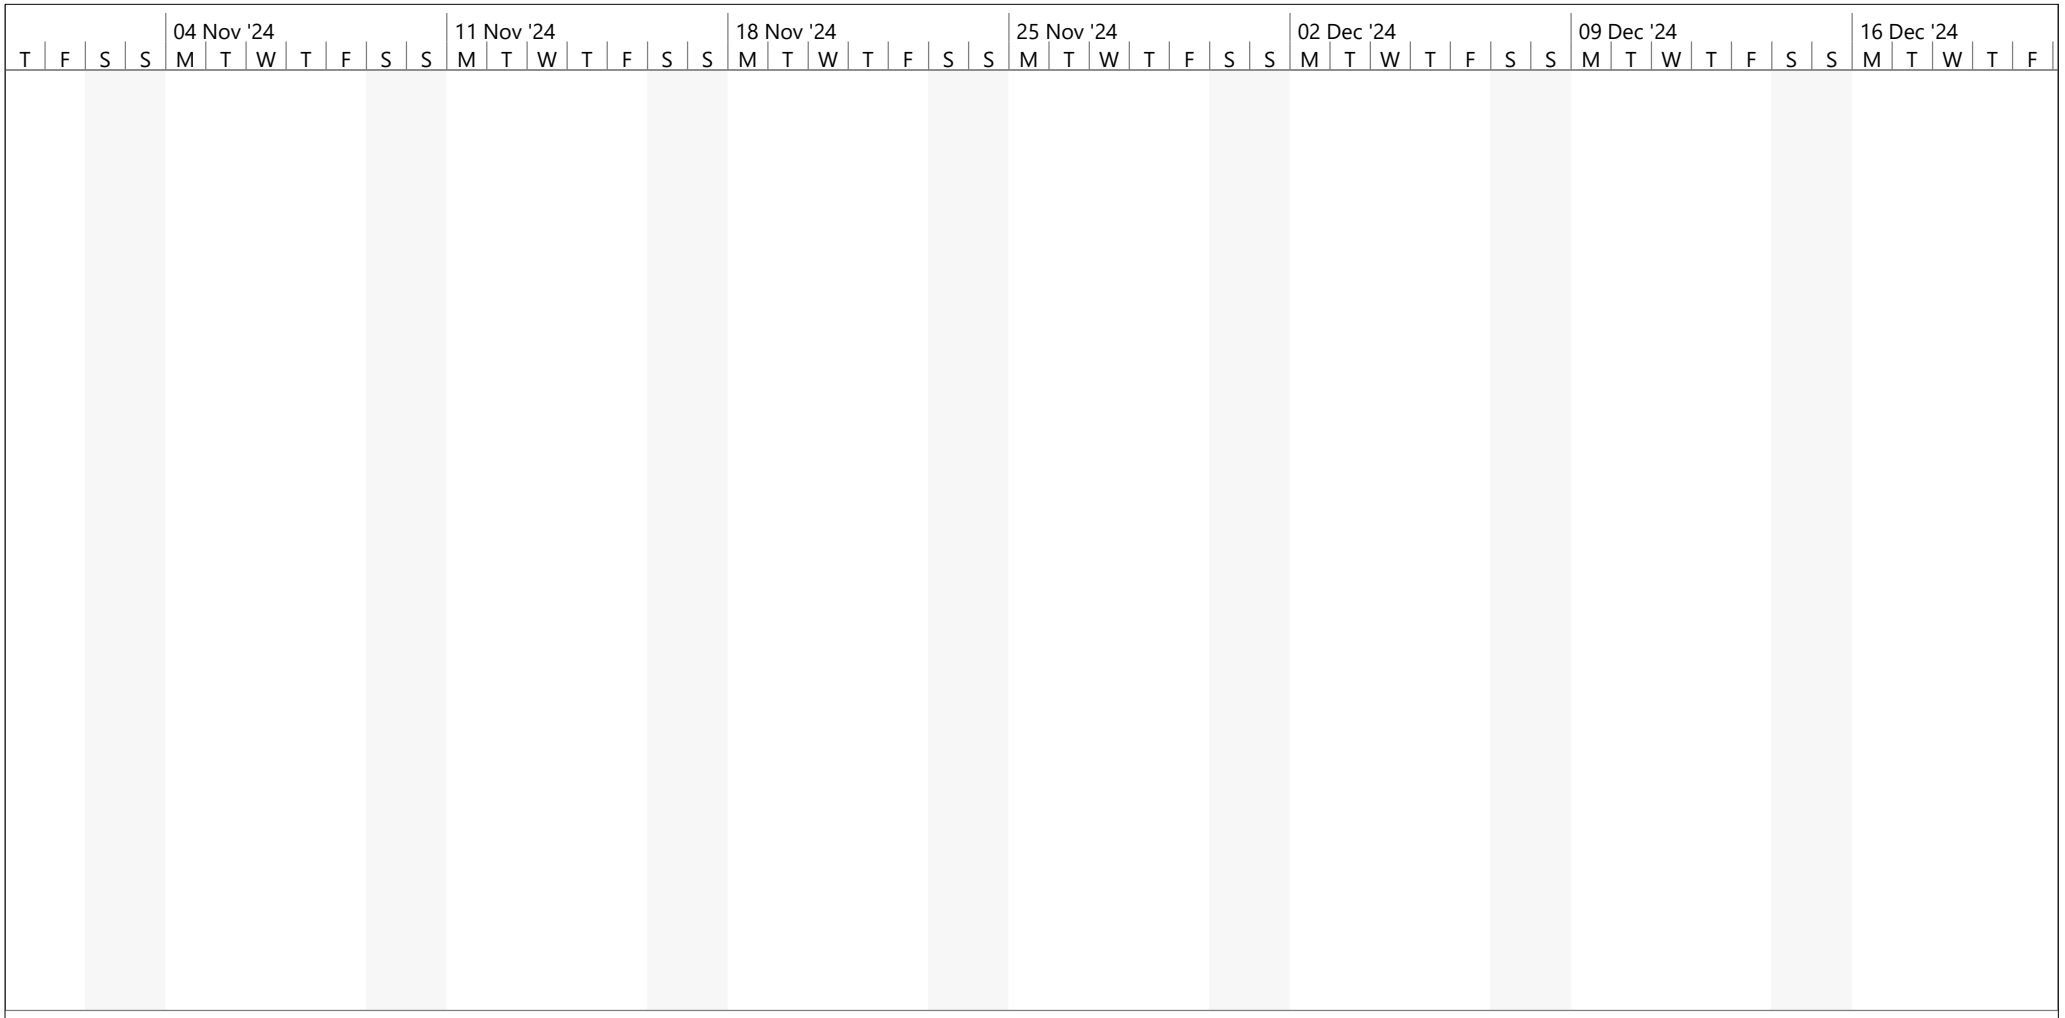


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

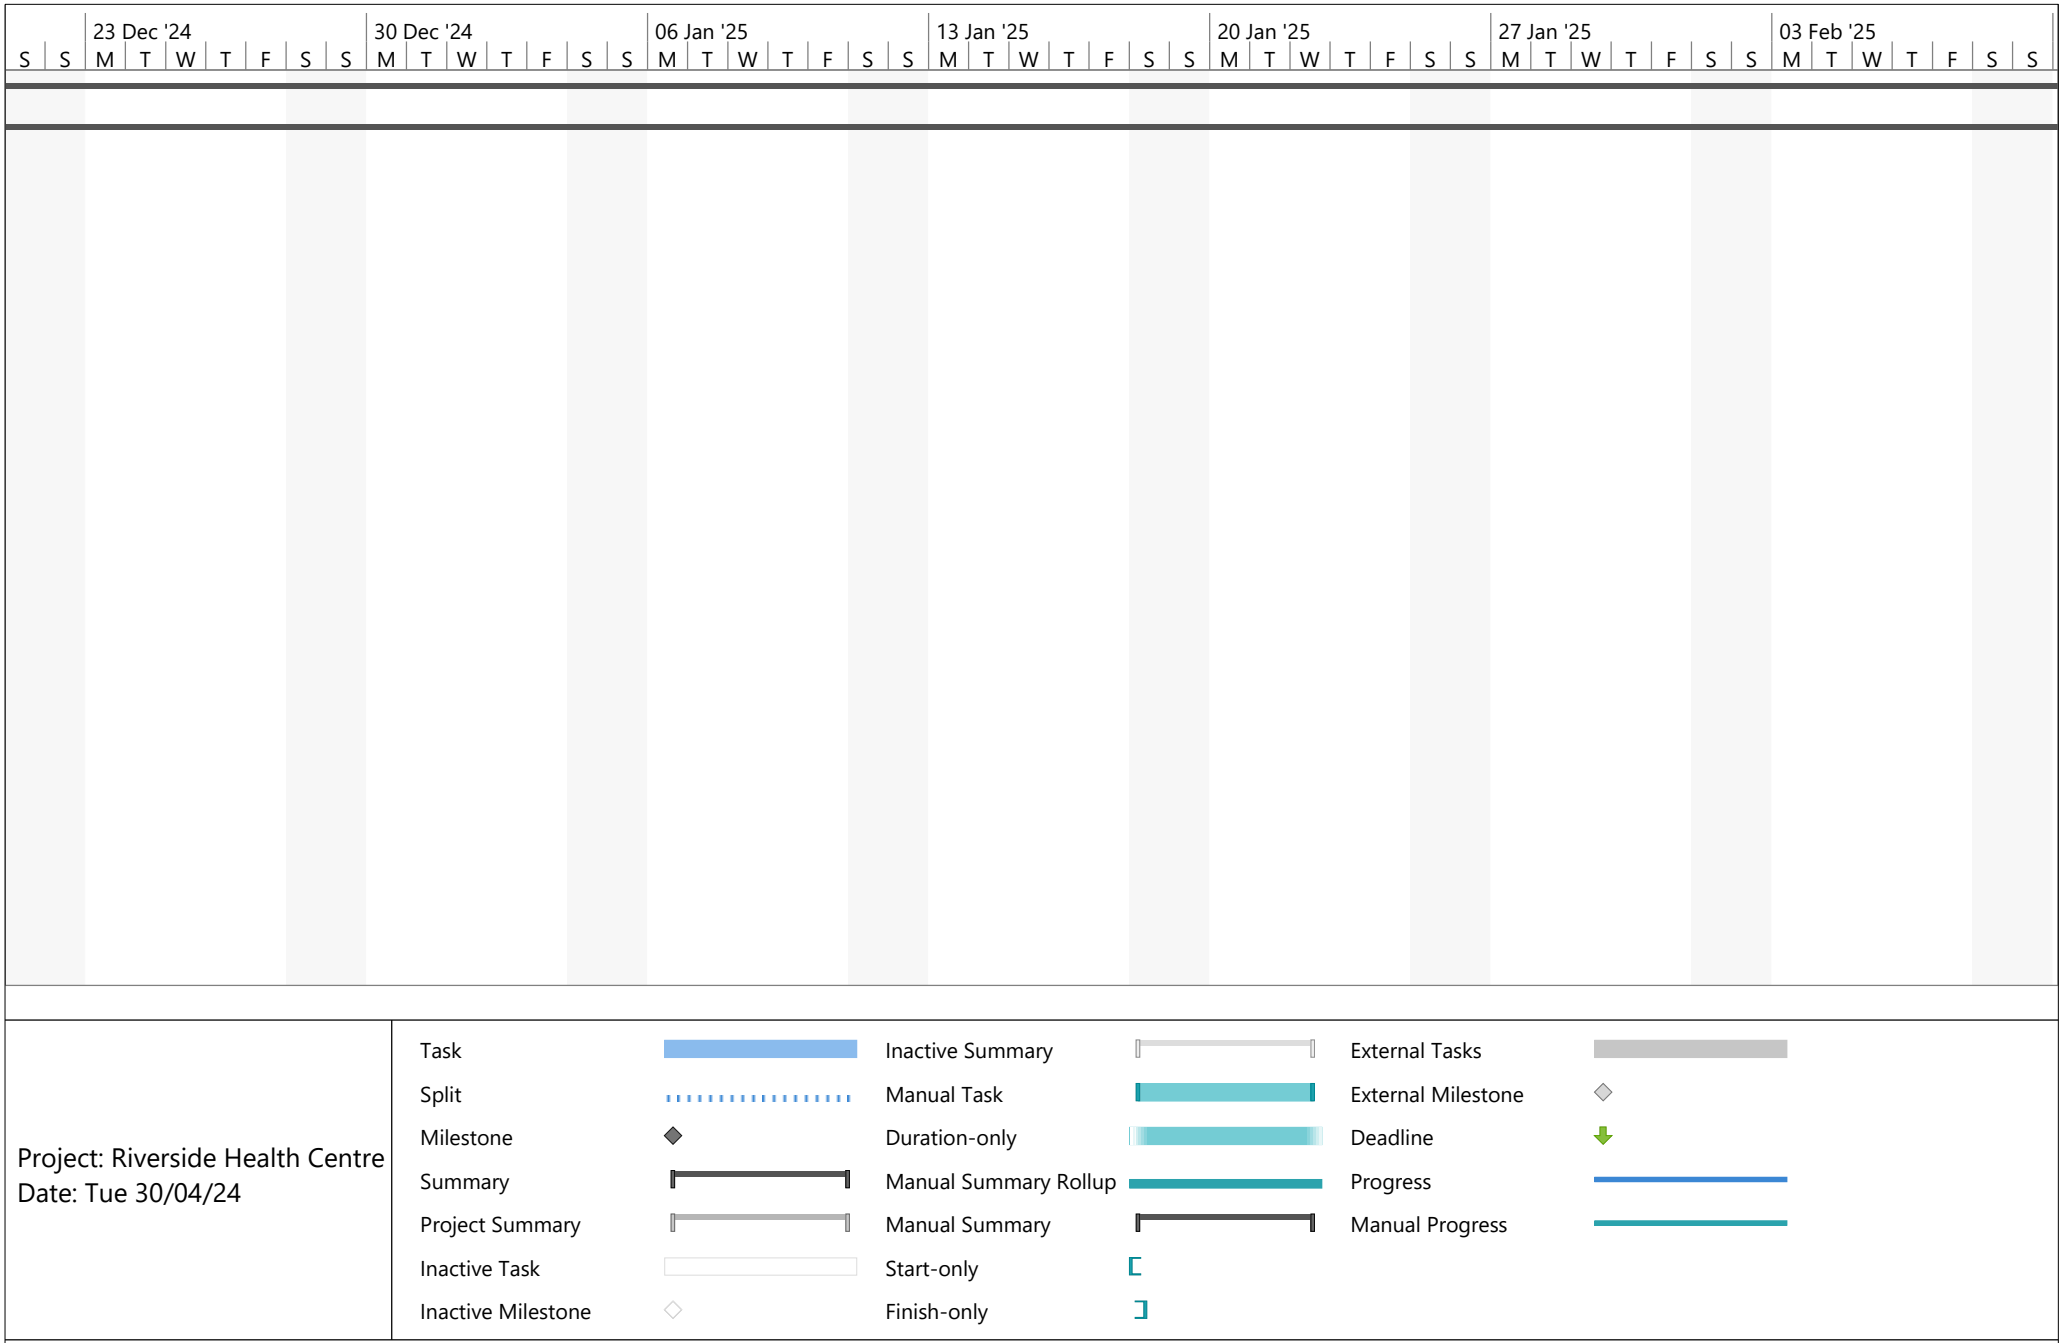


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

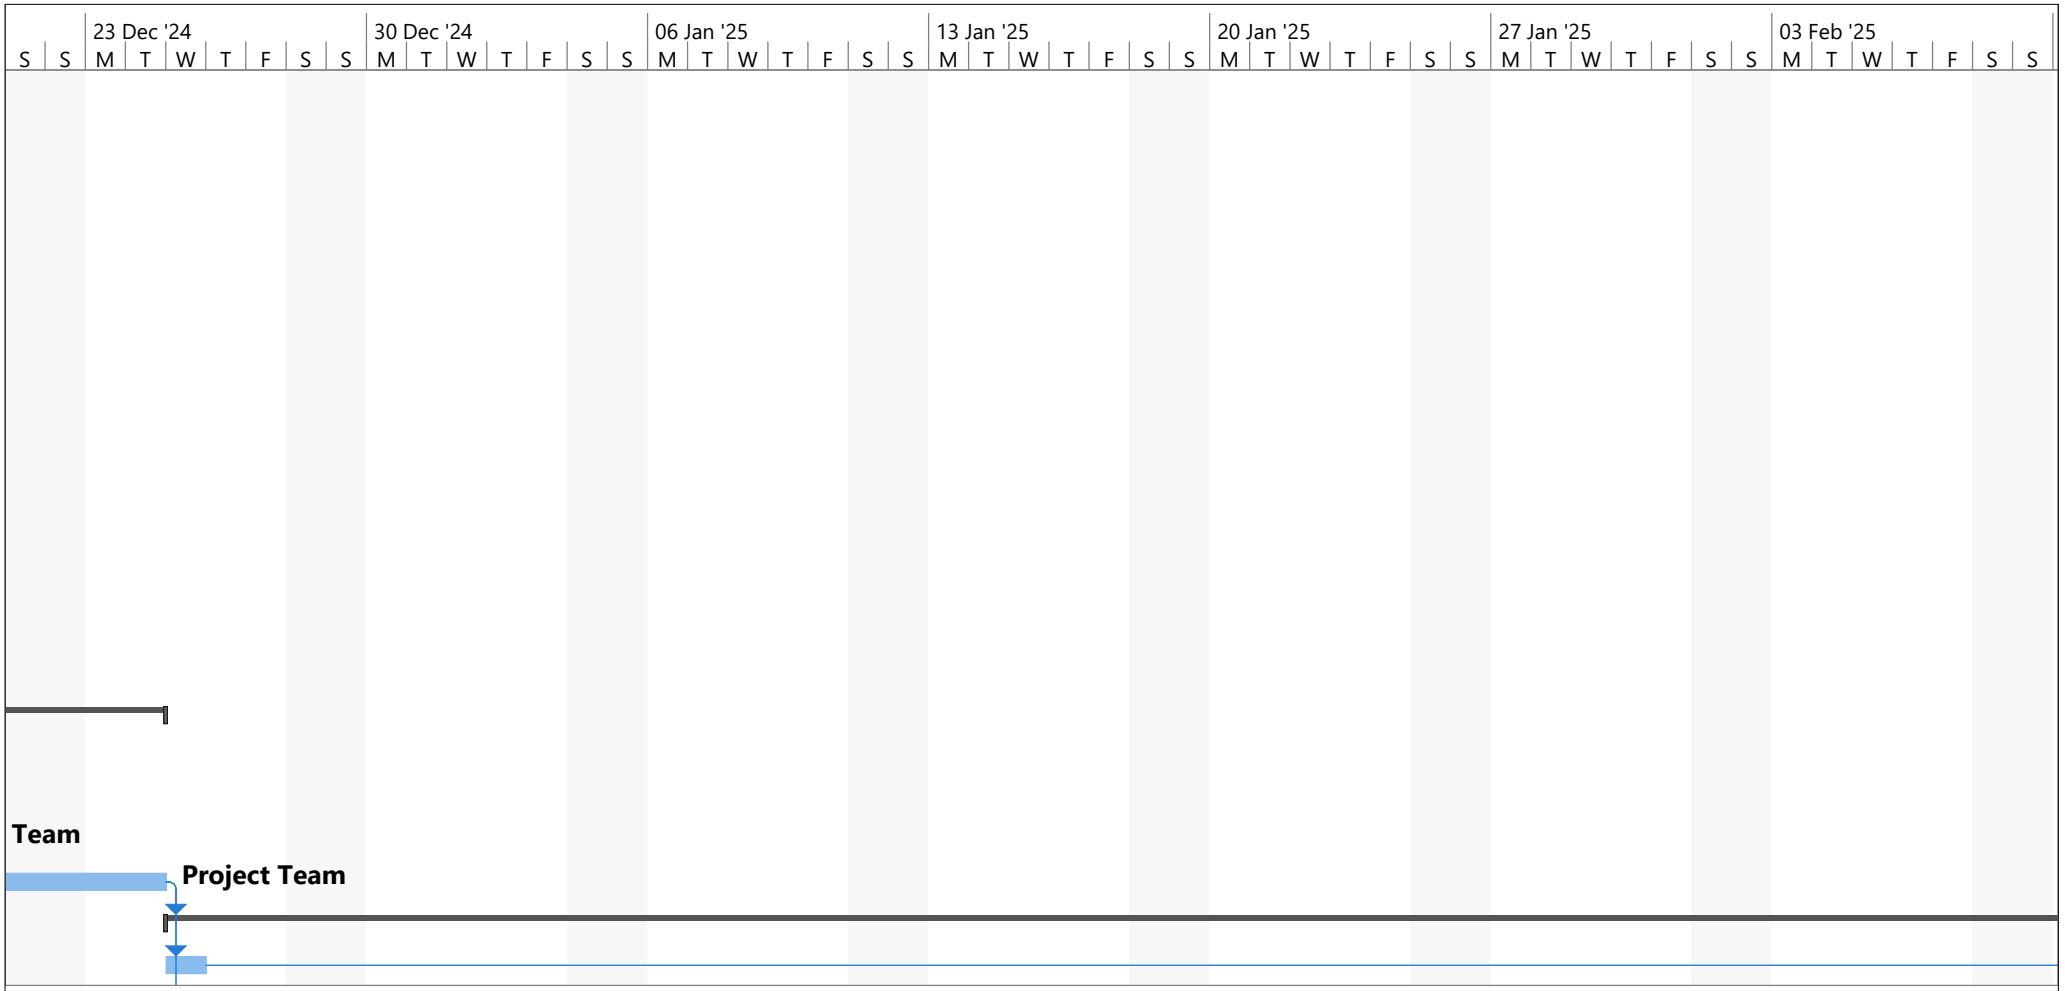


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

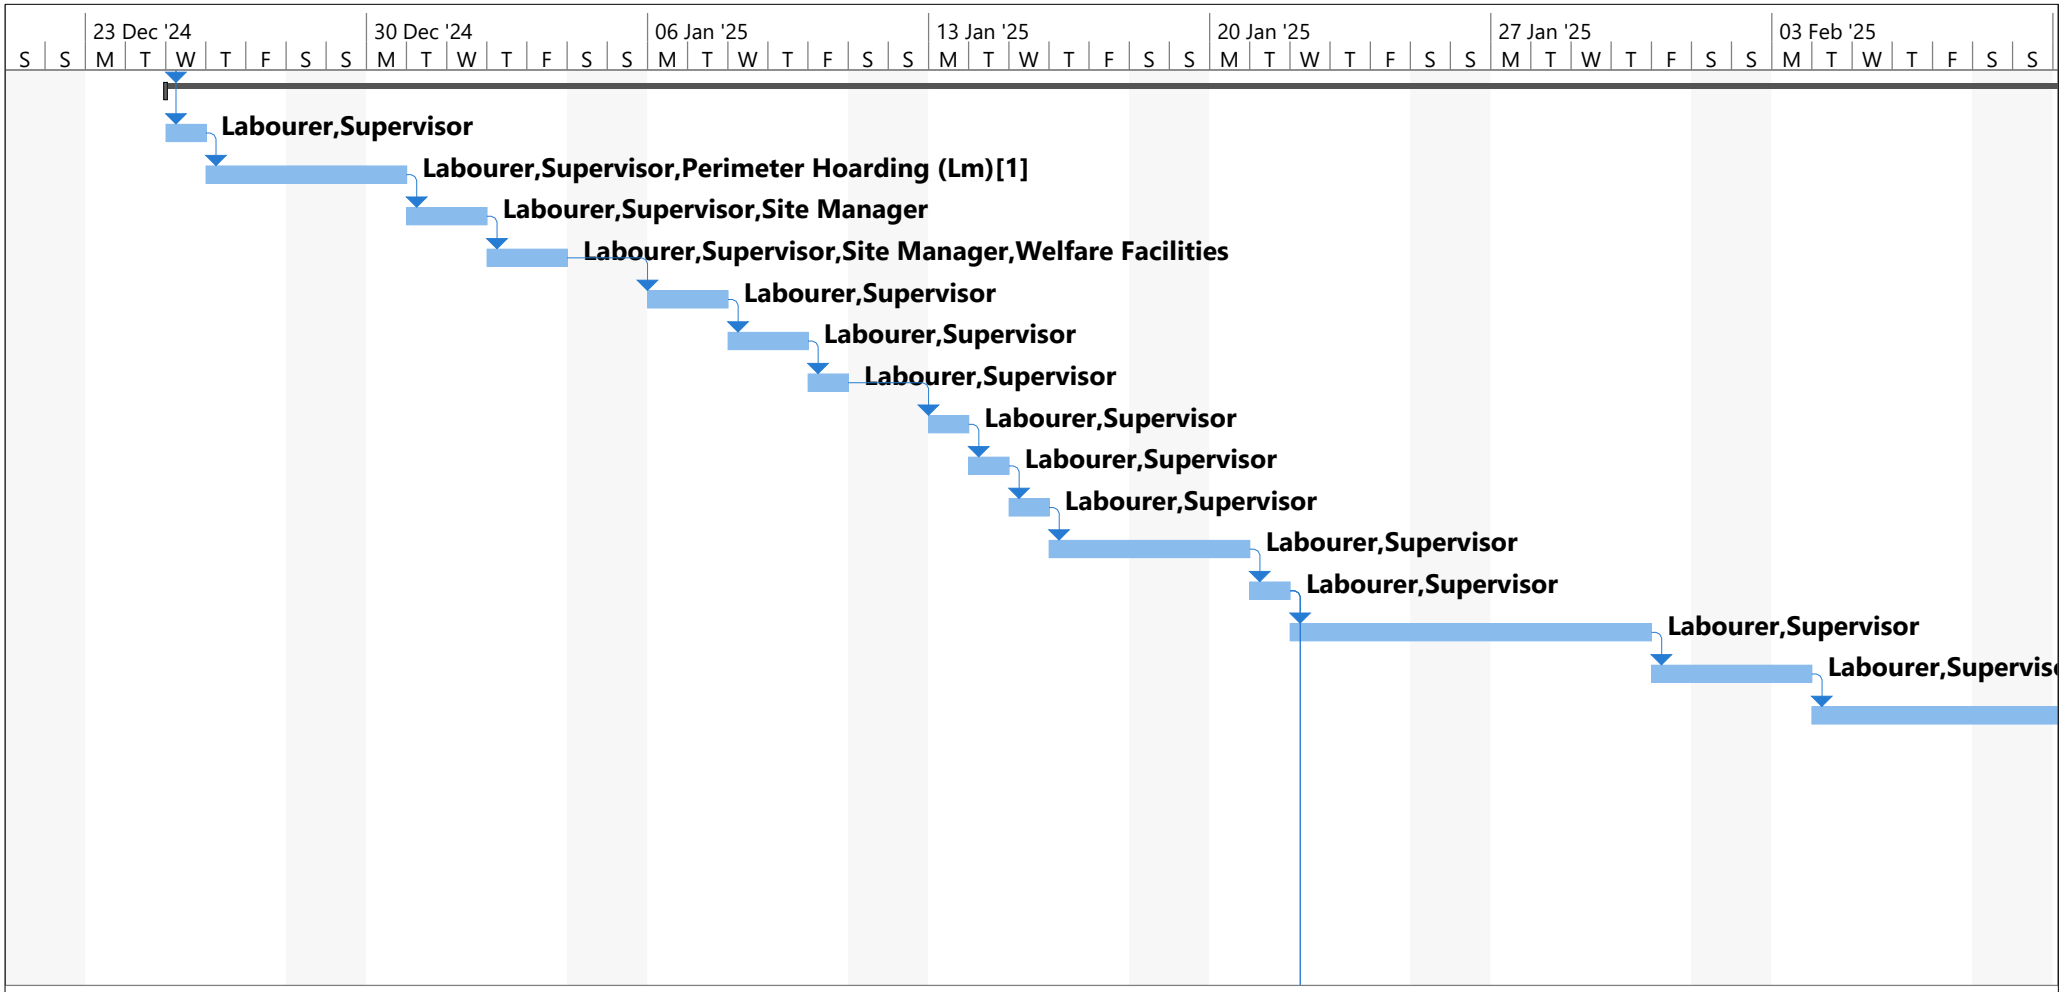


Project: Riverside Health Centre
Date: Tue 30/04/24

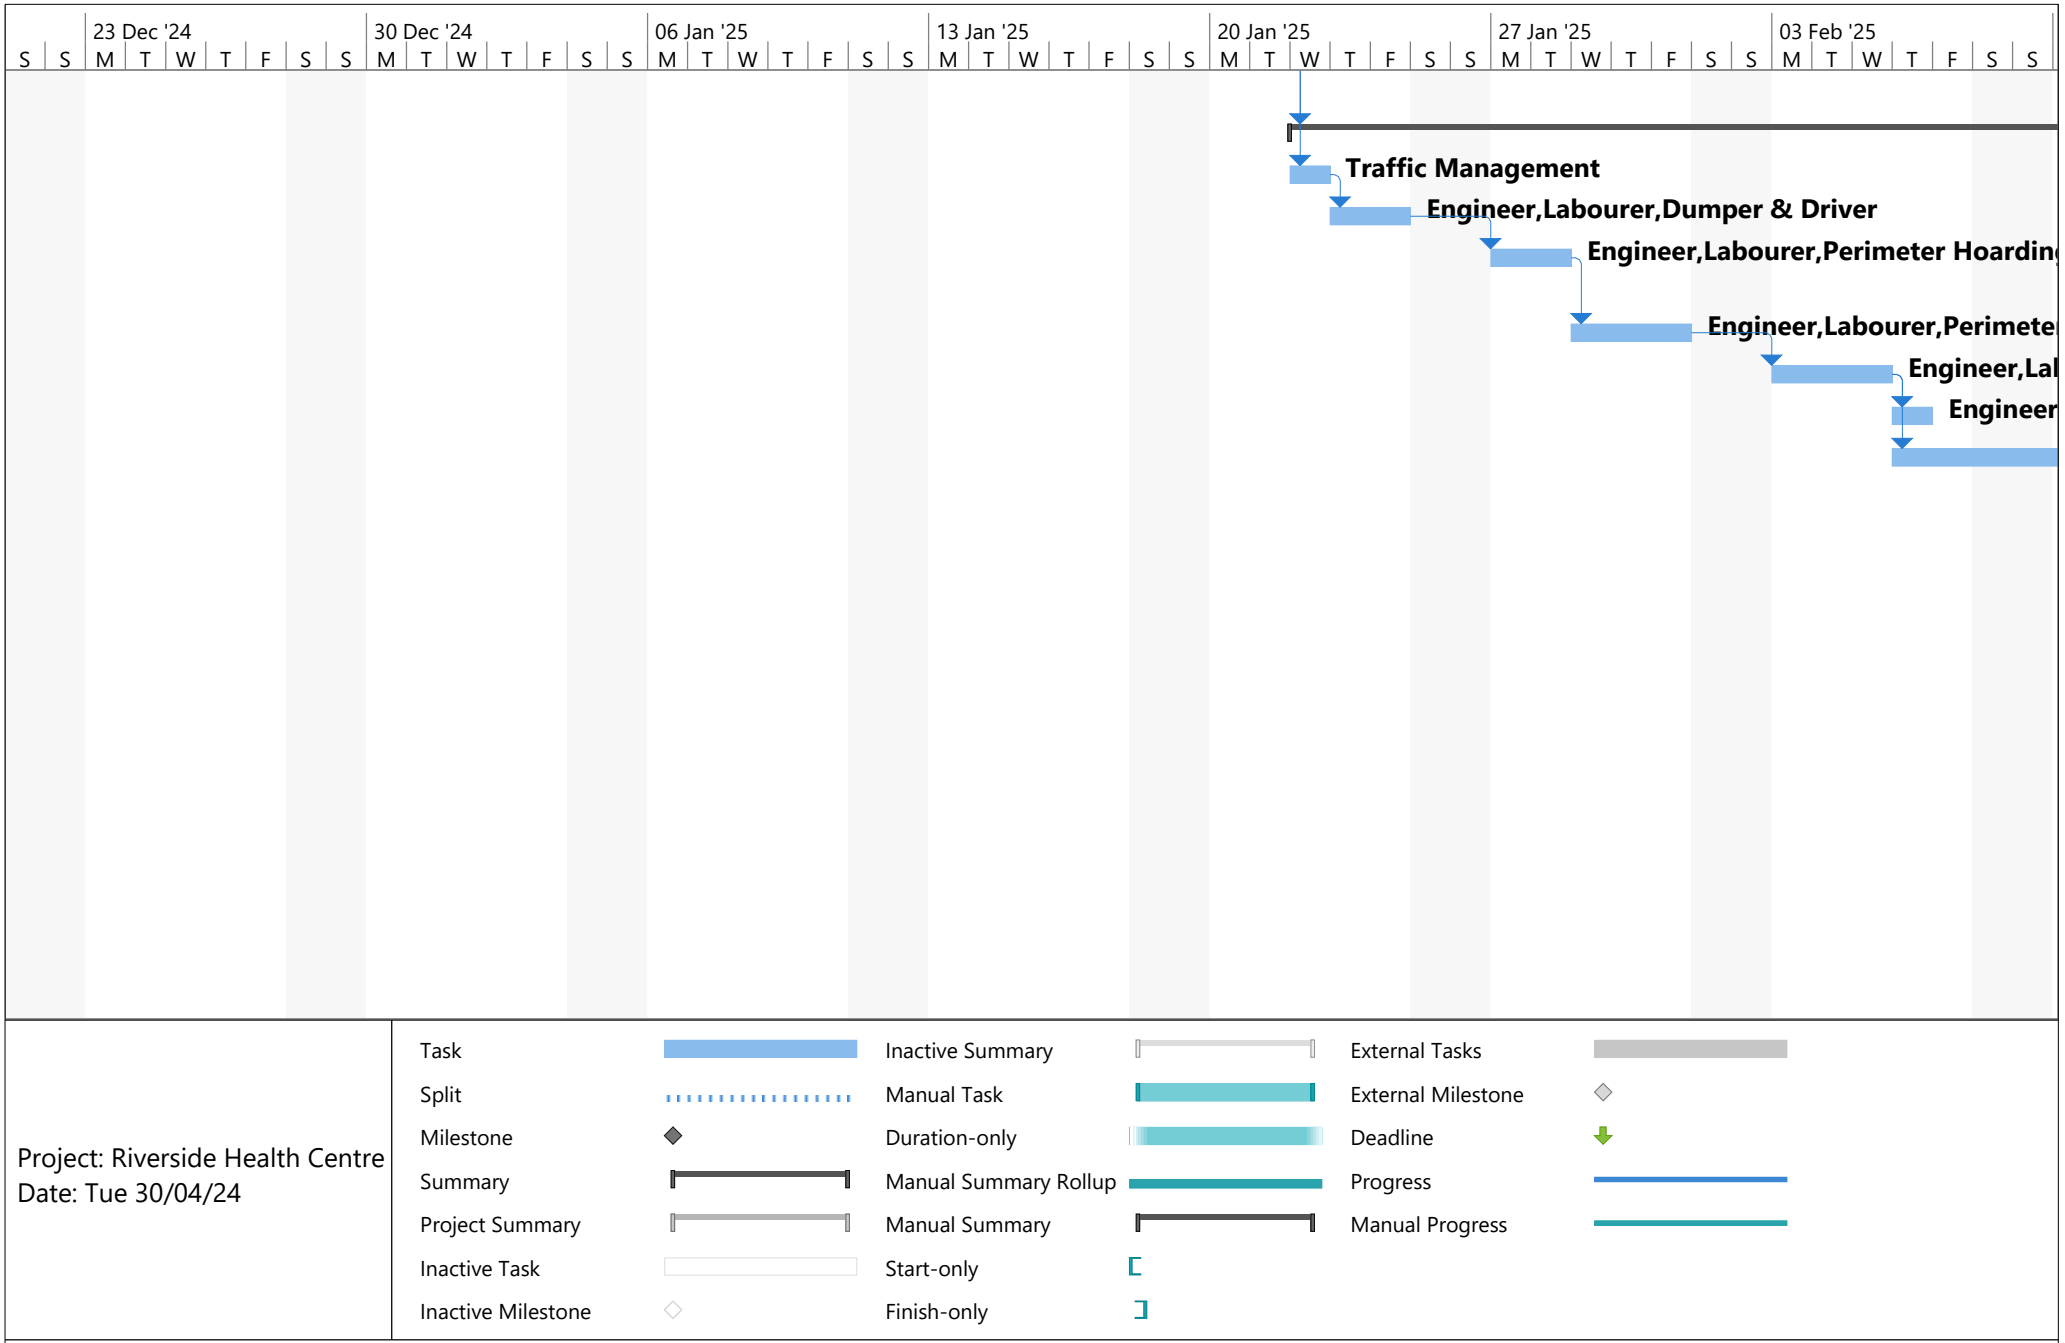


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

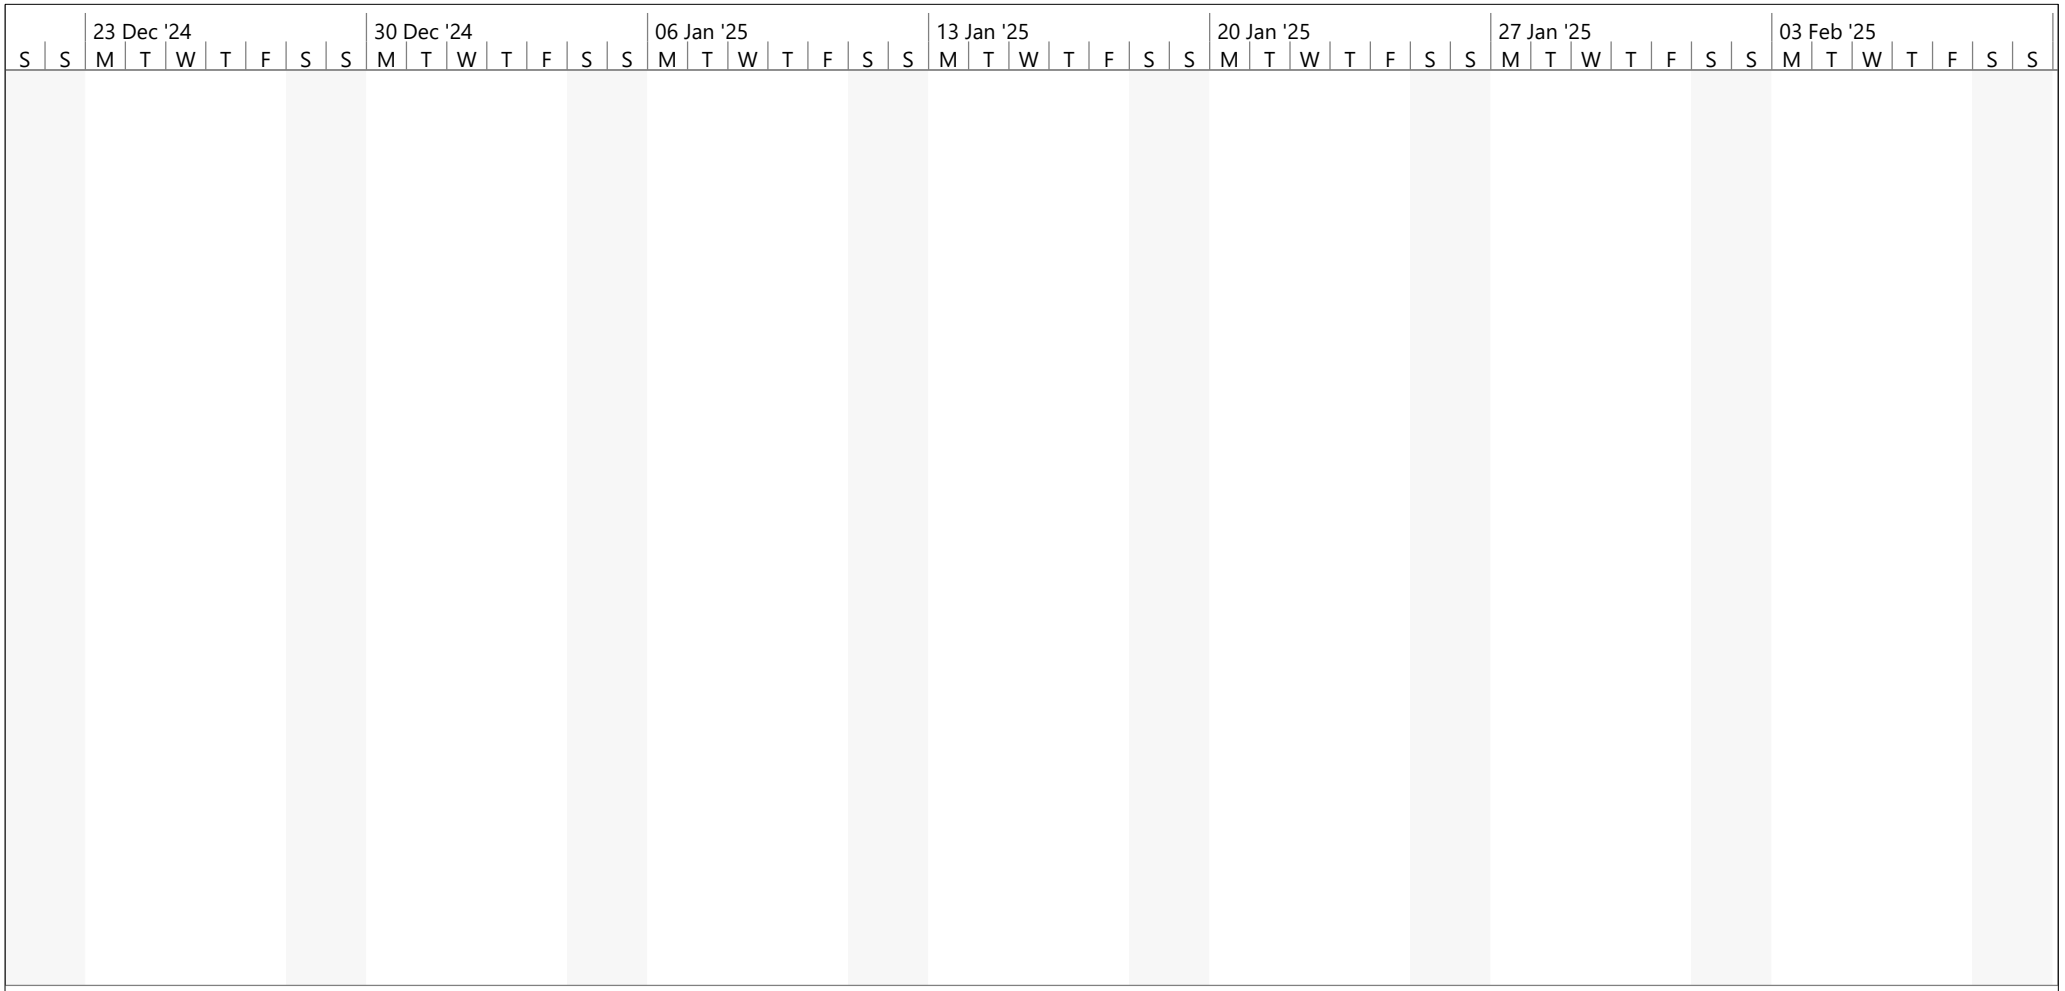


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

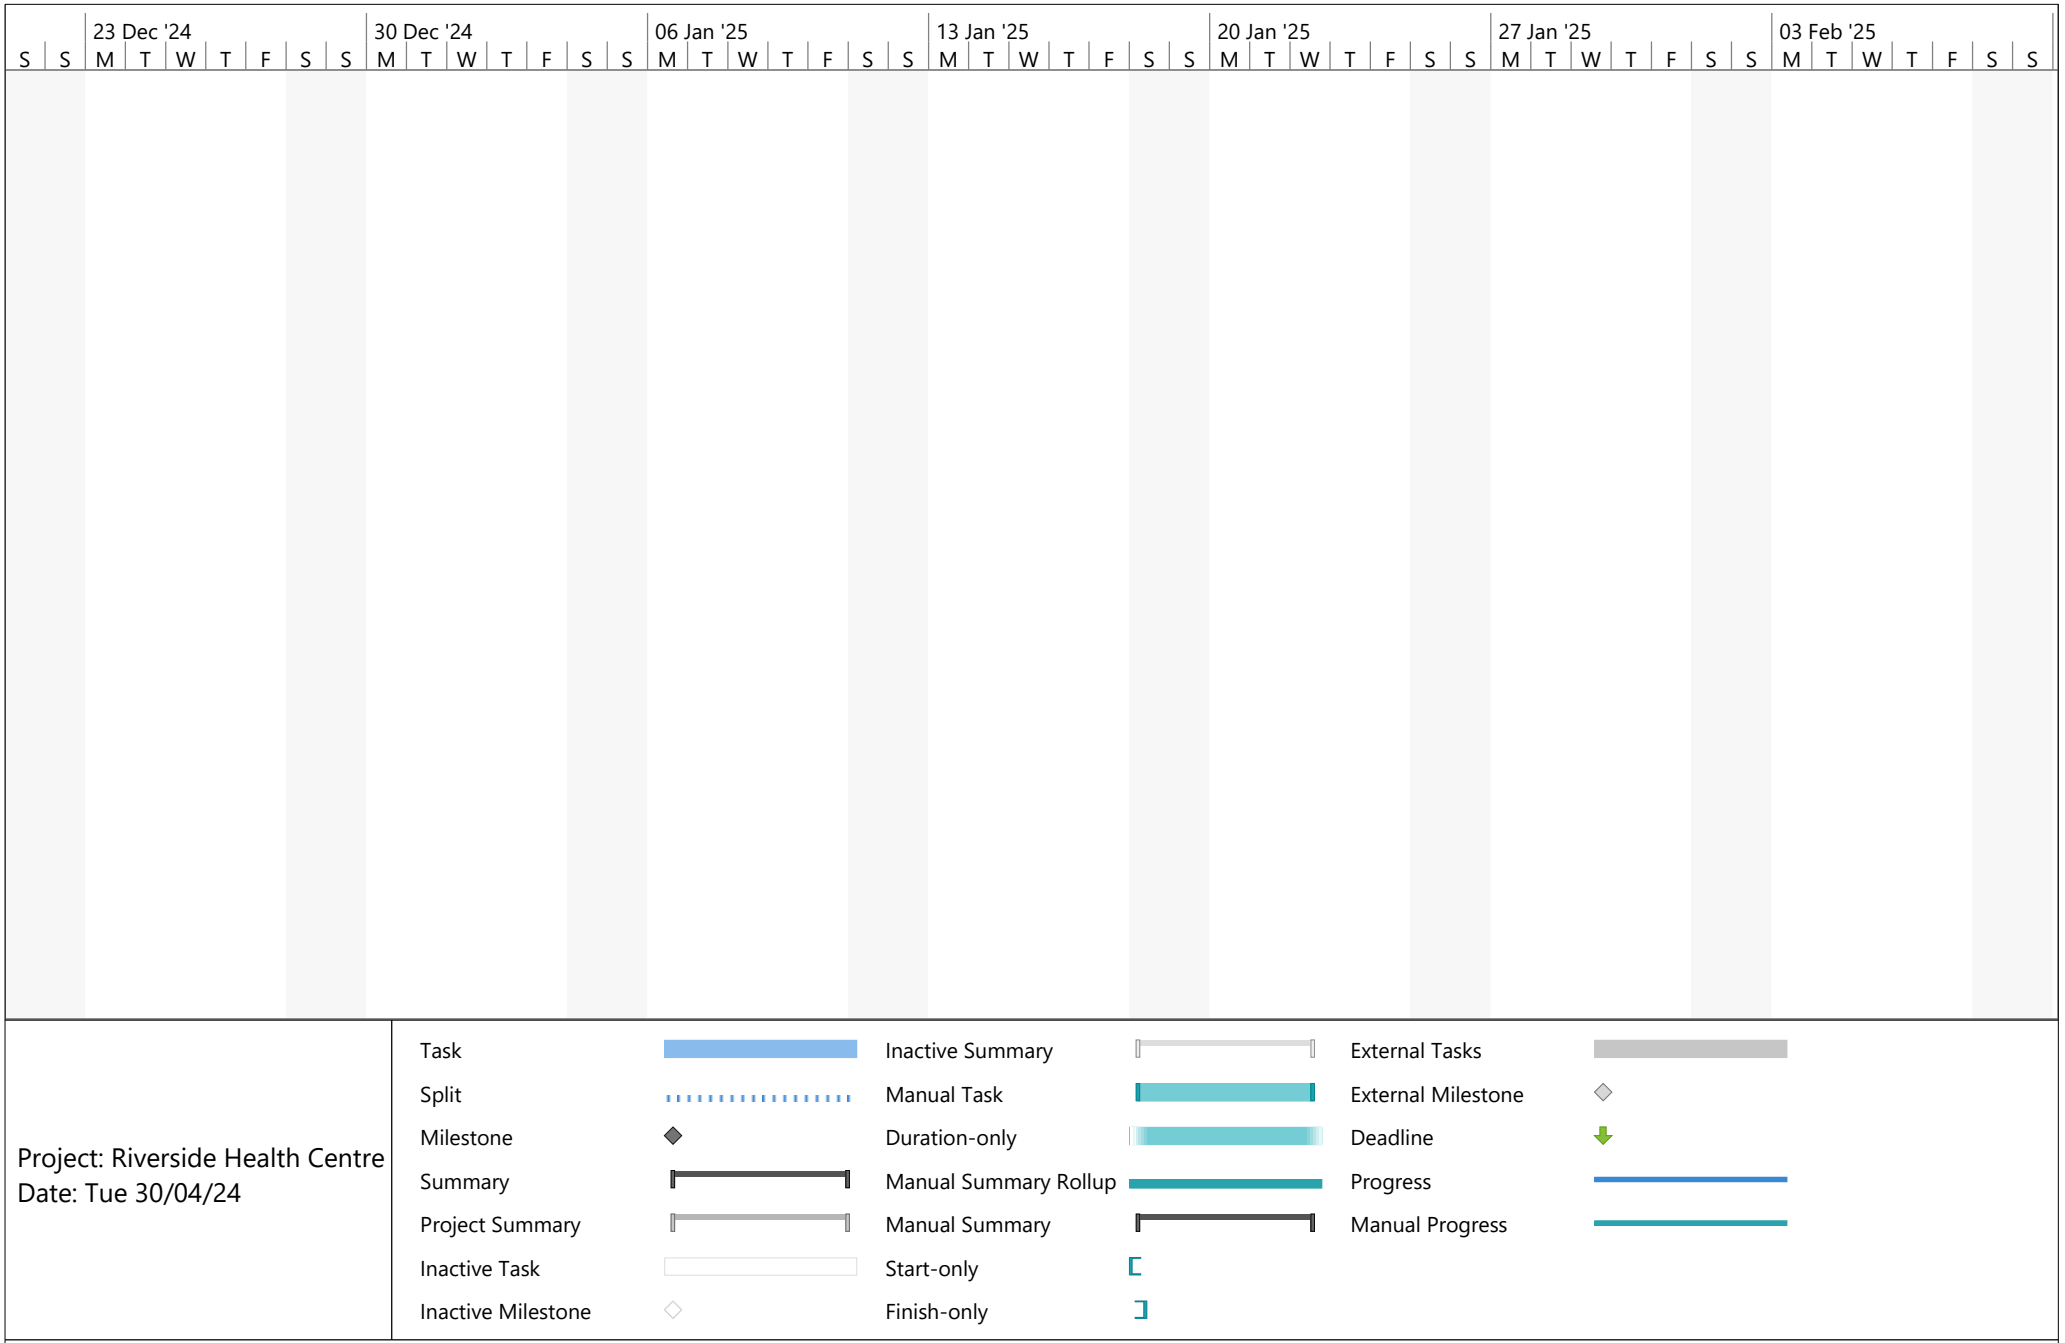


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

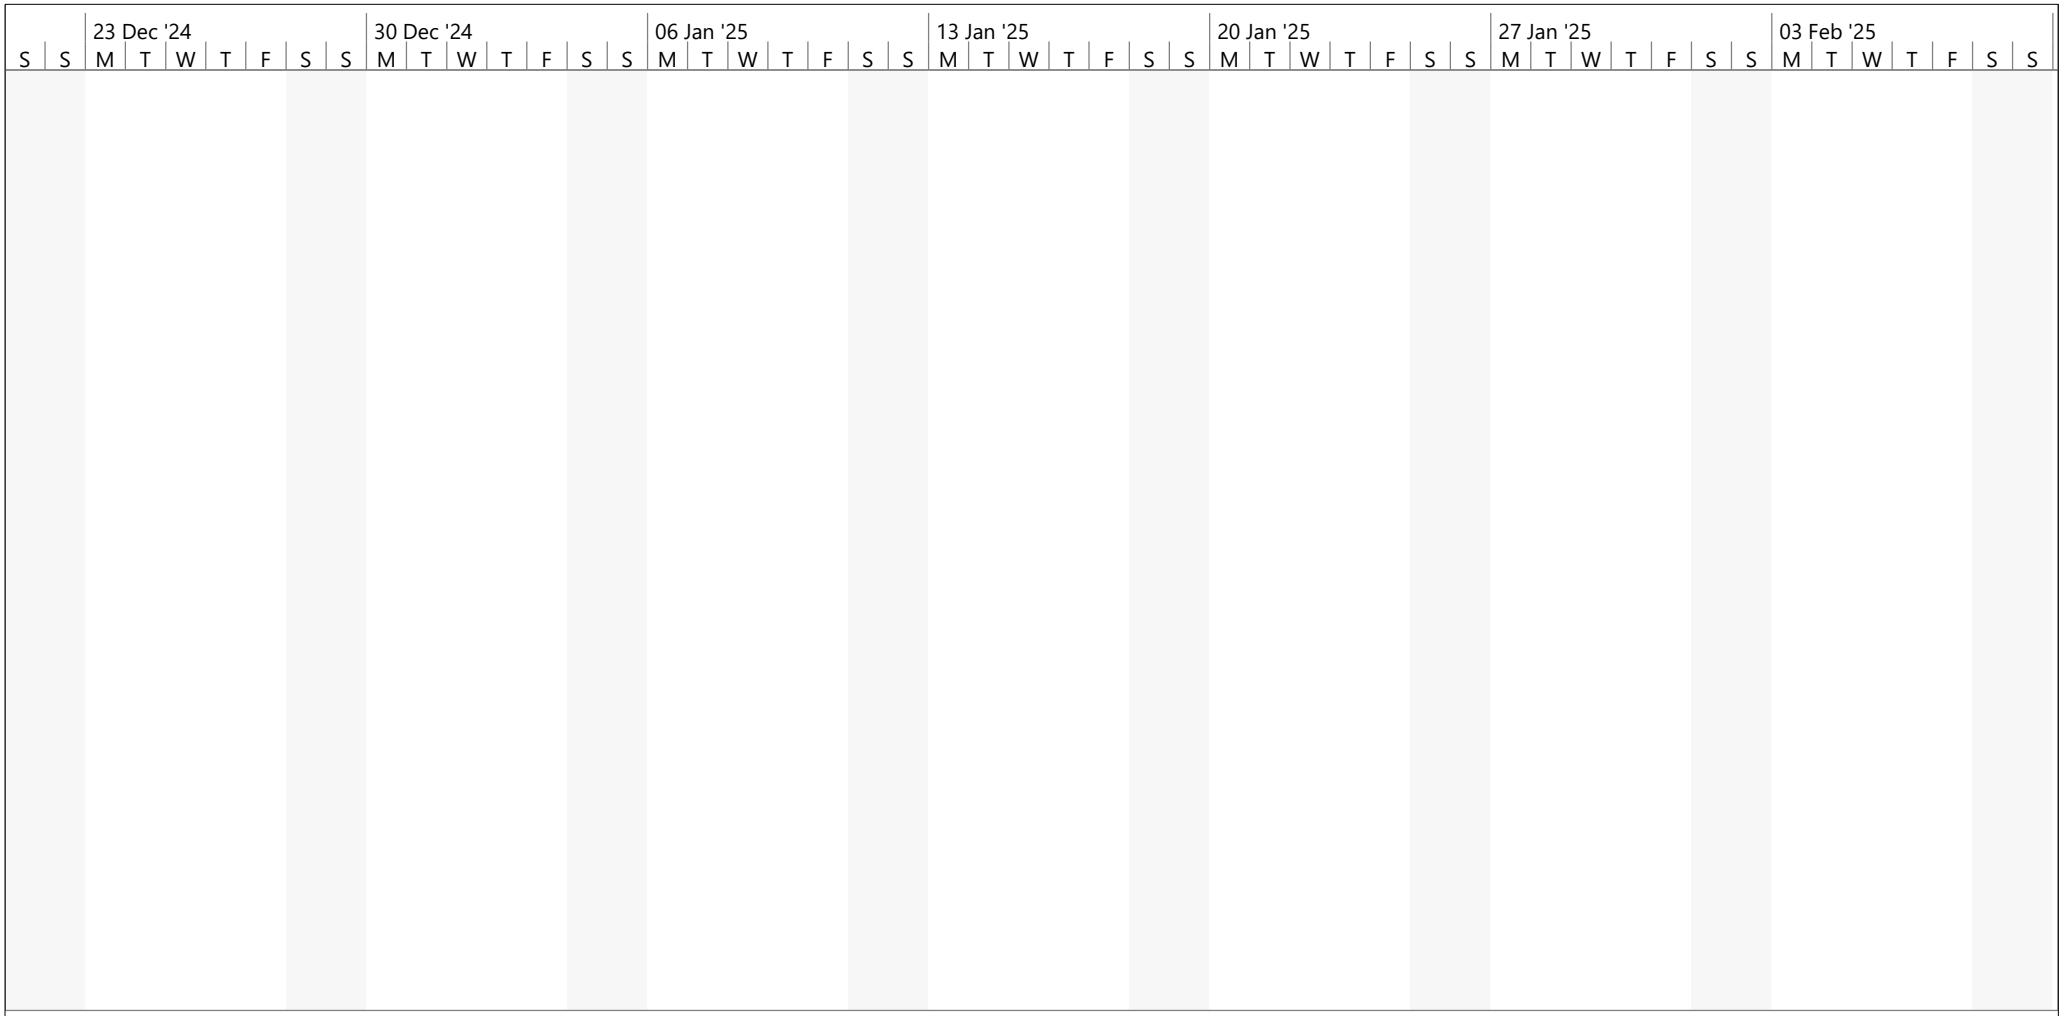


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

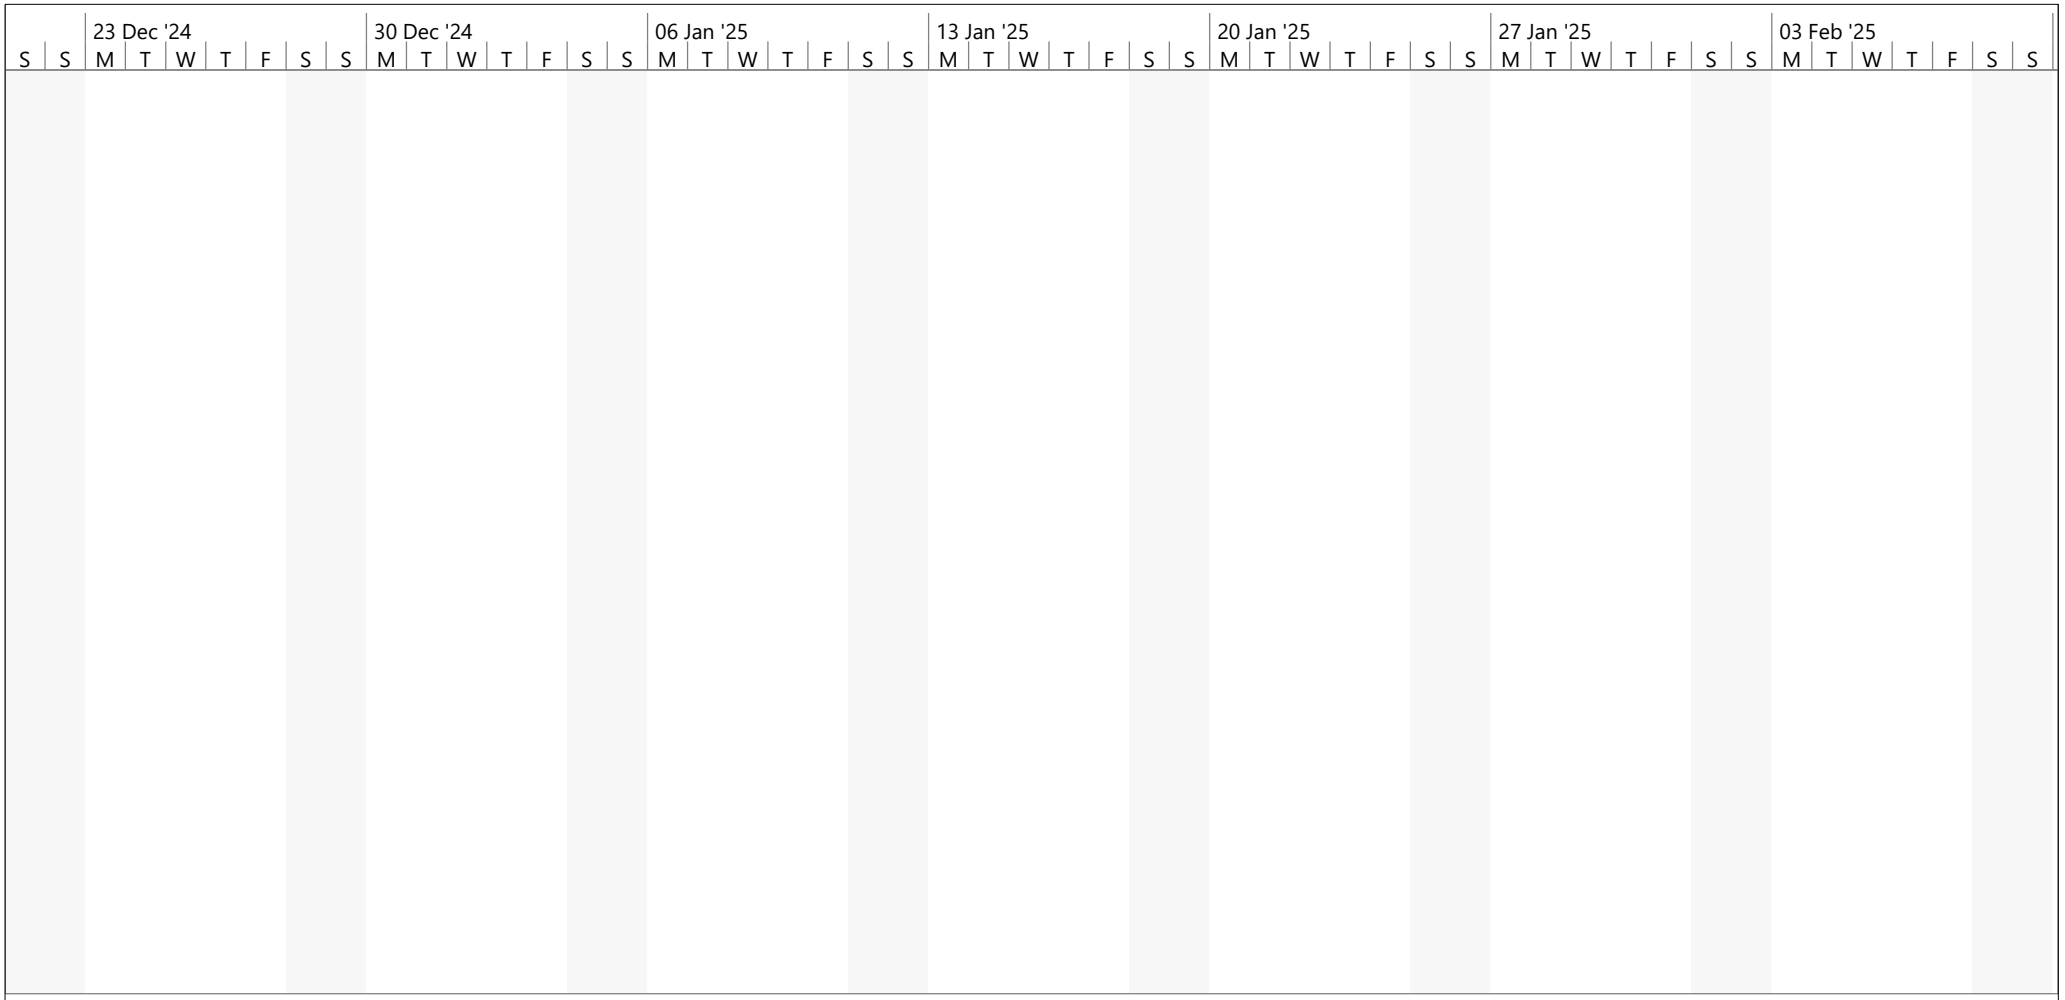


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

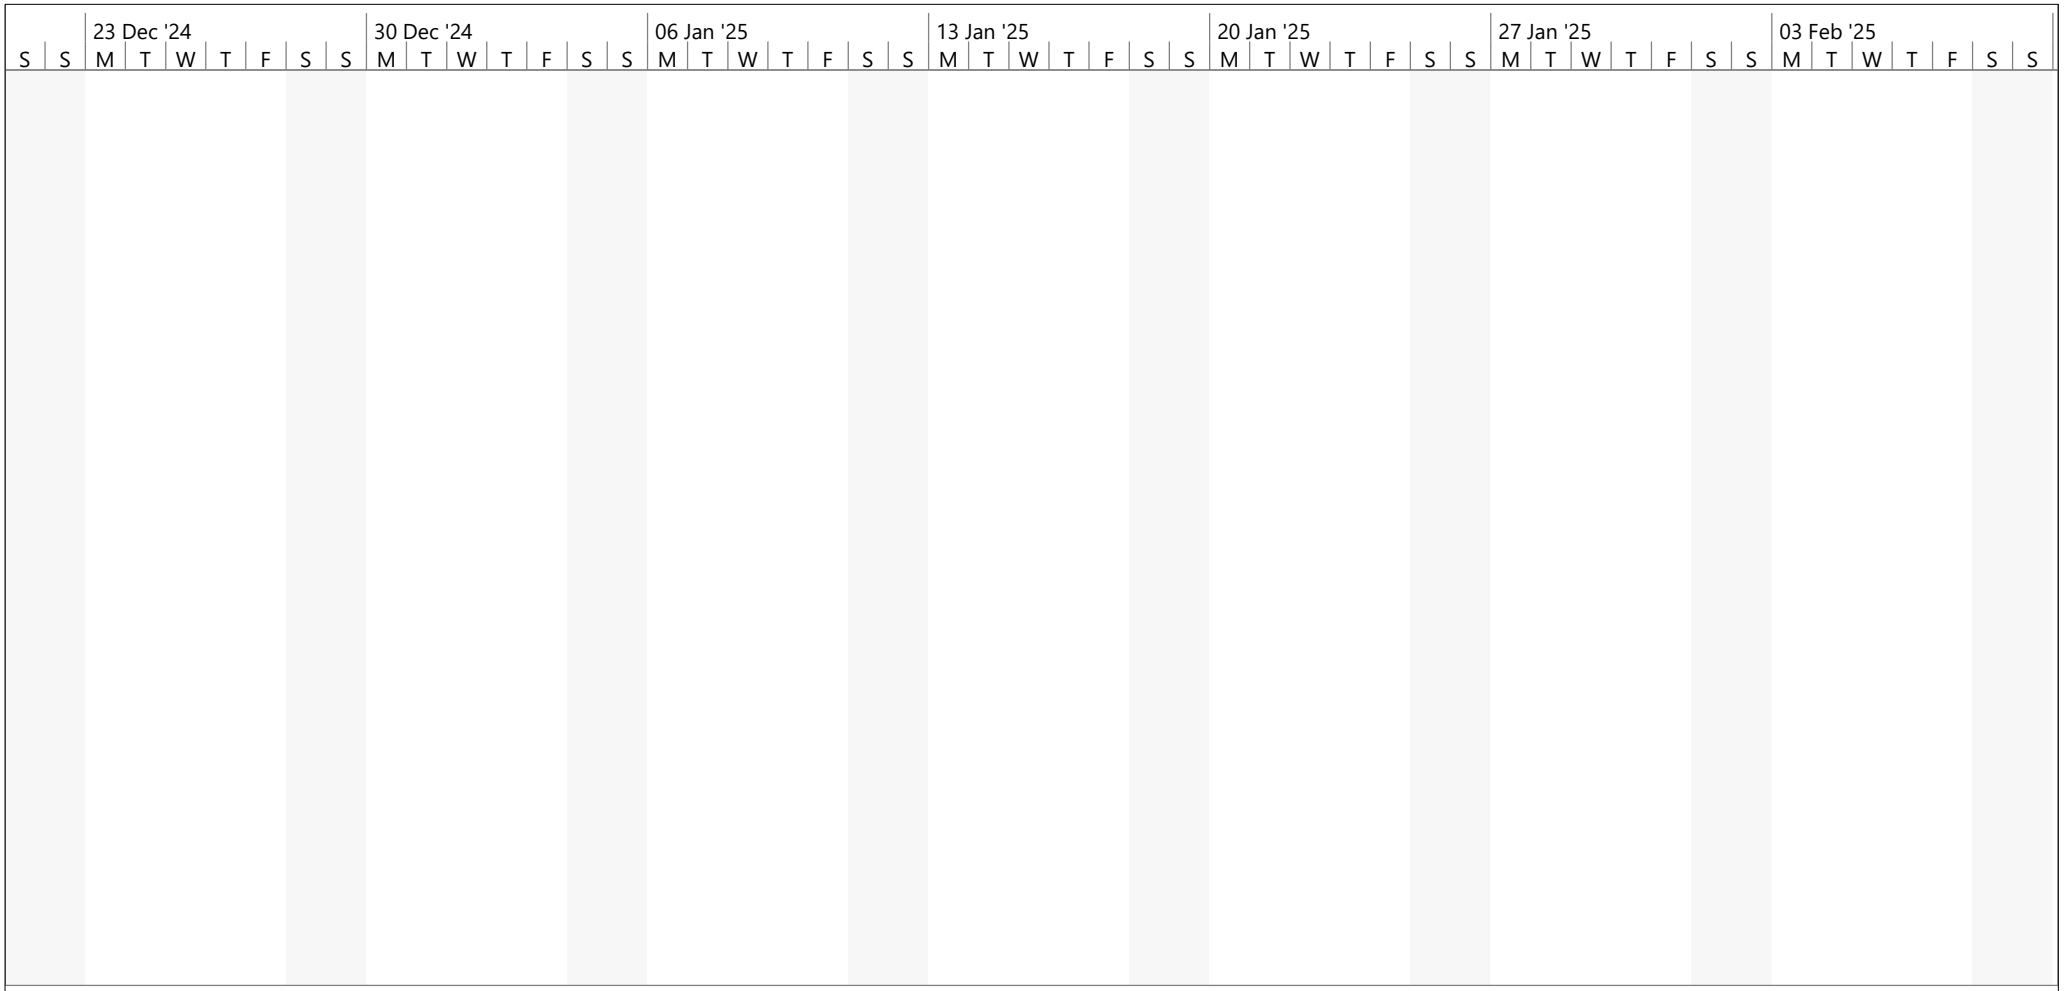


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

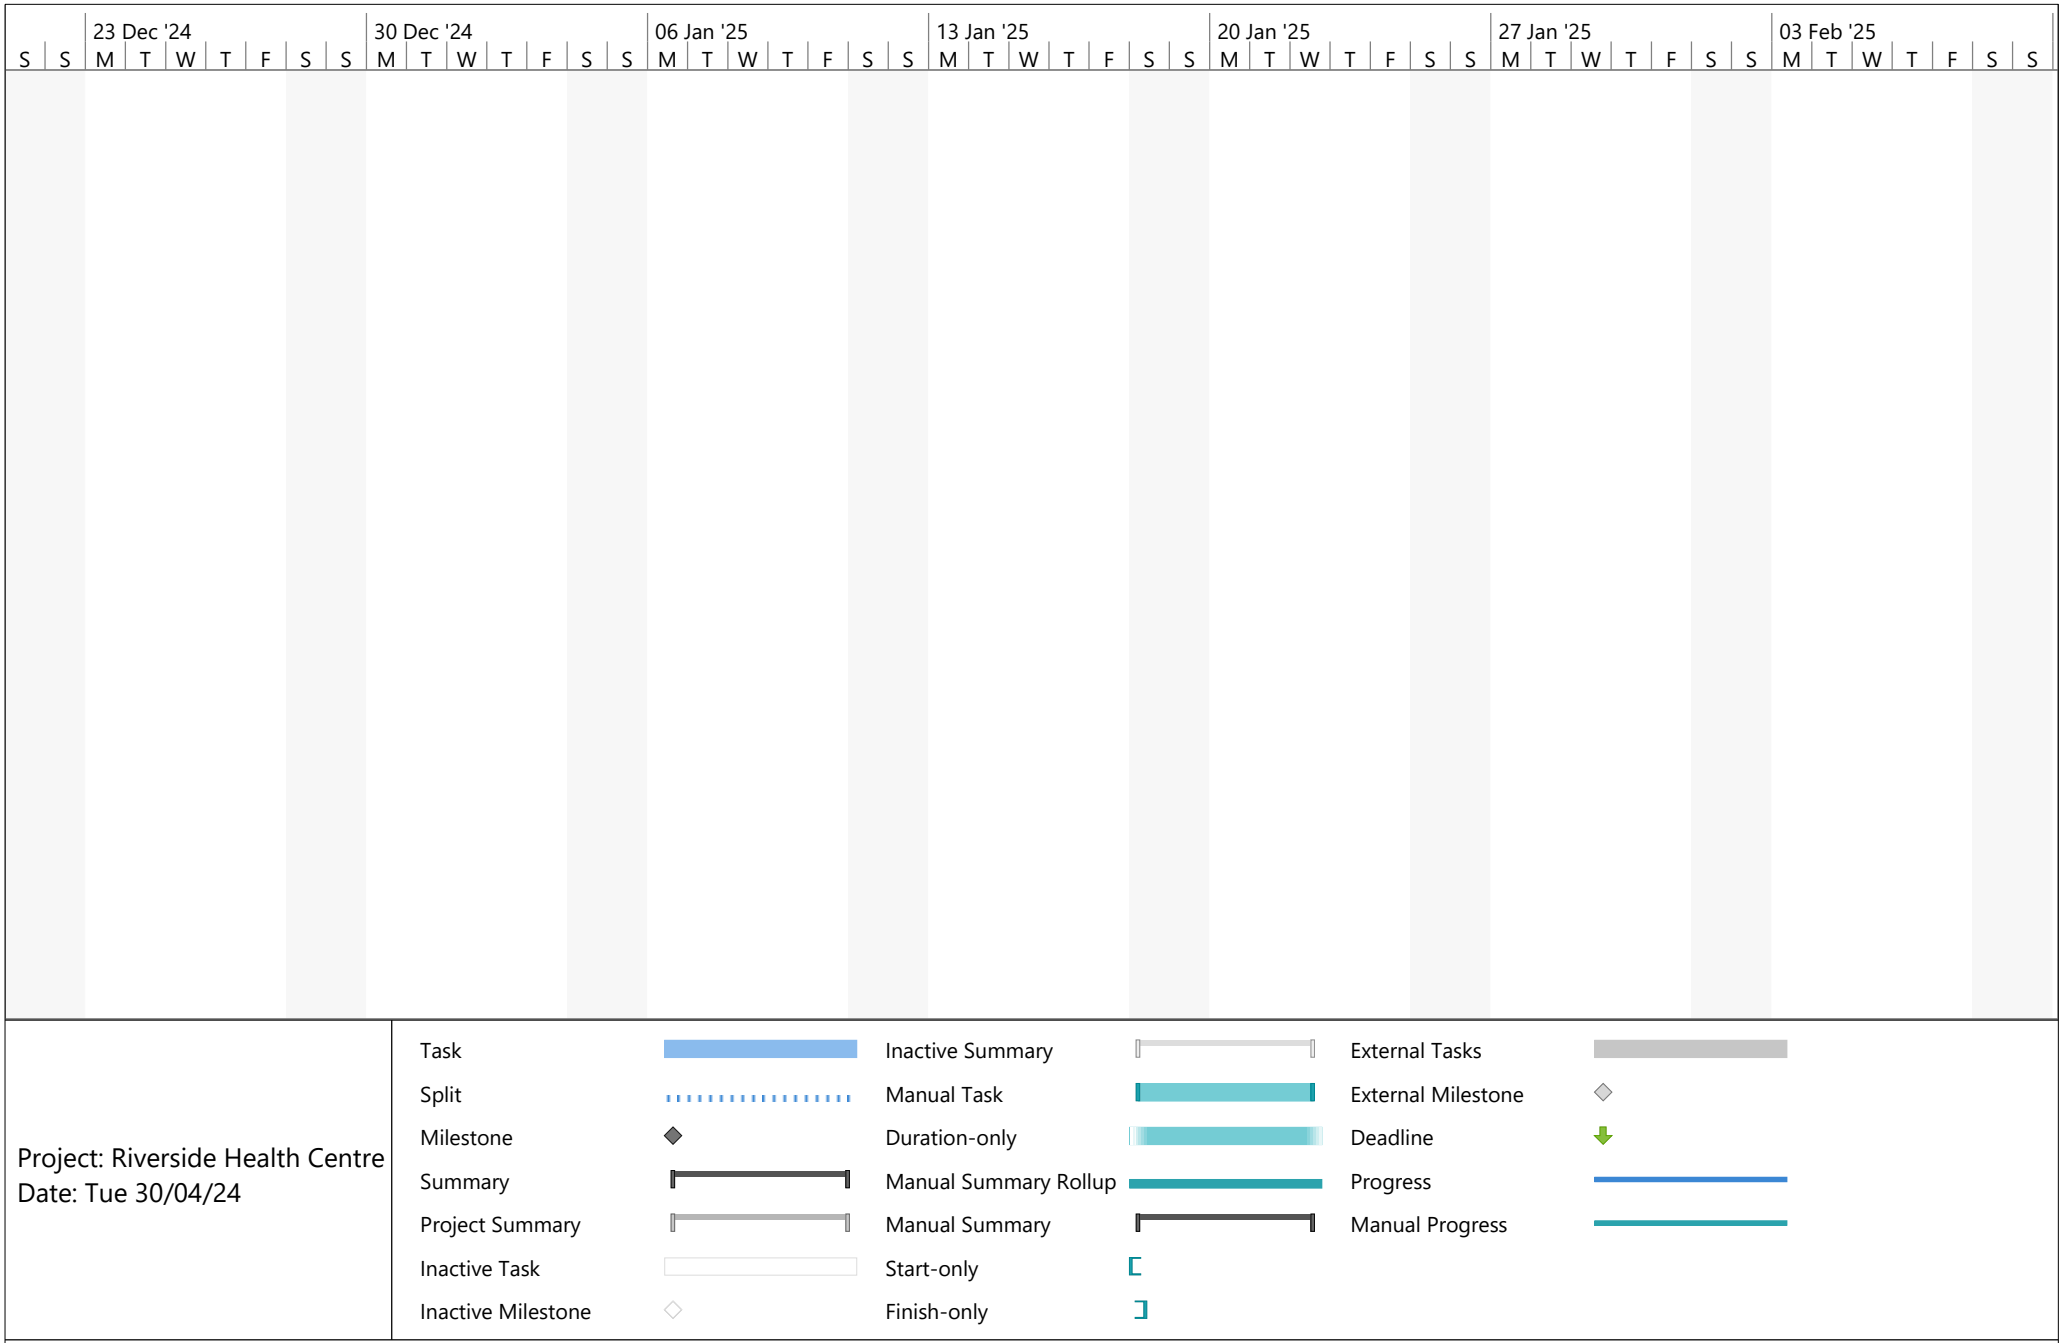


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

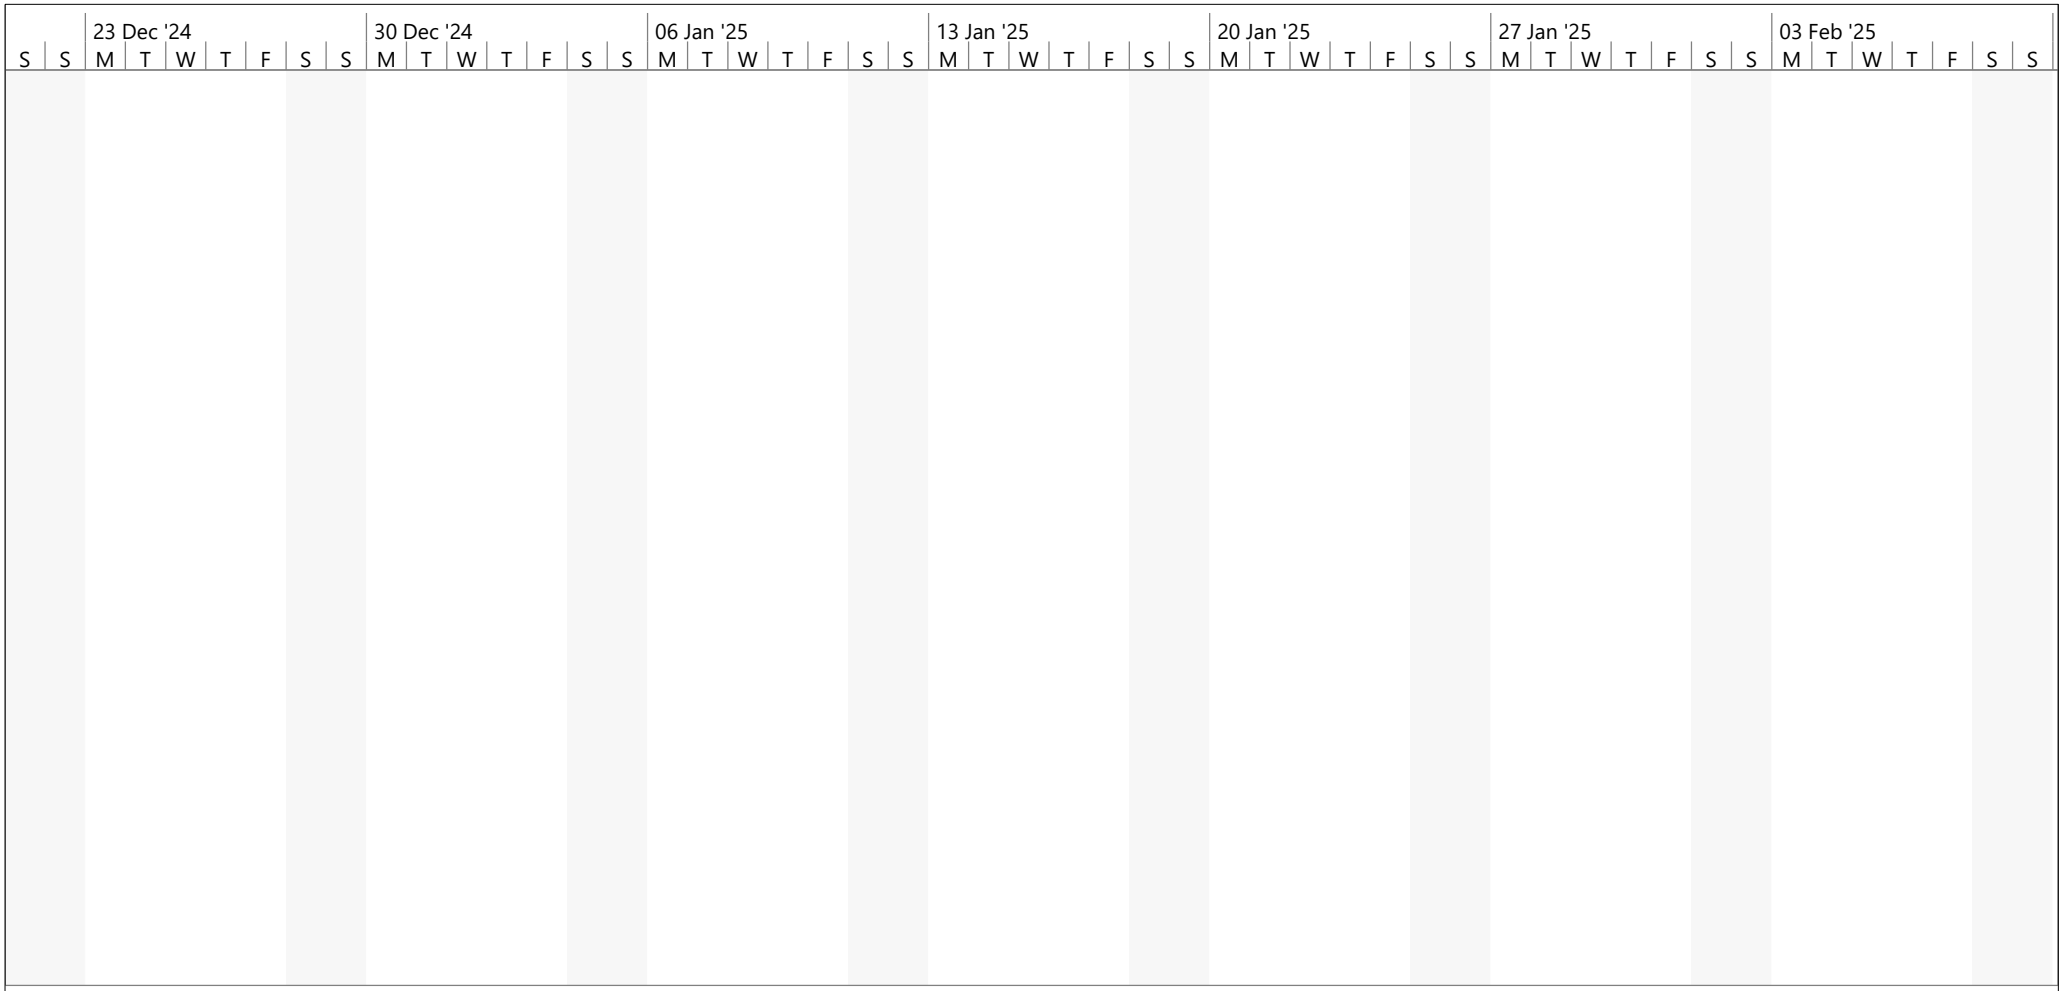


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

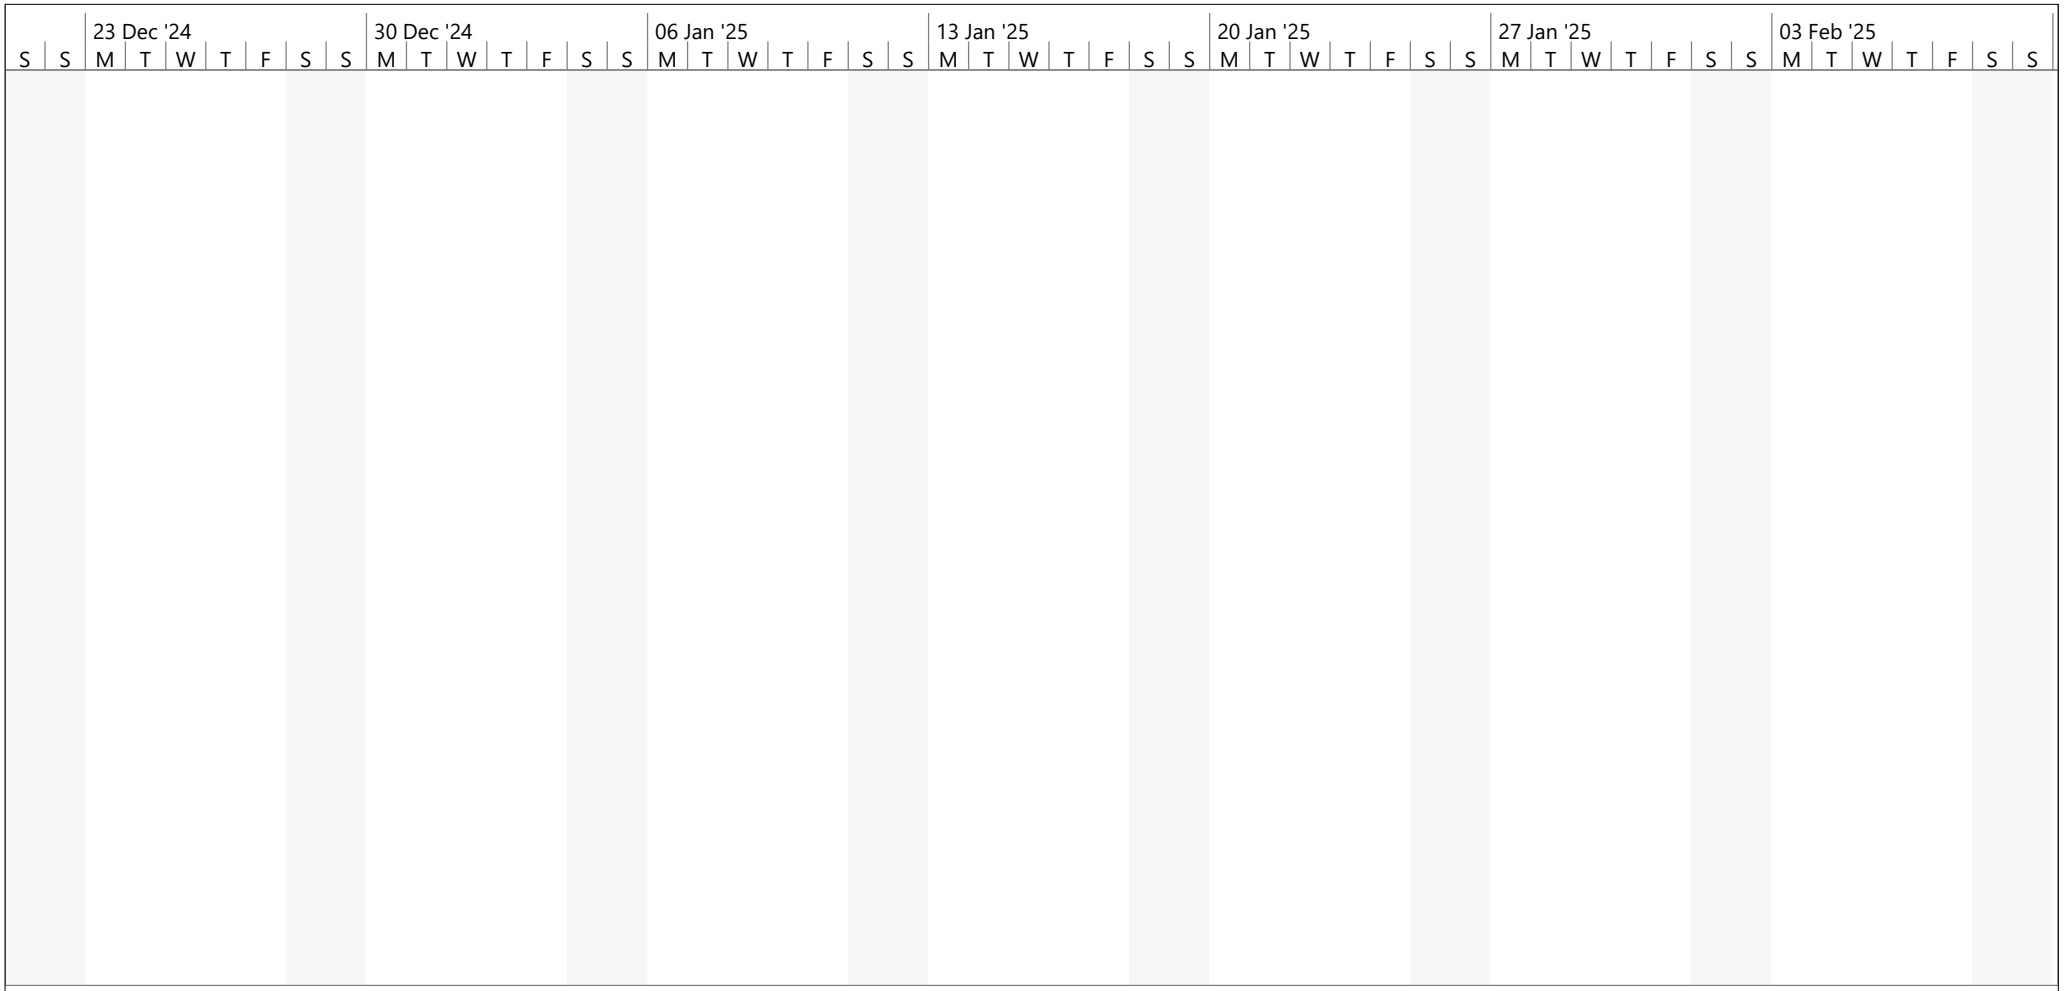


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

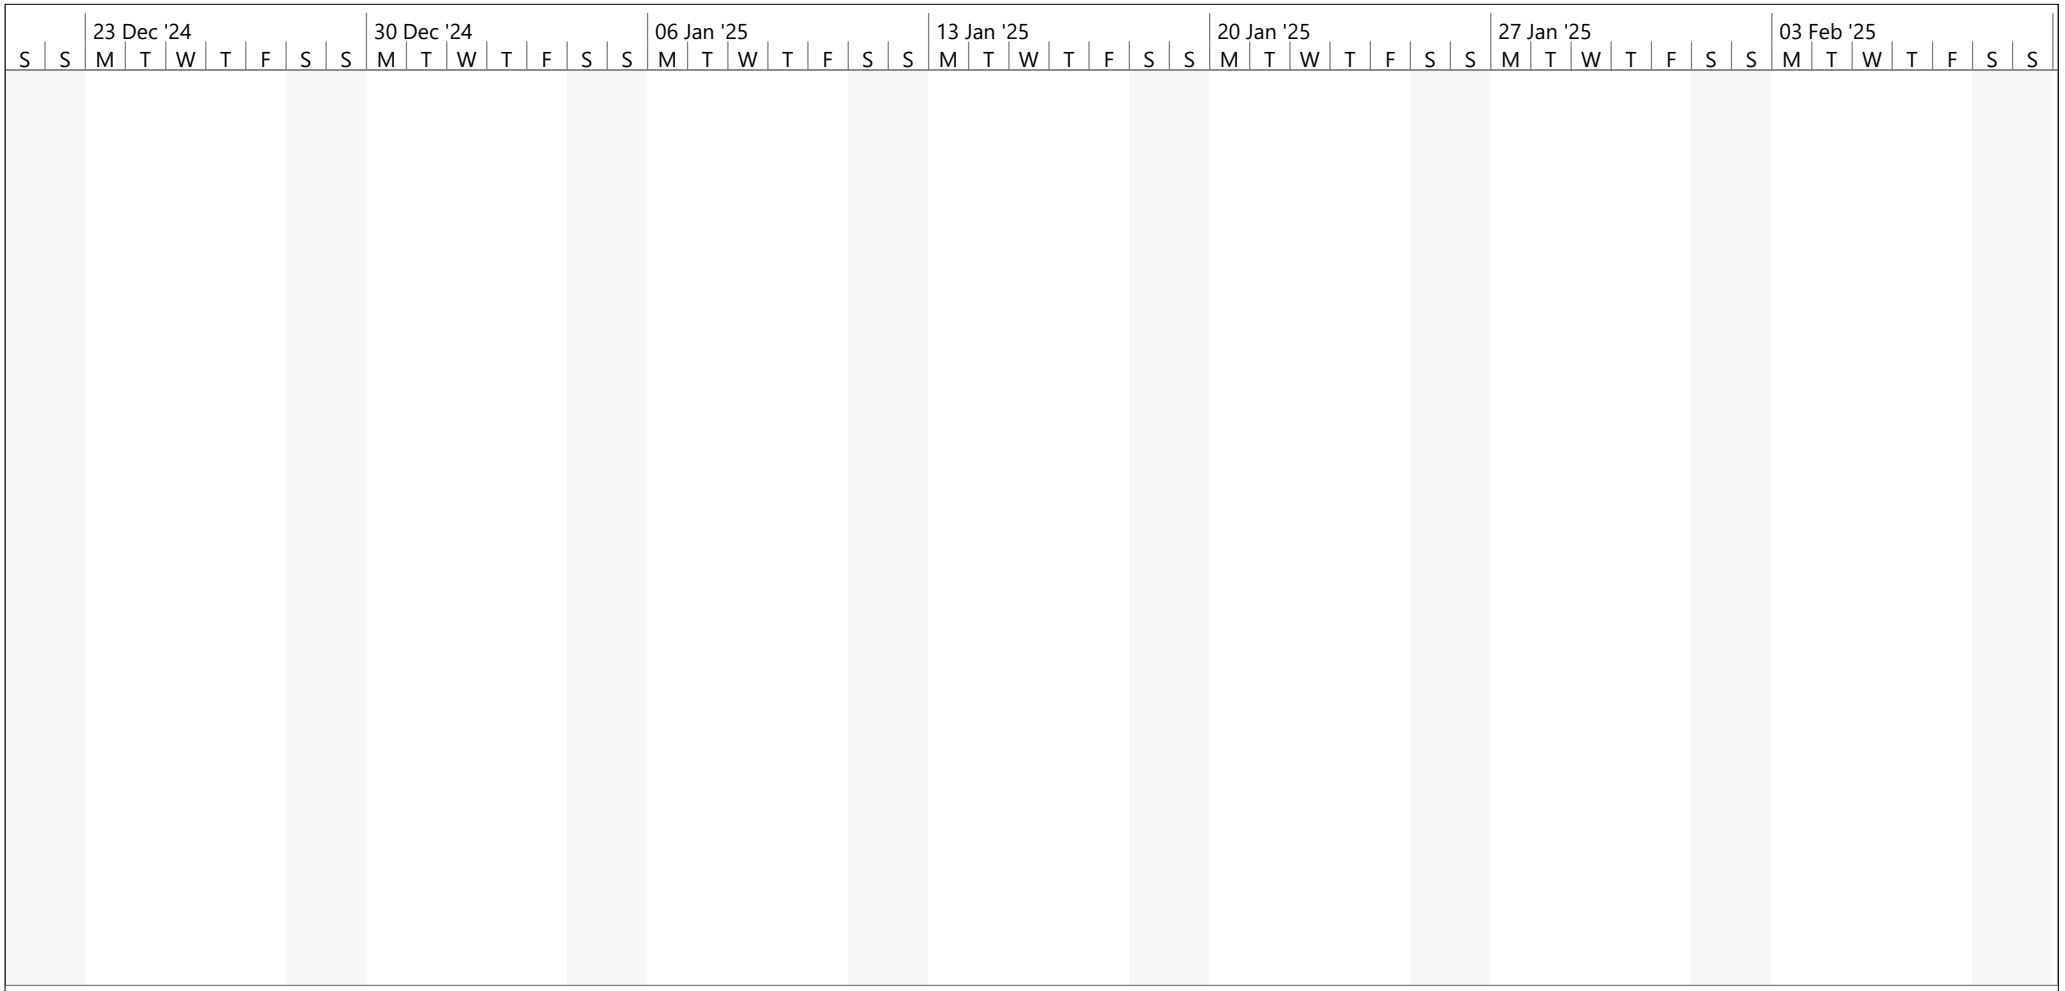


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

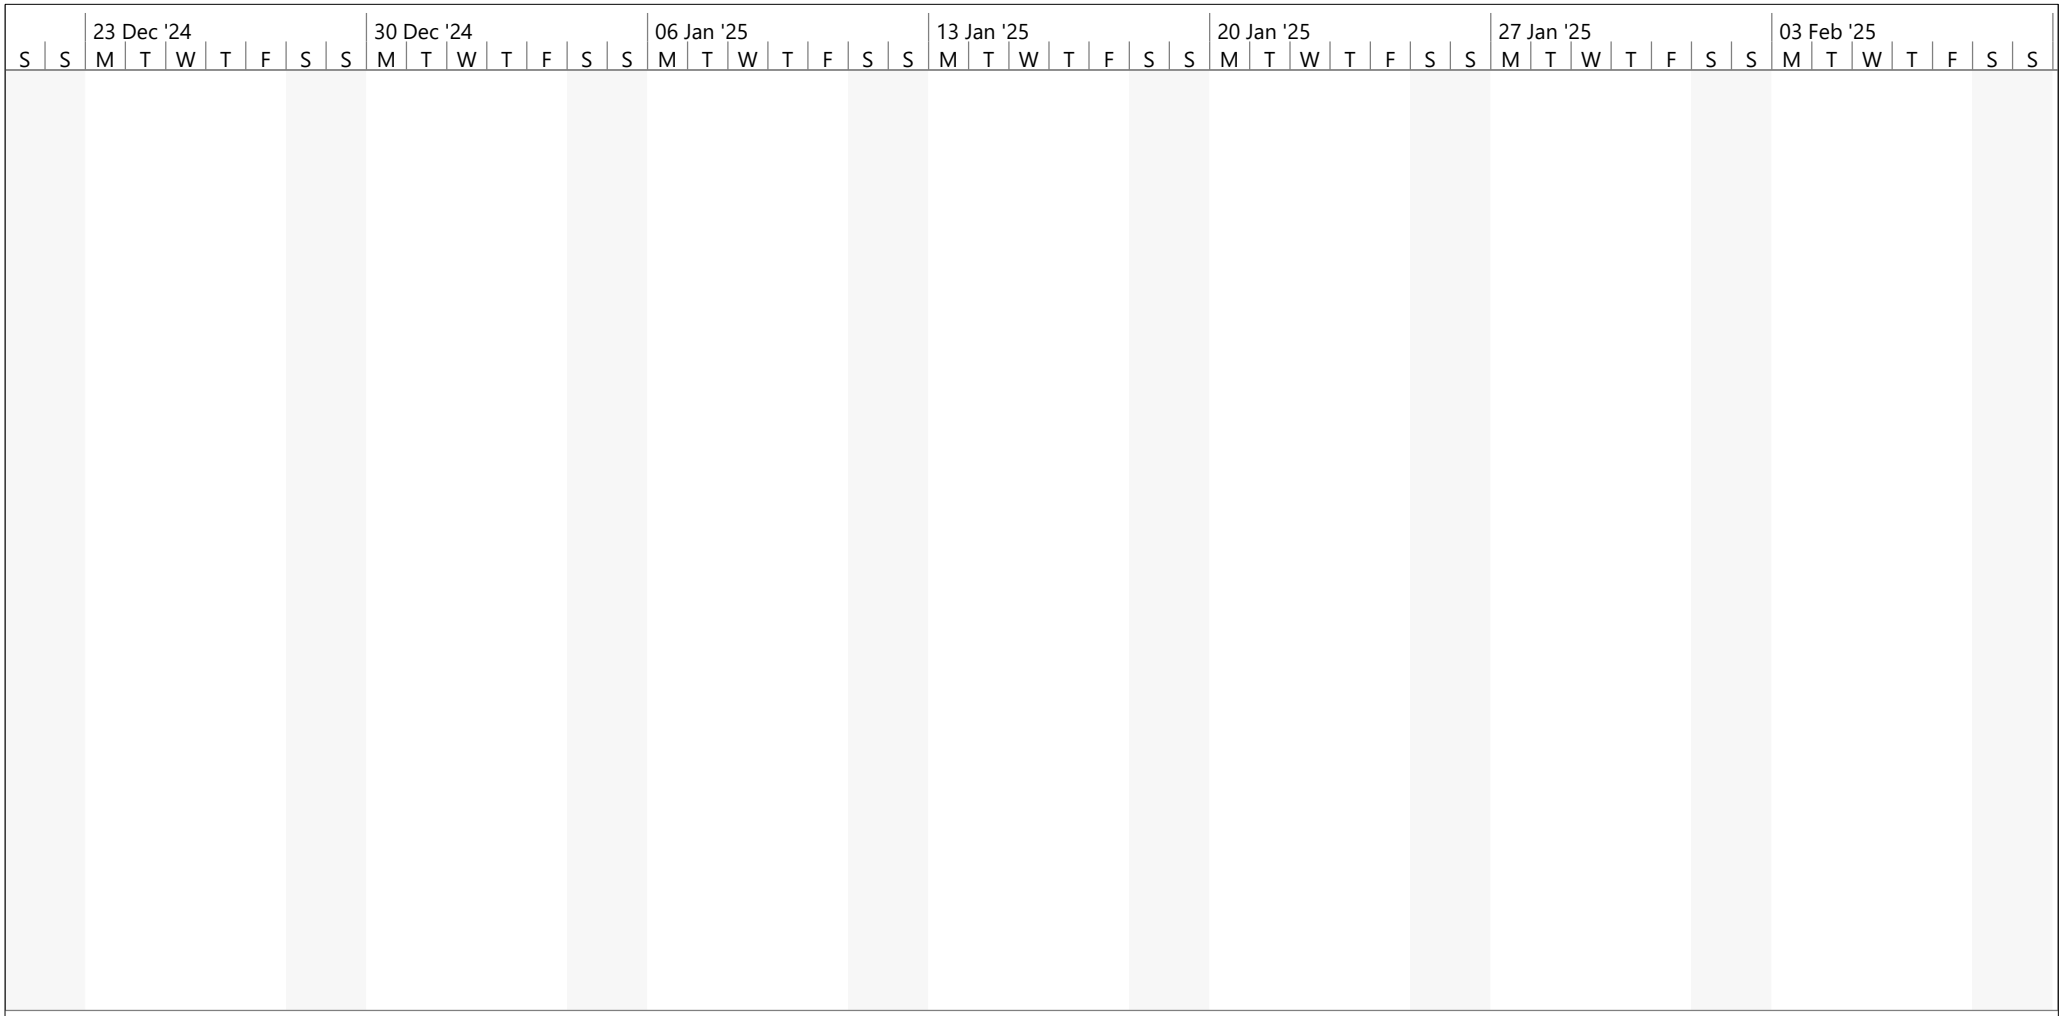


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

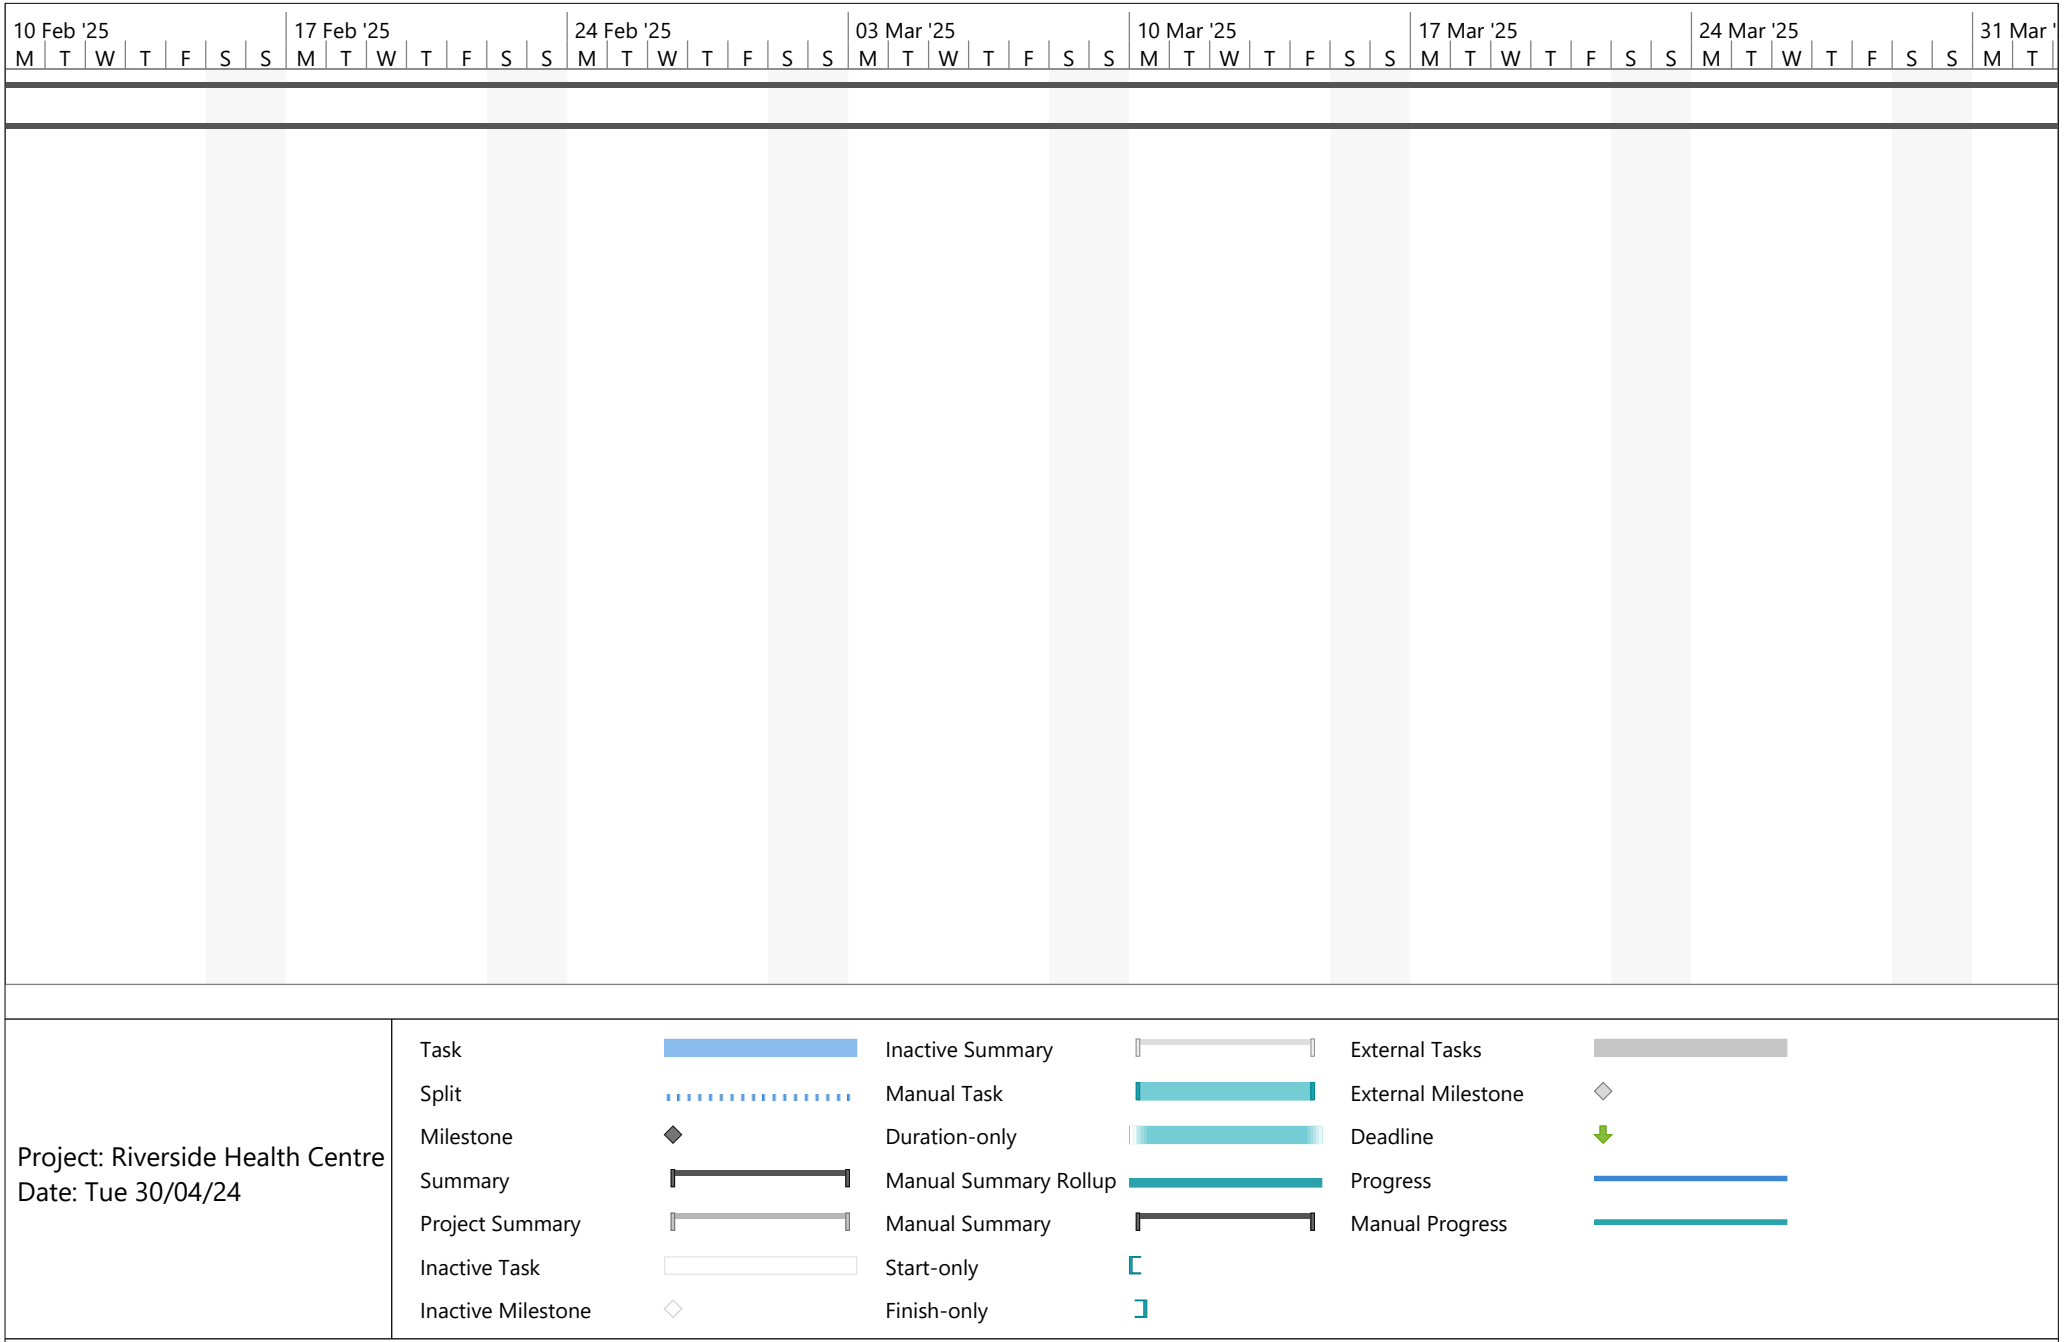


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

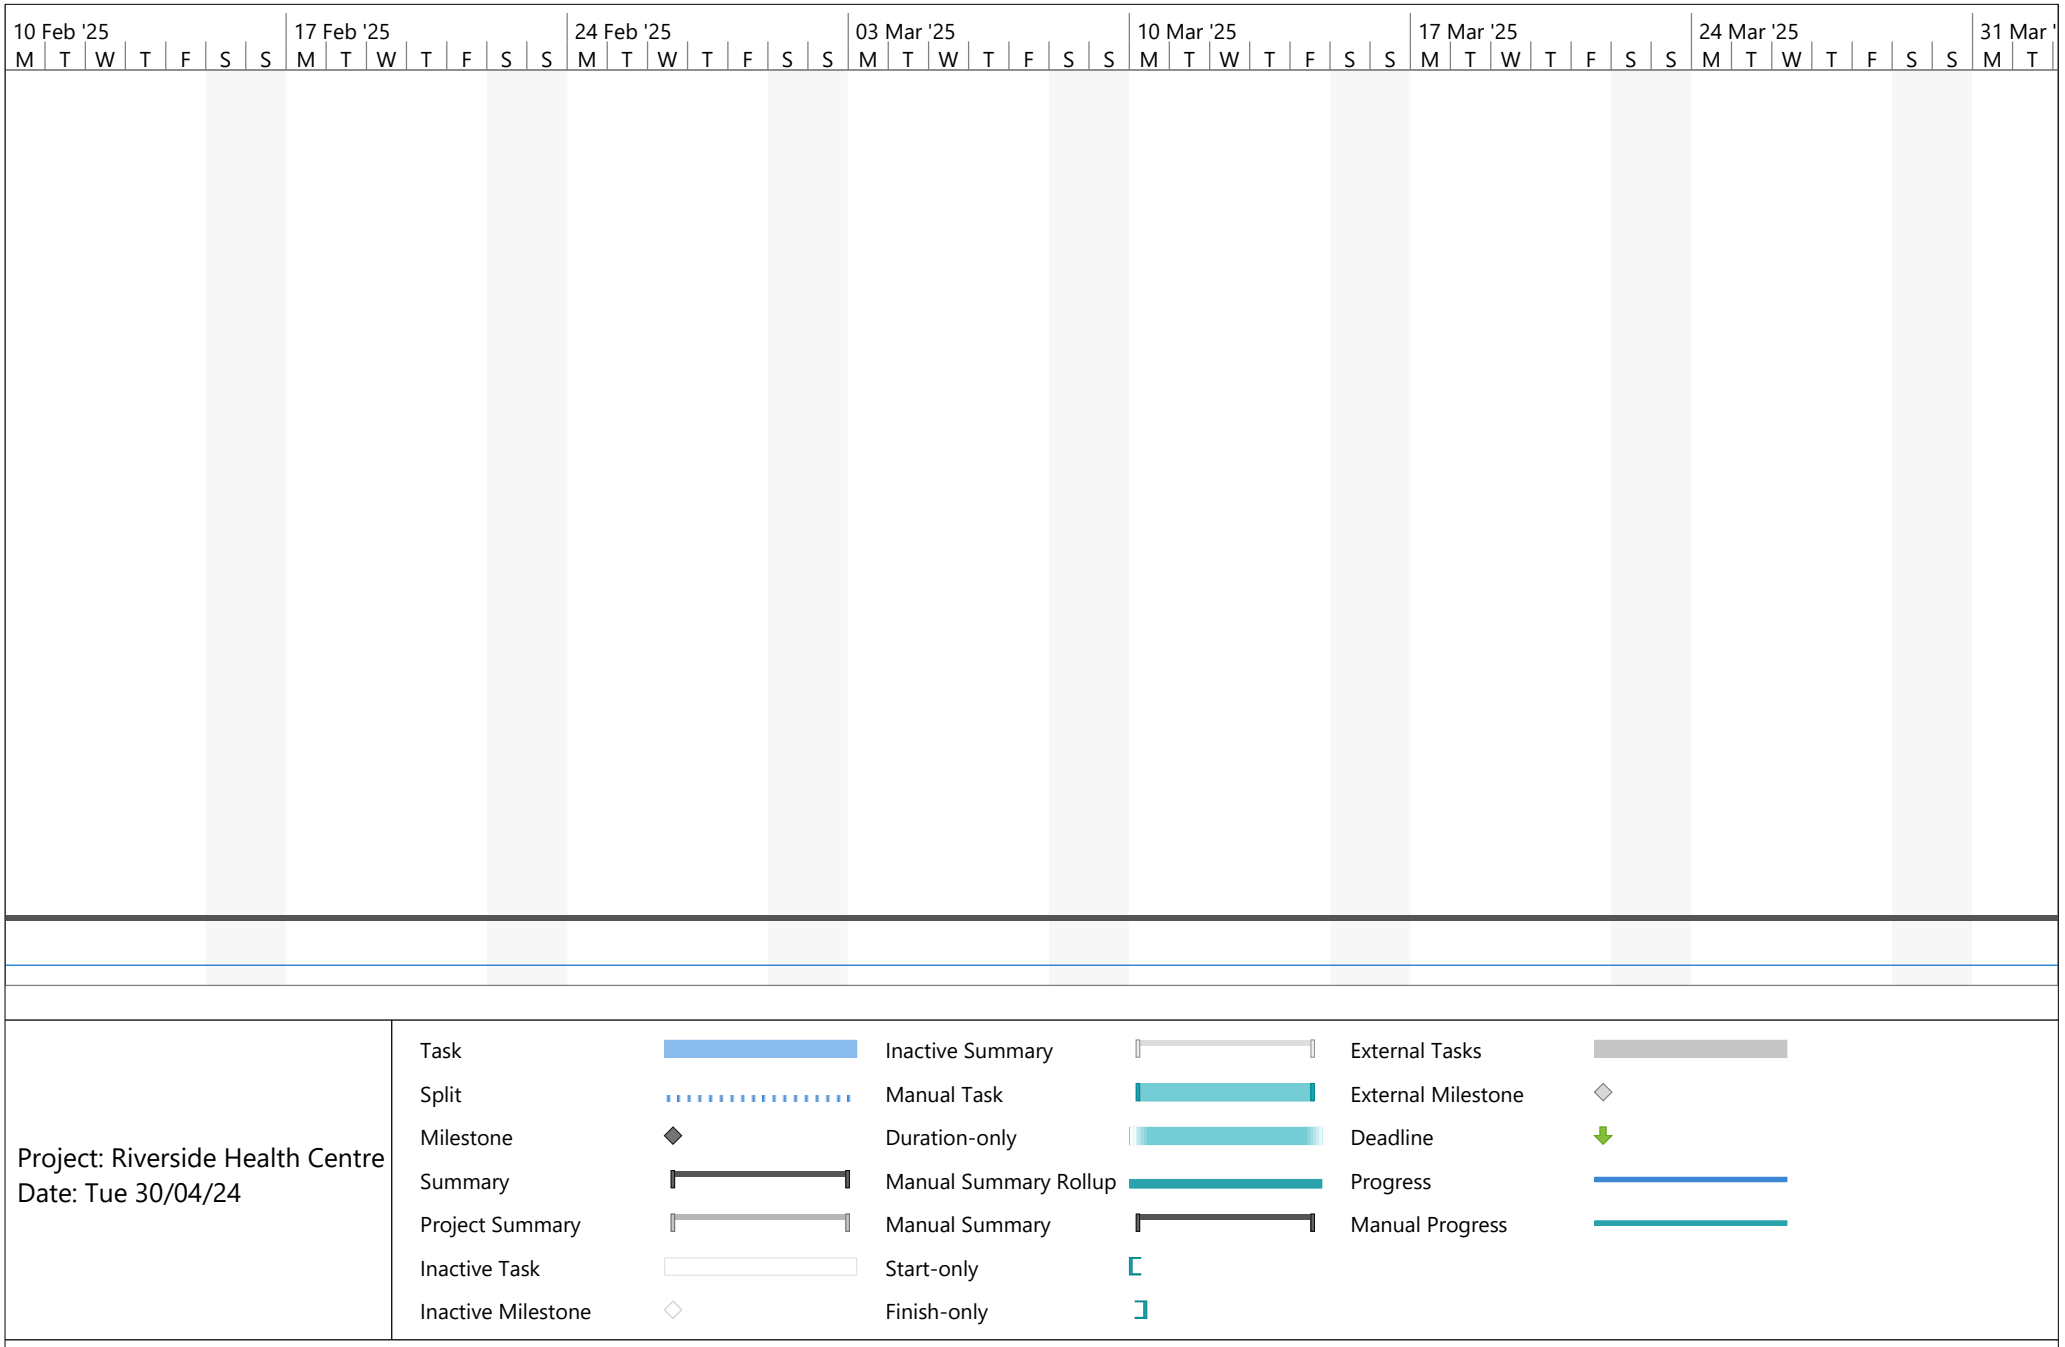


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

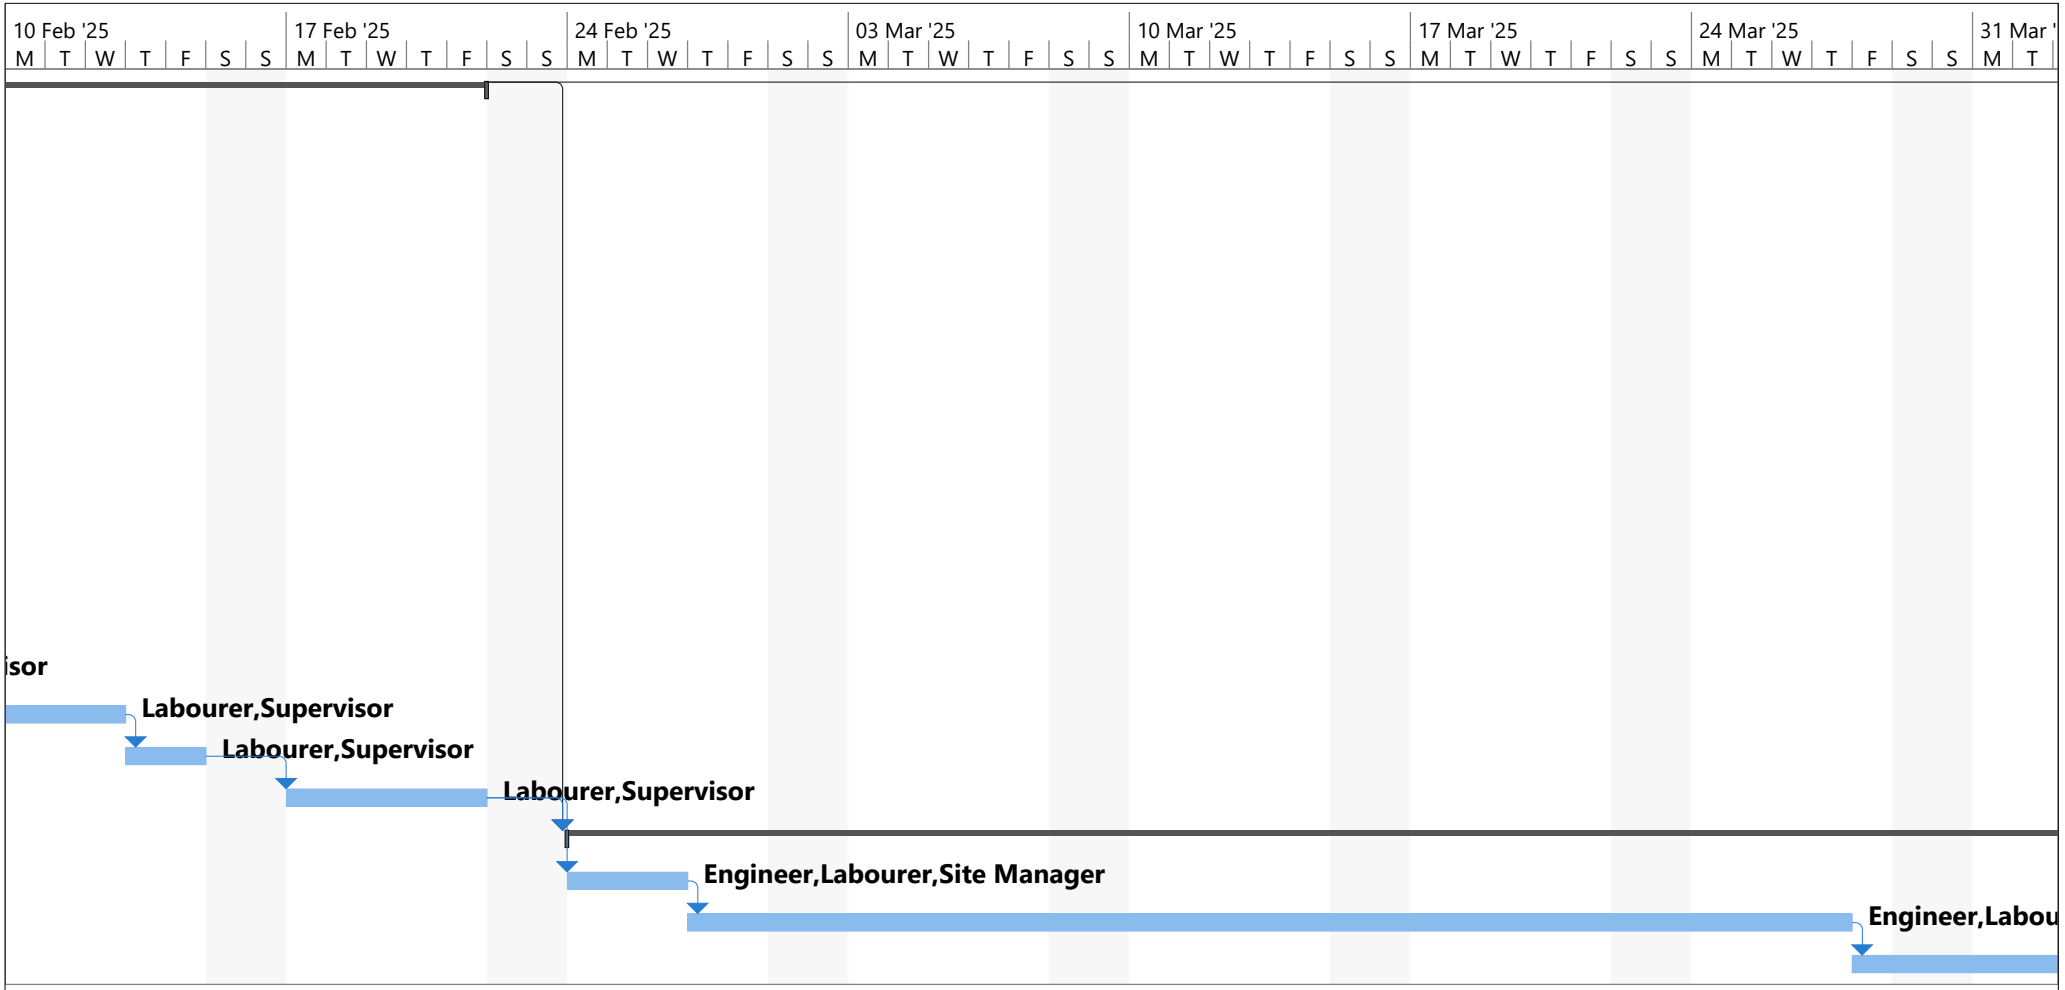

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

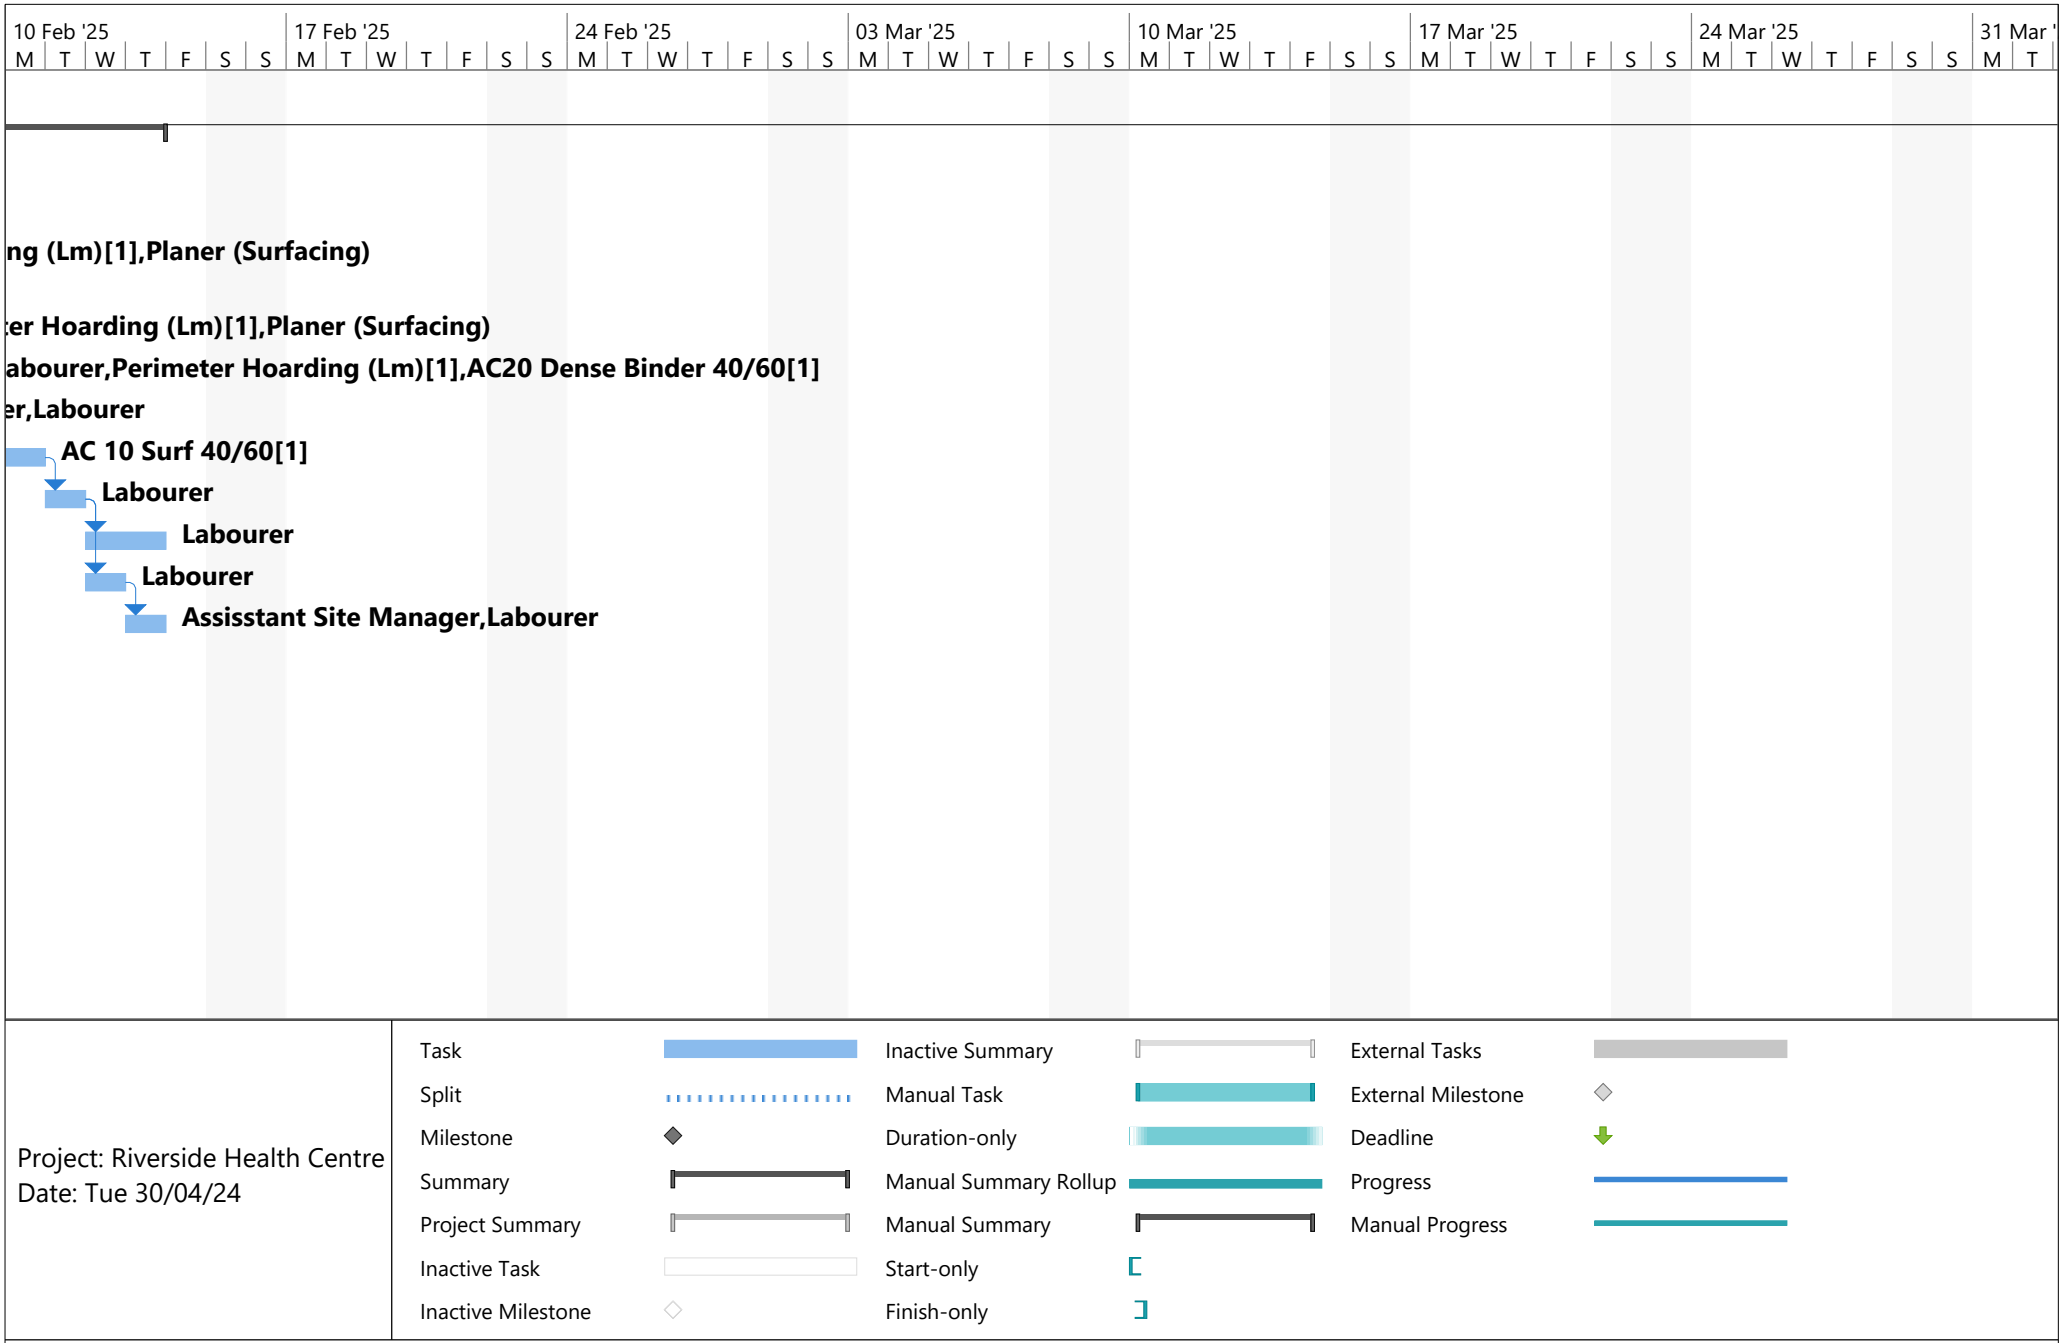
10 Feb '25
M T W T F S S
17 Feb '25
M T W T F S S
24 Feb '25
M T W T F S S
03 Mar '25
M T W T F S S
10 Mar '25
M T W T F S S
17 Mar '25
M T W T F S S
24 Mar '25
M T W T F S S
31 Mar '
M T
ng (Lm)[1],Planer (Surfacing)
er Hoarding (Lm)[1],Planer (Surfacing)
abourer,Perimeter Hoarding (Lm)[1],AC20 Dense Binder 40/60[1]
er,Labourer
AC 10 Surf 40/60[1]
Labourer
Labourer
Labourer
Assisstant Site Manager,Labourer
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

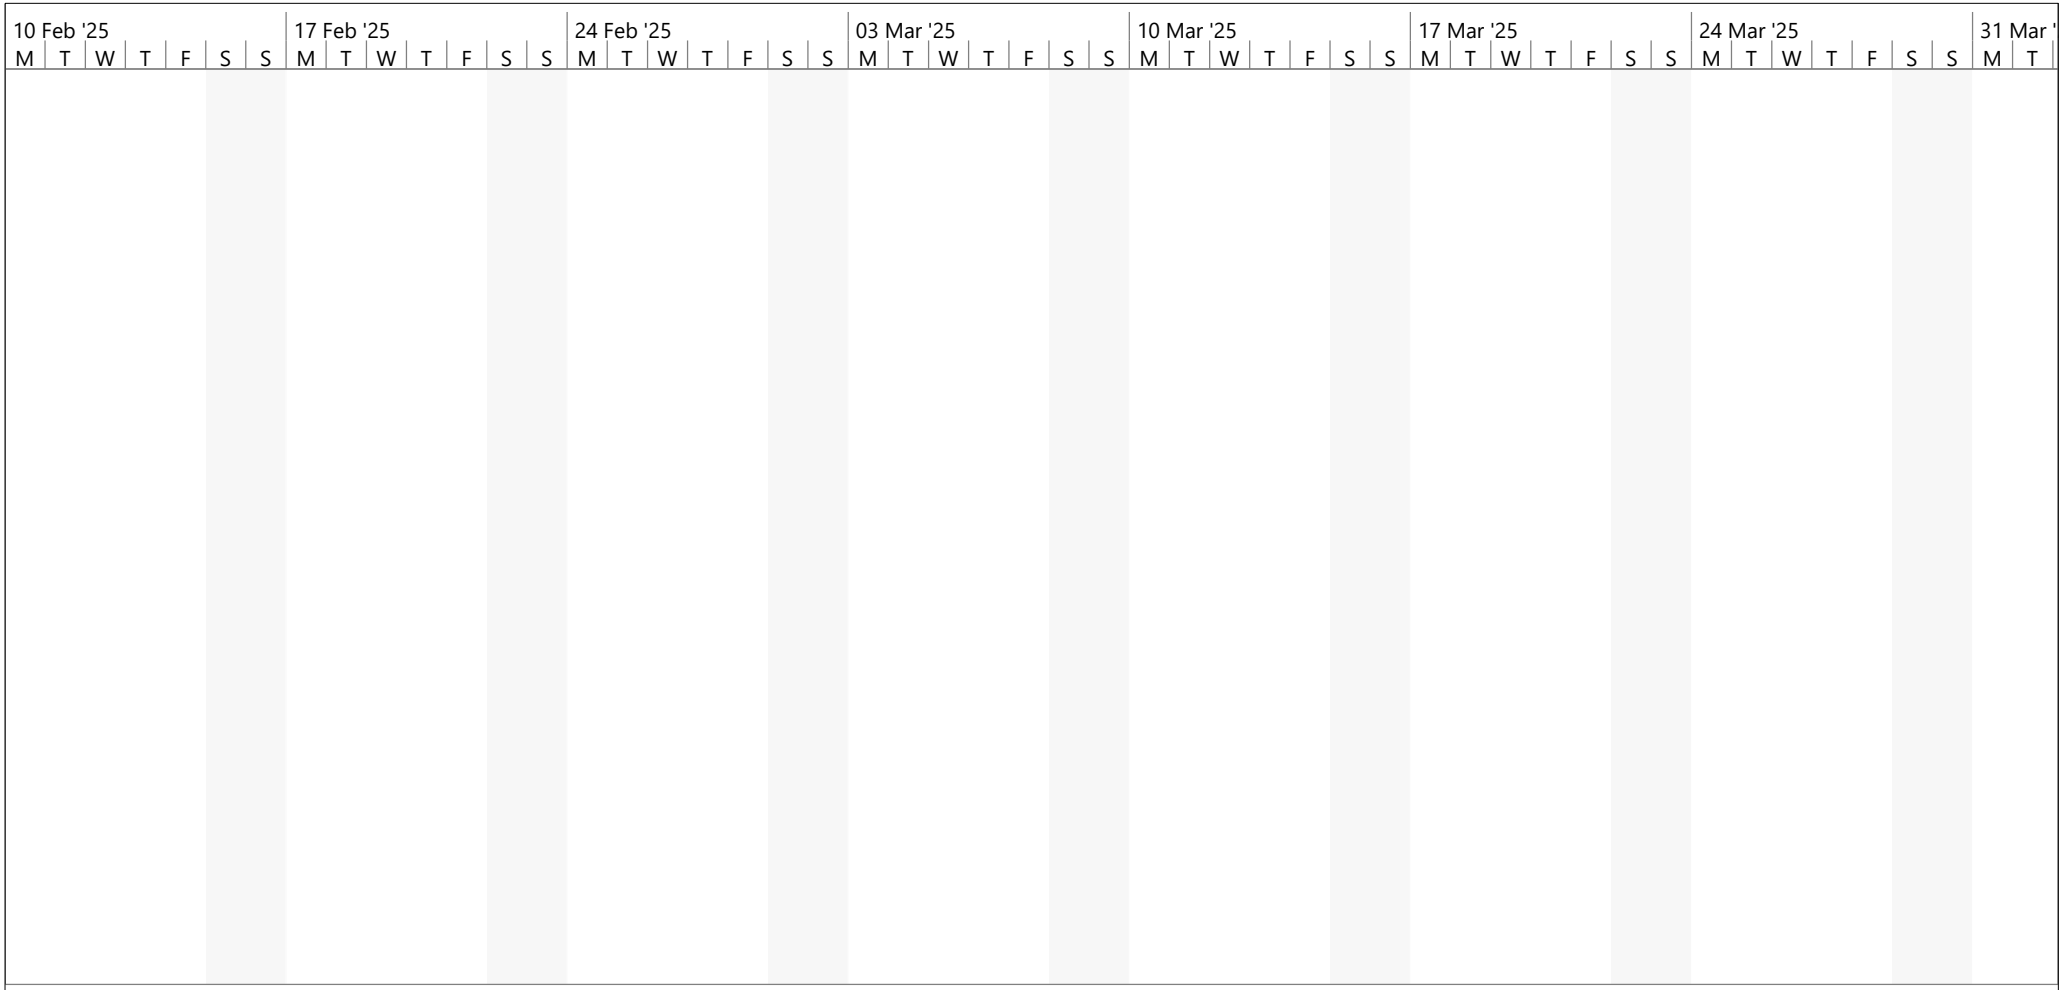


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

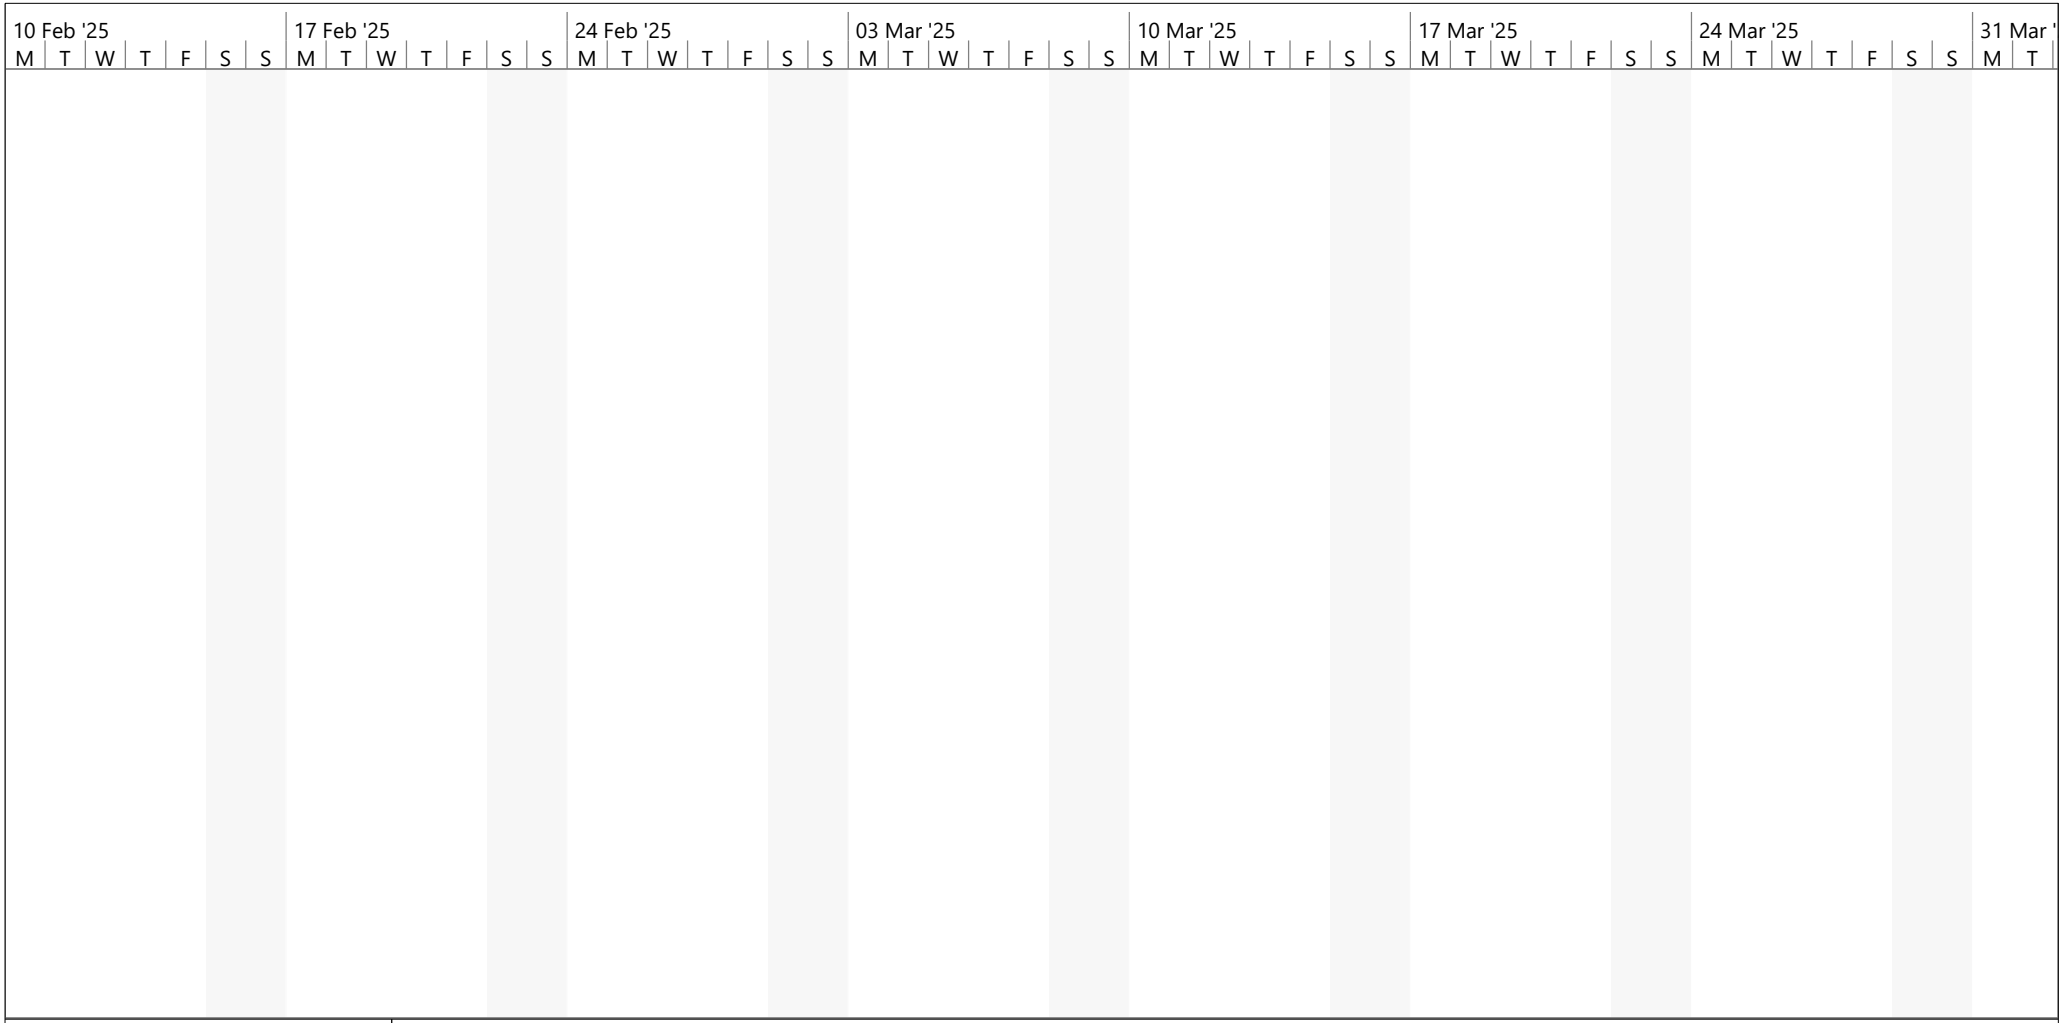


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

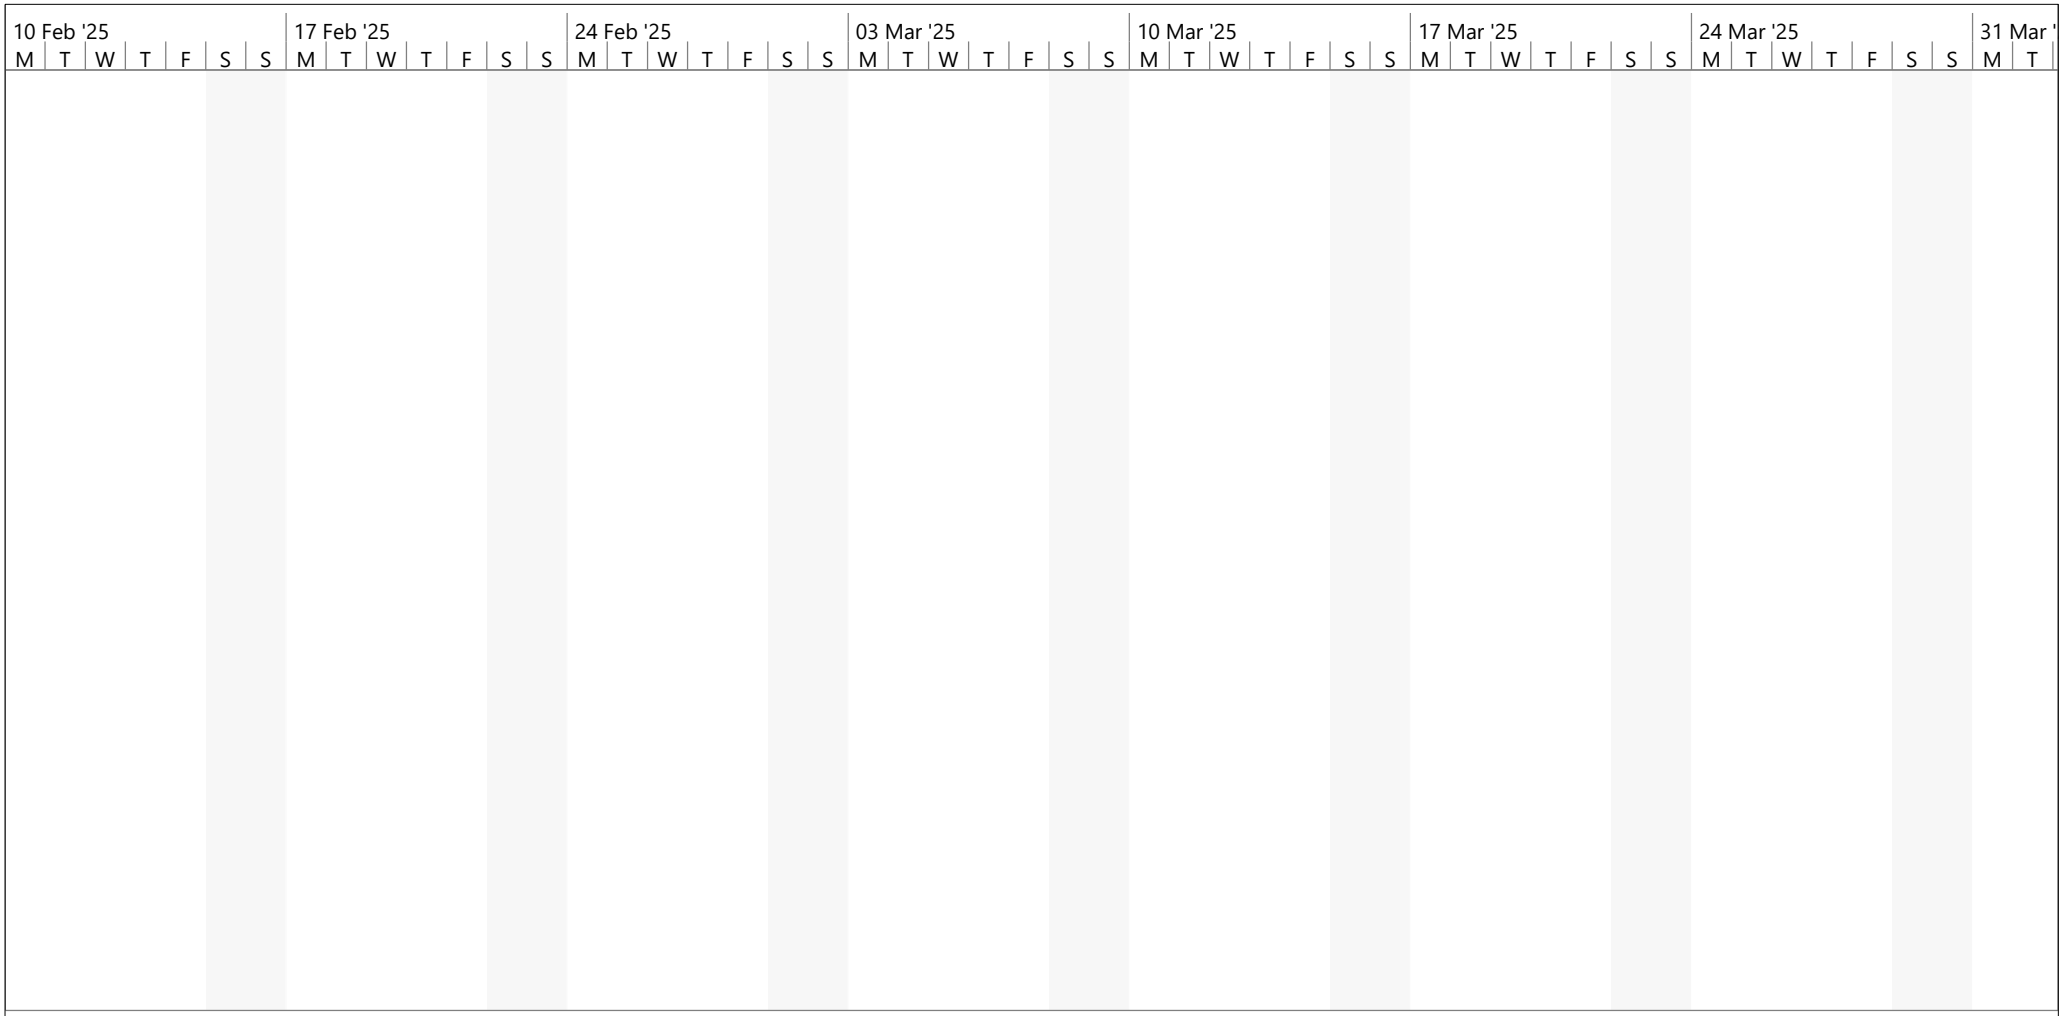


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

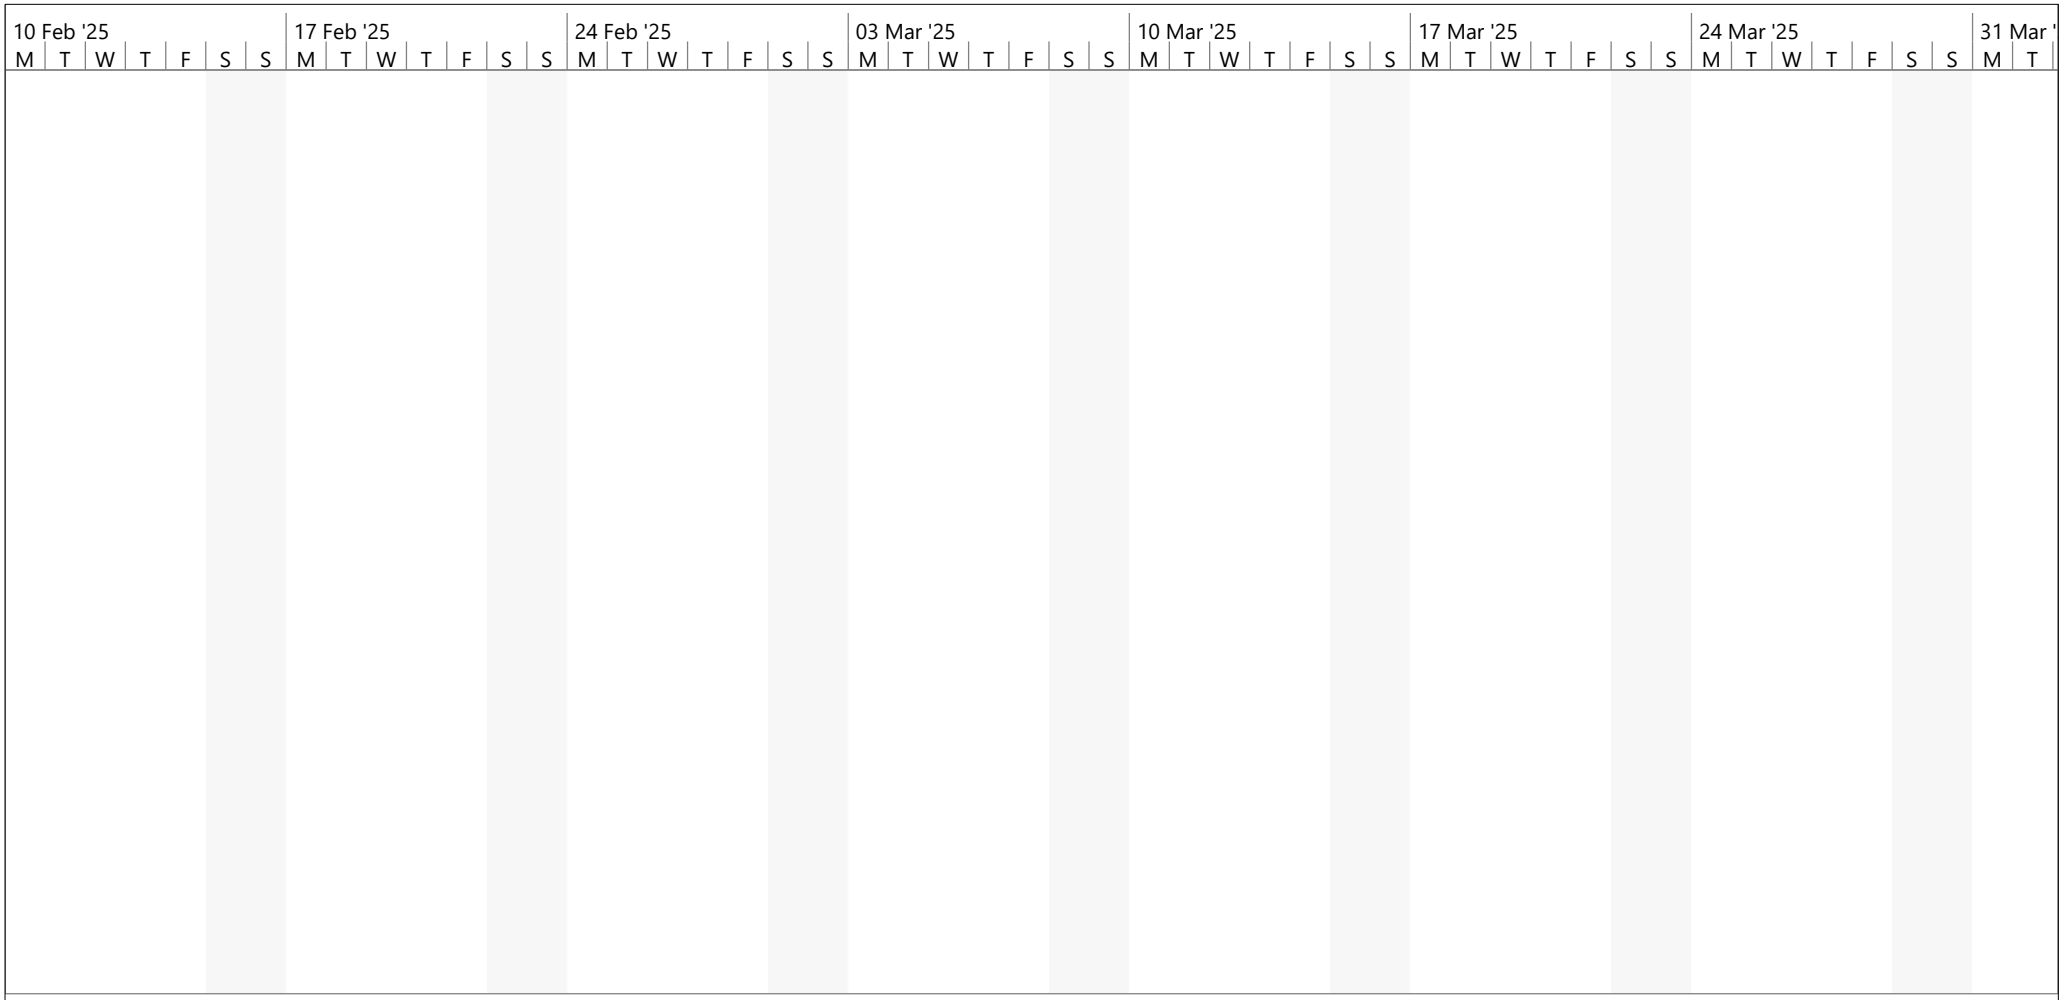


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

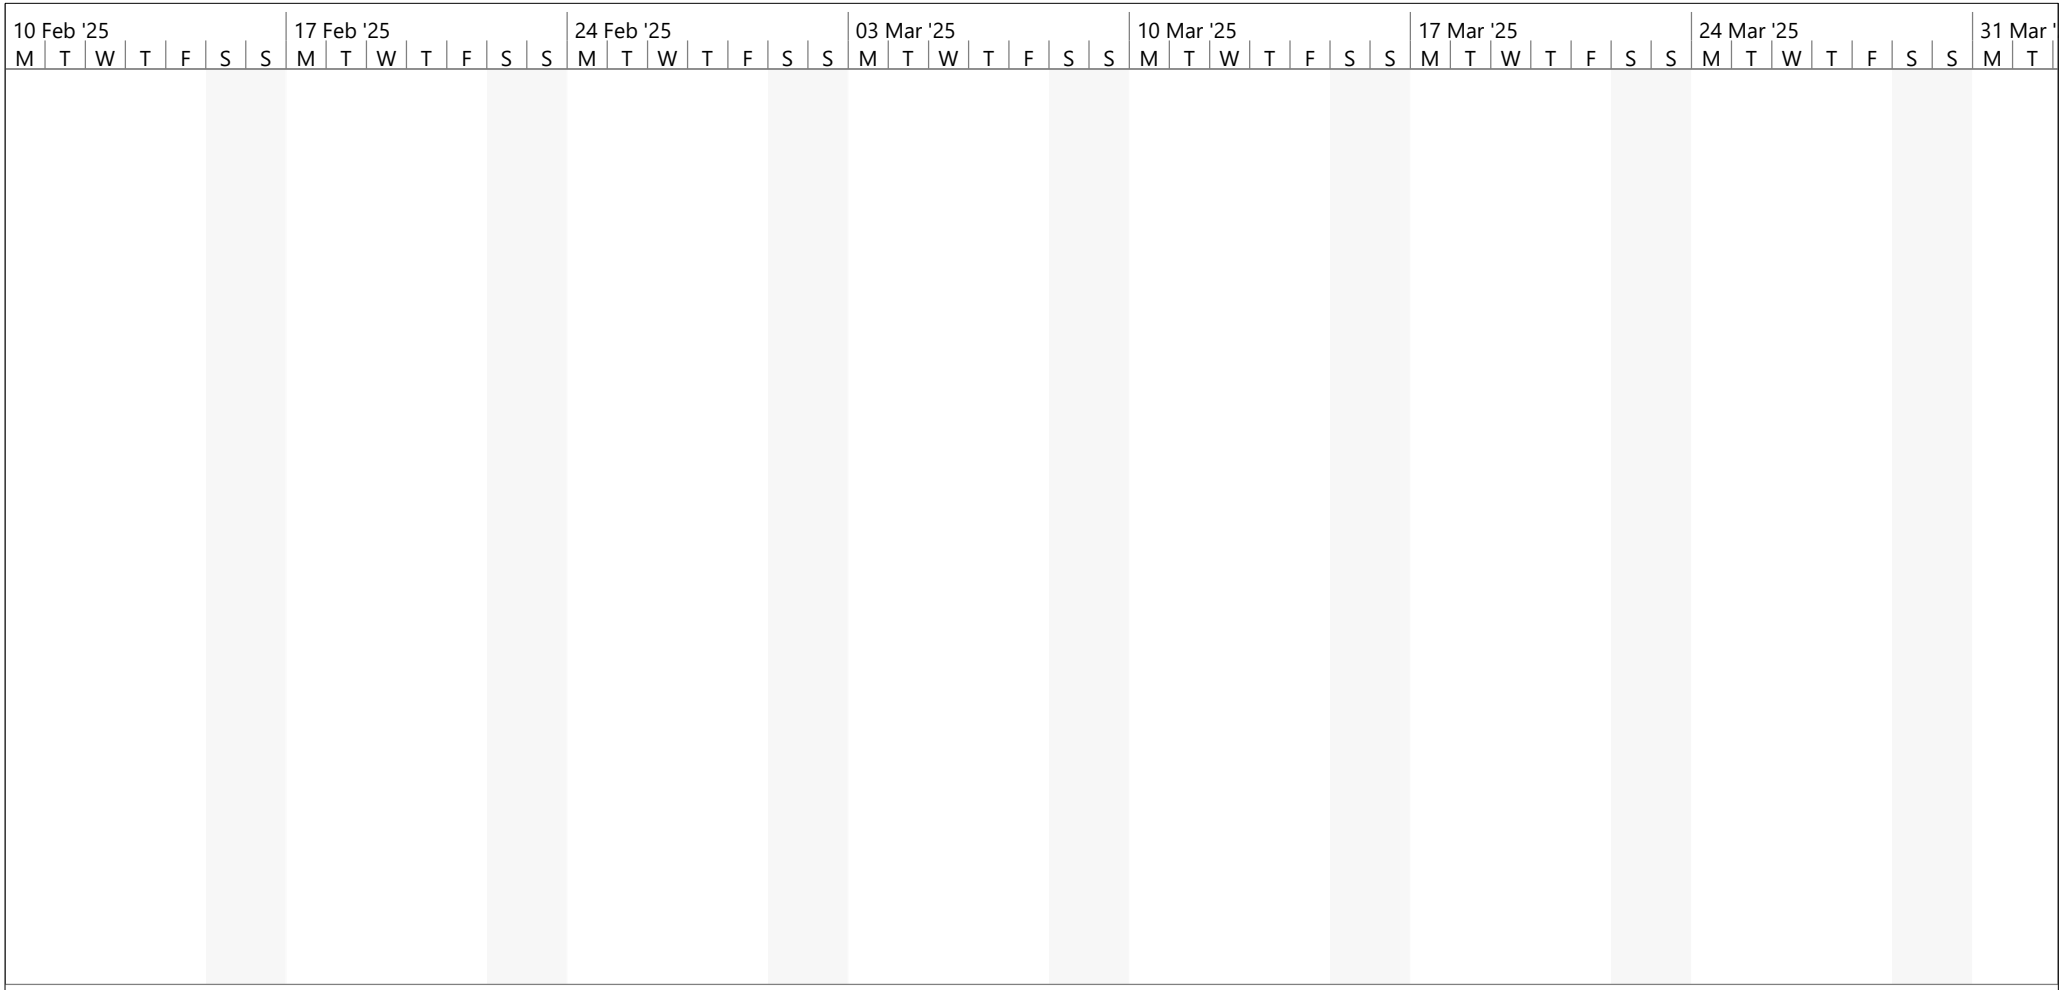


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

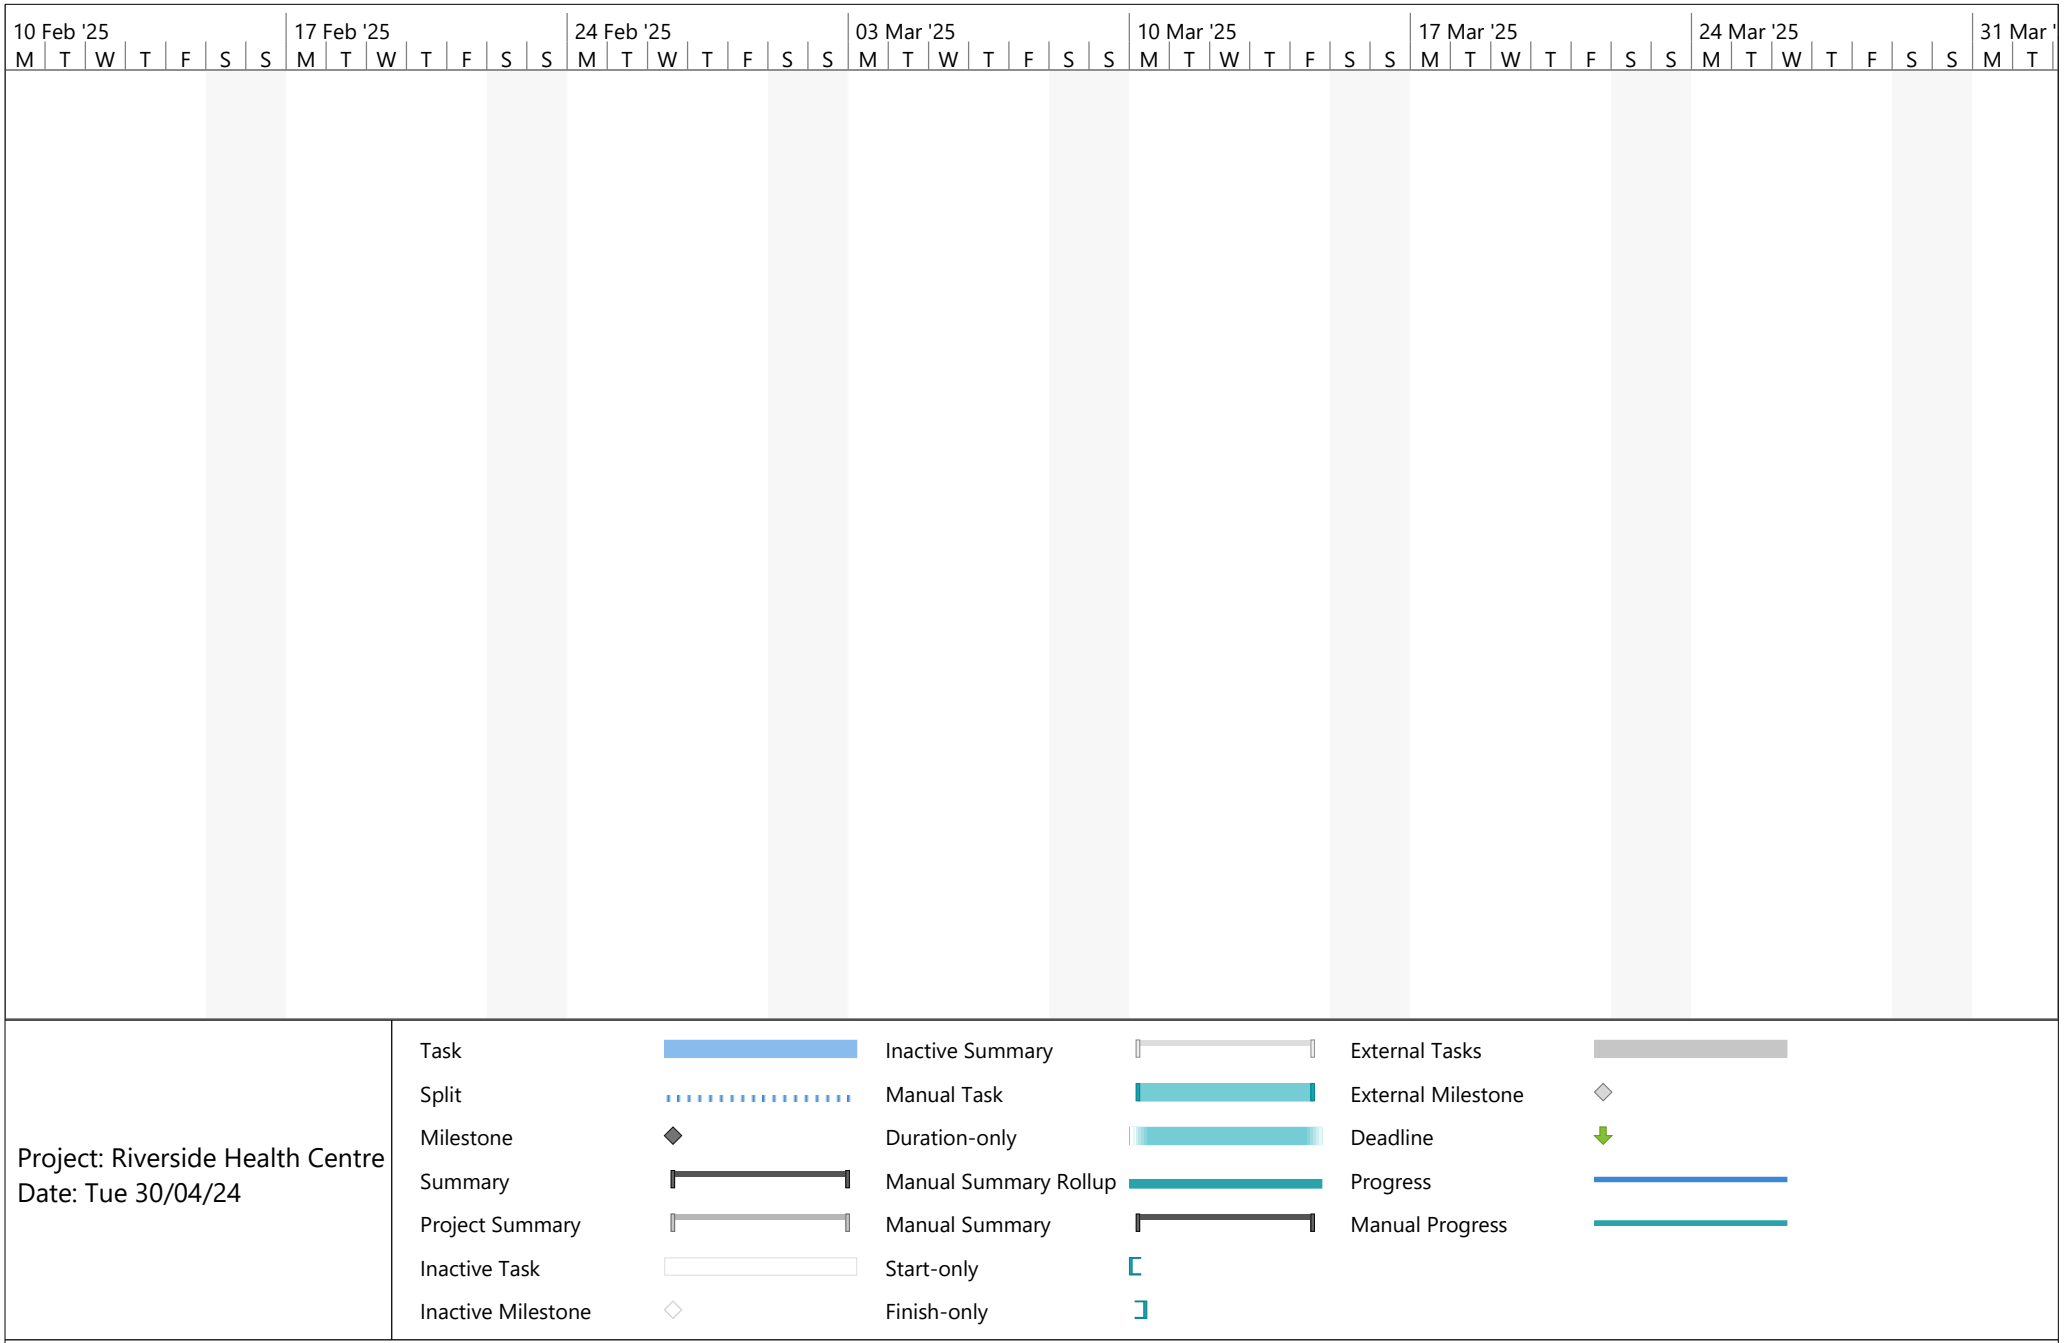


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

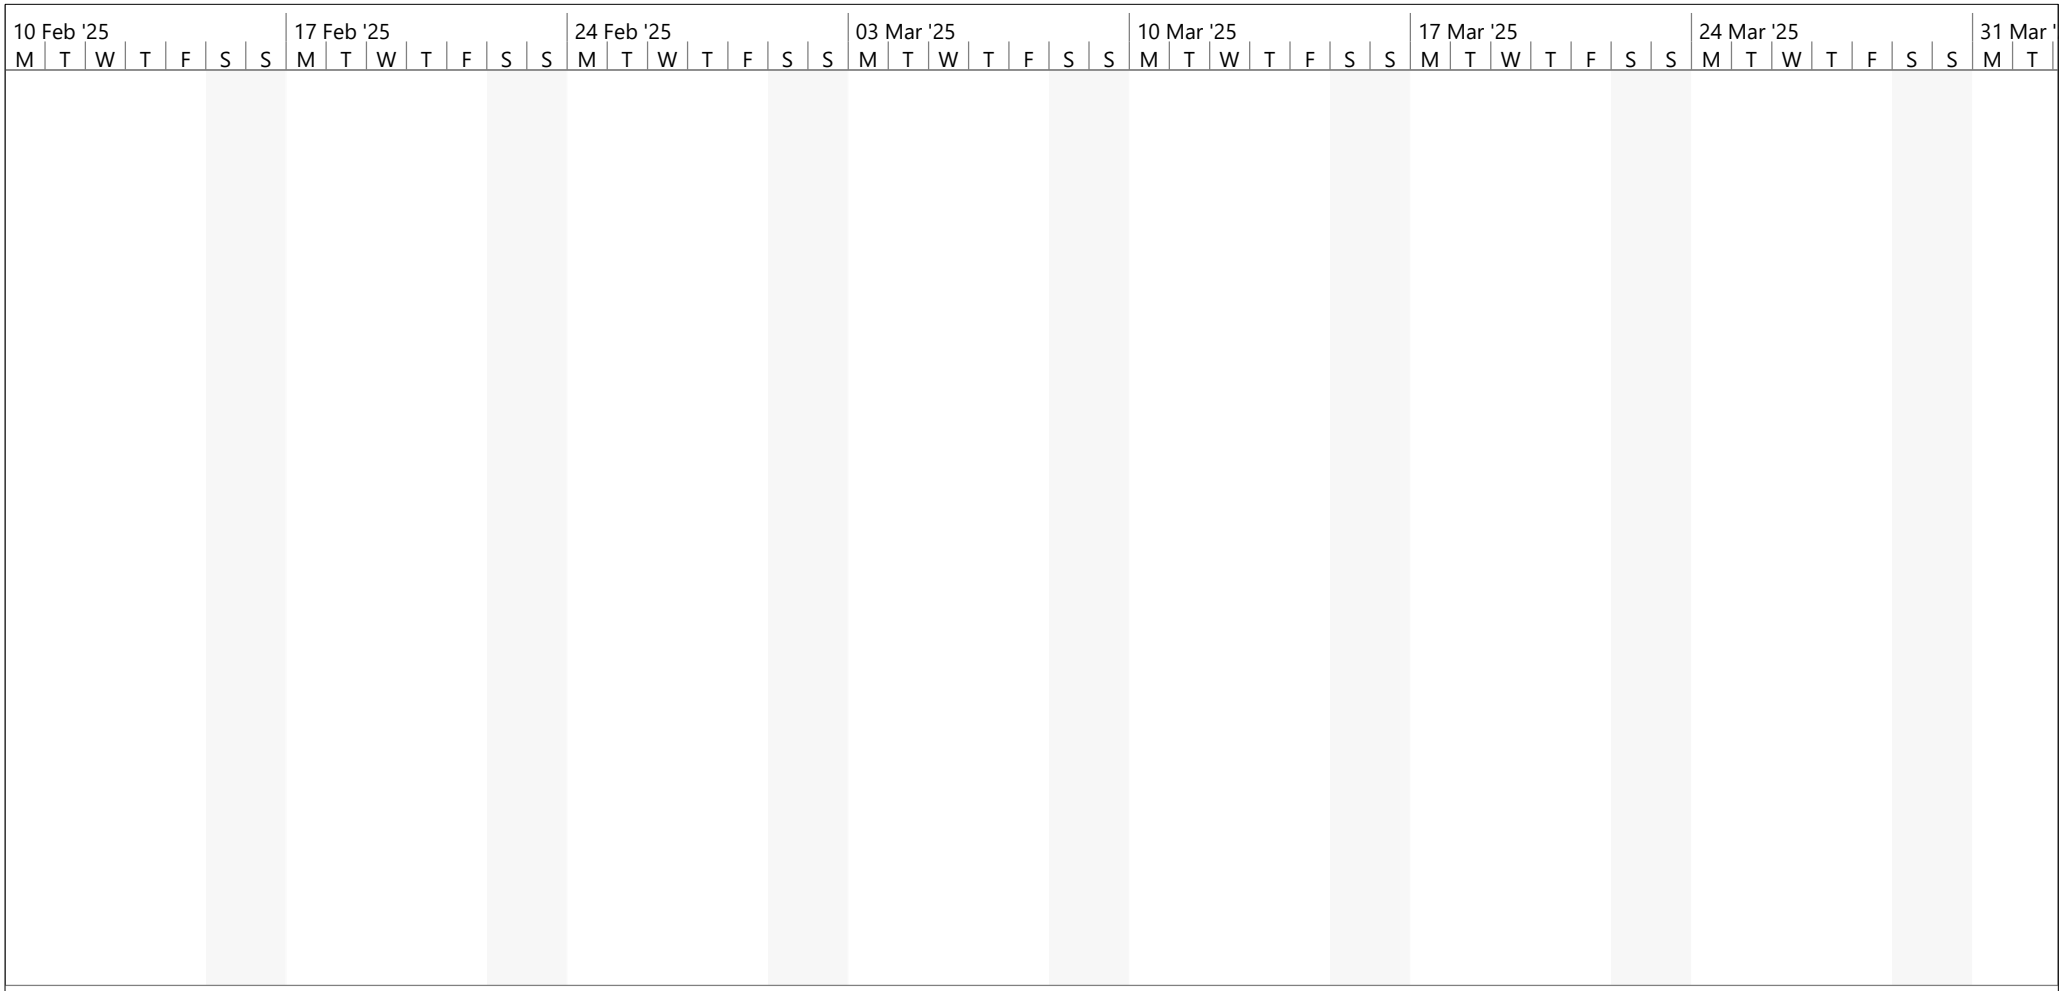


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

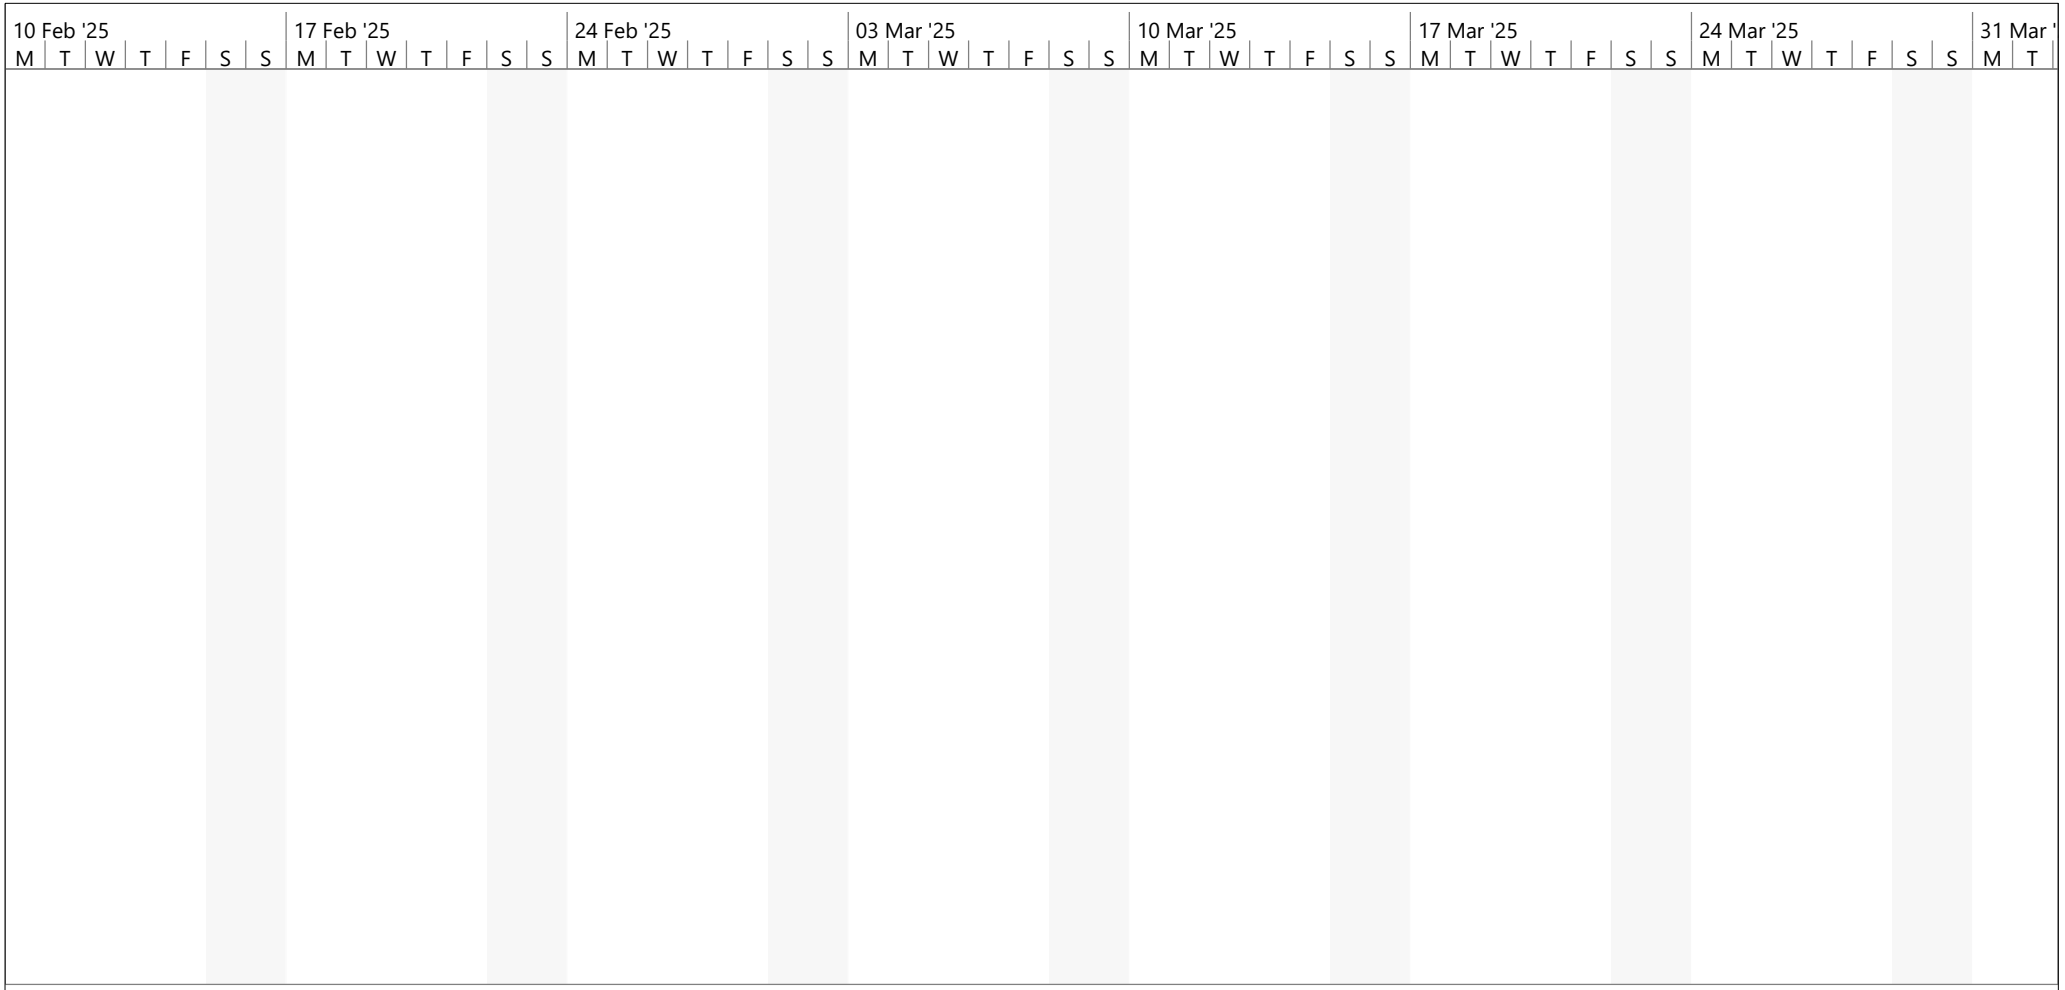


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

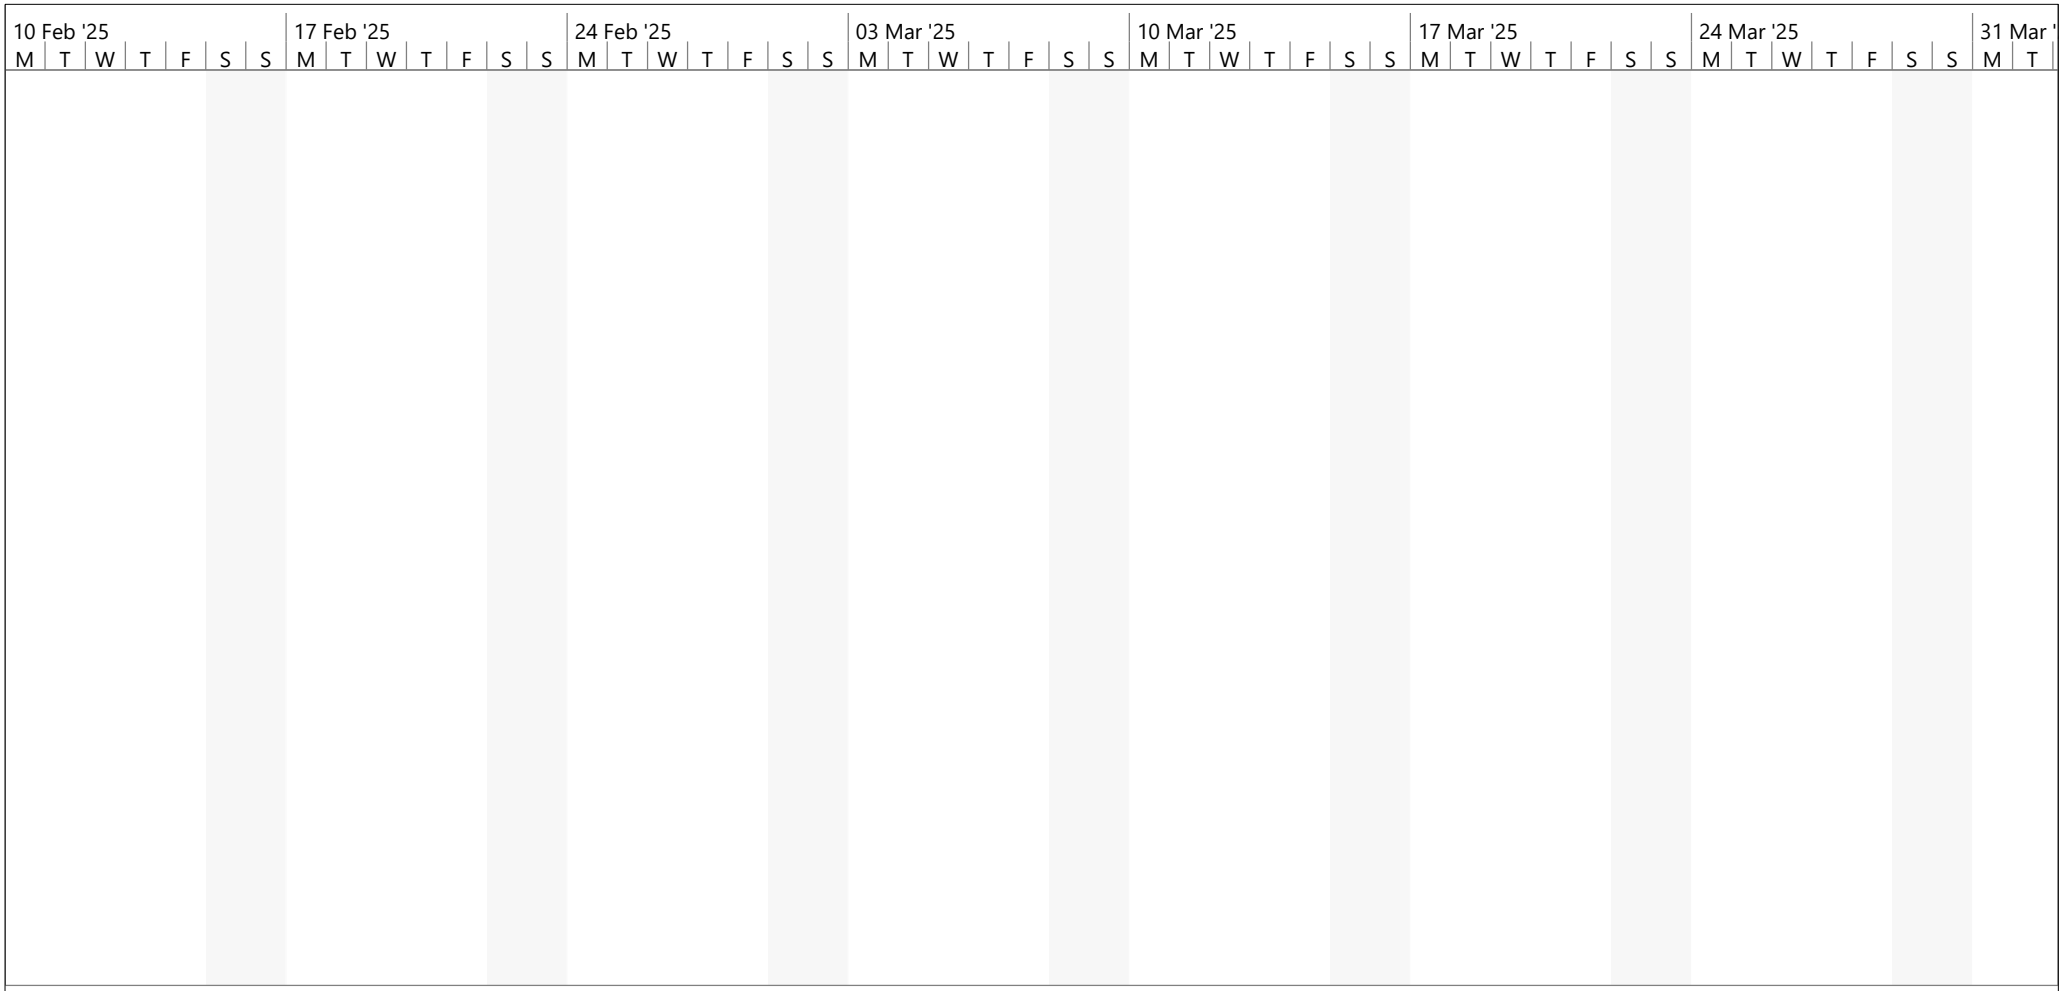


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

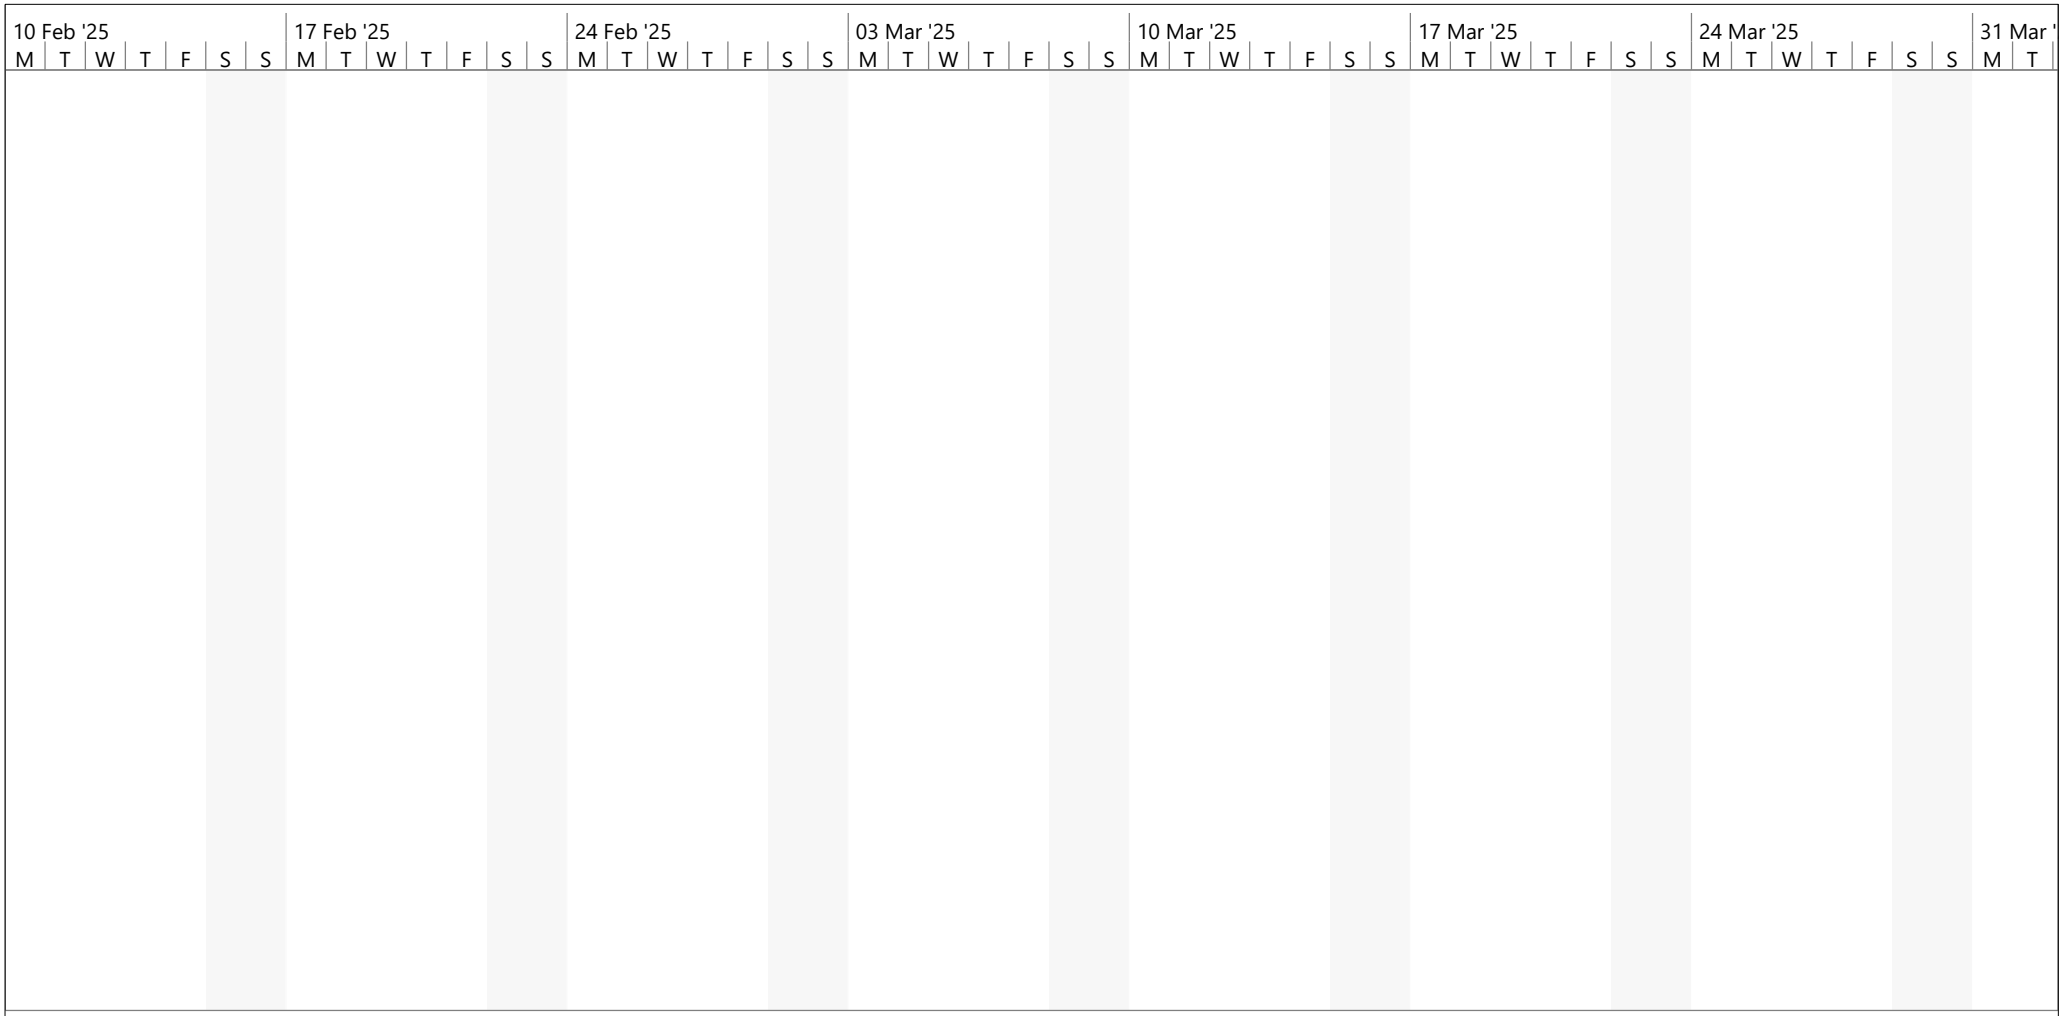

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

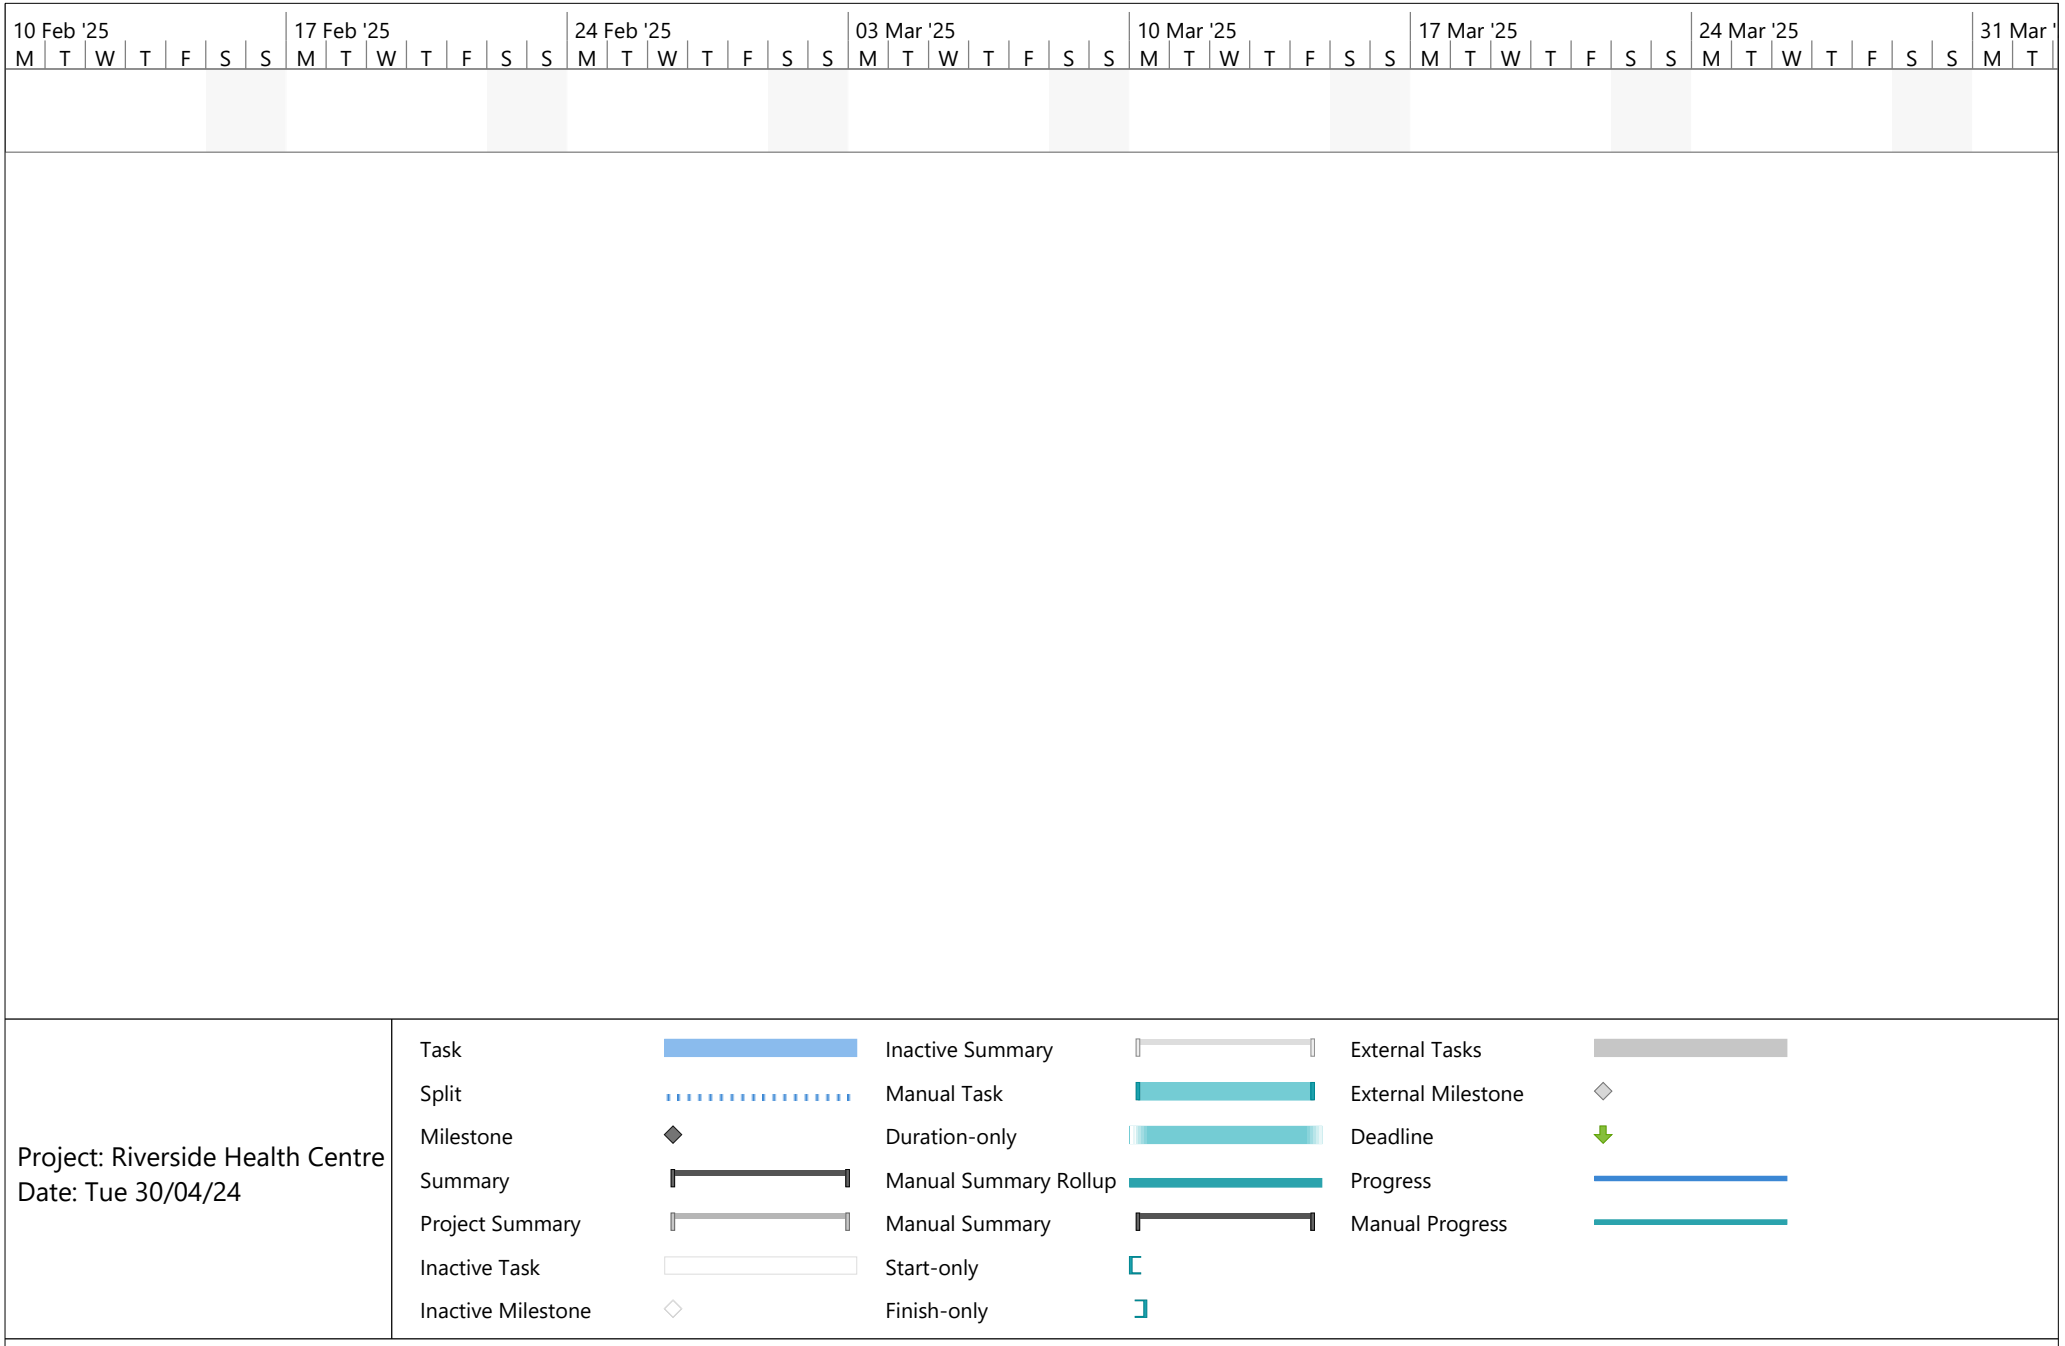
10 Feb '25
M T W T F S S
17 Feb '25
M T W T F S S
24 Feb '25
M T W T F S S
03 Mar '25
M T W T F S S
10 Mar '25
M T W T F S S
17 Mar '25
M T W T F S S
24 Mar '25
M T W T F S S
31 Mar '
M T
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

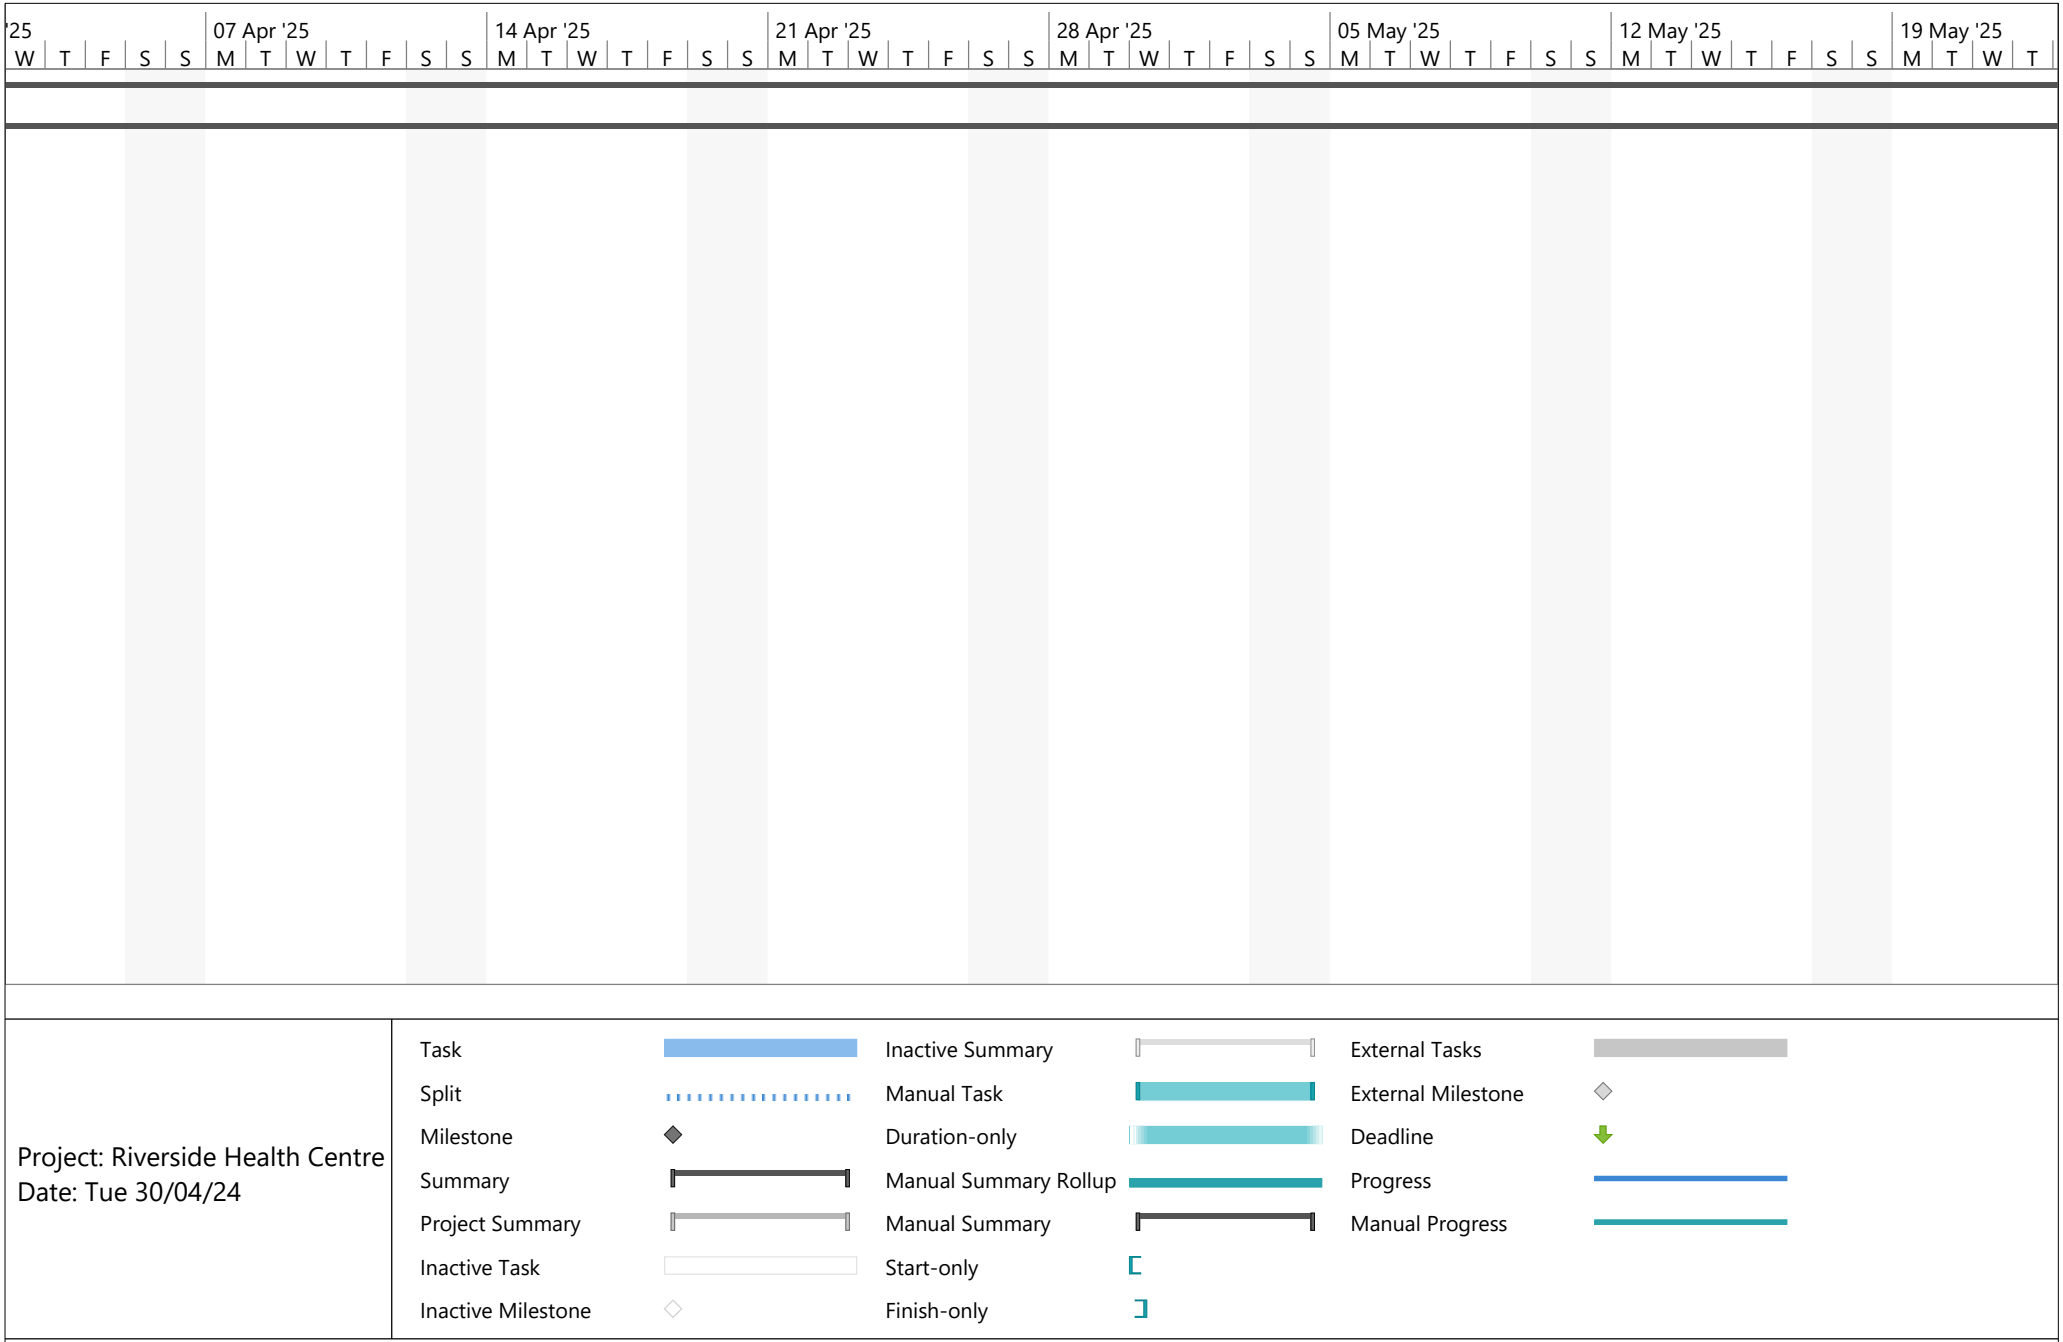


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

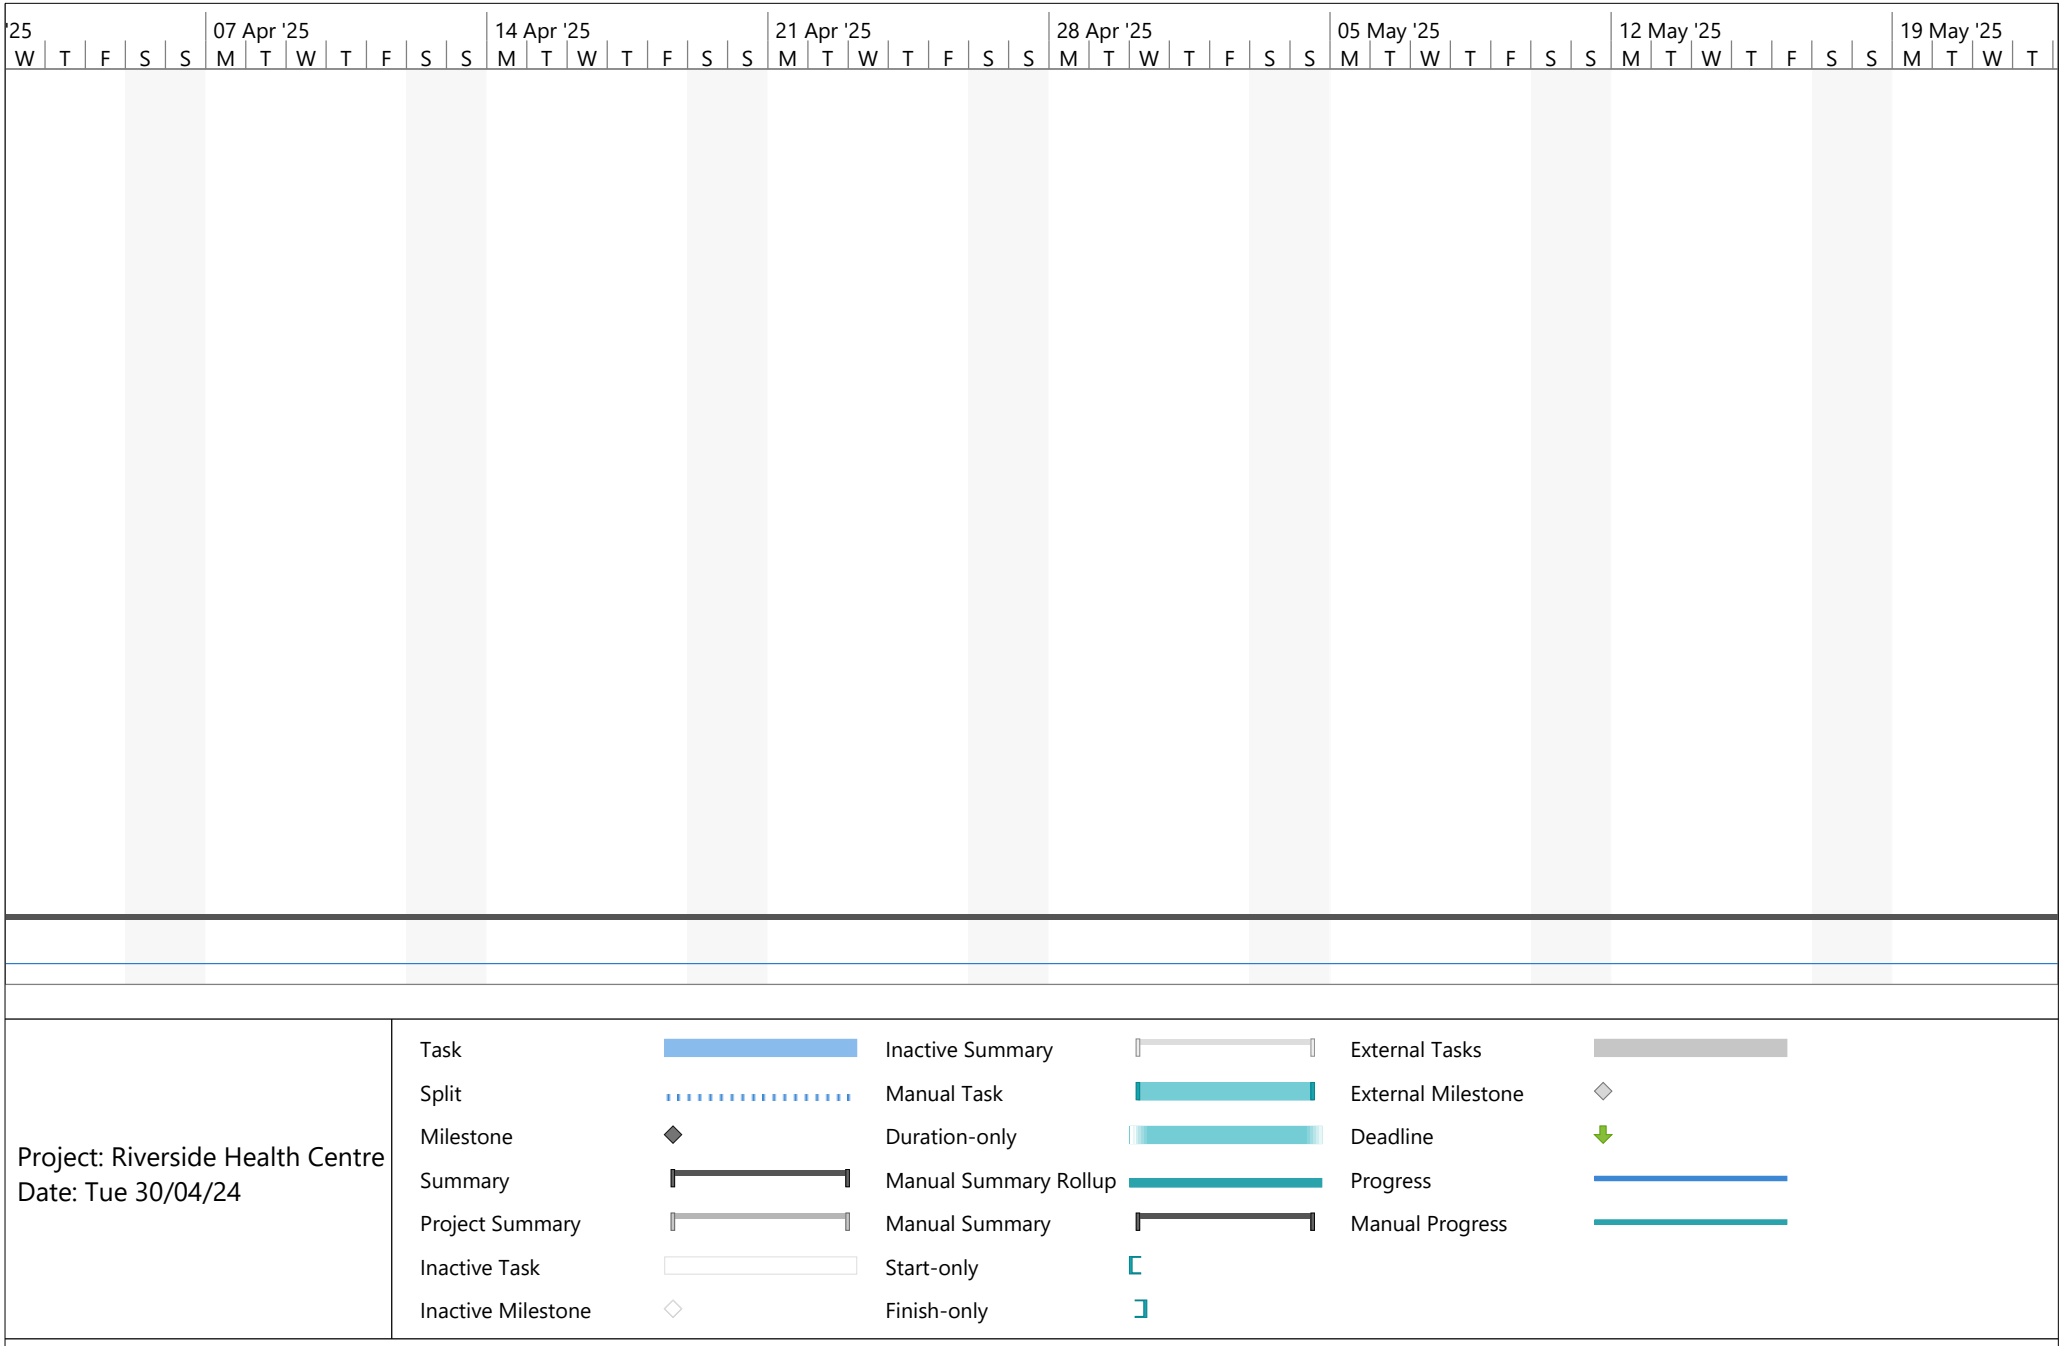


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

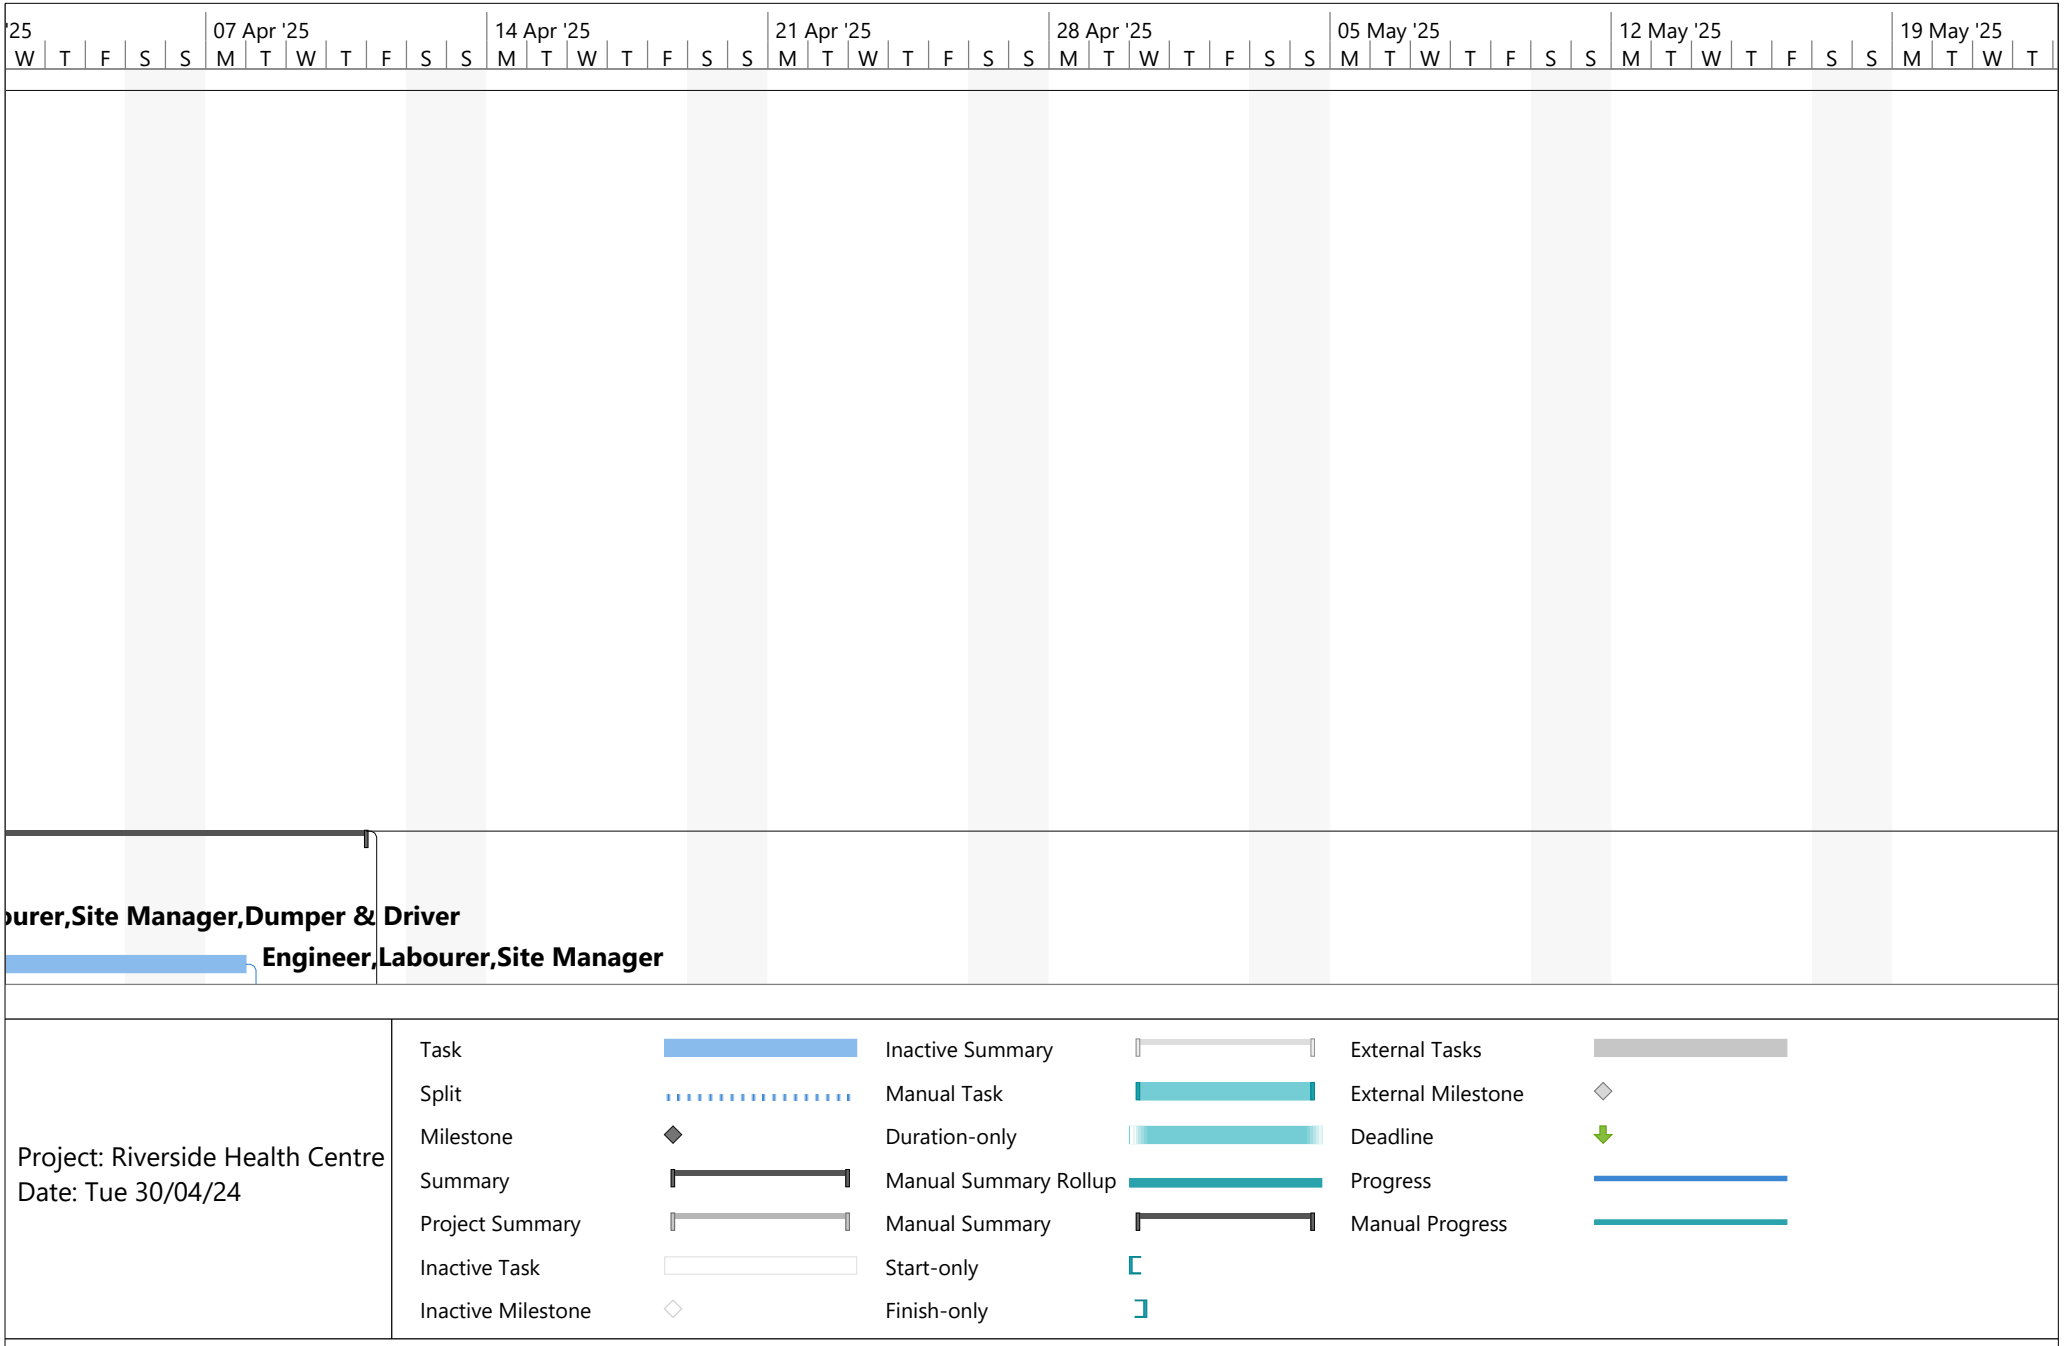


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

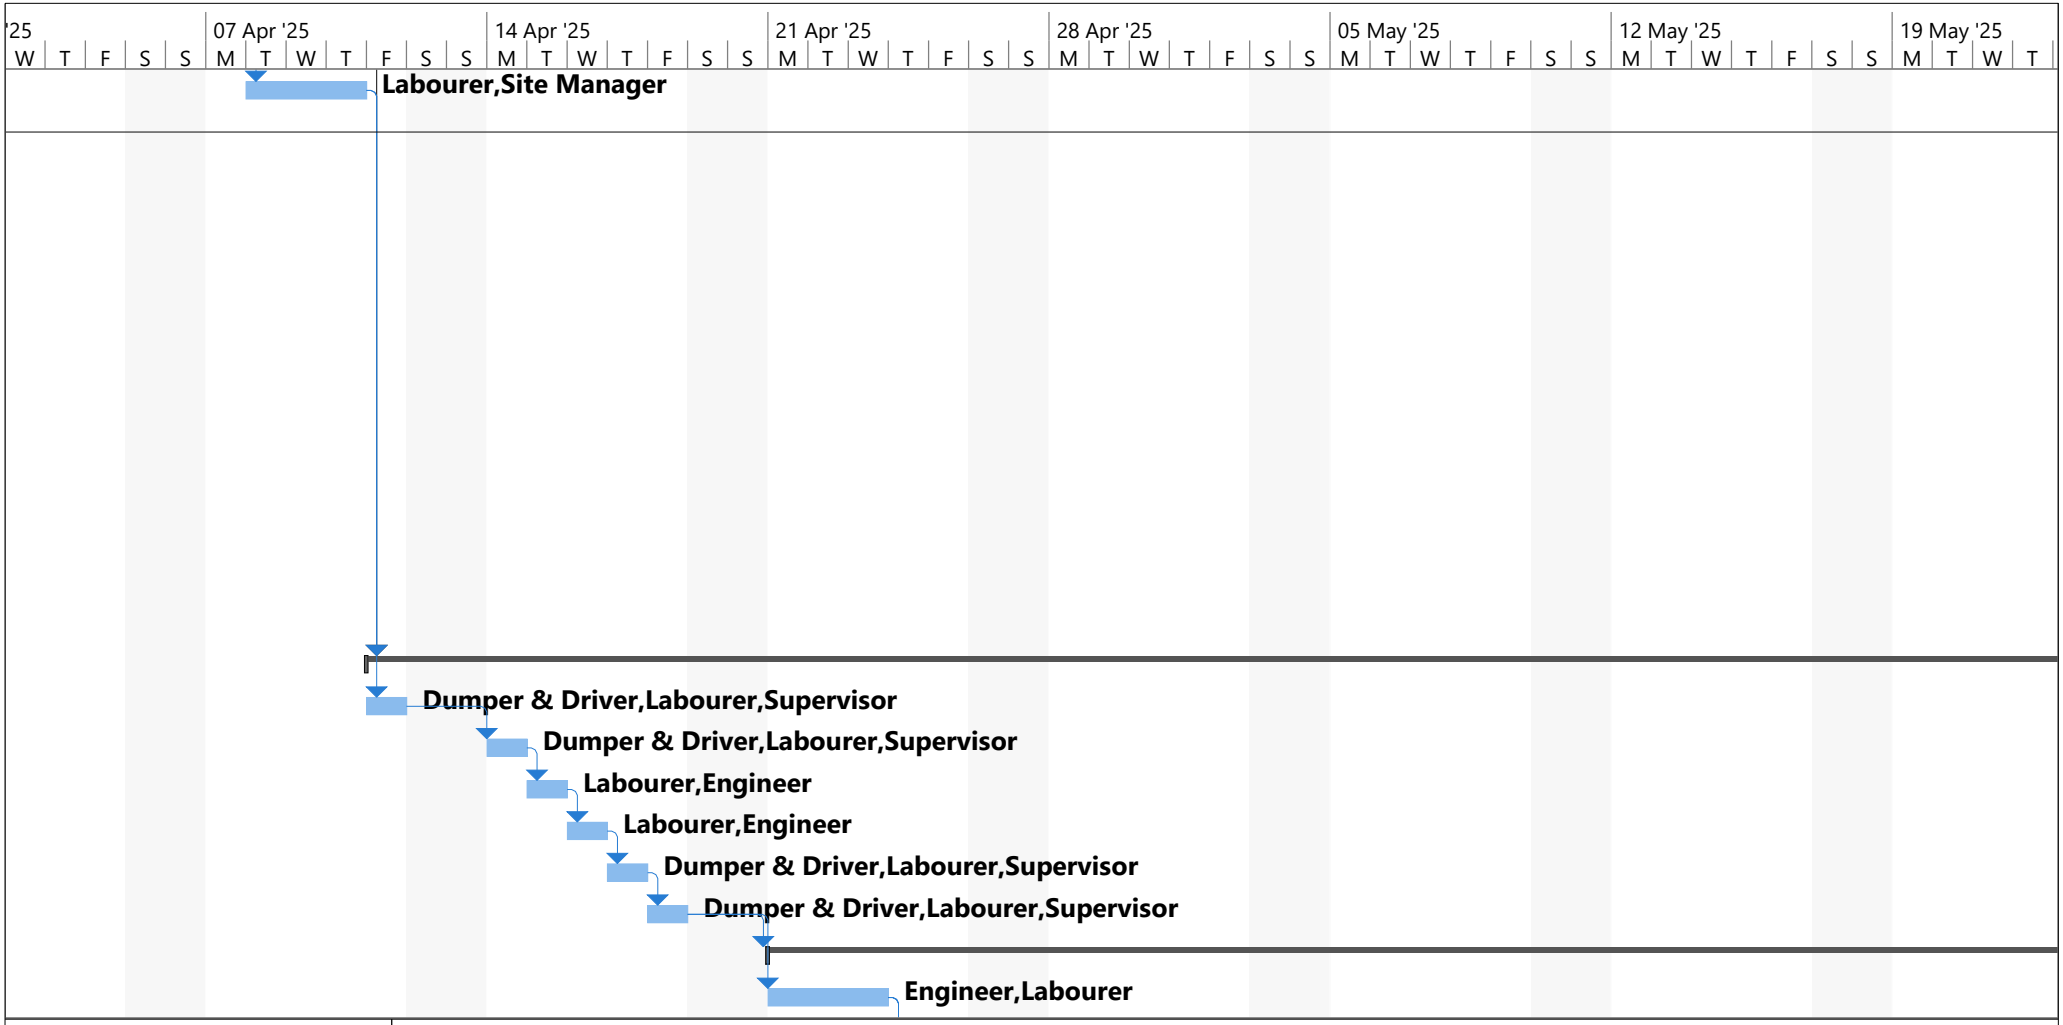


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

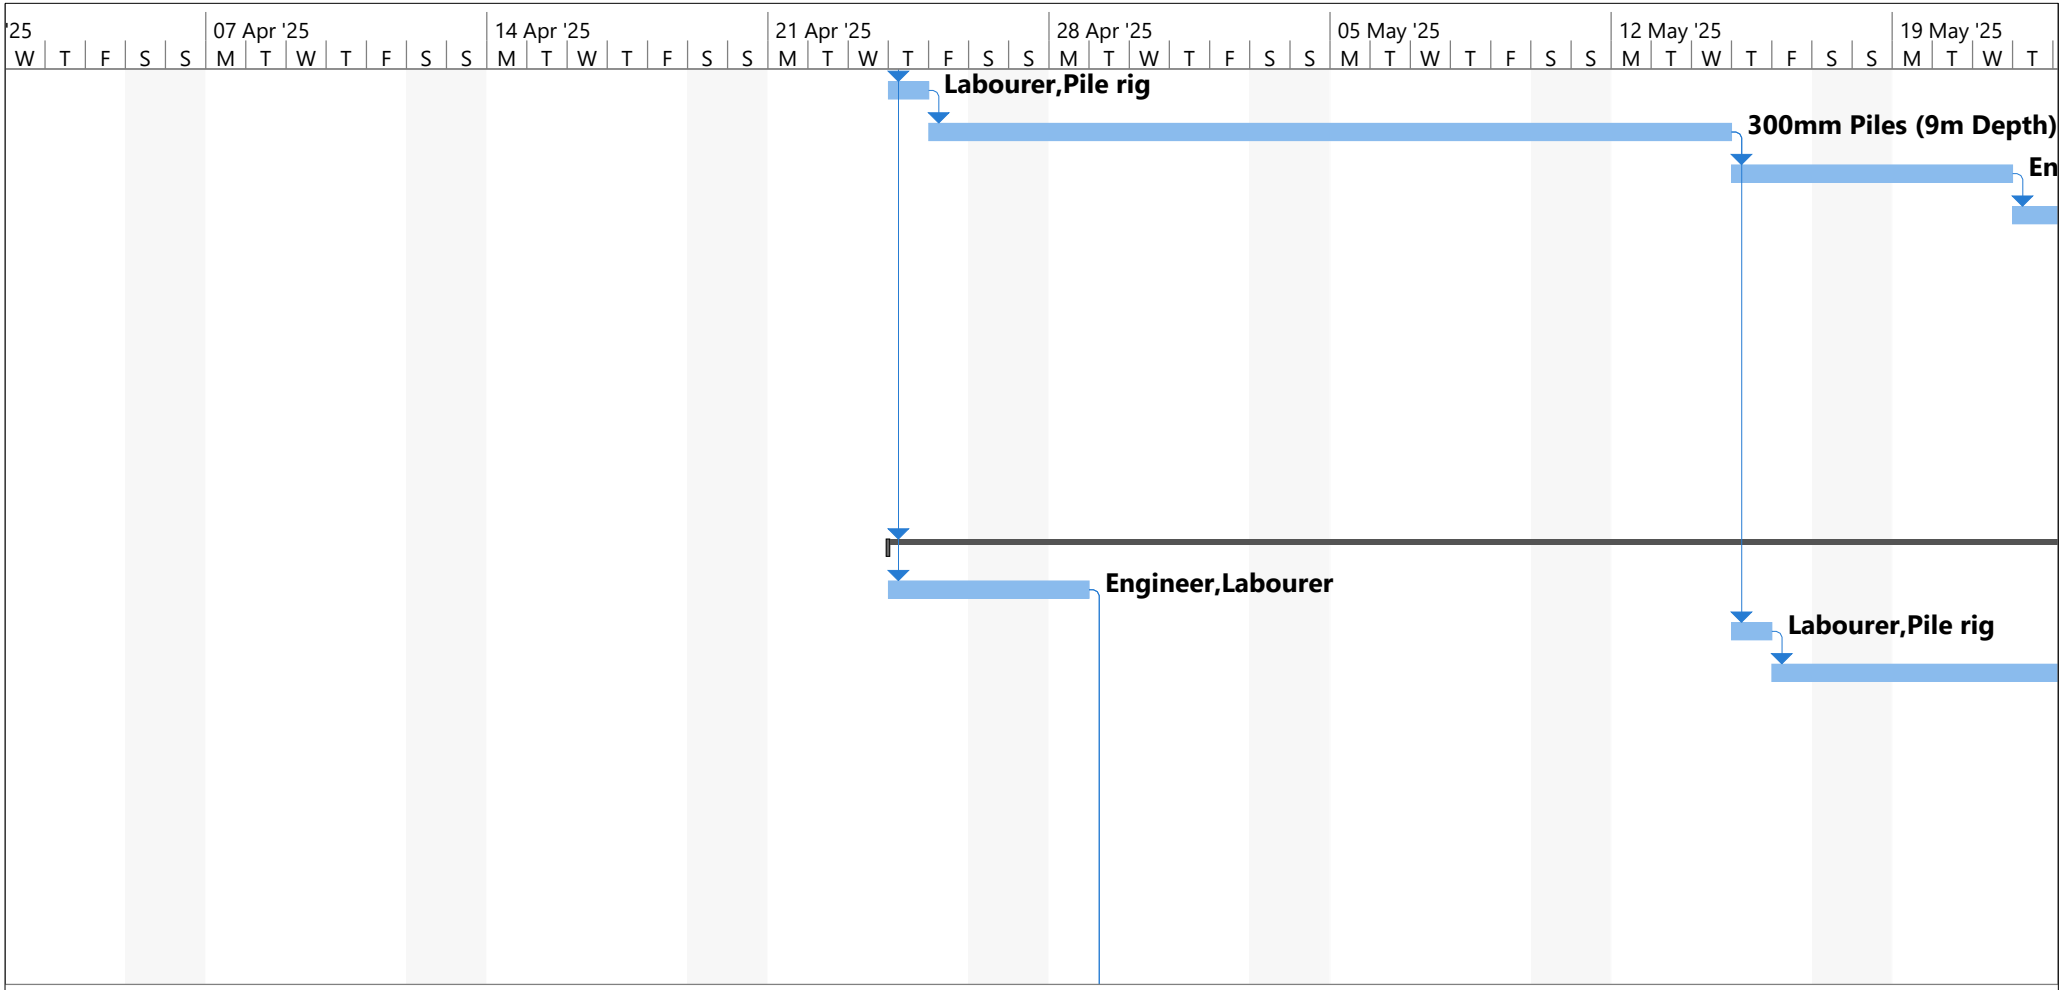


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

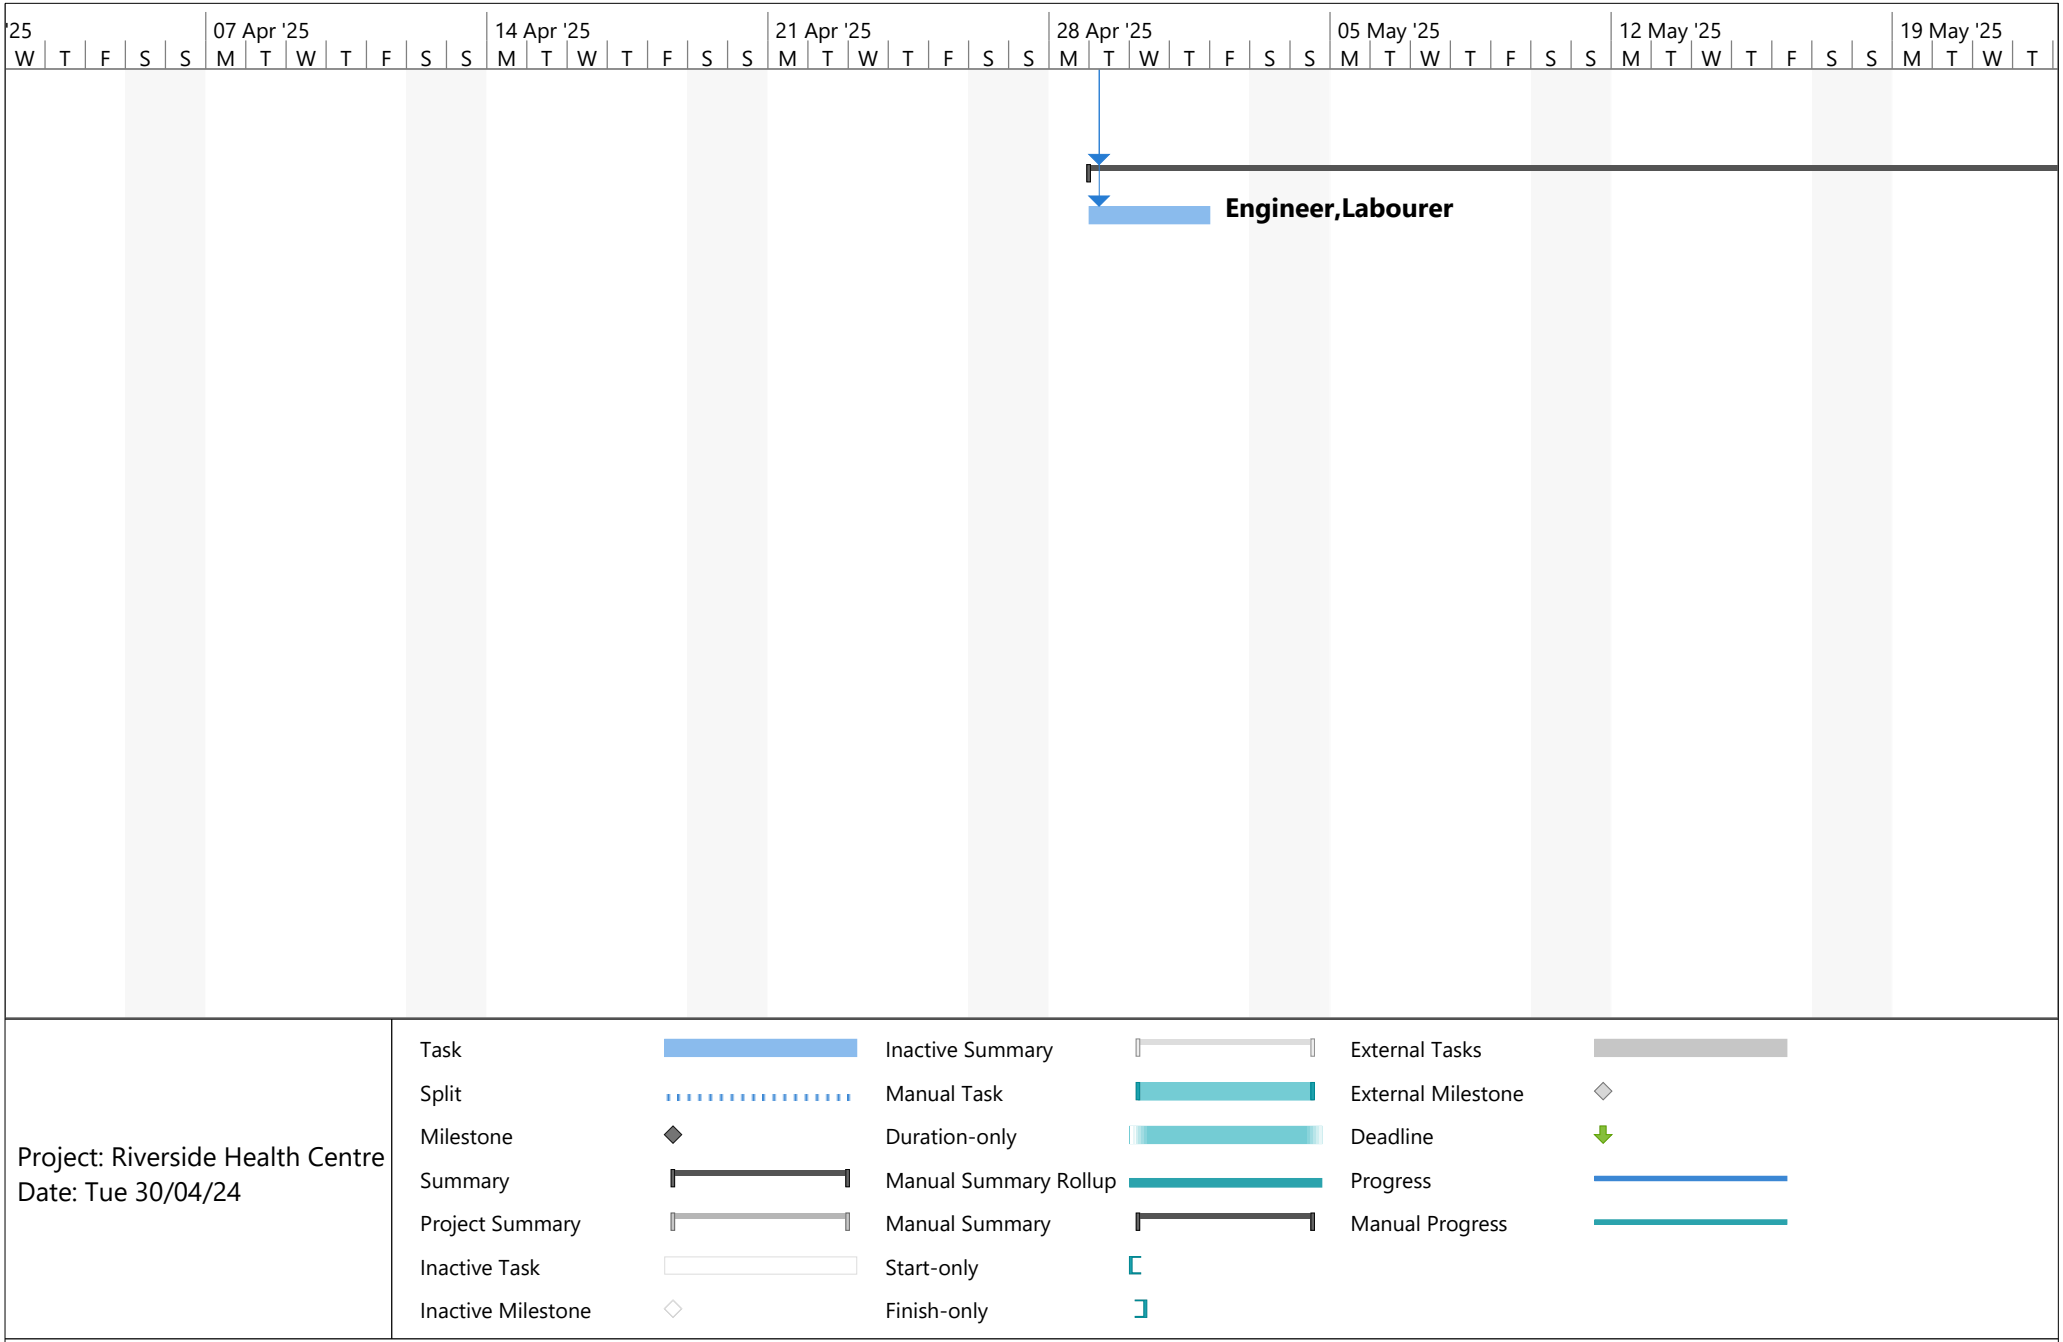


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

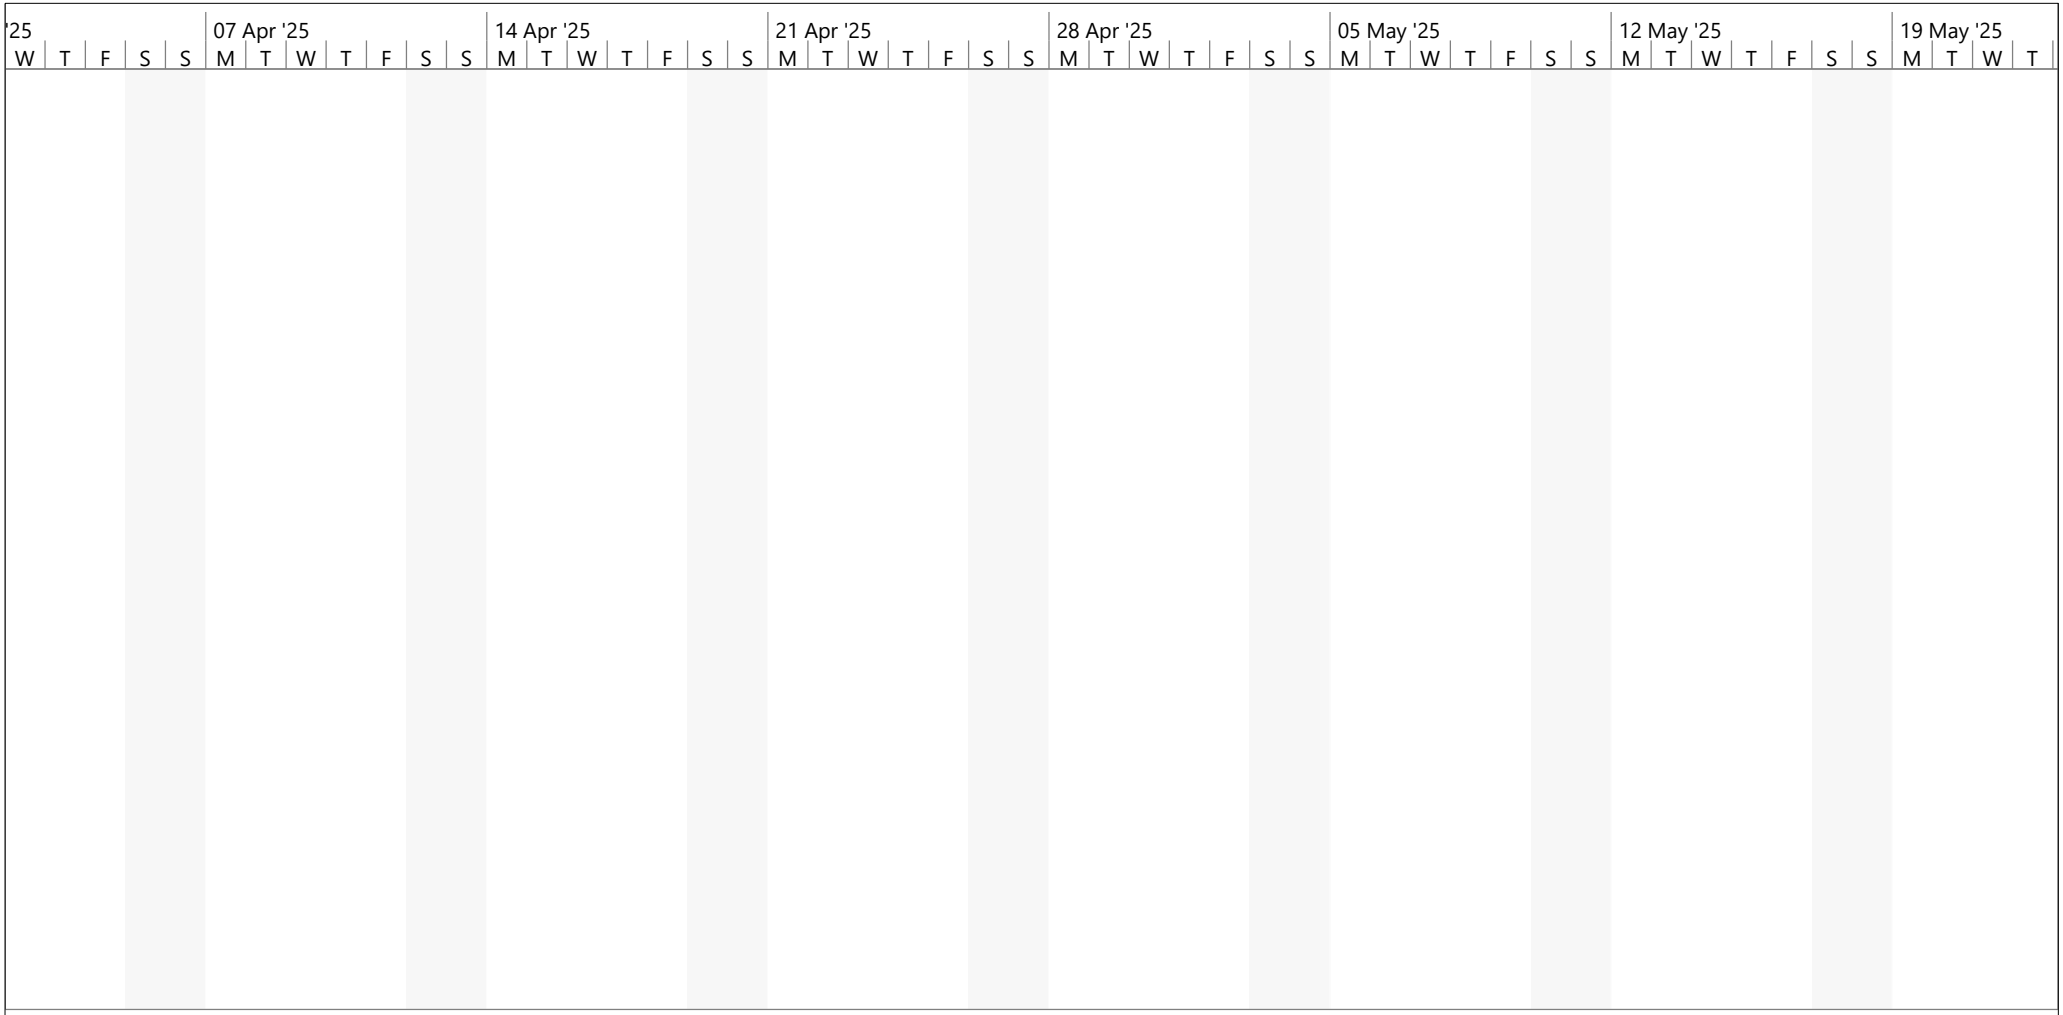


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

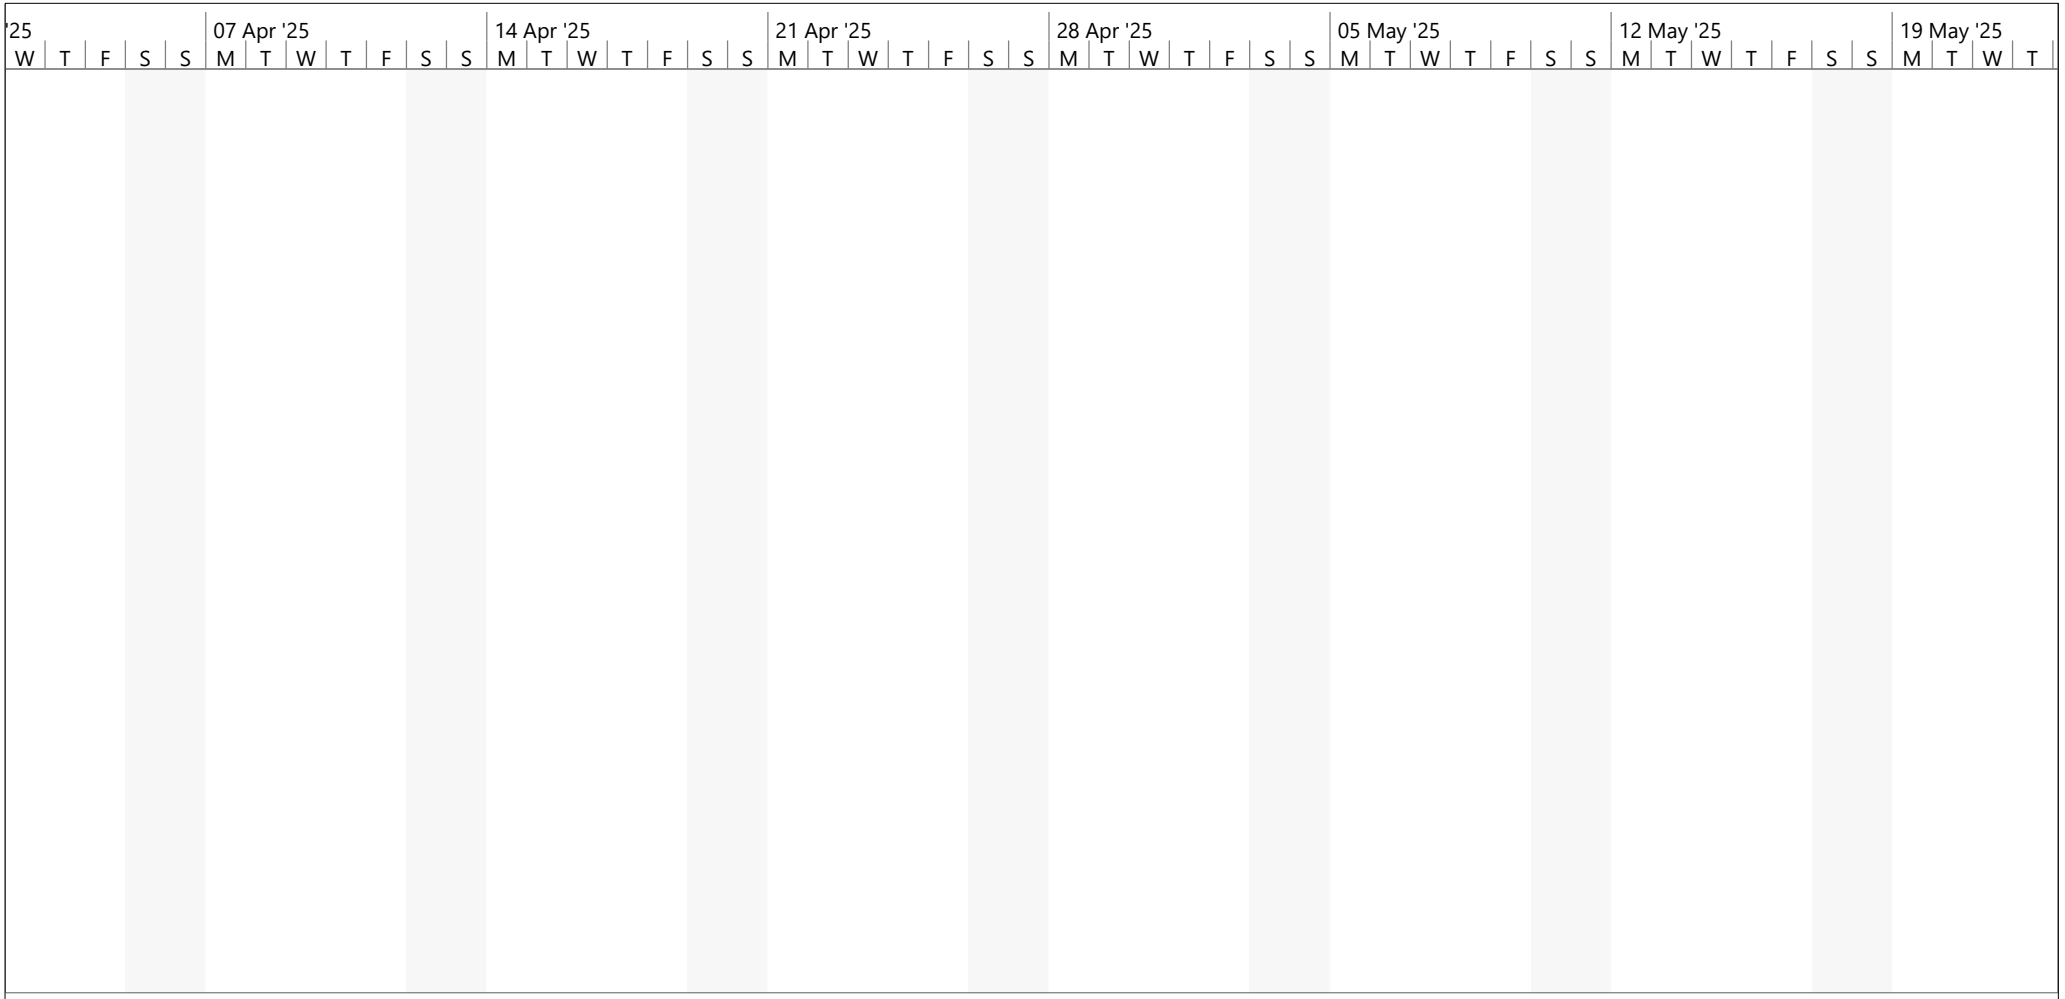


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

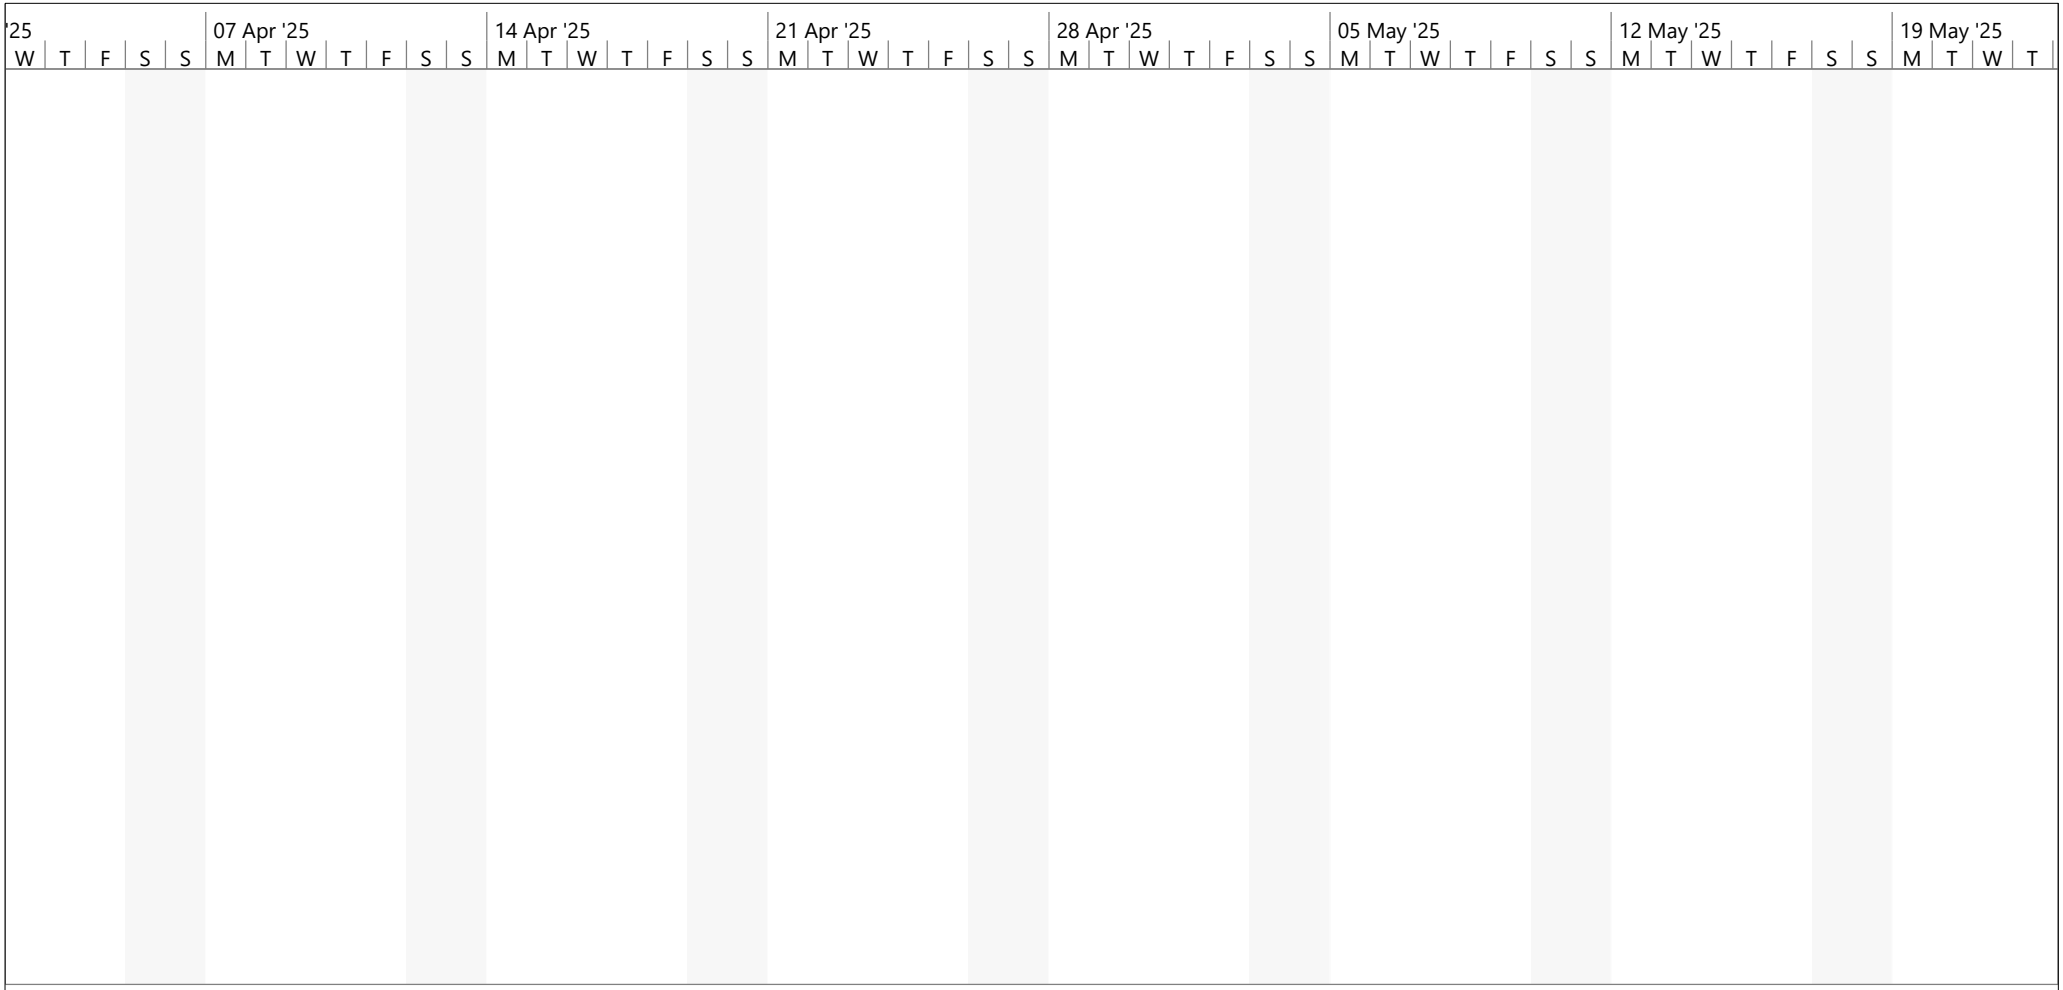


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

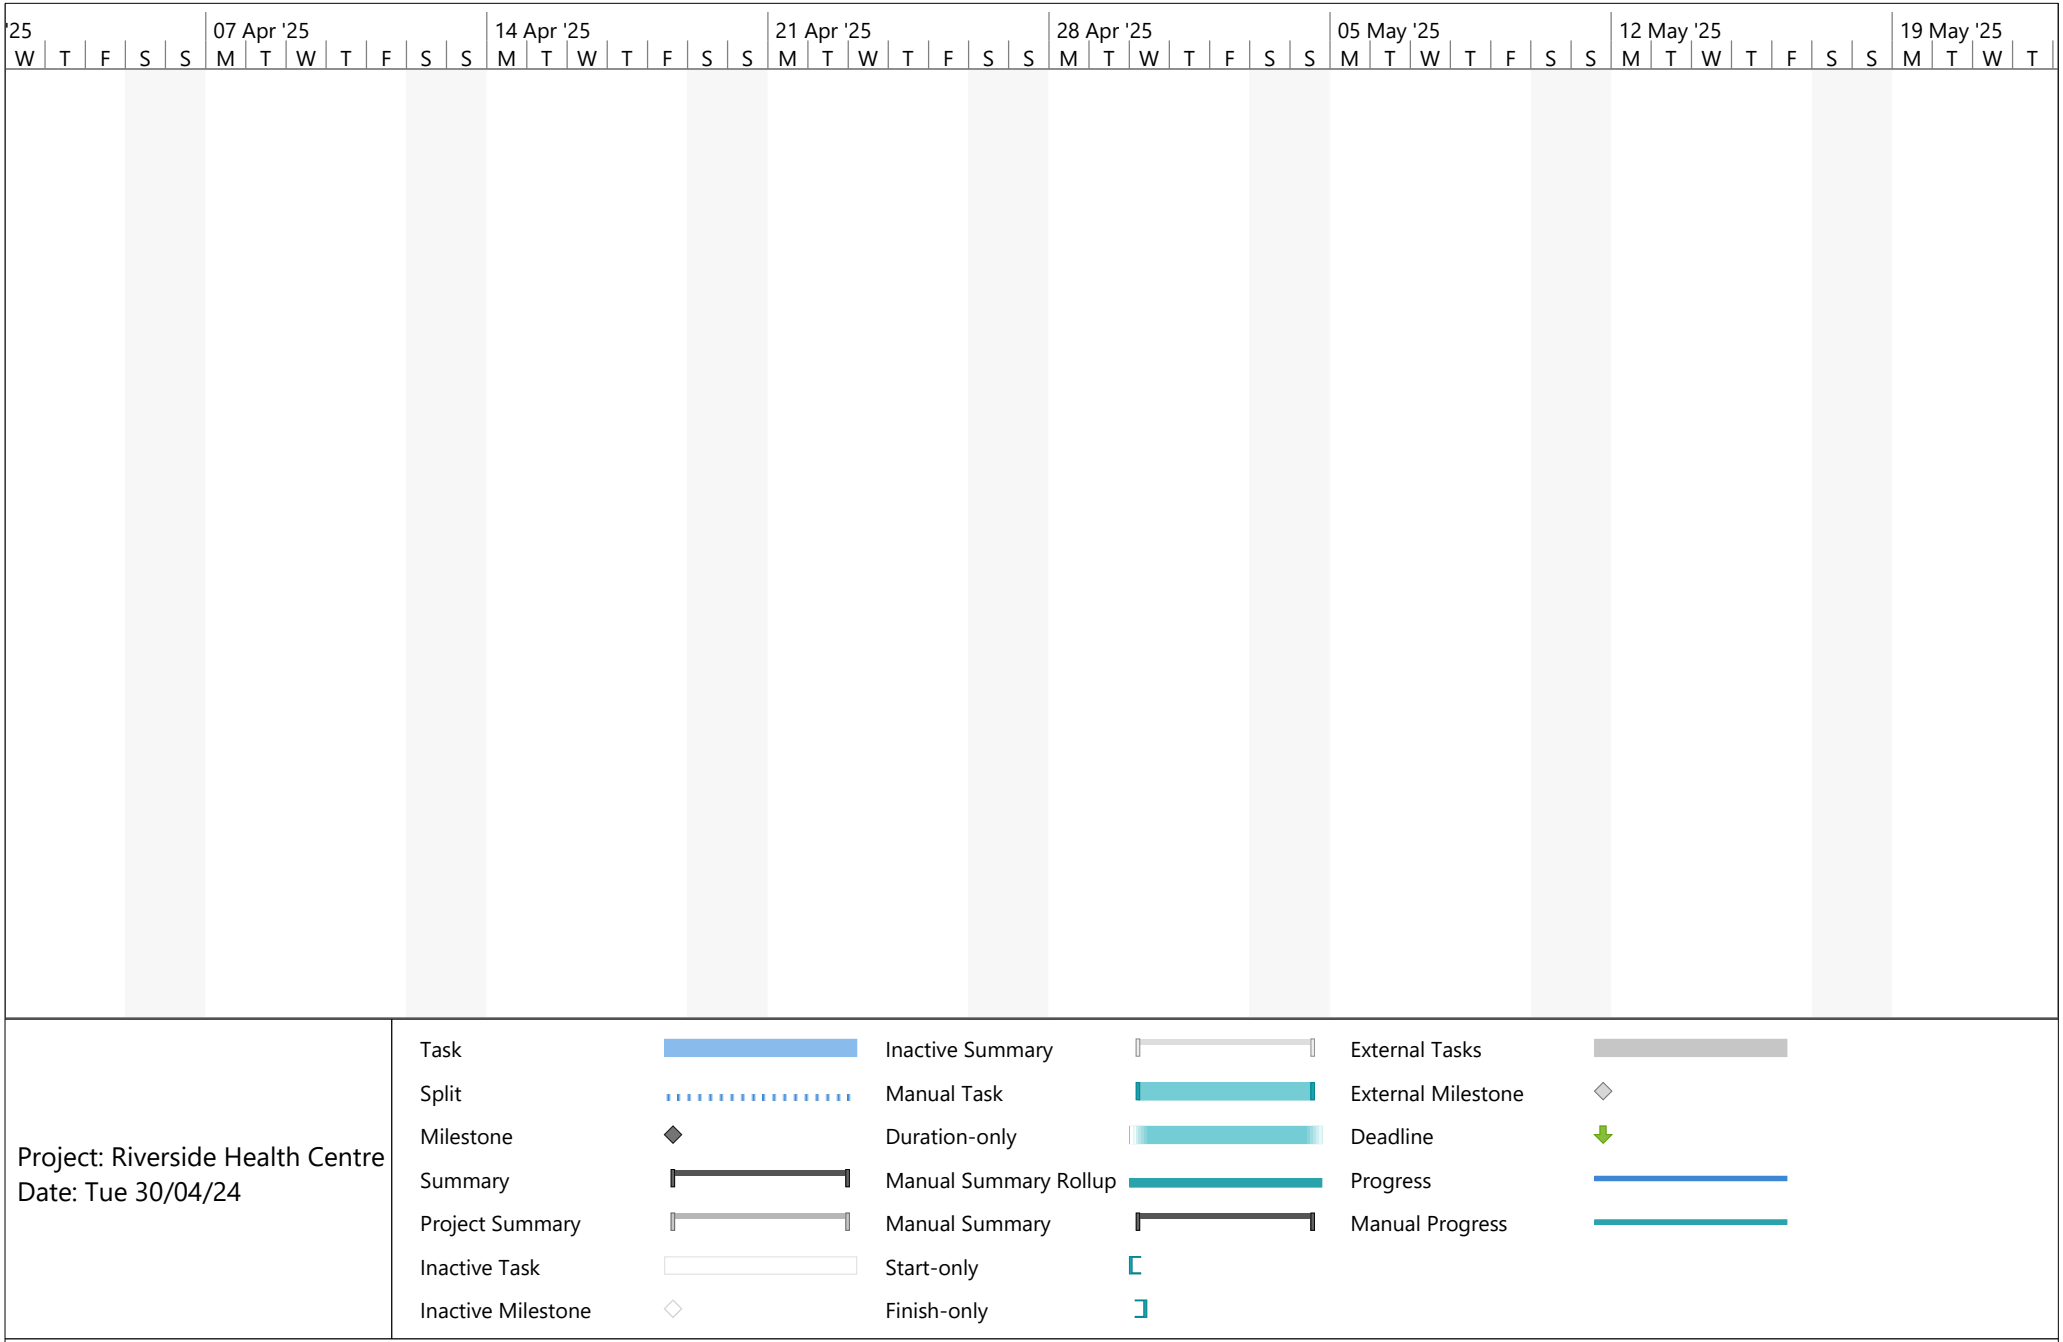


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

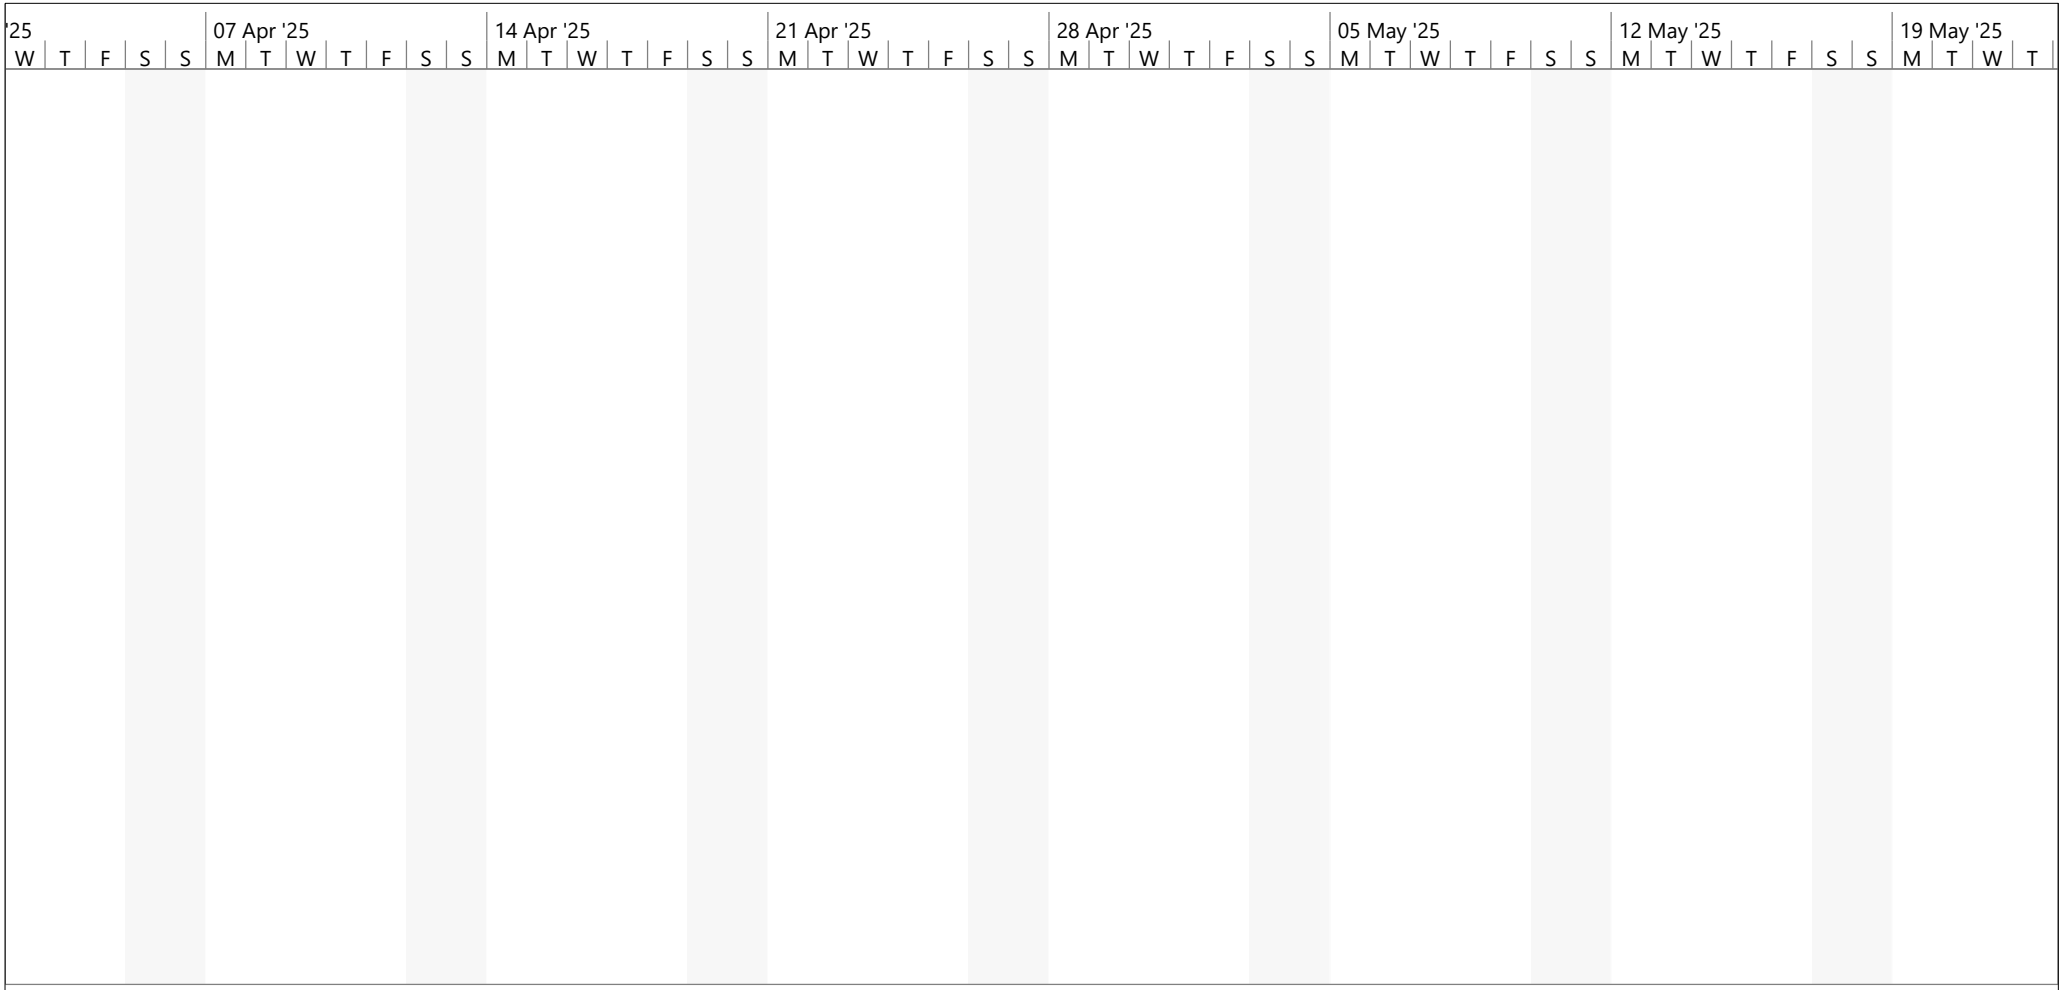


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

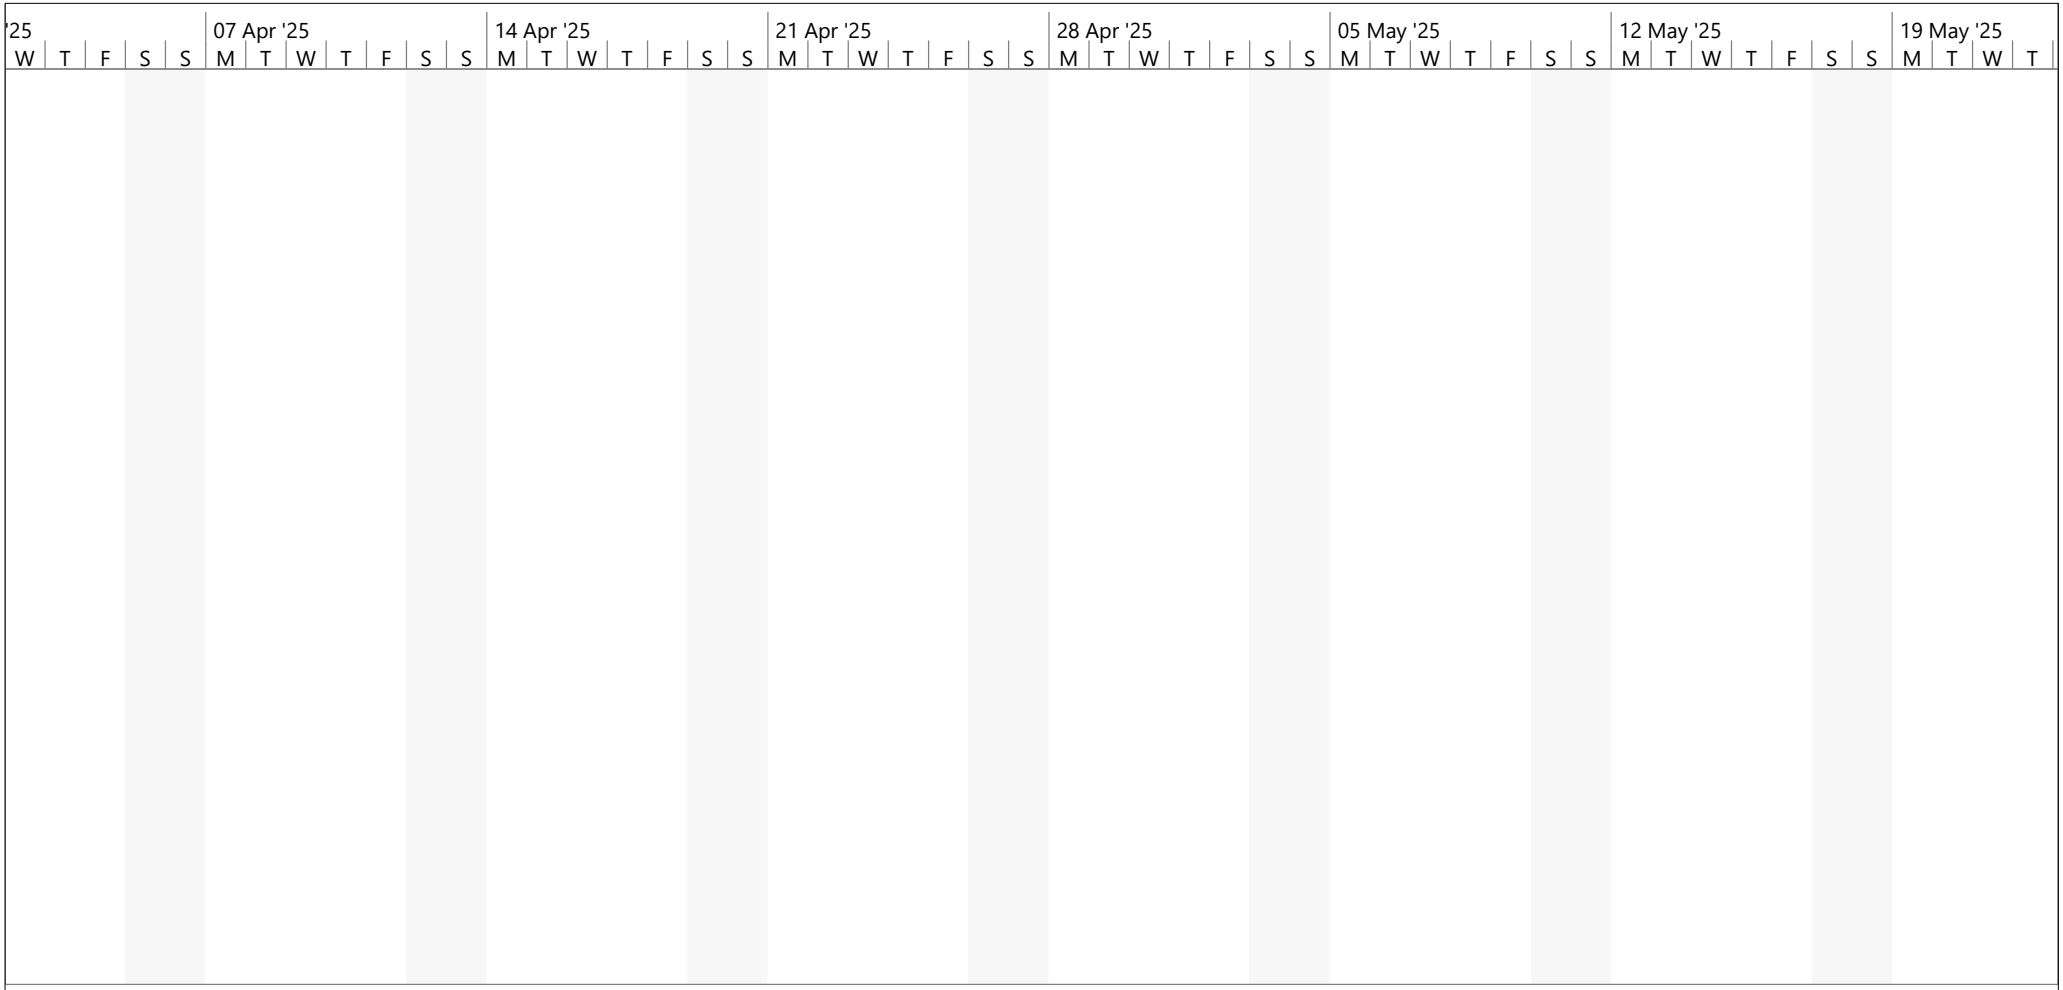


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

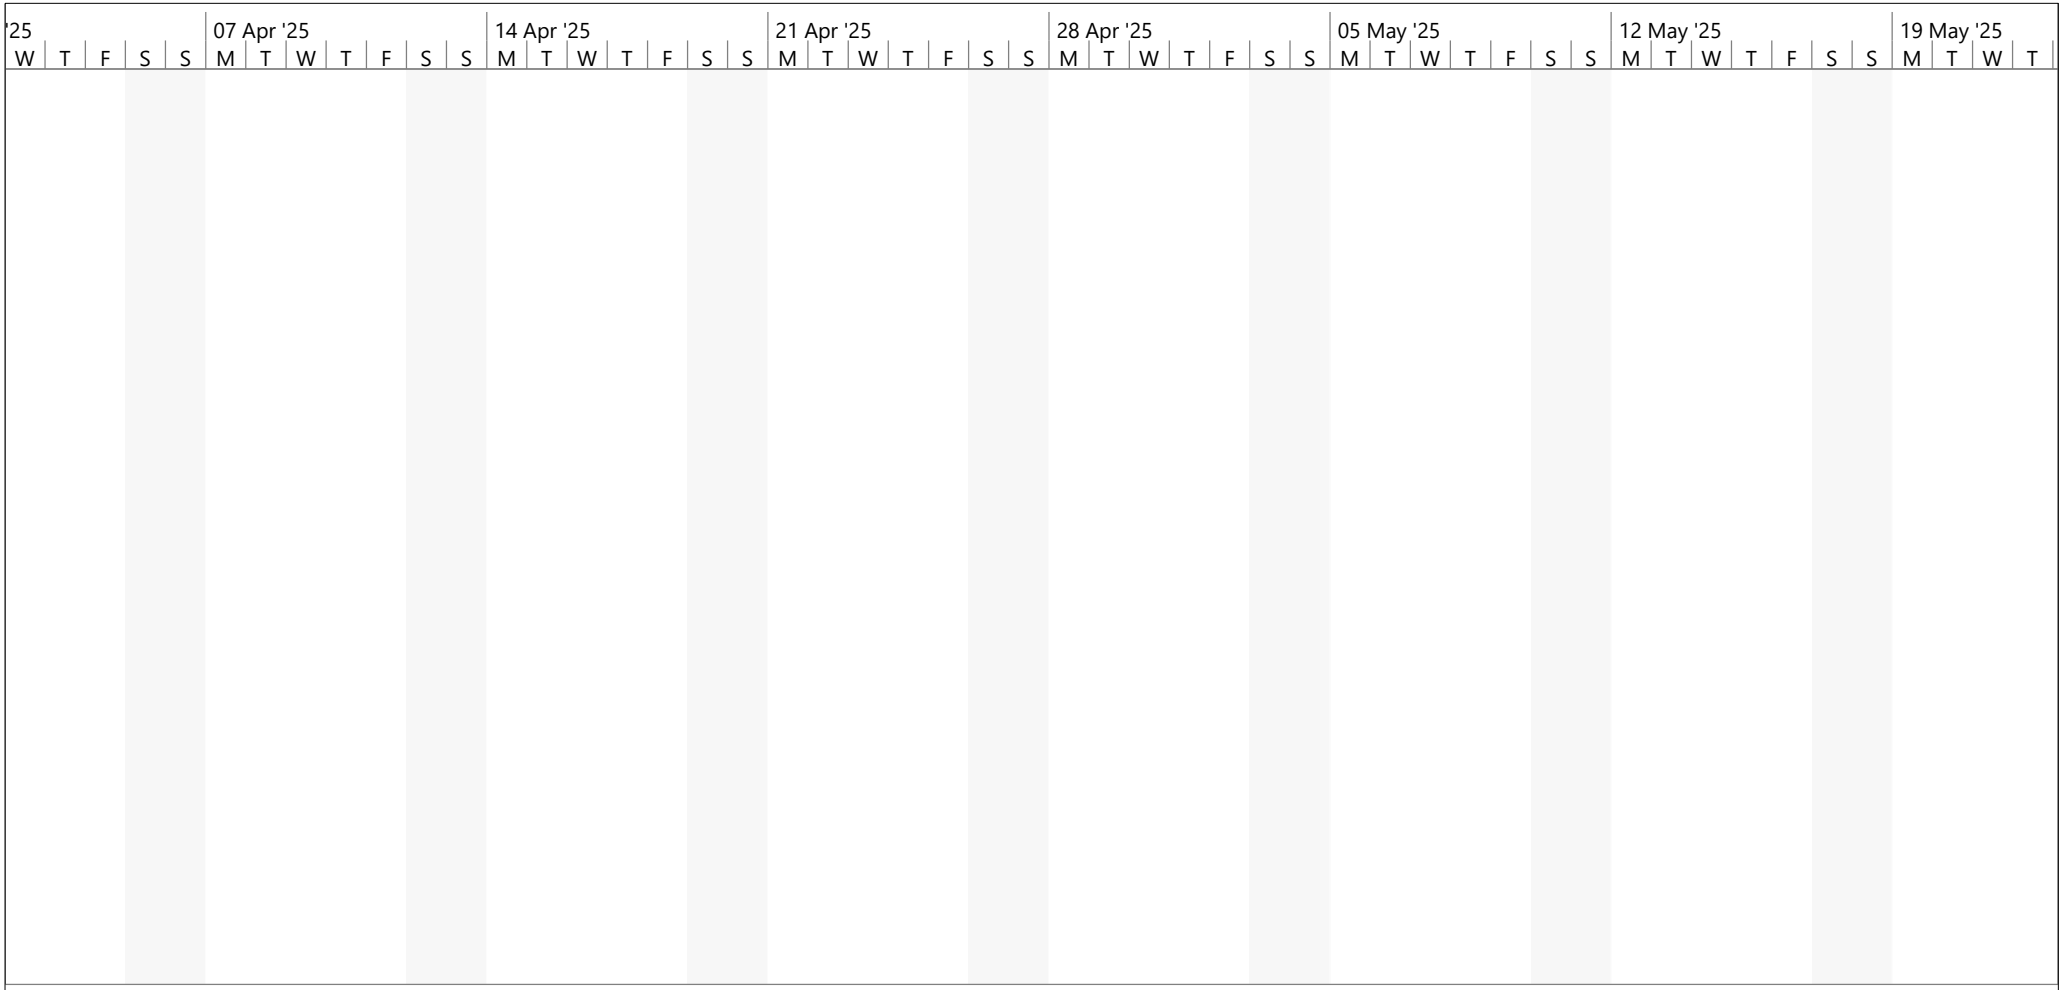


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

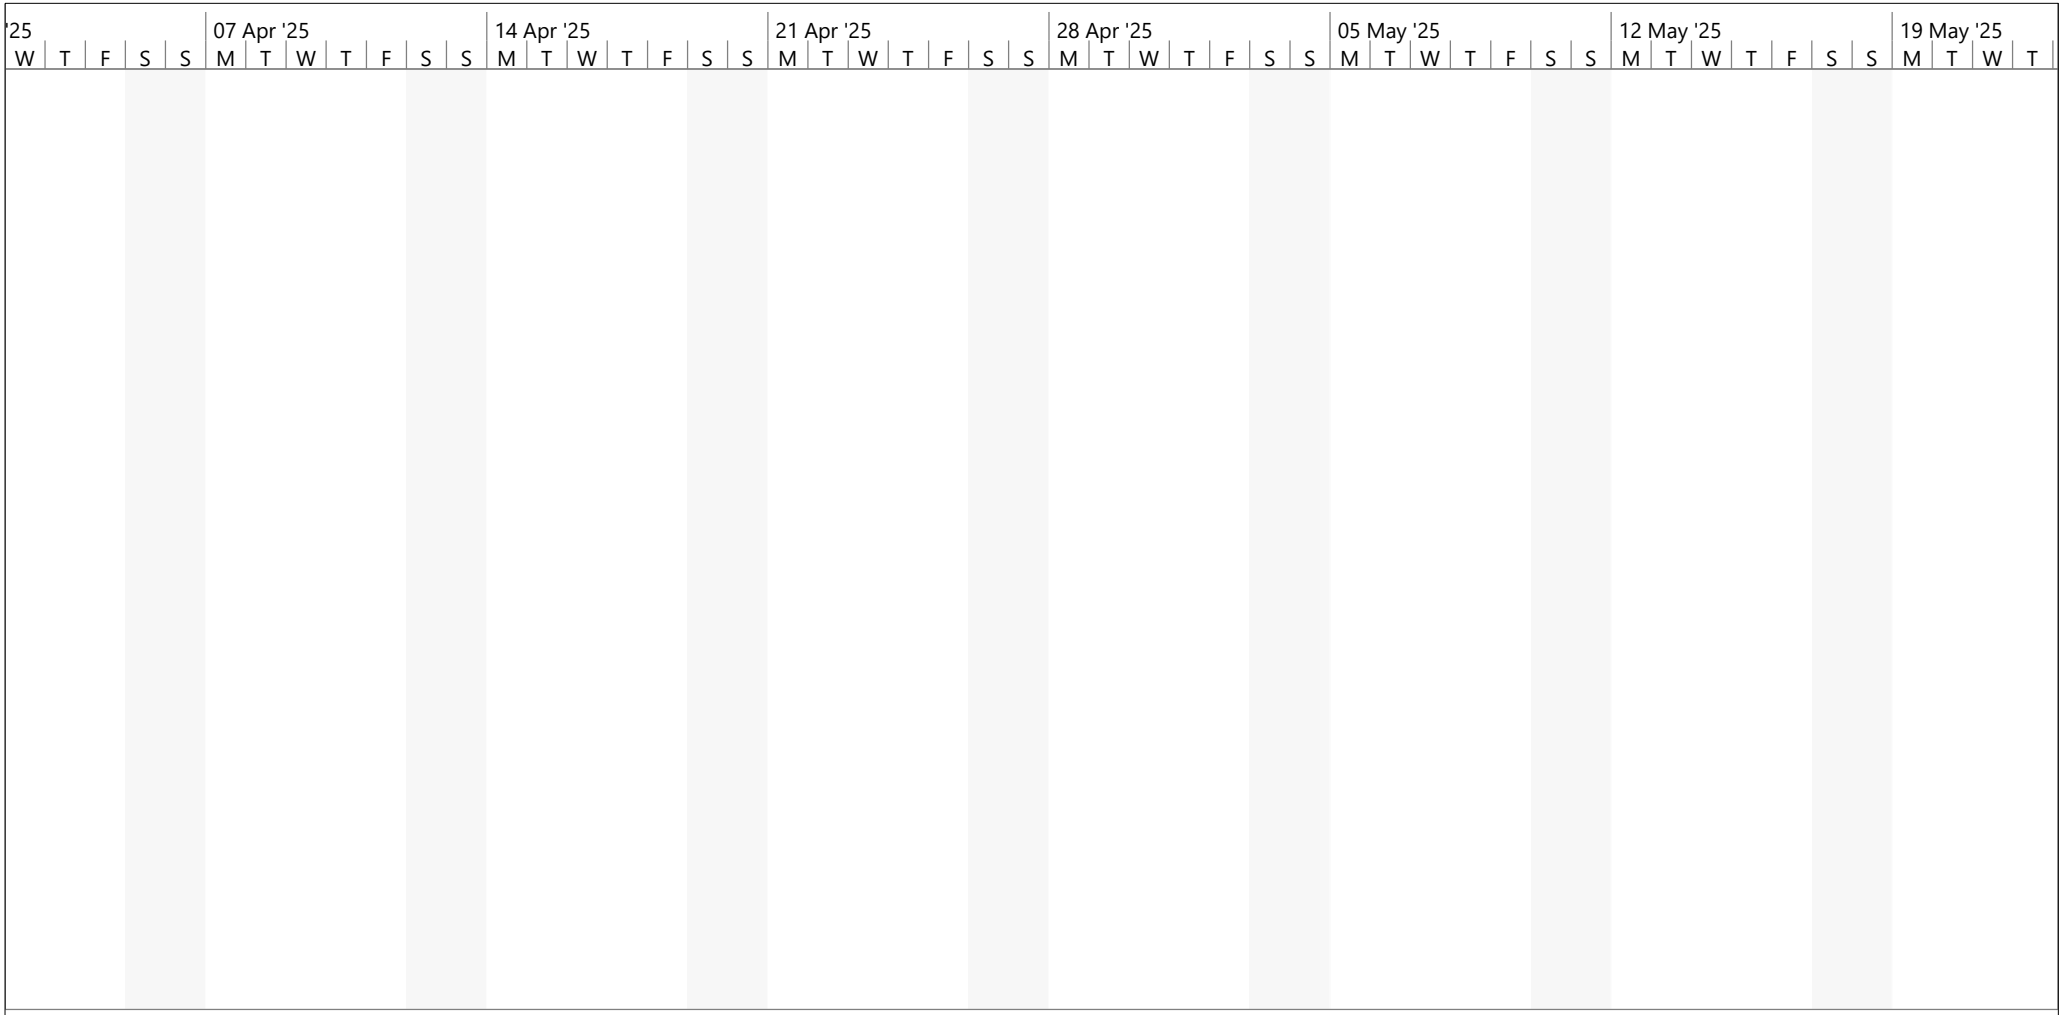


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

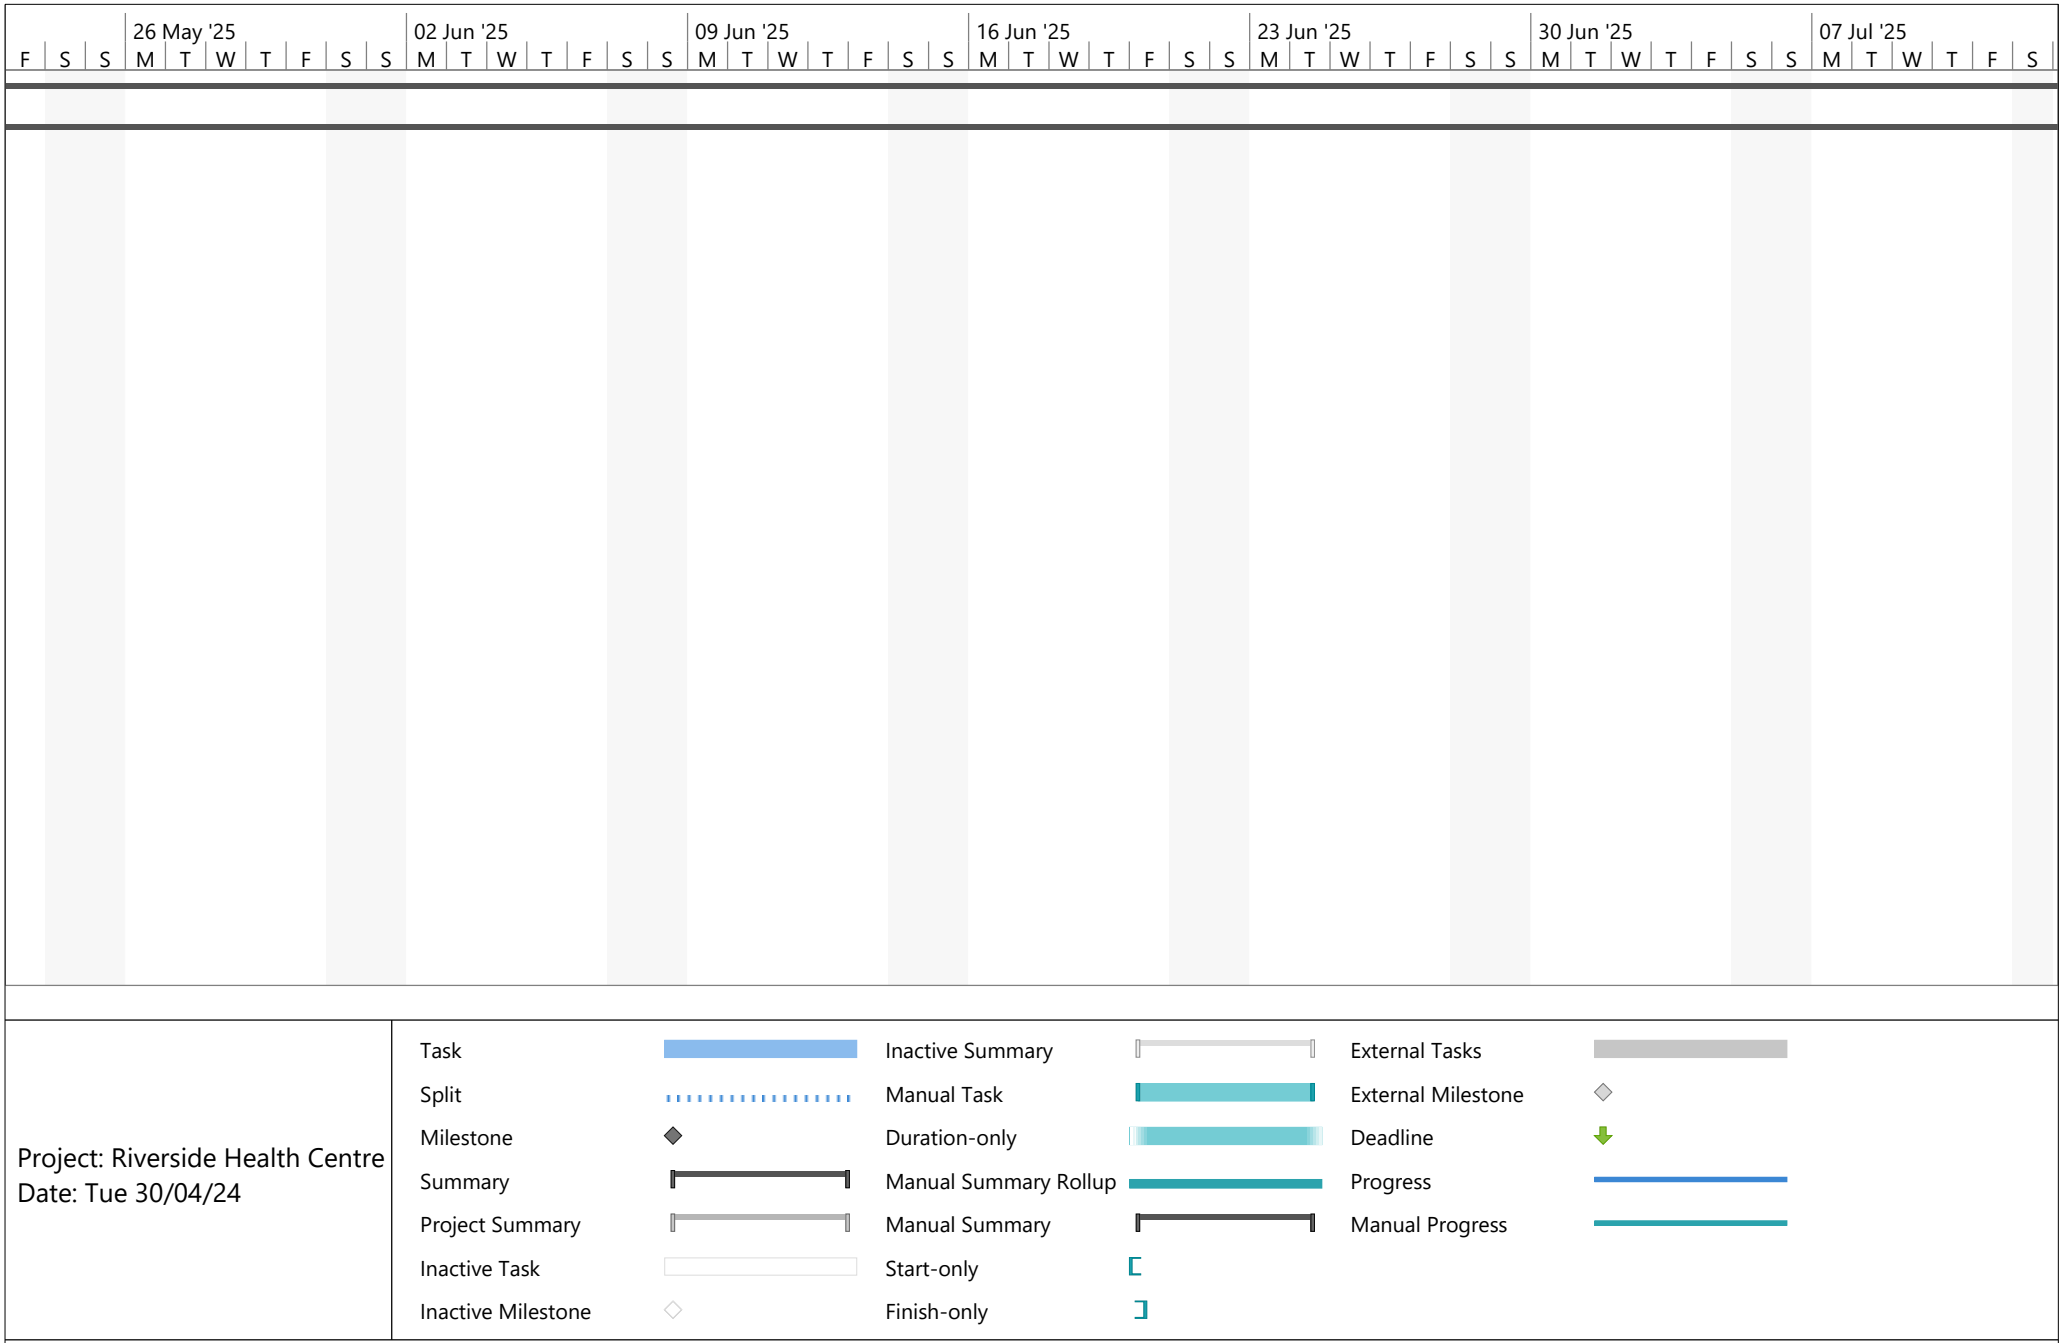


Project: Riverside Health Centre
Date: Tue 30/04/24


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

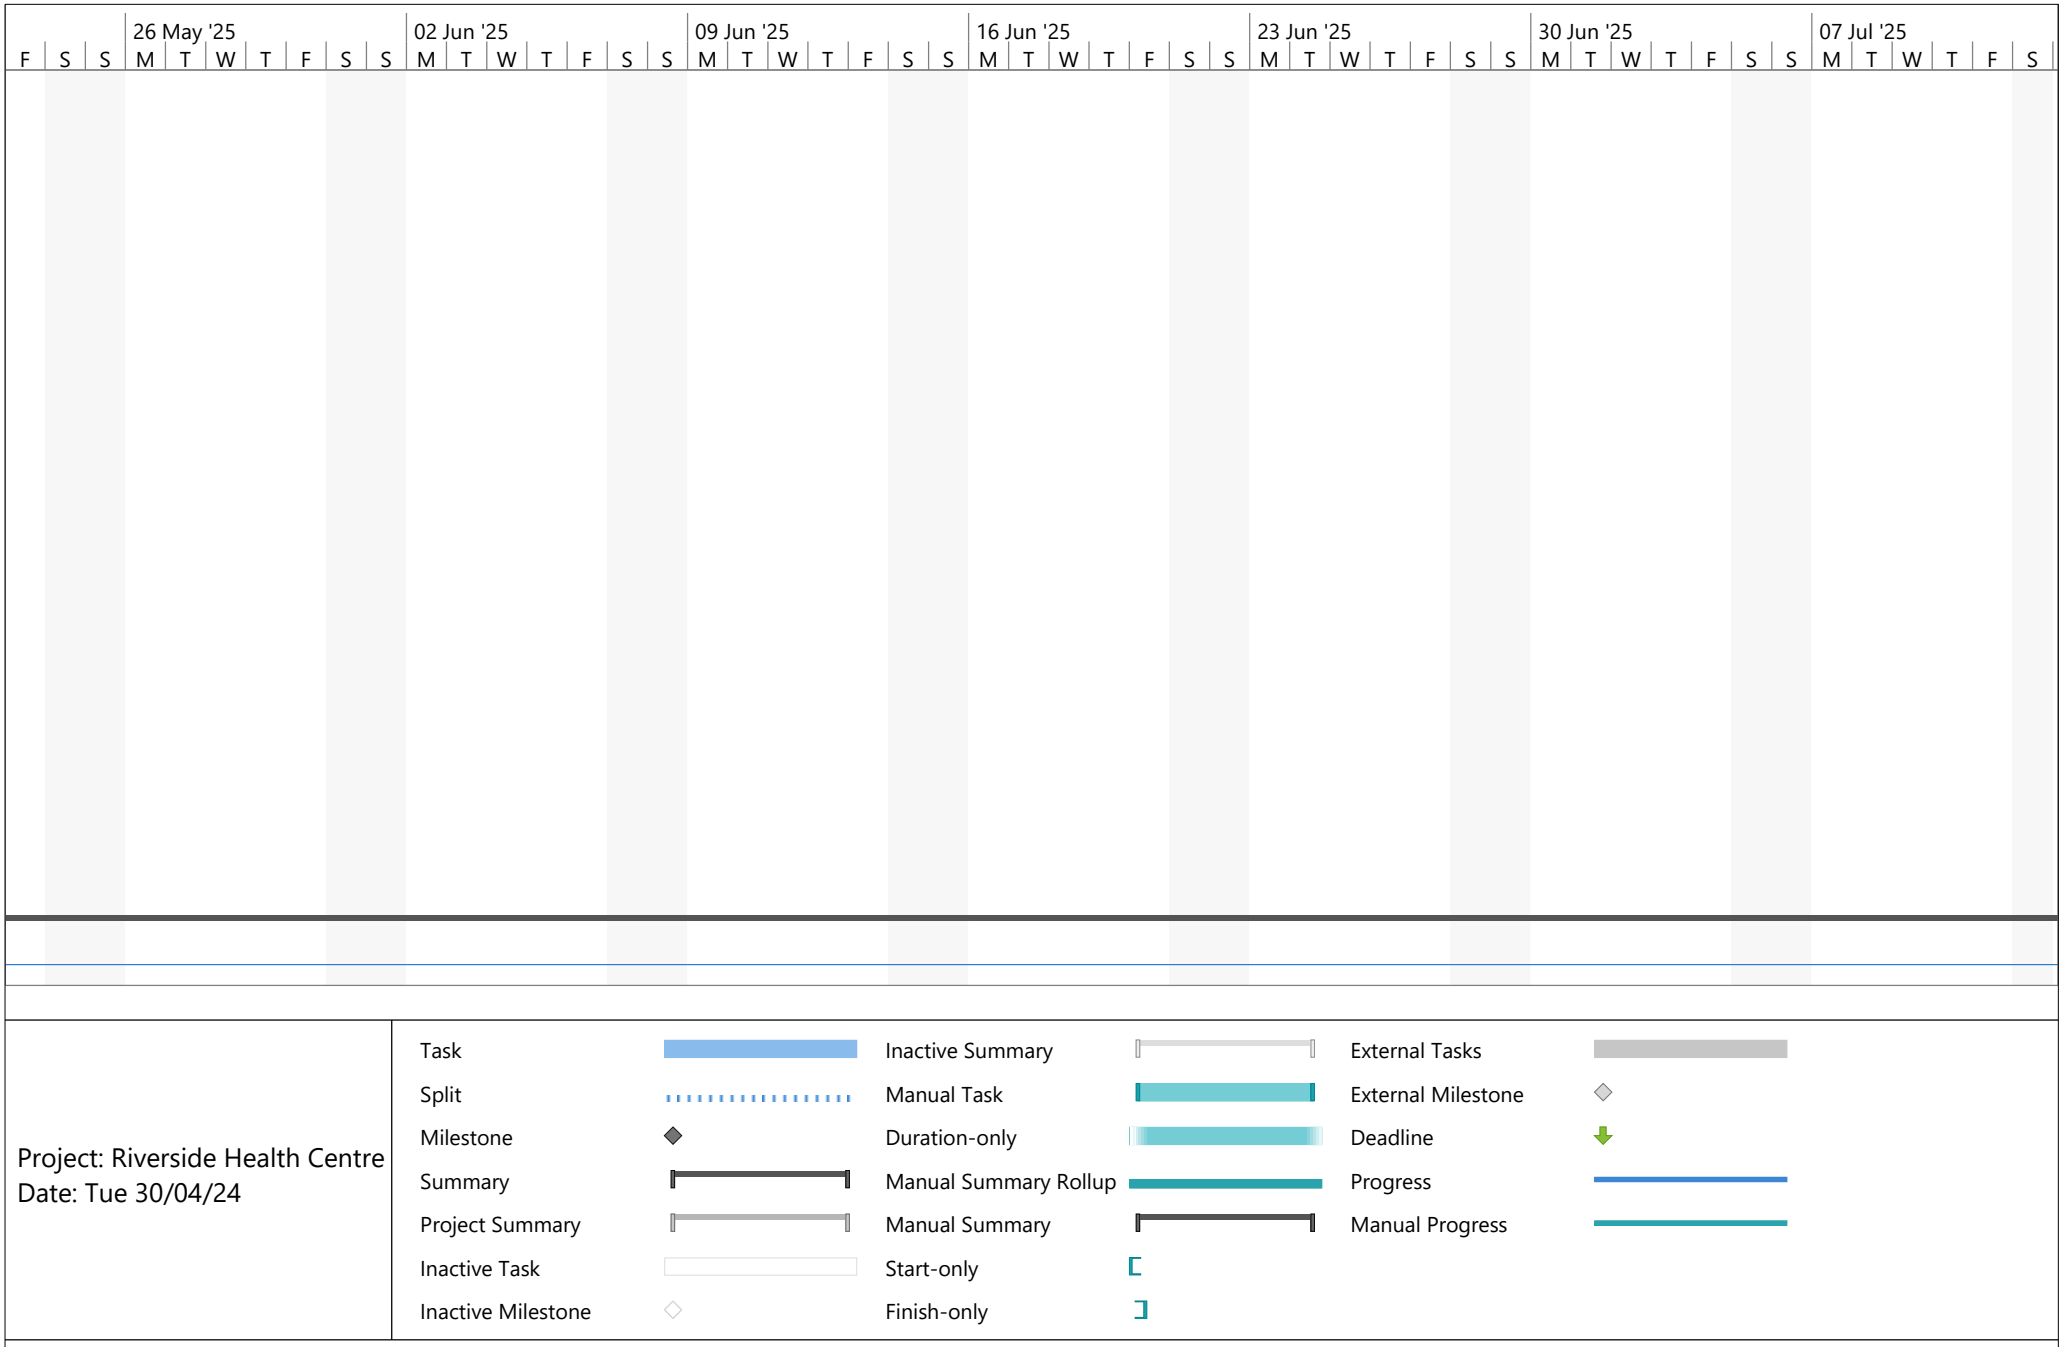

Project: Riverside Health Centre
Date: Tue 30/04/24


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

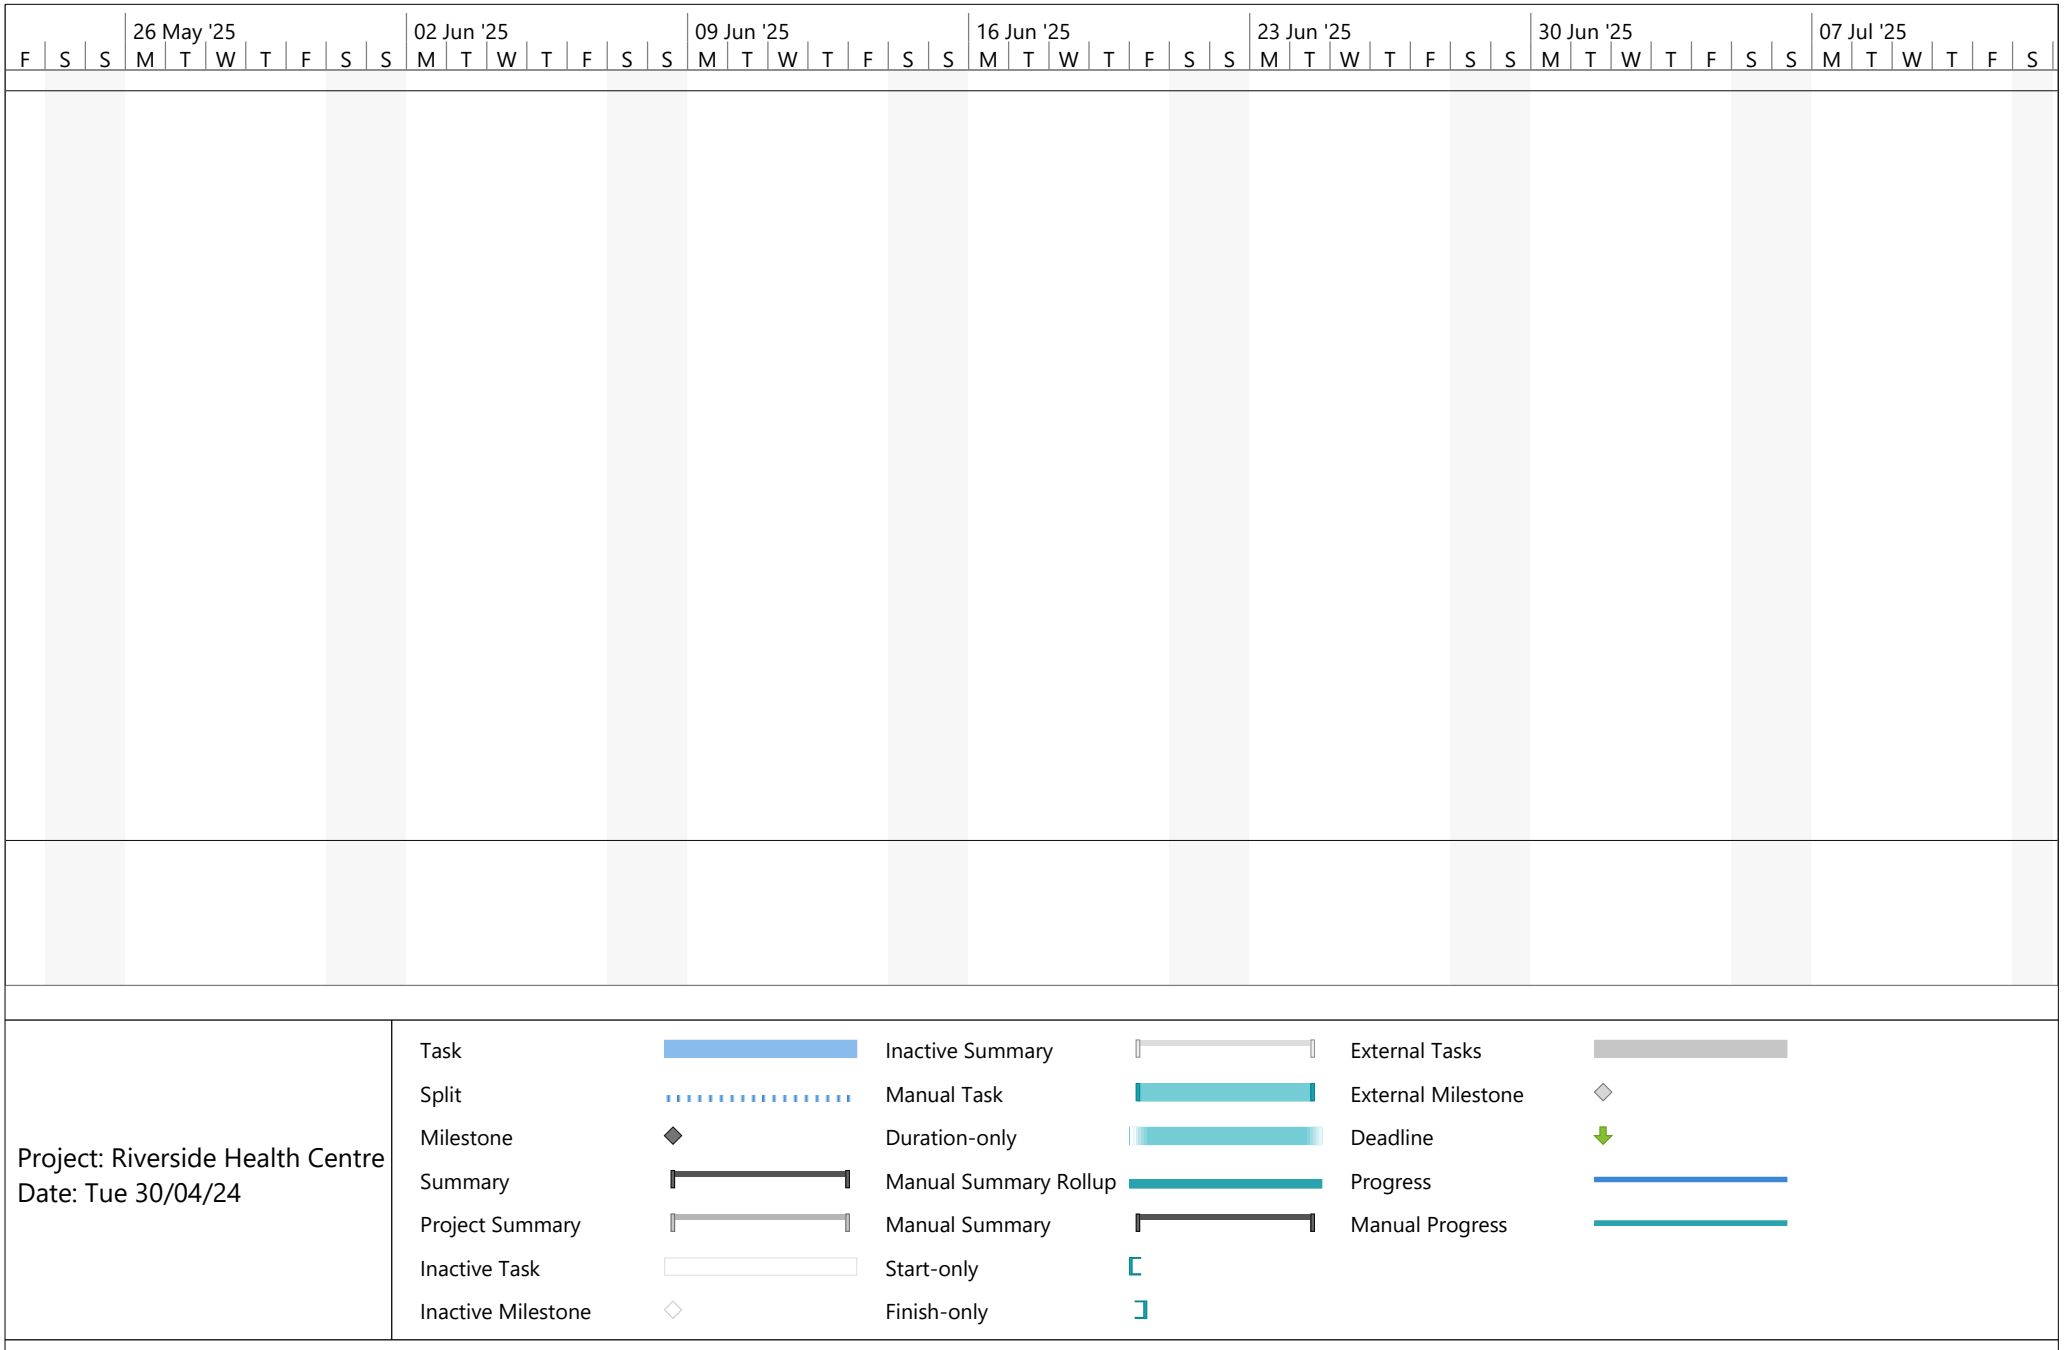
26 May '25
02 Jun '25
09 Jun '25
16 Jun '25
23 Jun '25
30 Jun '25
07 Jul '25
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

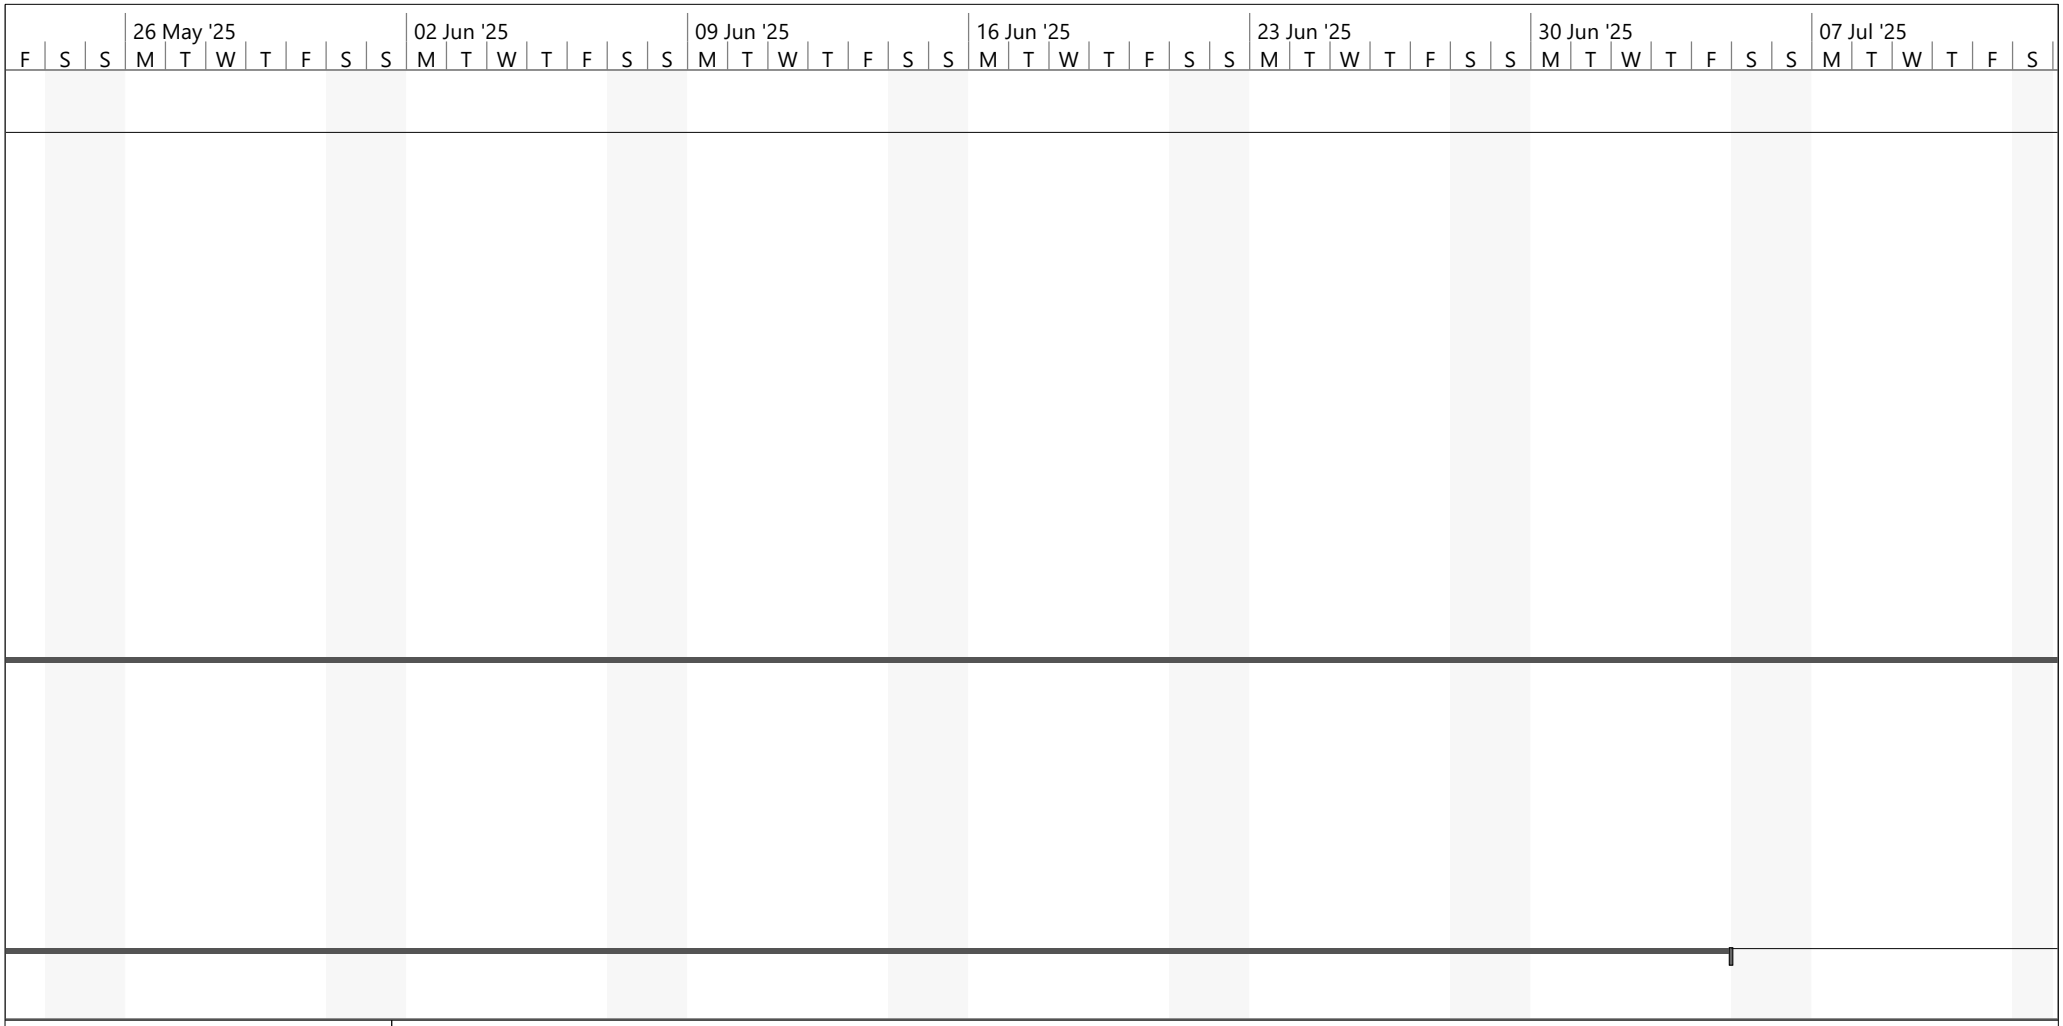


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

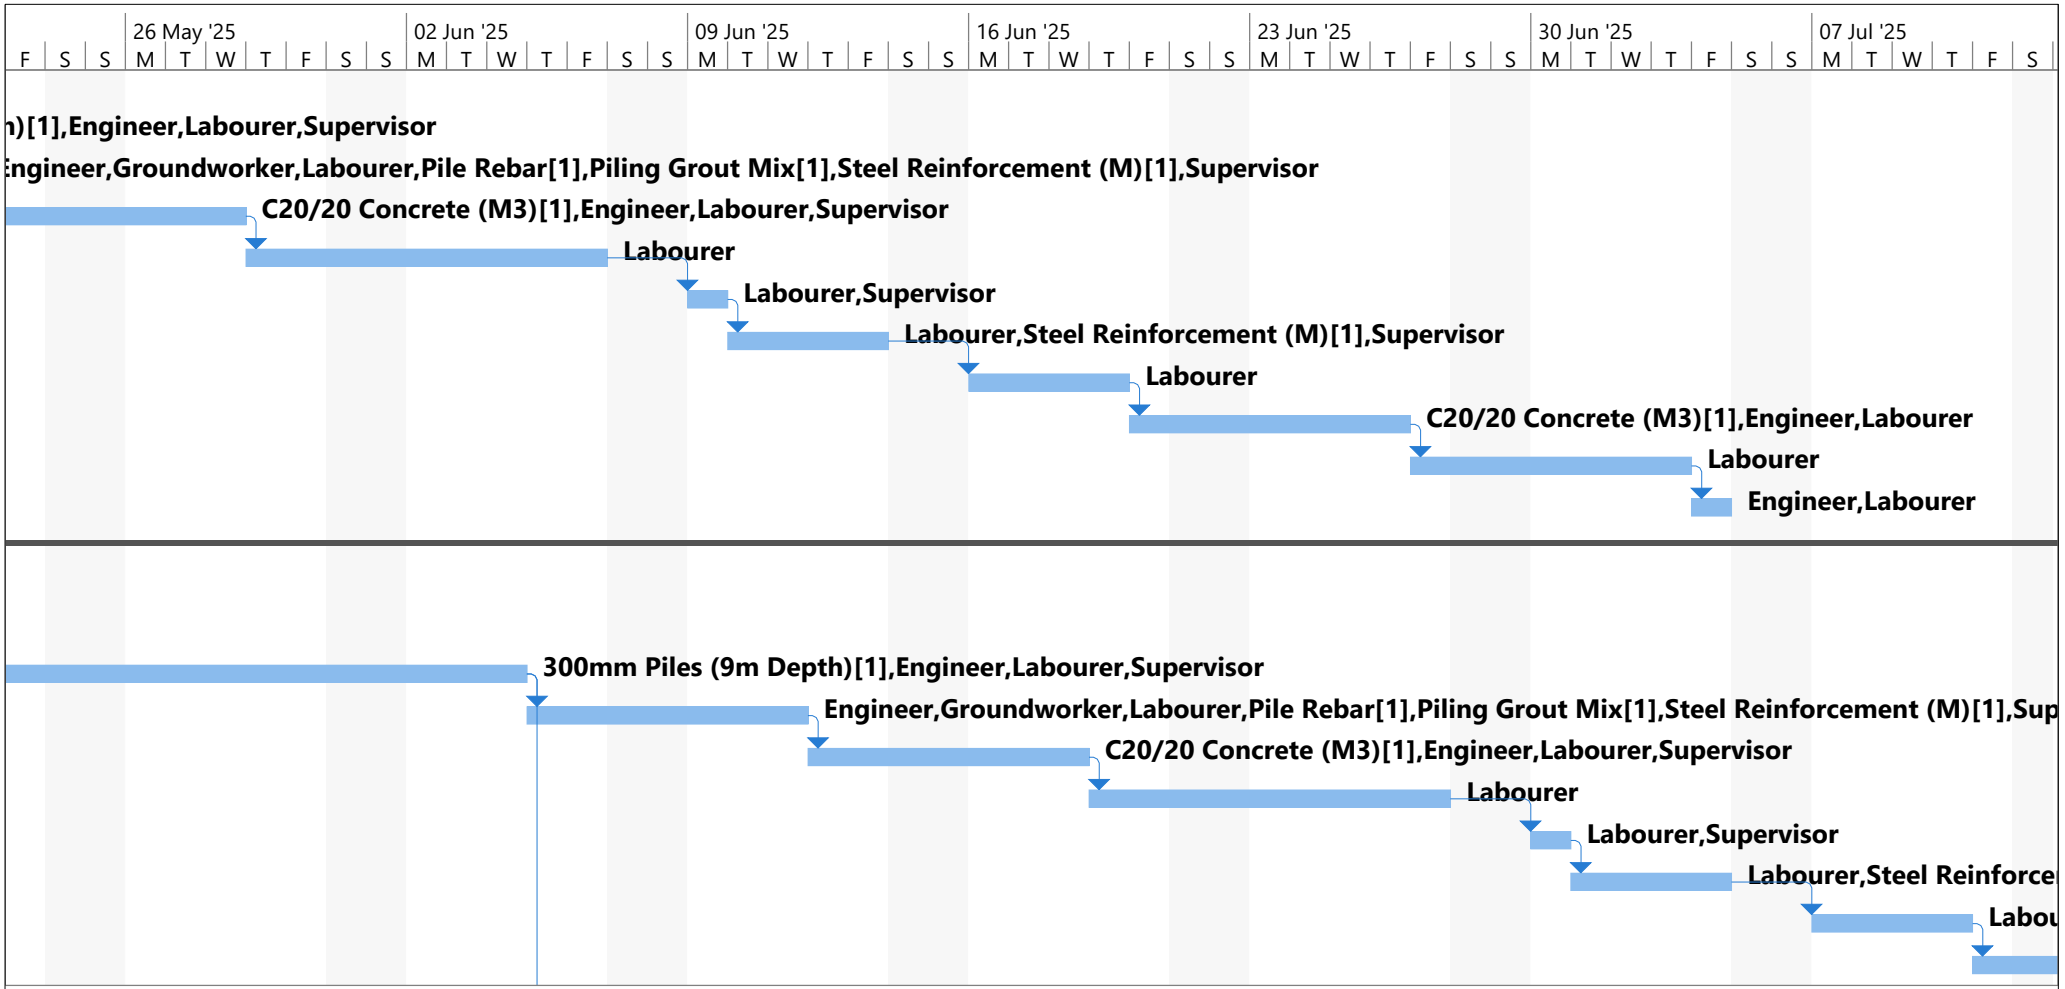


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

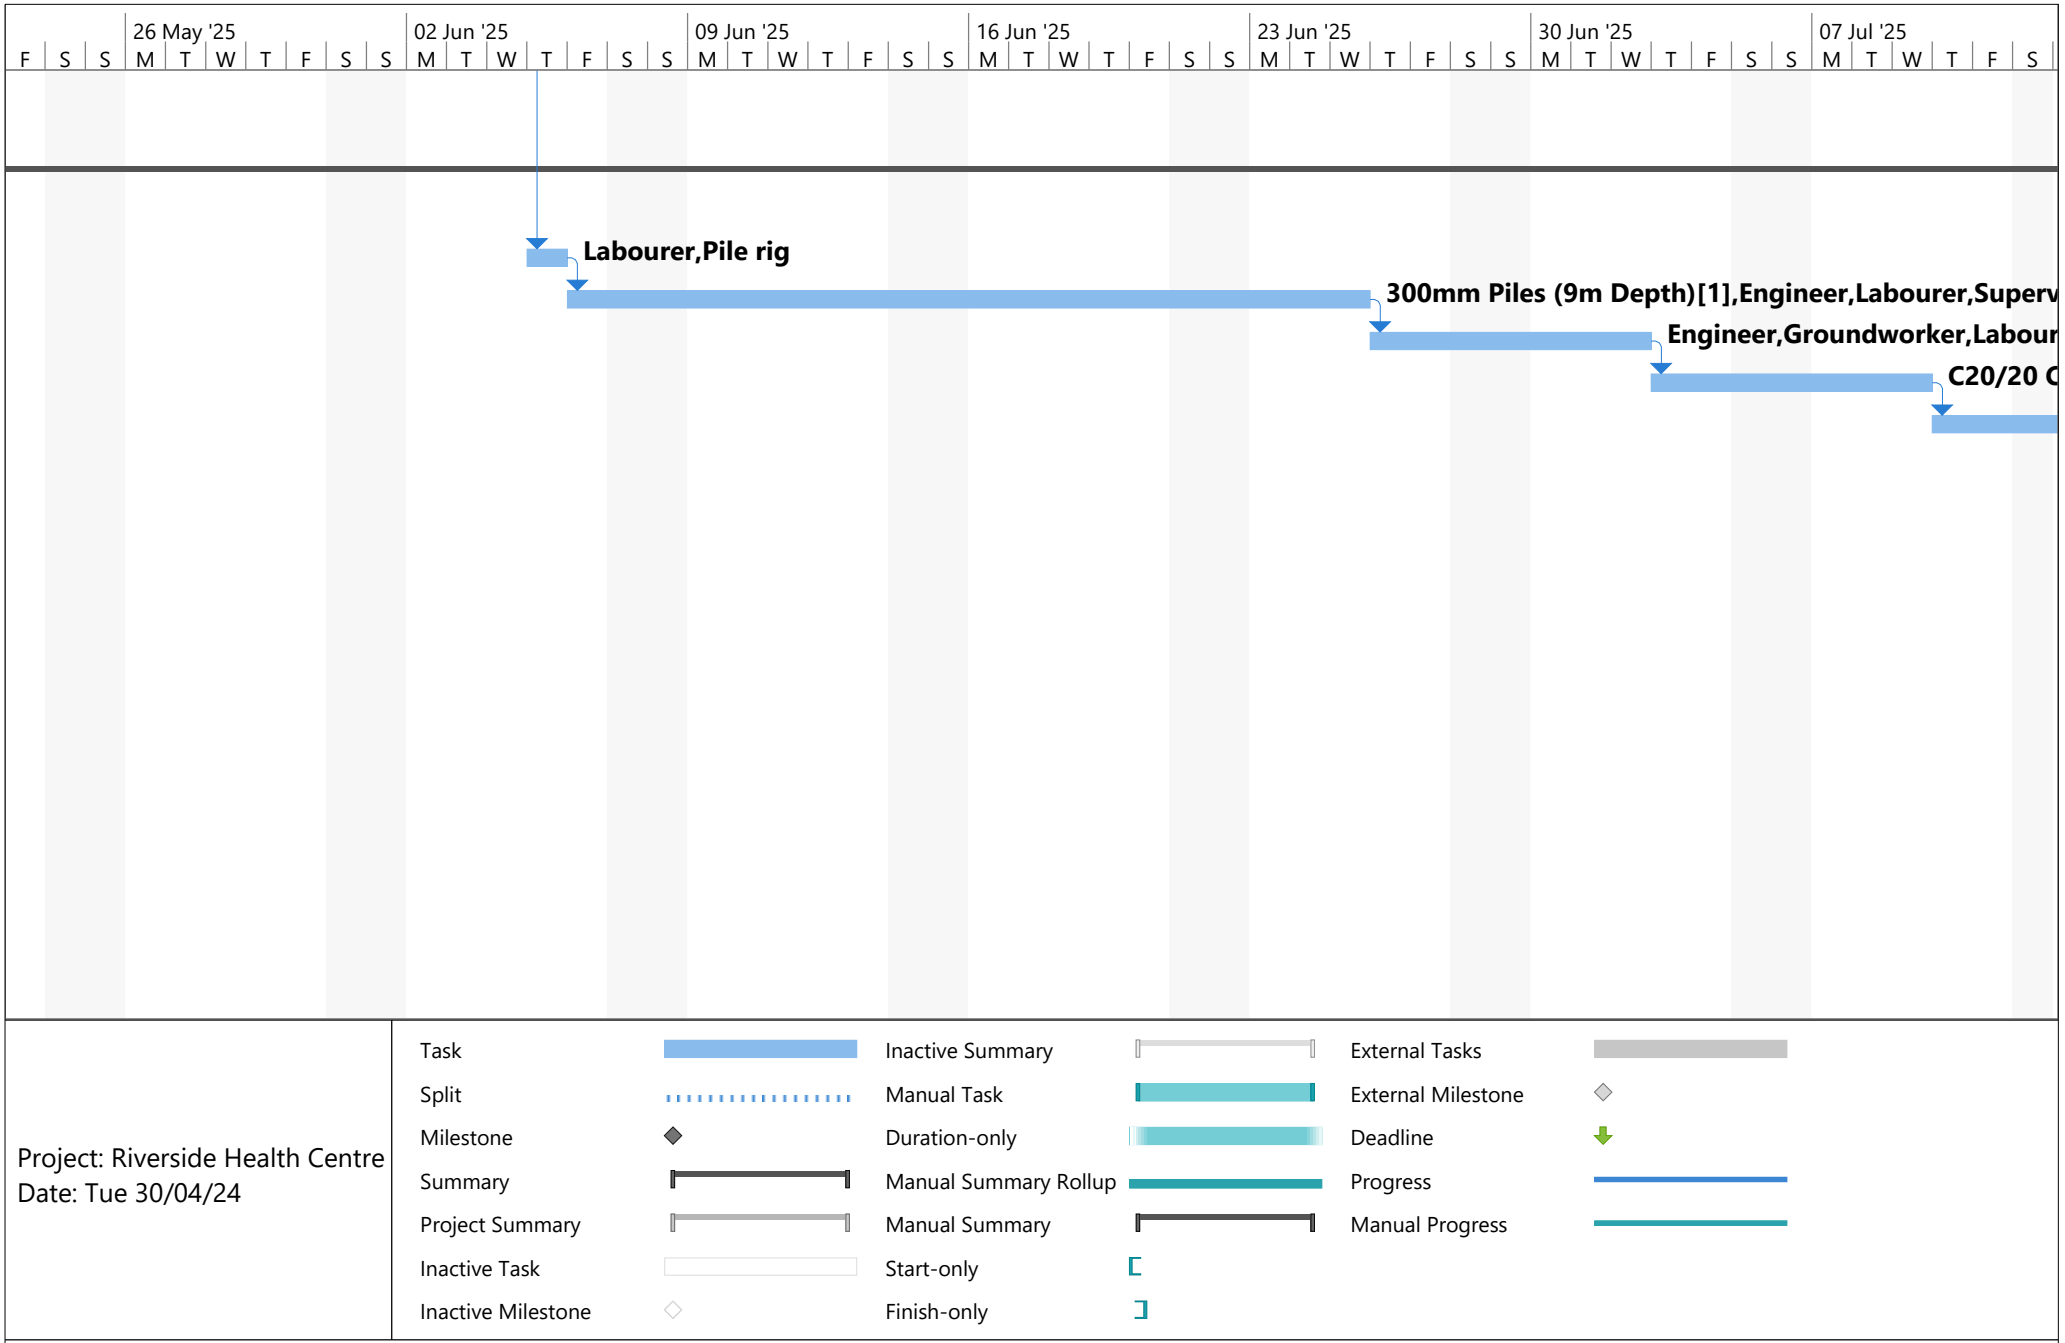


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

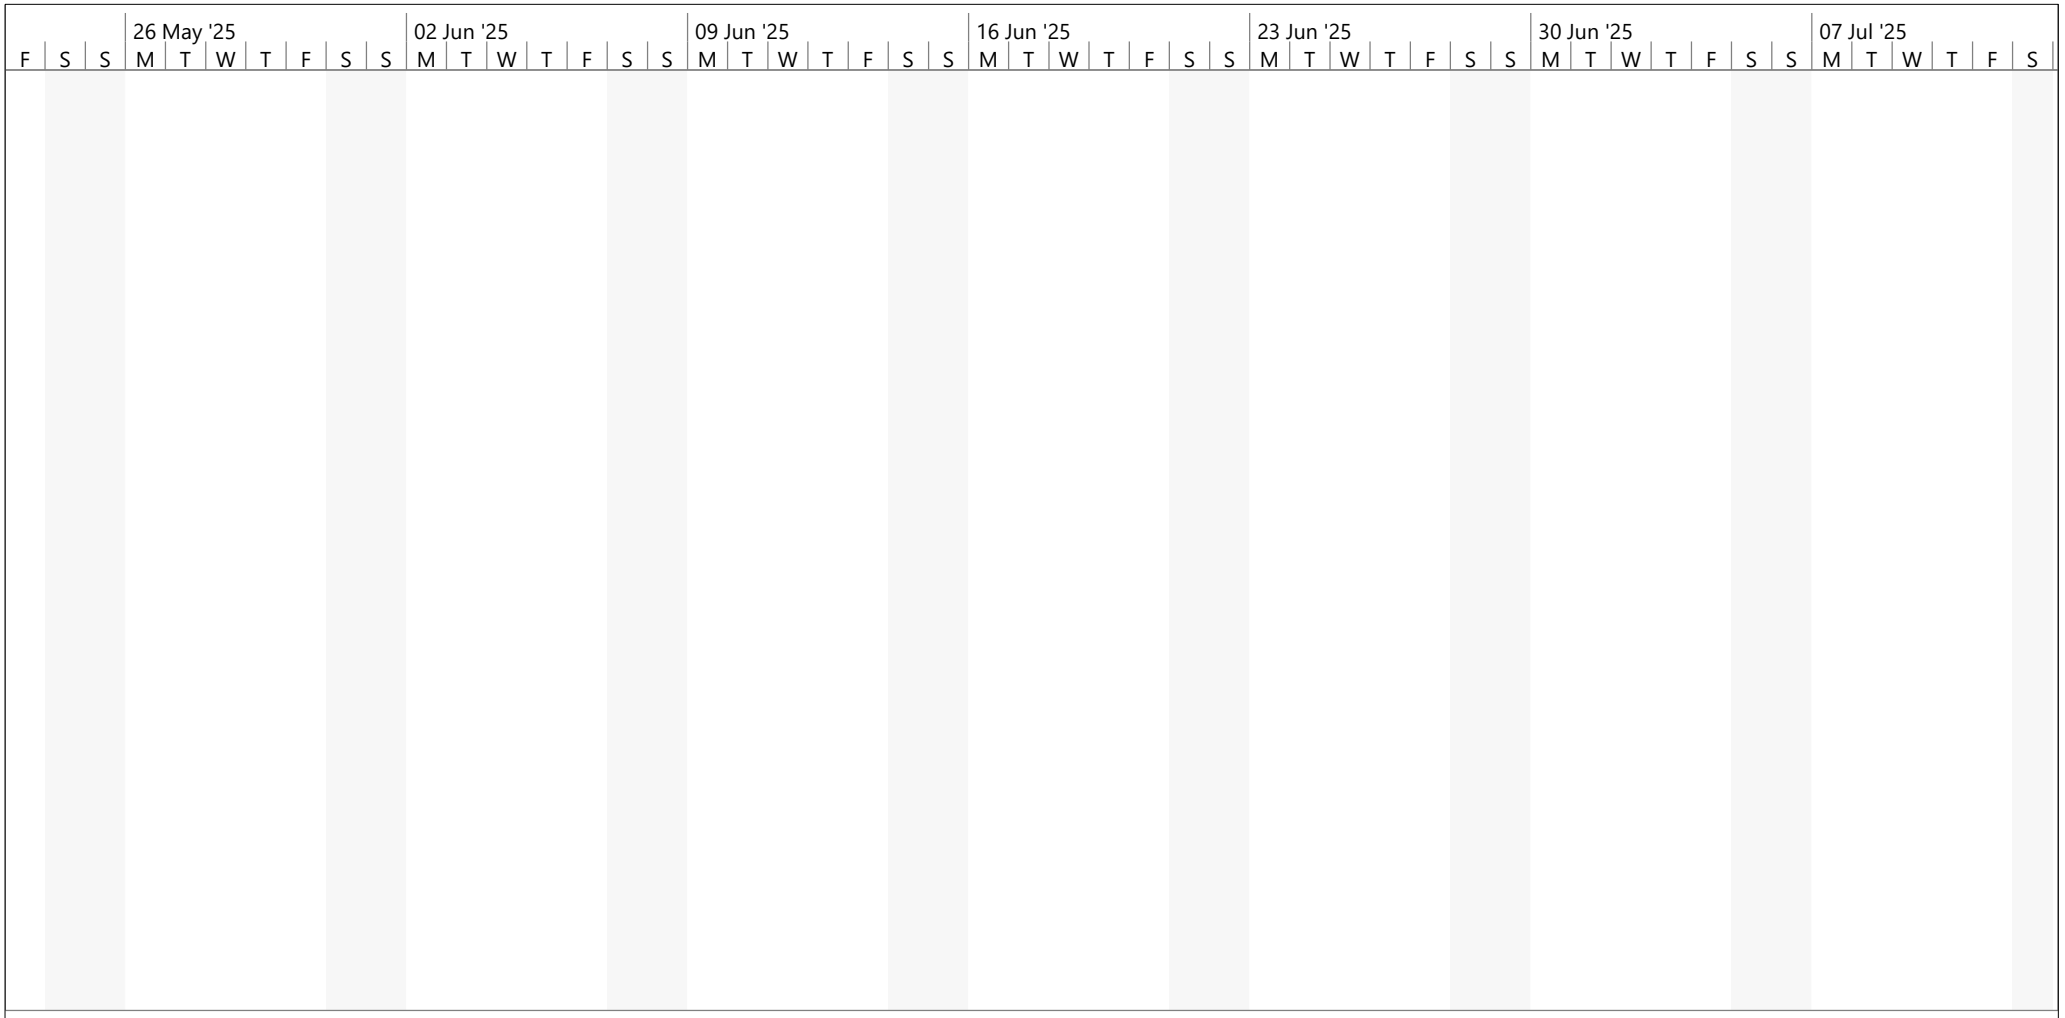


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

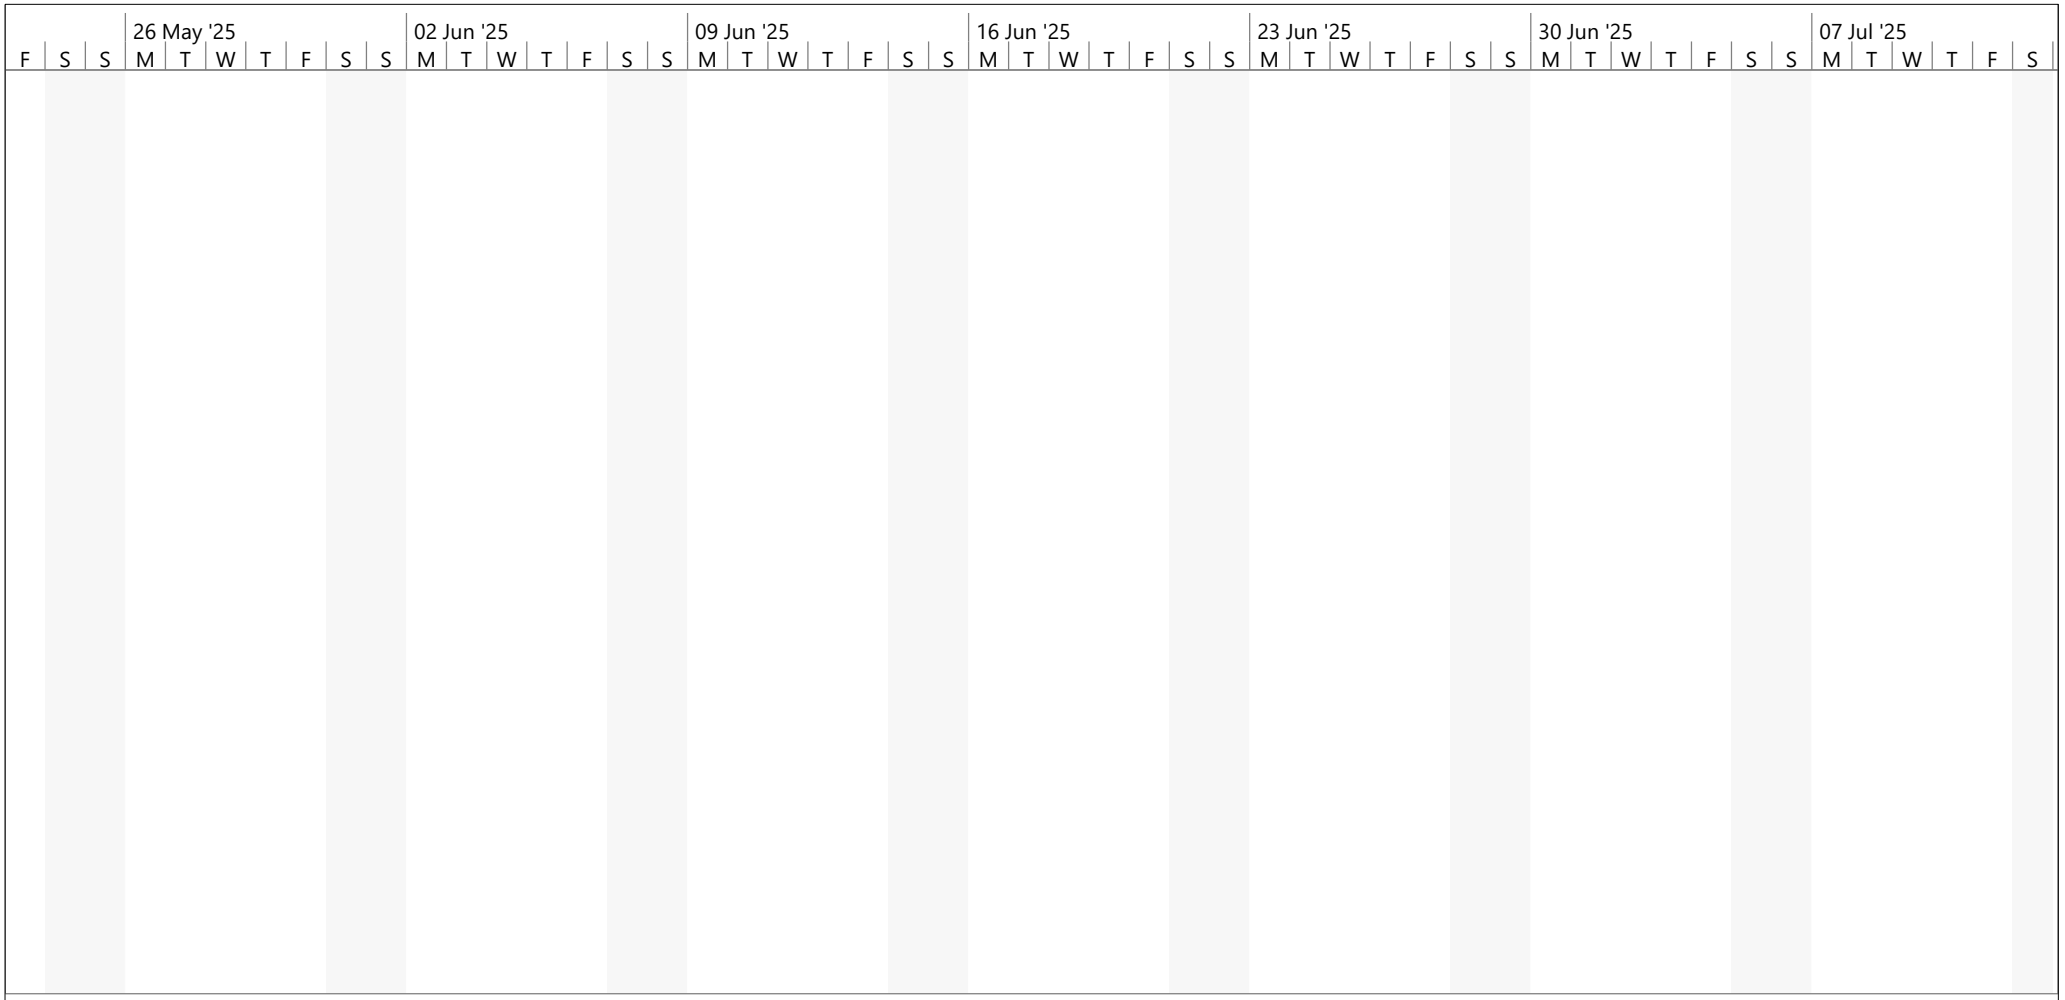


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

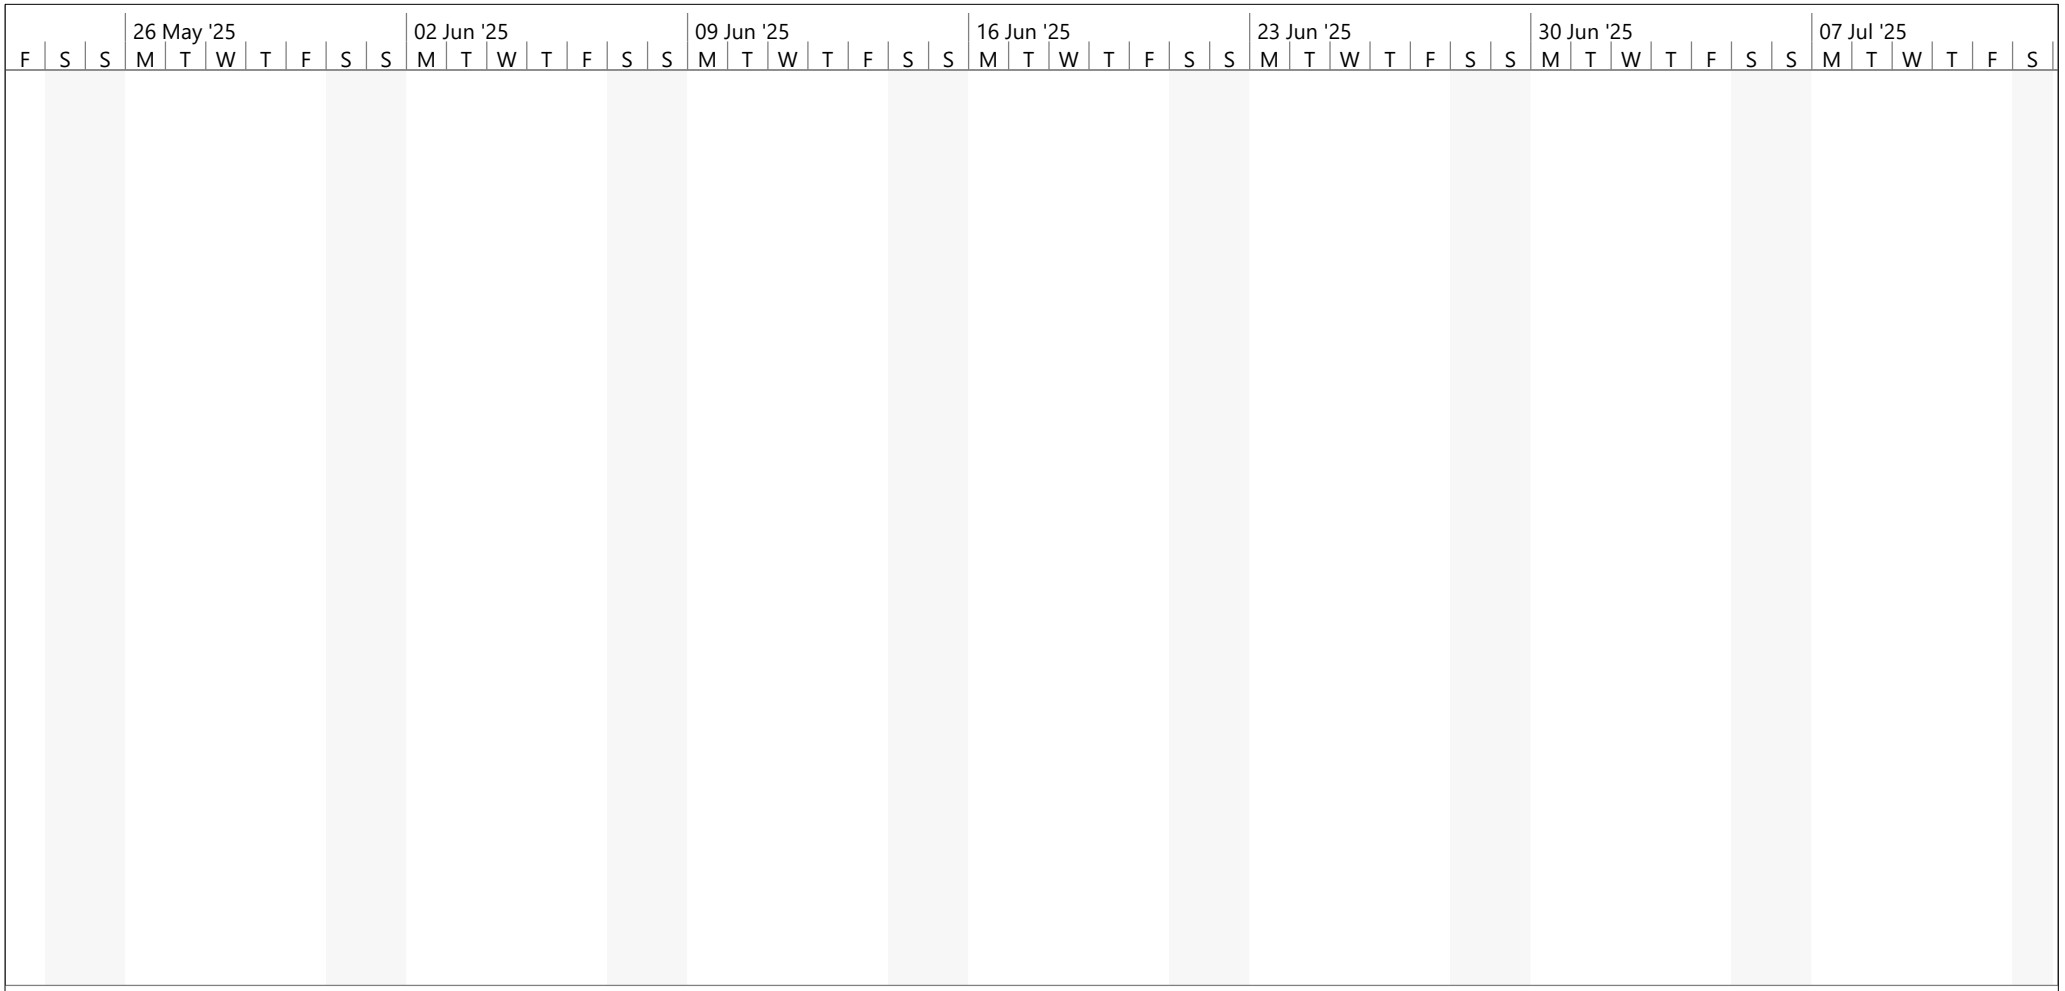


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

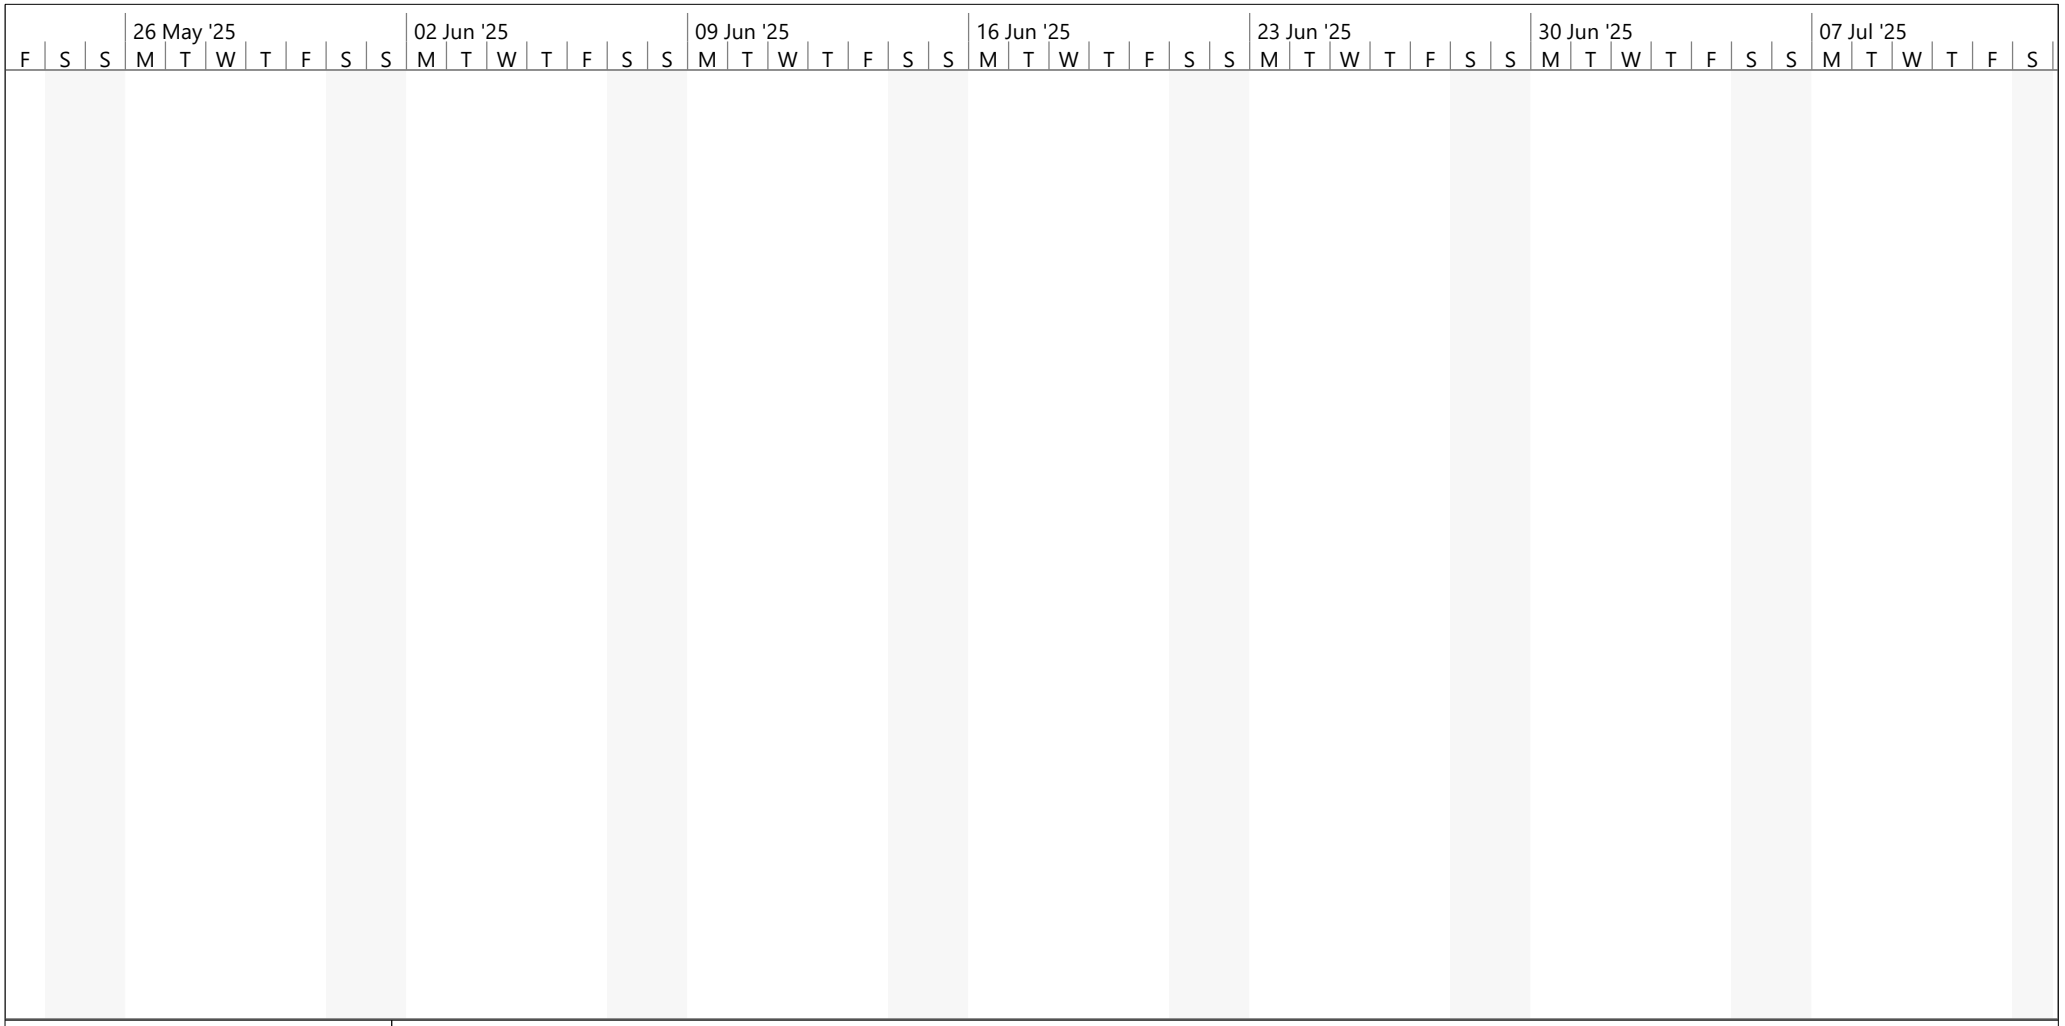


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

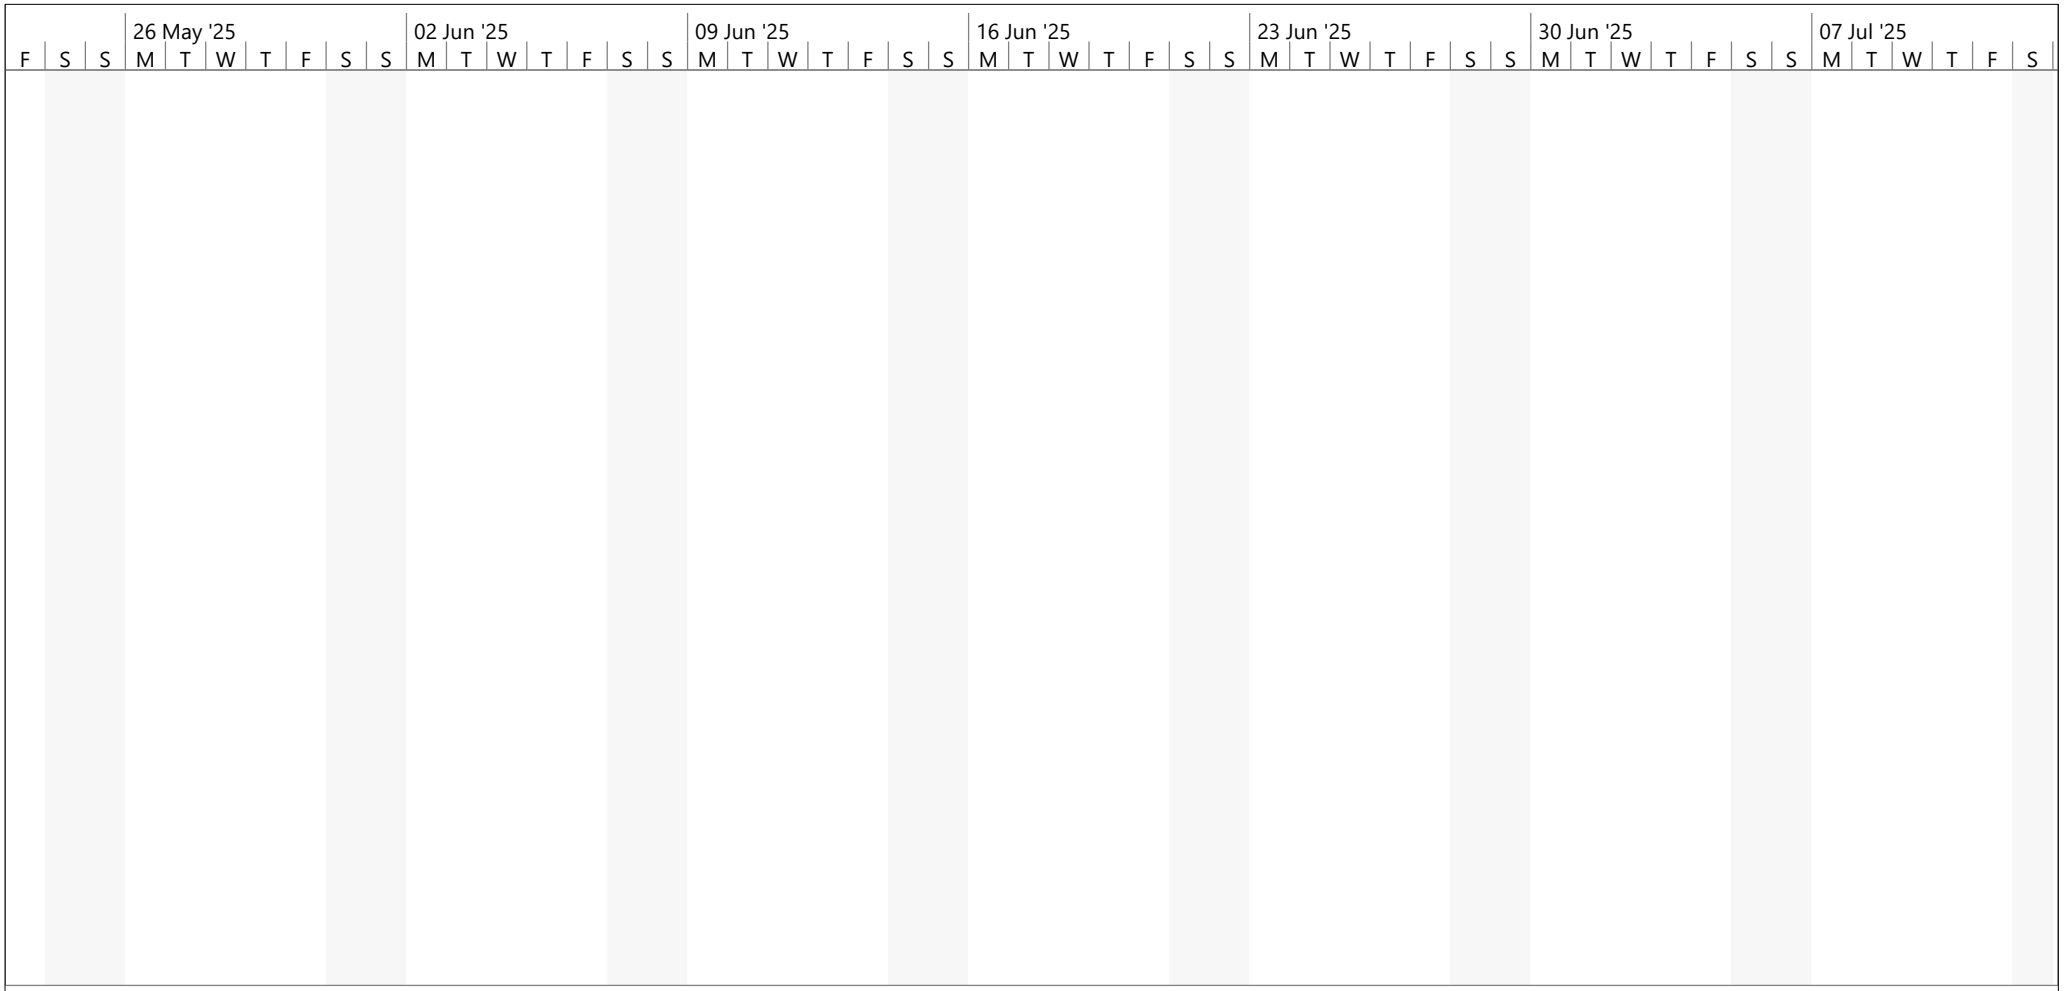


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

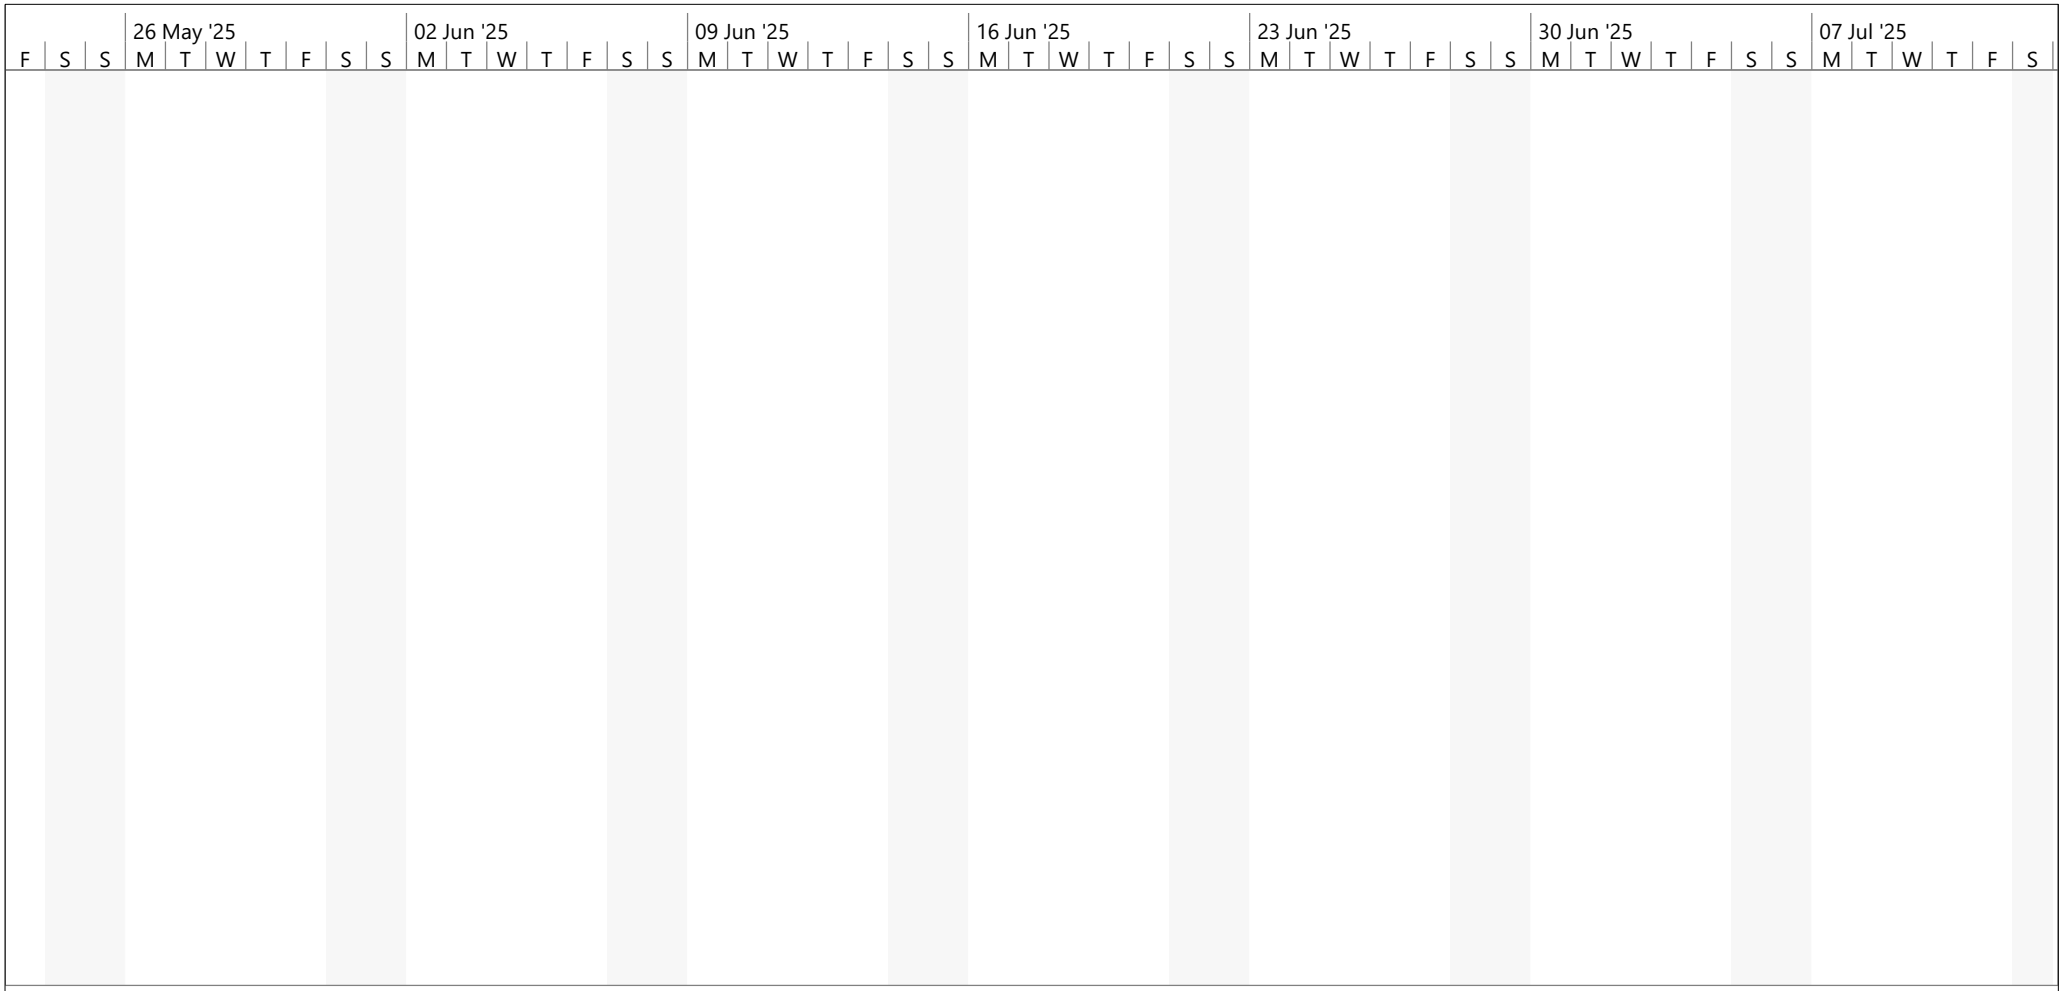


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

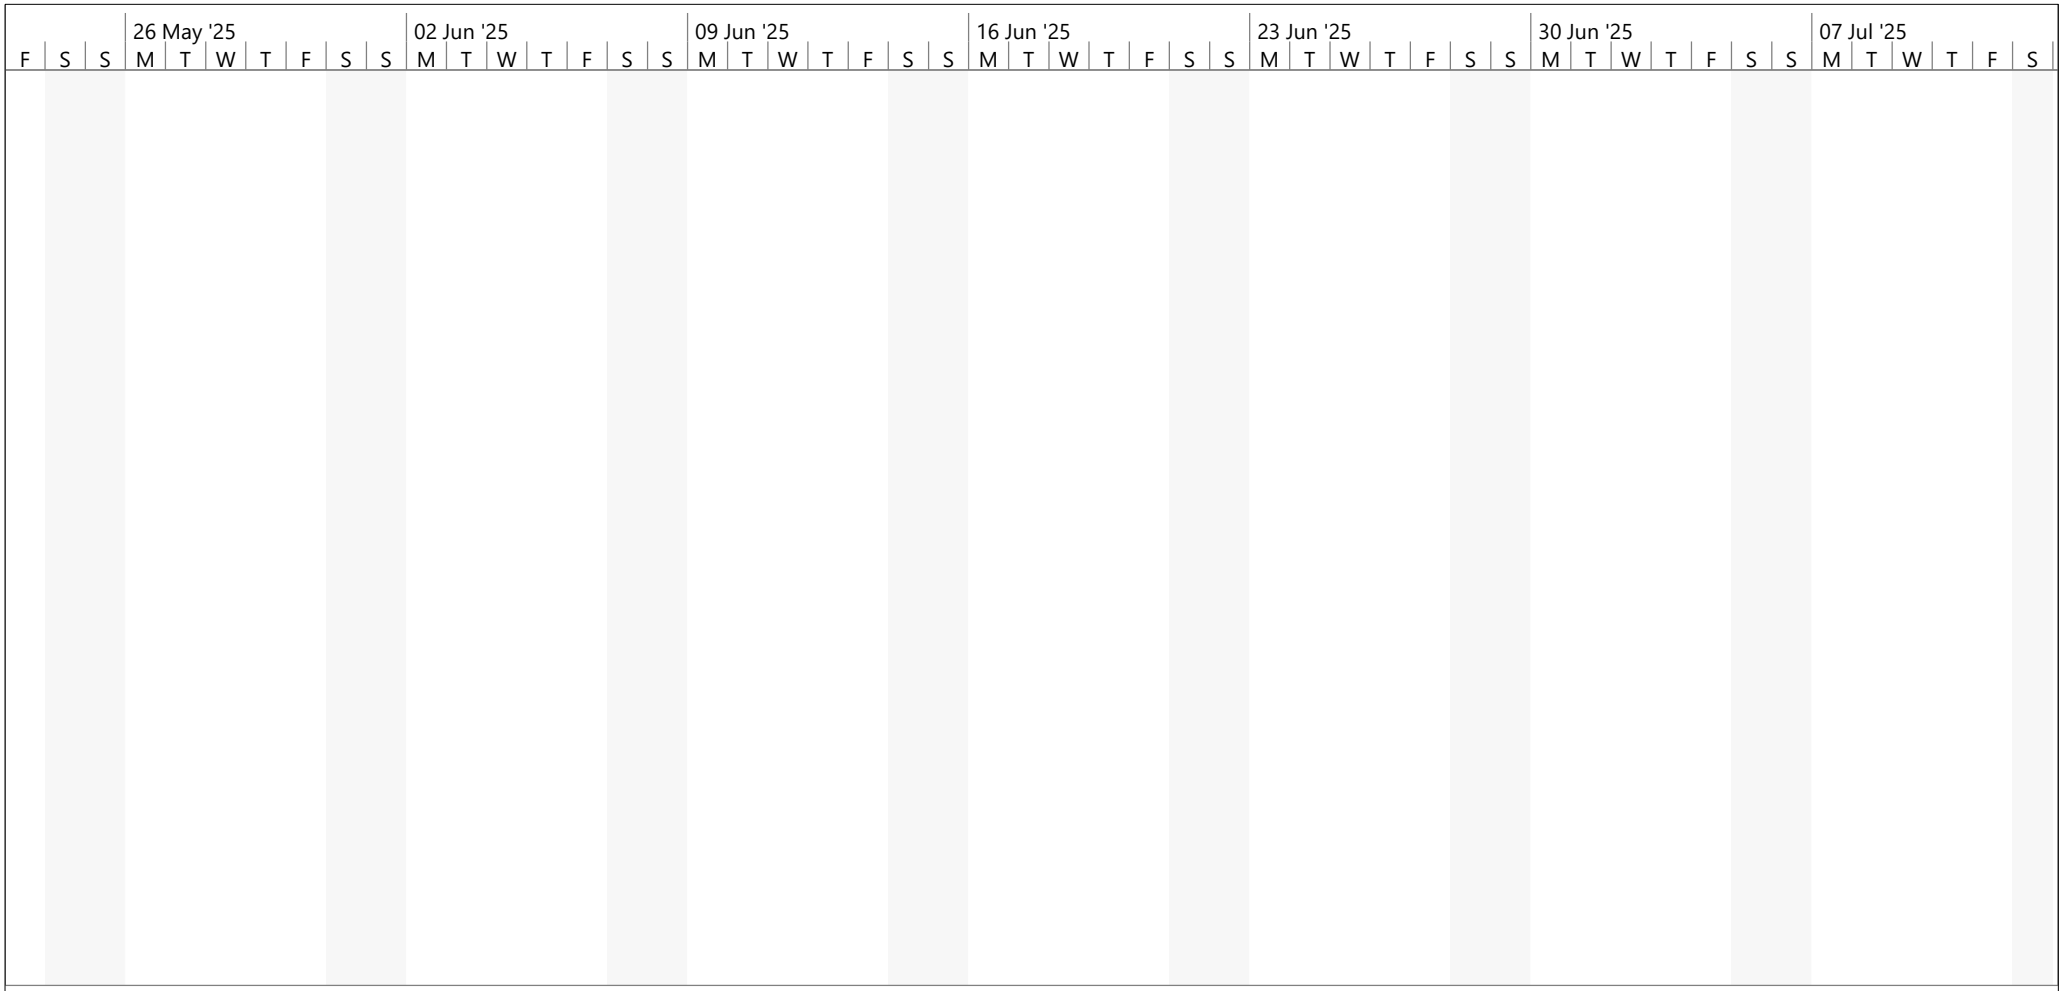


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

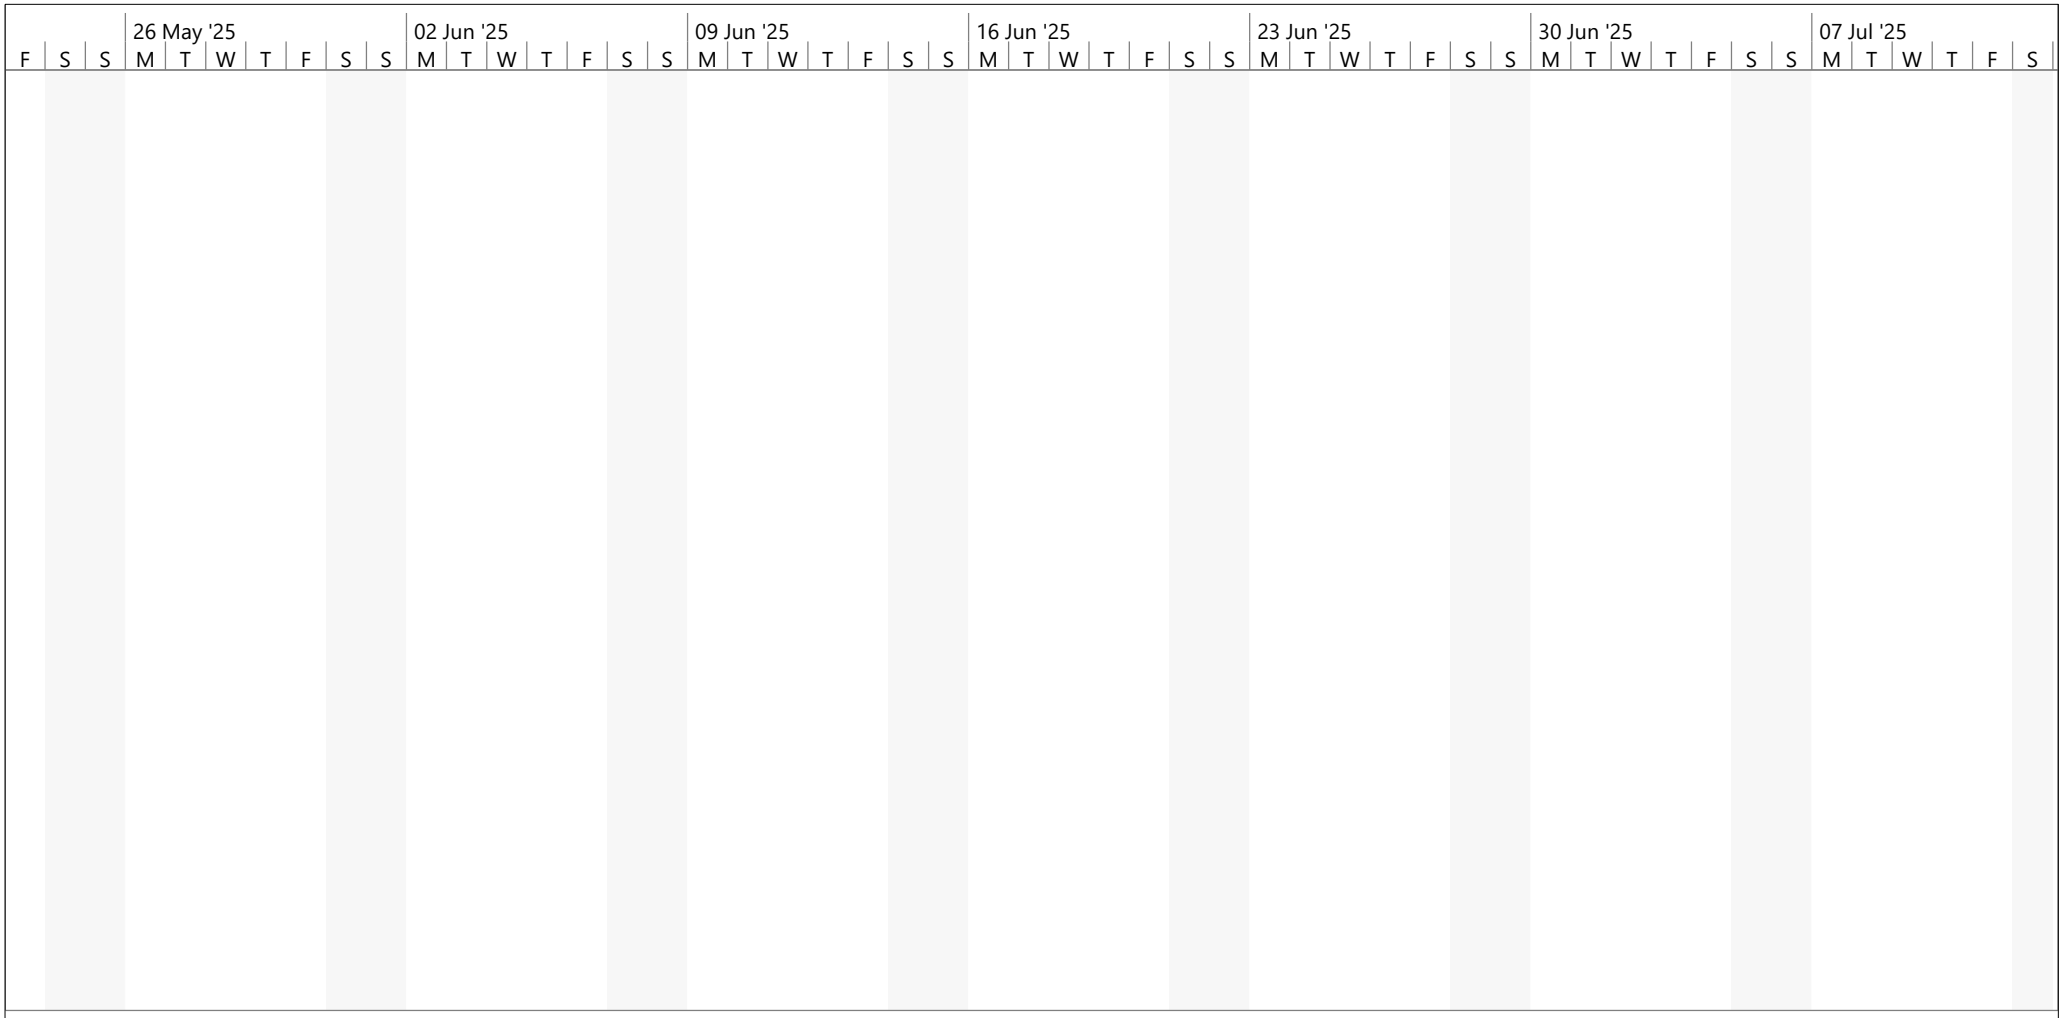


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

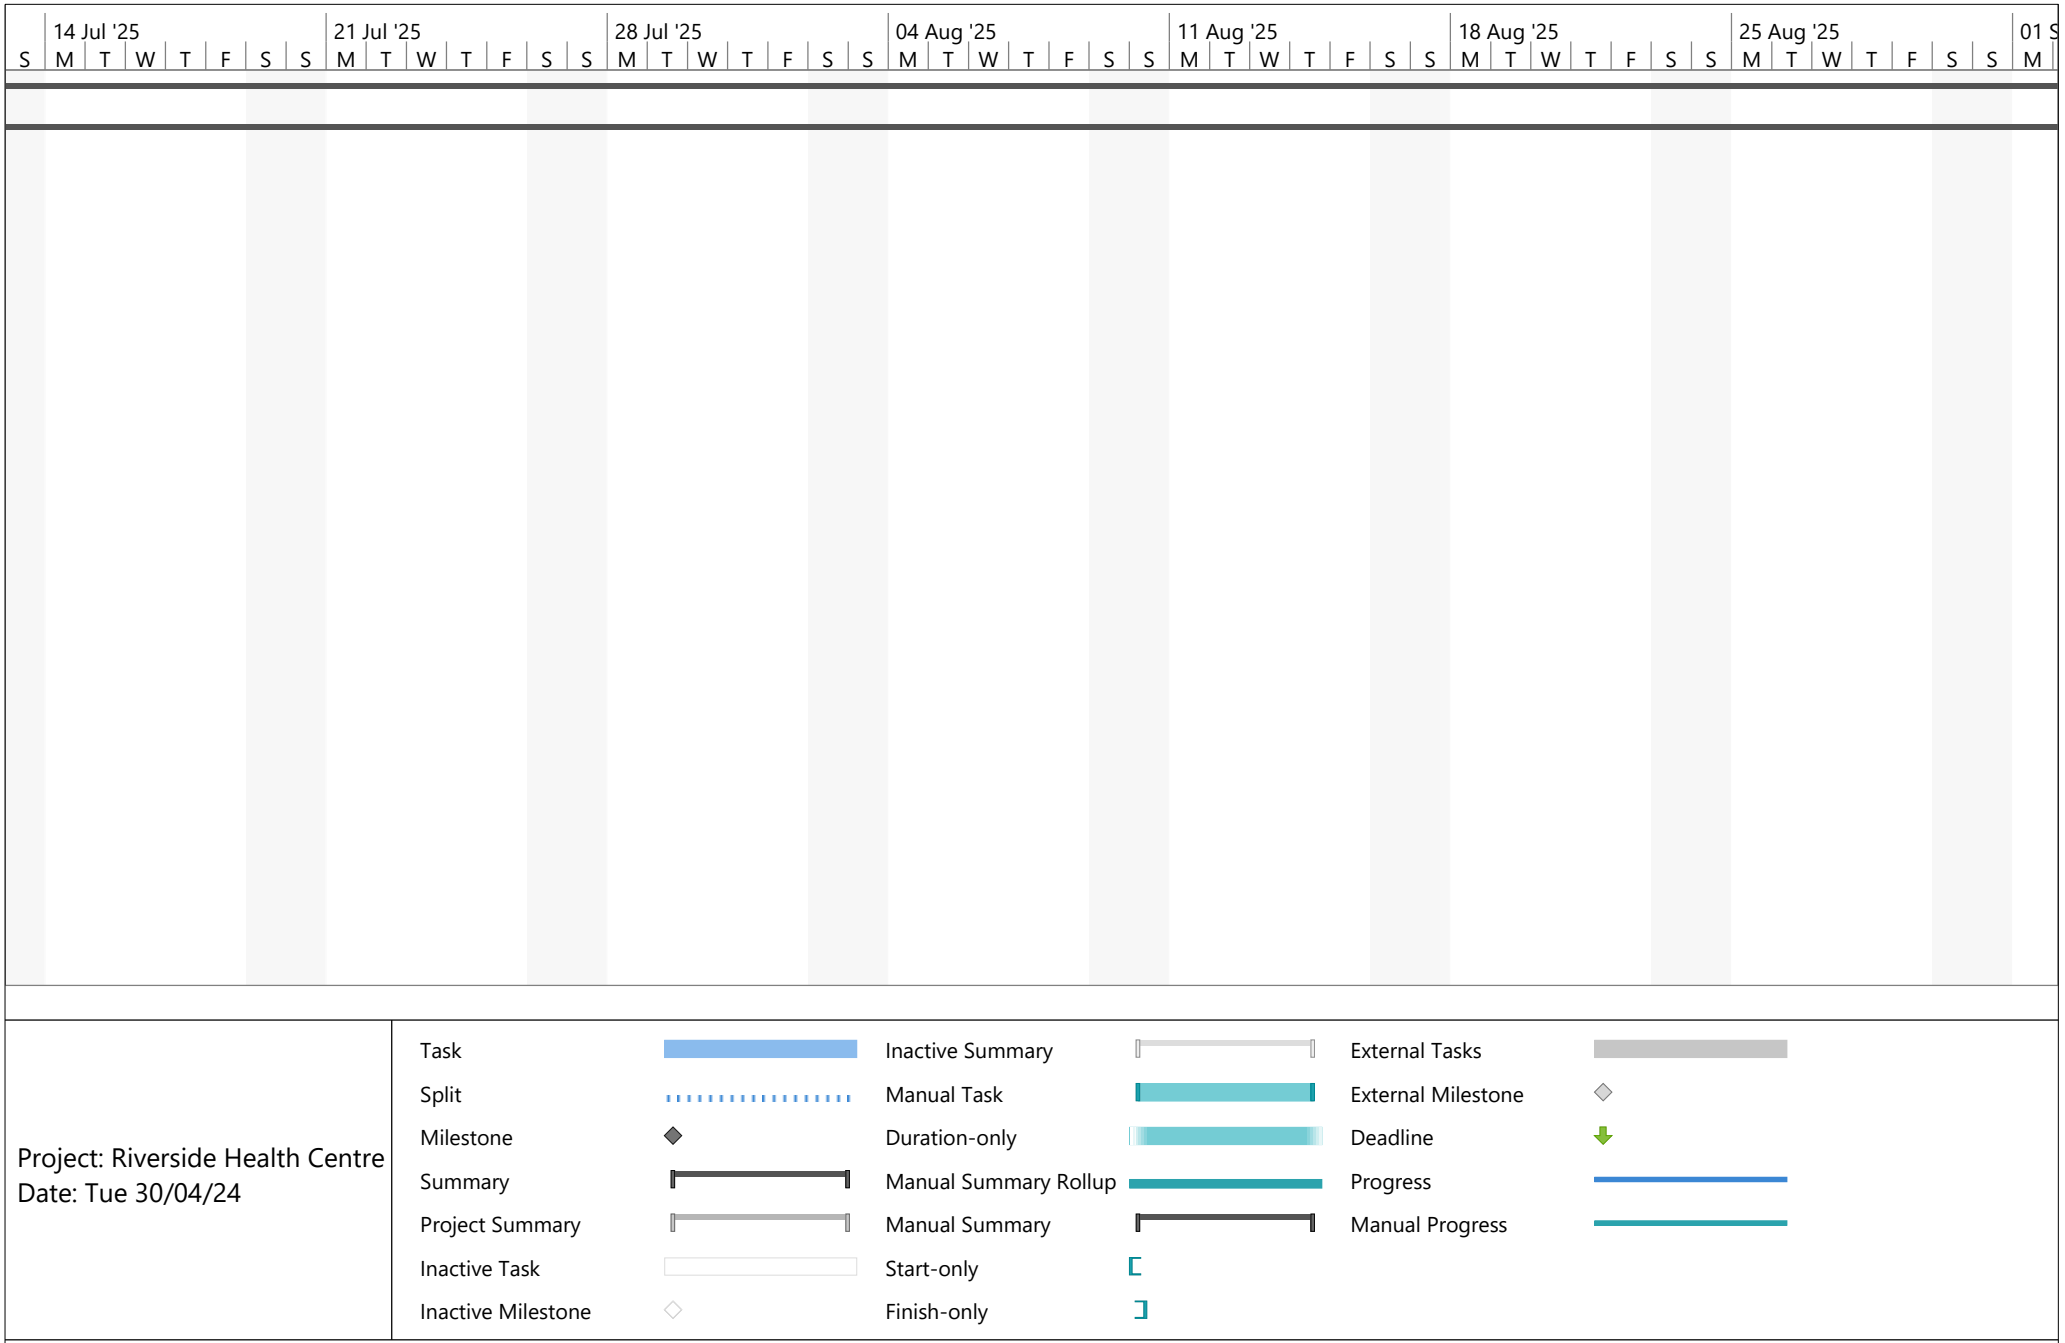


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

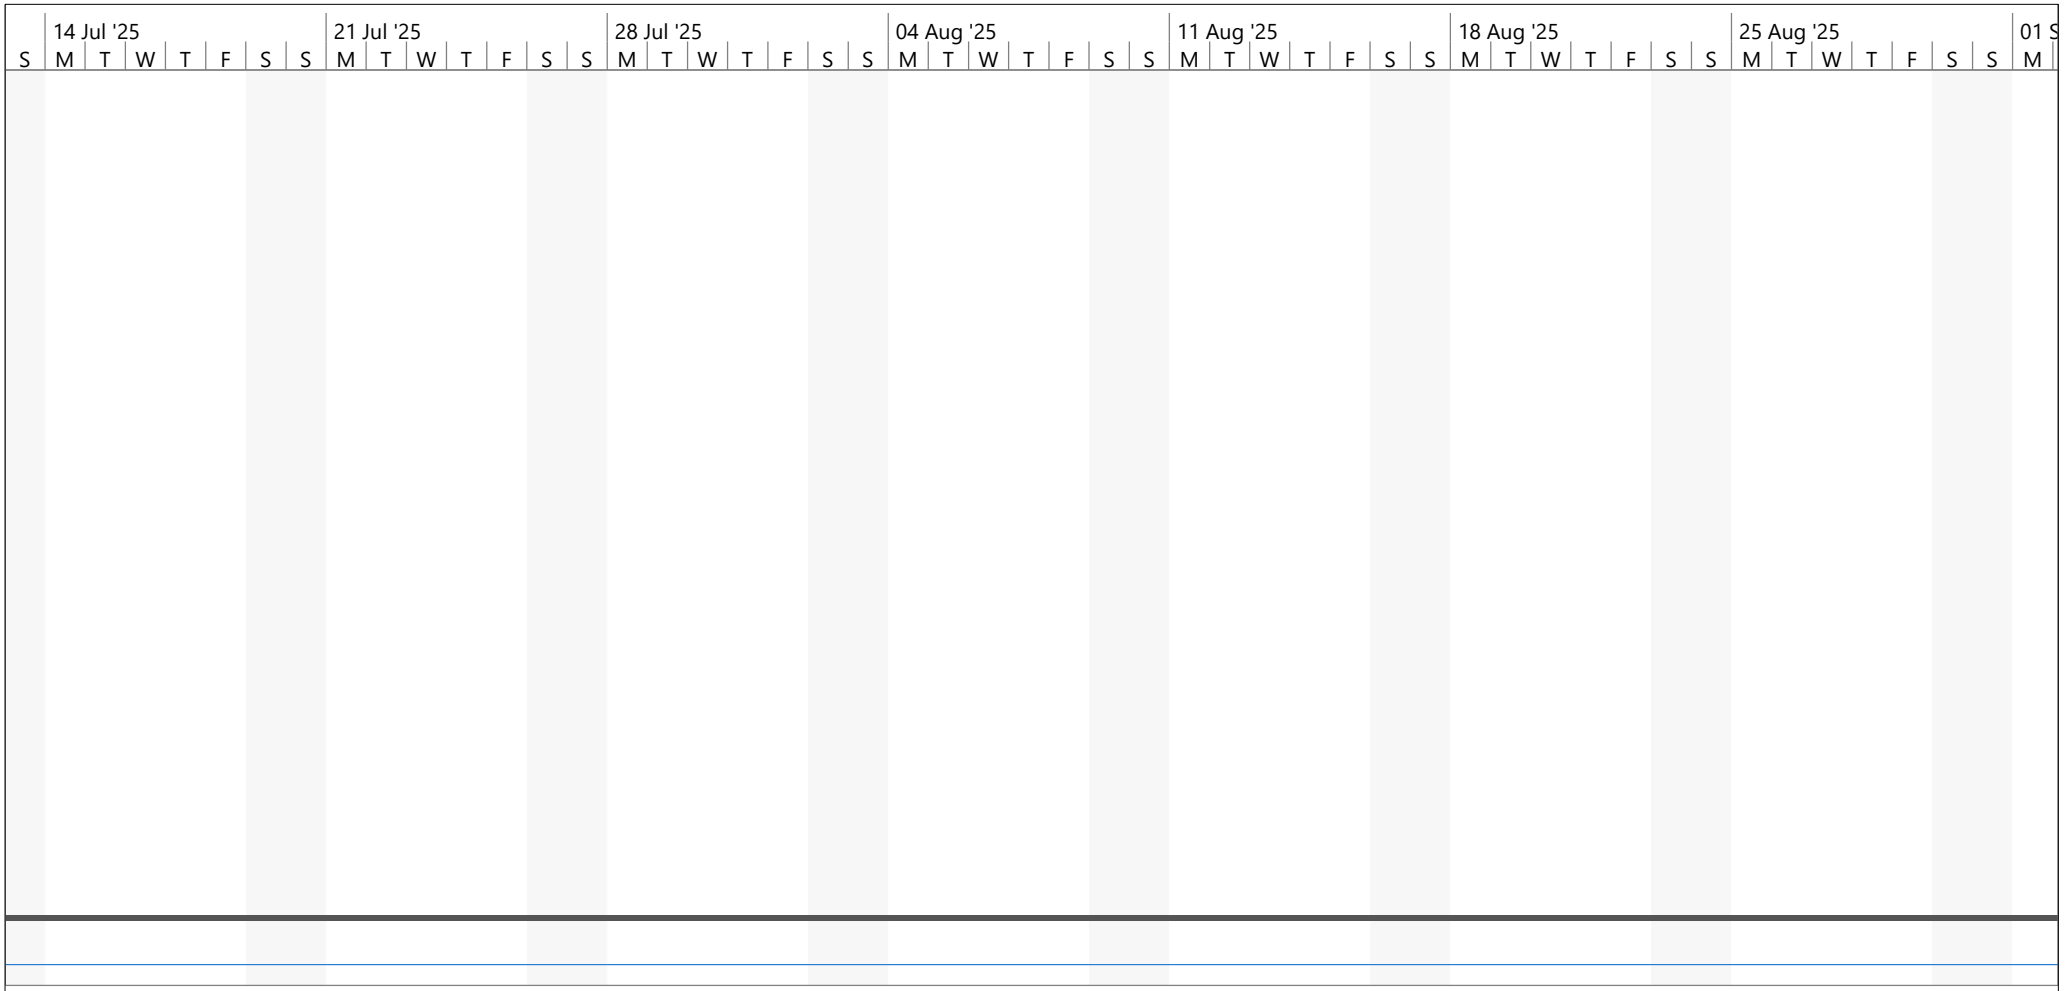


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

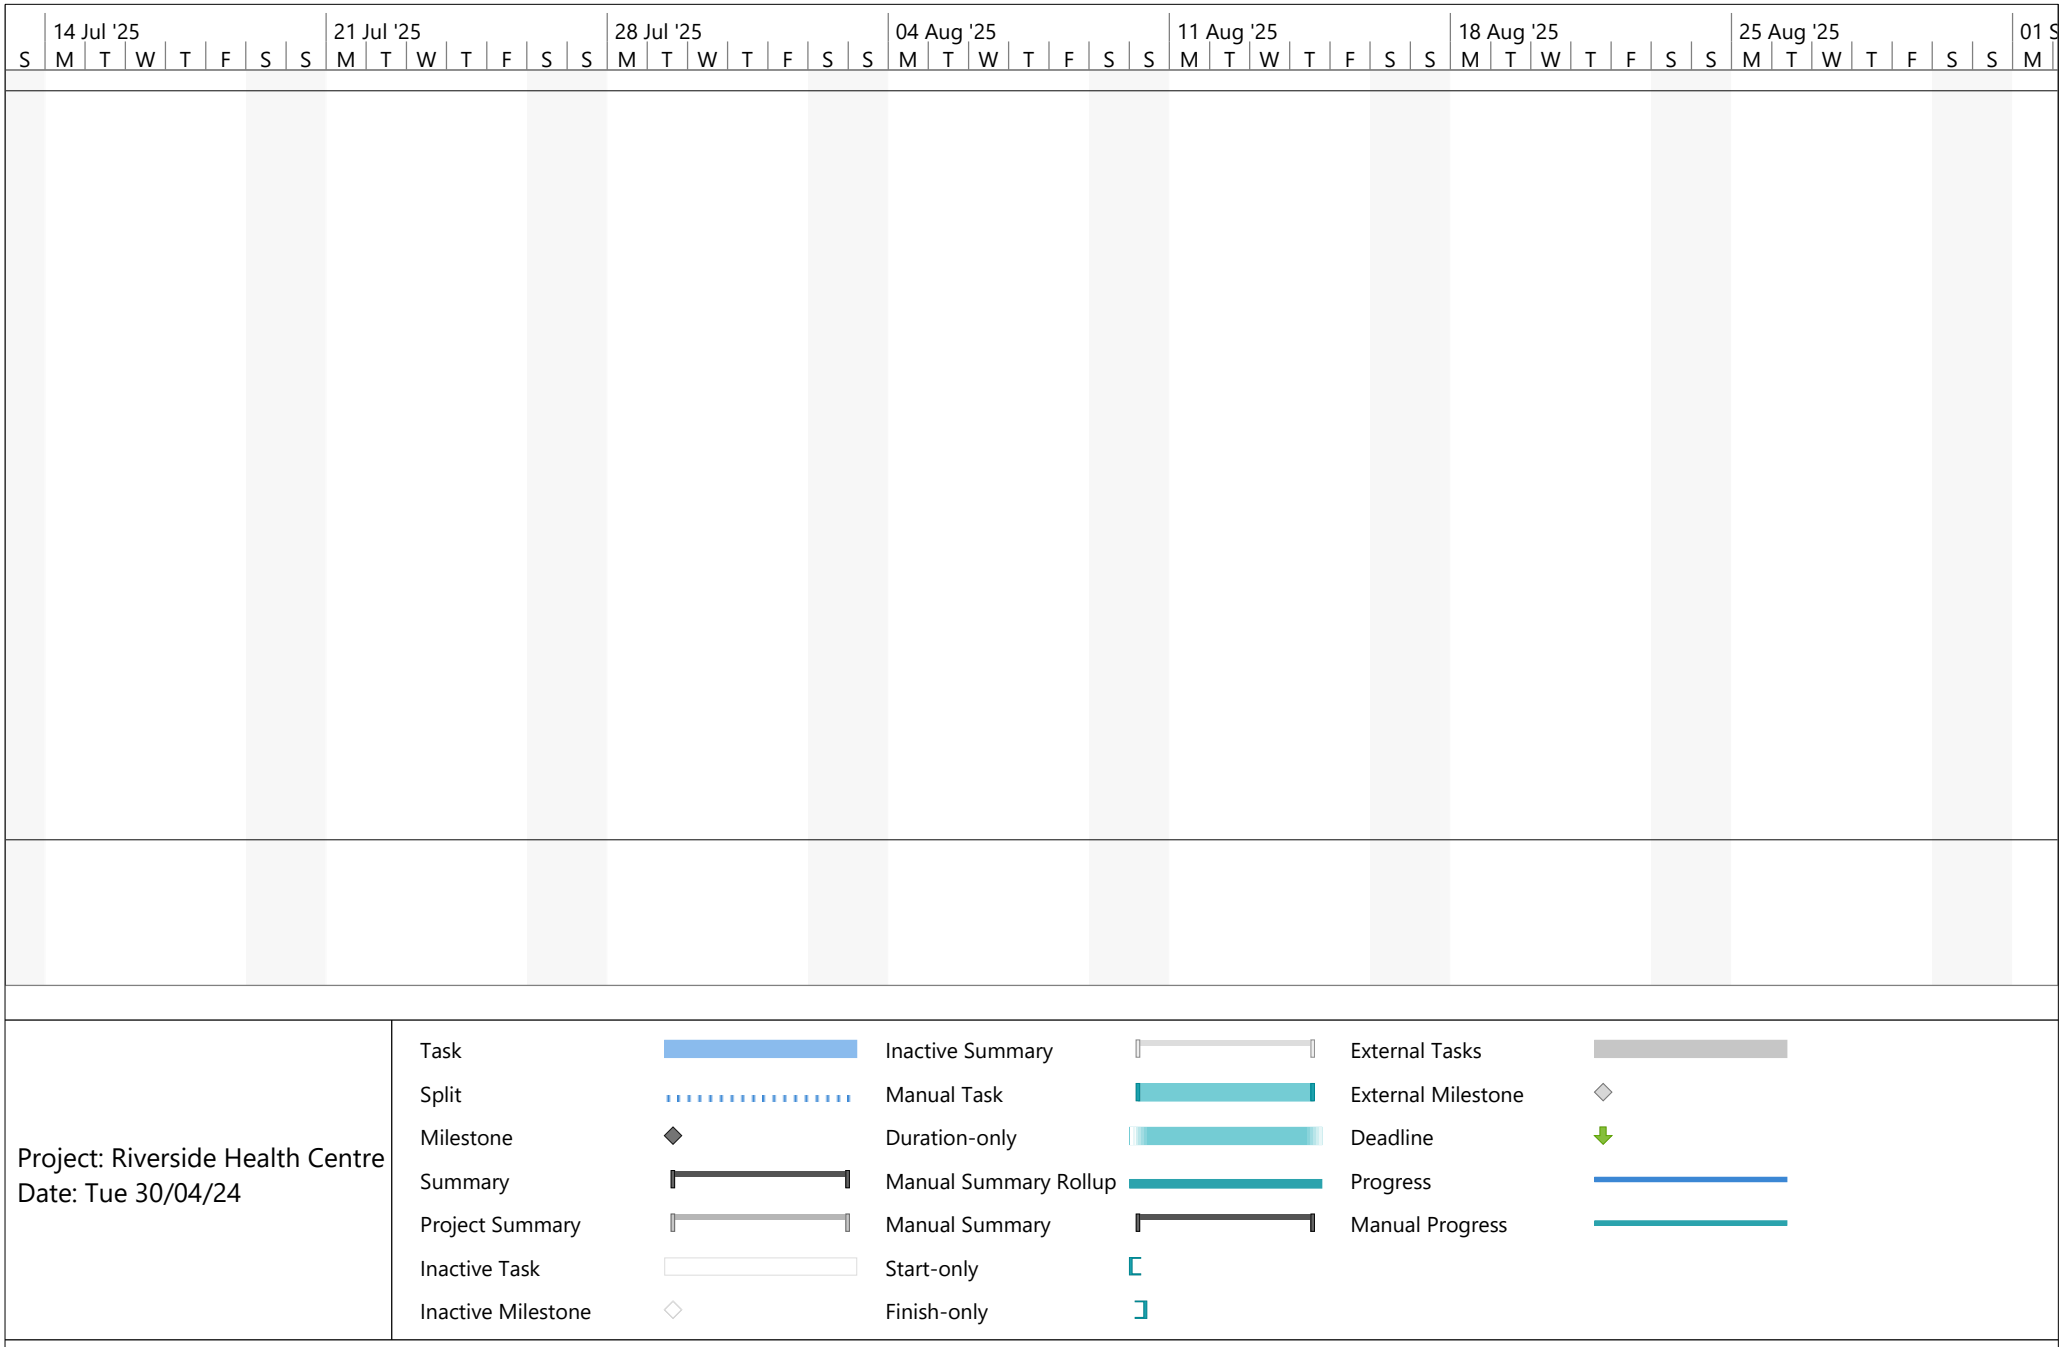

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

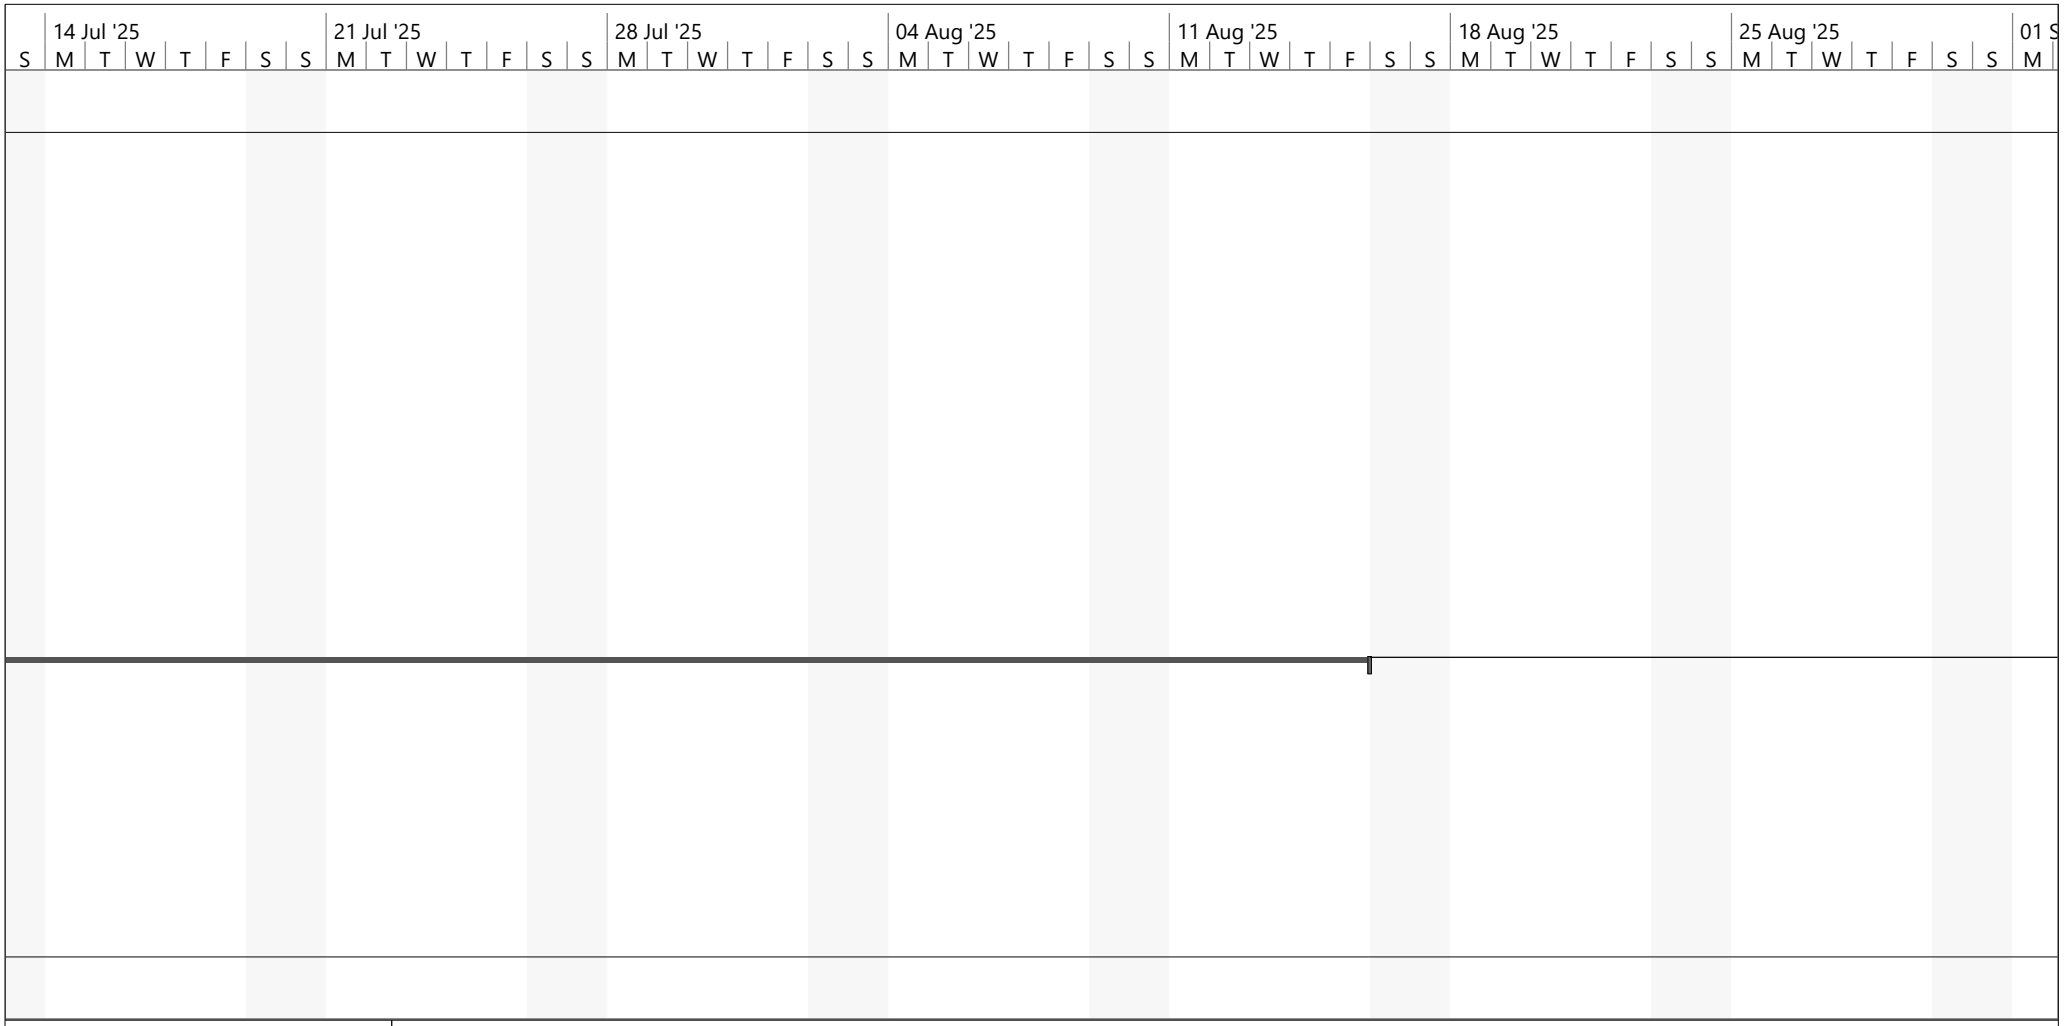


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

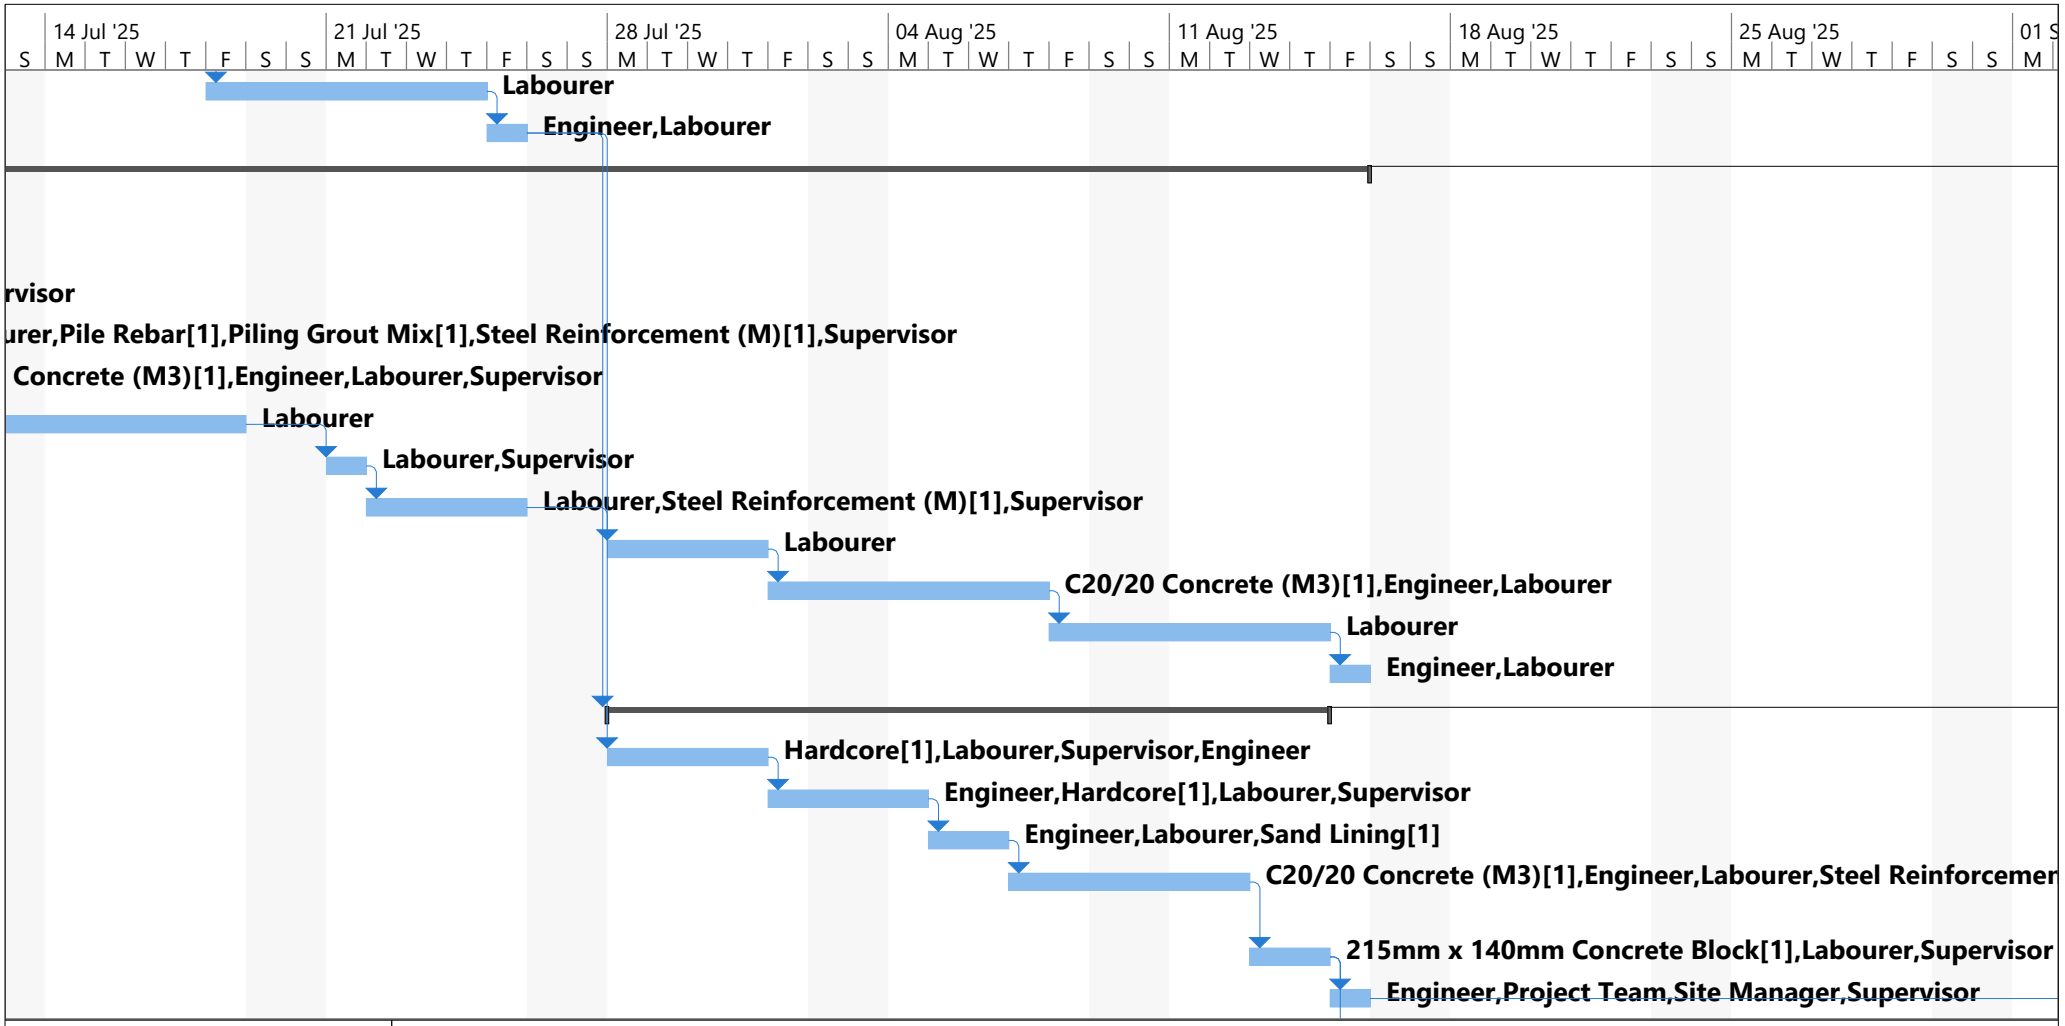


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

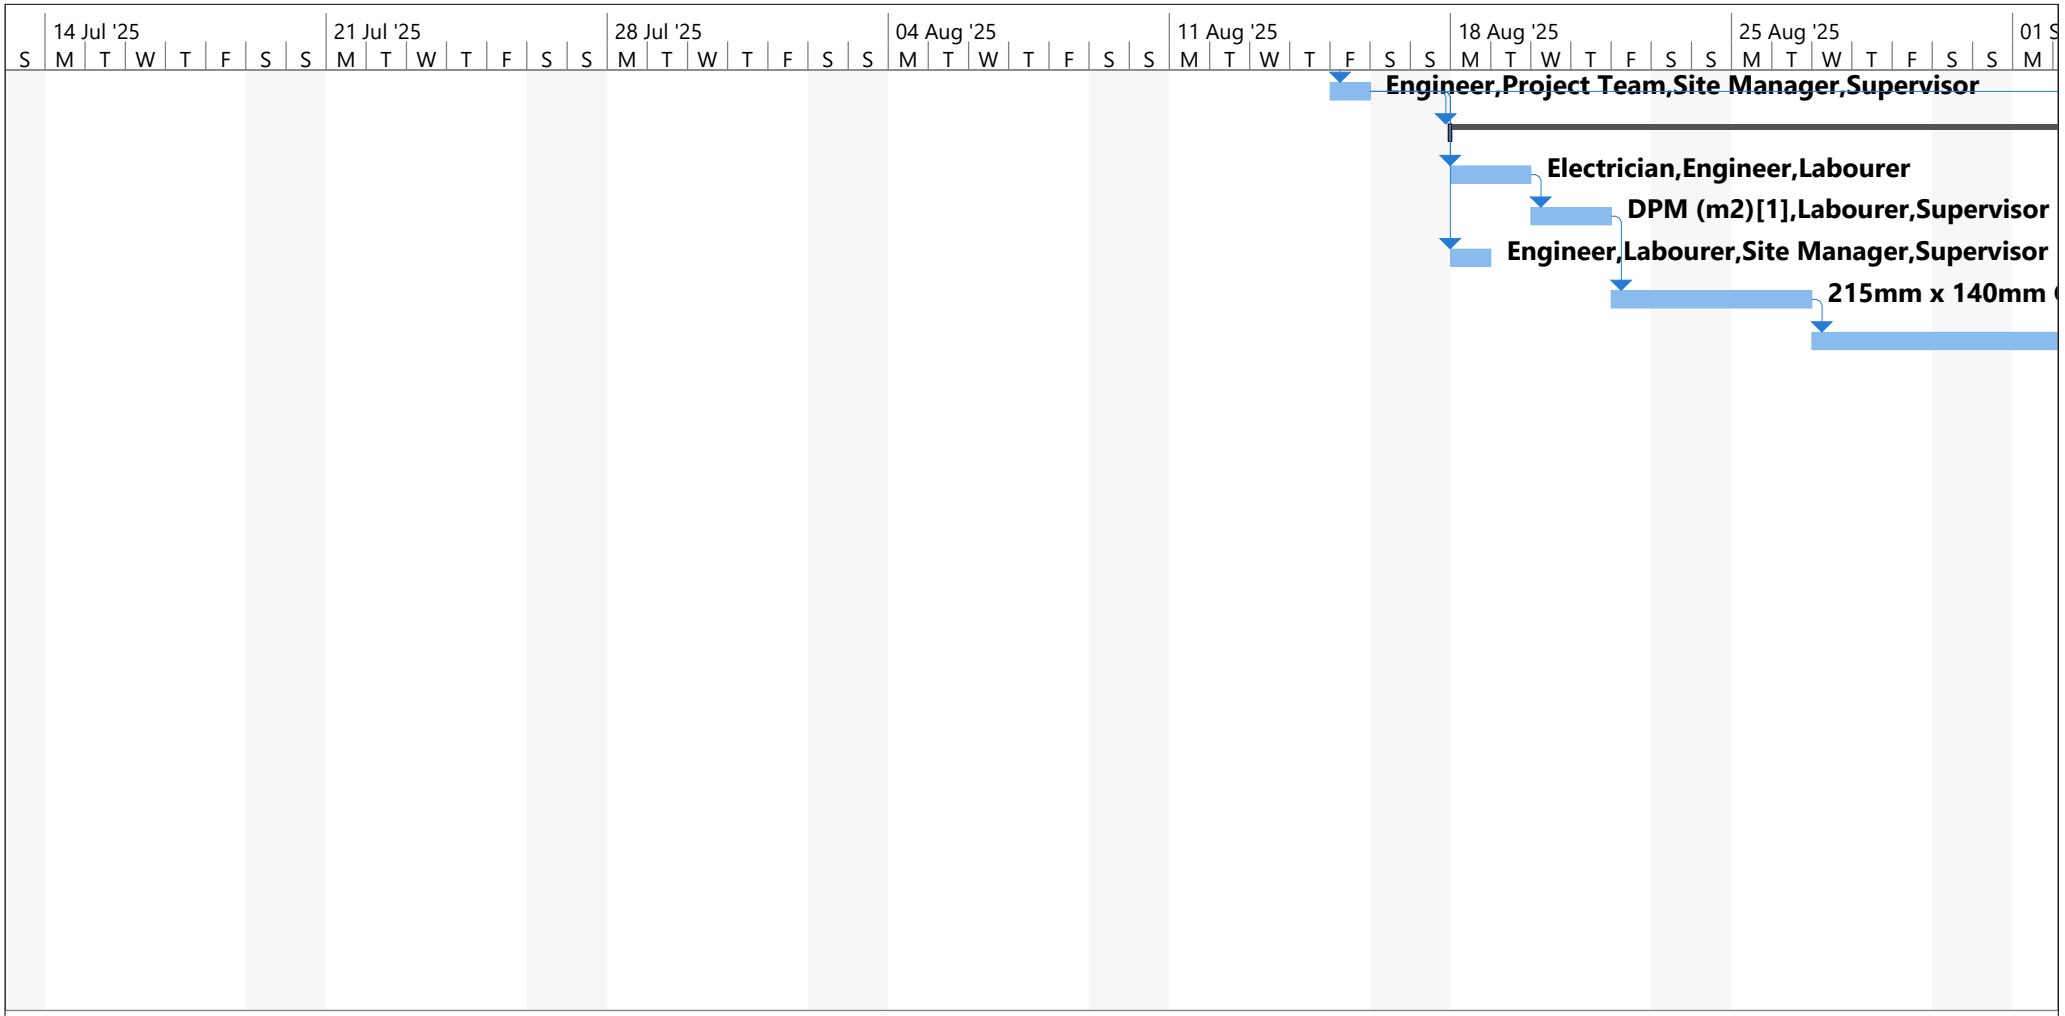


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

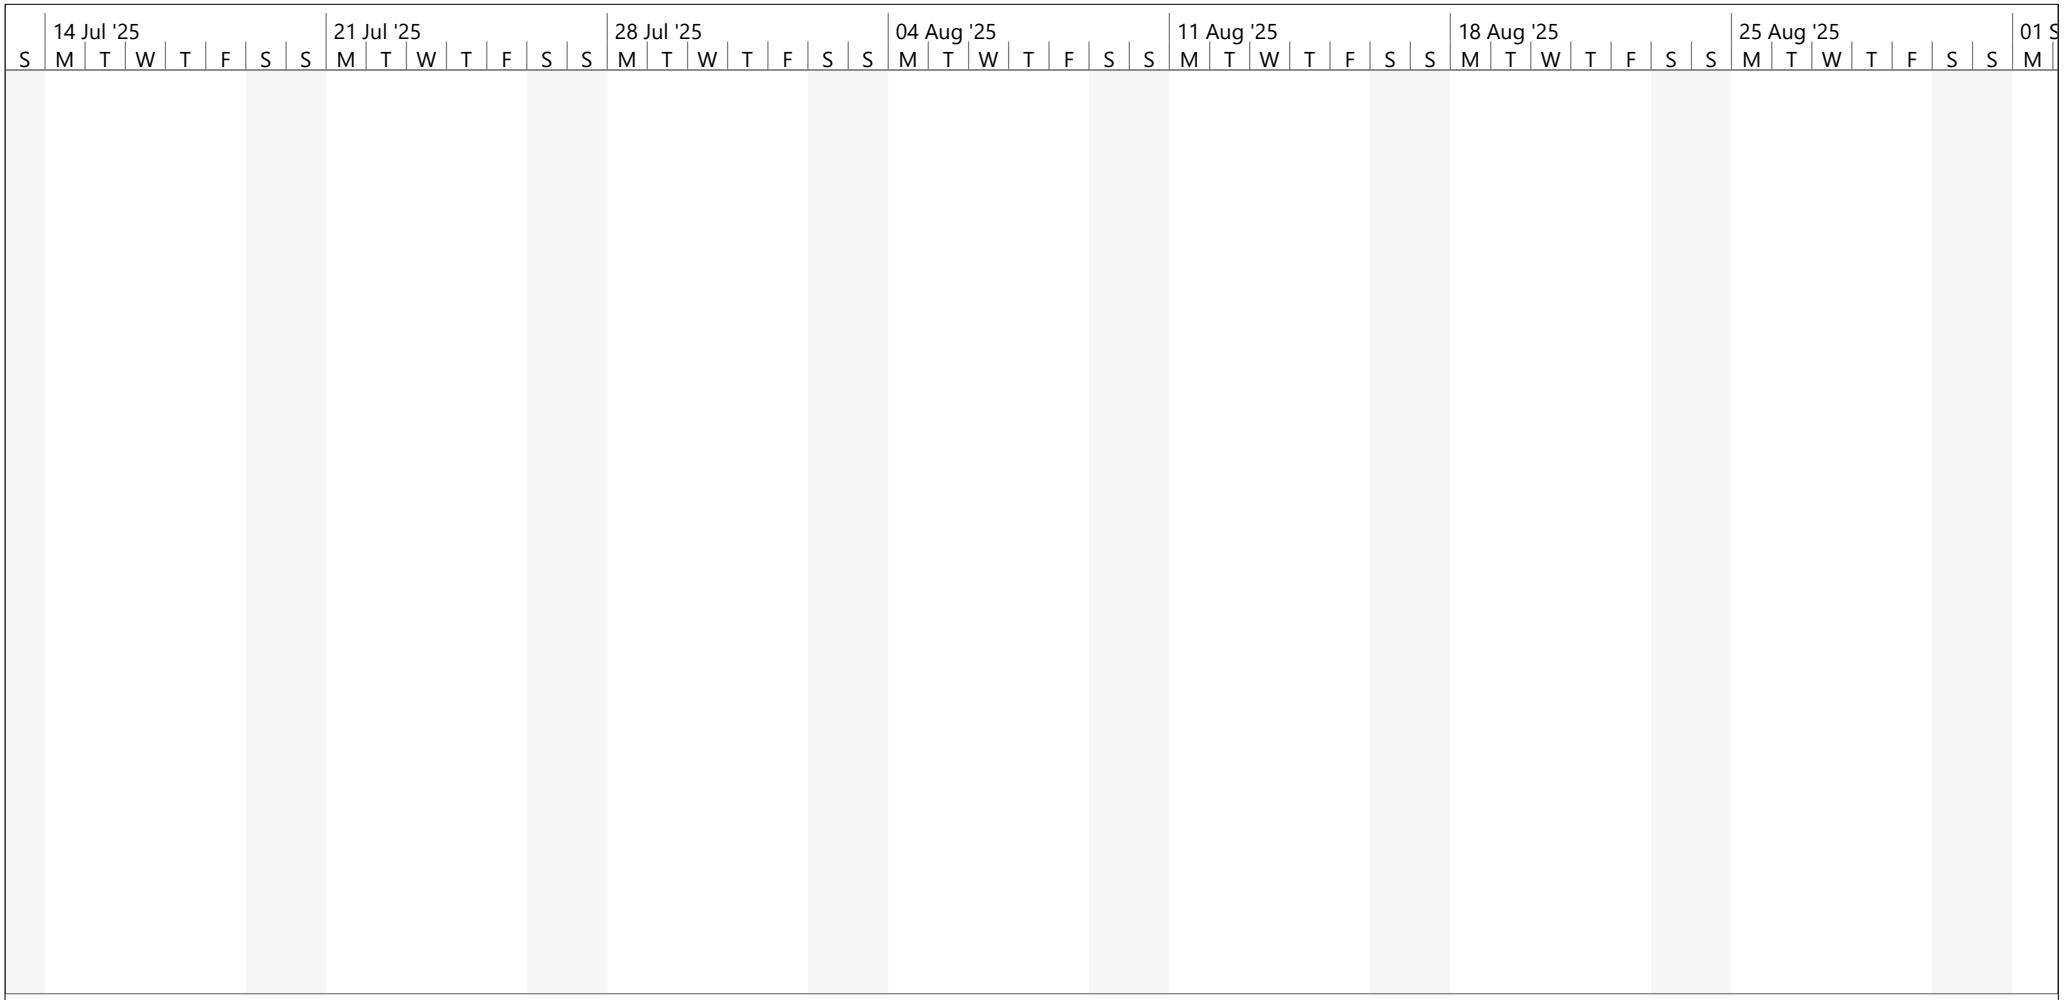


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

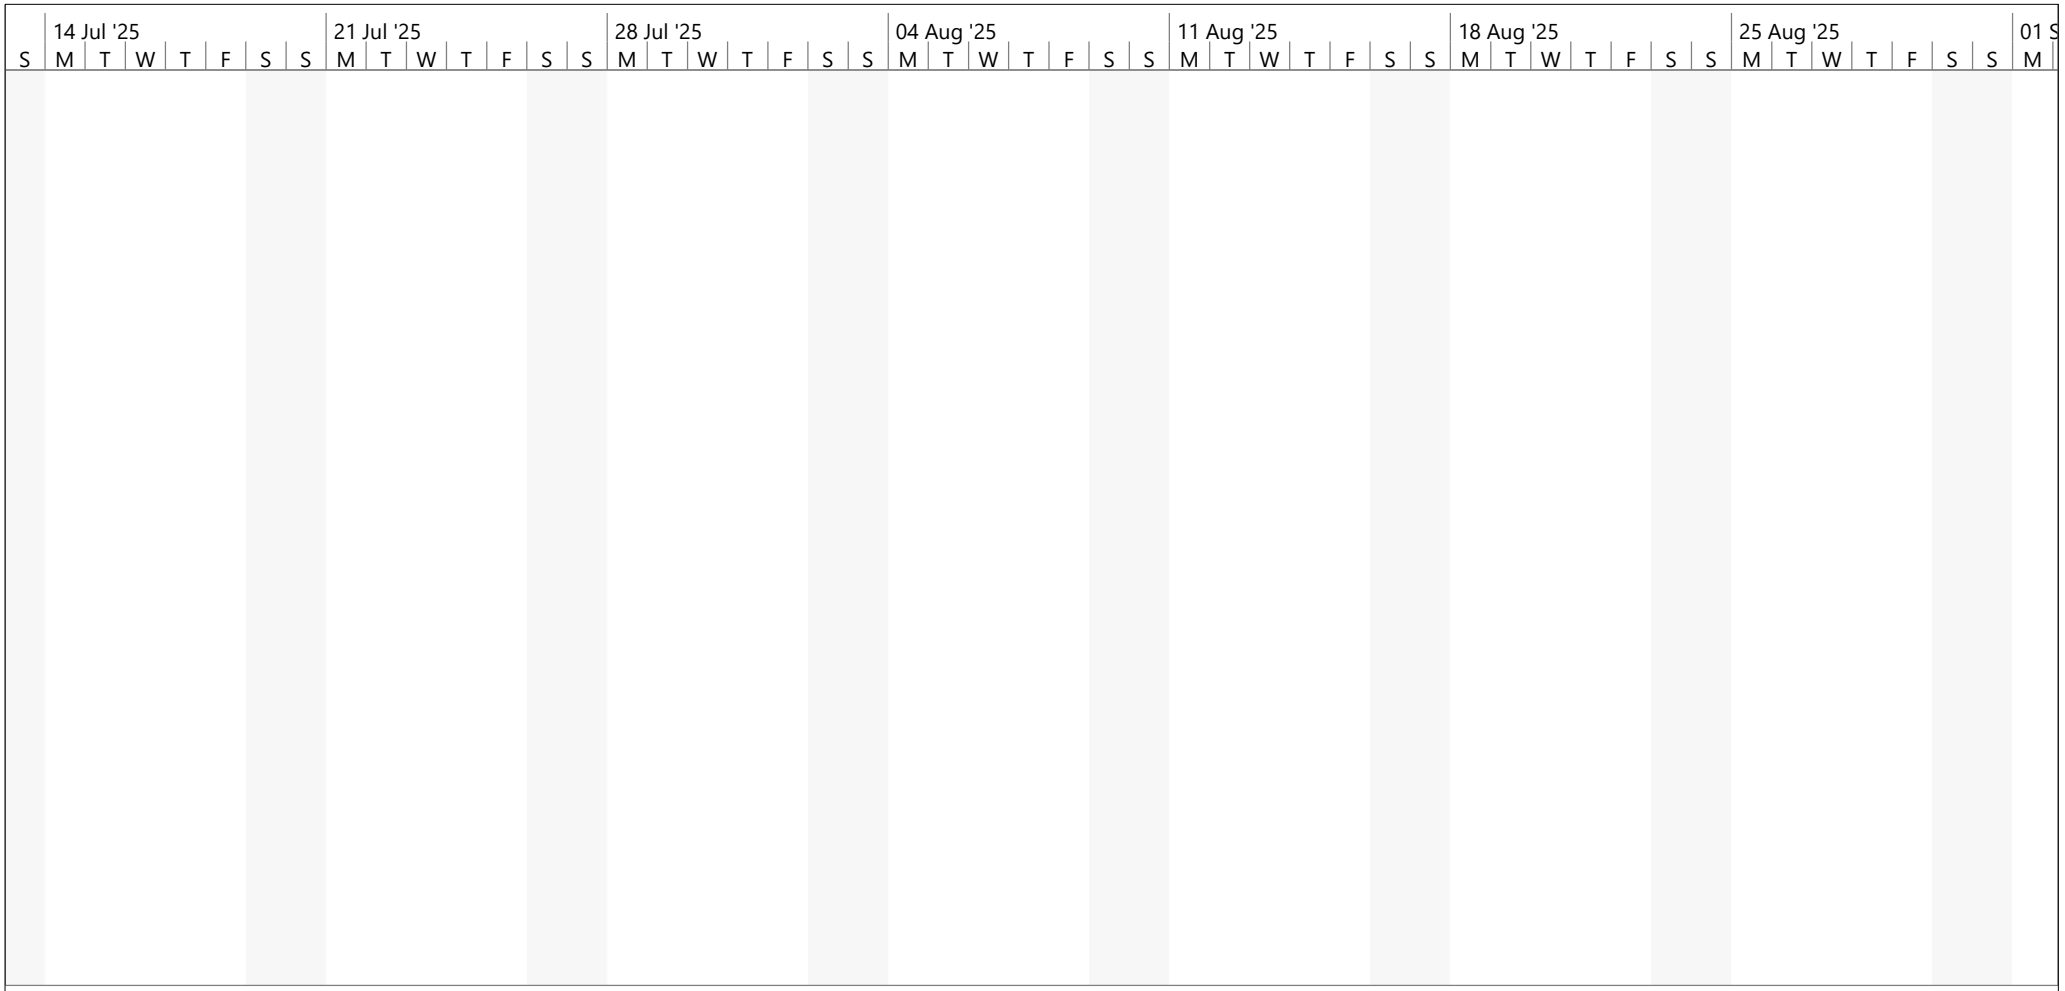


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

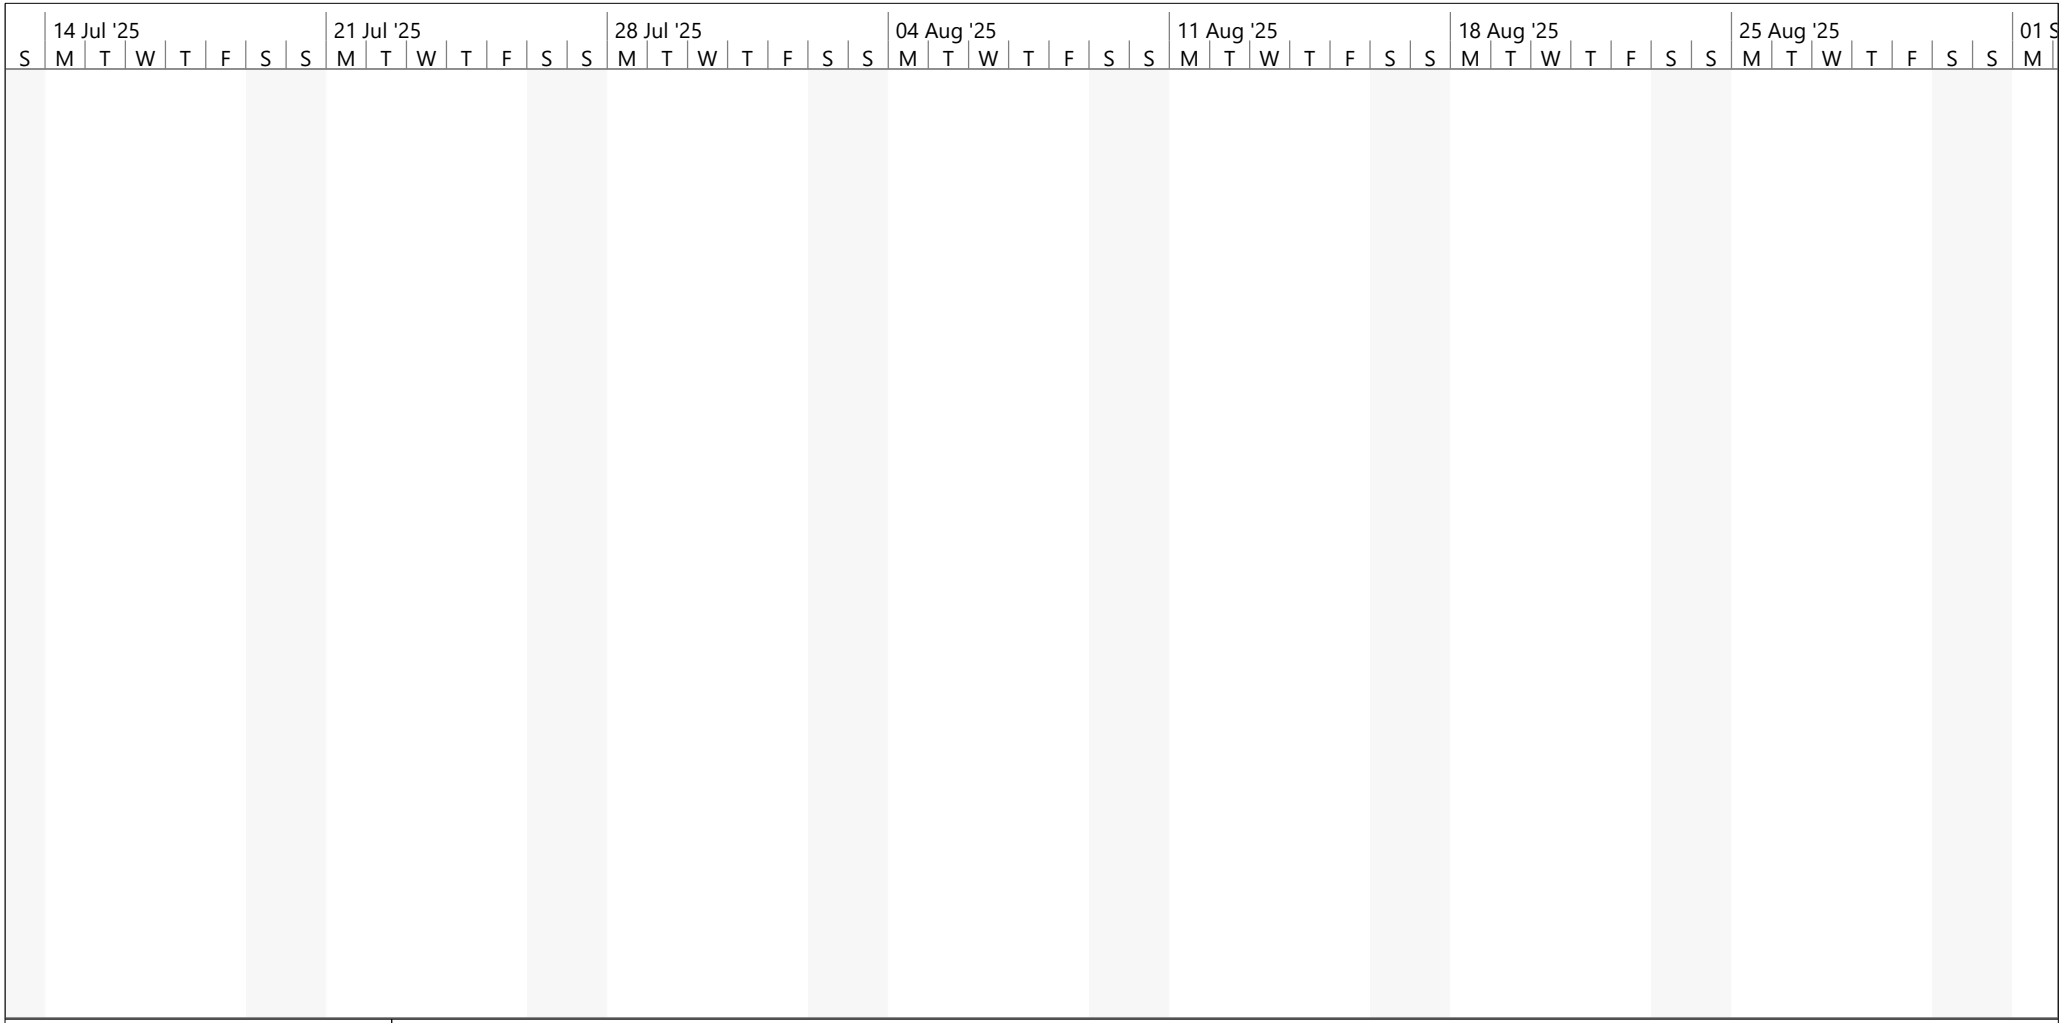


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

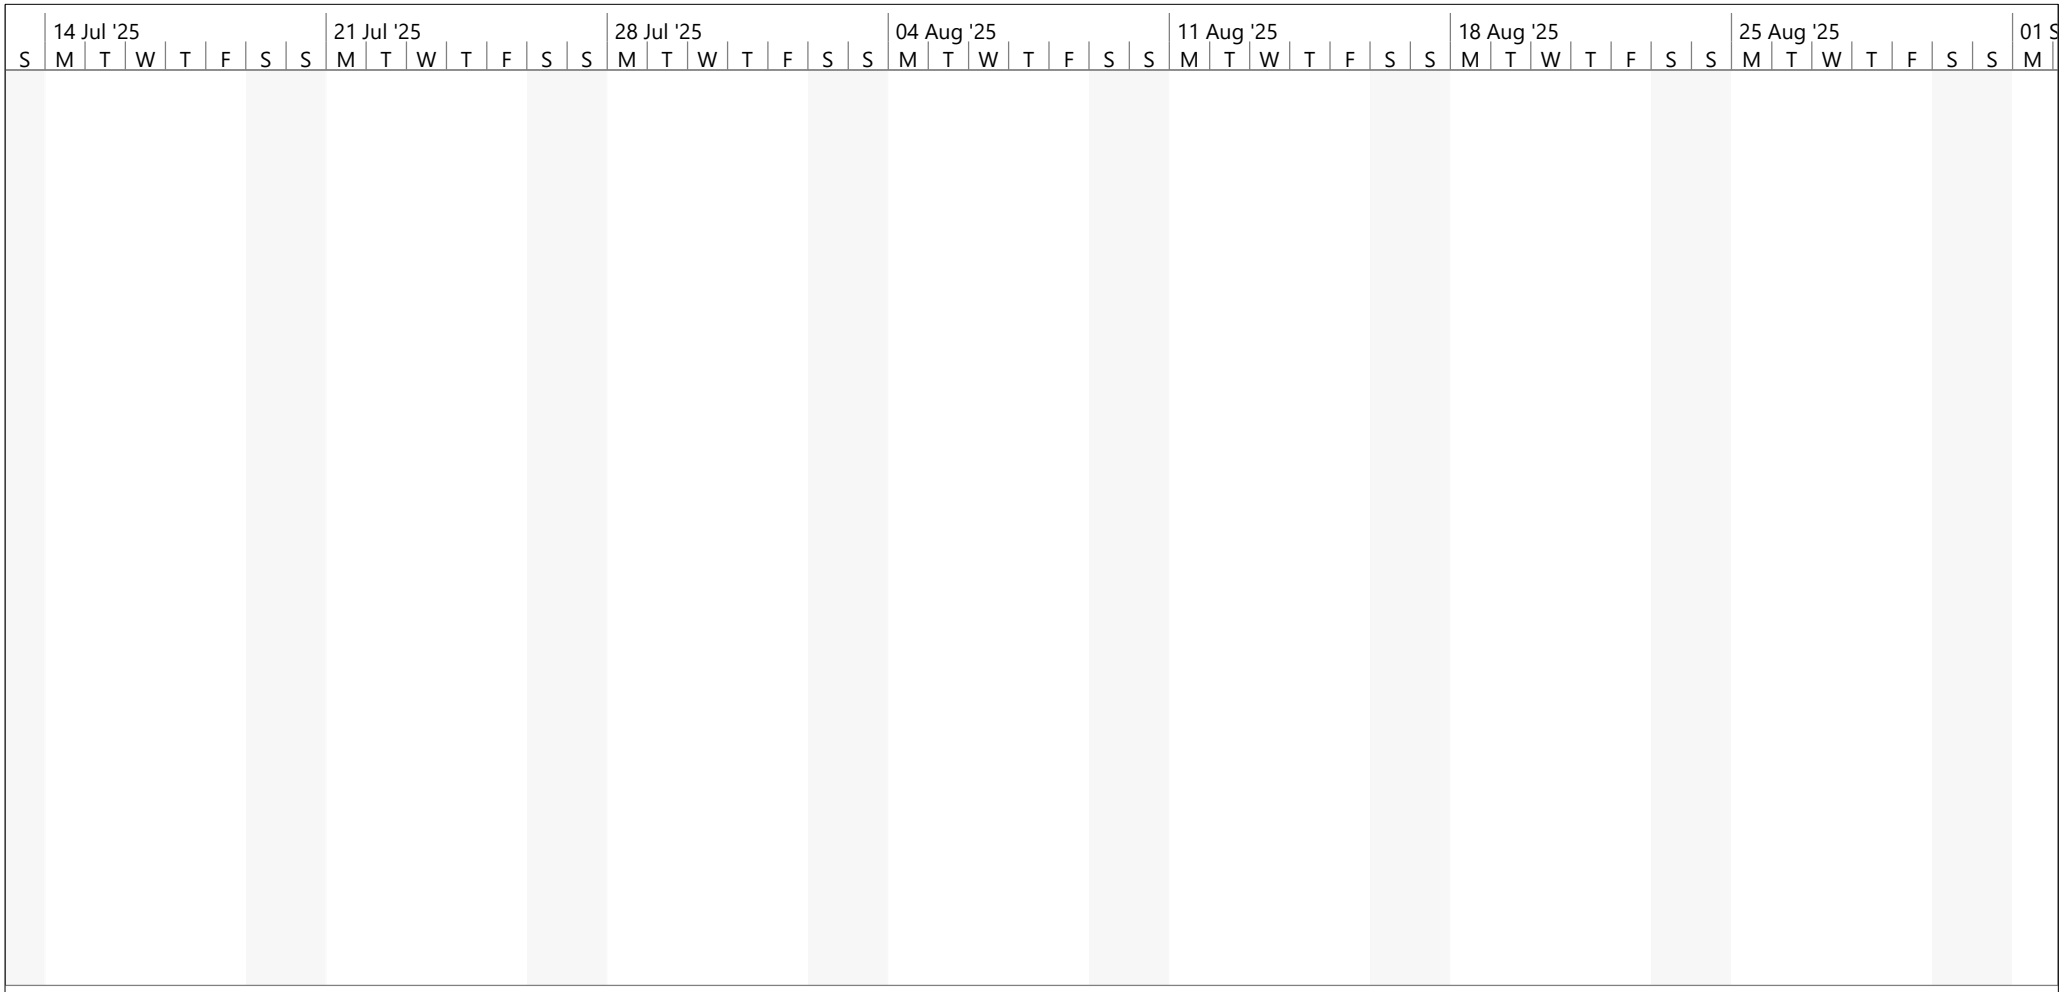


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

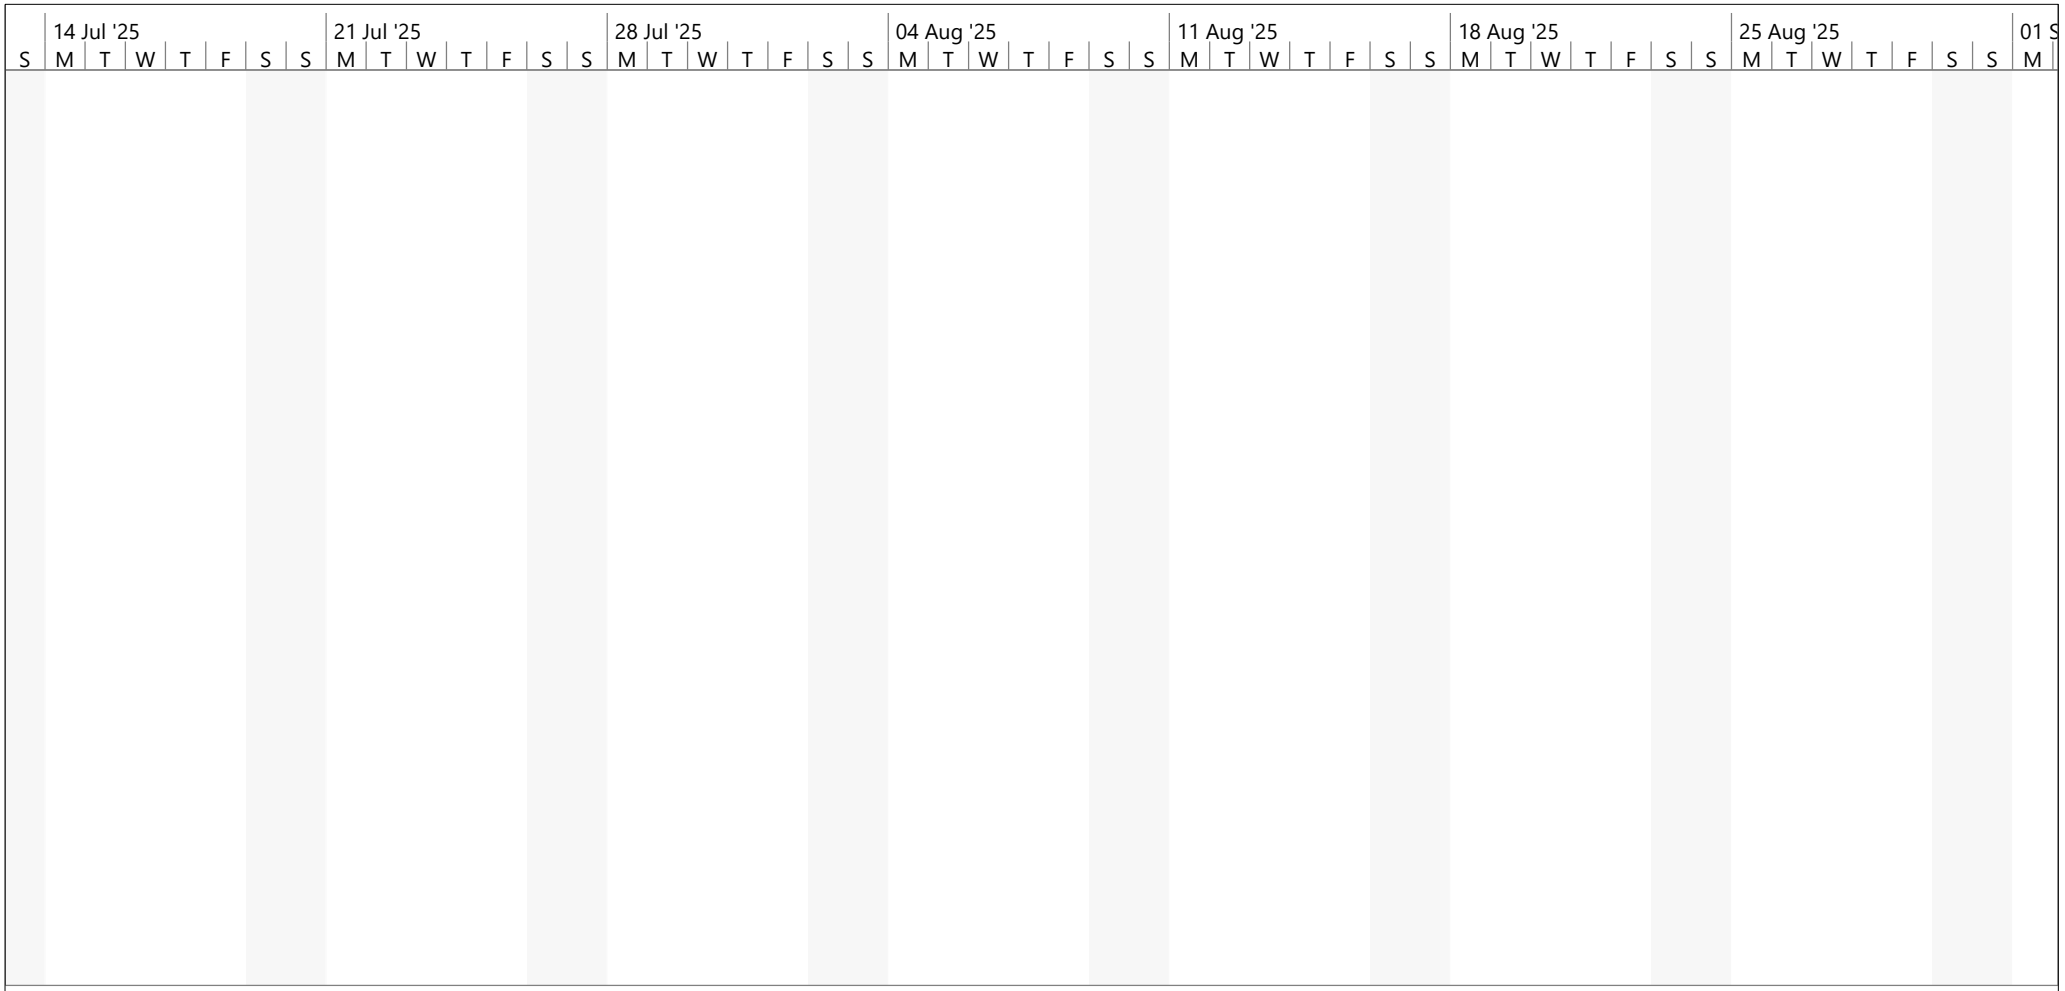


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

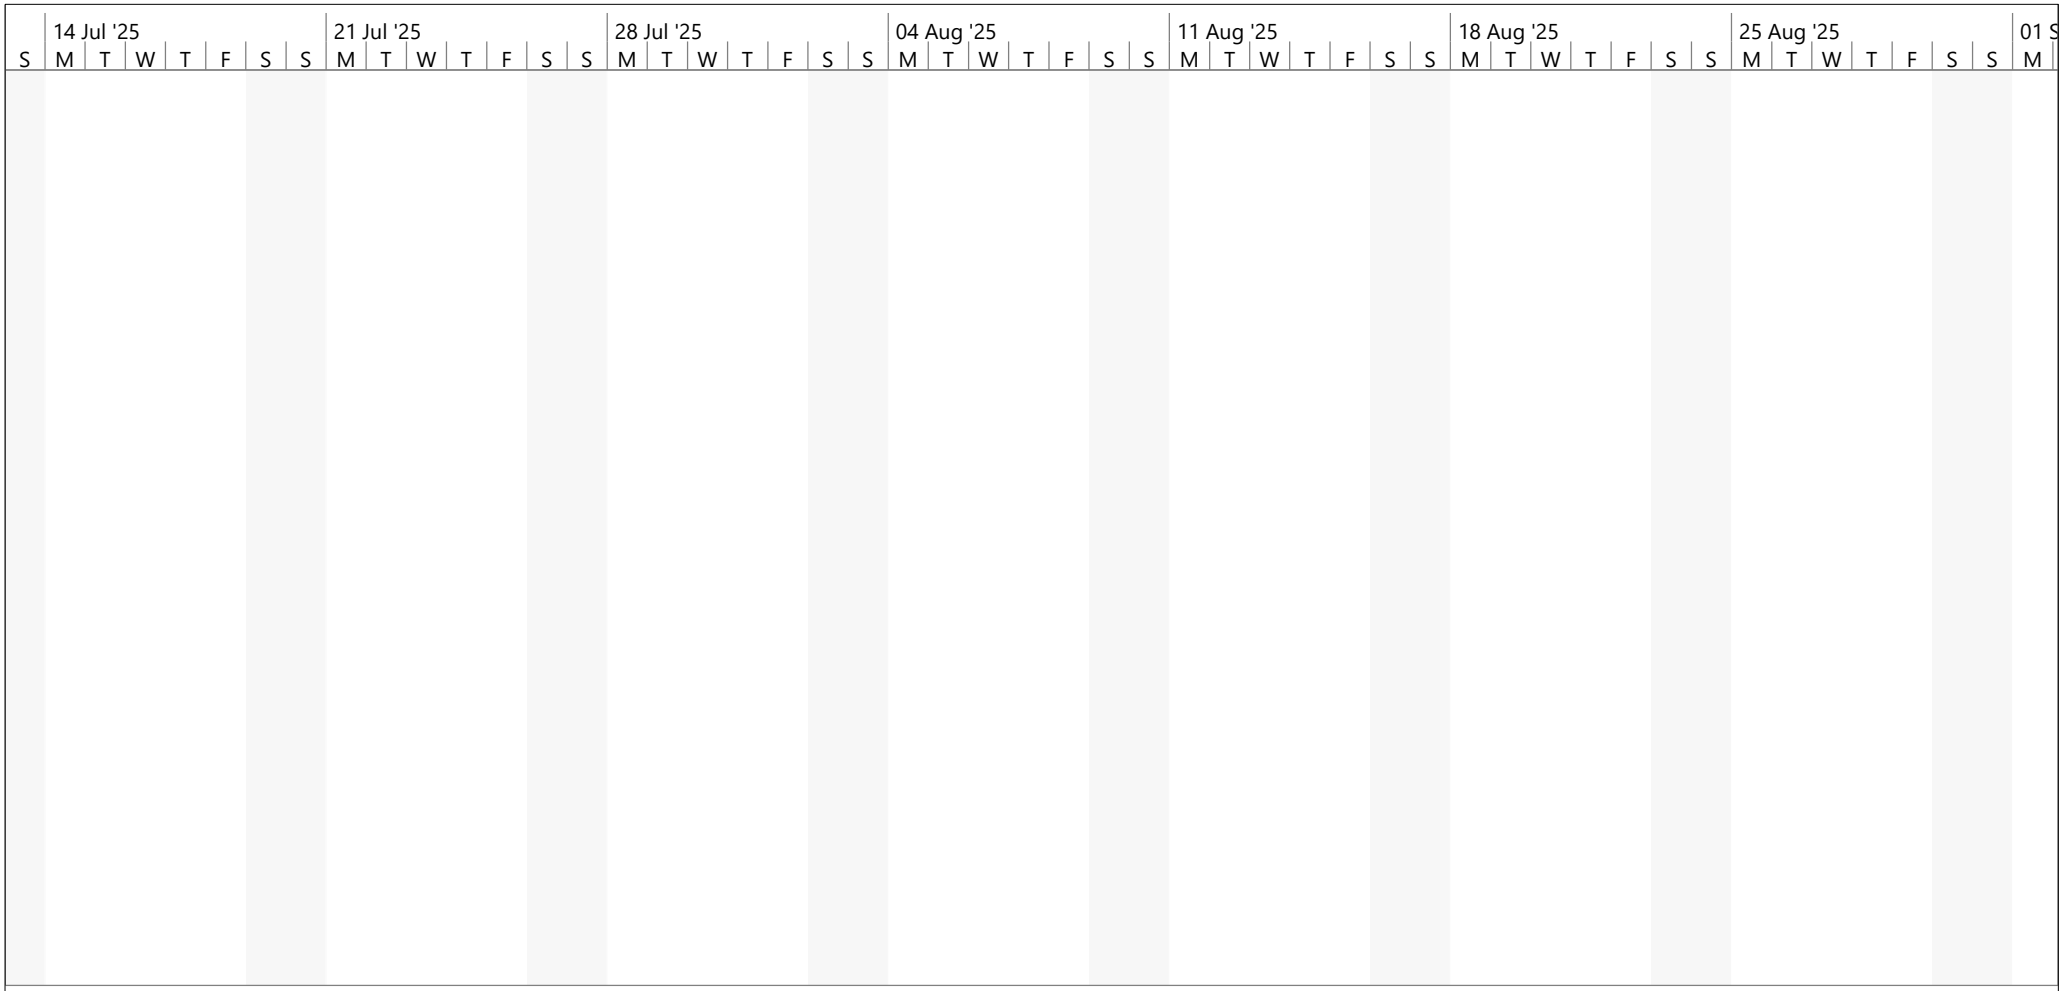


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

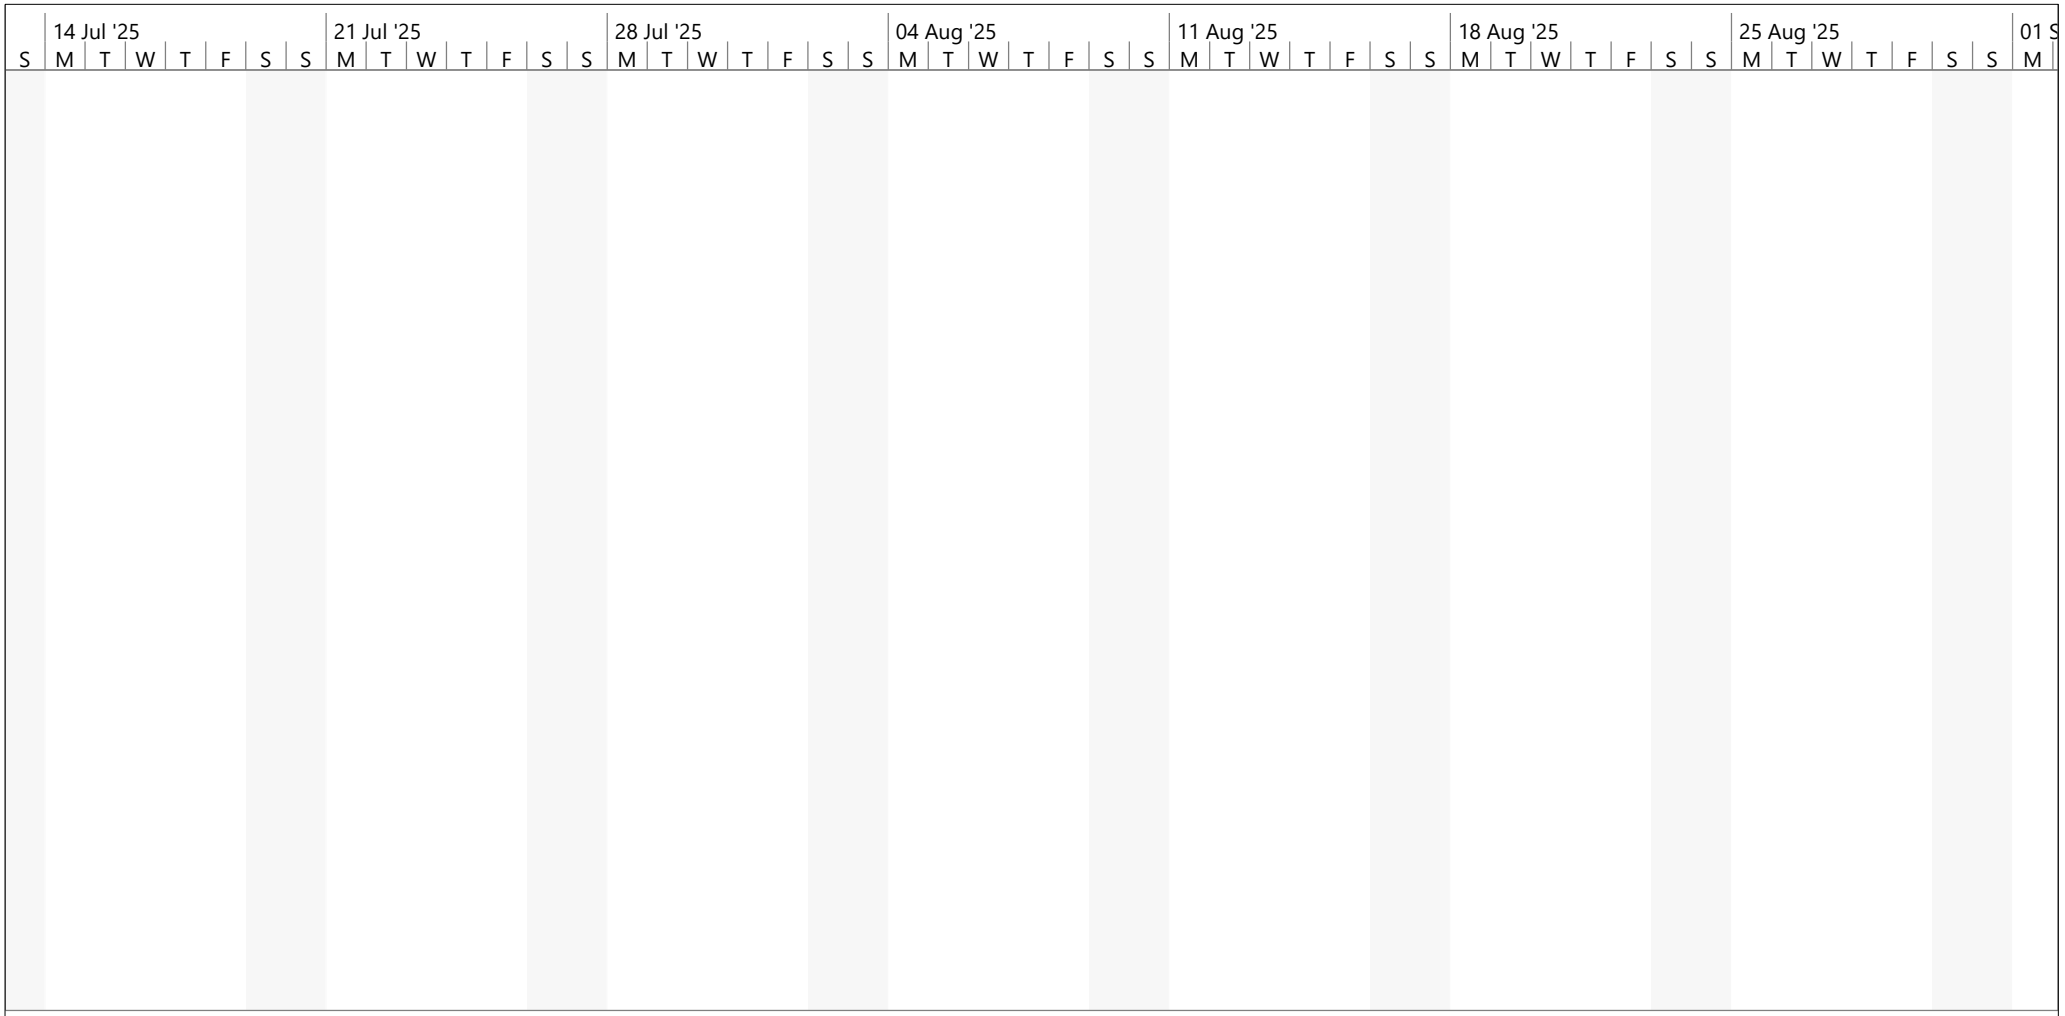


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

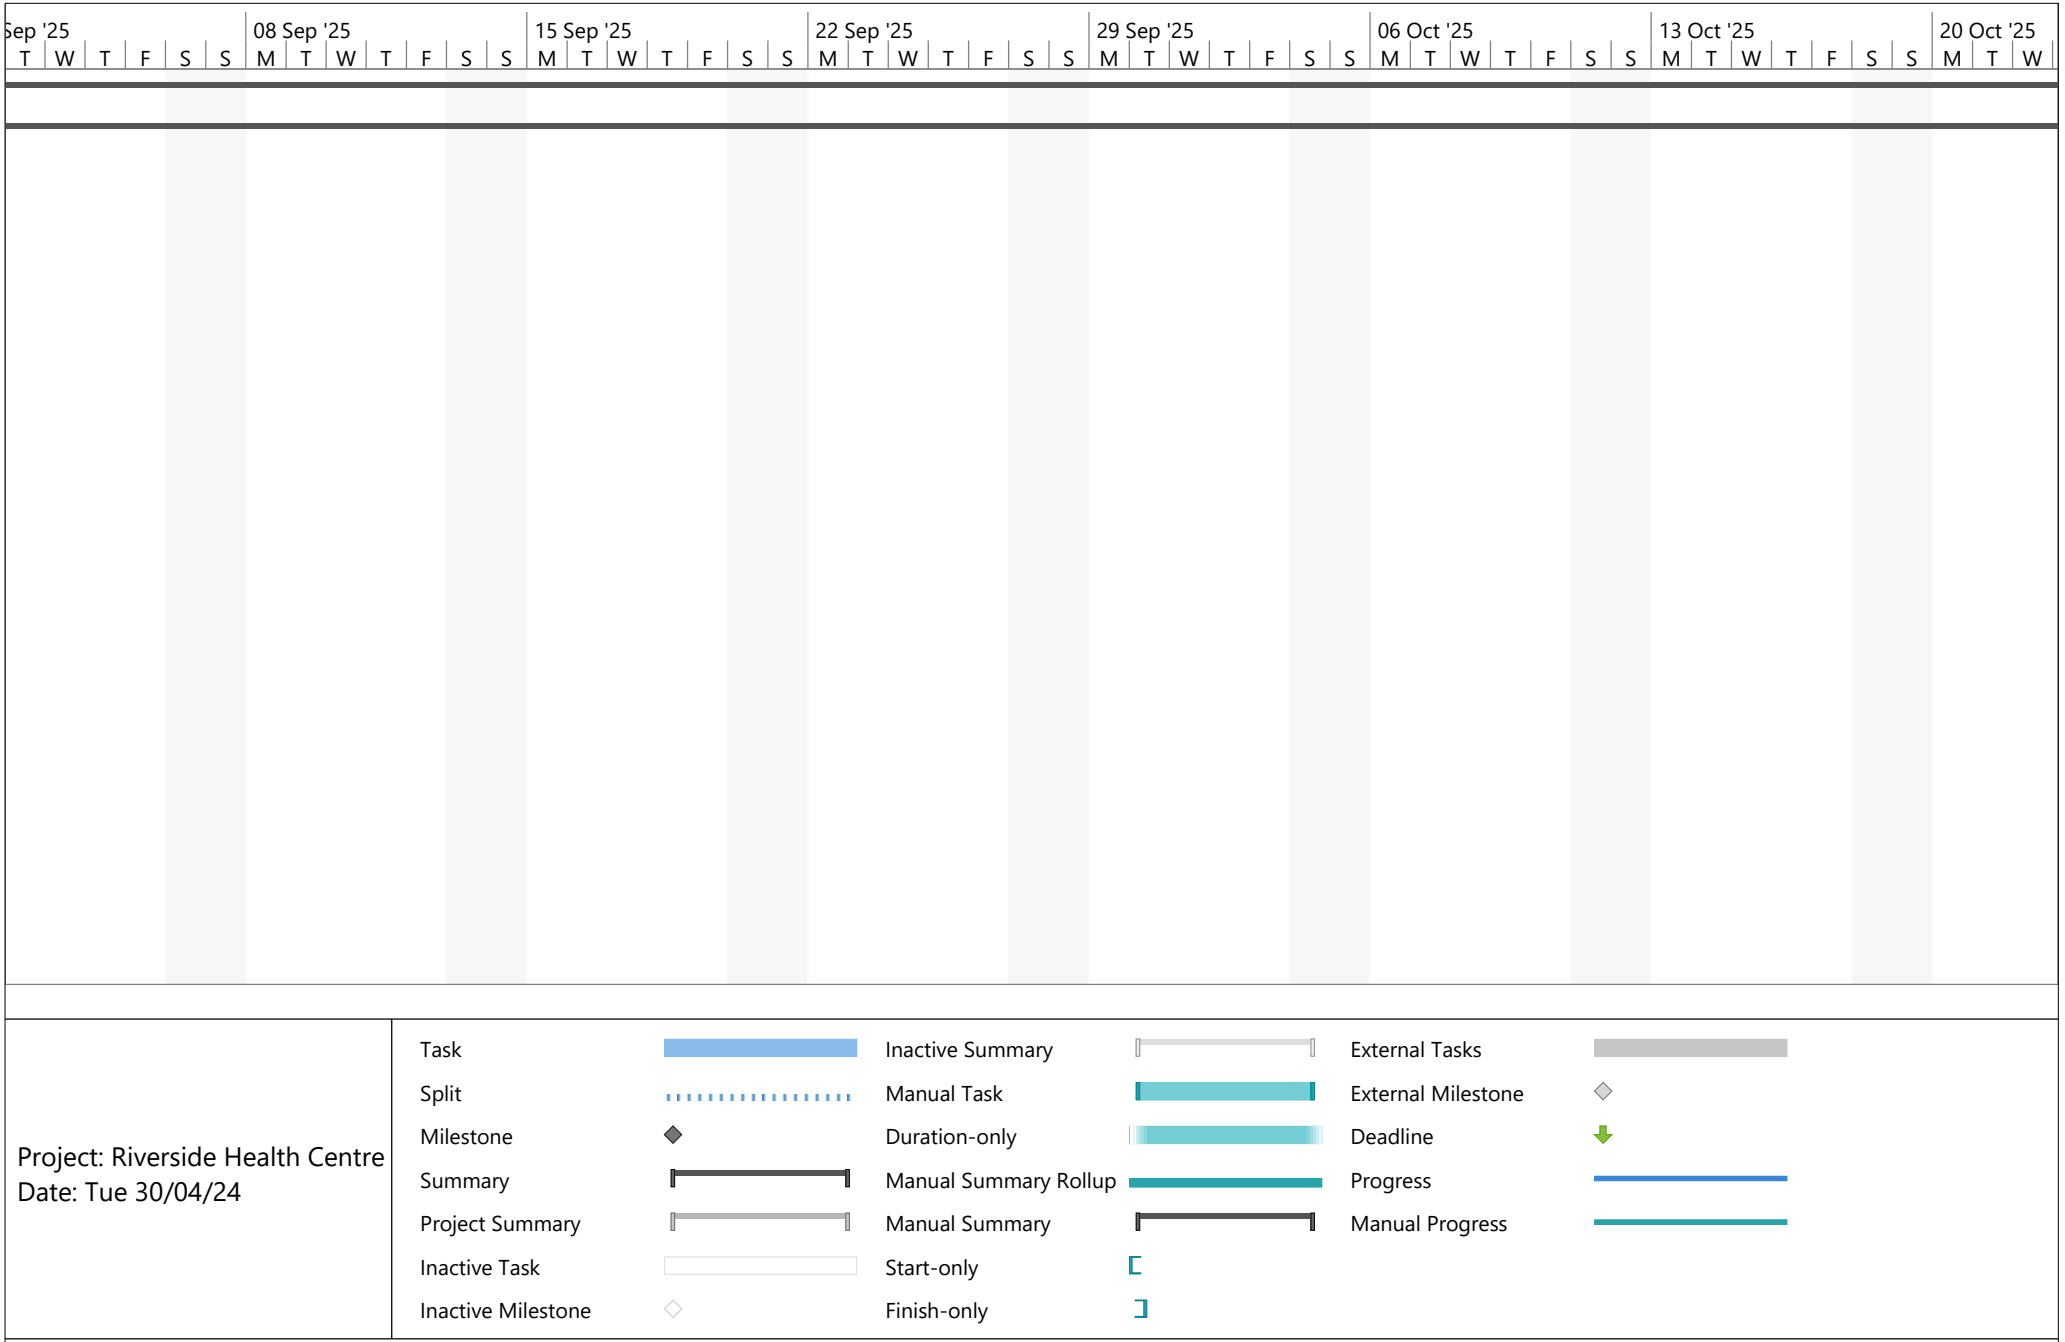


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

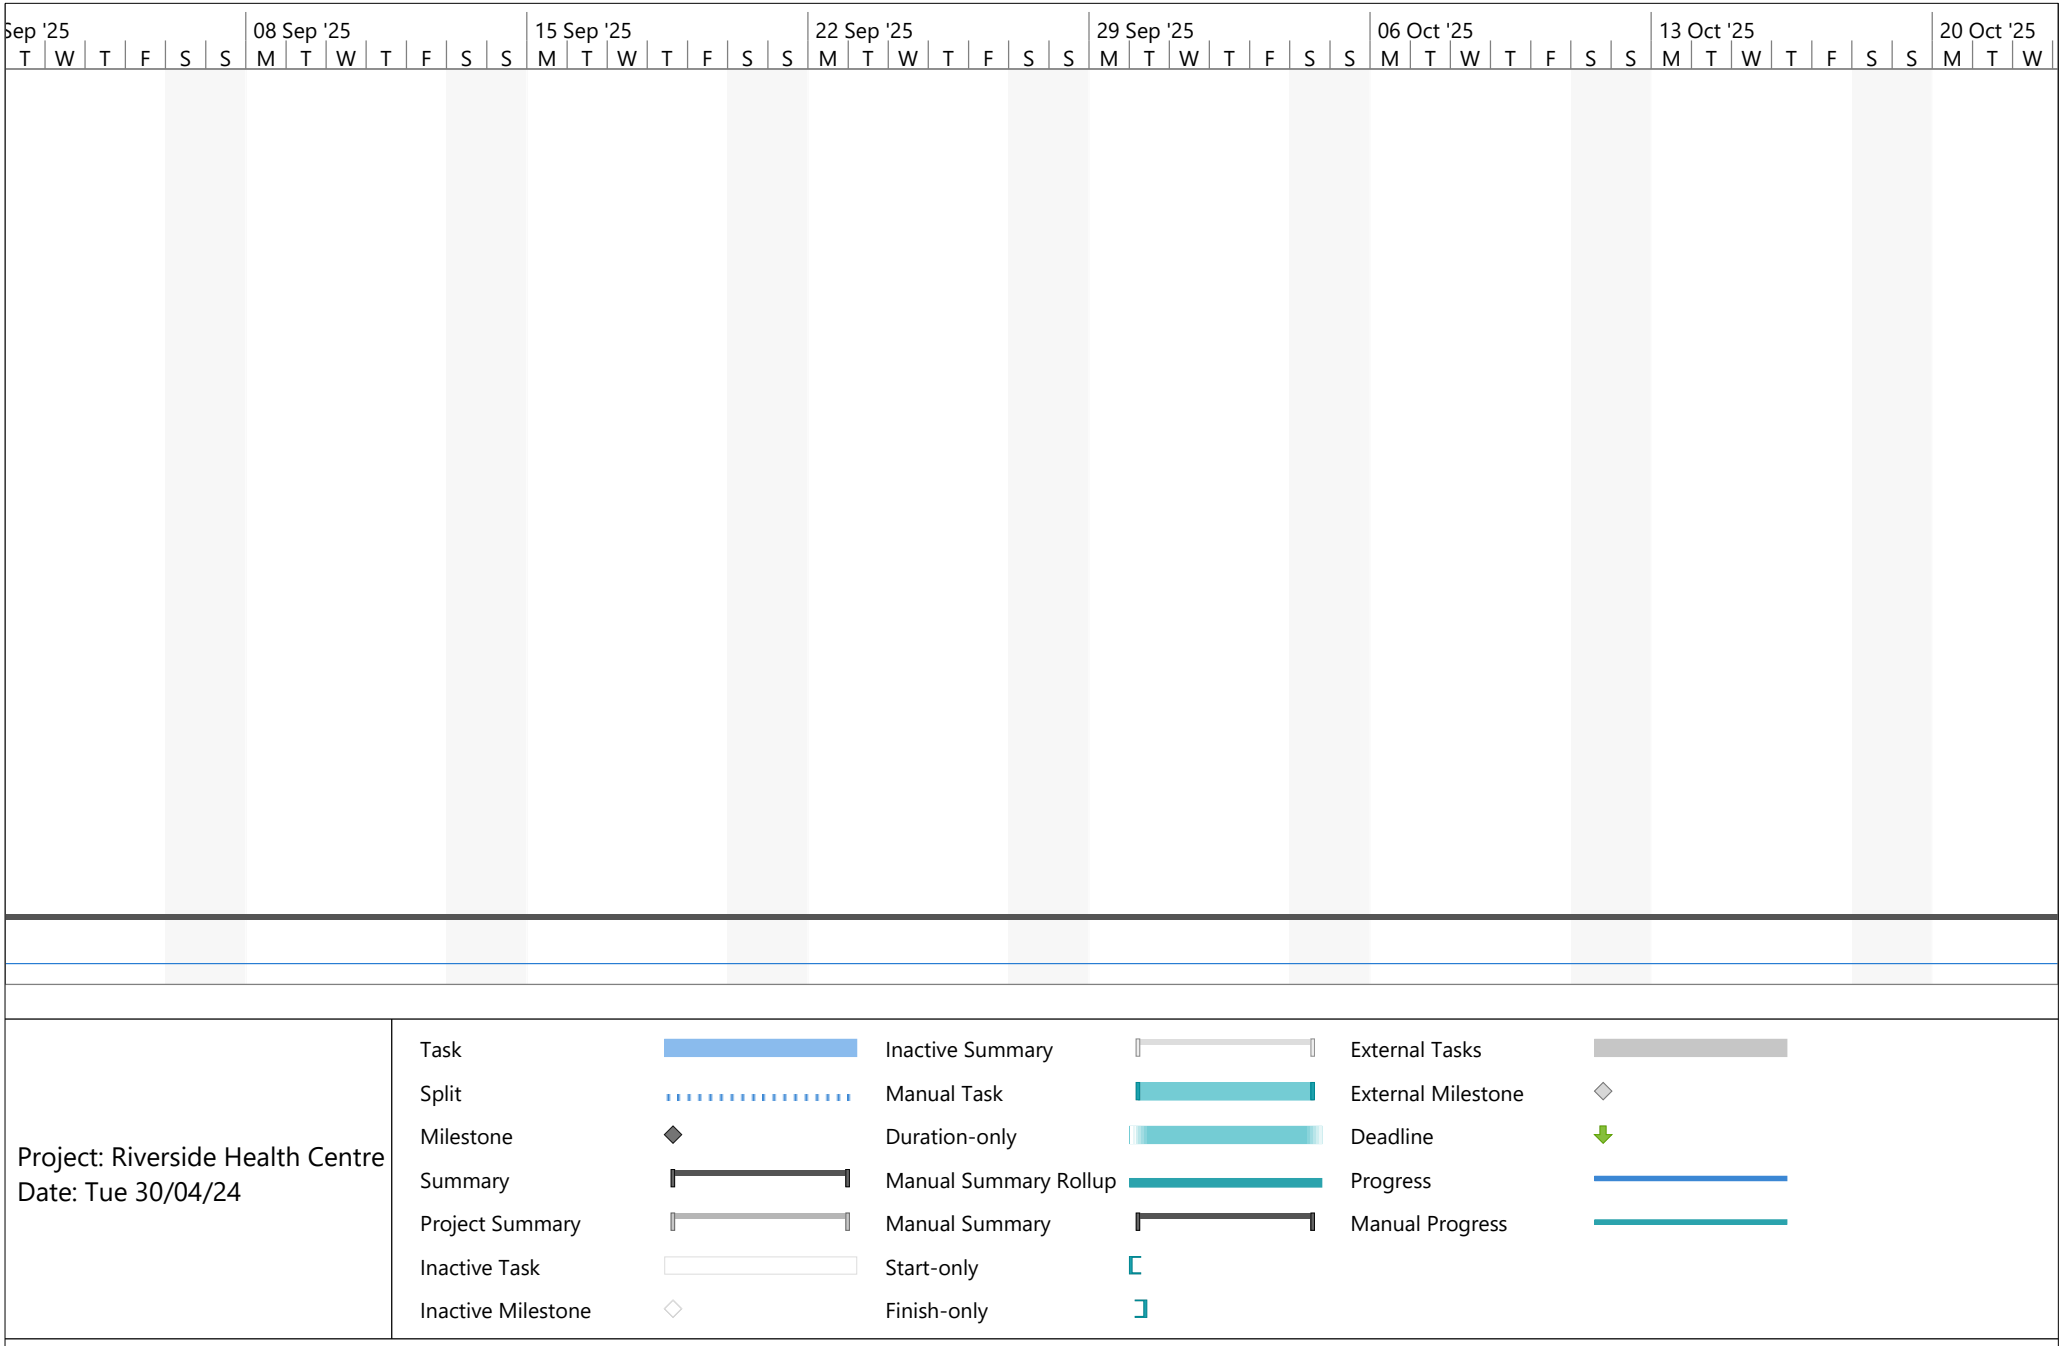


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

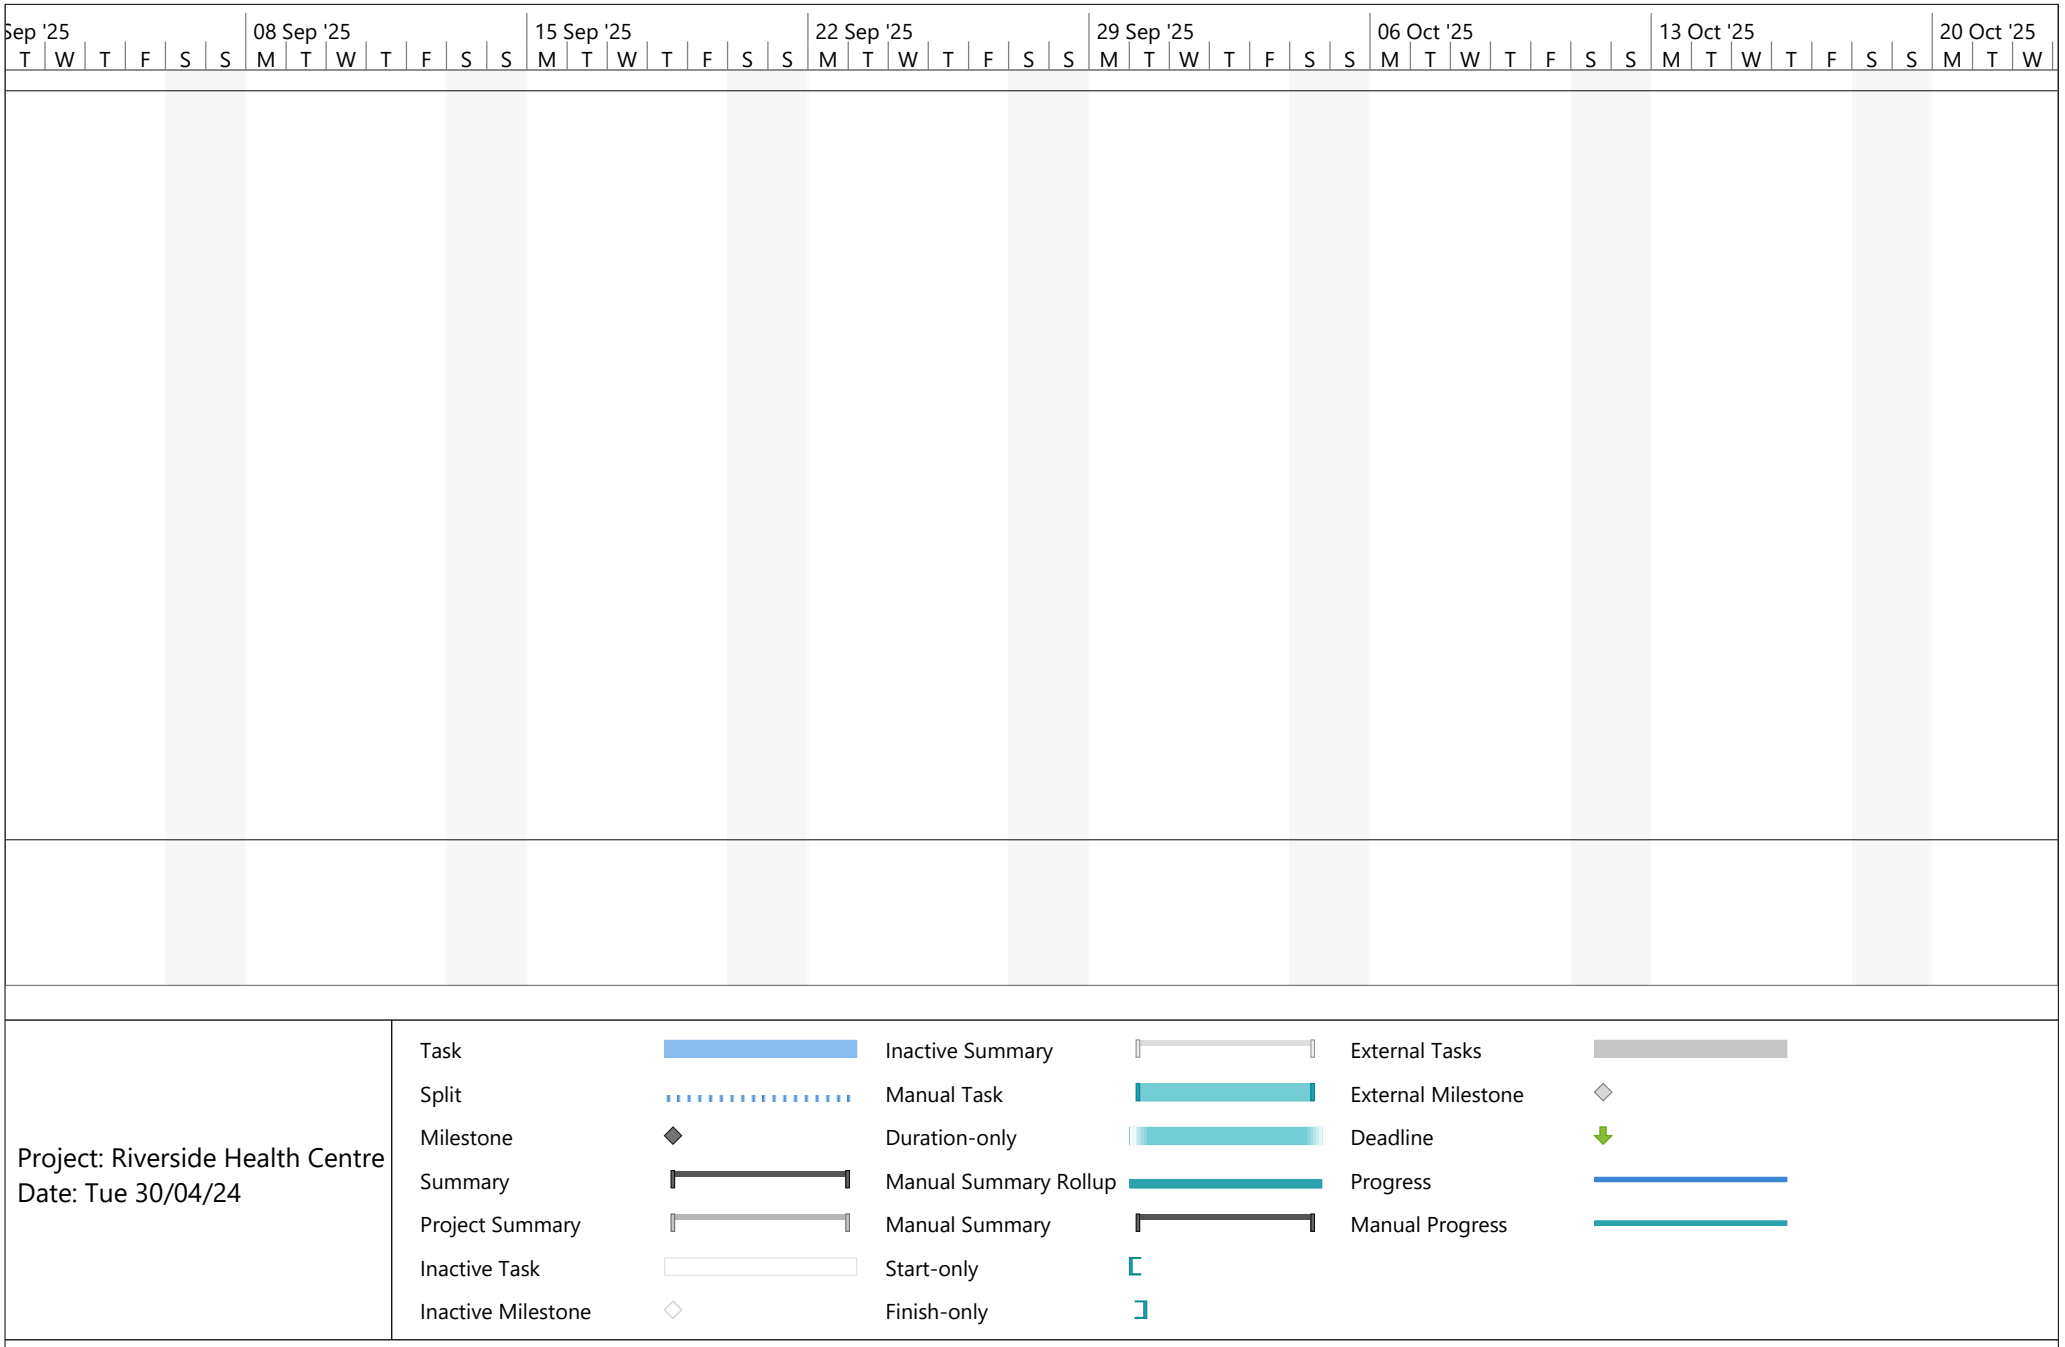


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

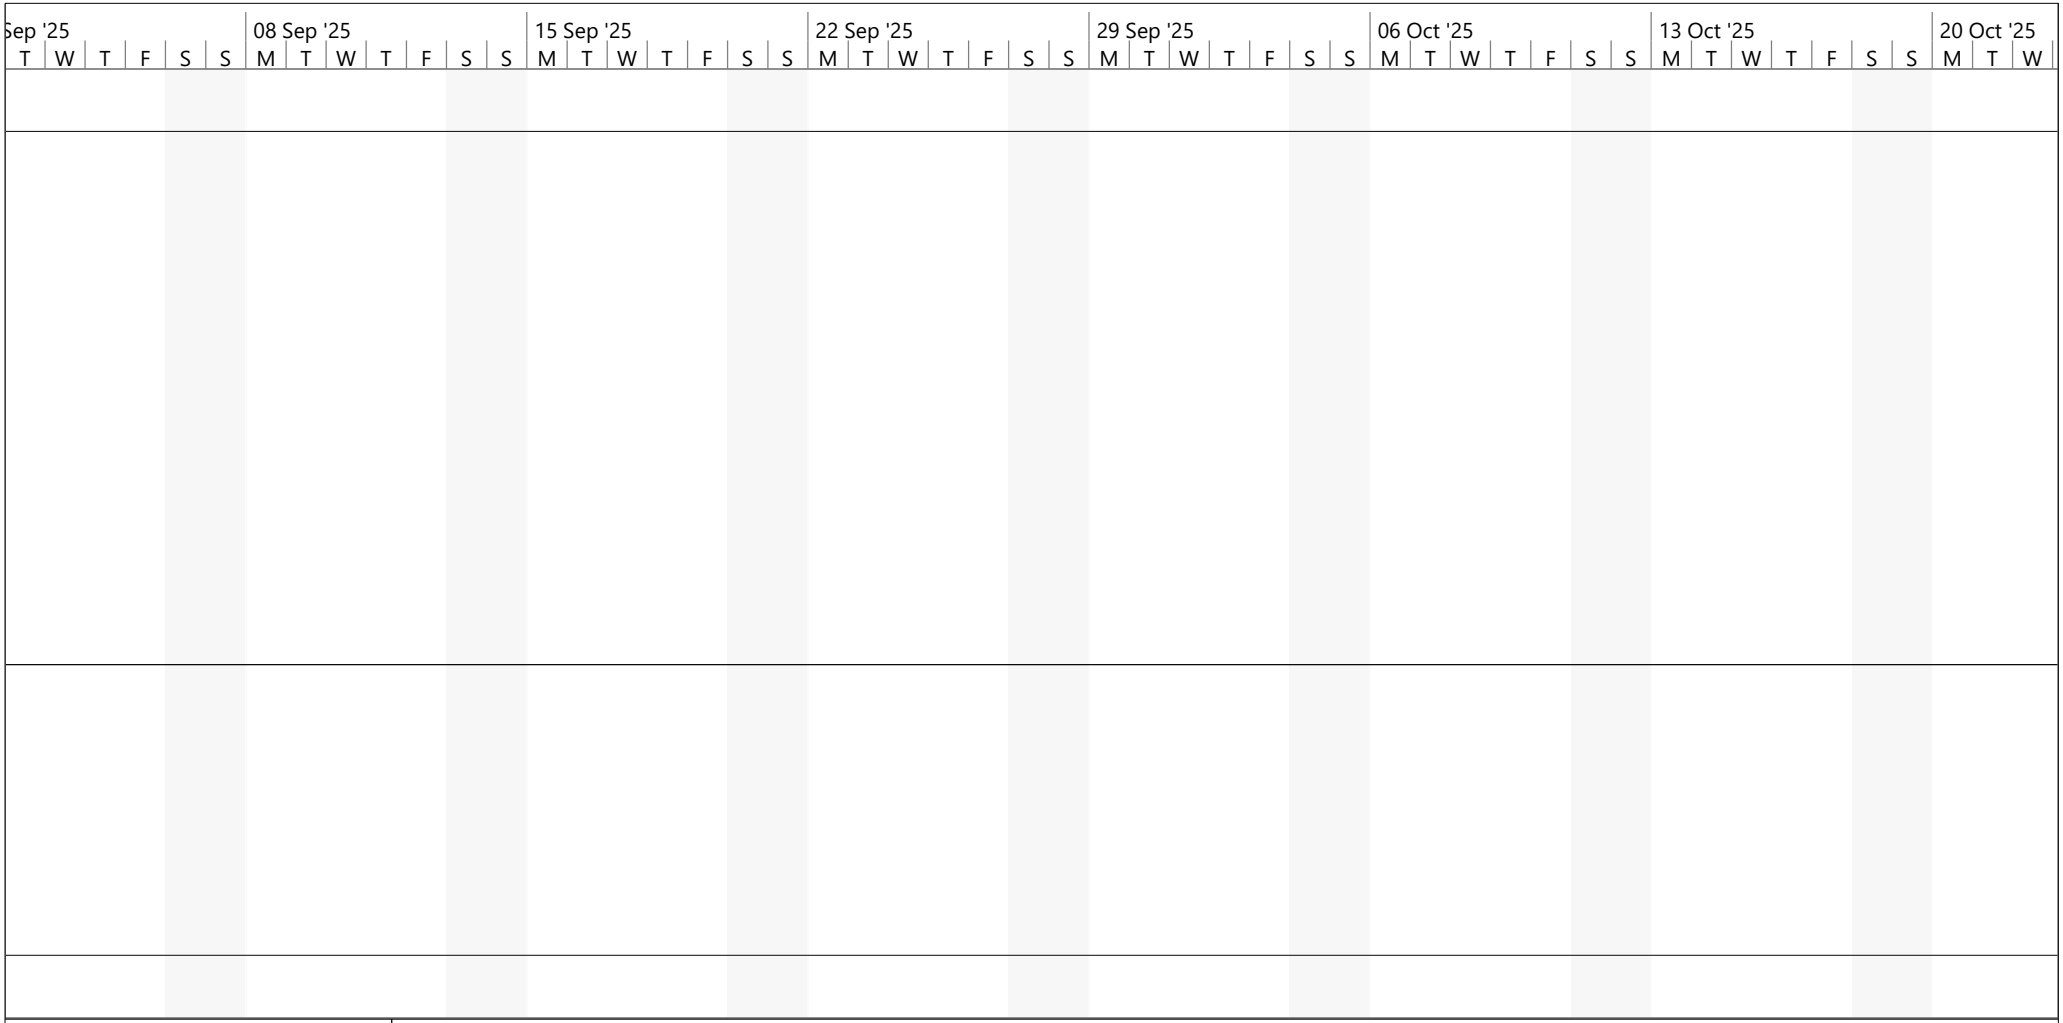


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

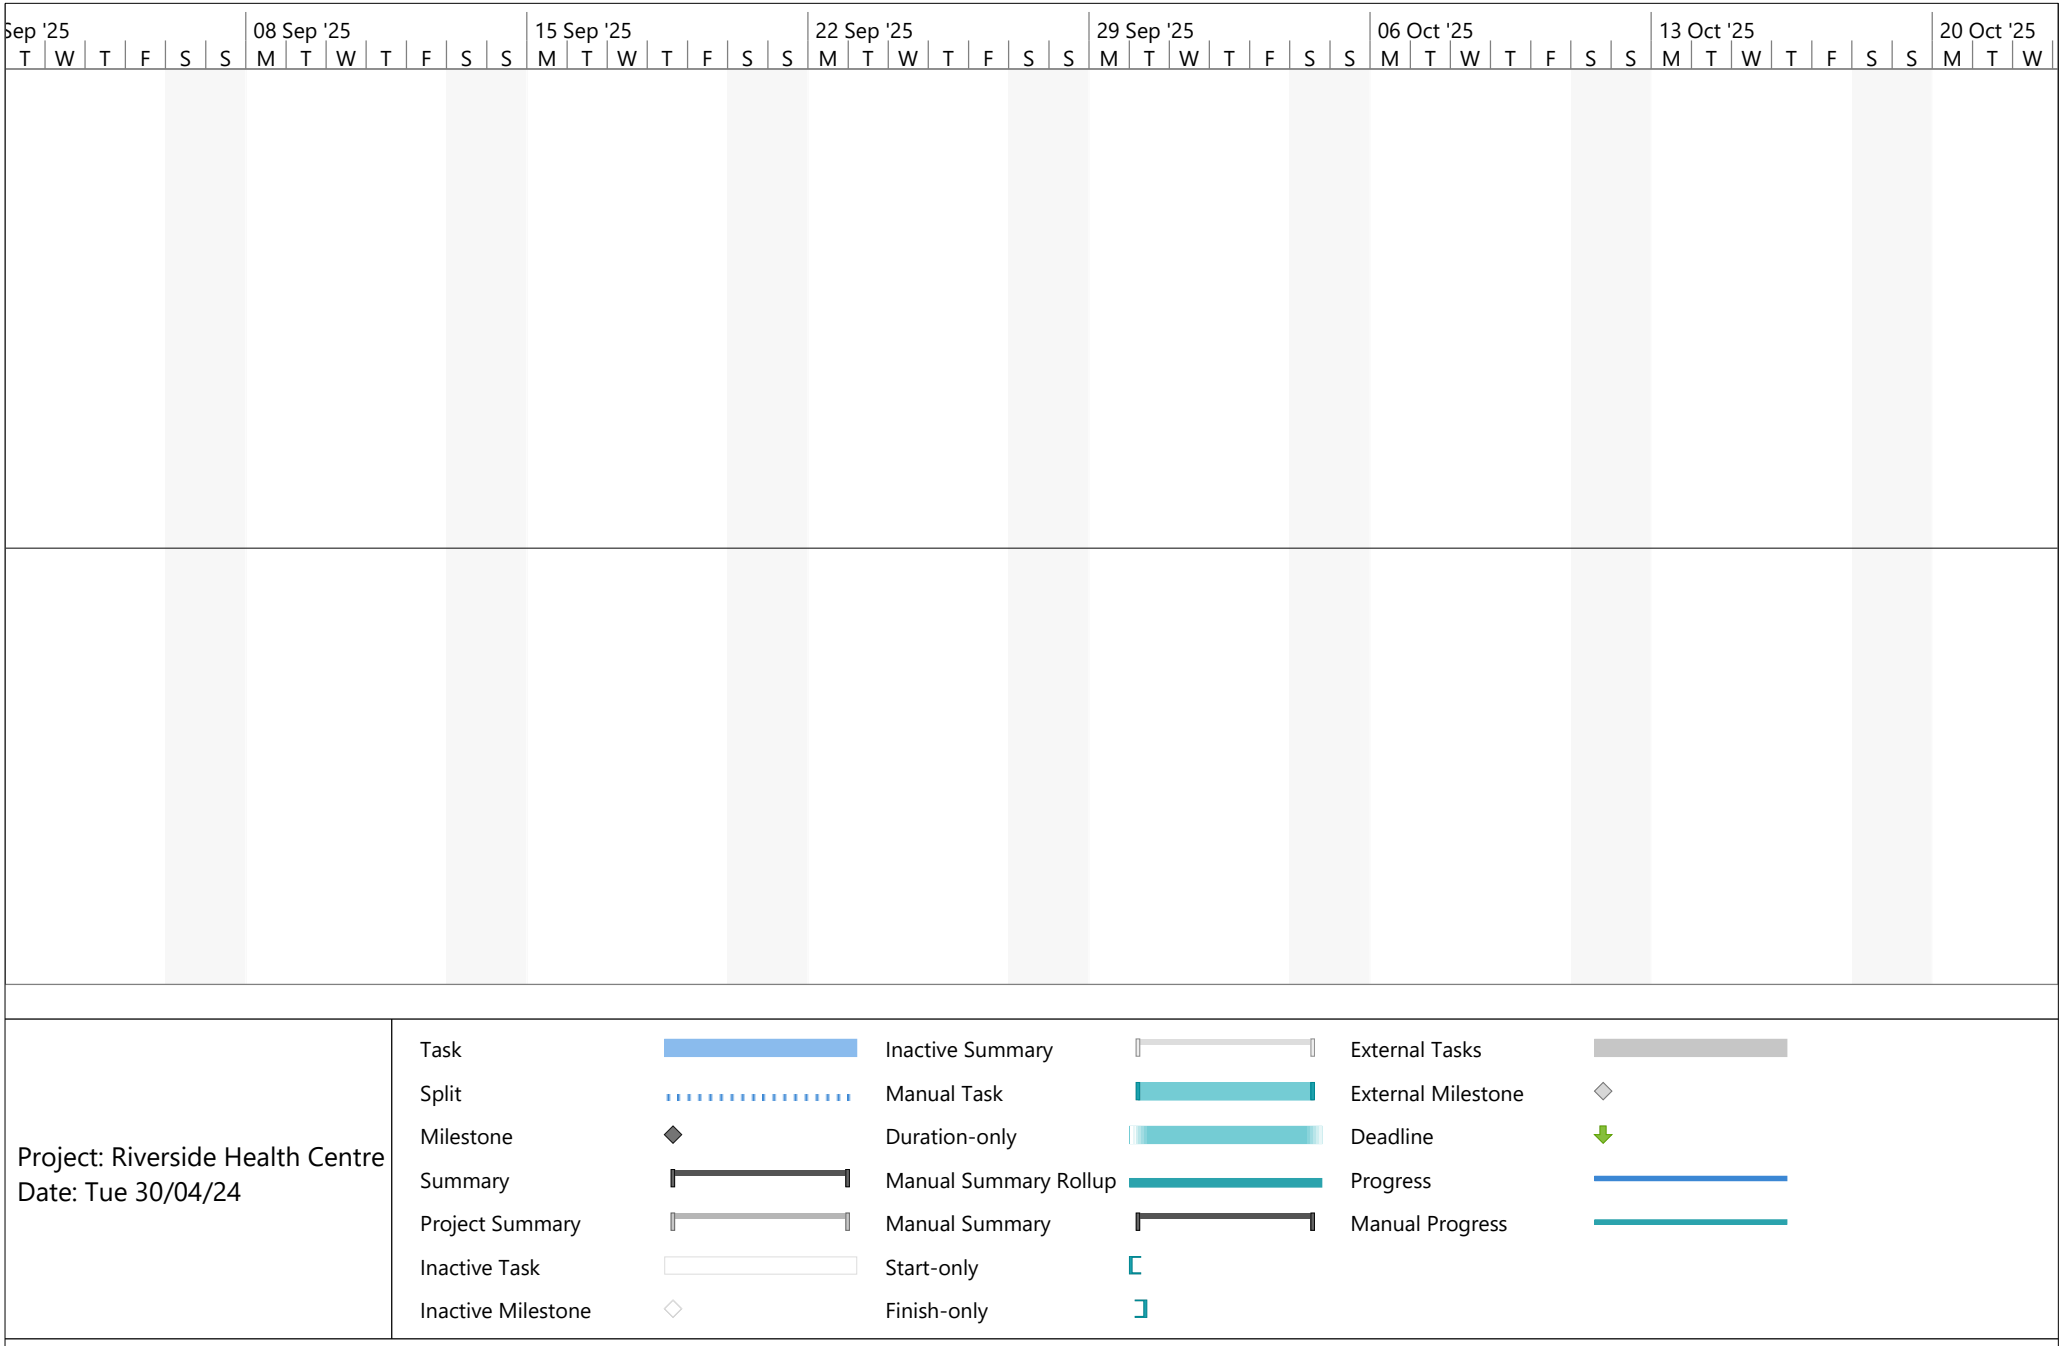


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

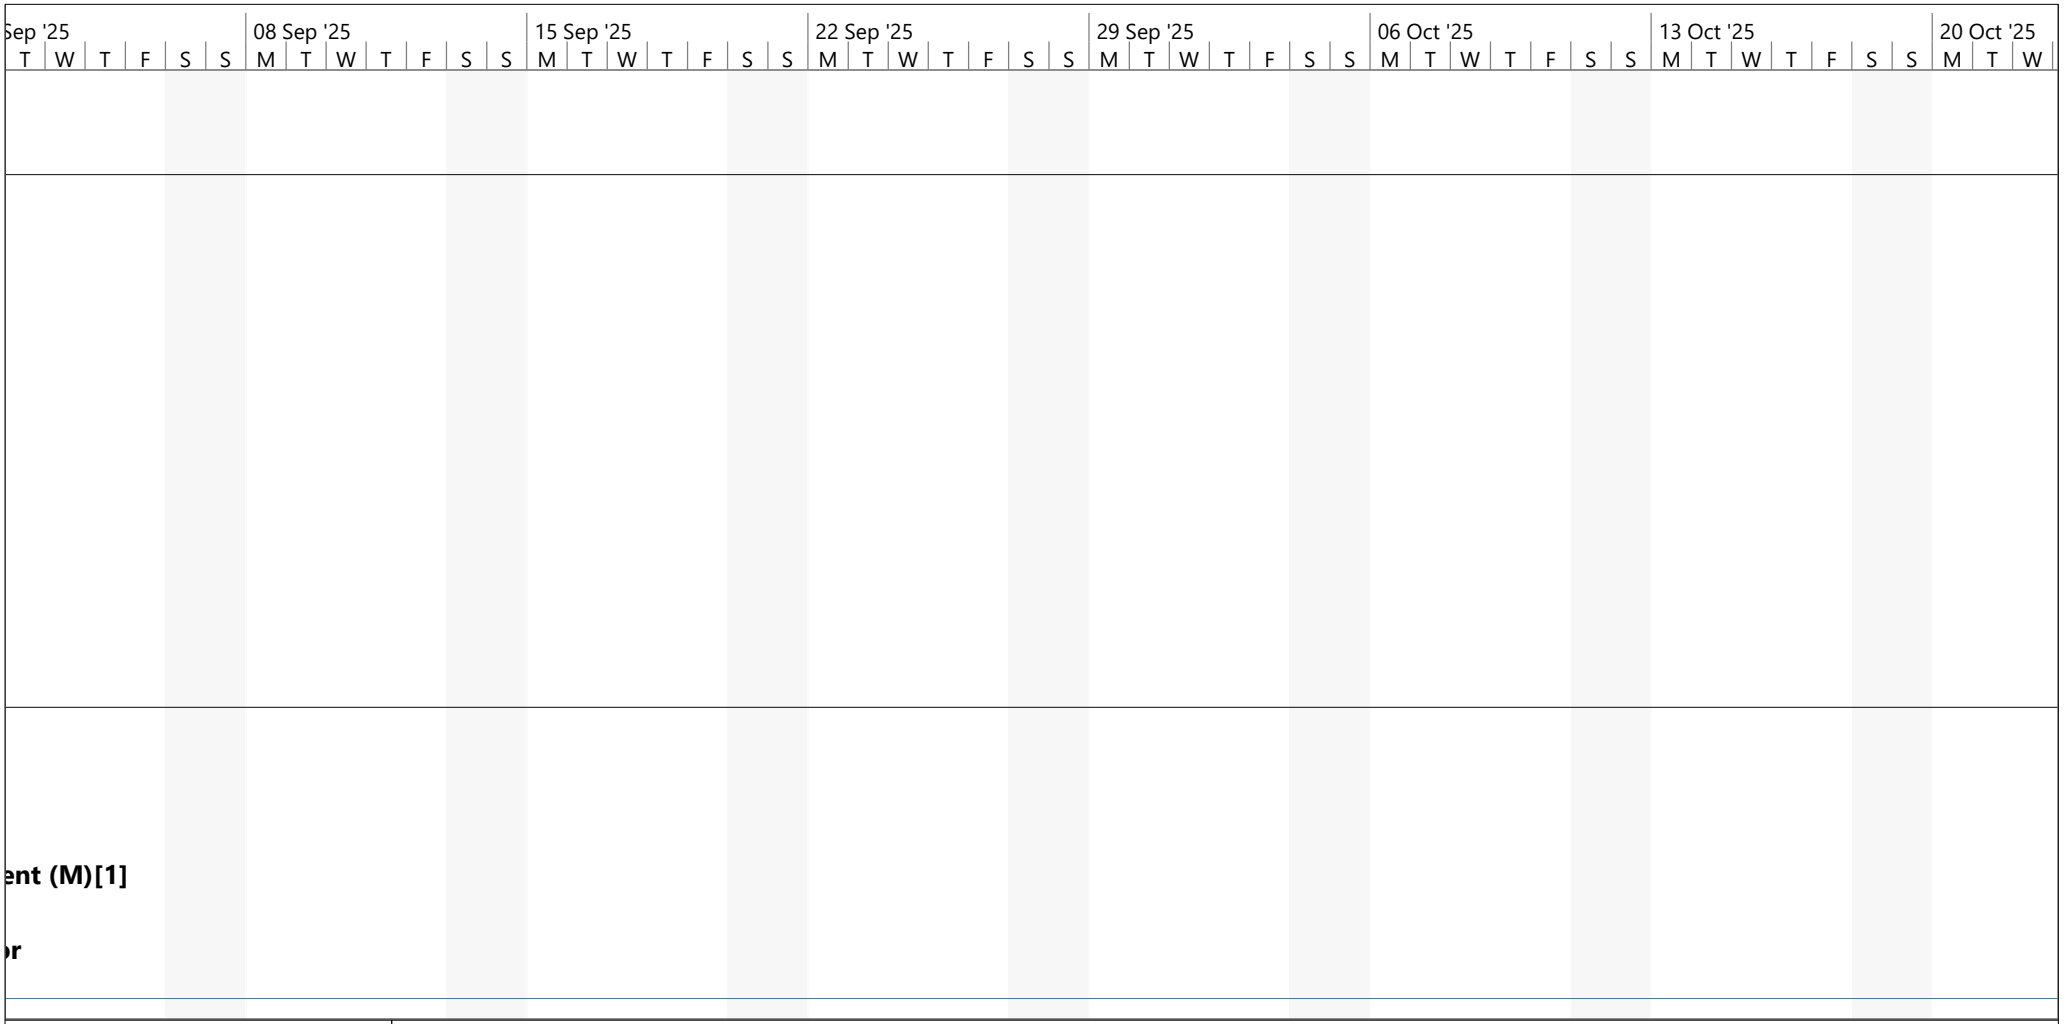


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

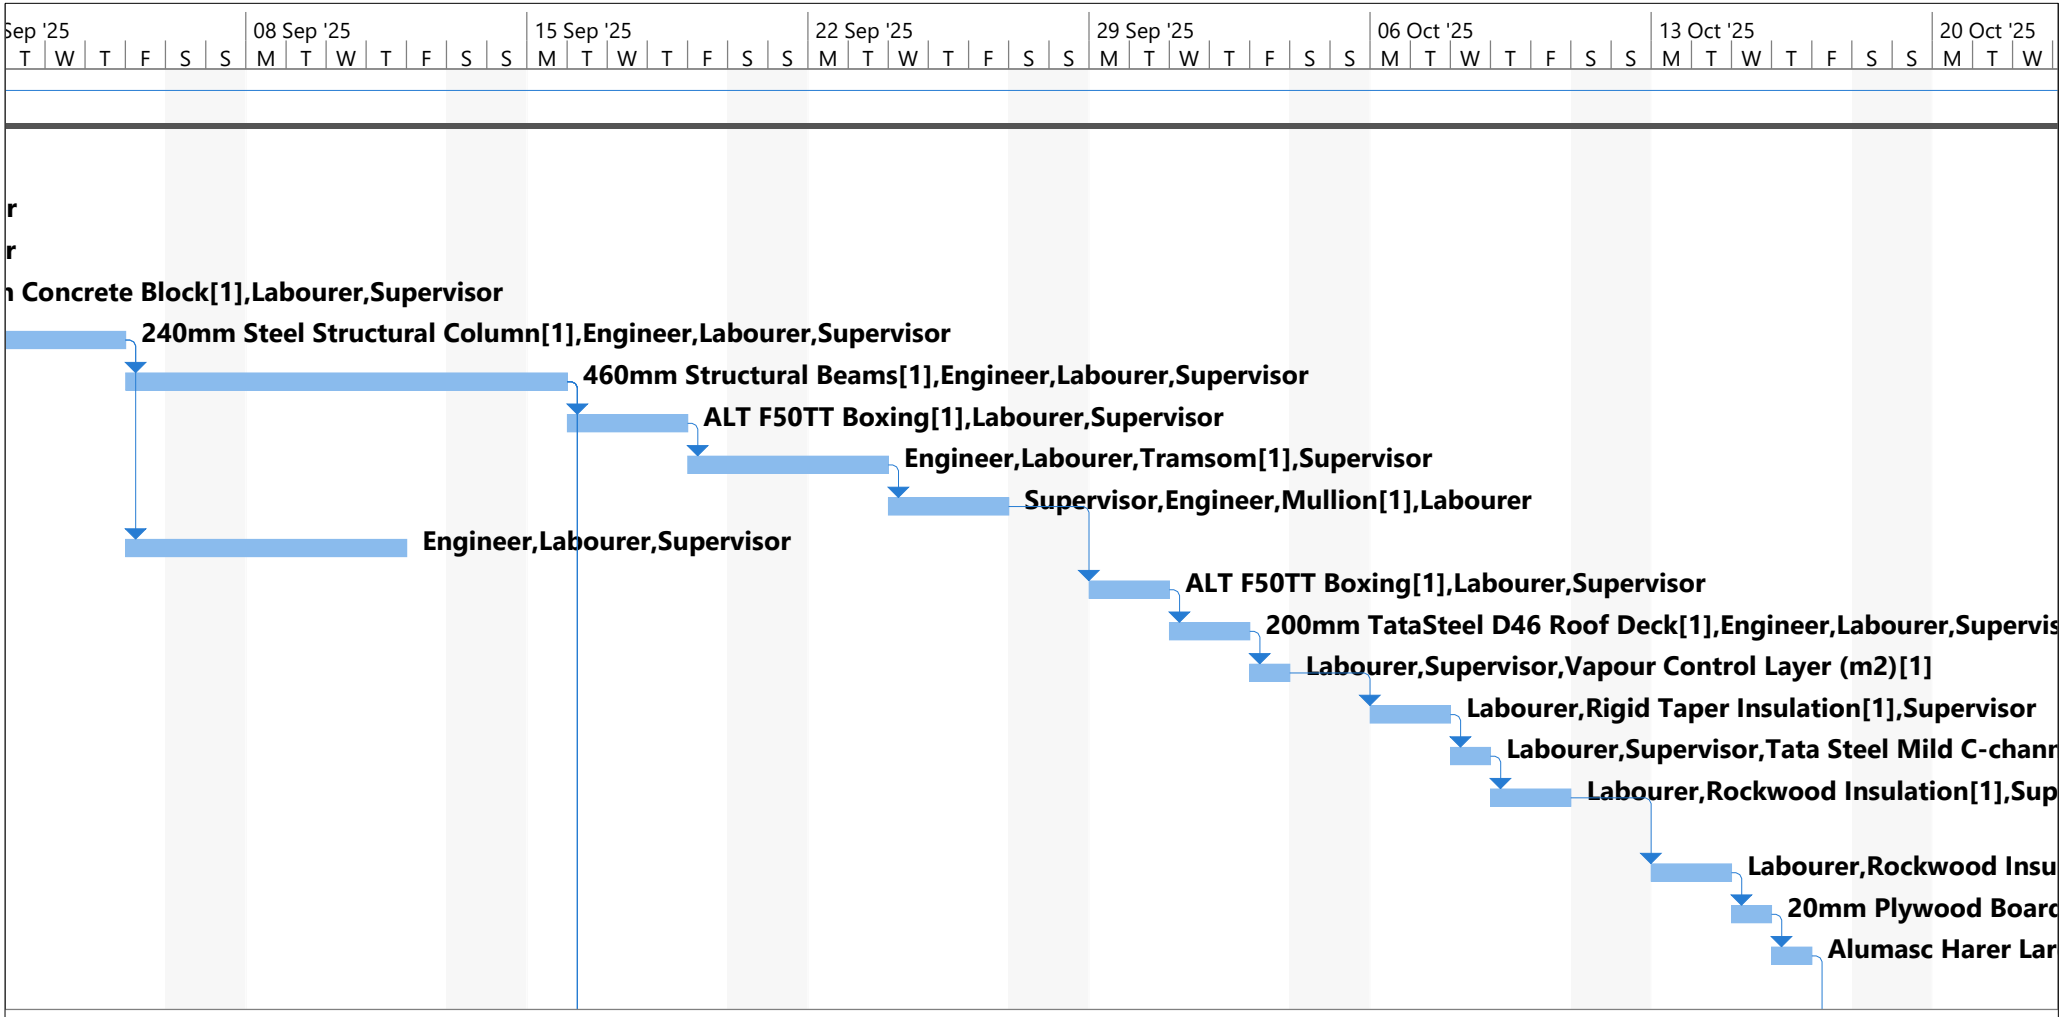


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

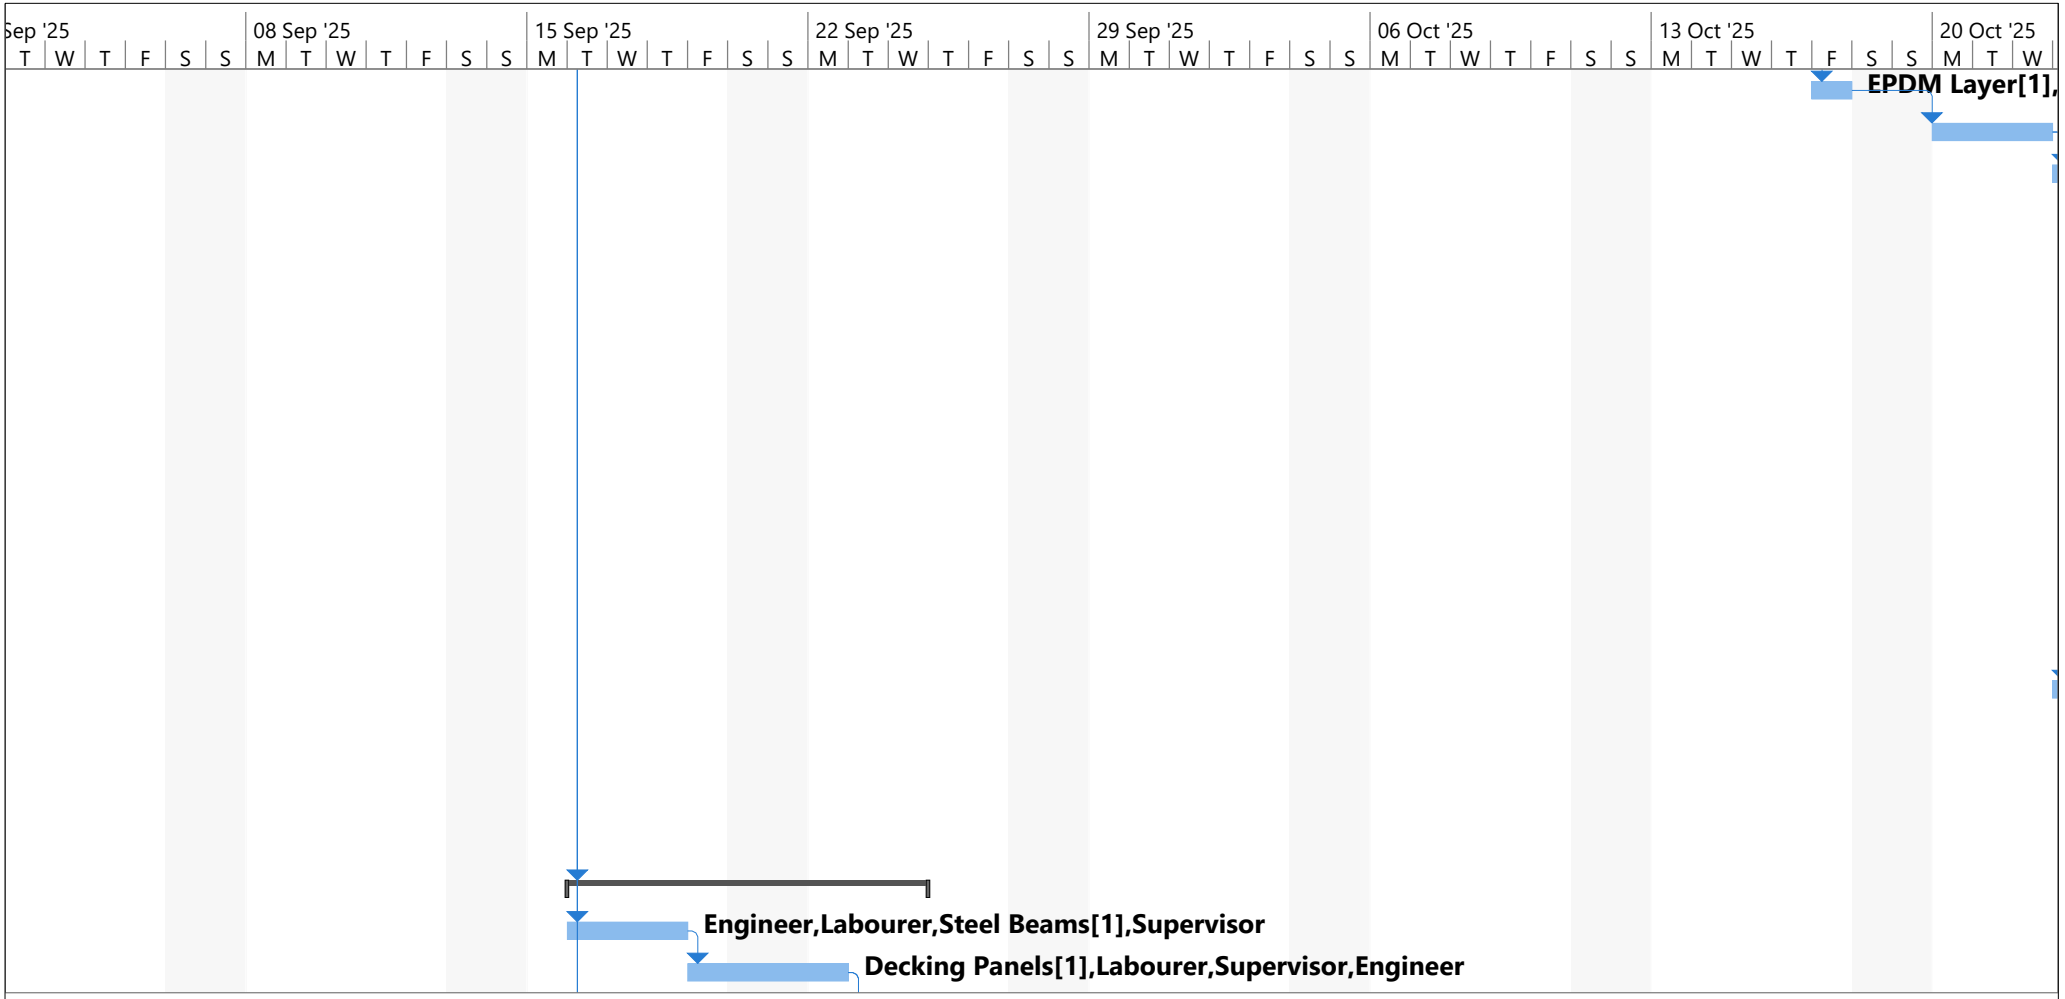


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

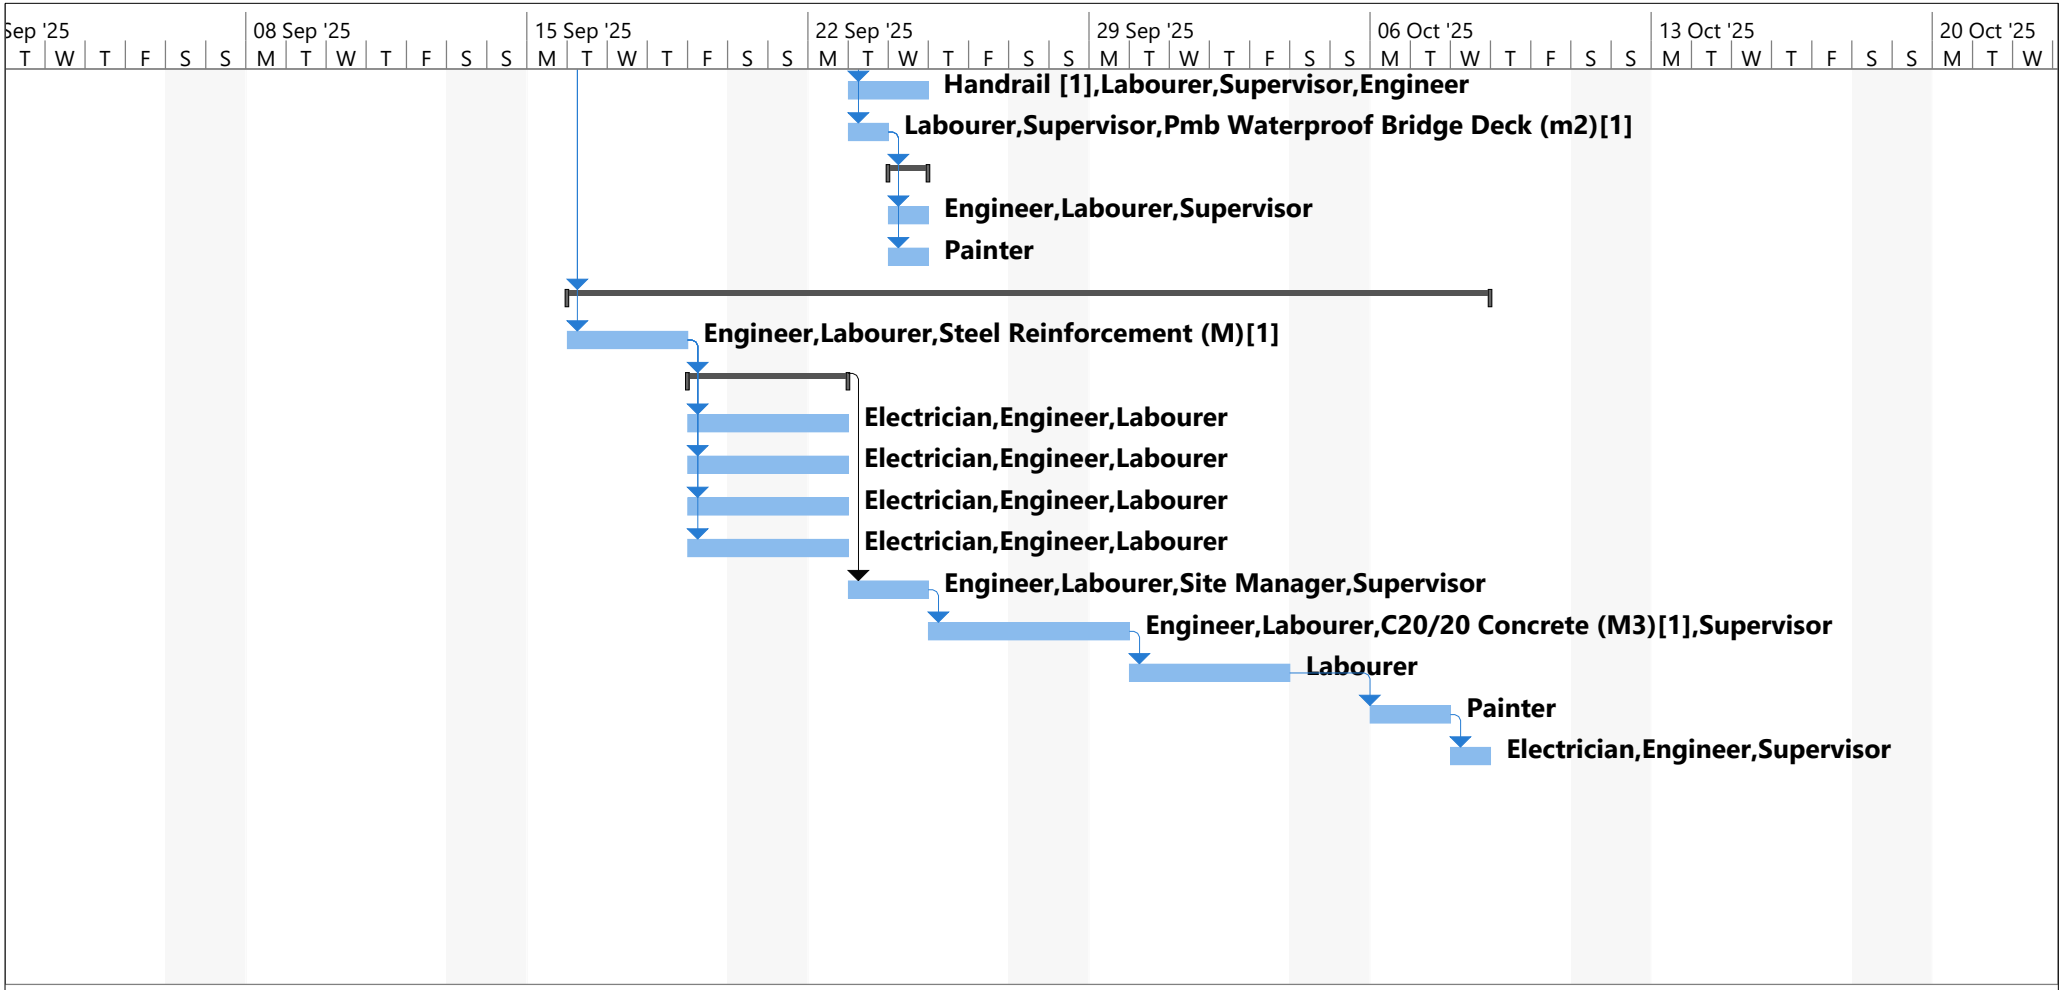


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

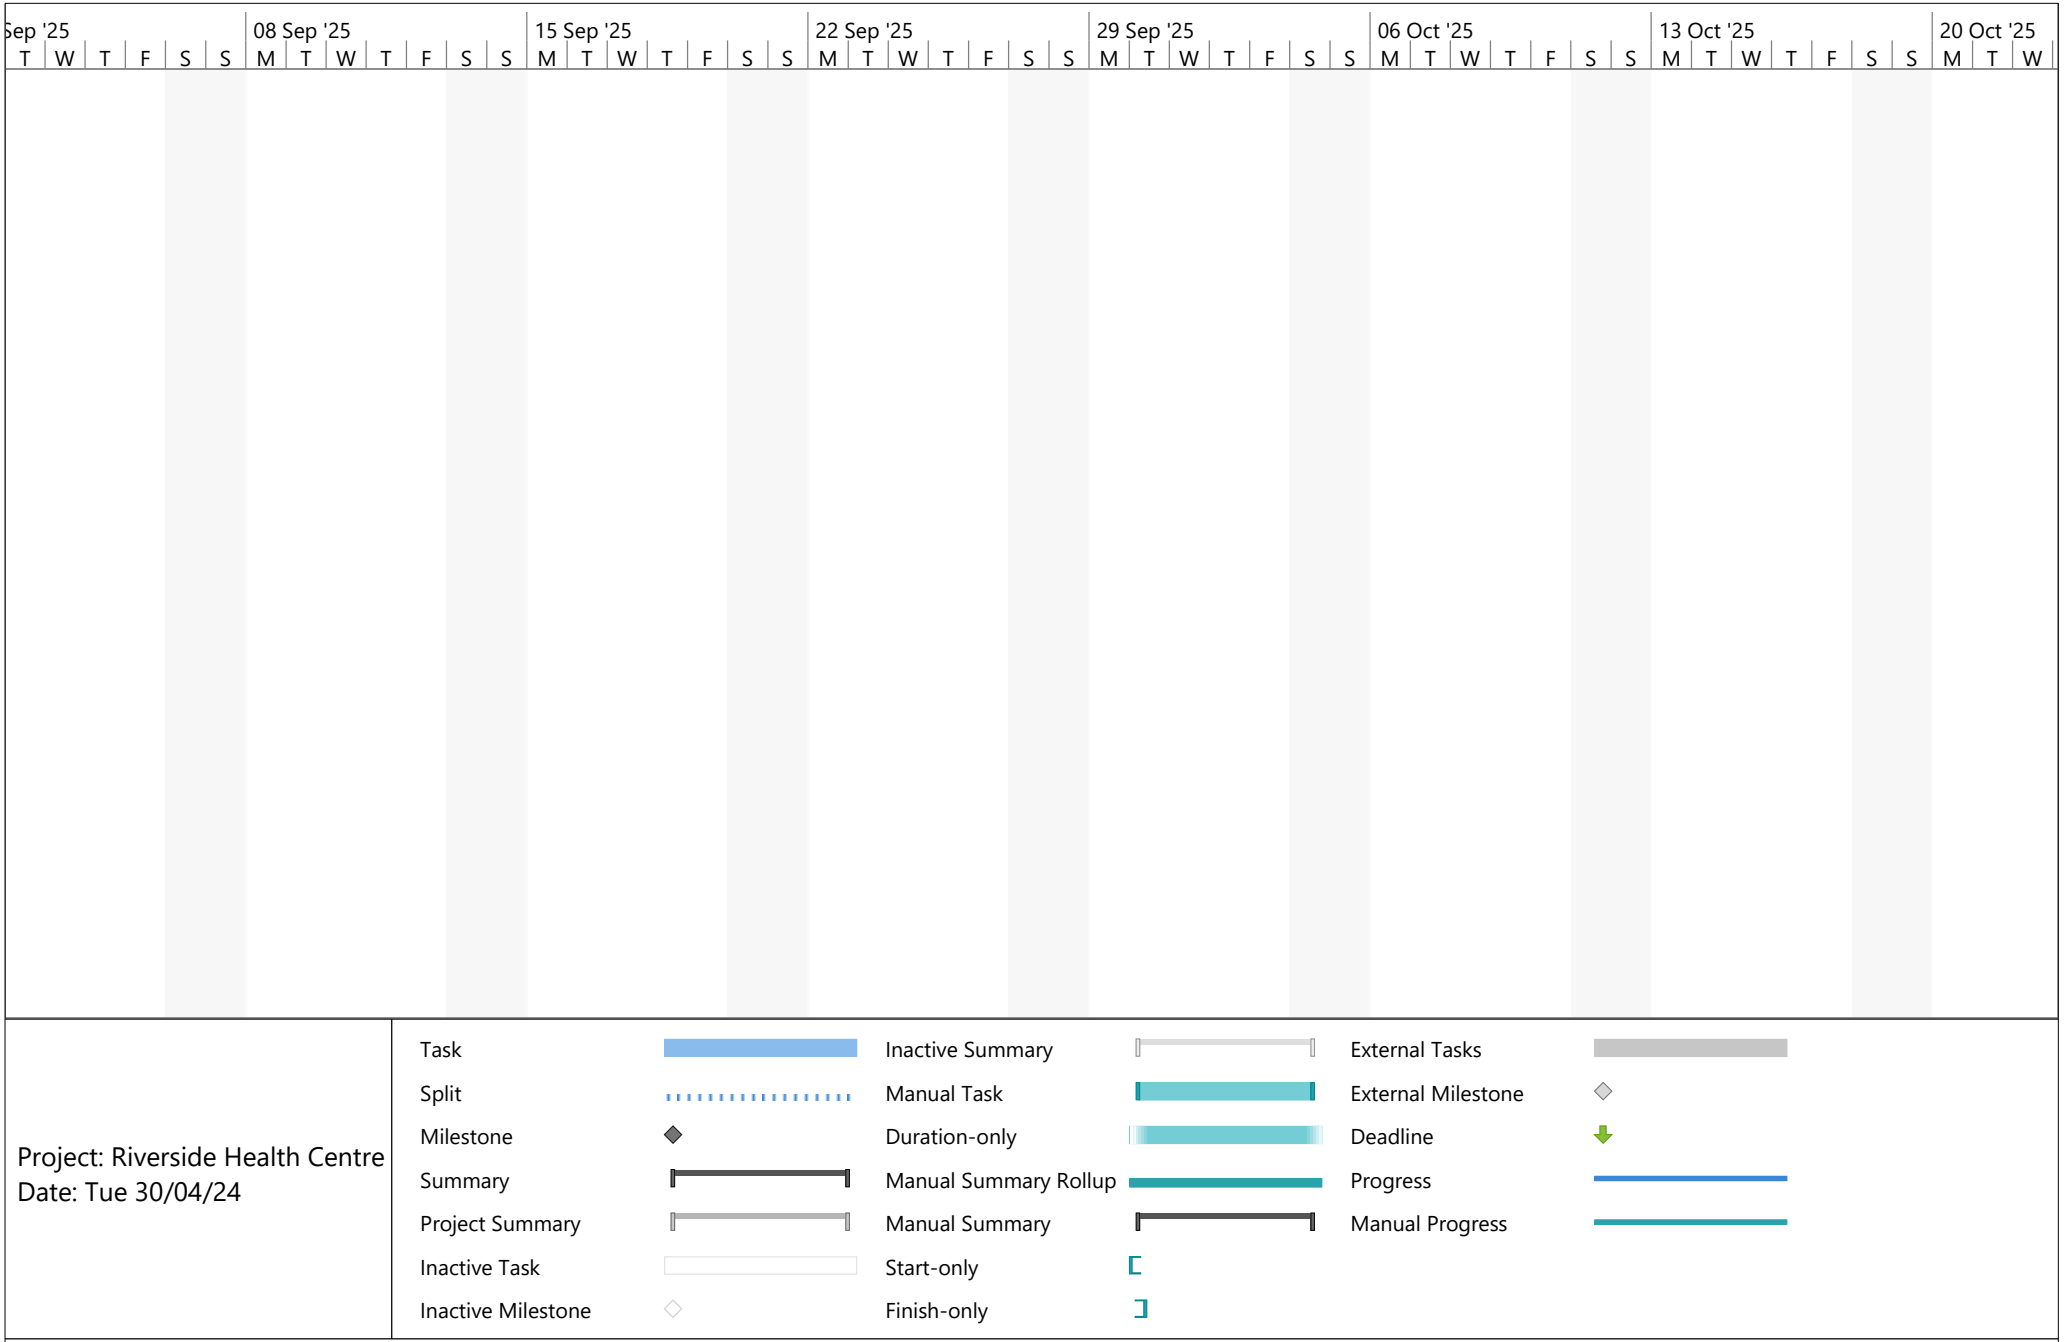


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

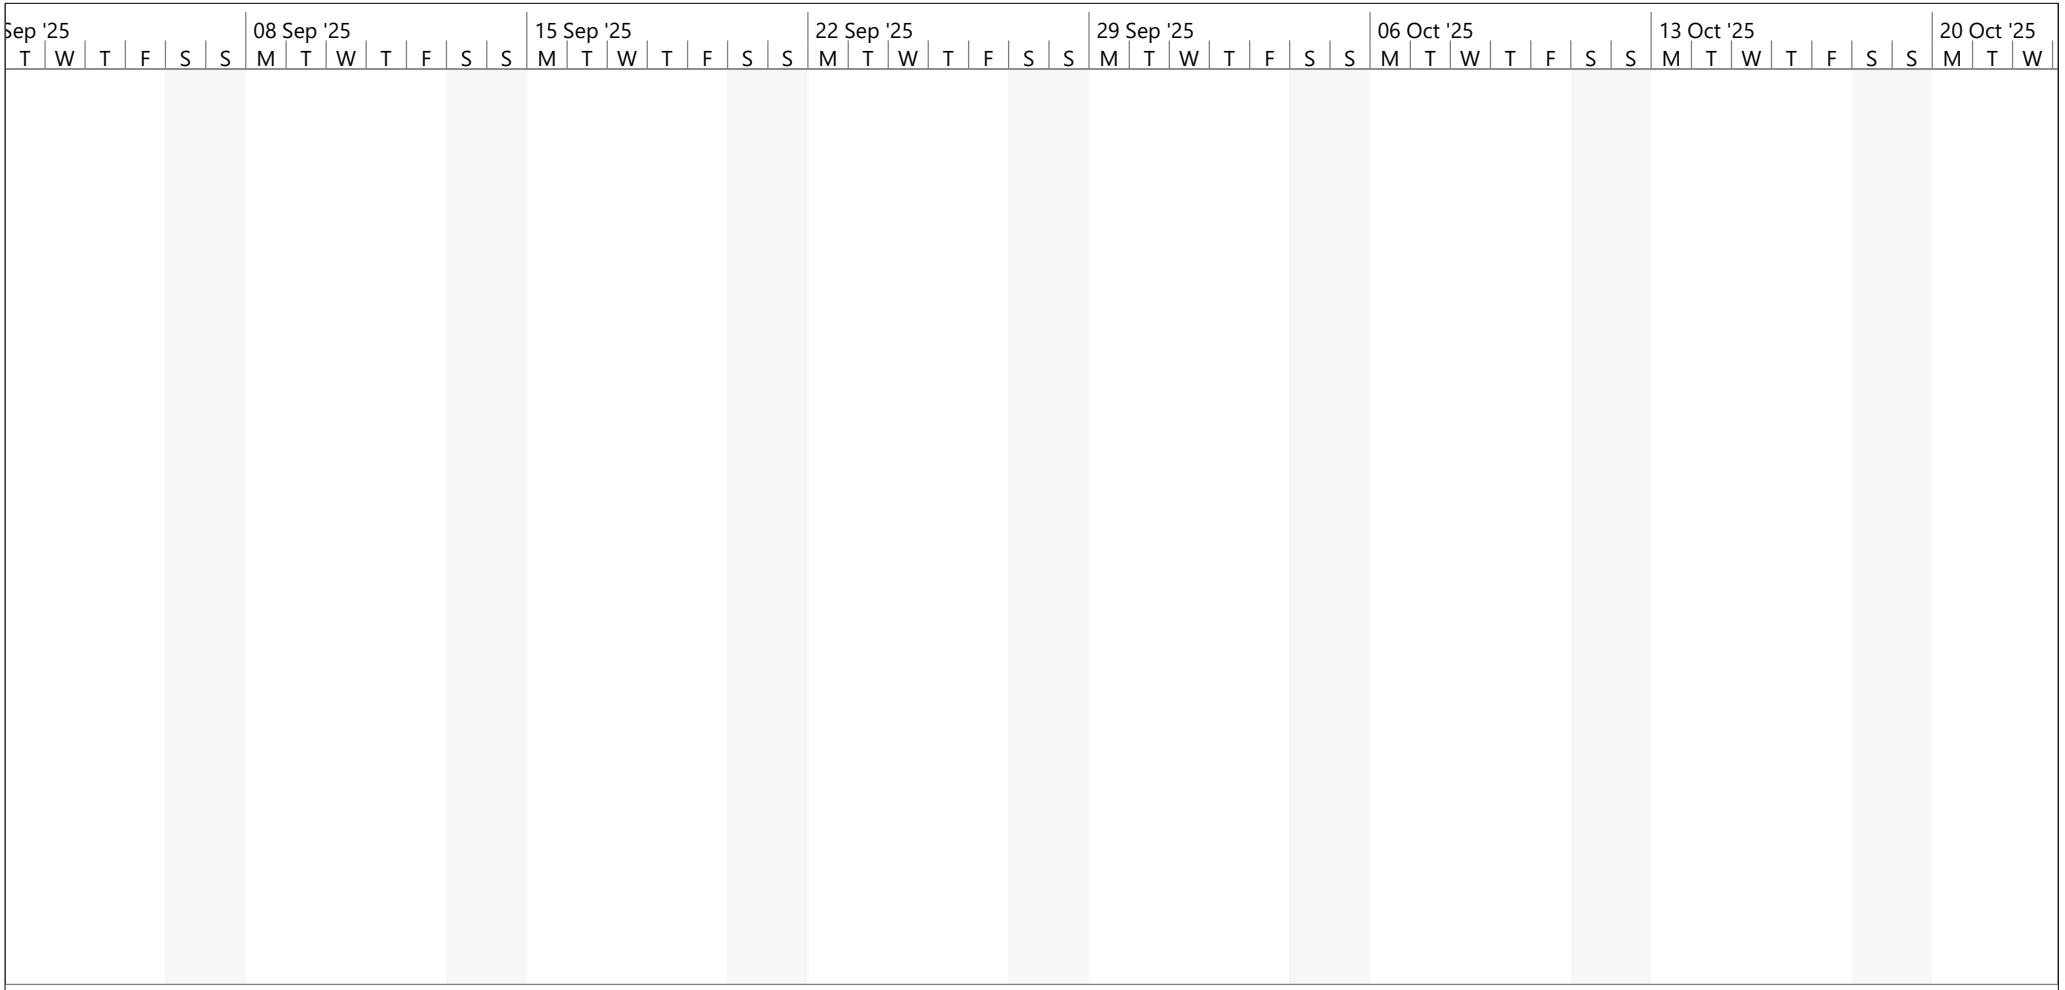


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

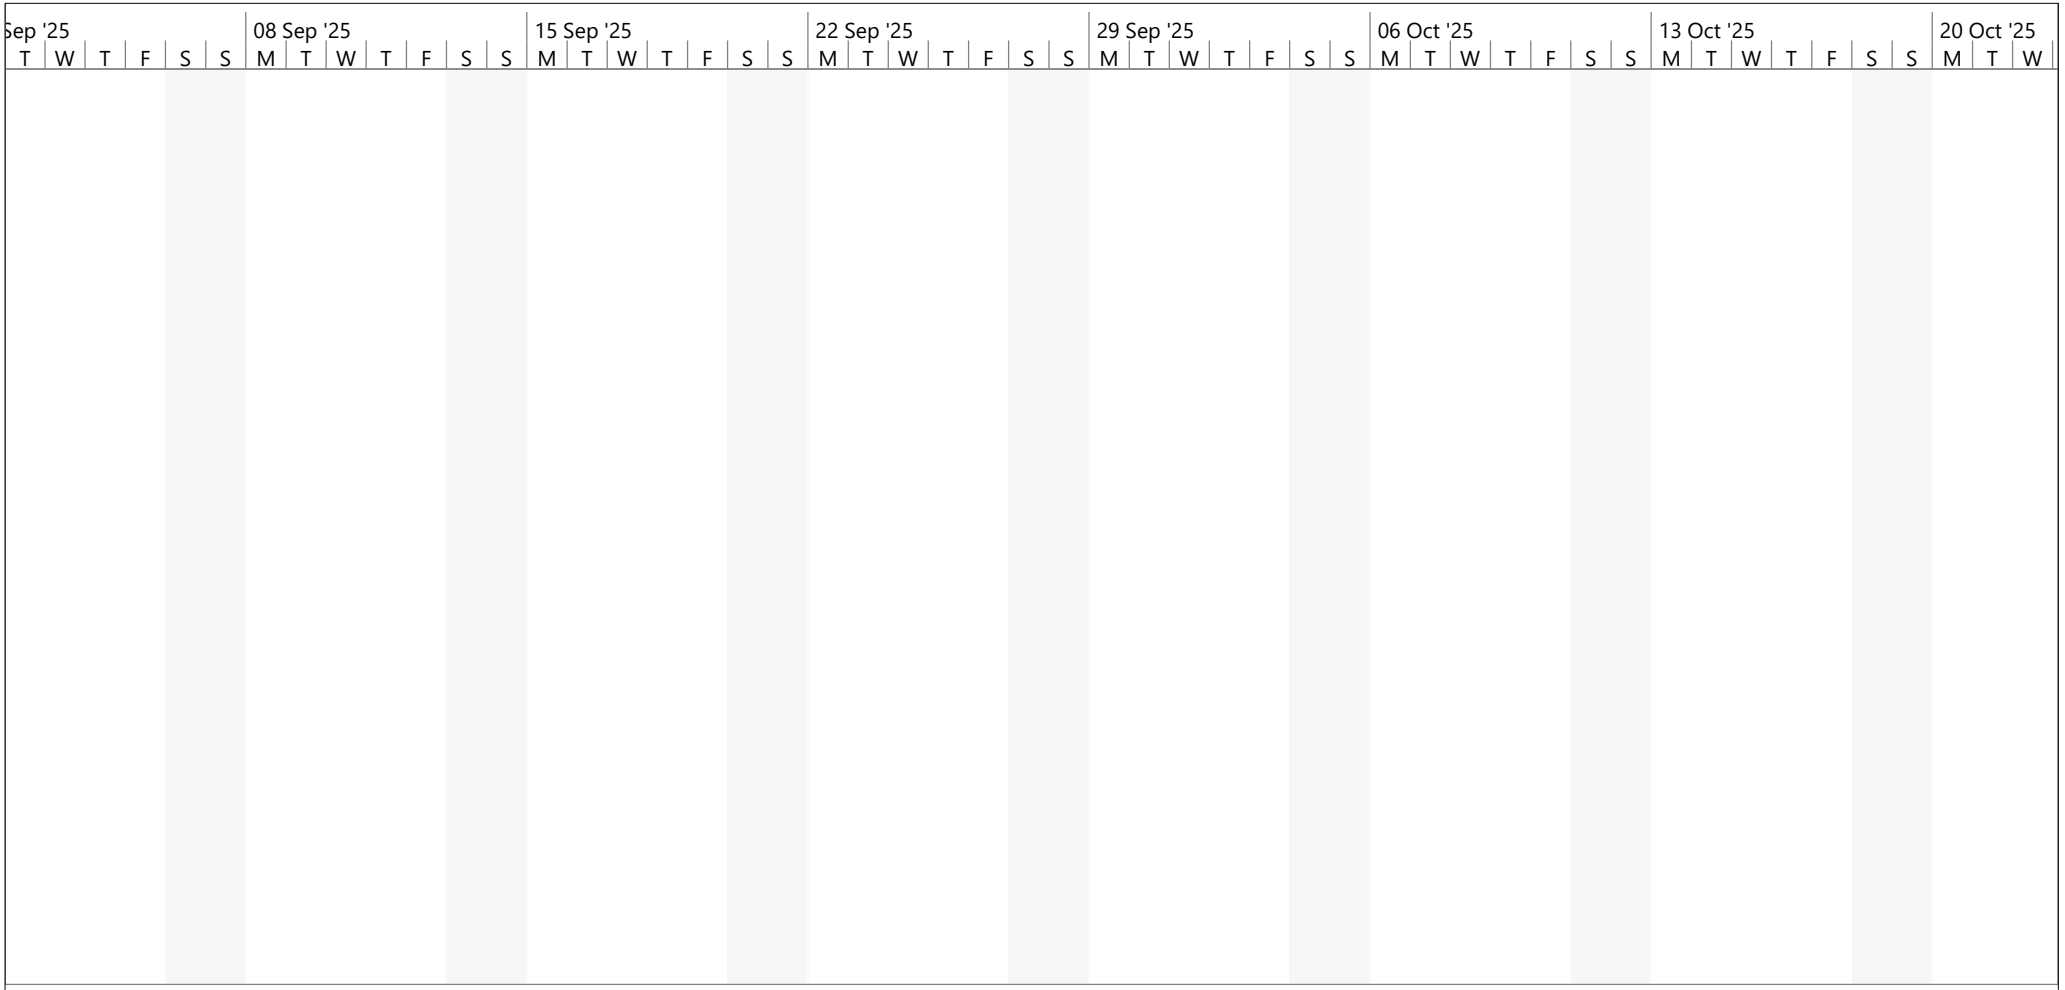


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

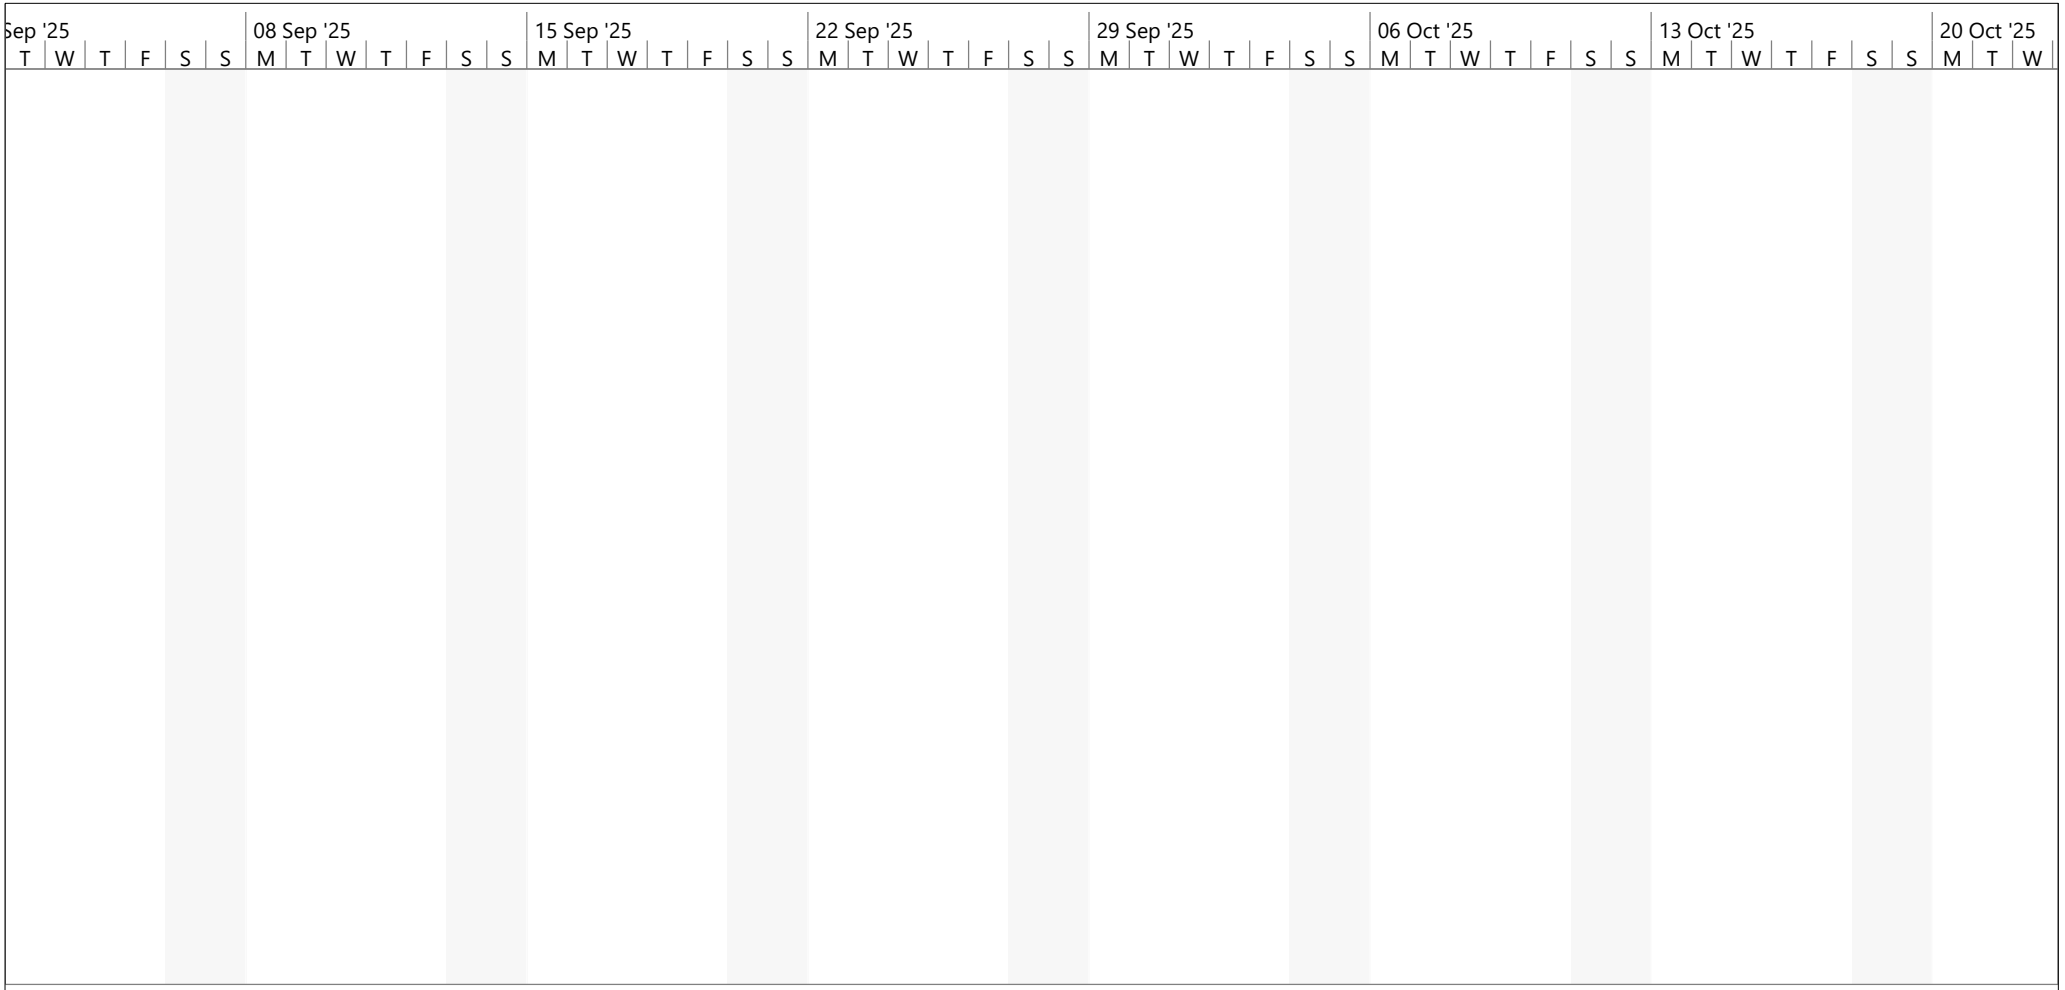


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

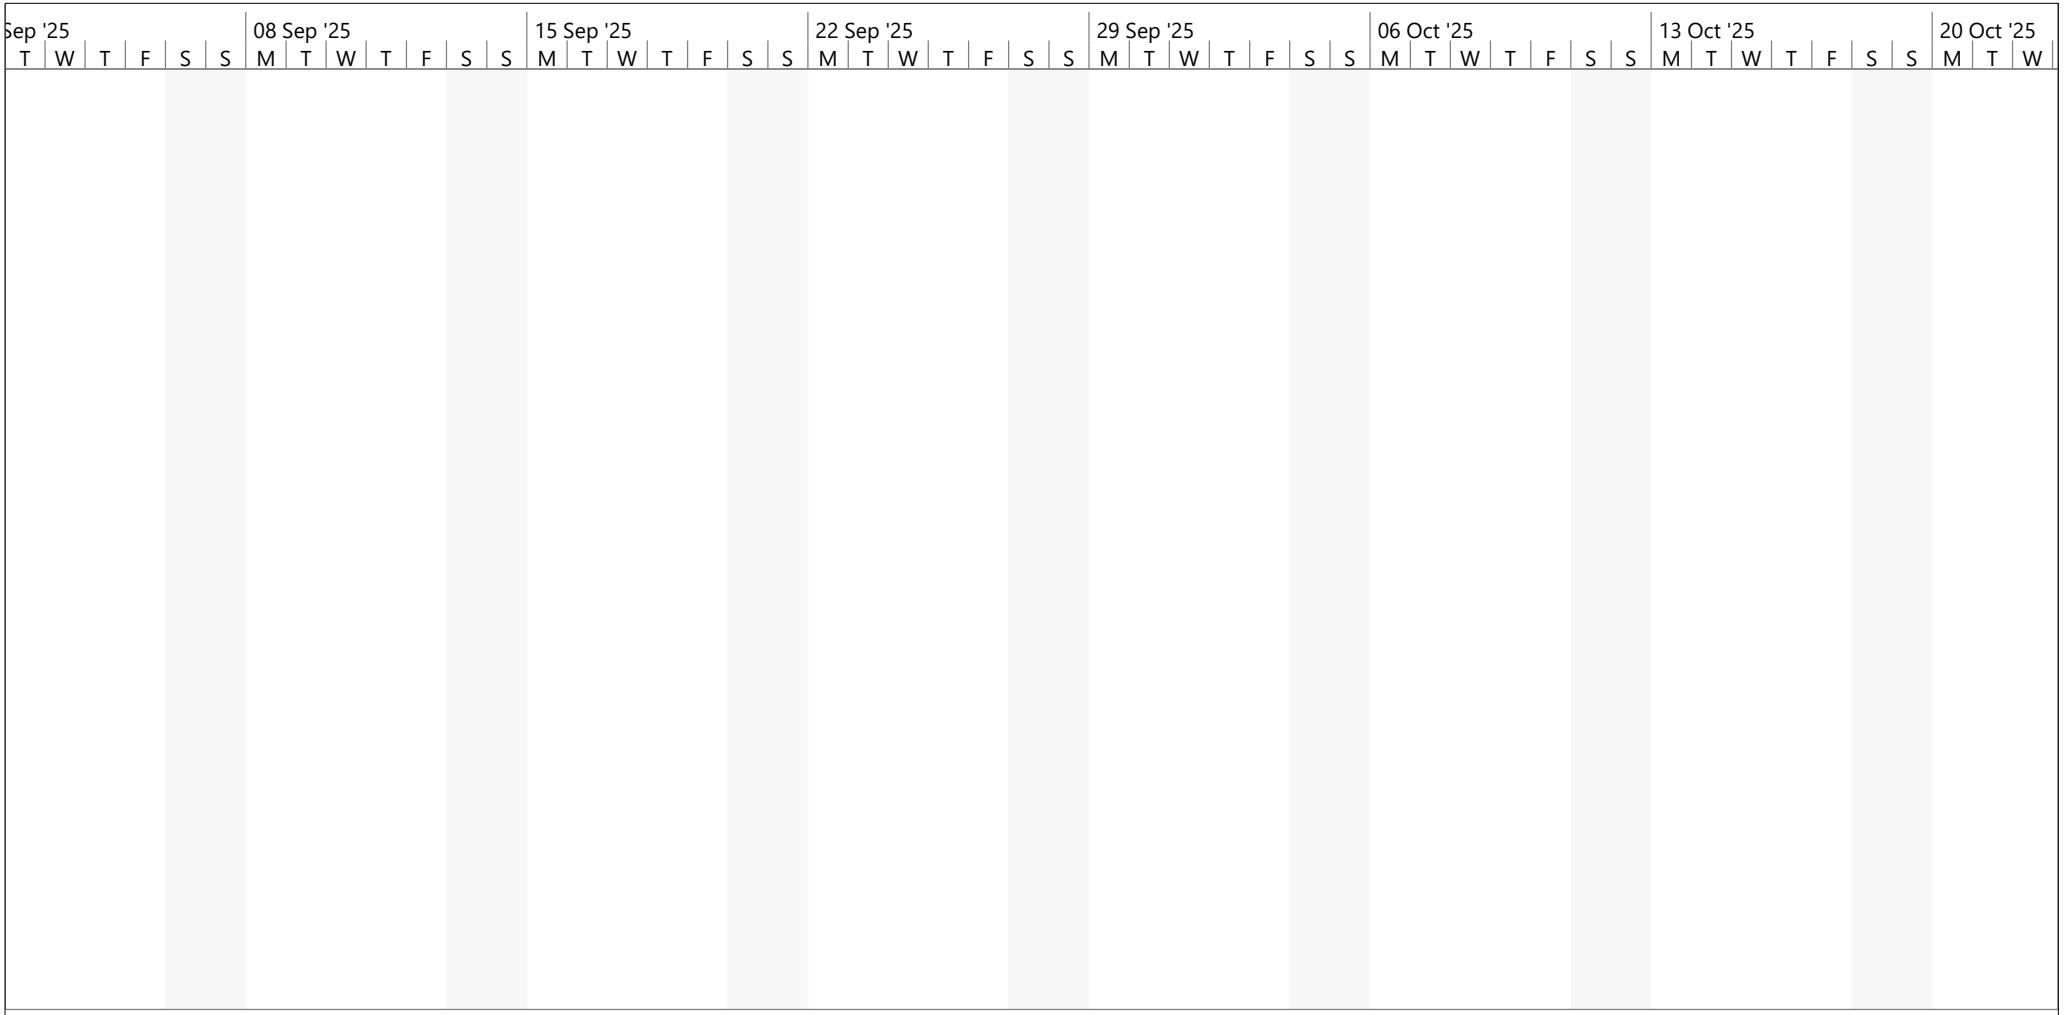


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

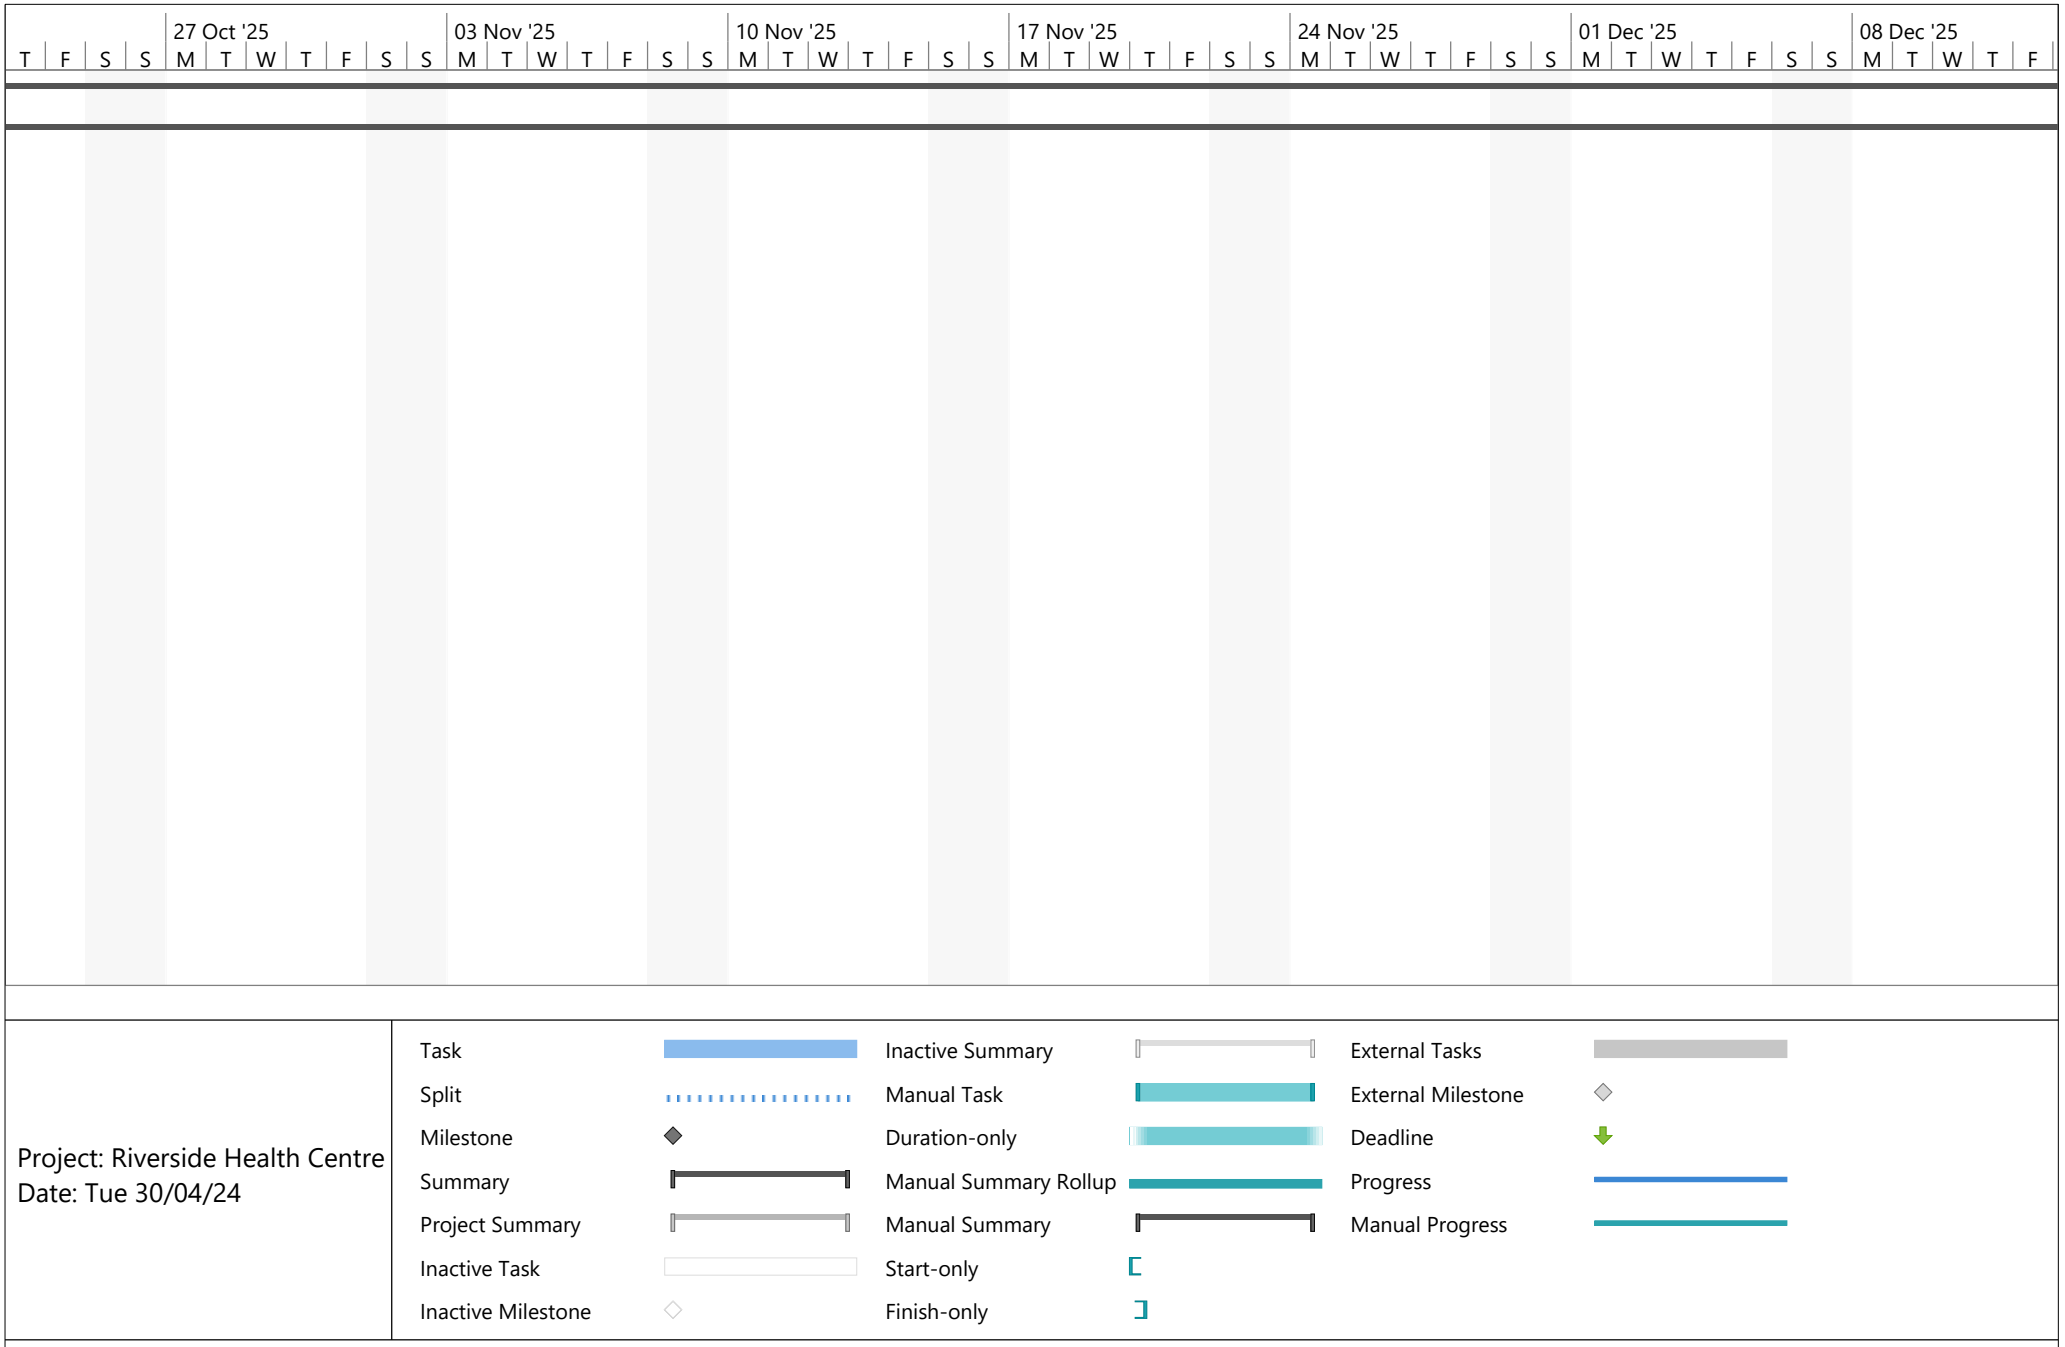


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

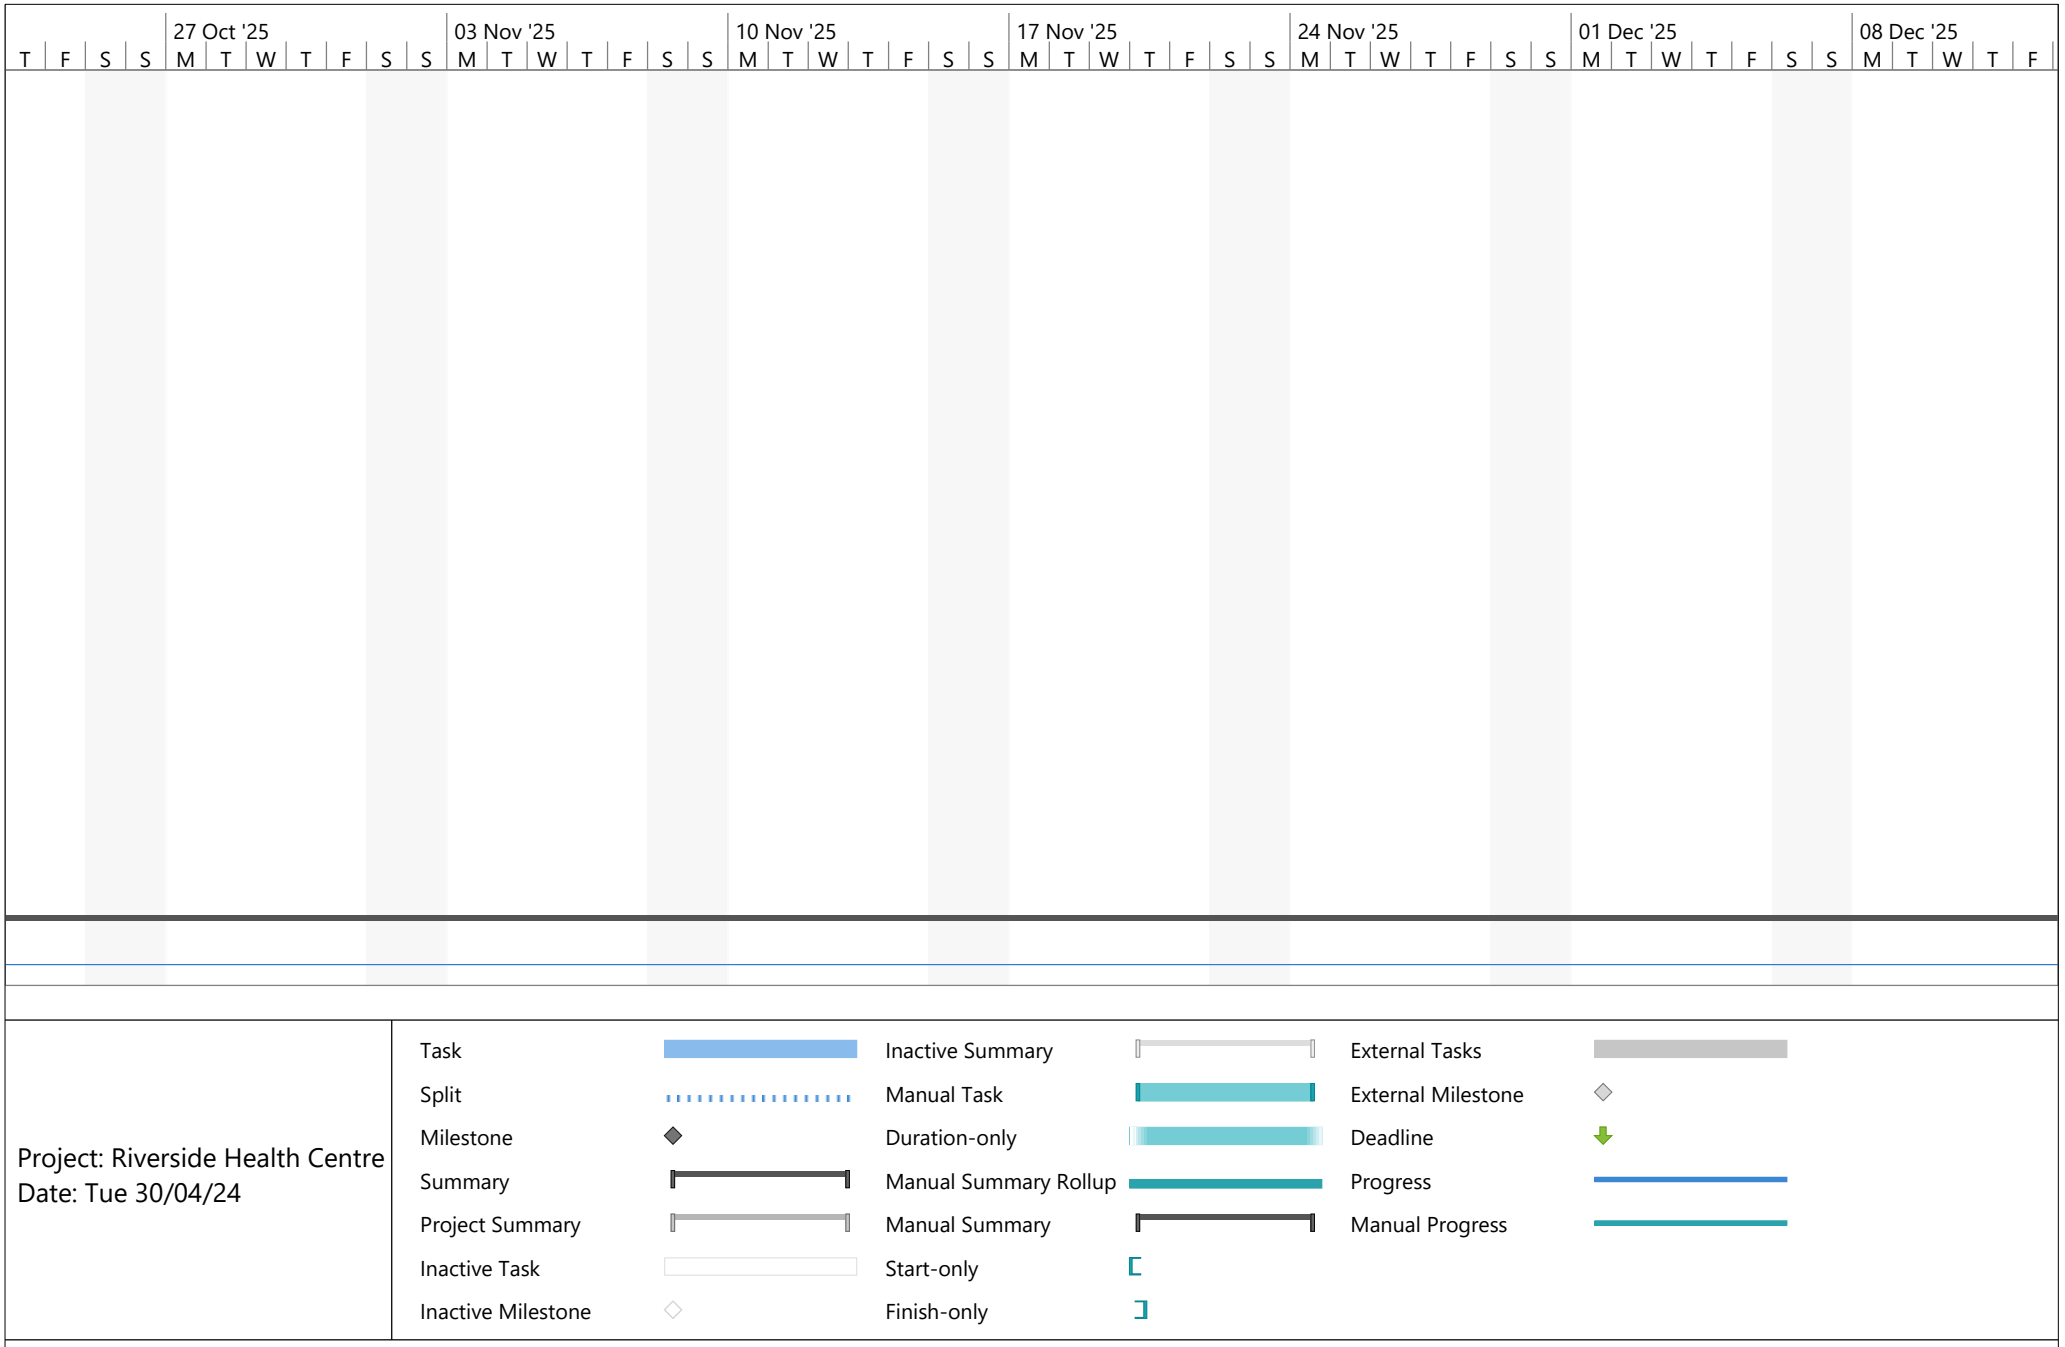

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

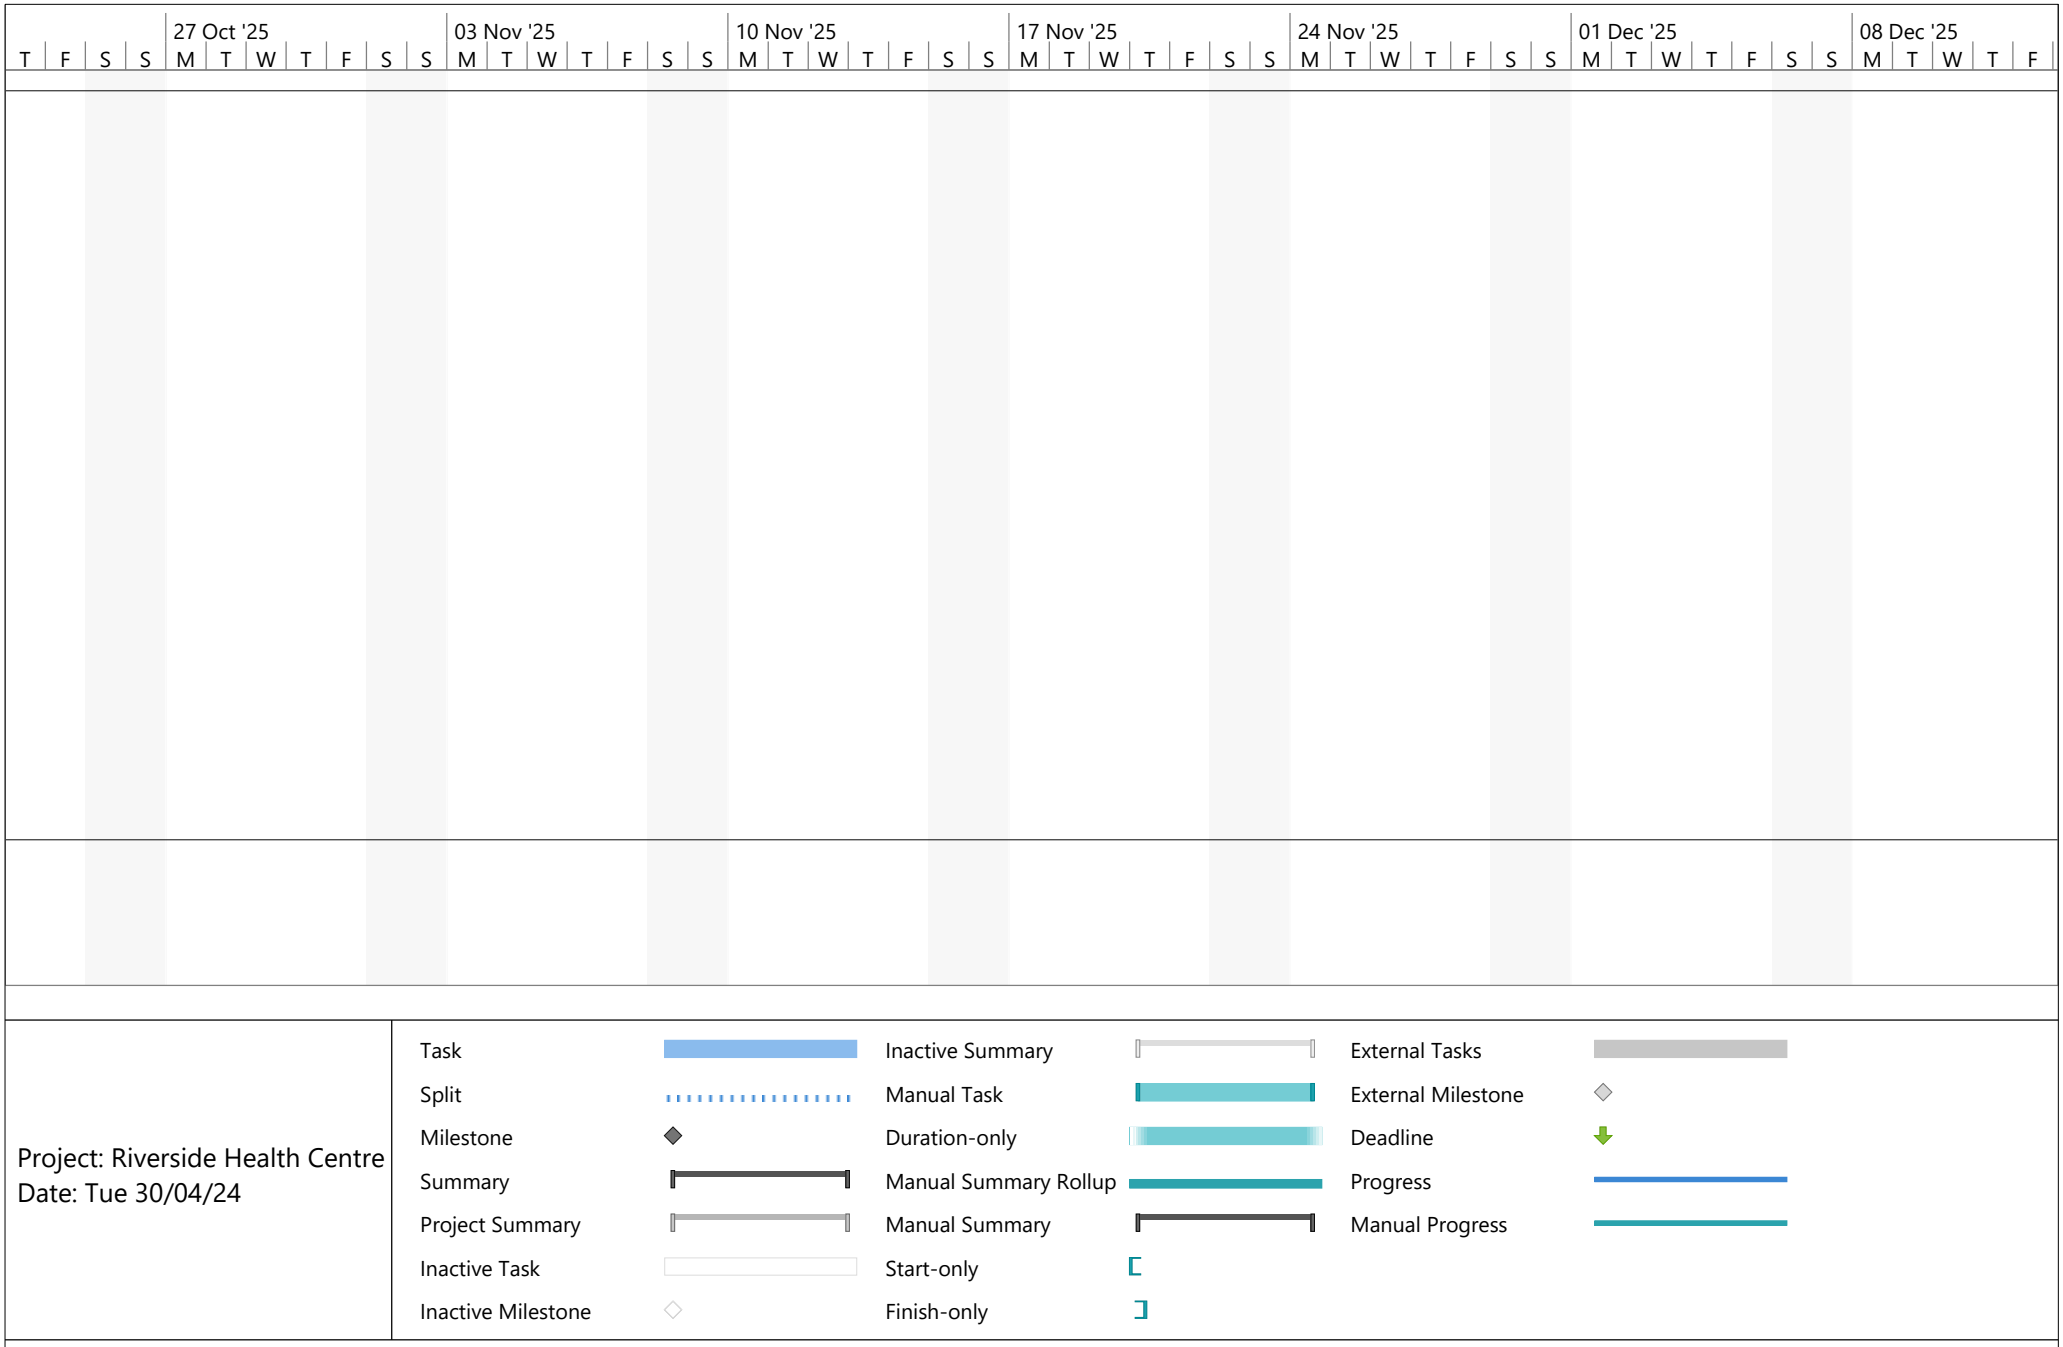


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

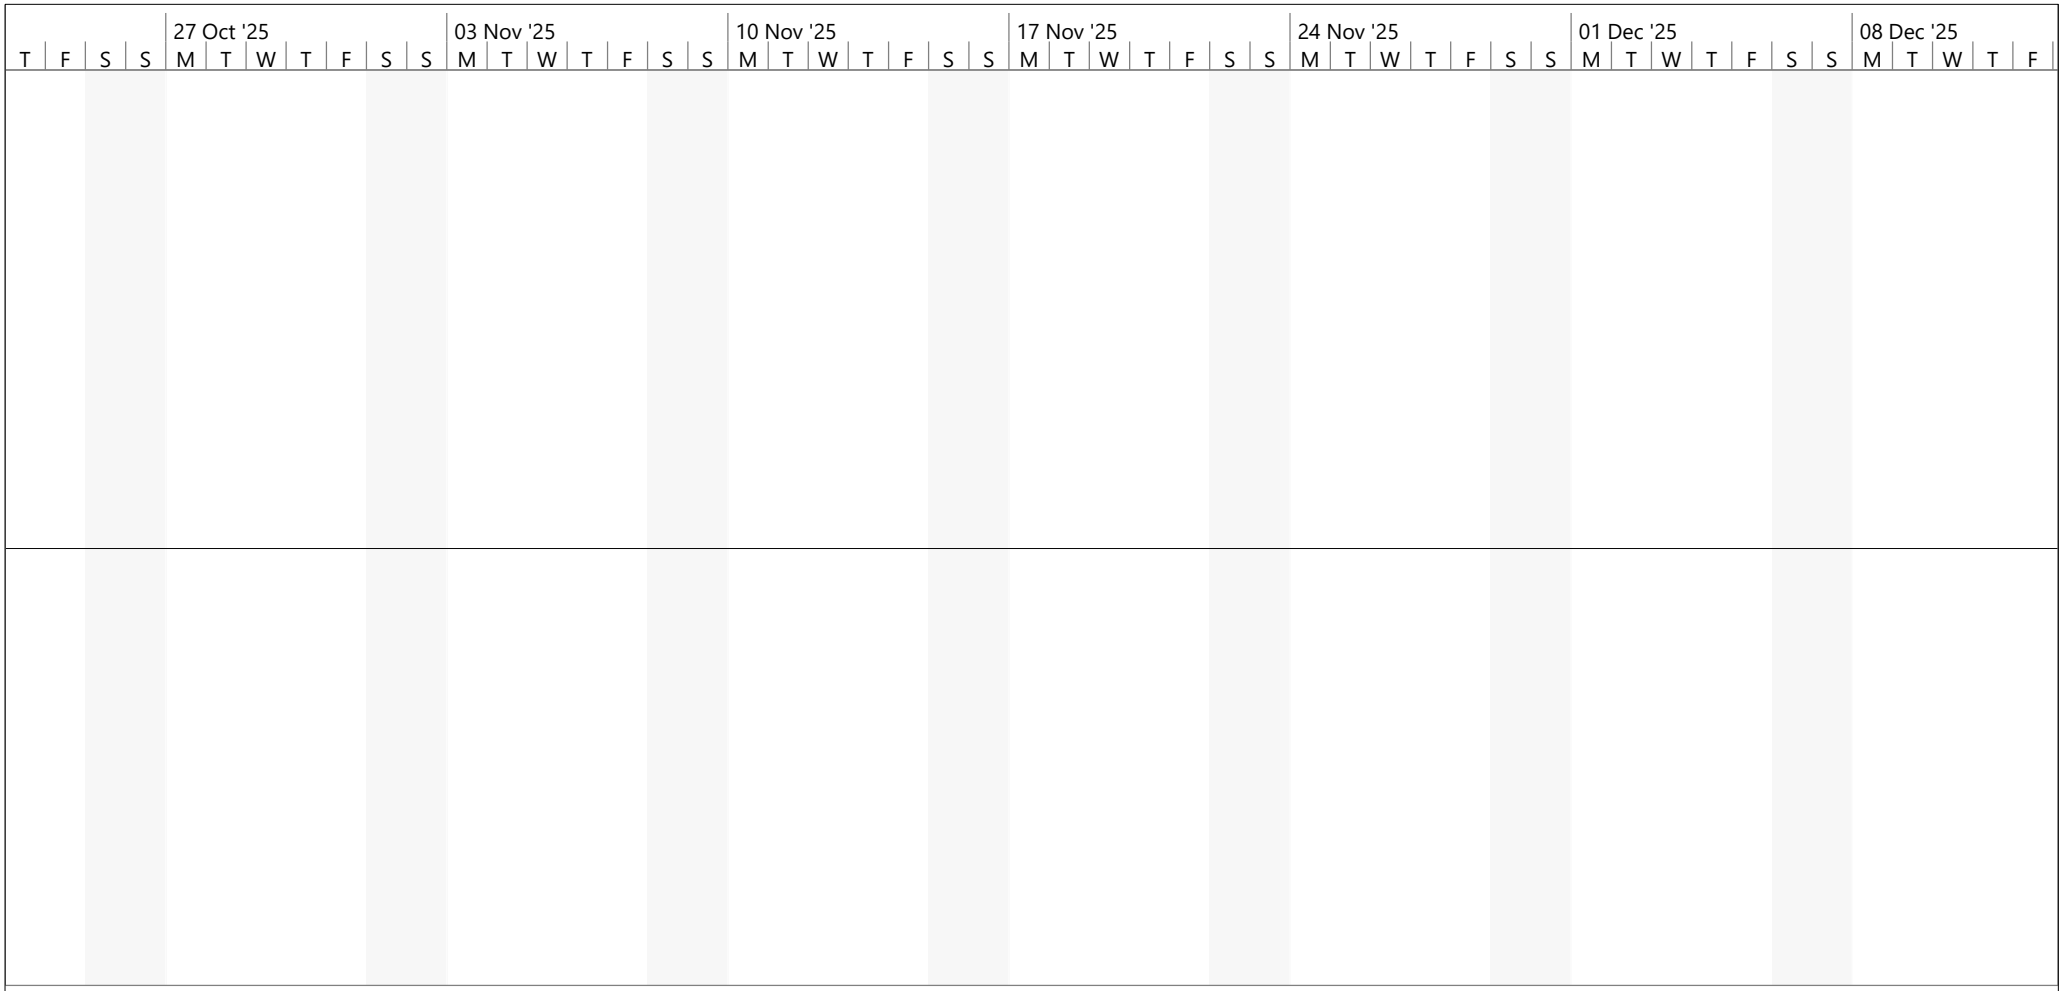

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

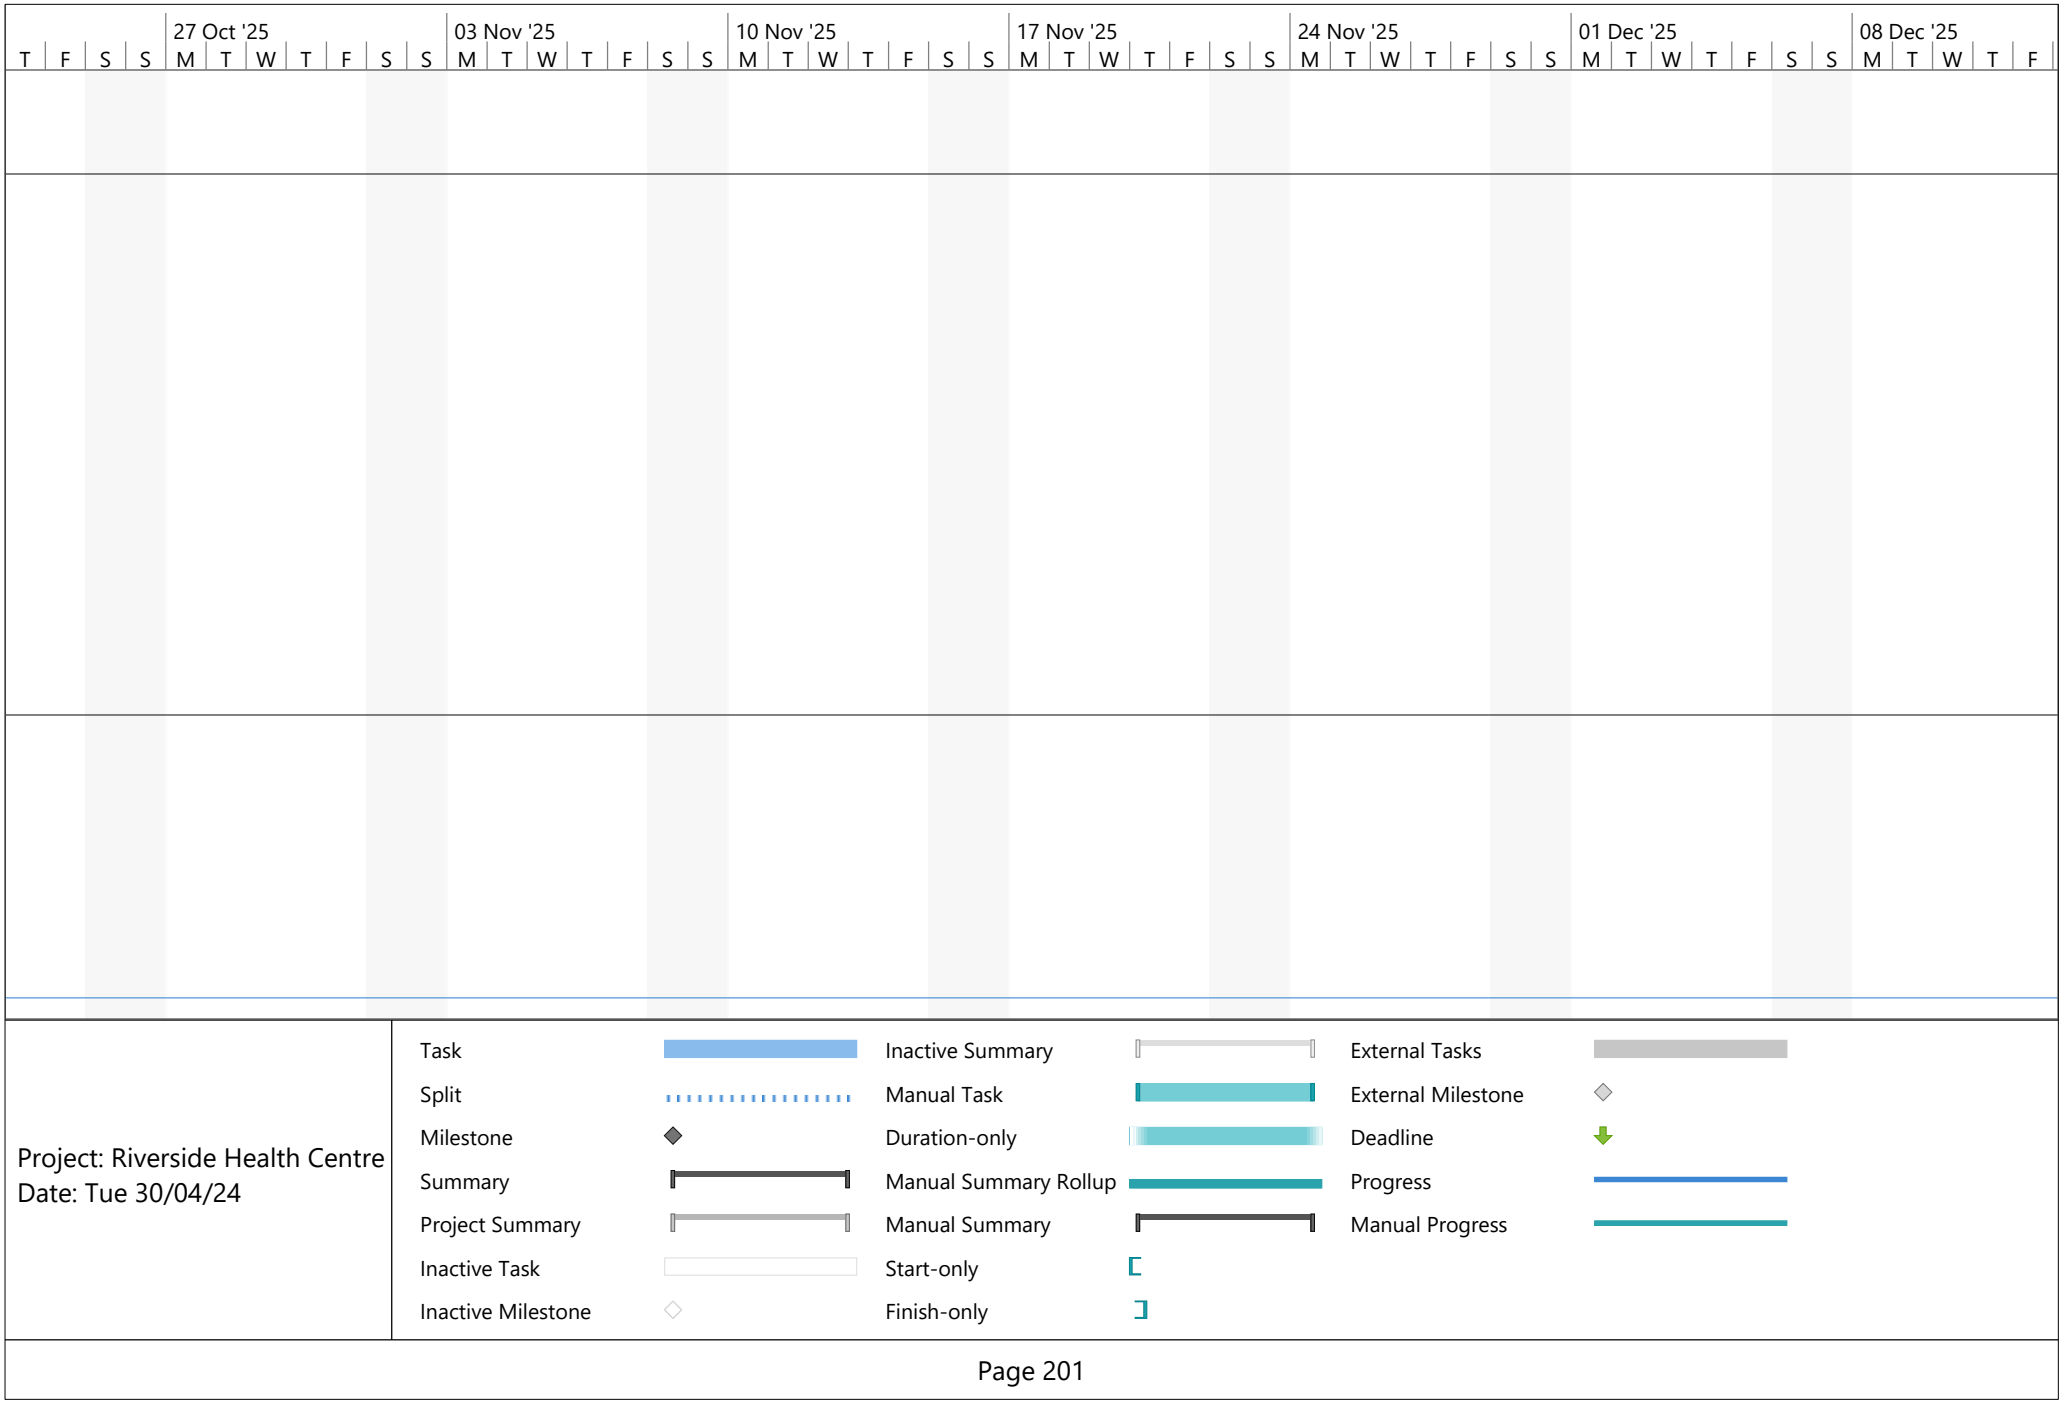
T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F
27 Oct '25
03 Nov '25
10 Nov '25
17 Nov '25
24 Nov '25
01 Dec '25
08 Dec '25
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

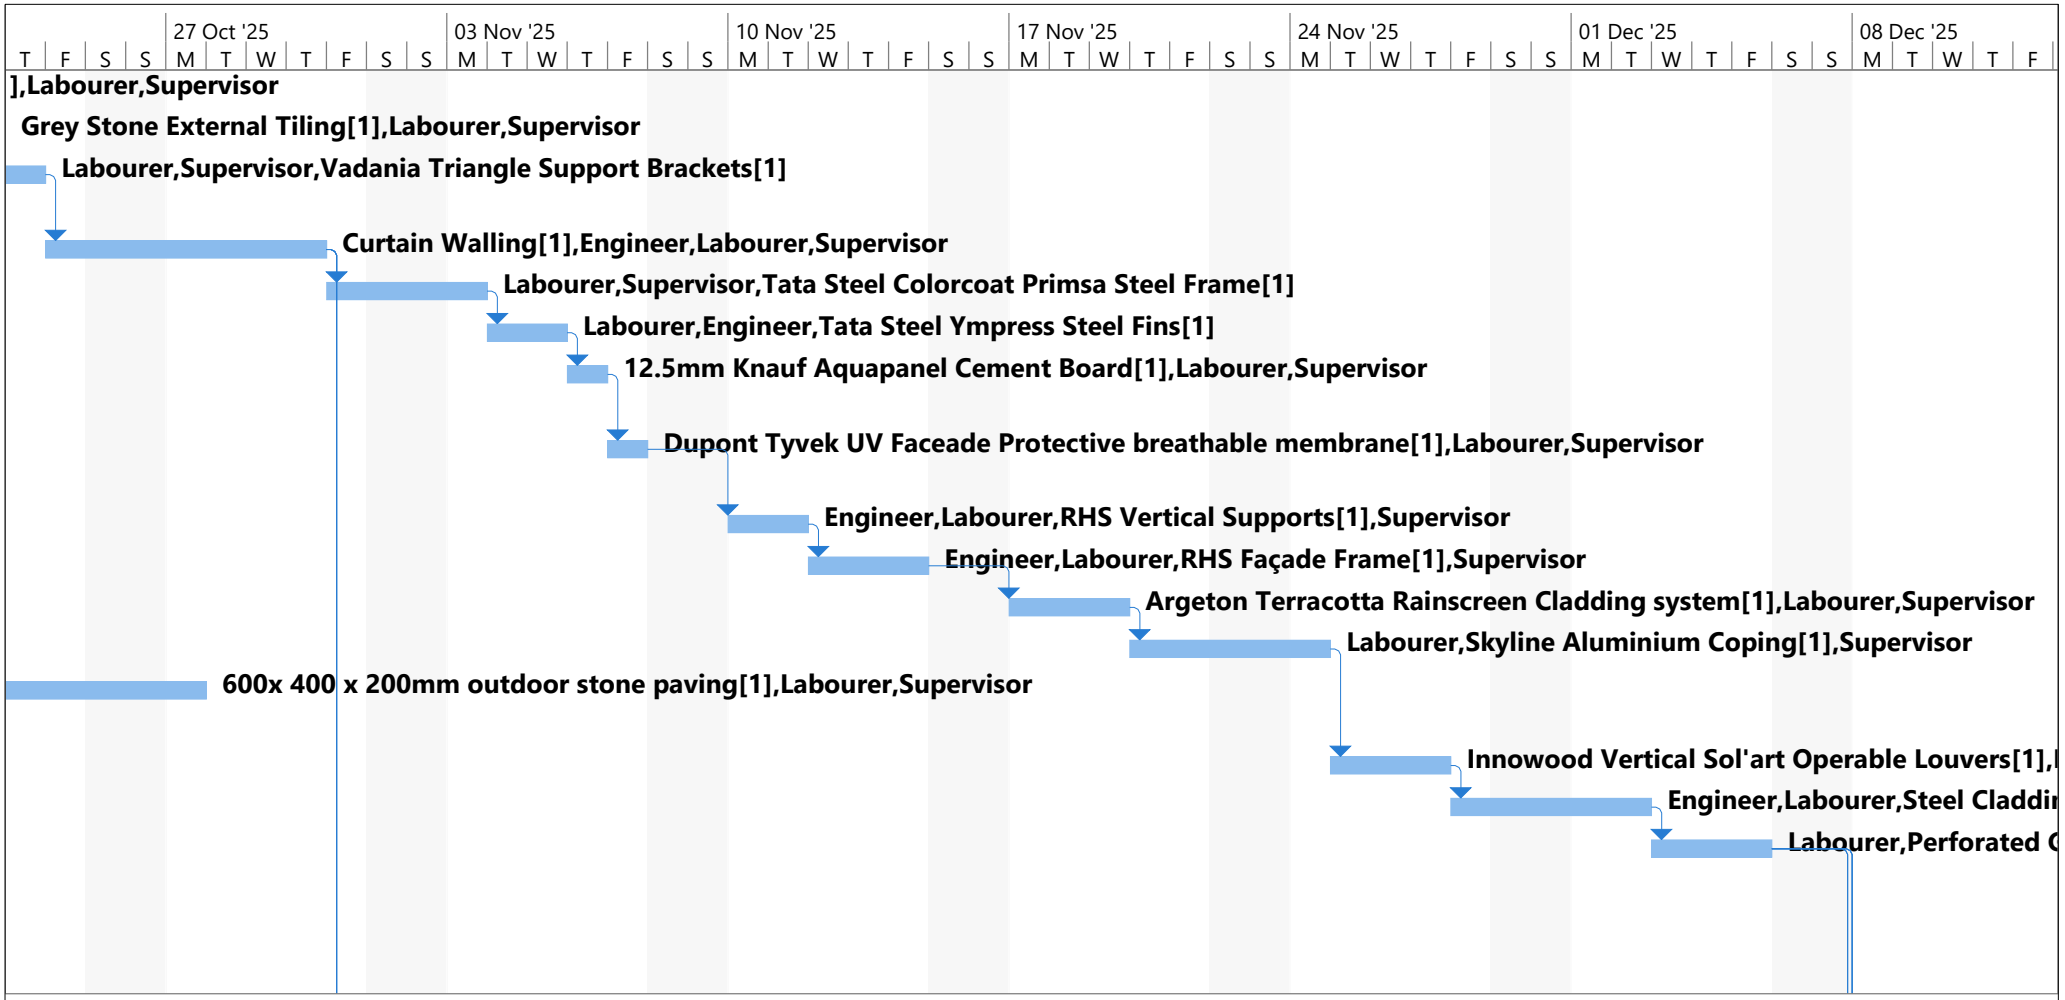


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

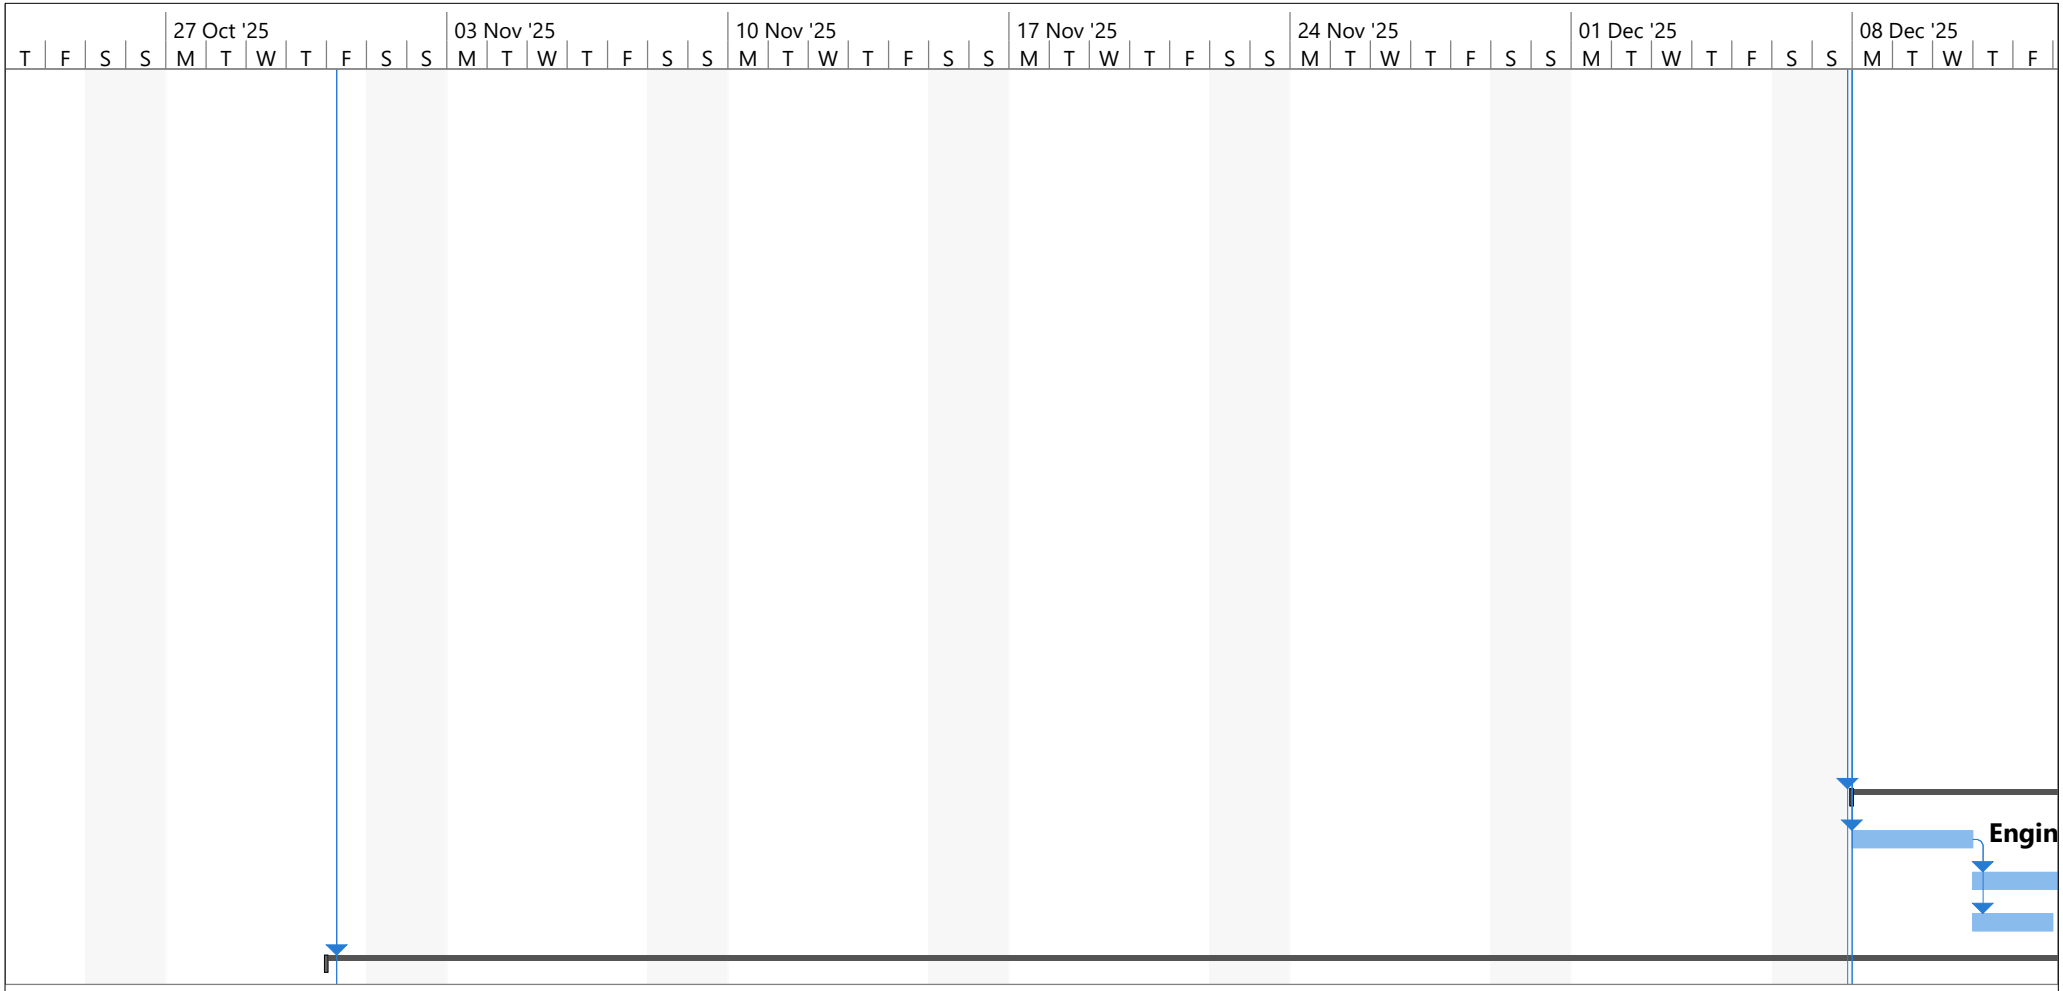


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

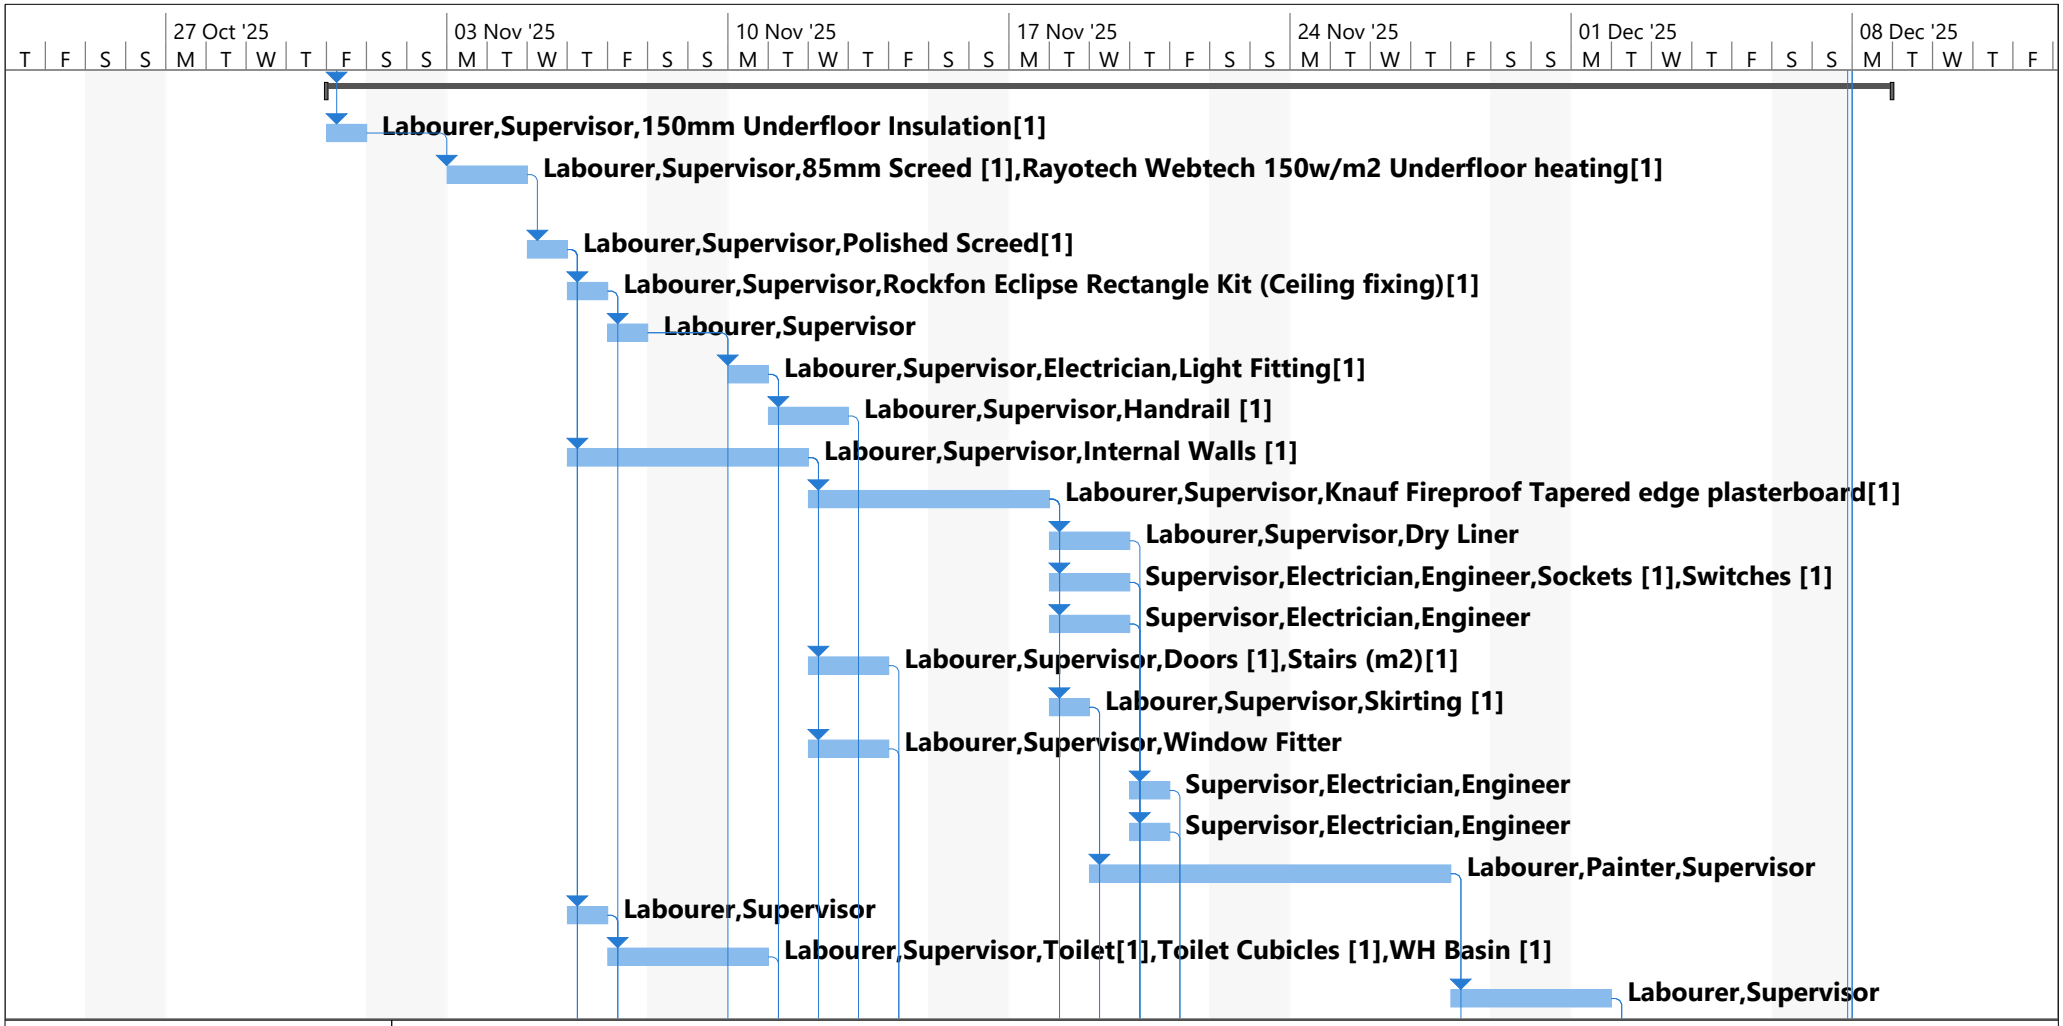


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

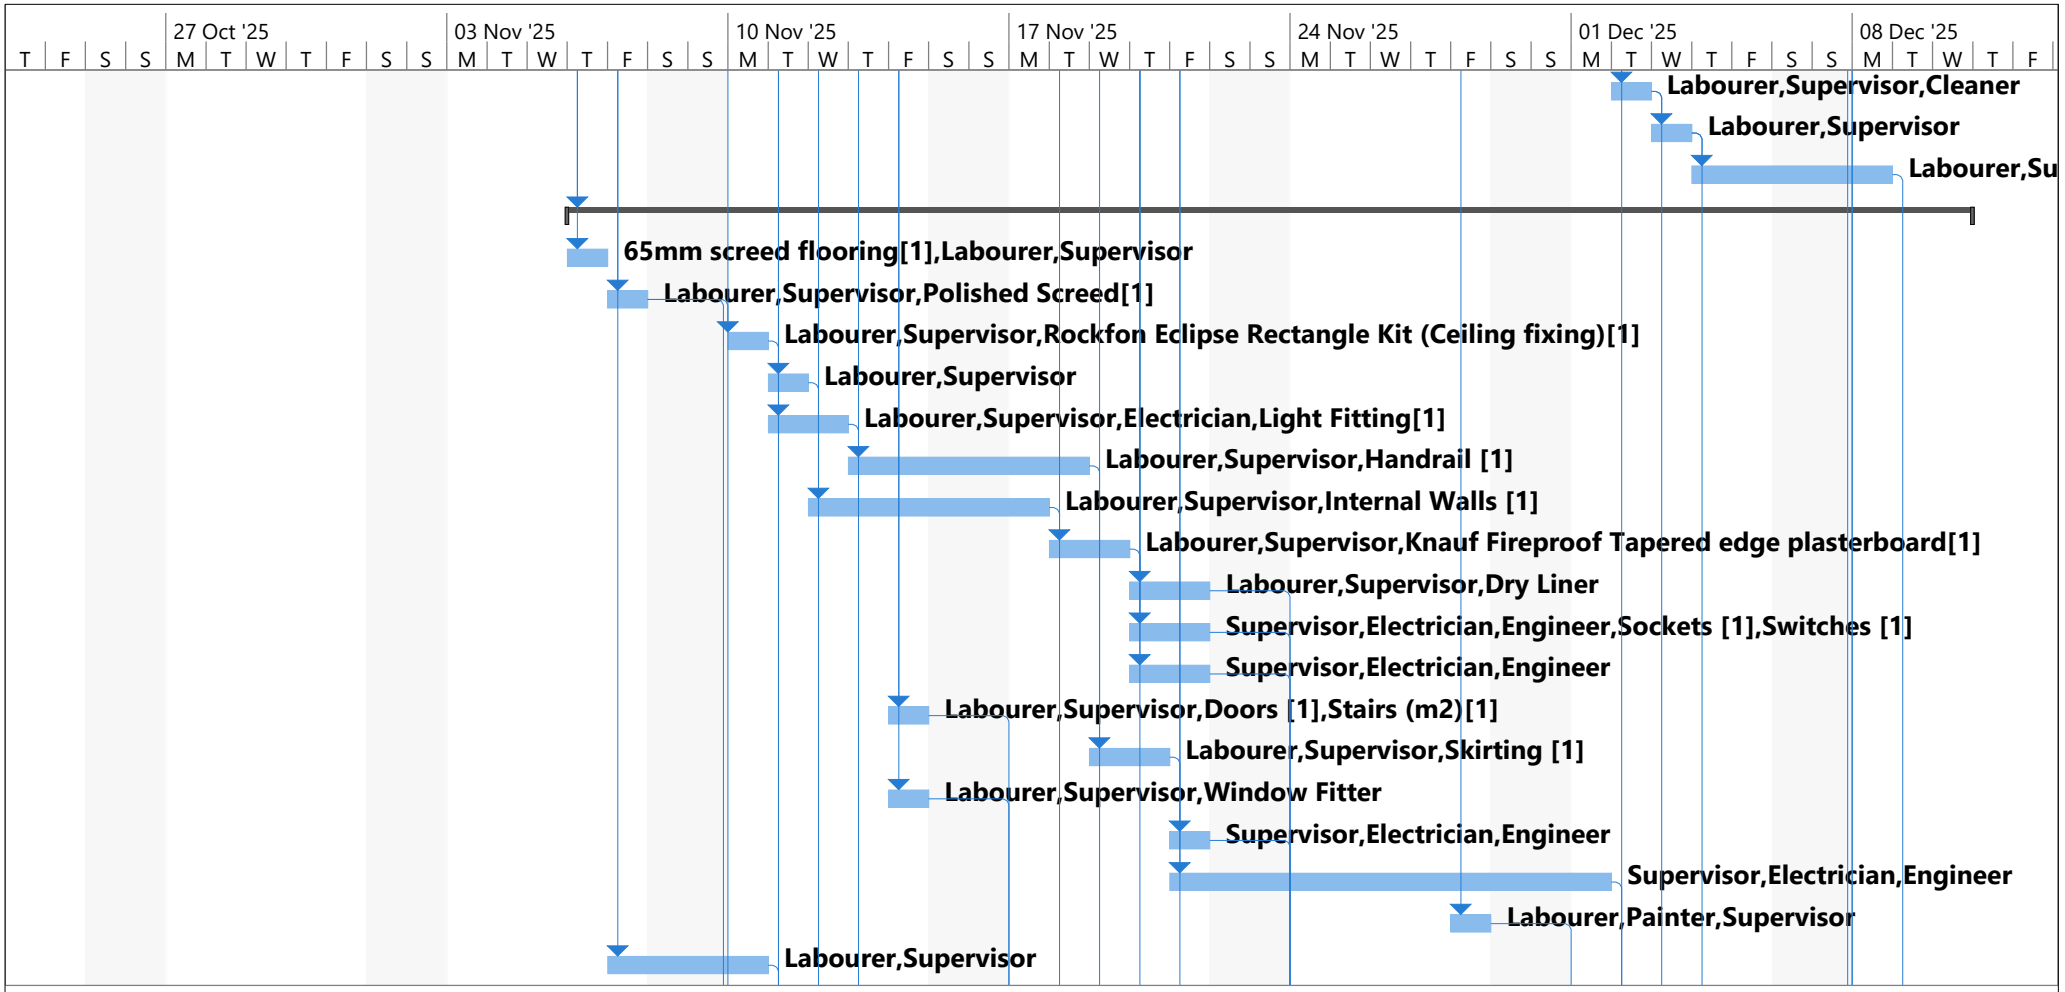


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

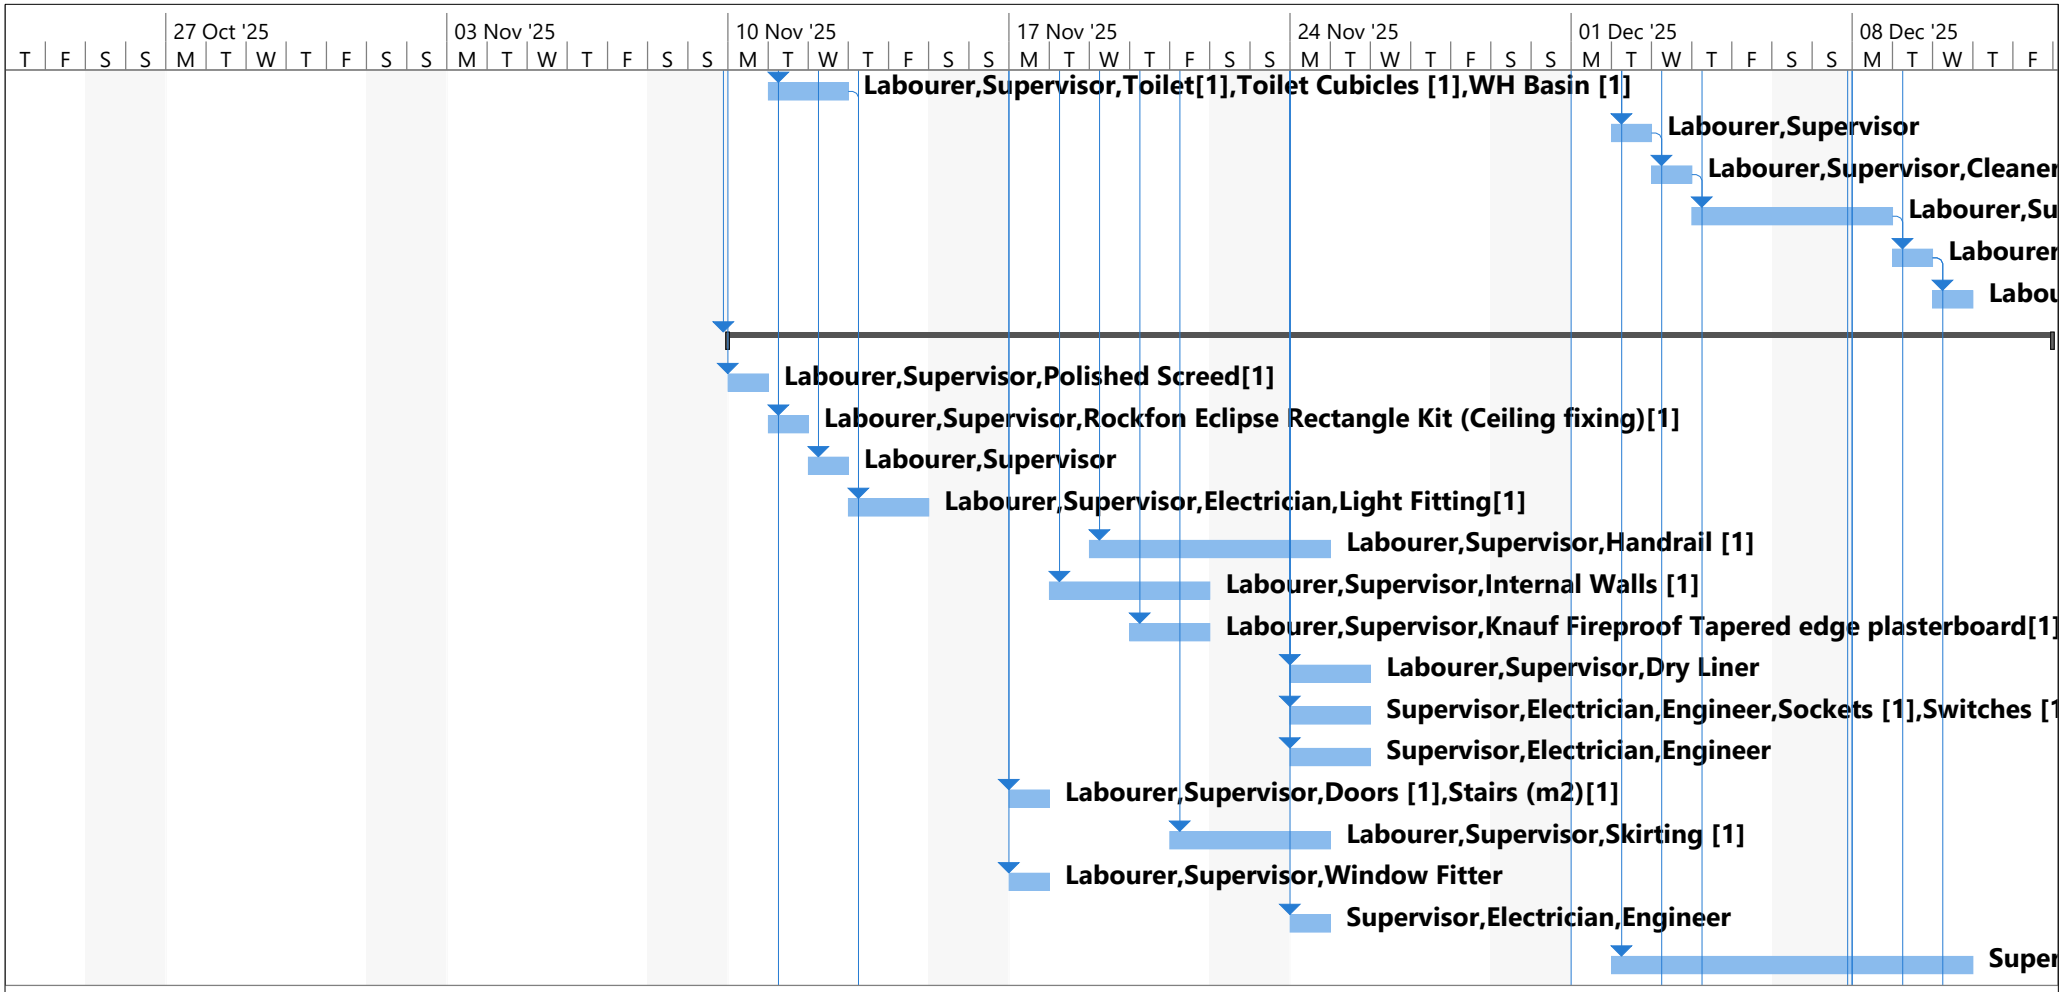


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

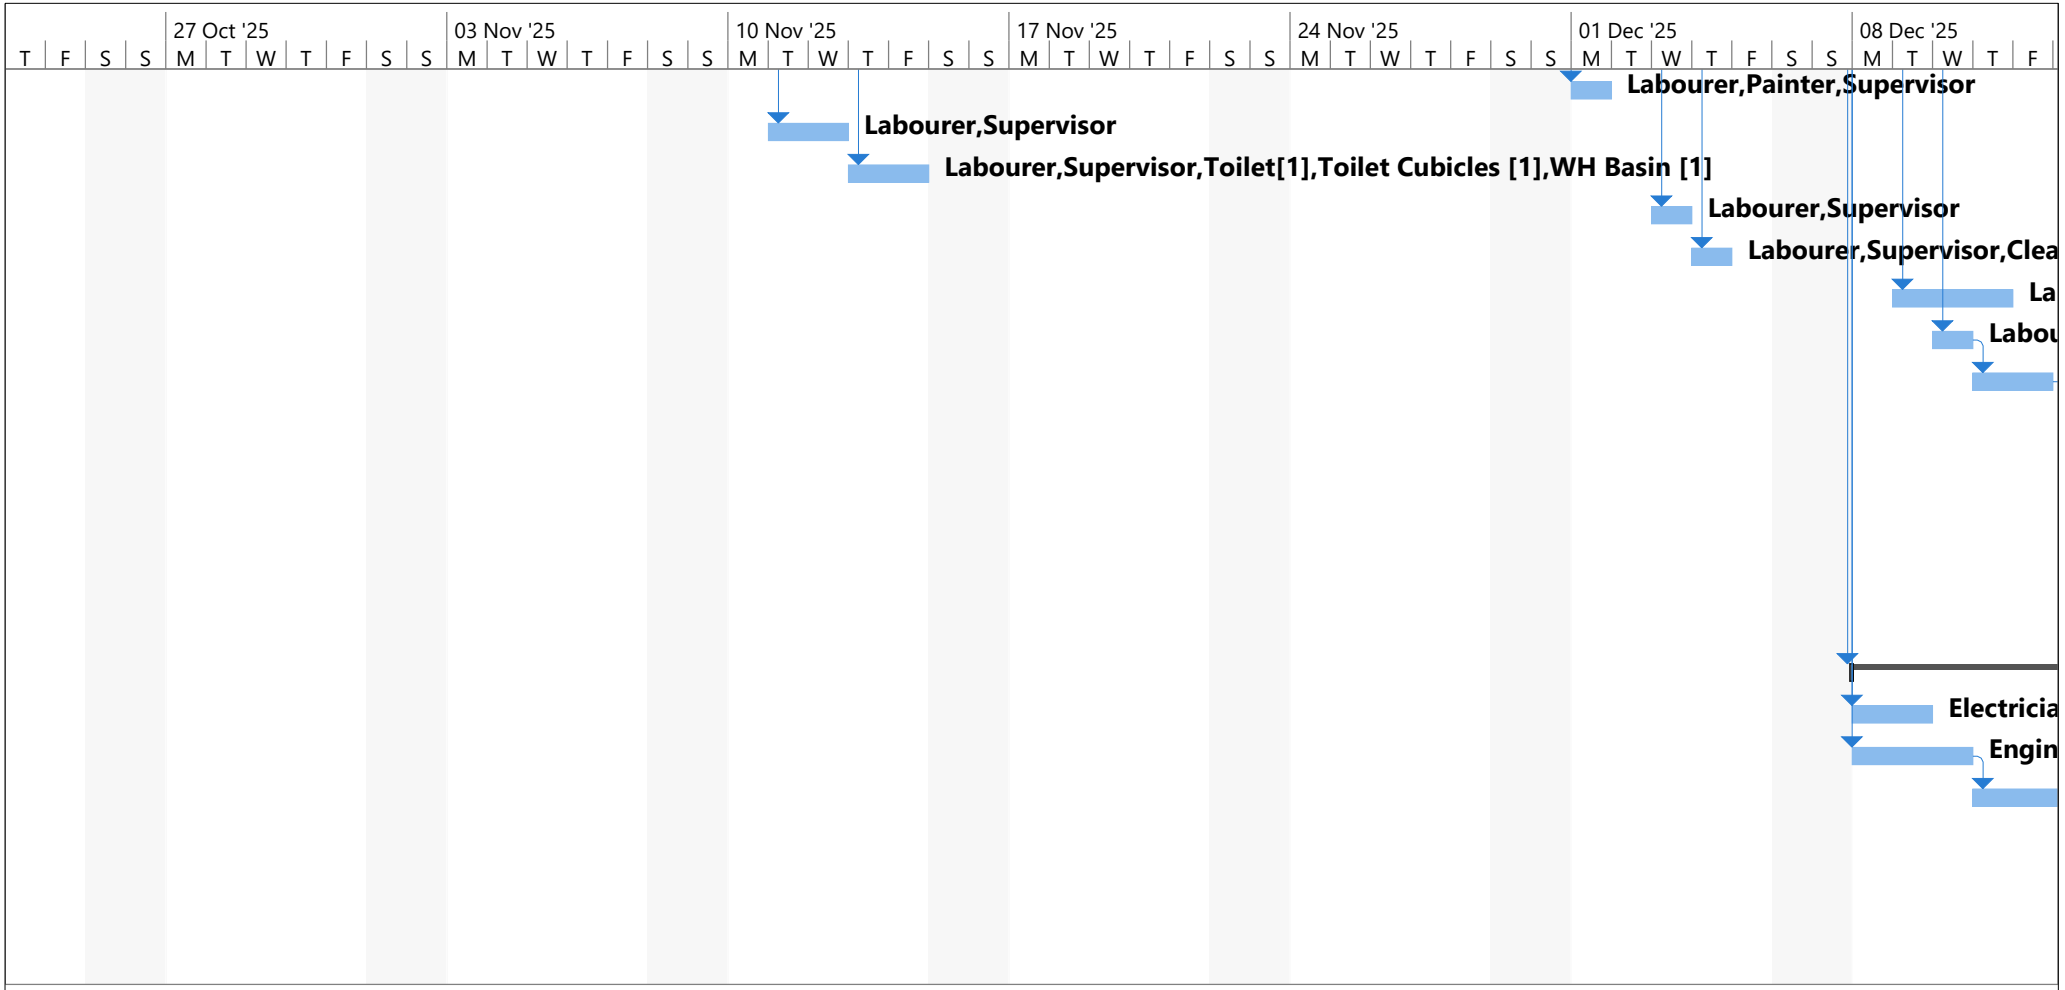


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

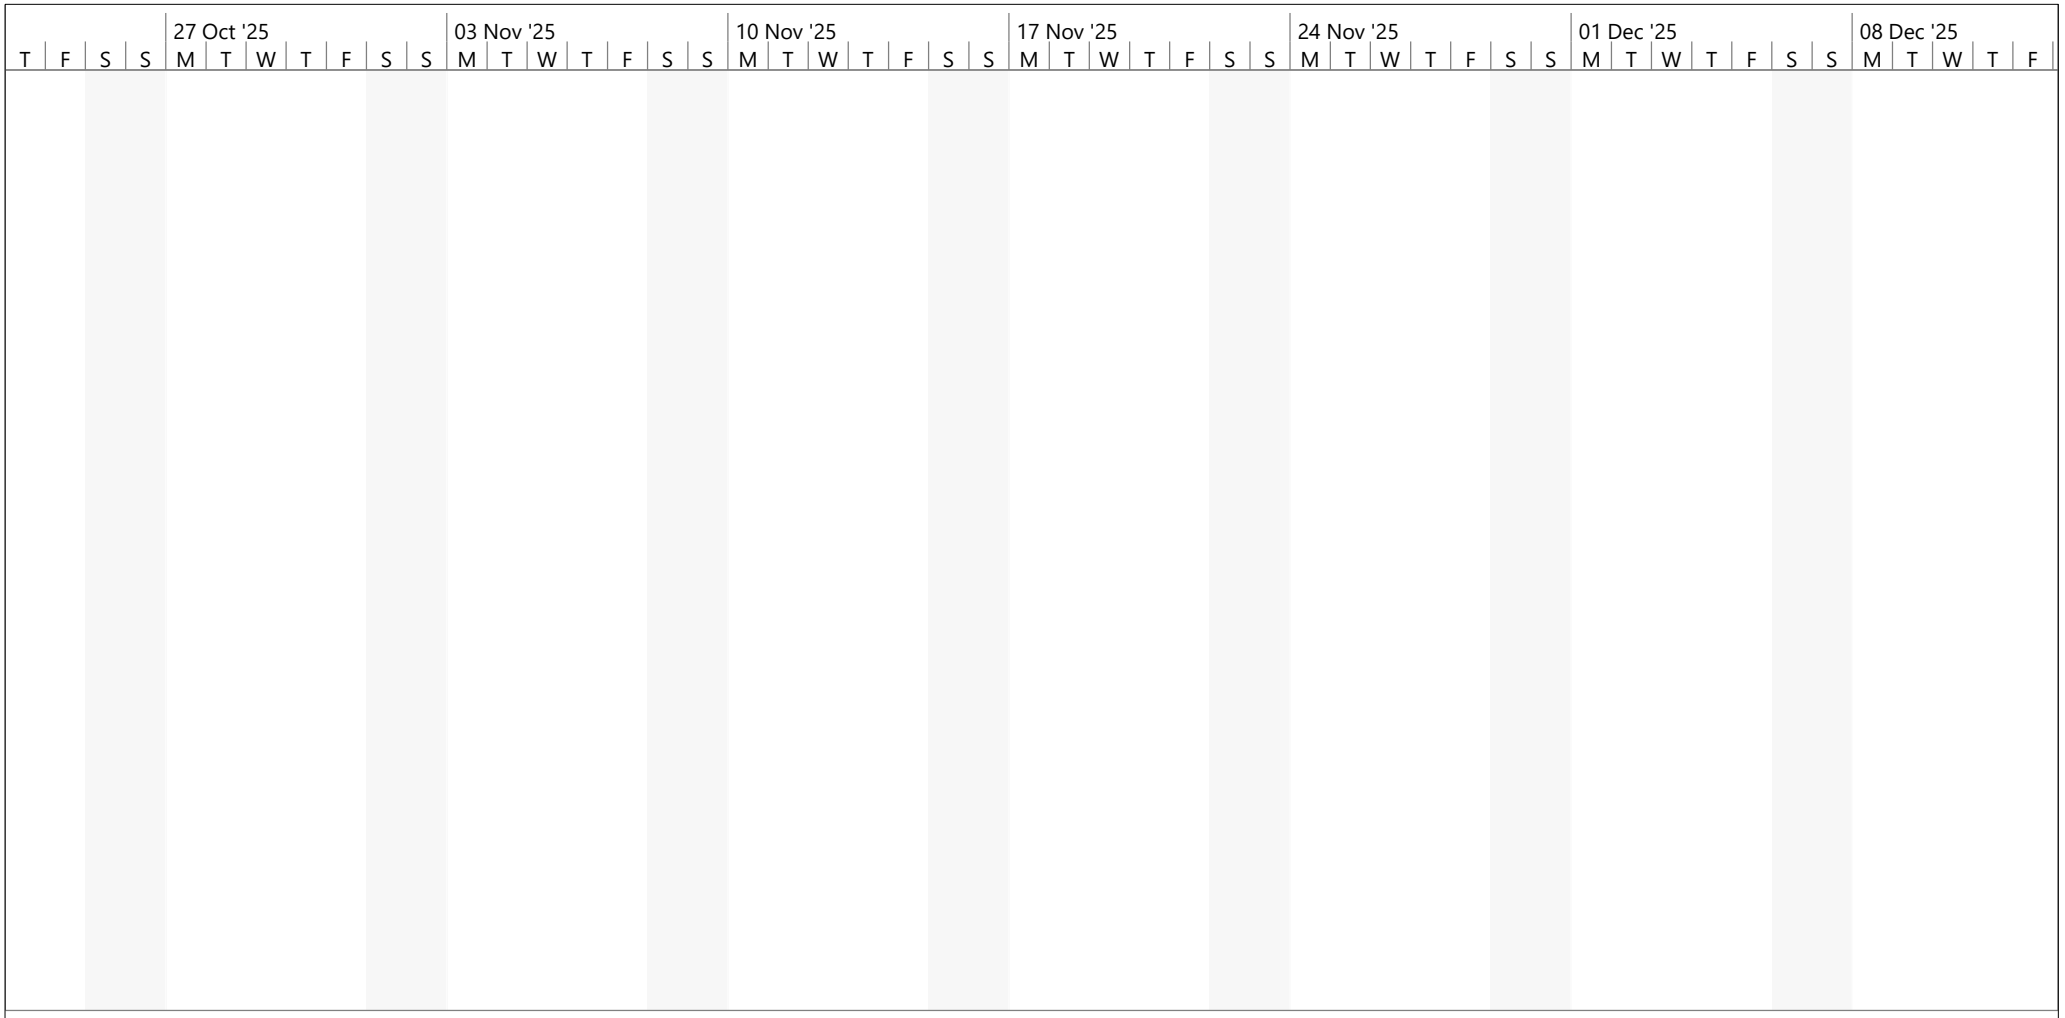


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

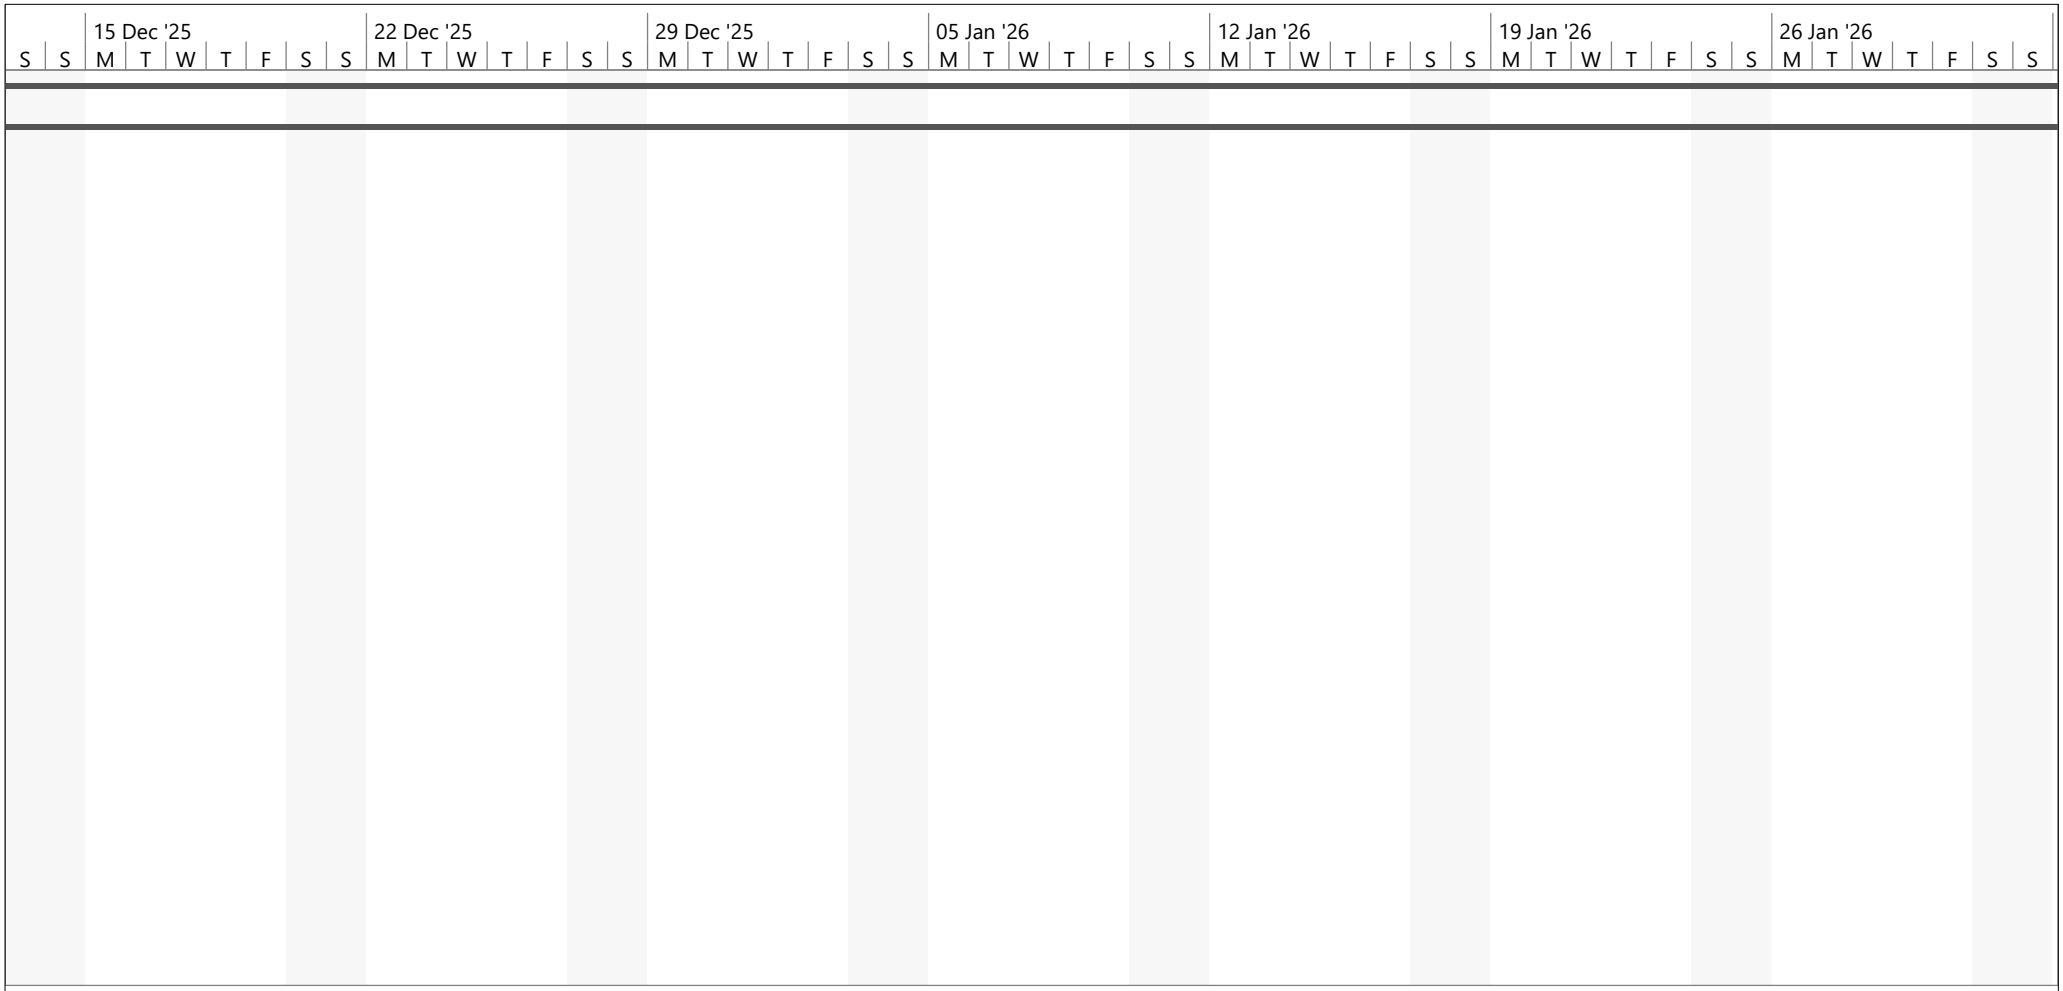


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

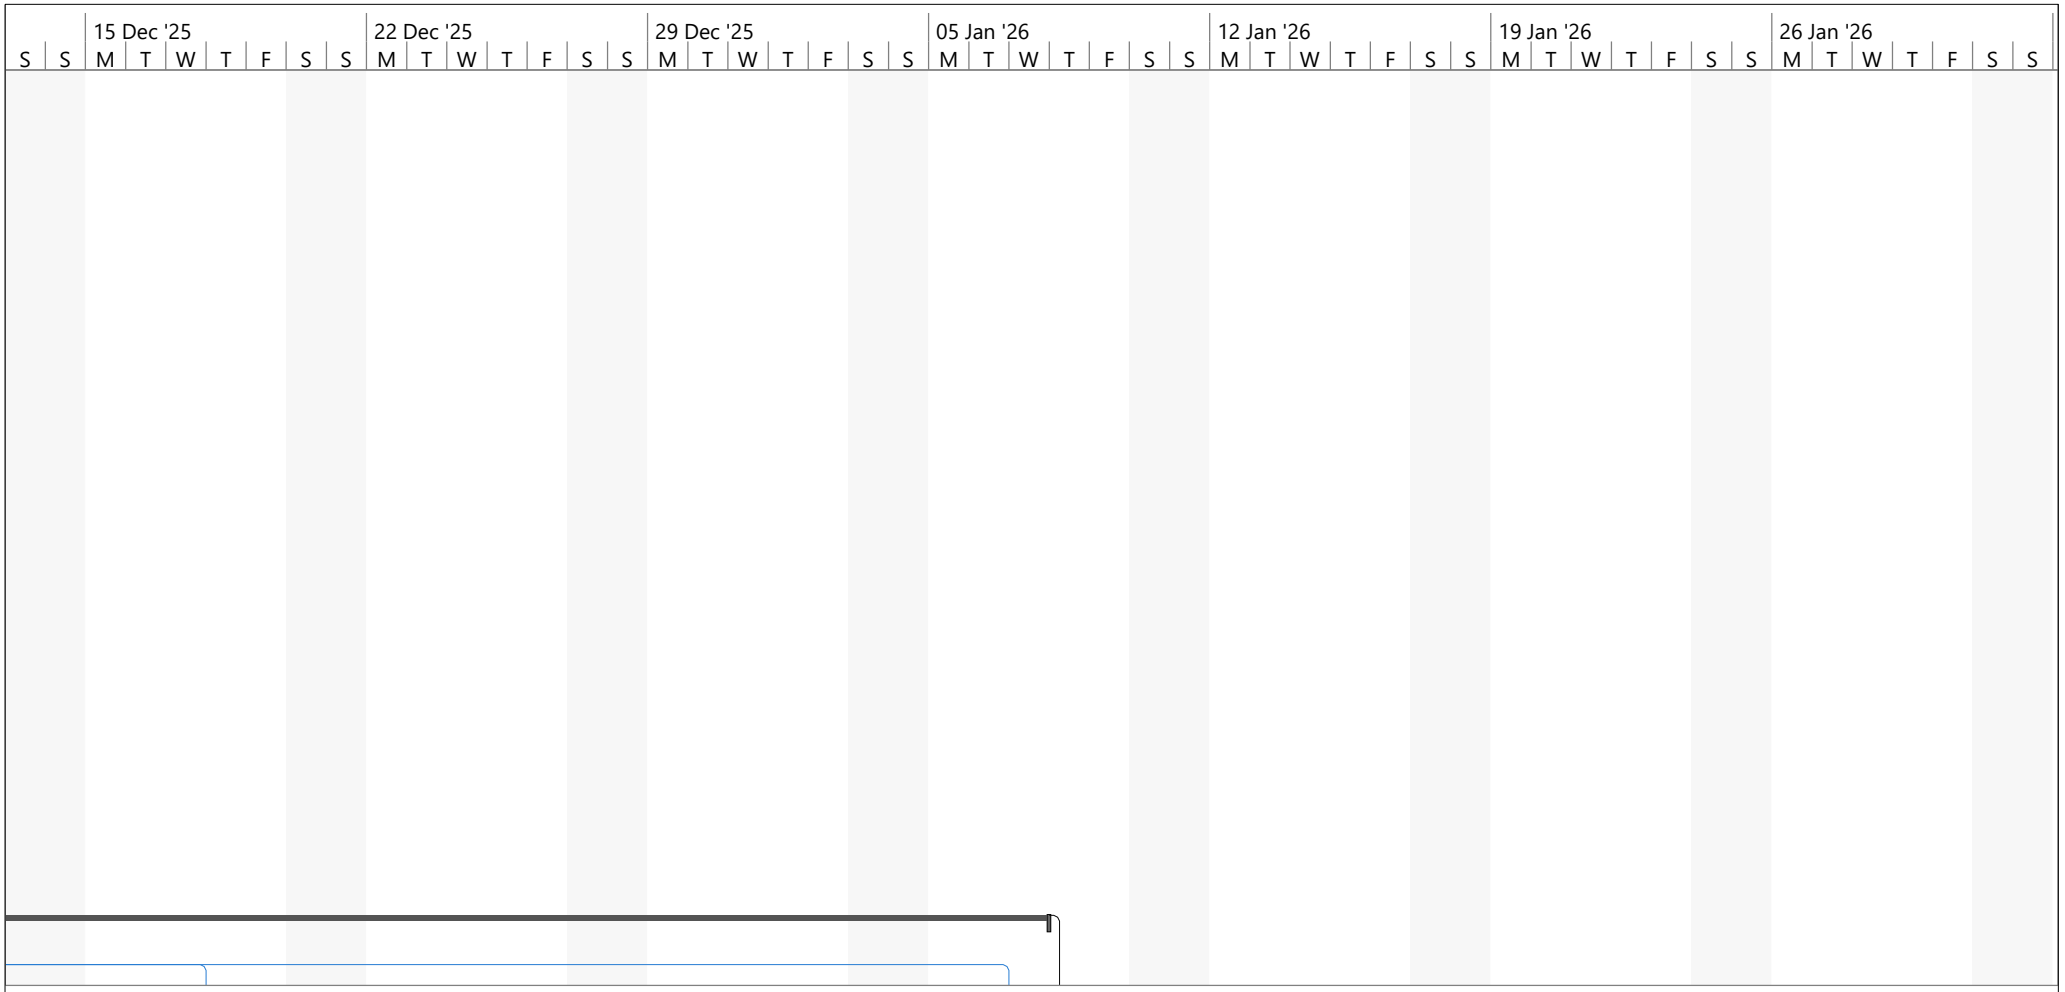


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

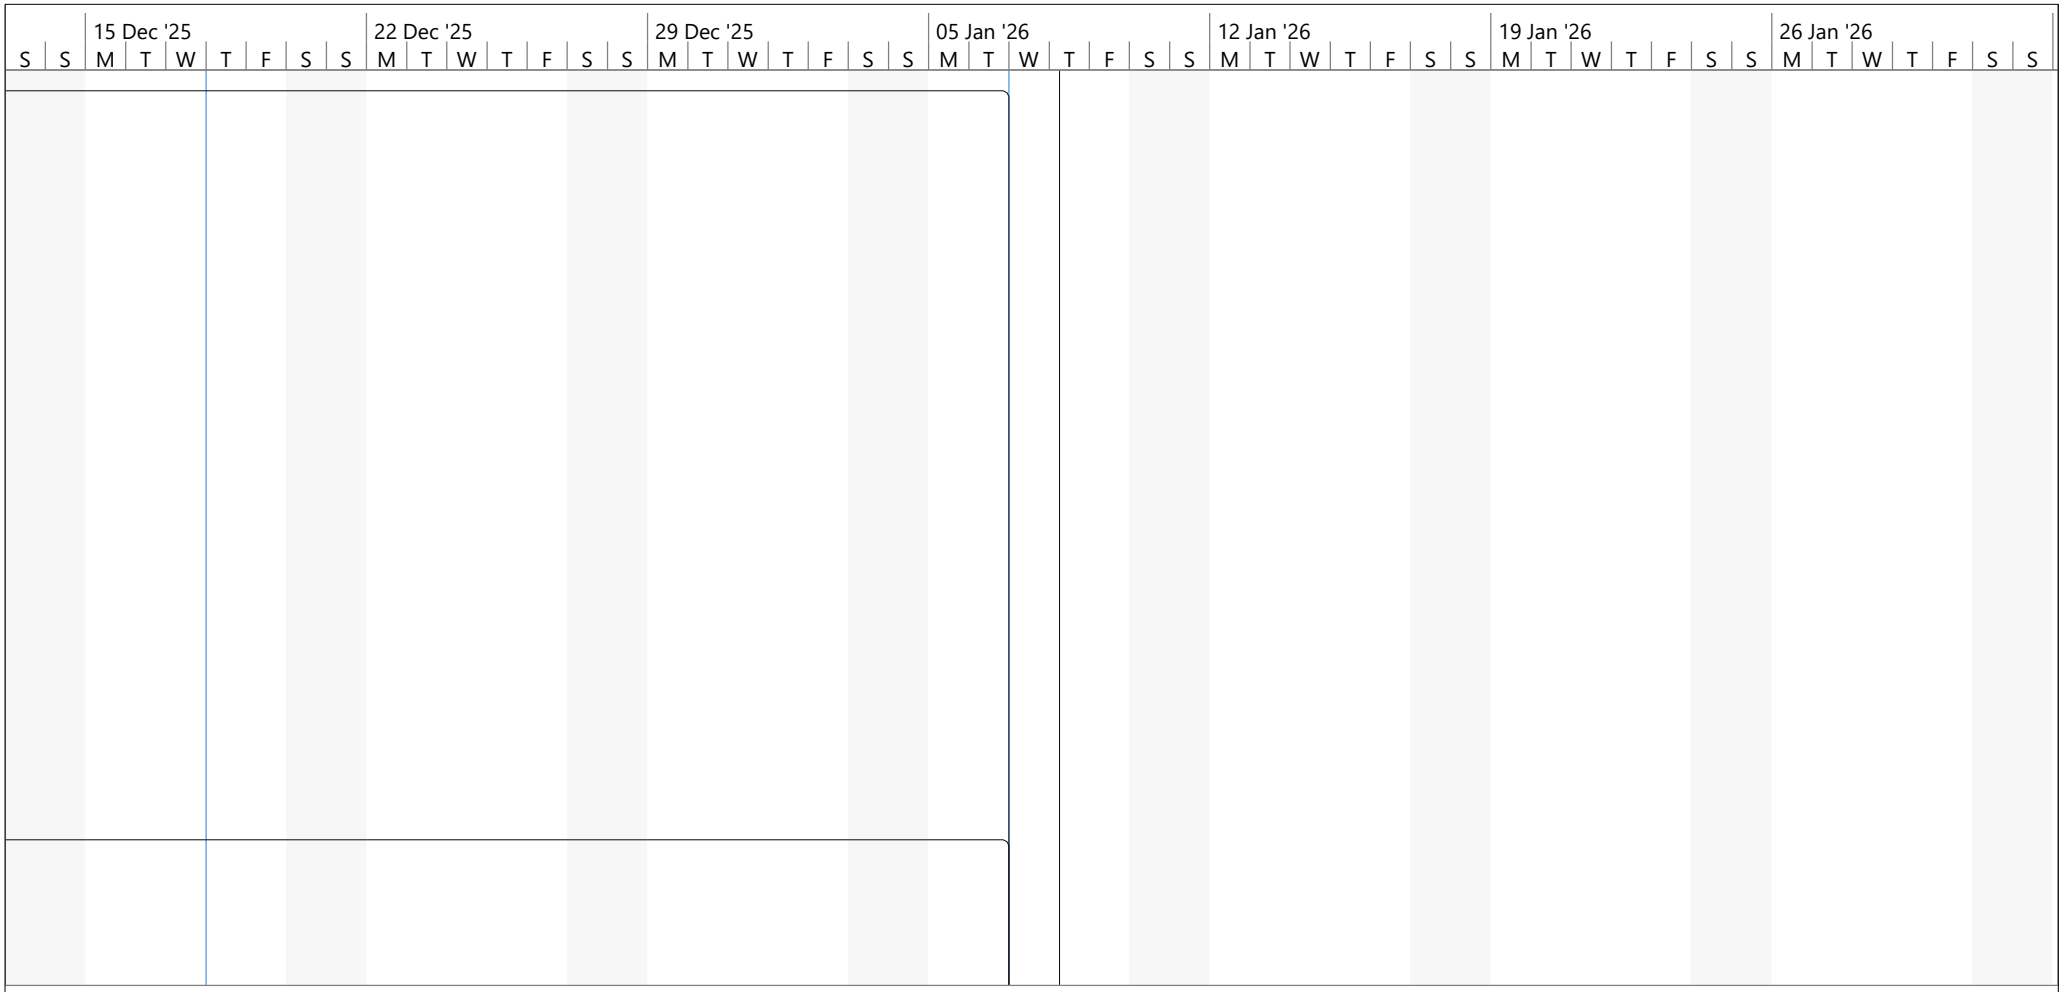


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

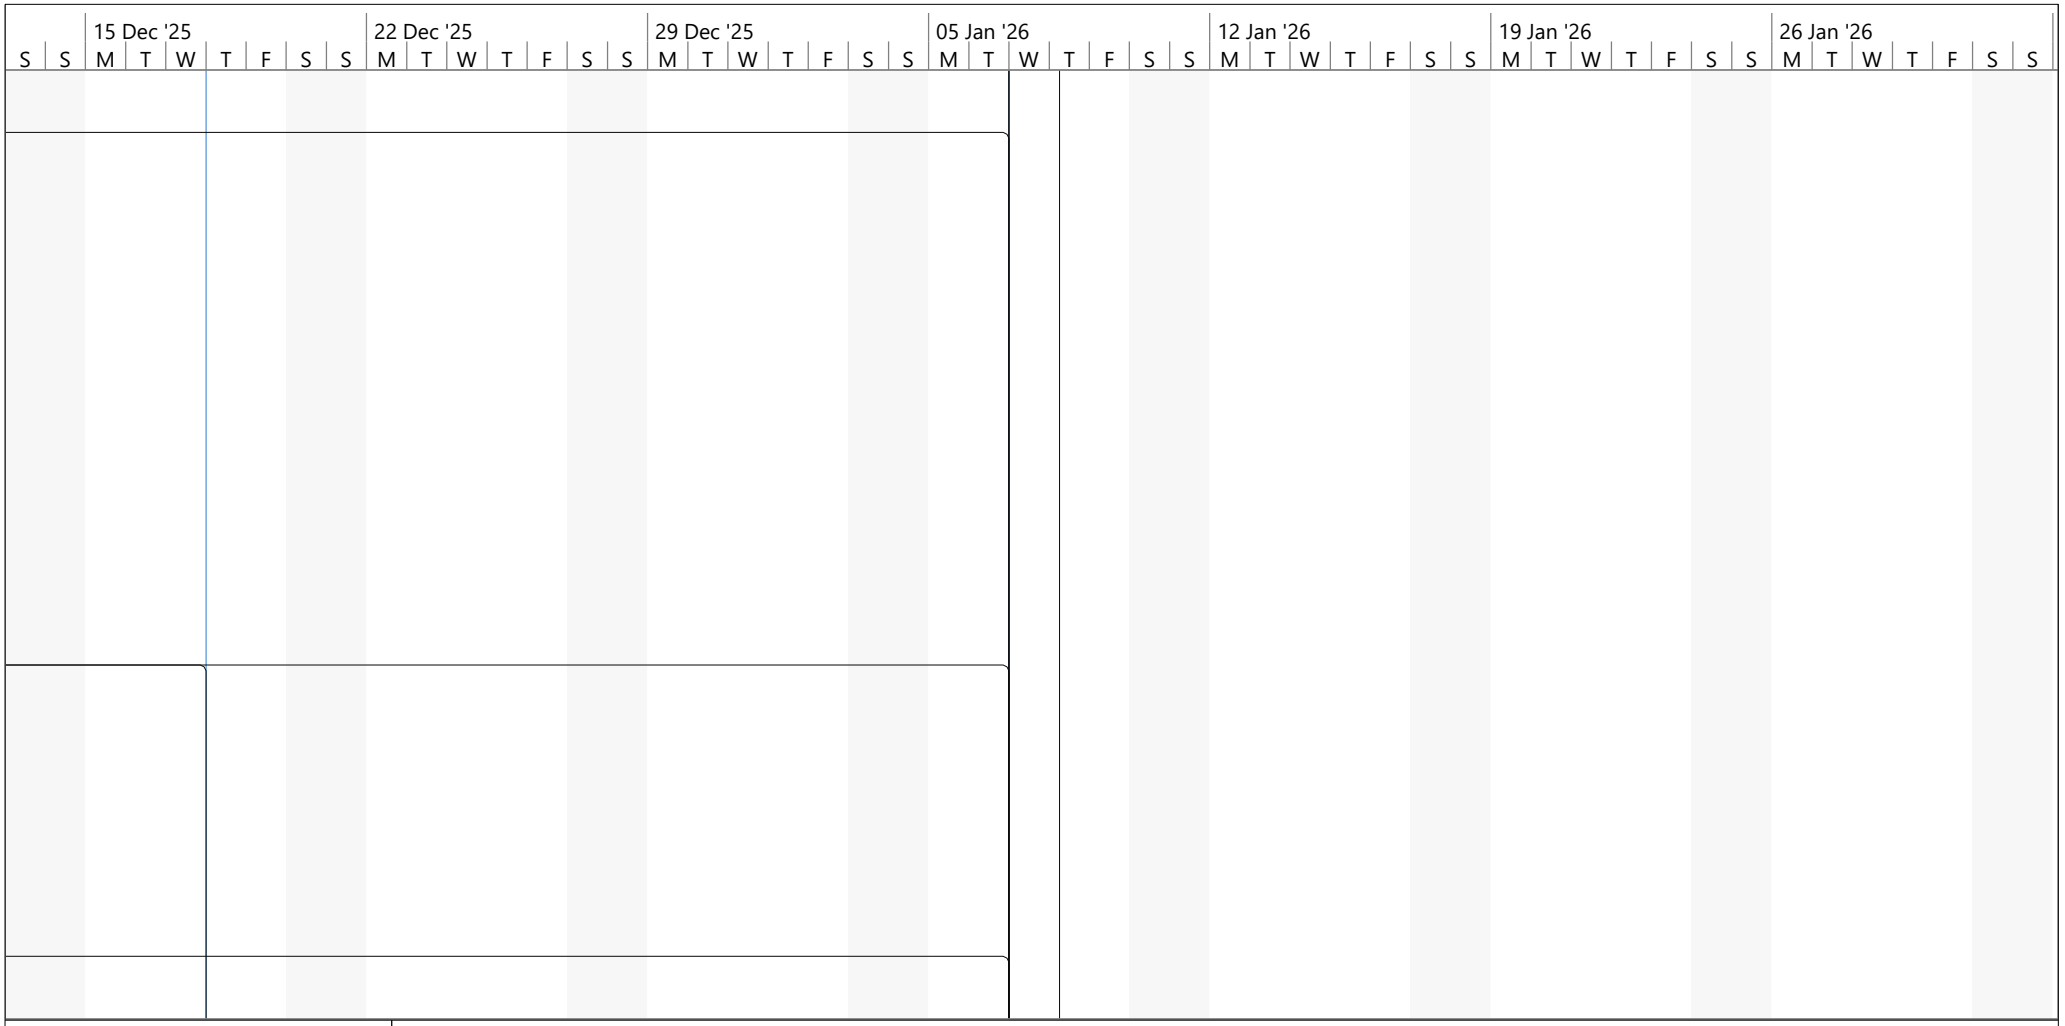


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

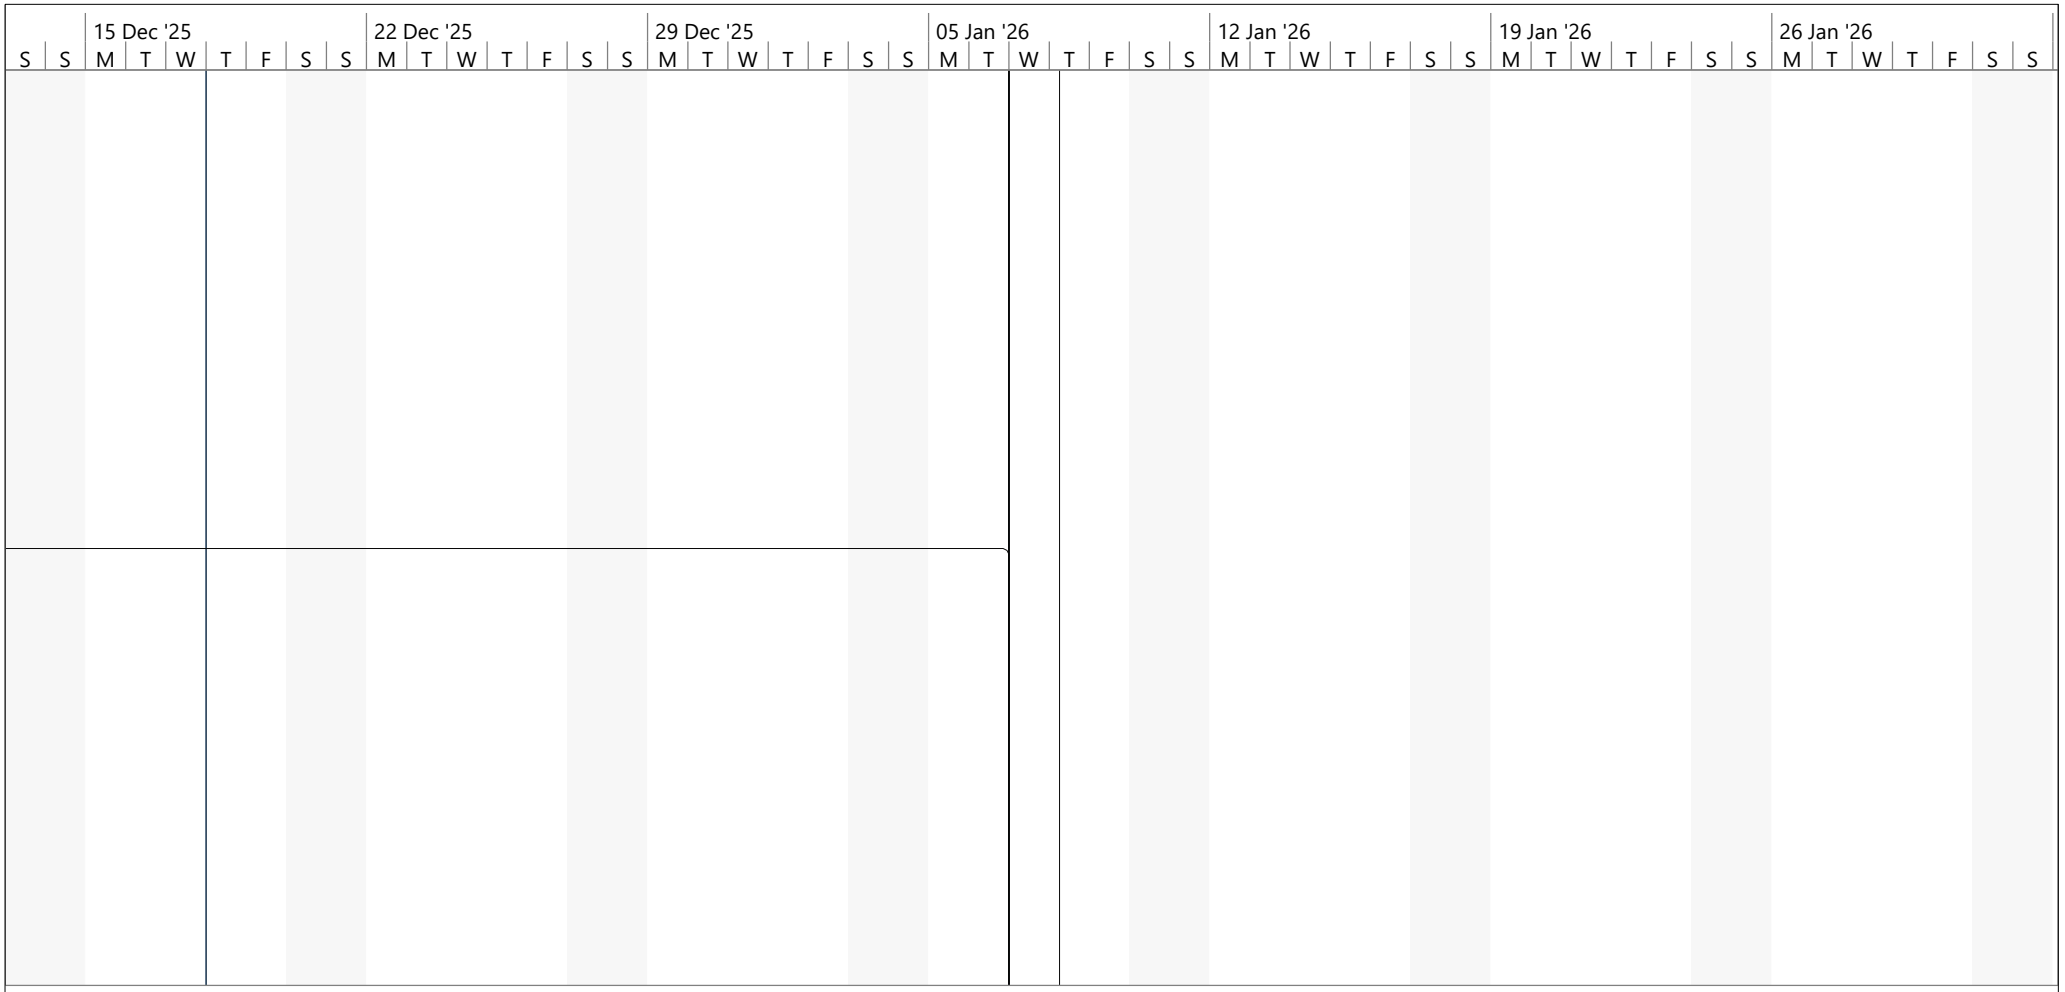


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

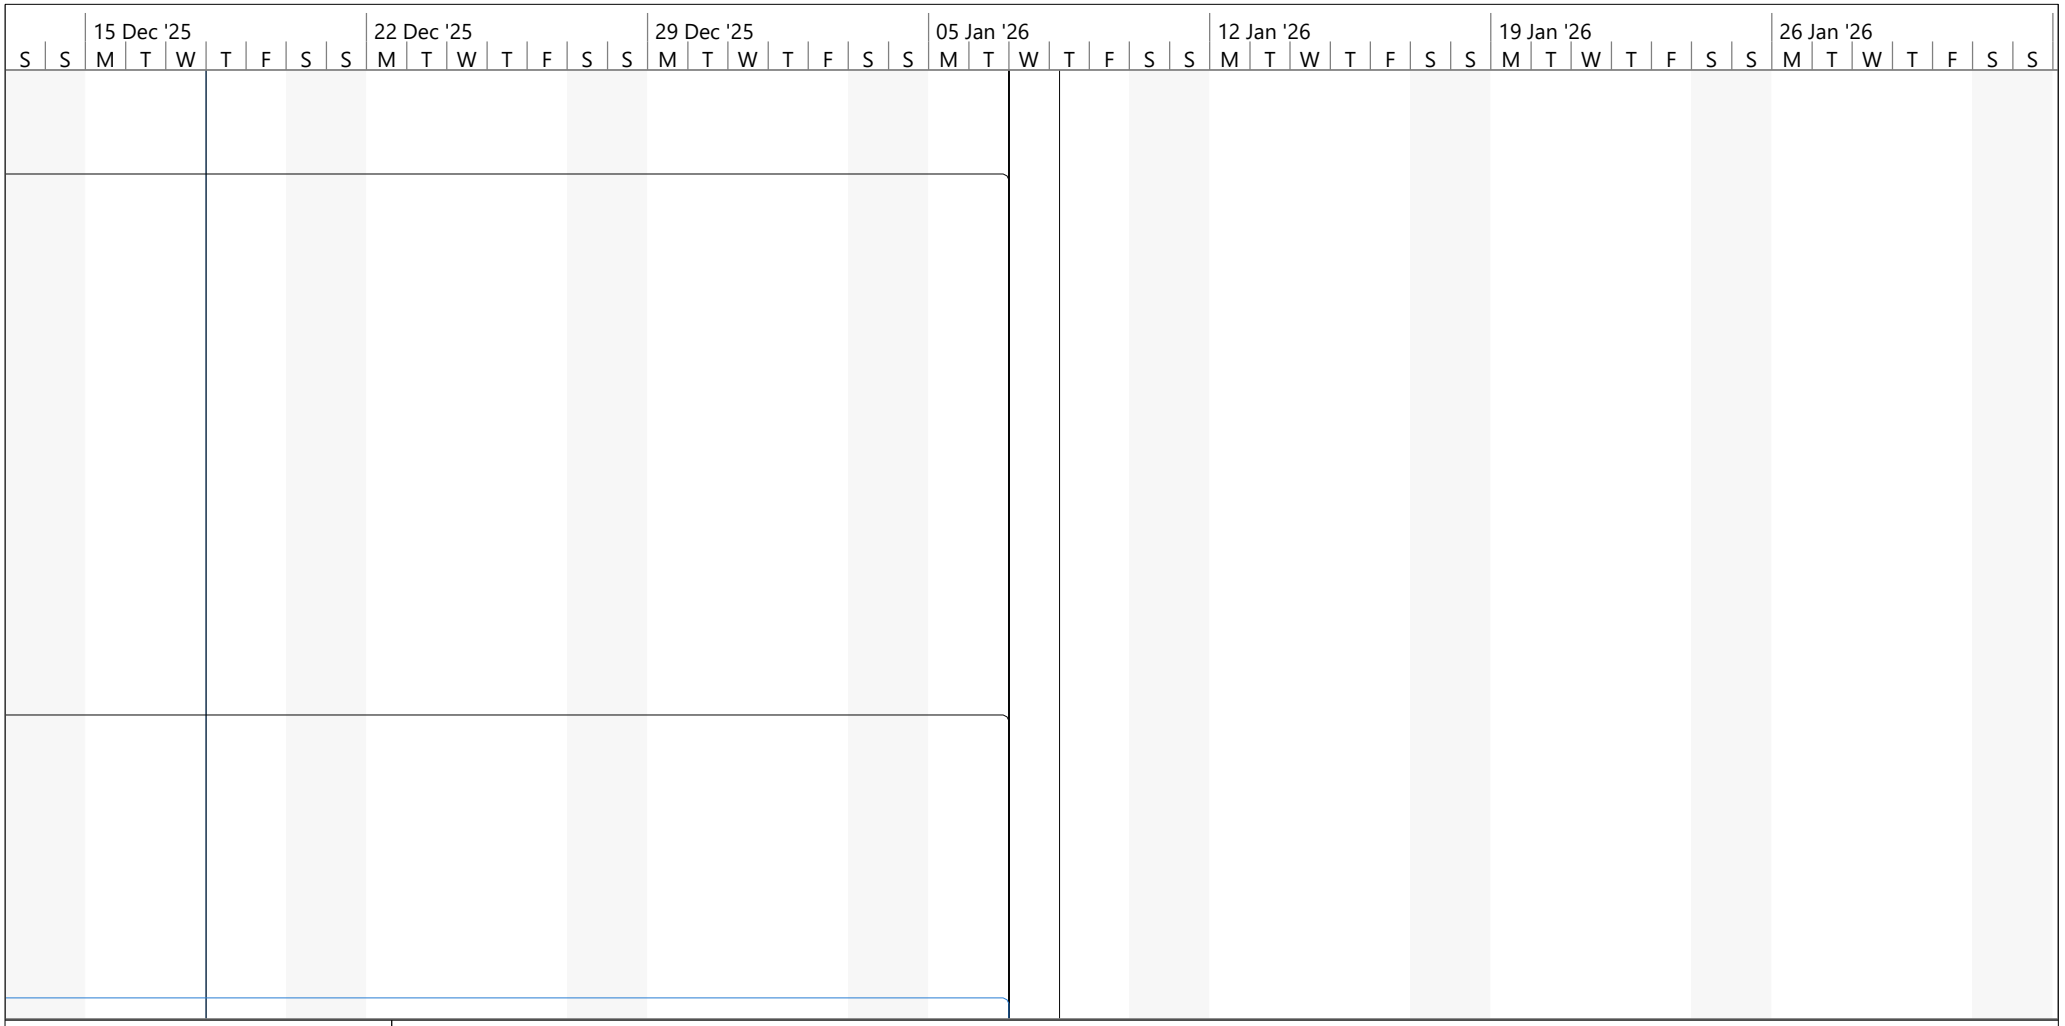

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

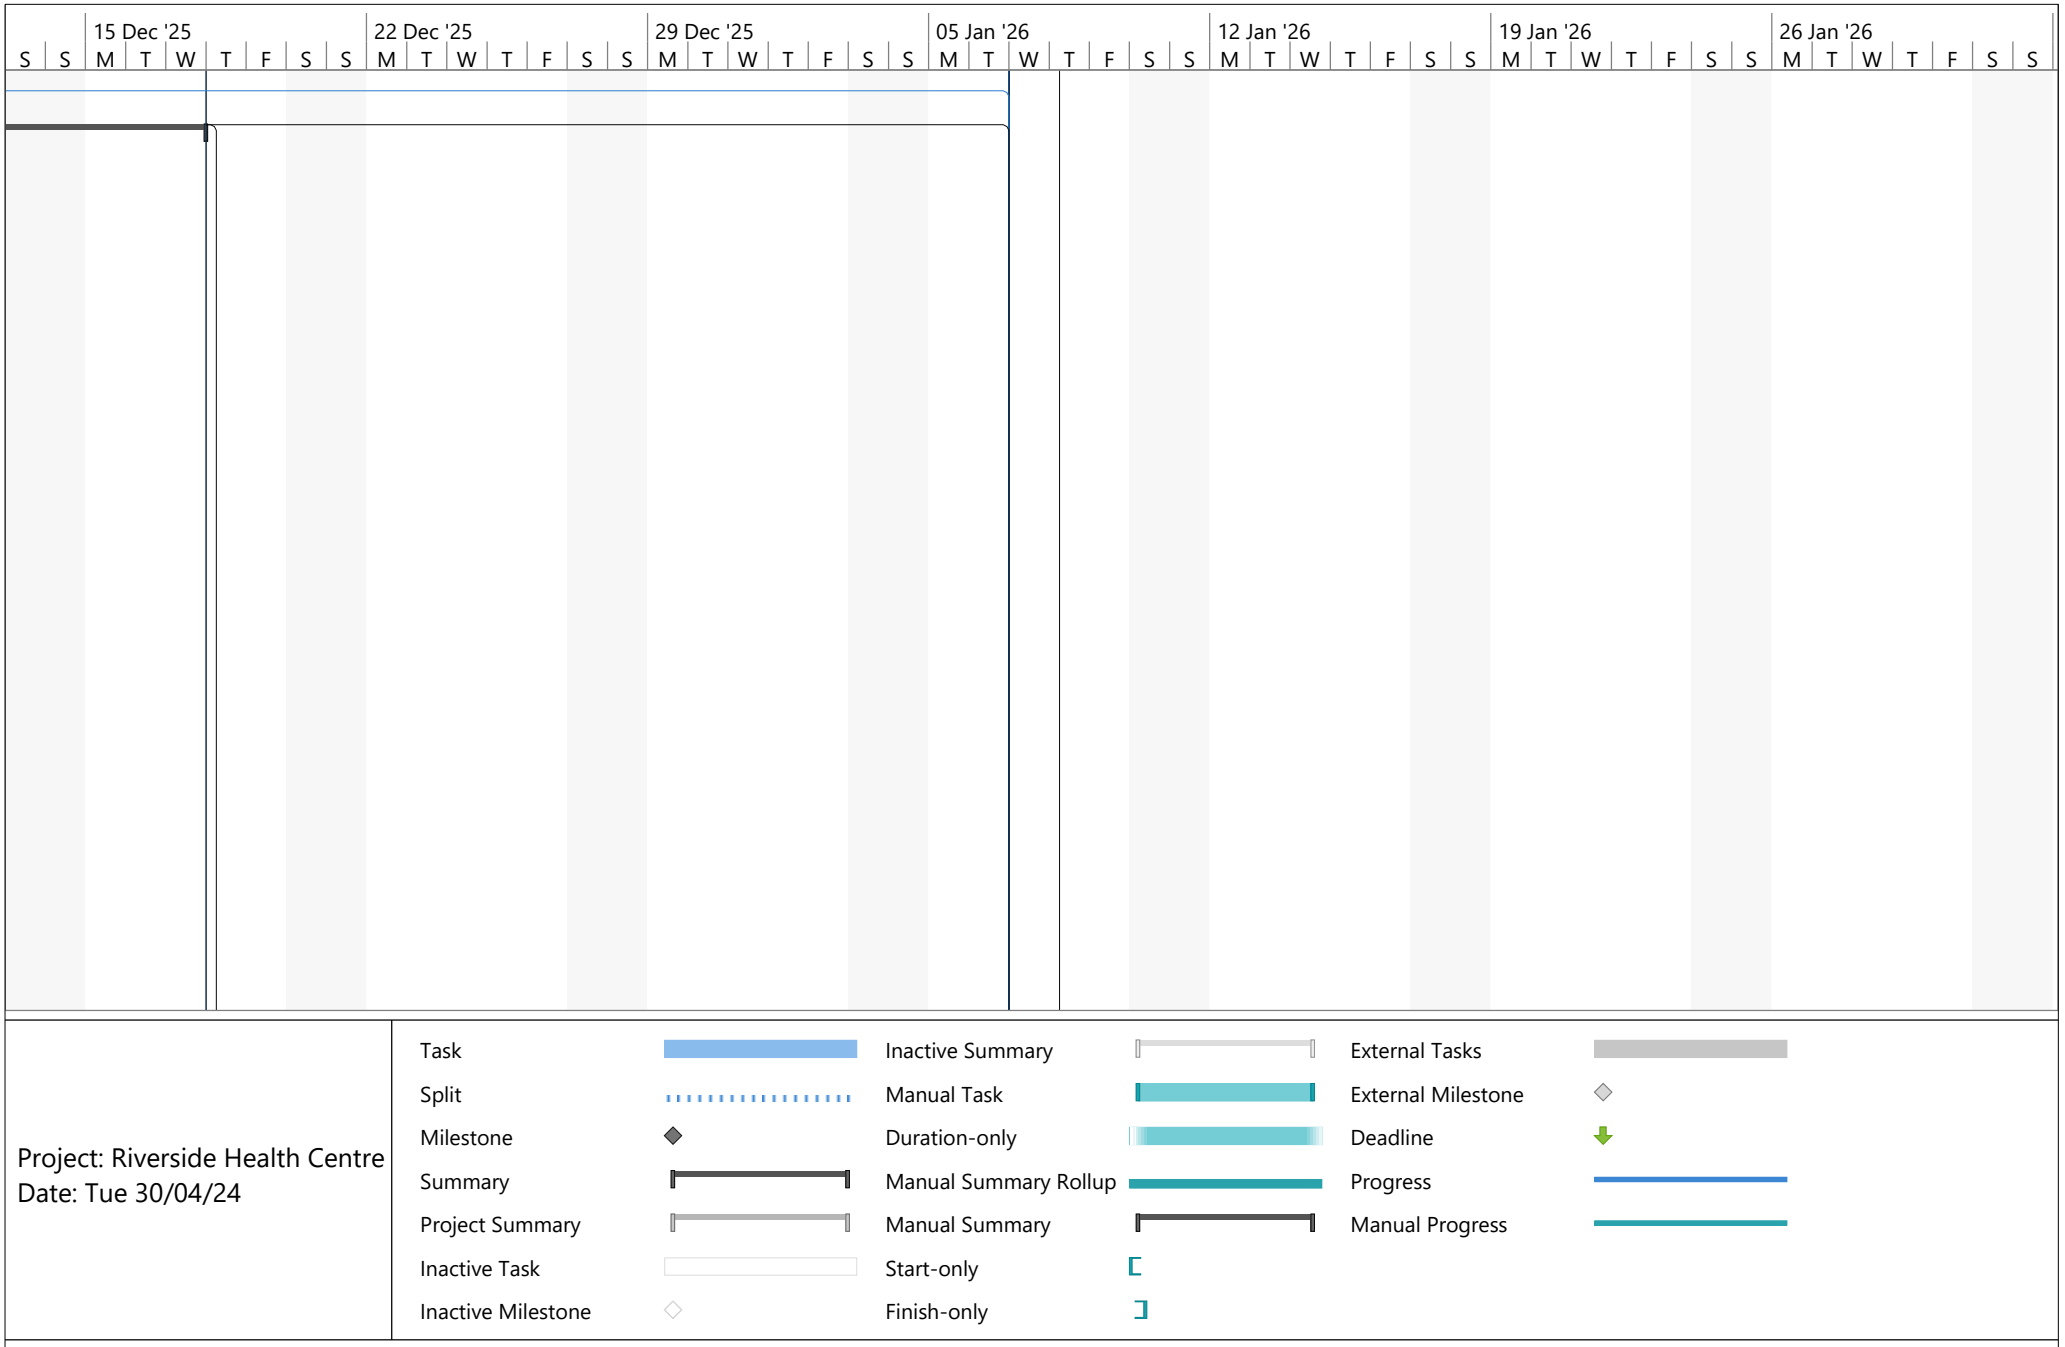
15 Dec '25
22 Dec '25
29 Dec '25
05 Jan '26
12 Jan '26
19 Jan '26
26 Jan '26
S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

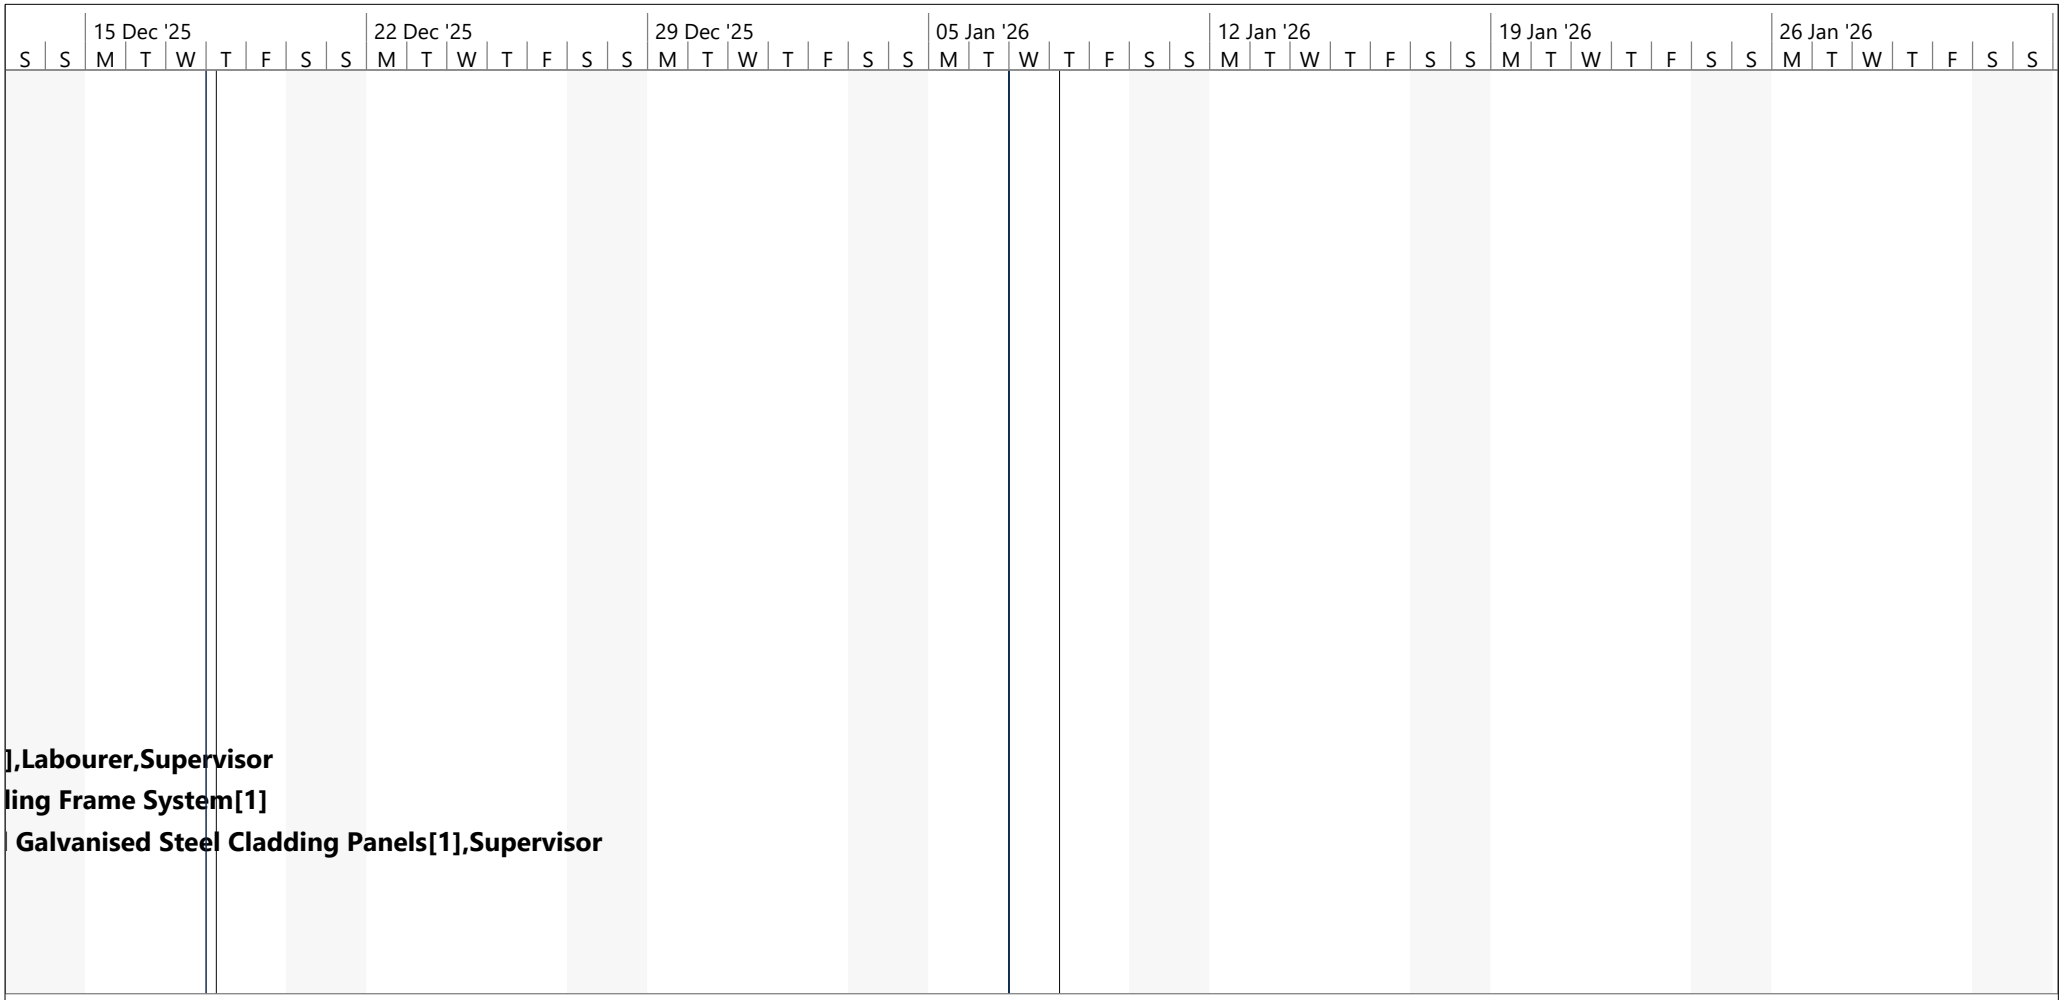


Project: Riverside Health Centre
Date: Tue 30/04/24


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

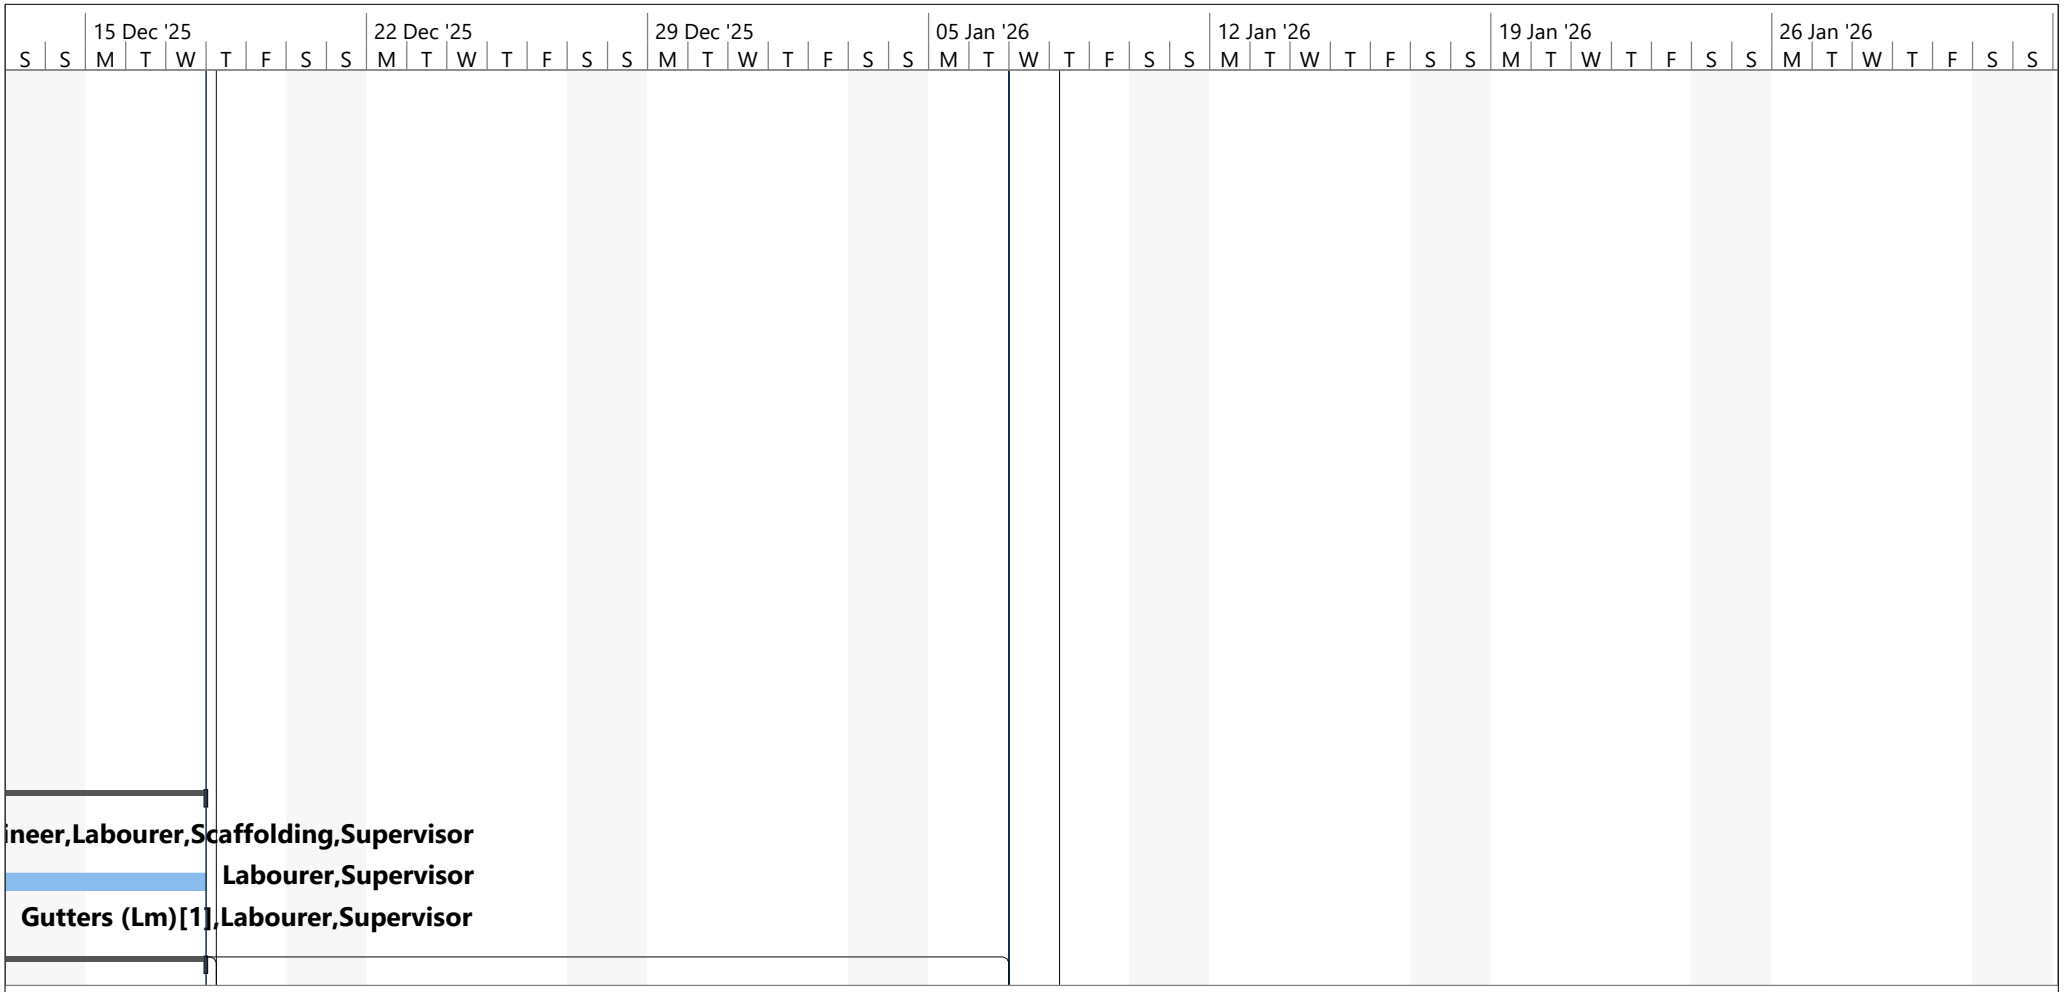

Project: Riverside Health Centre
Date: Tue 30/04/24


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

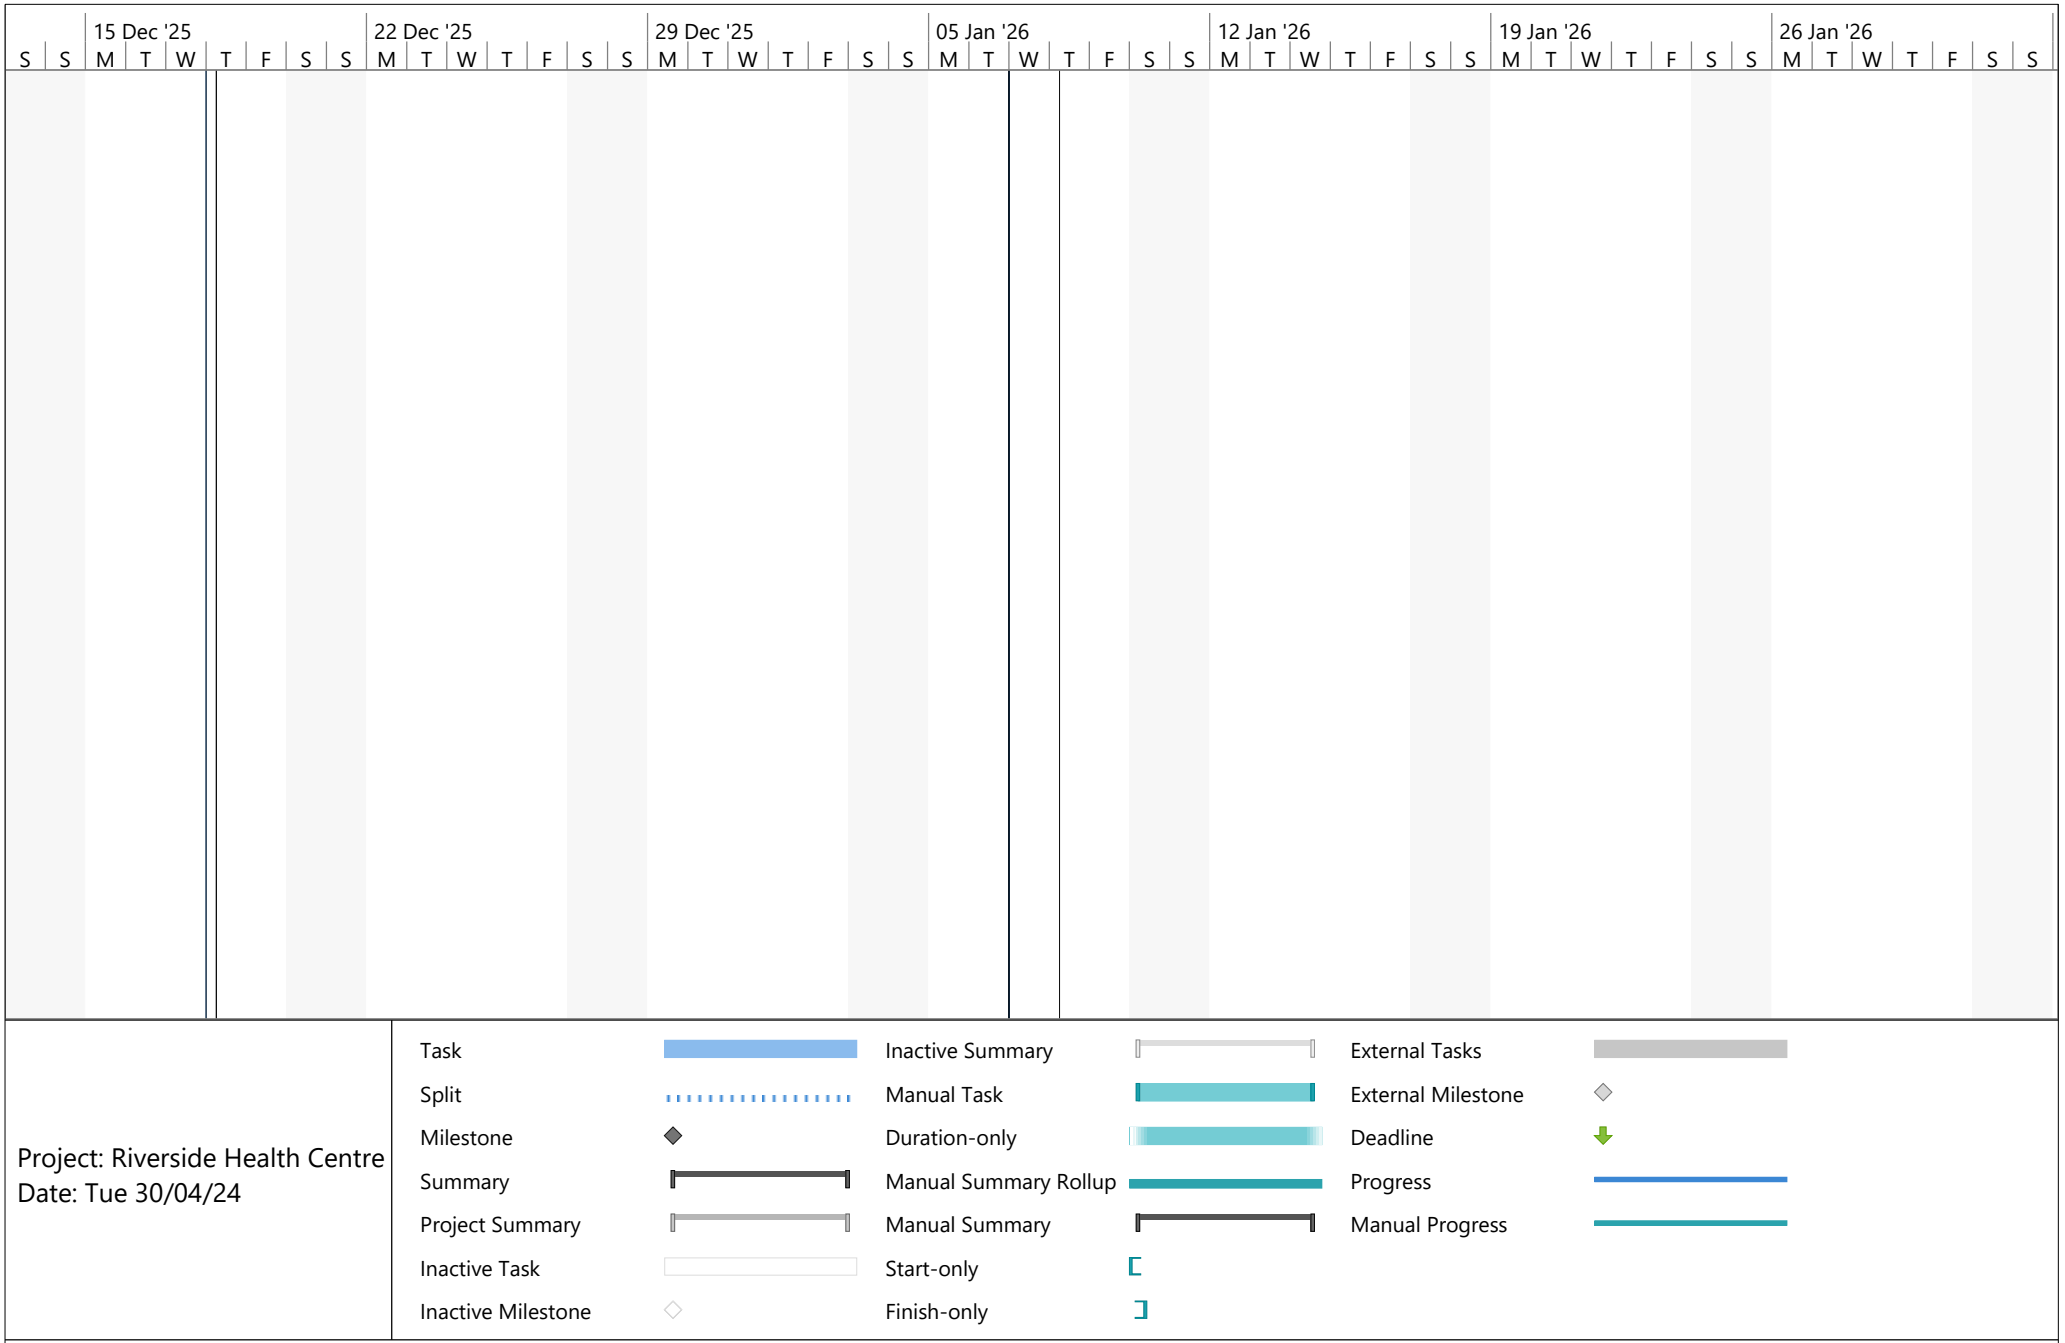
15 Dec '25
22 Dec '25
29 Dec '25
05 Jan '26
12 Jan '26
19 Jan '26
26 Jan '26
S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

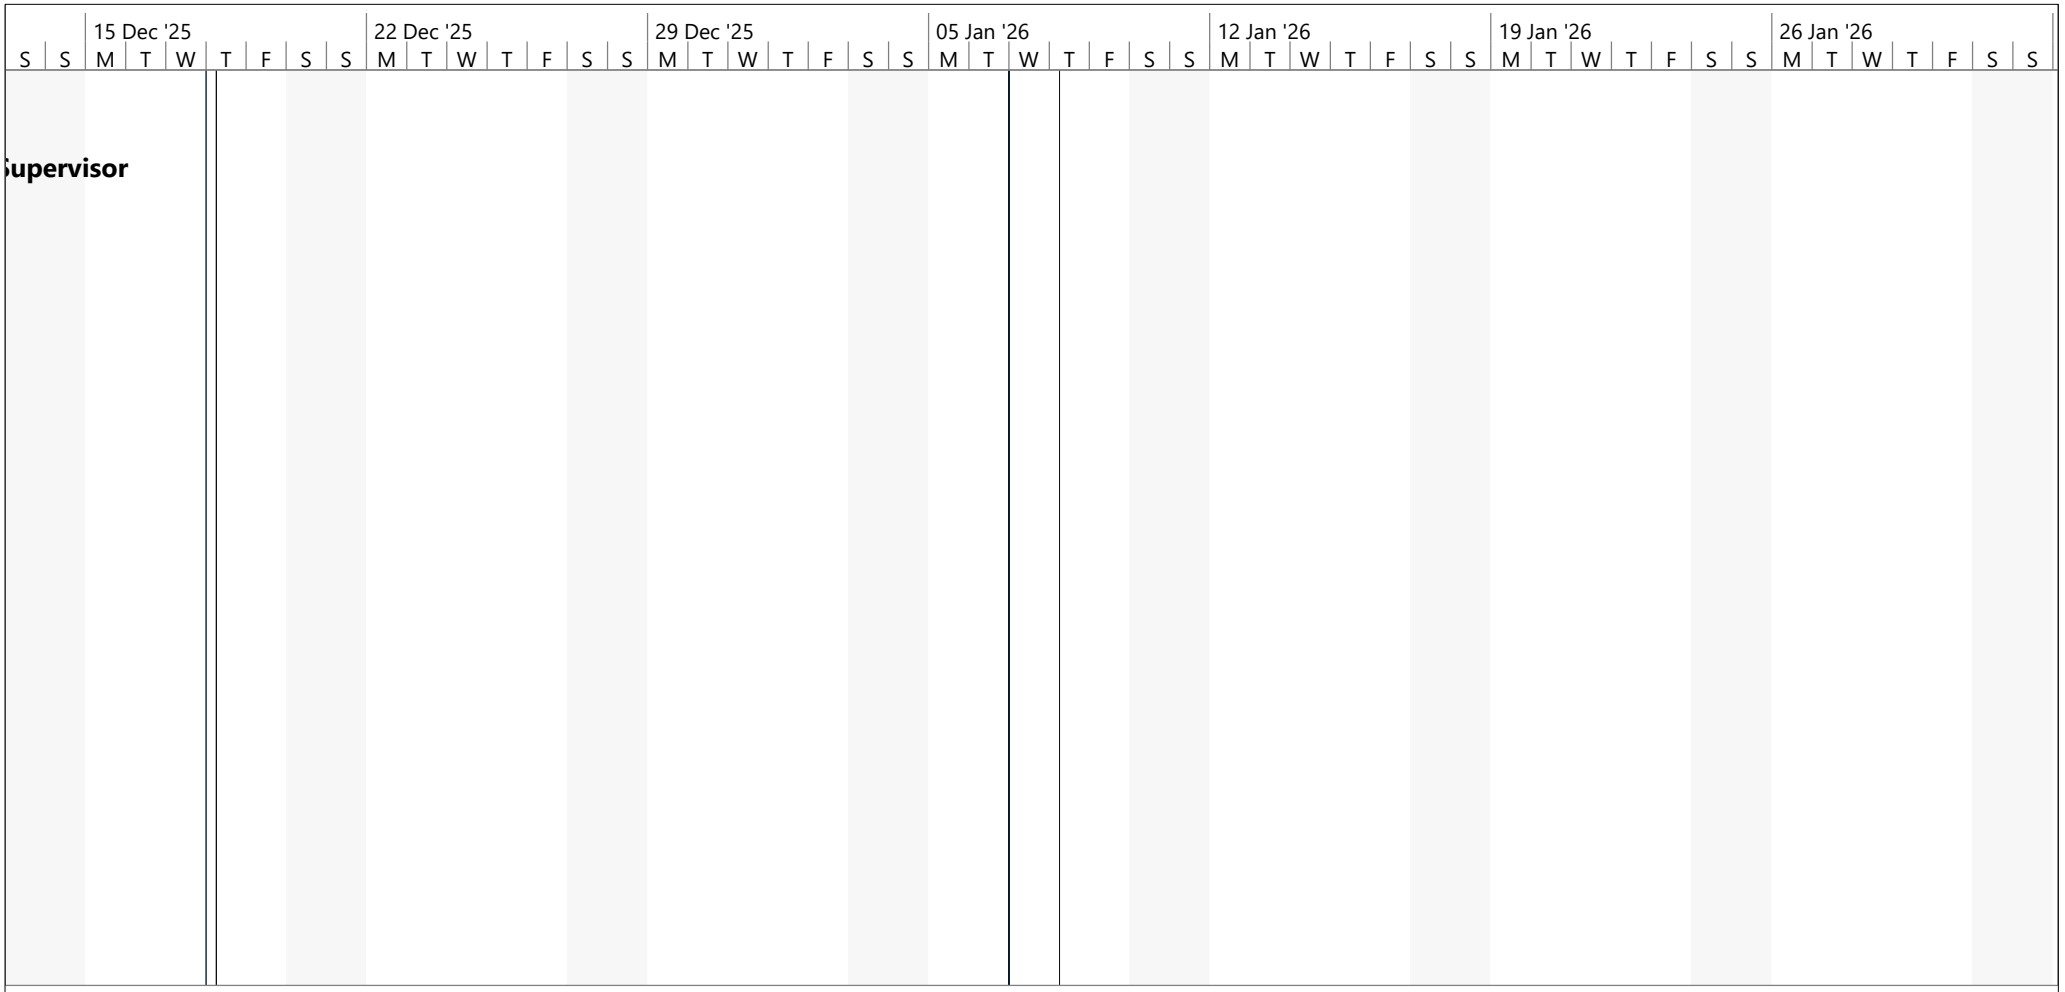


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

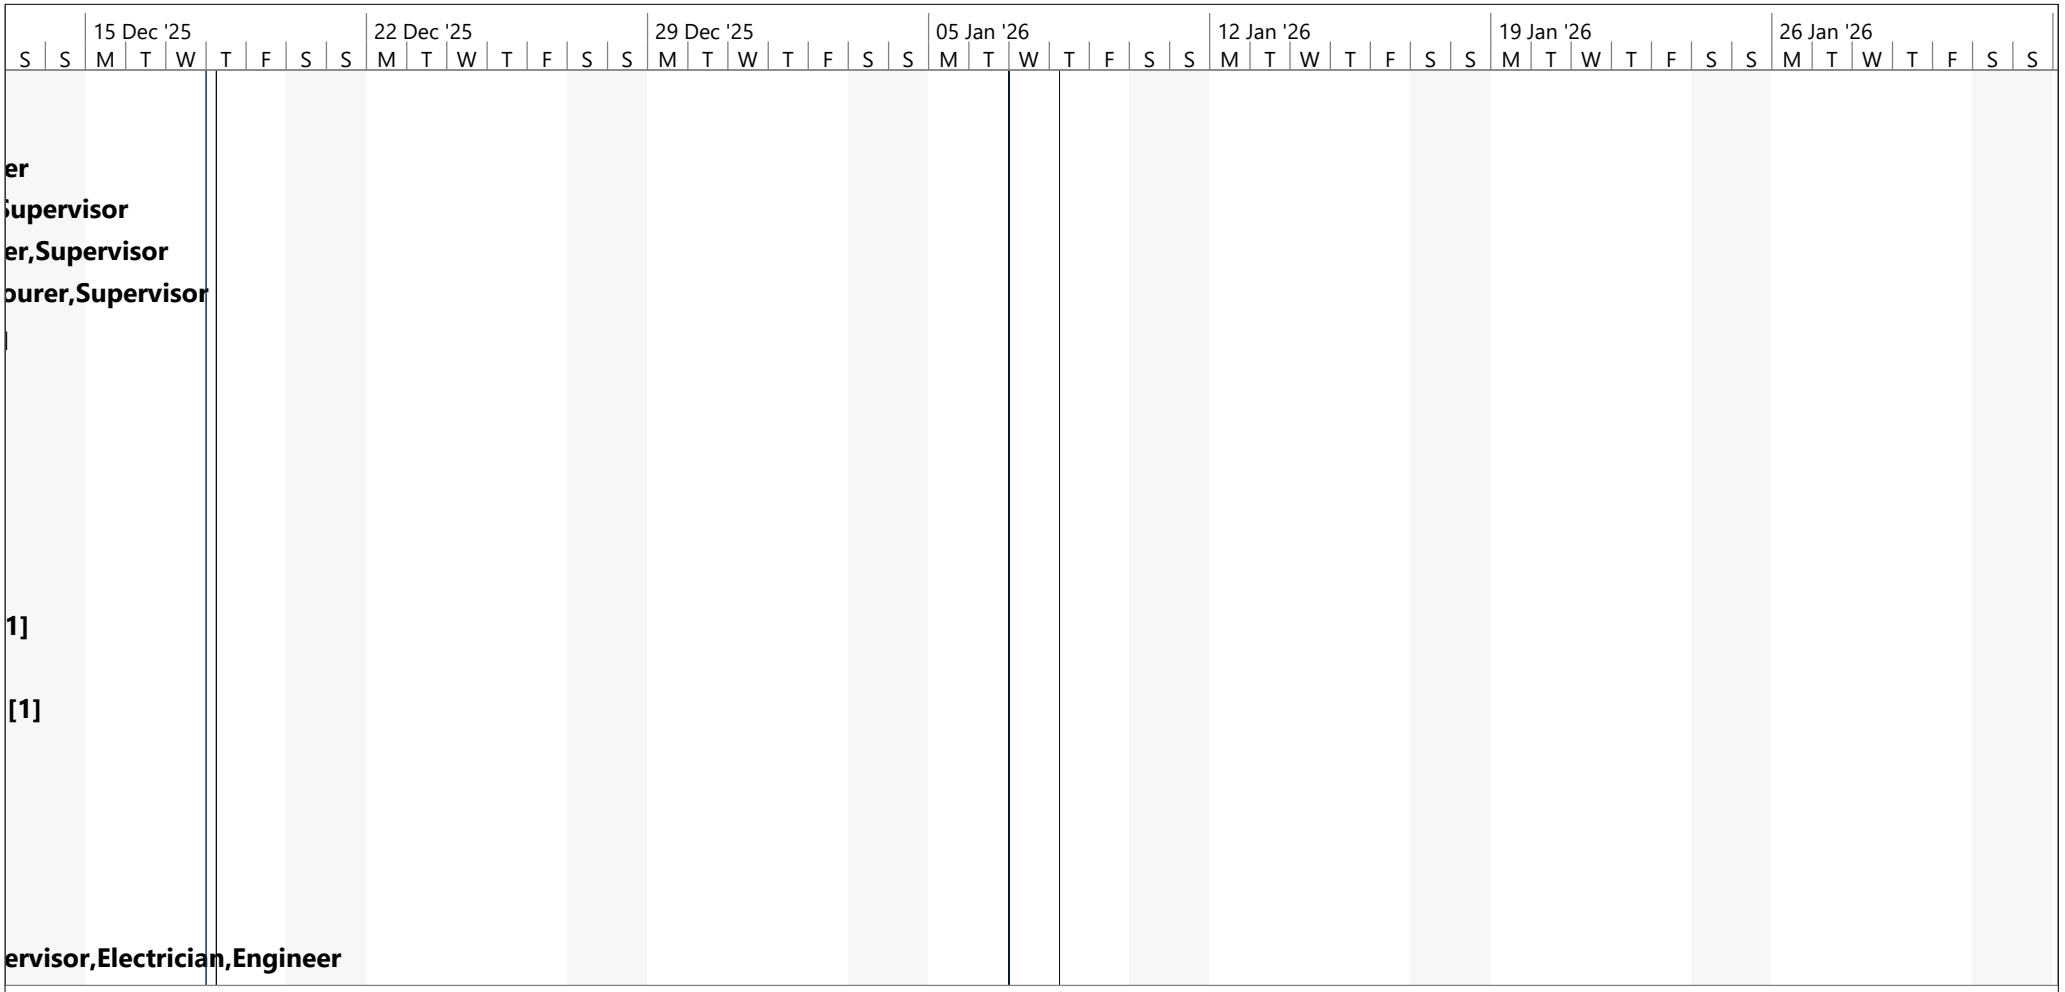


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

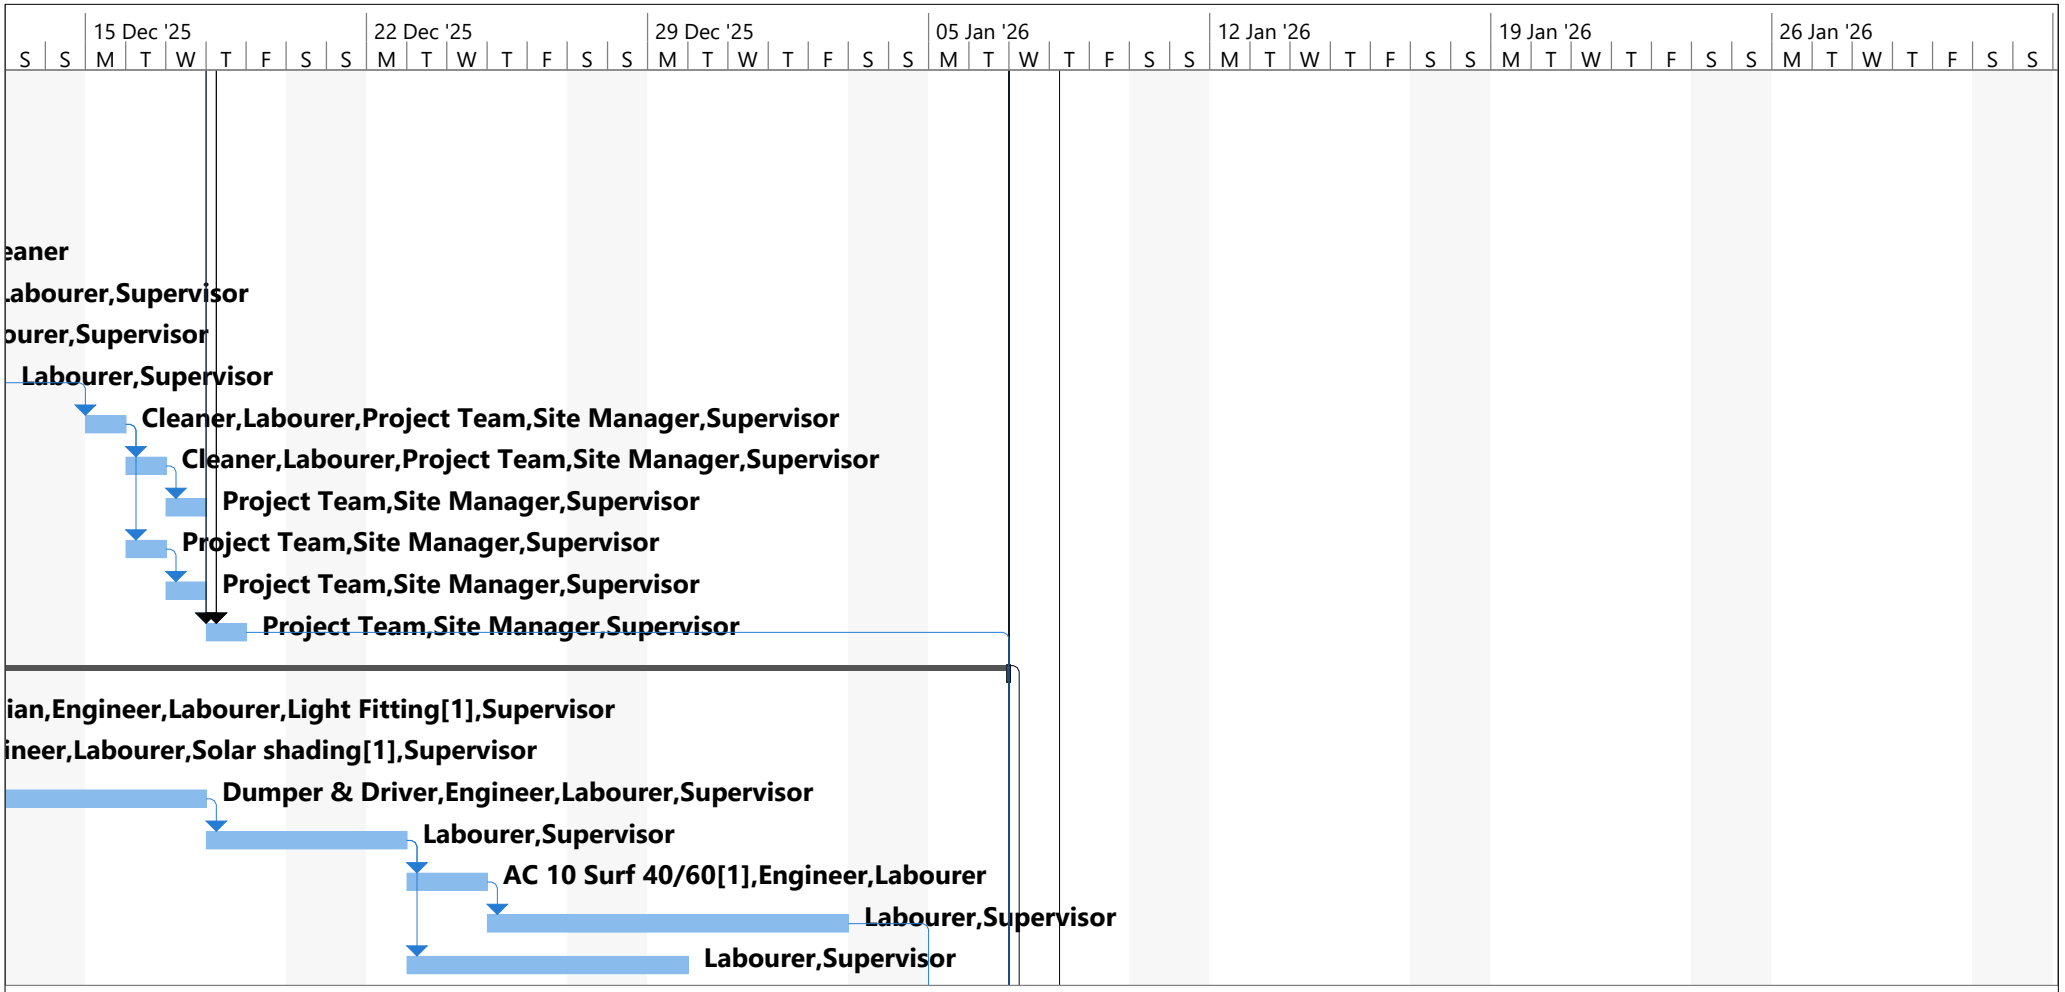


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

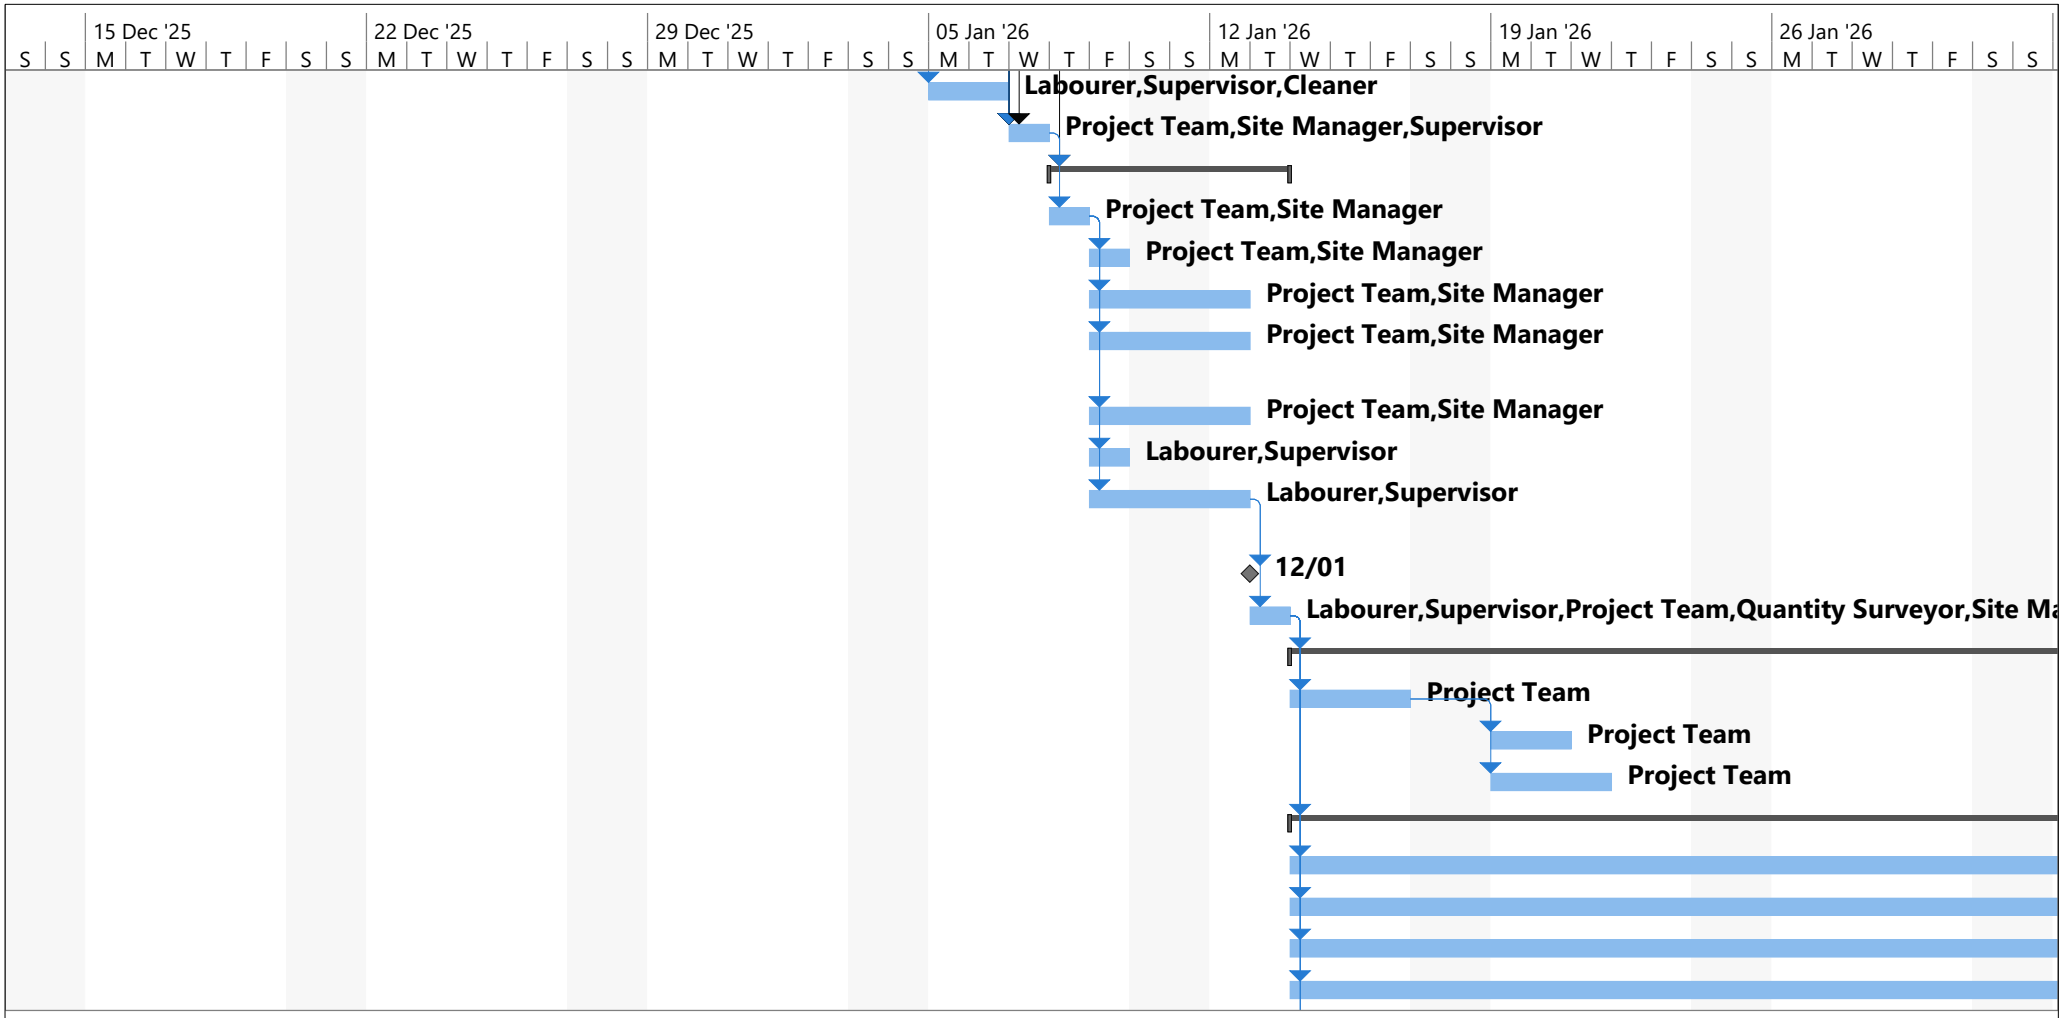


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

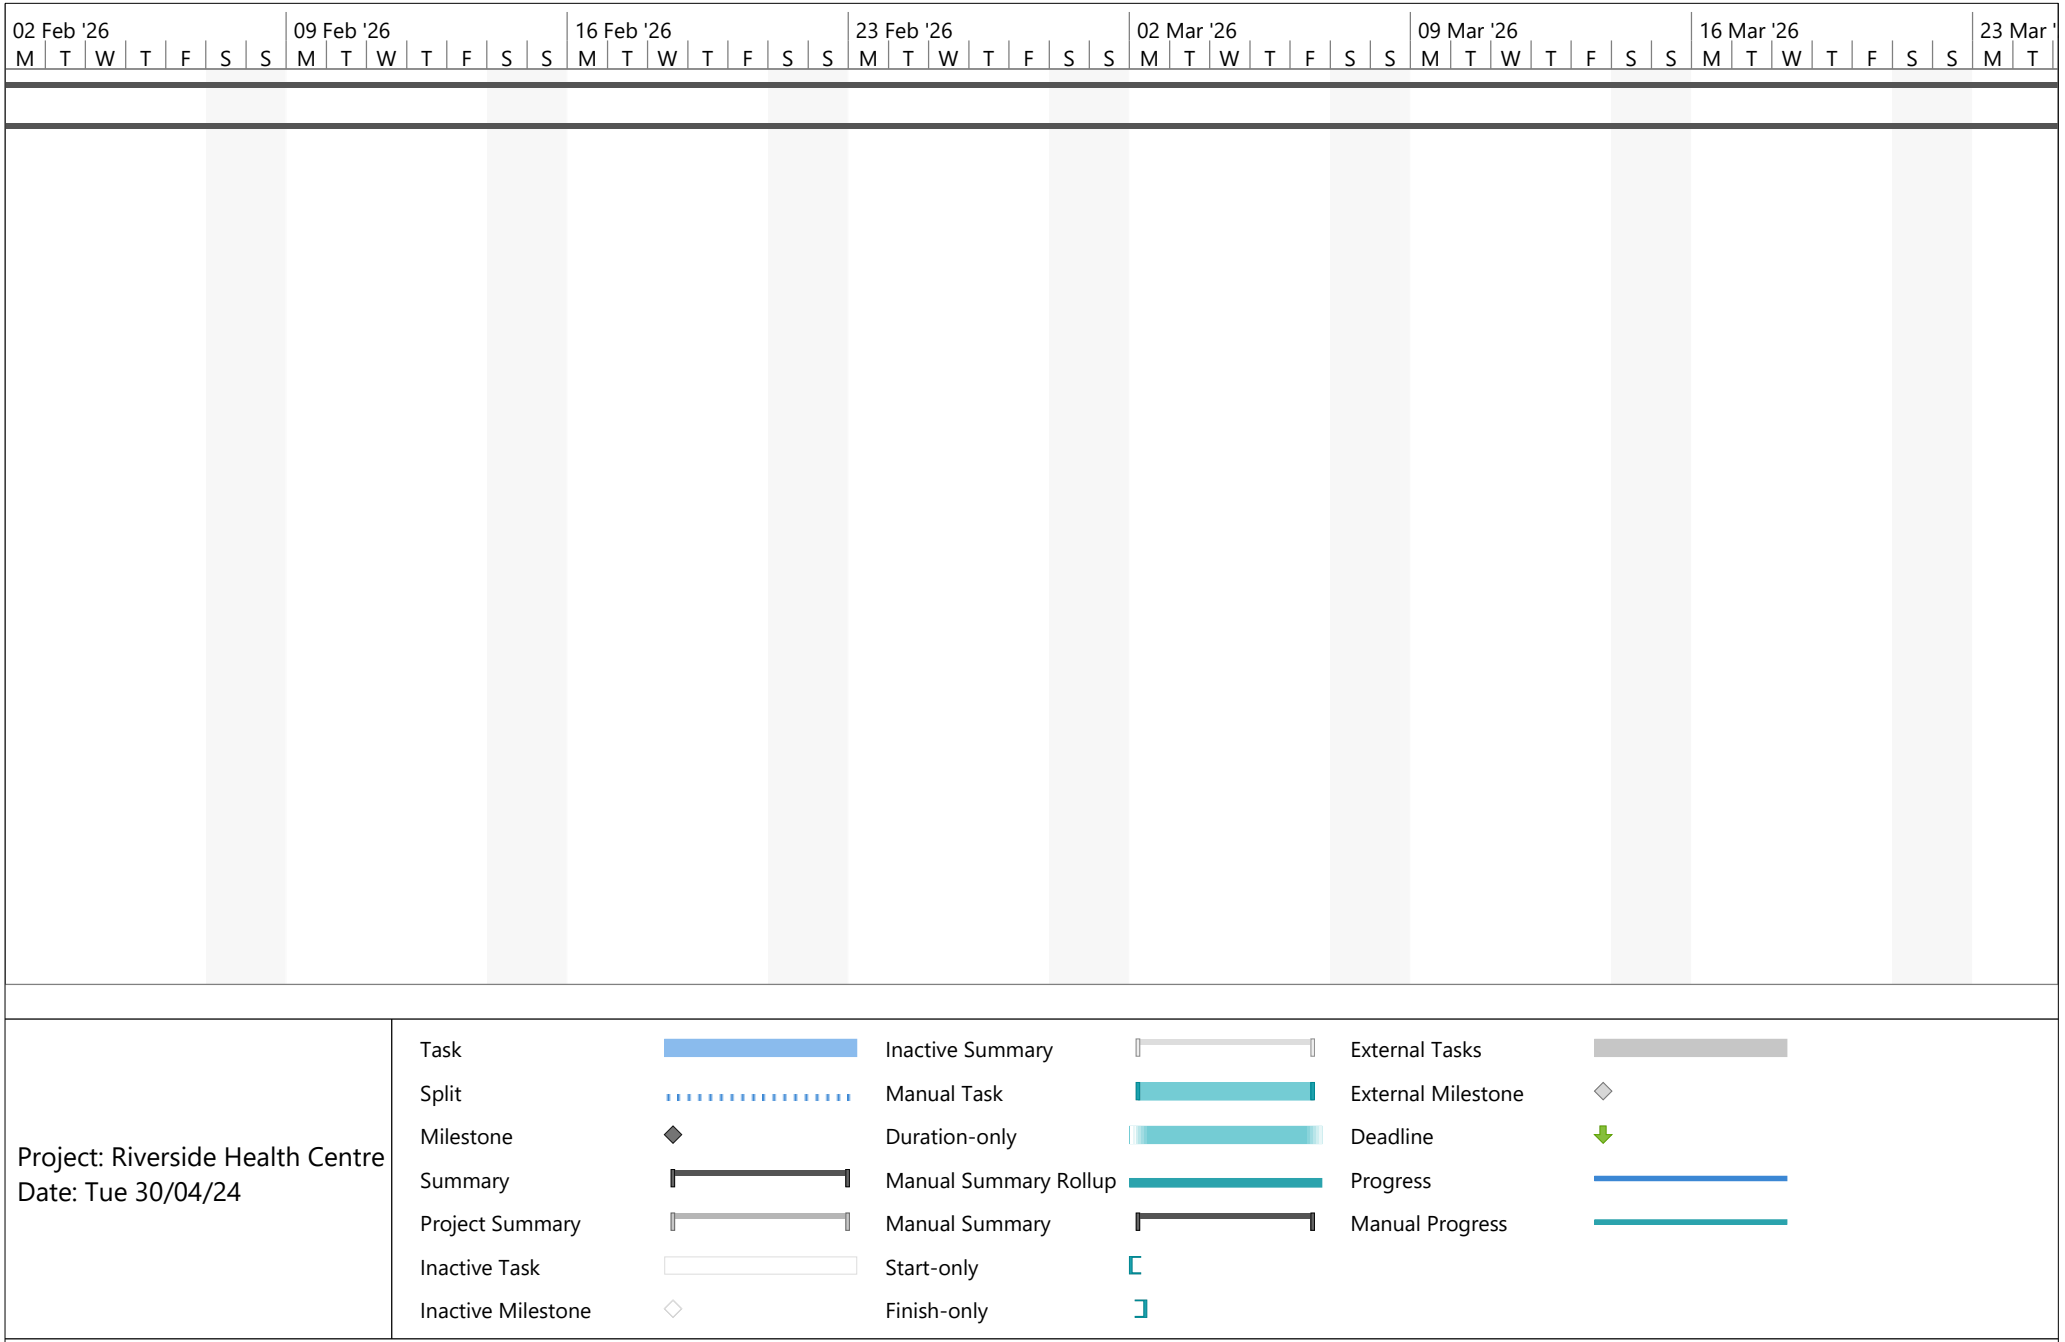


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

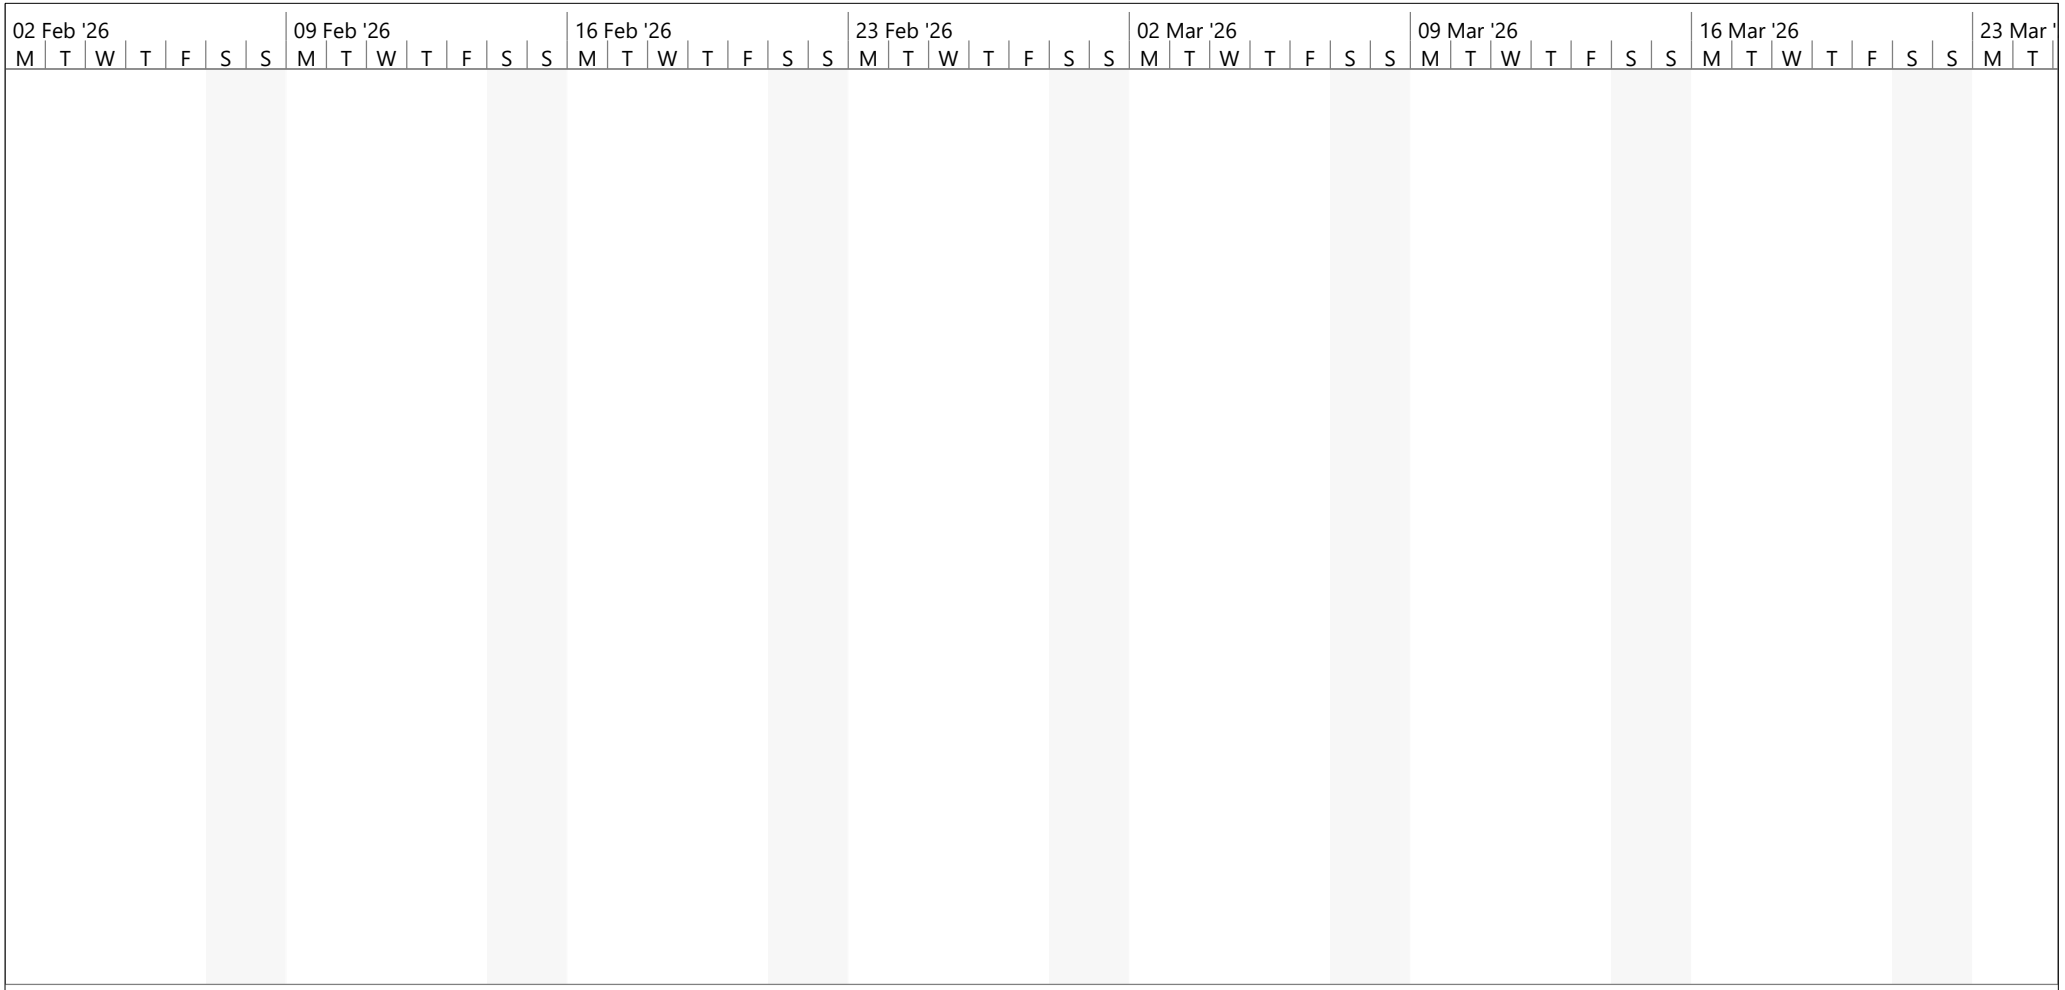


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

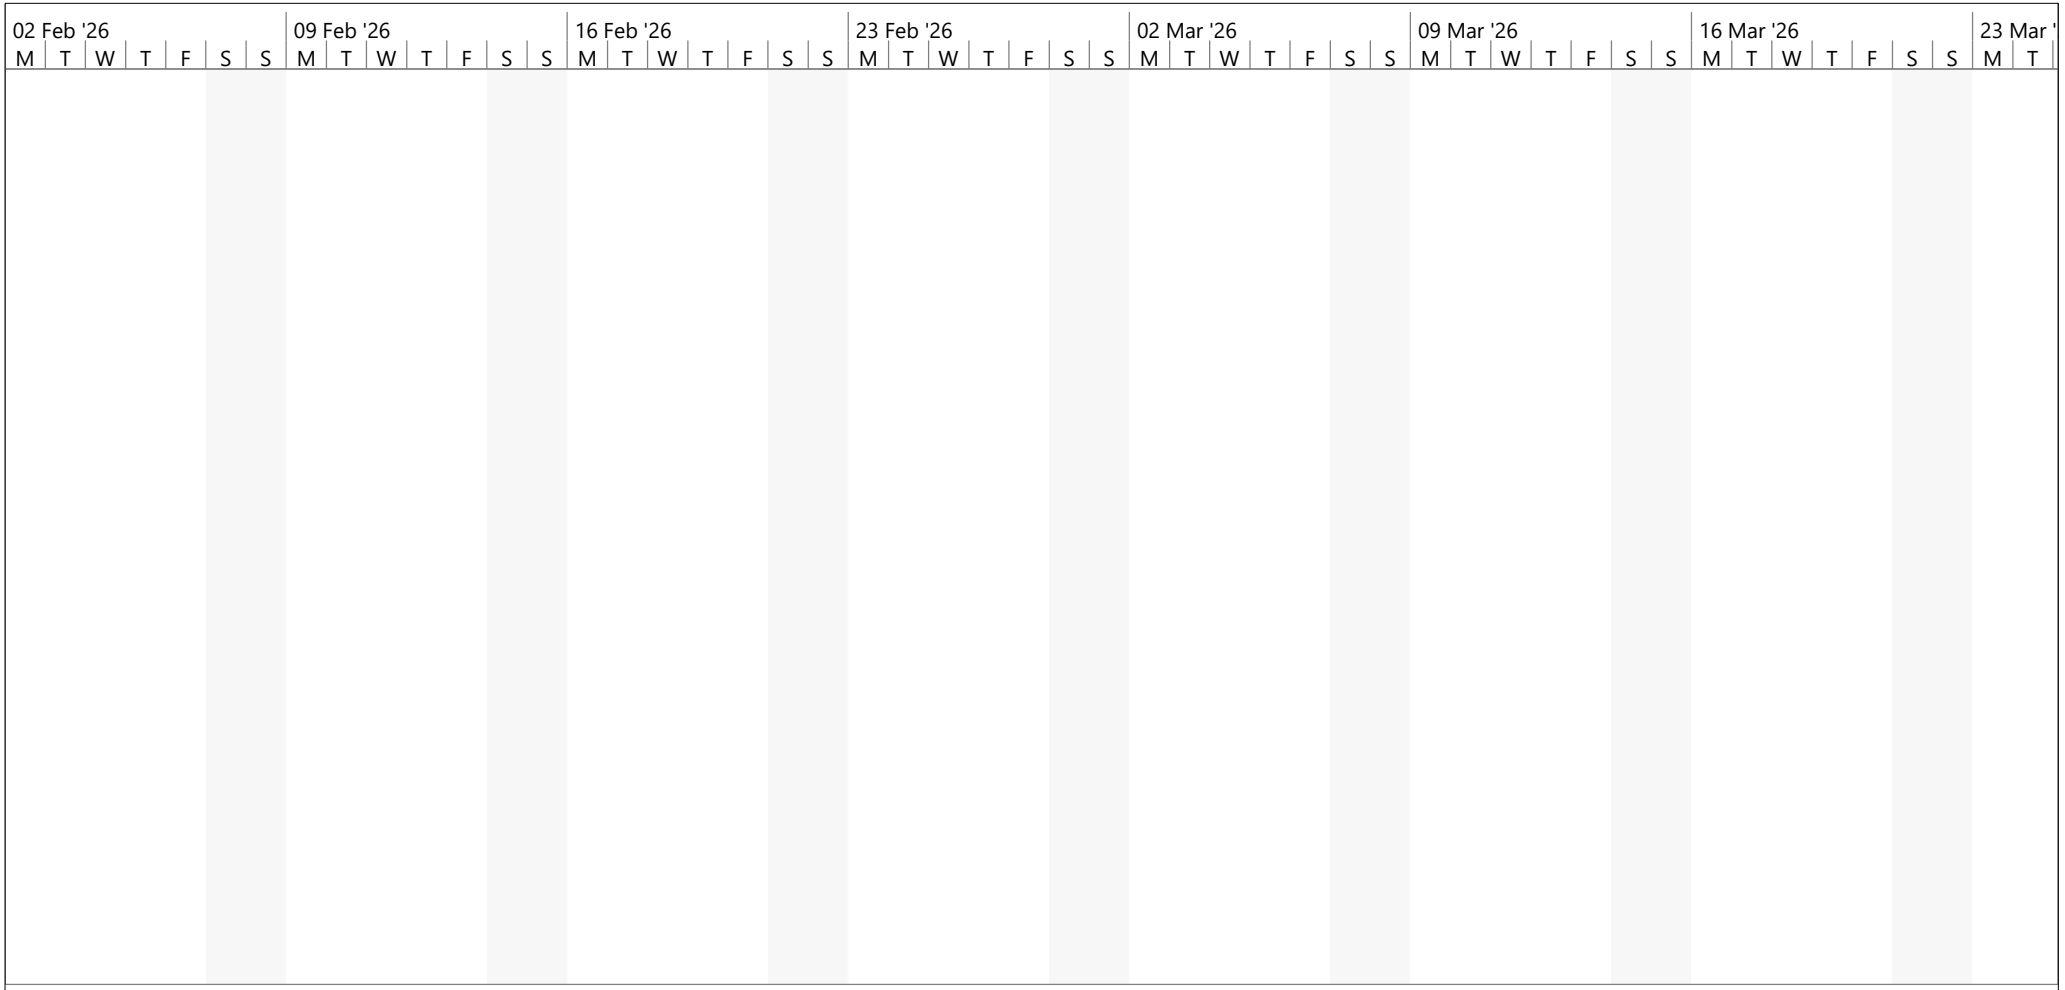

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

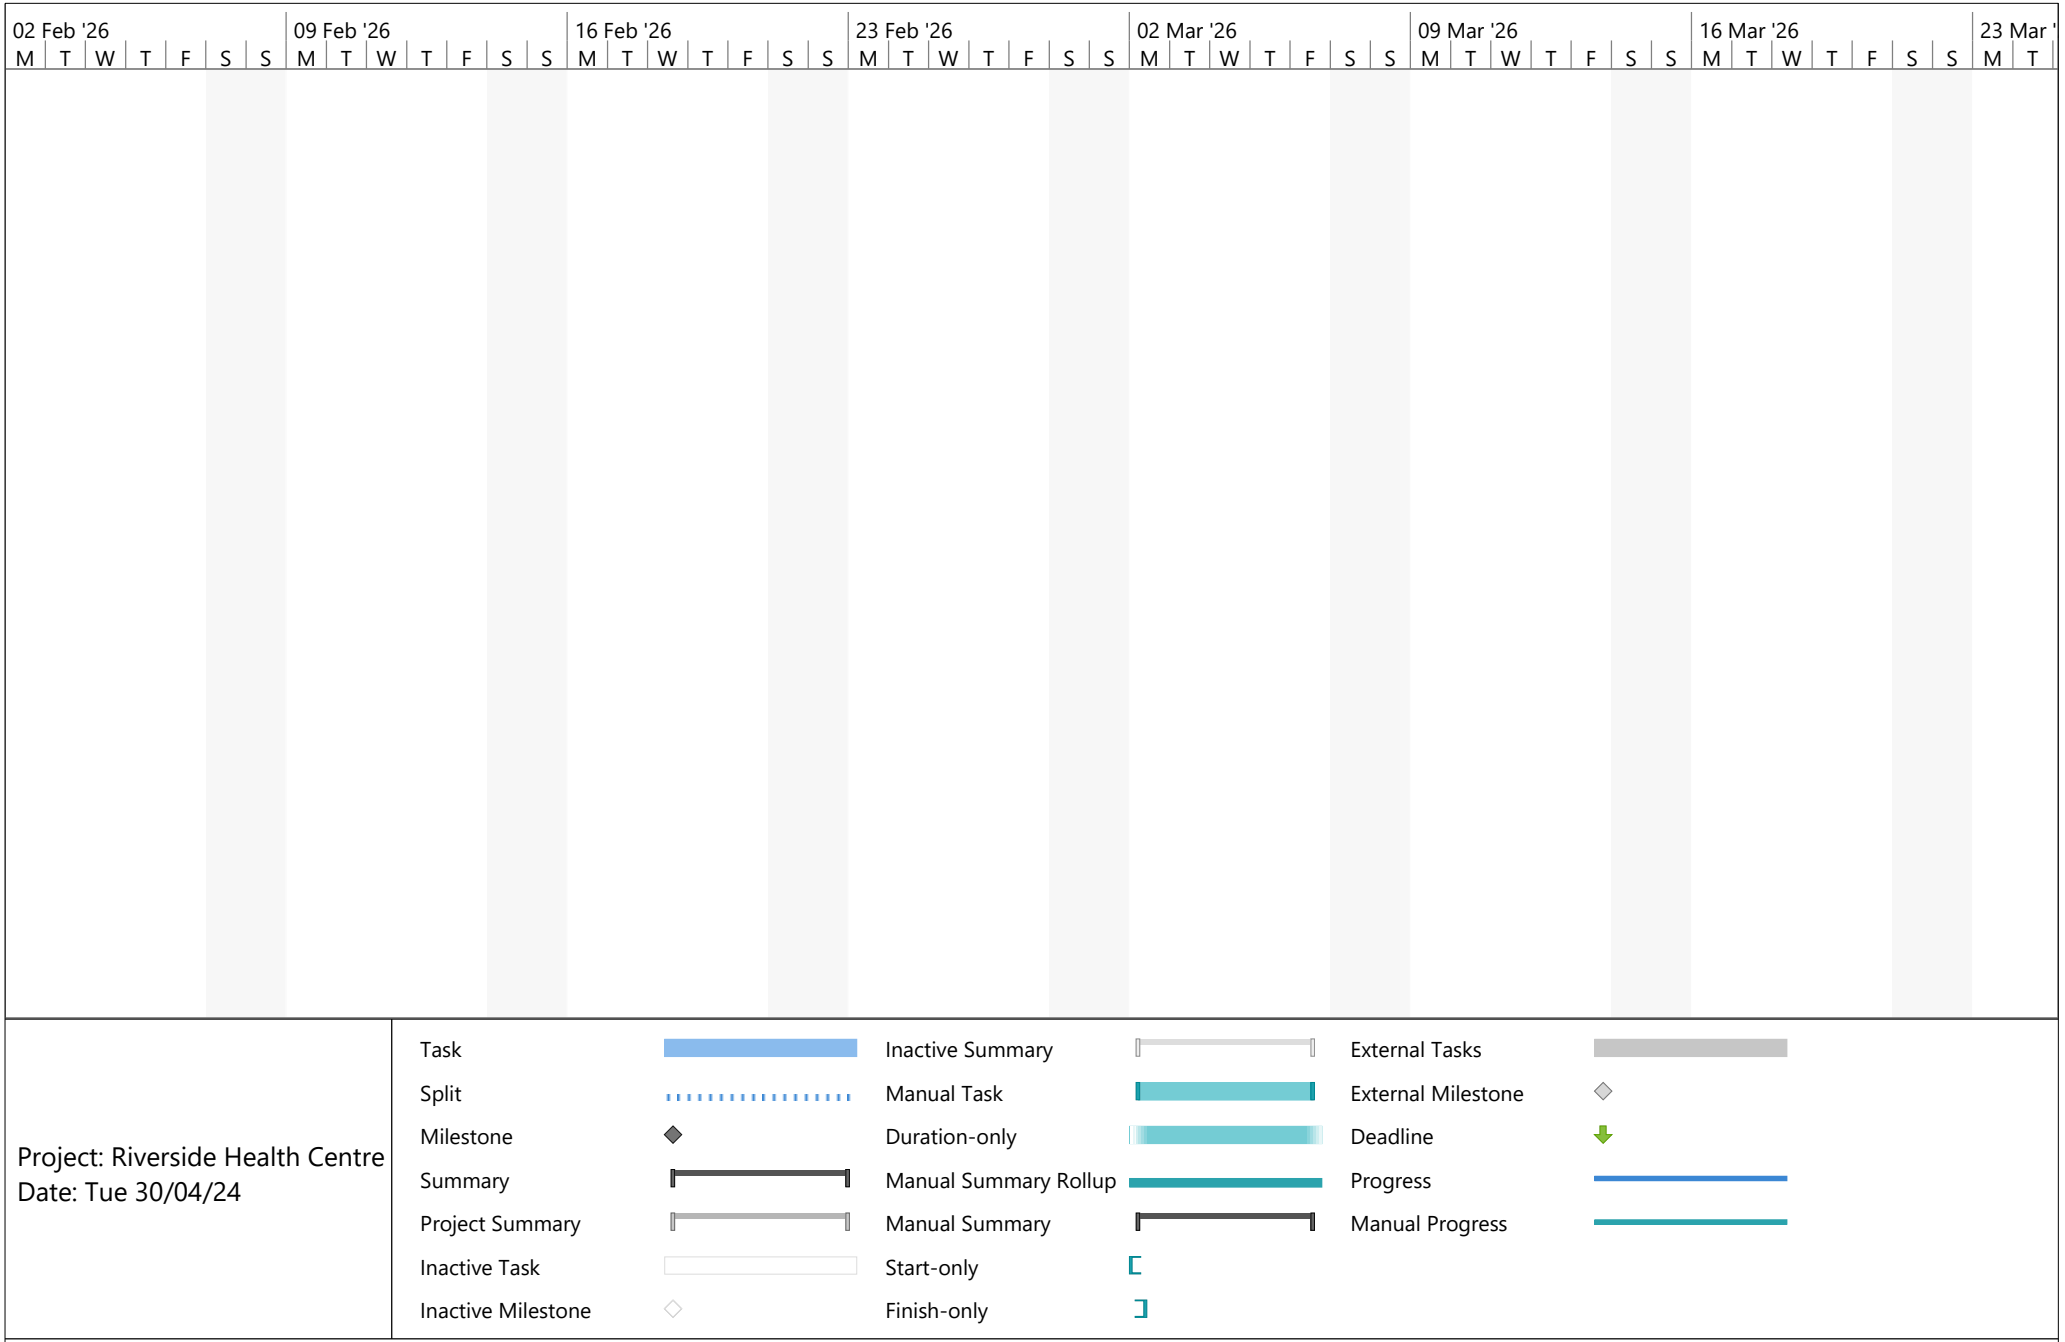
02 Feb '26
M T W T F S S
09 Feb '26
M T W T F S S
16 Feb '26
M T W T F S S
23 Feb '26
M T W T F S S
02 Mar '26
M T W T F S S
09 Mar '26
M T W T F S S
16 Mar '26
M T W T F S S
23 Mar '
M T
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

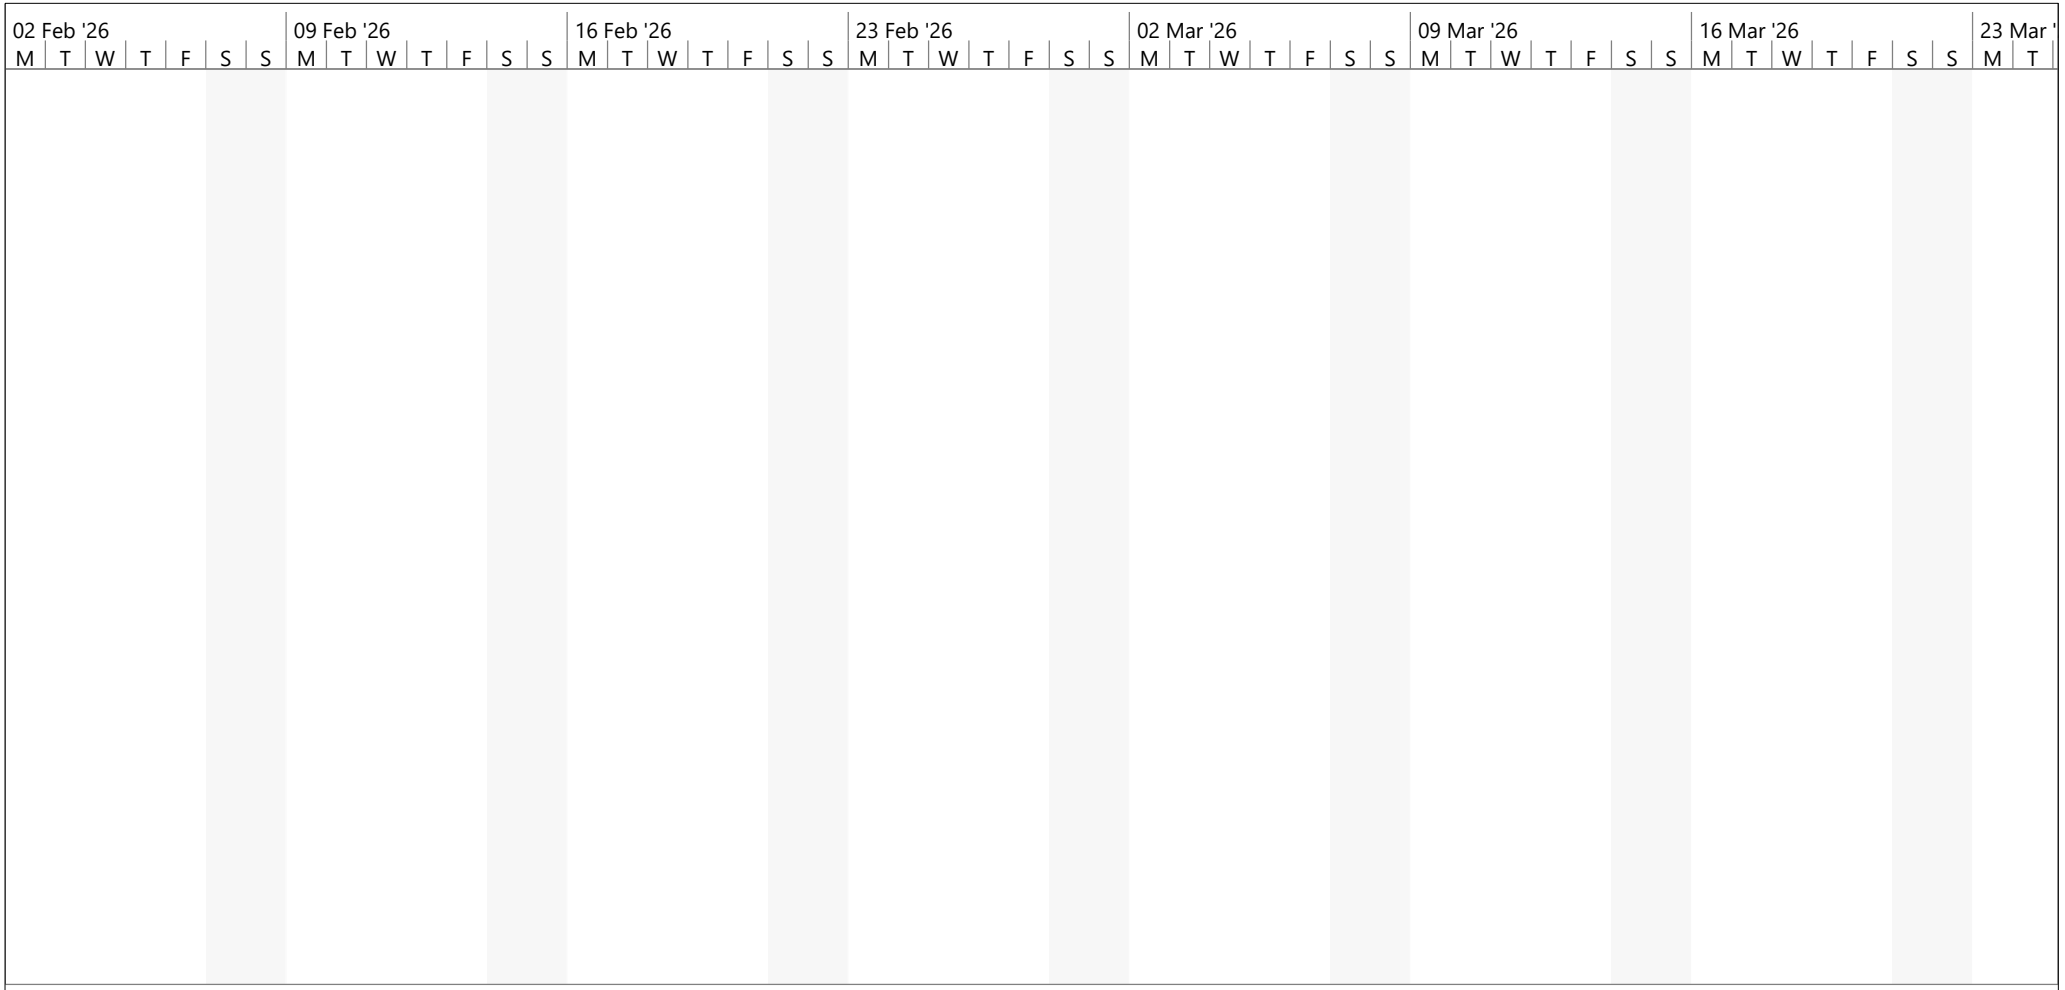


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

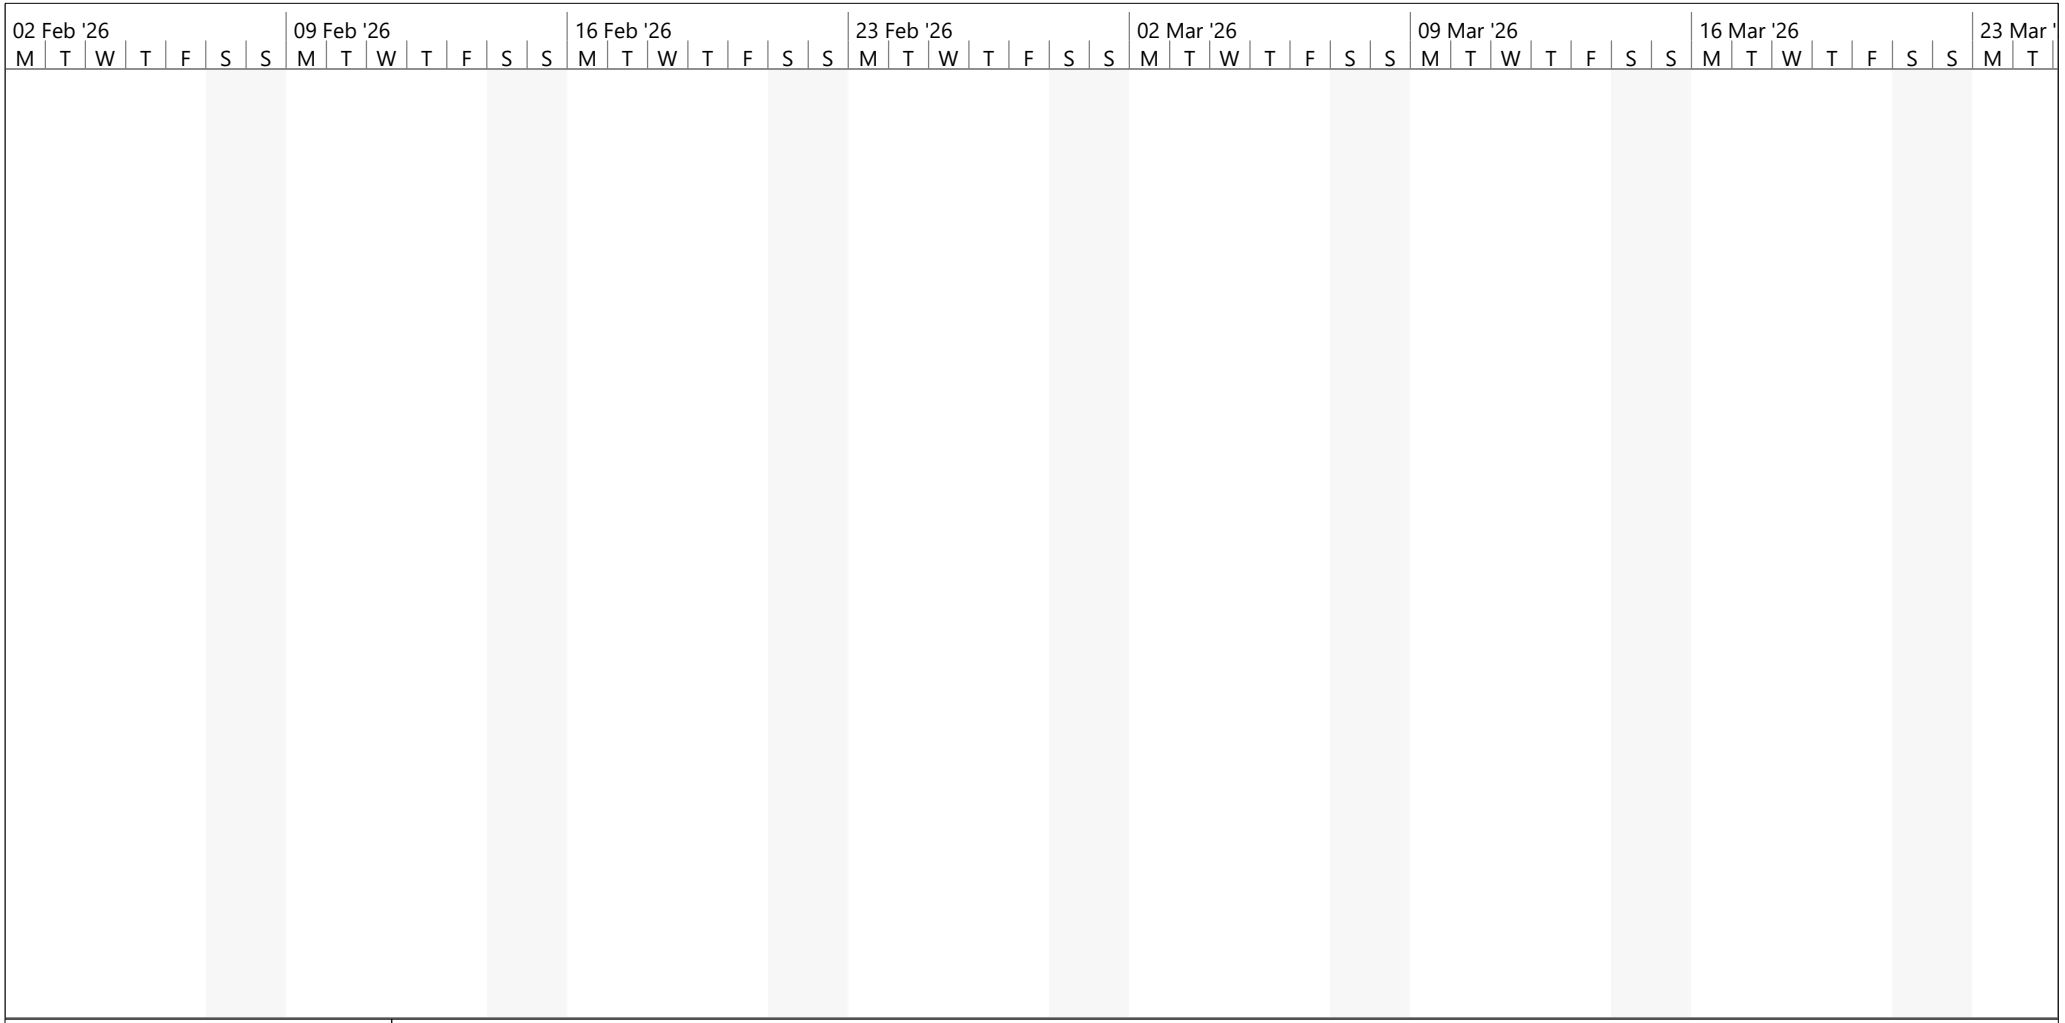


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

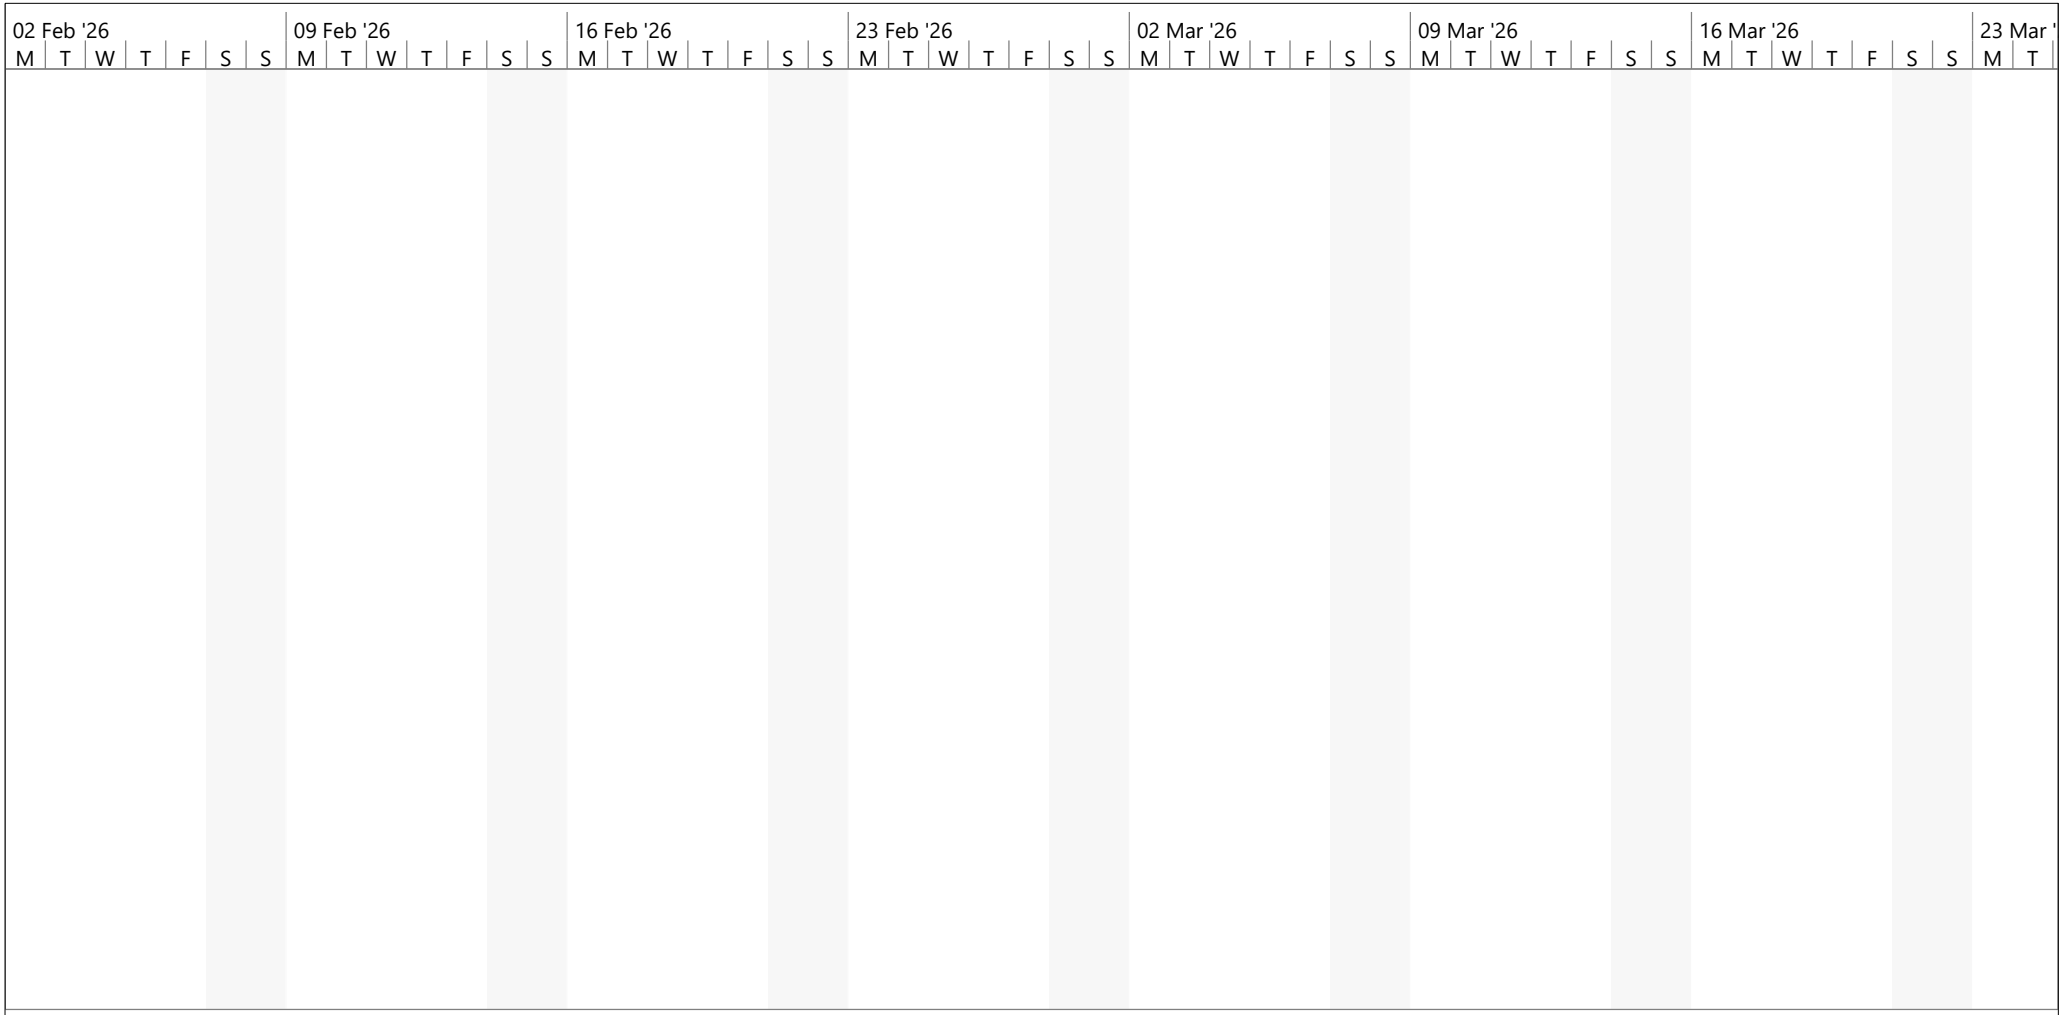


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

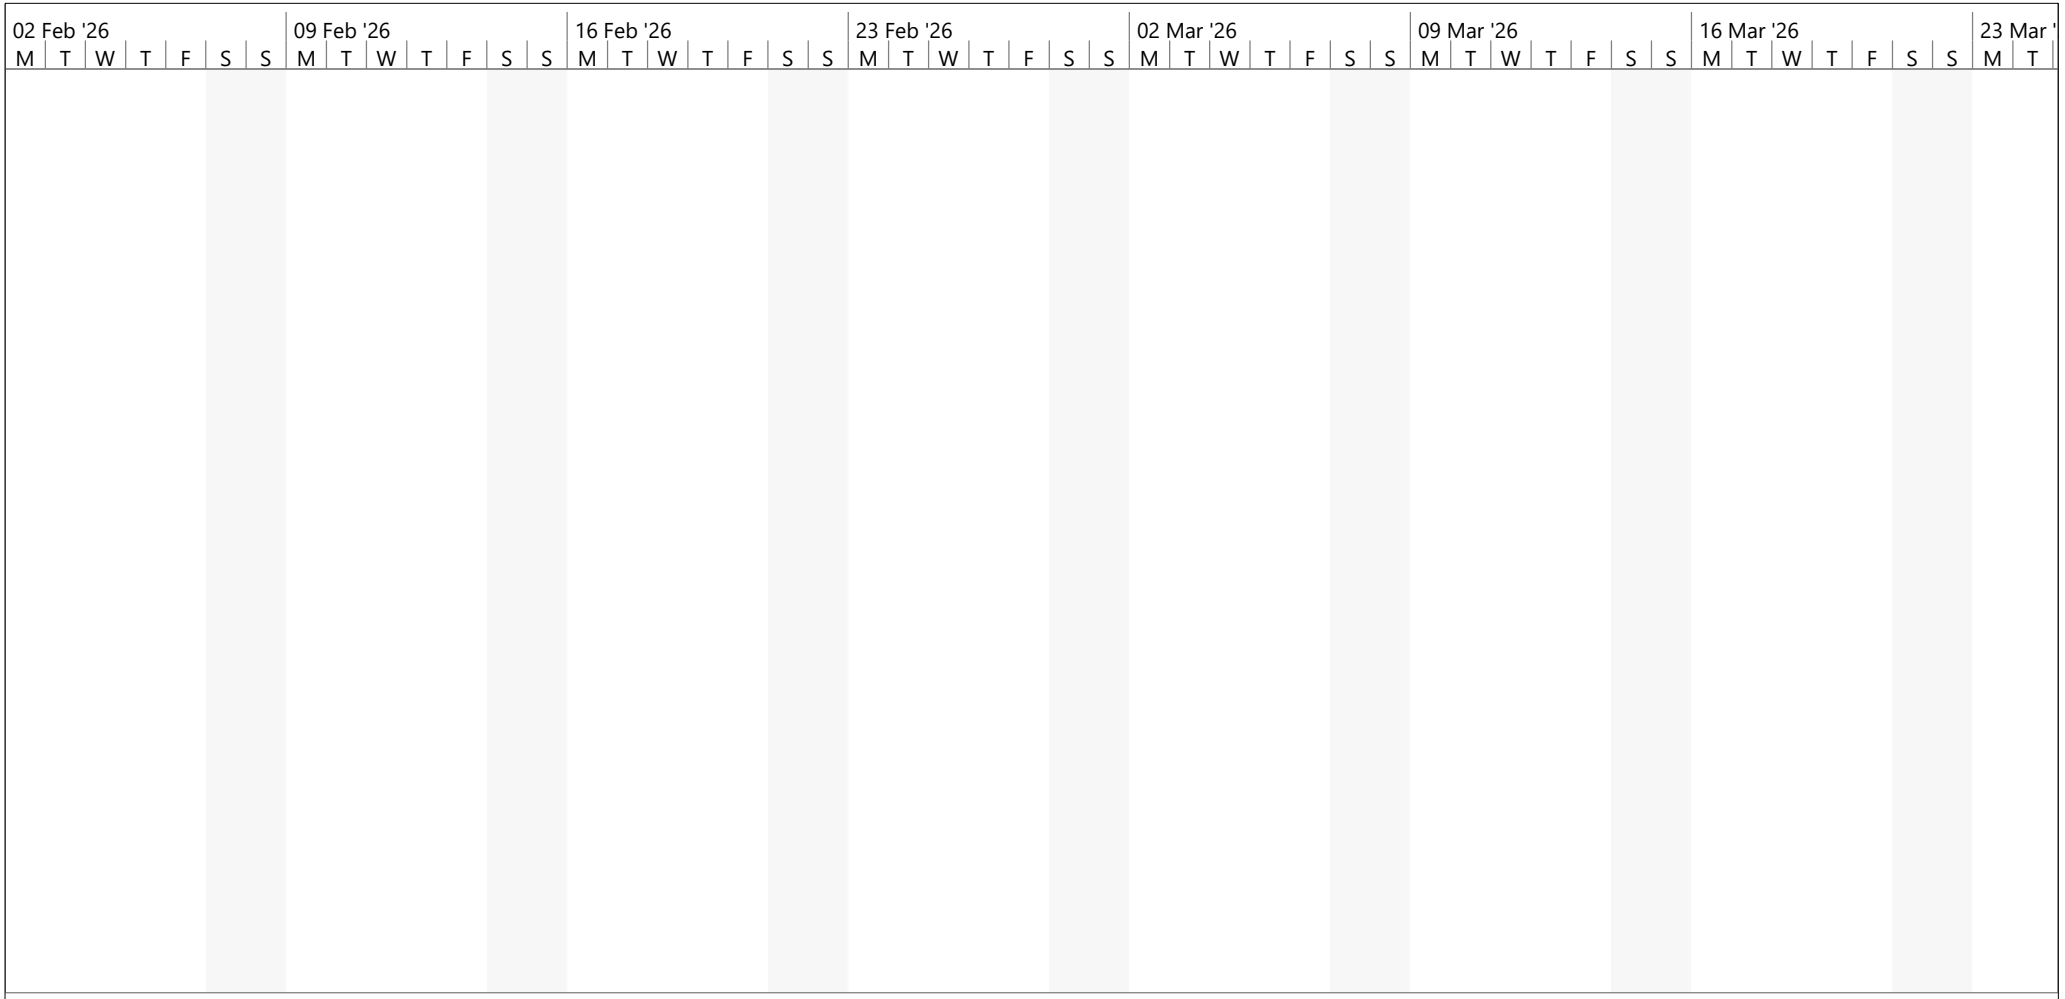


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

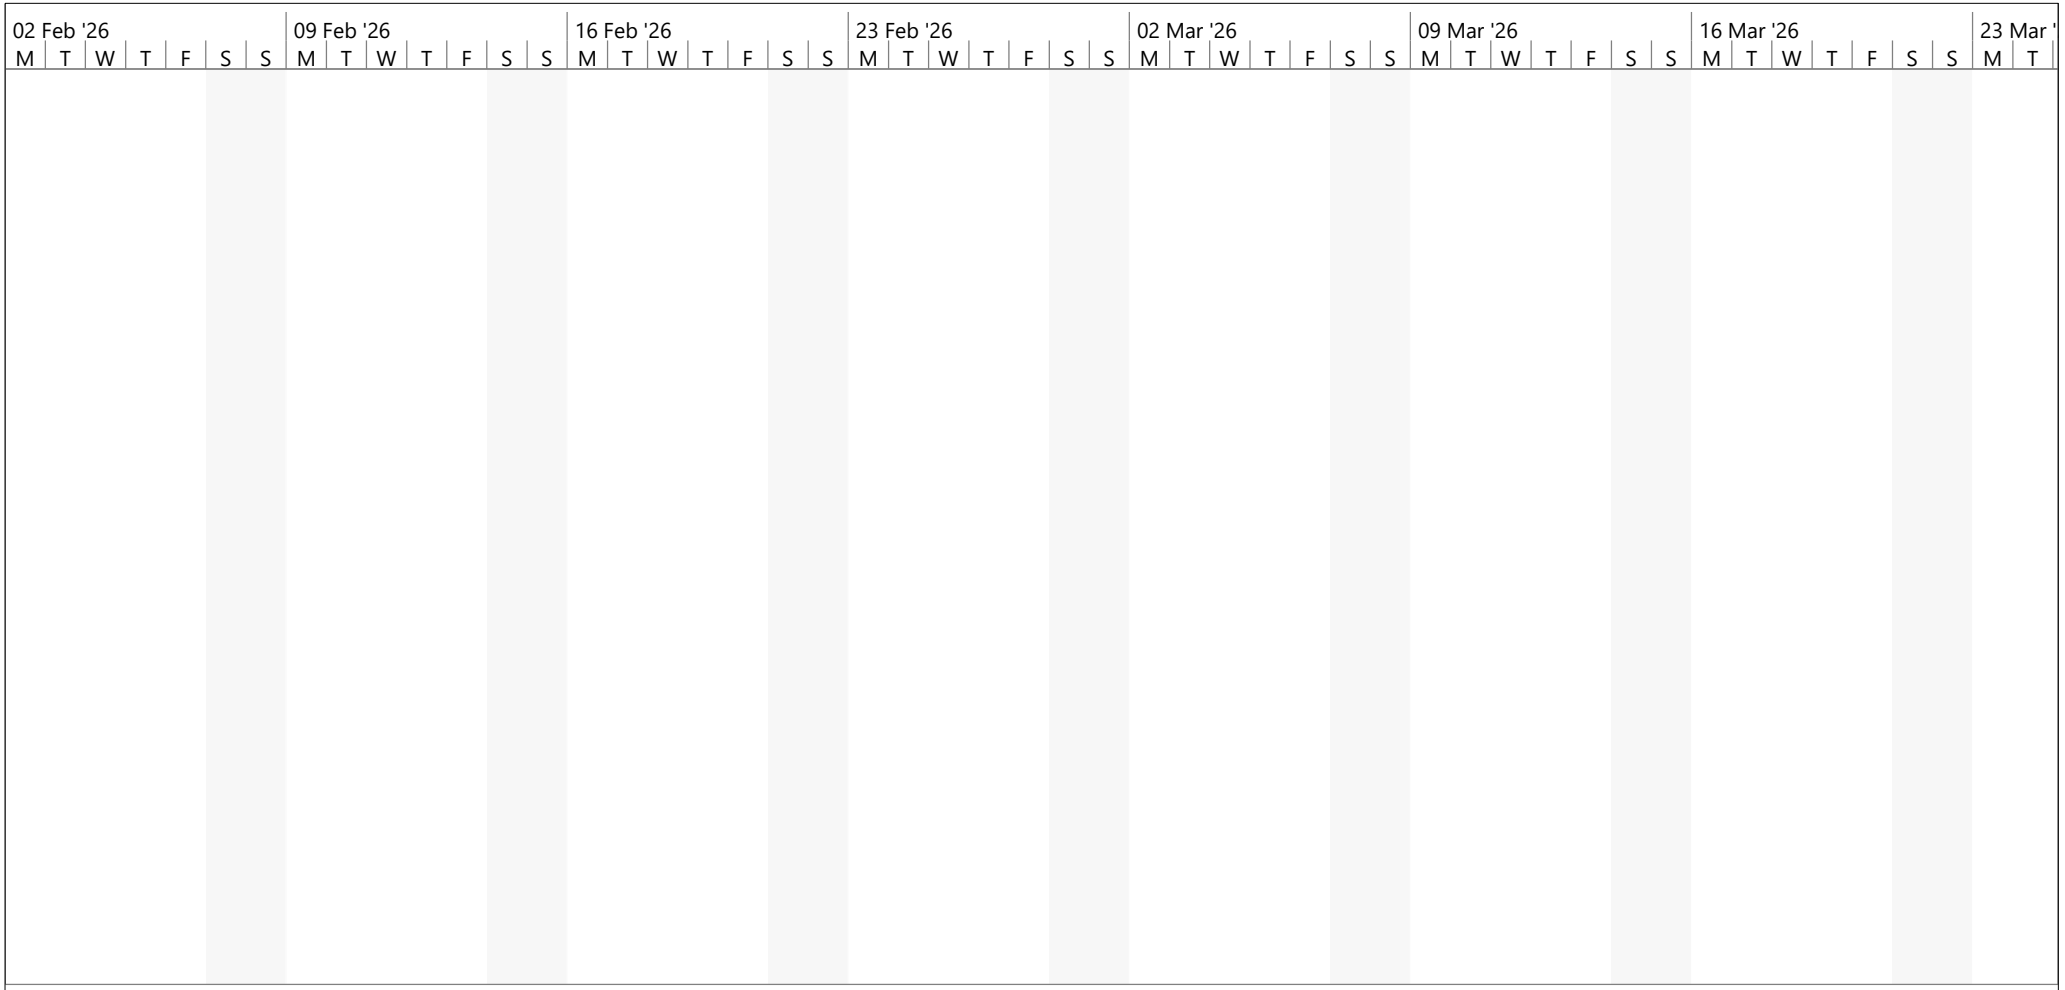


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

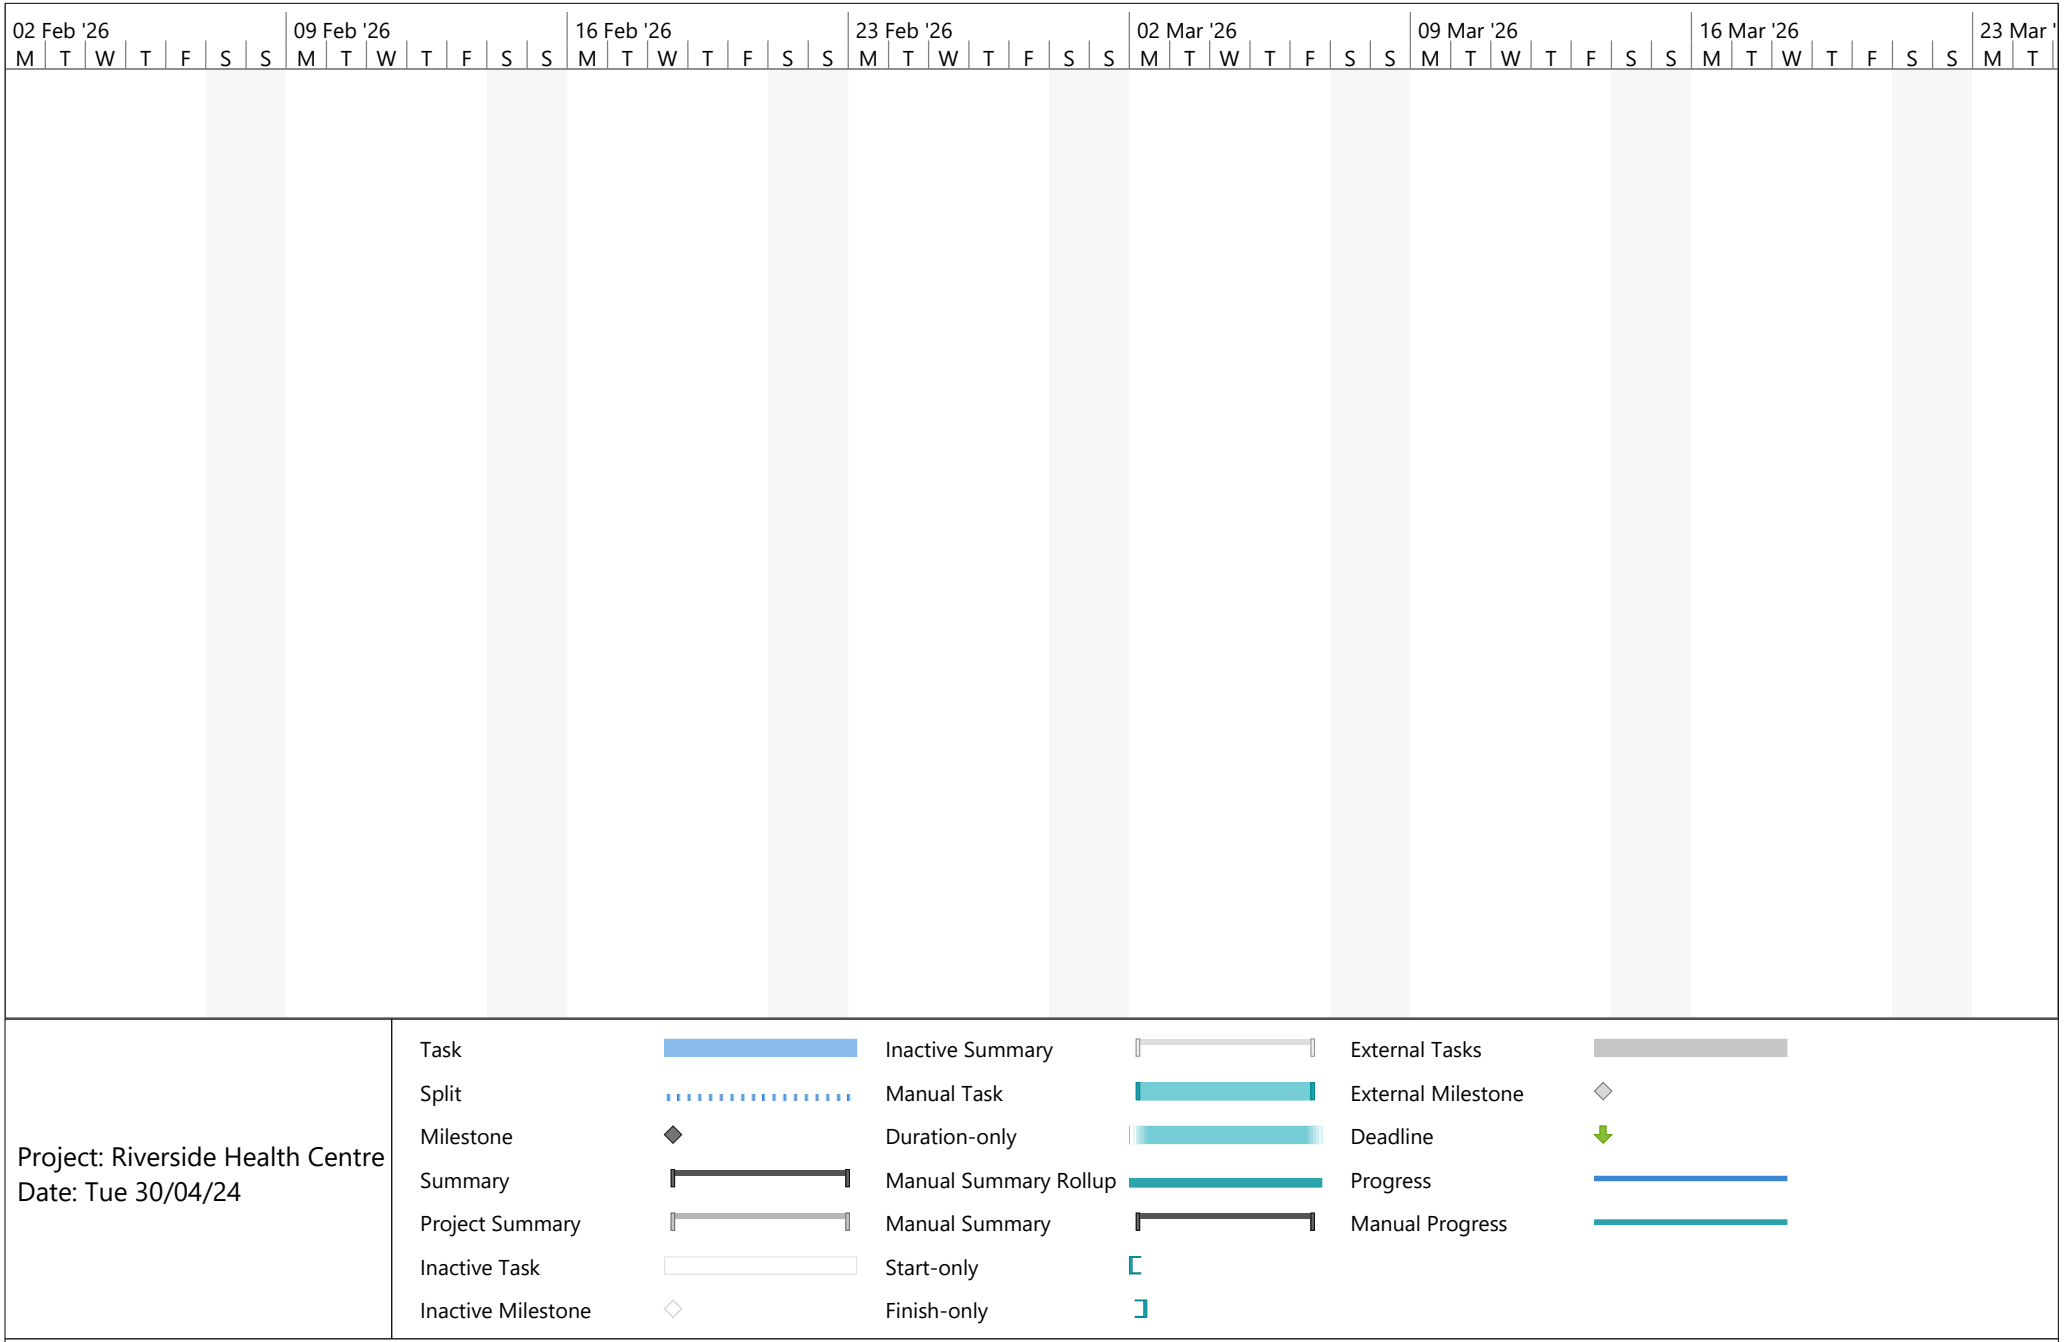


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

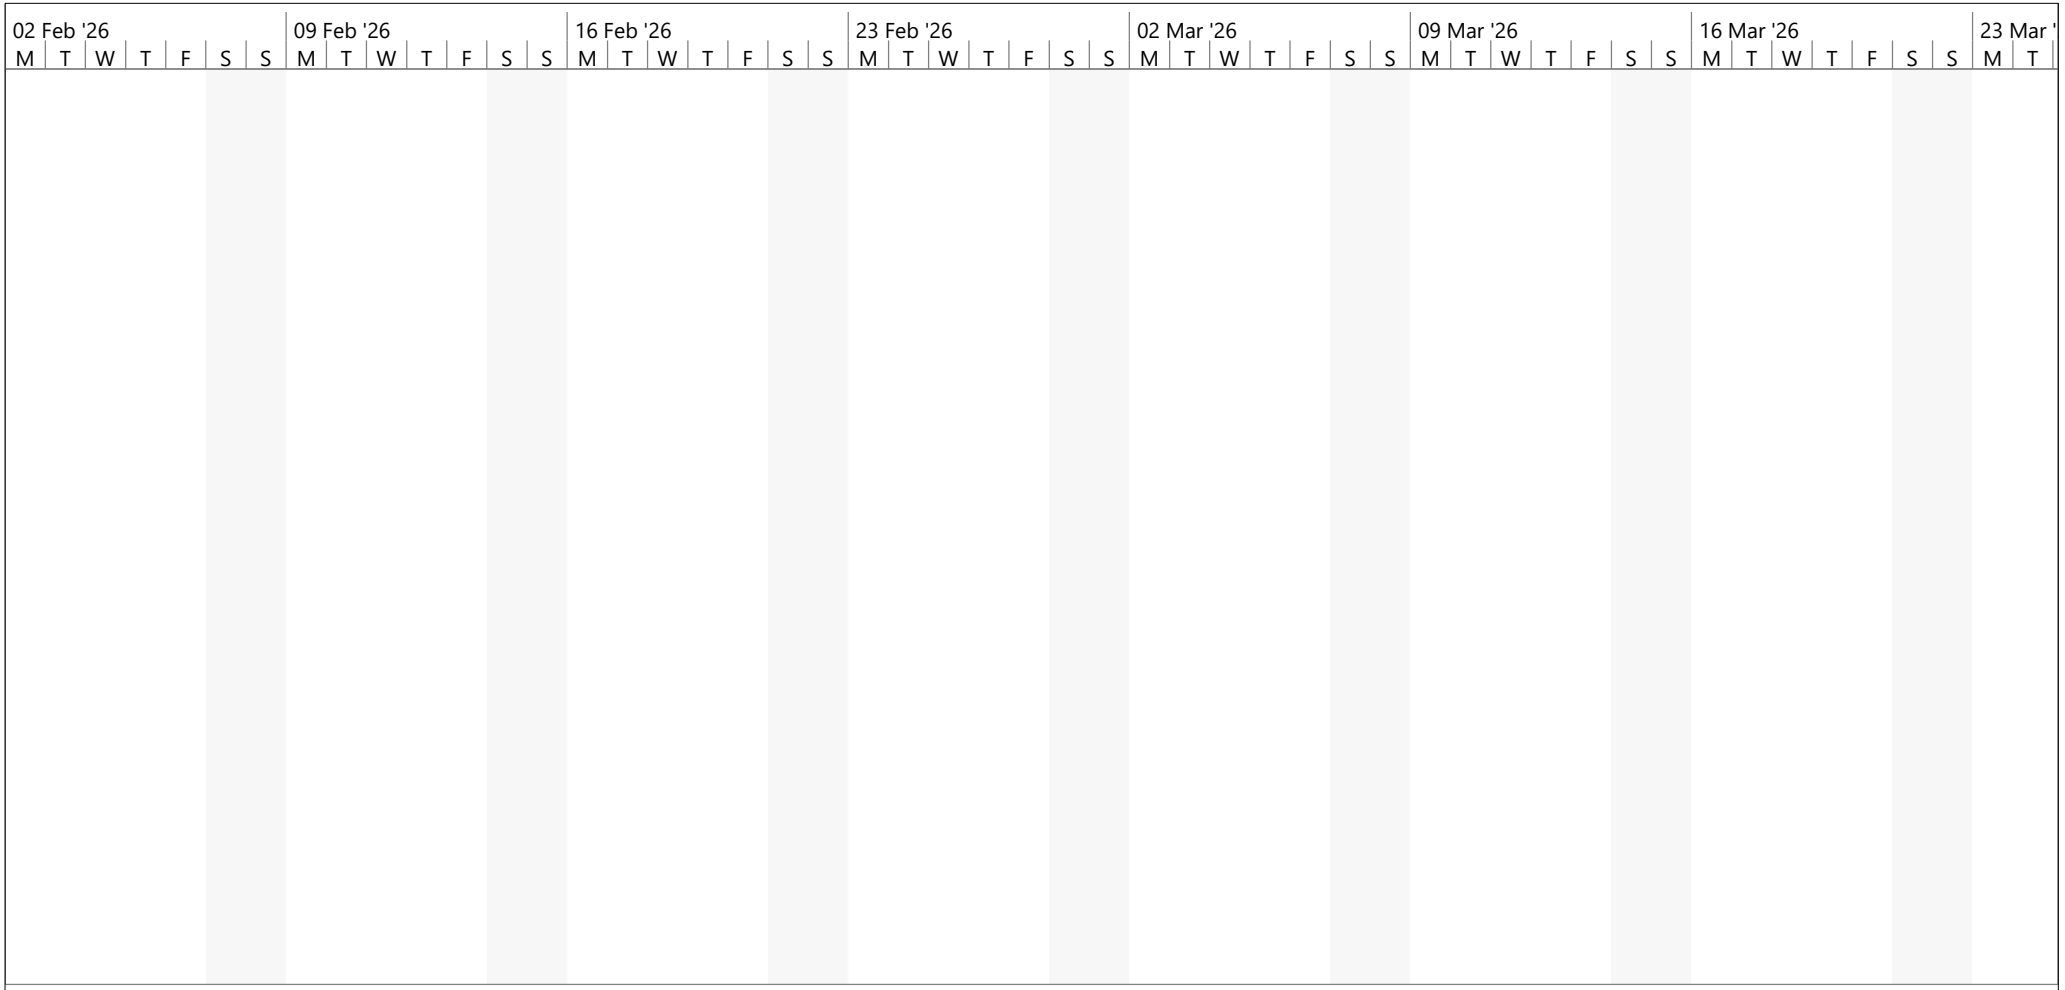


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

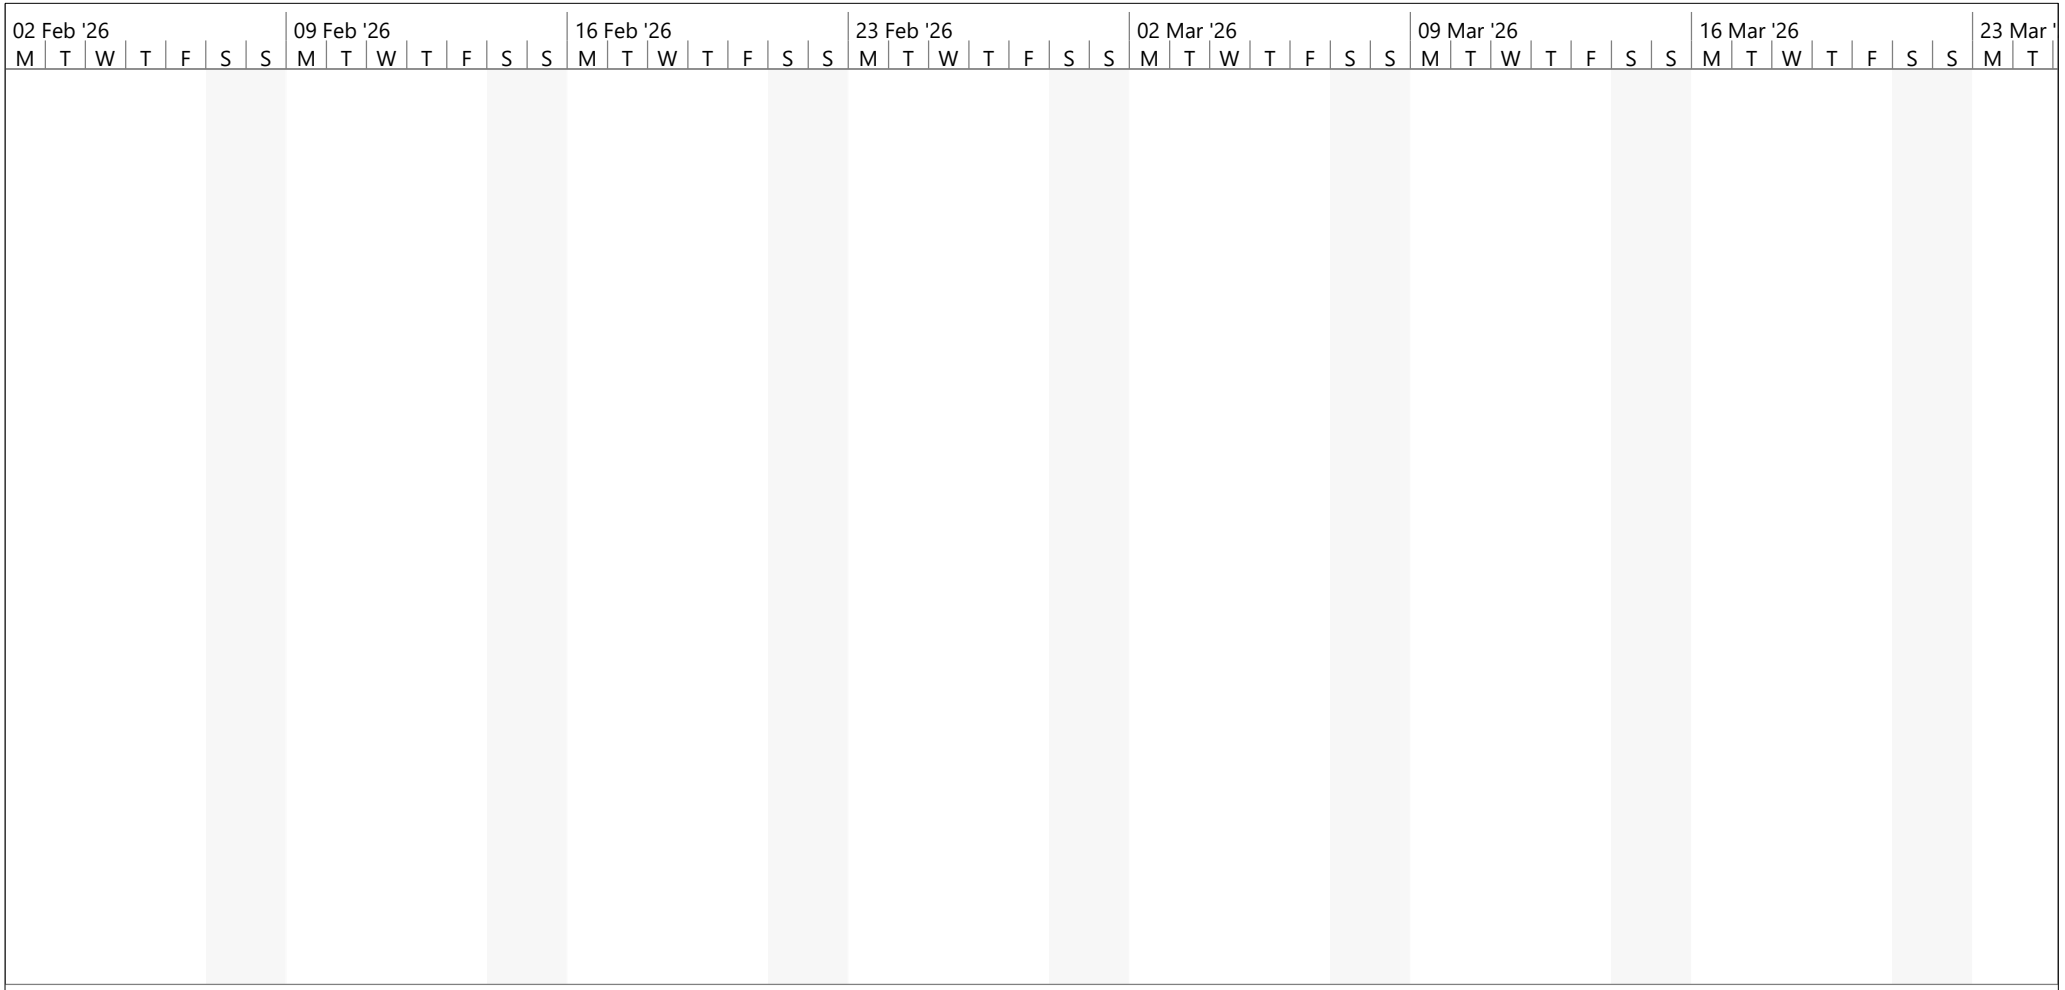


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

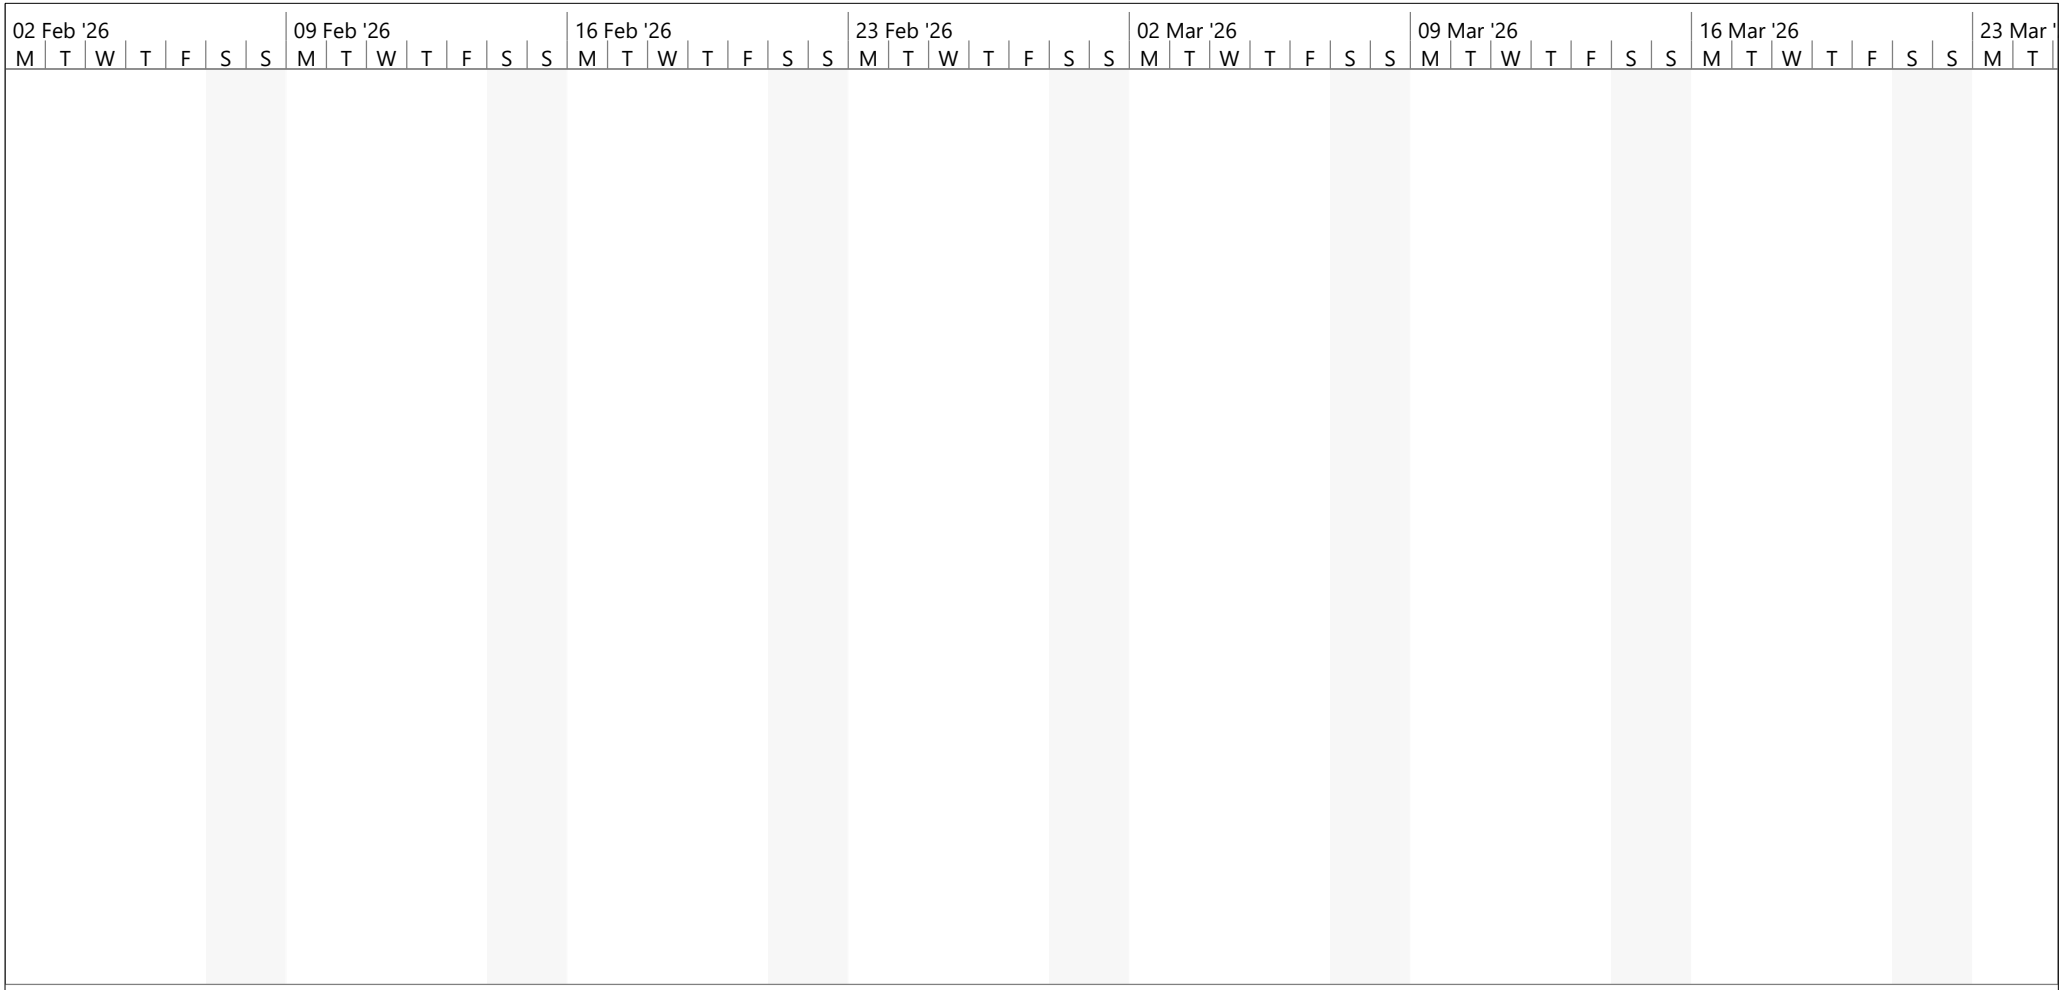

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

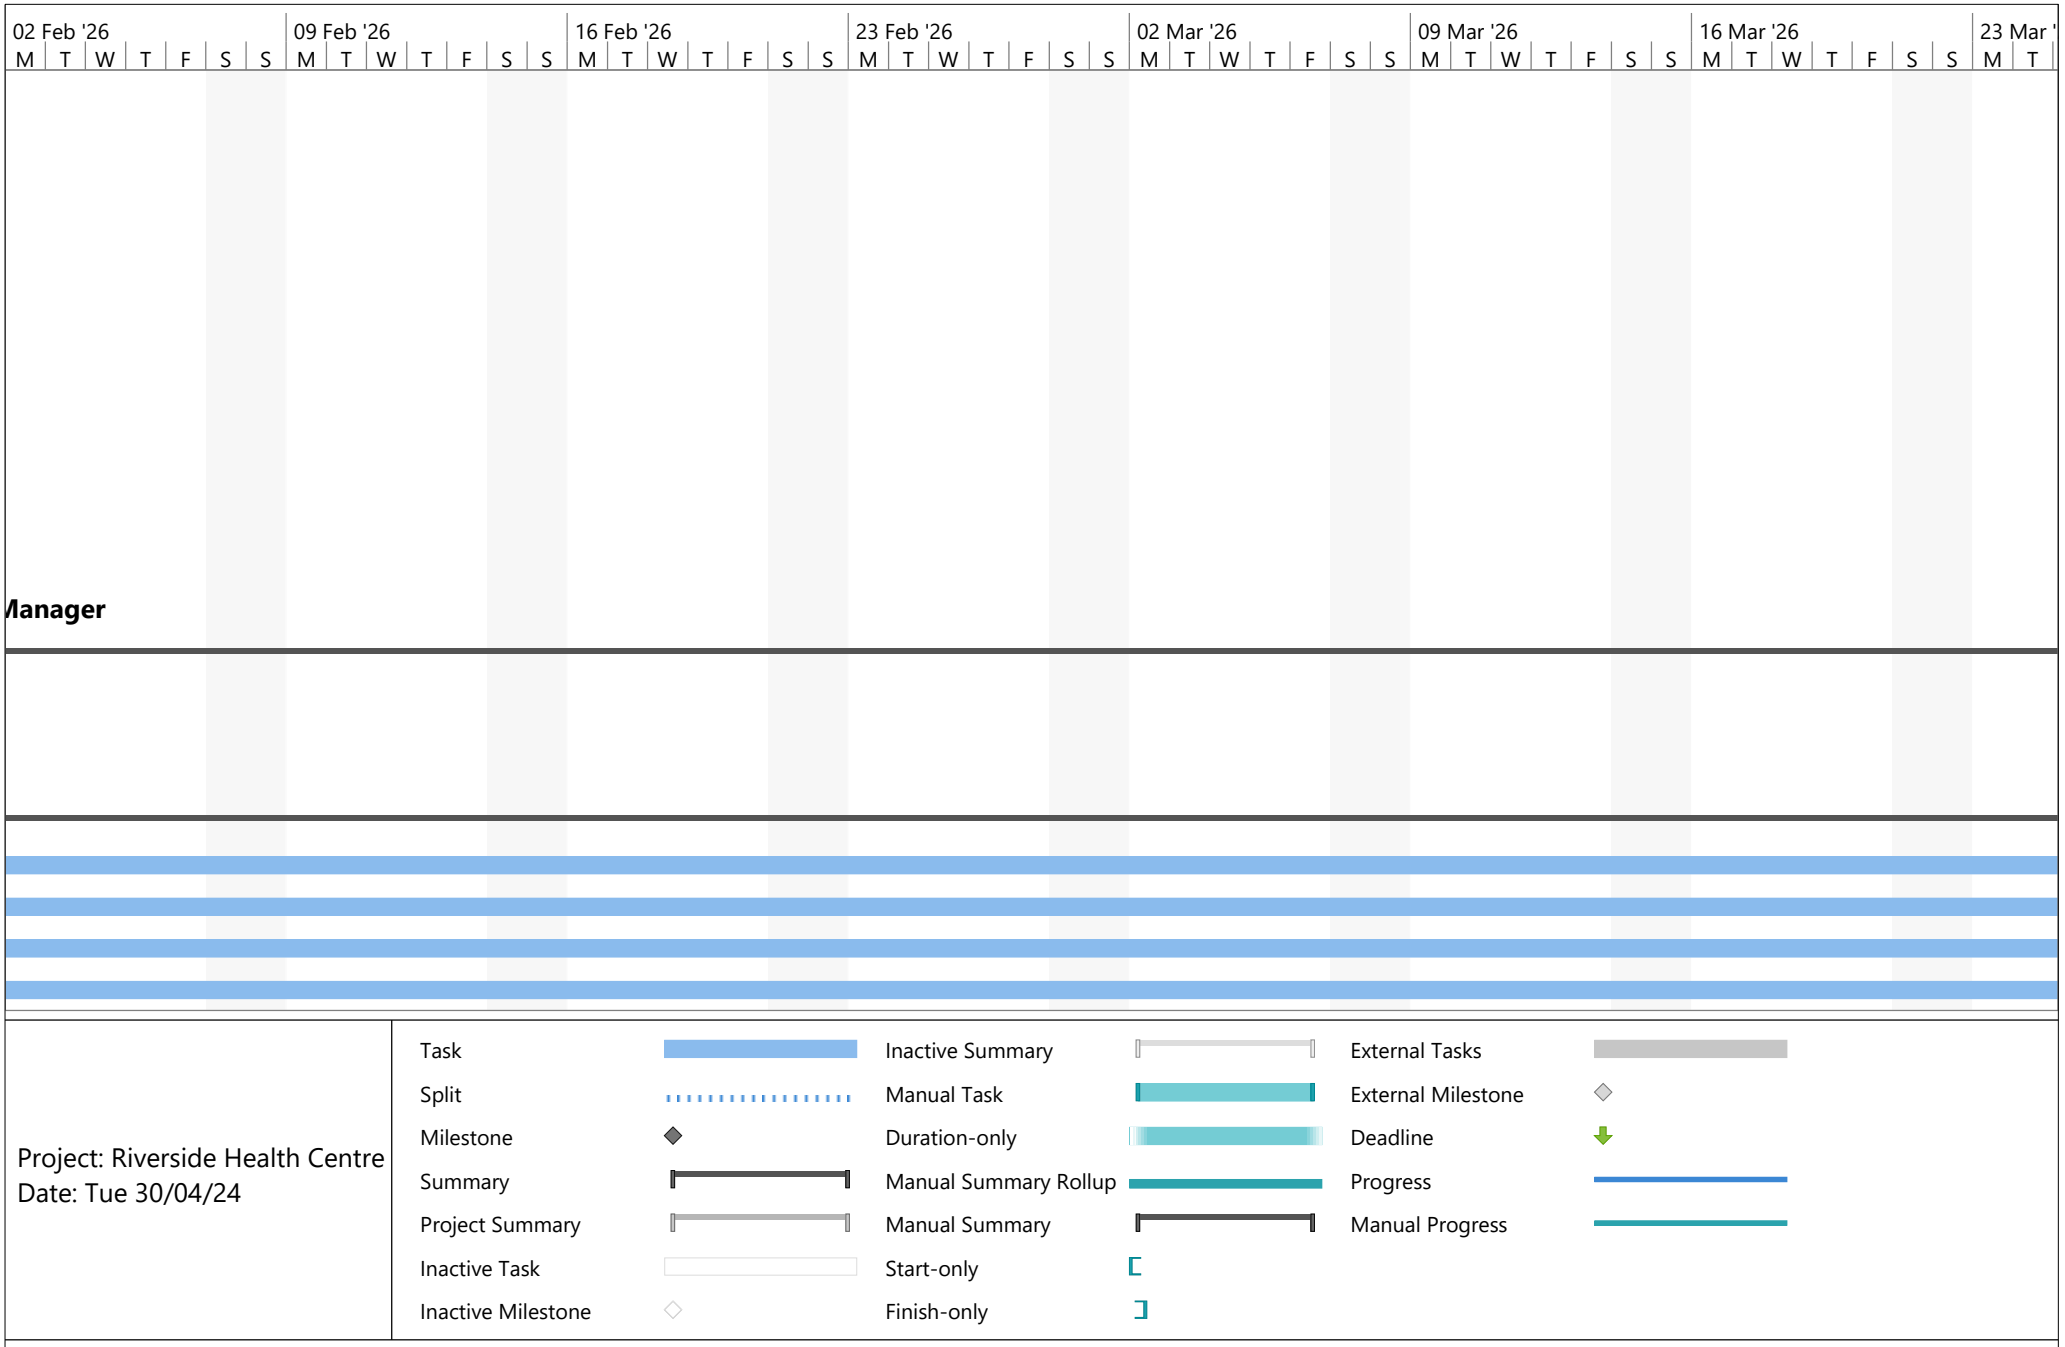

02 Feb '26
M T W T F S S
09 Feb '26
M T W T F S S
16 Feb '26
M T W T F S S
23 Feb '26
M T W T F S S
02 Mar '26
M T W T F S S
09 Mar '26
M T W T F S S
16 Mar '26
M T W T F S S
23 Mar '
M T
Manager
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress



Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

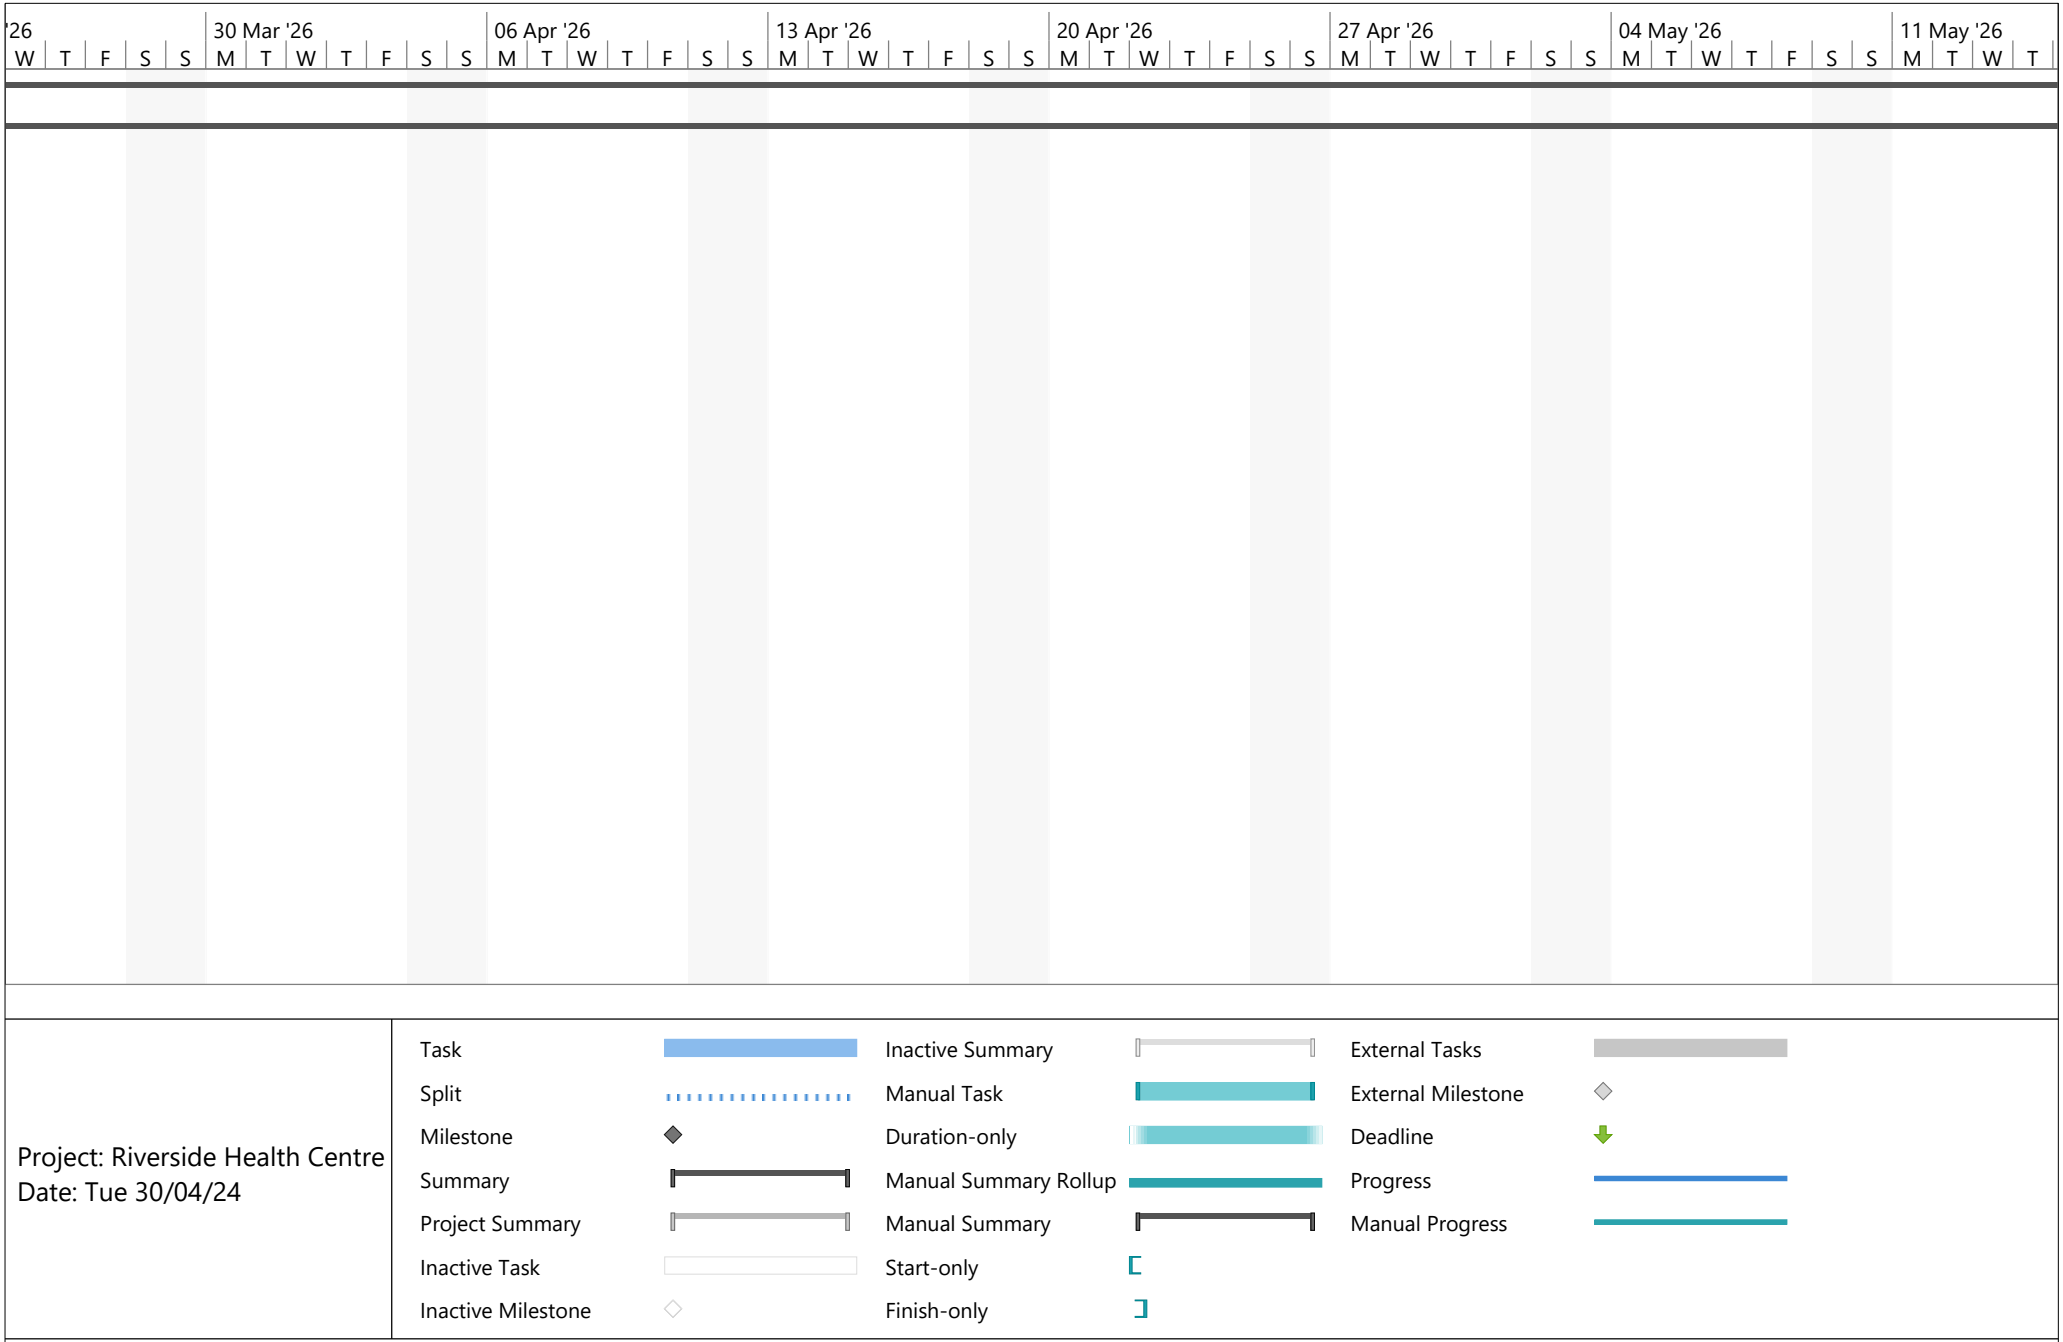
'26
W T F S S
30 Mar '26
M T W T F S S
06 Apr '26
M T W T F S S
13 Apr '26
M T W T F S S
20 Apr '26
M T W T F S S
27 Apr '26
M T W T F S S
04 May '26
M T W T F S S
11 May '26
M T W T
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

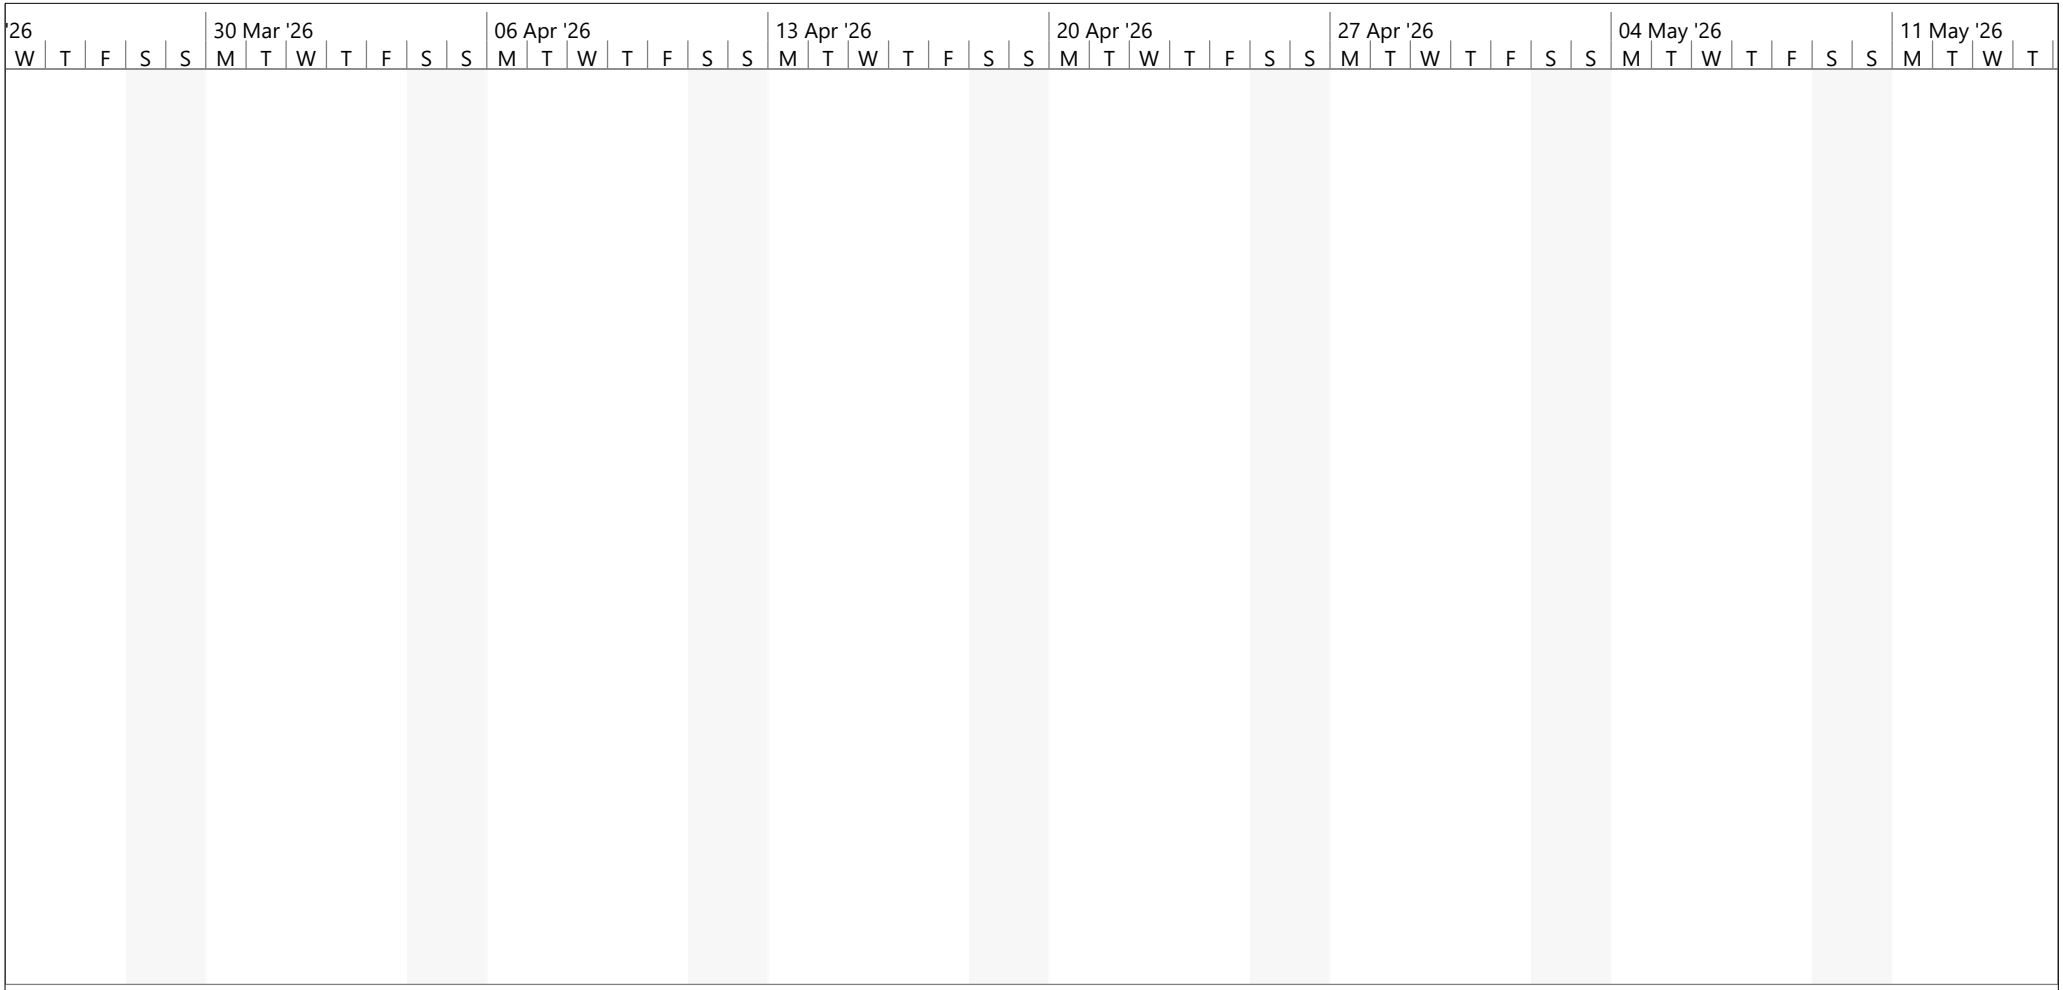


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

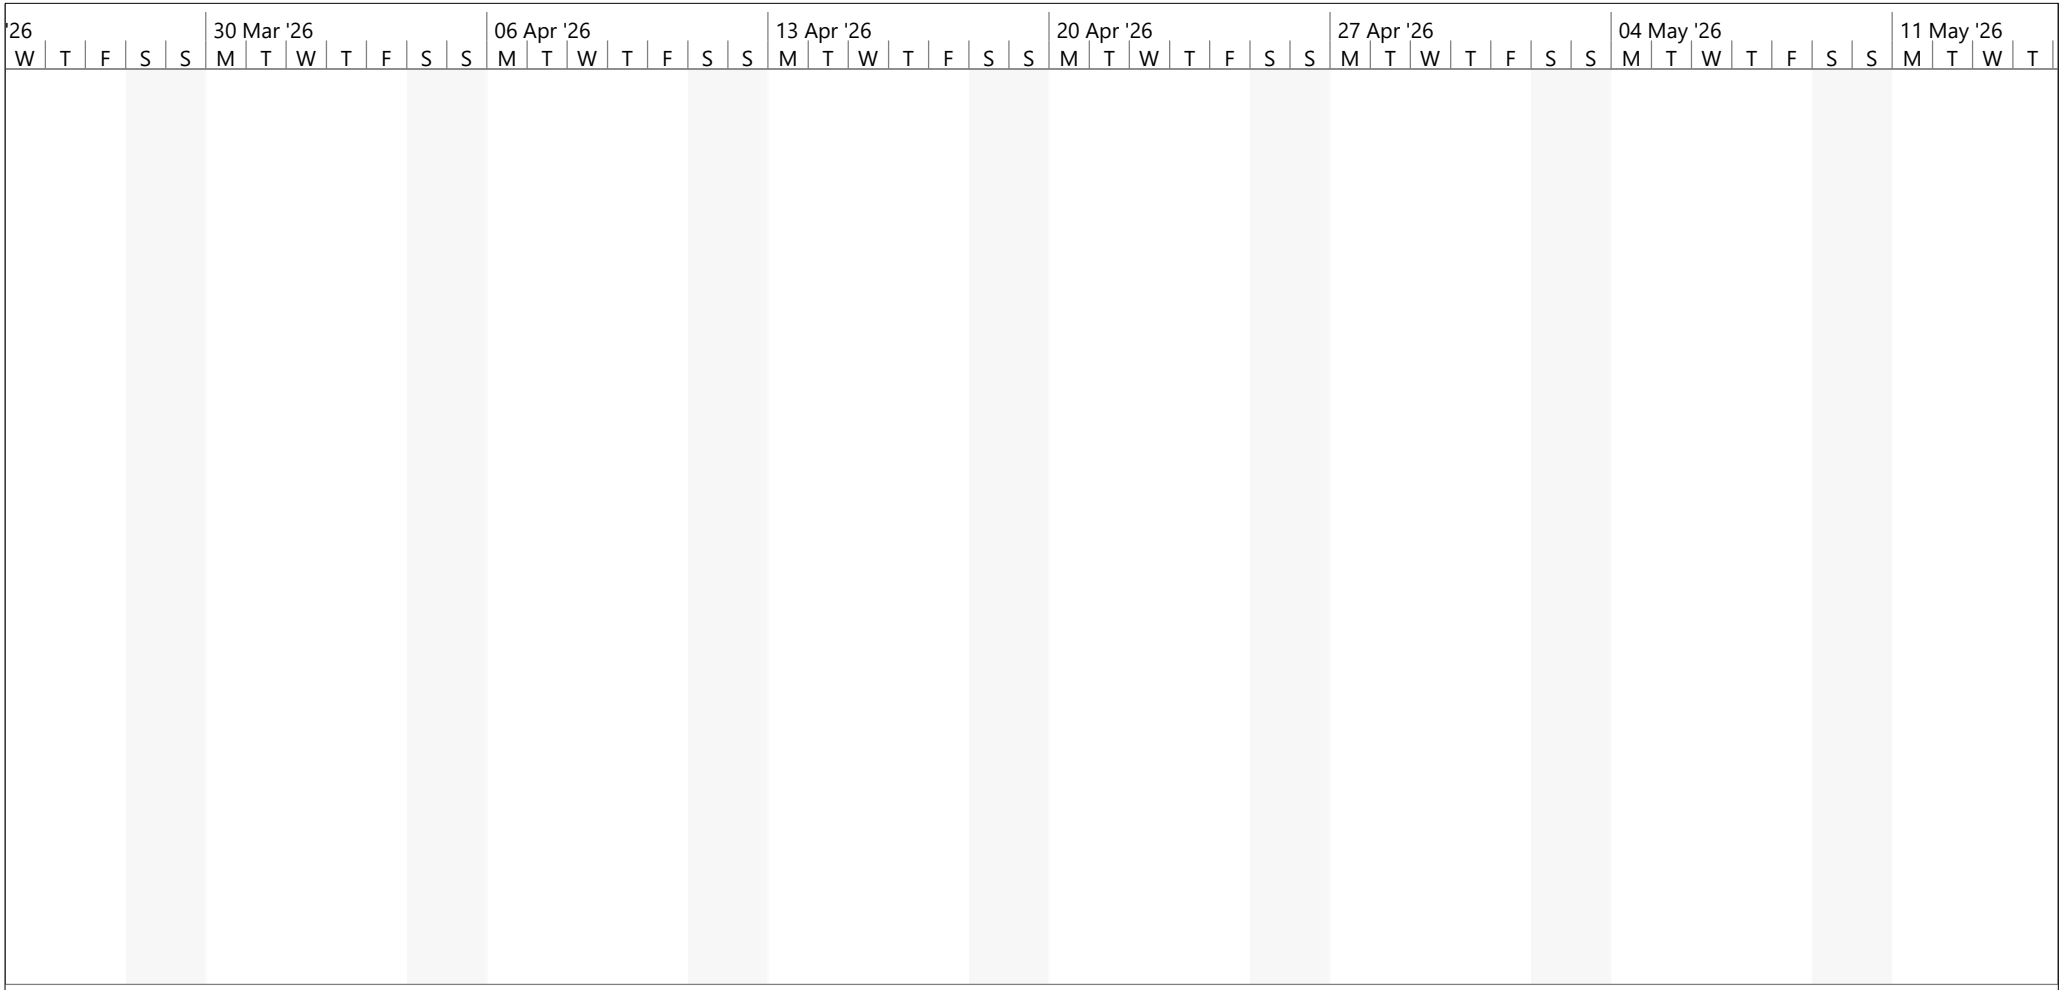


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

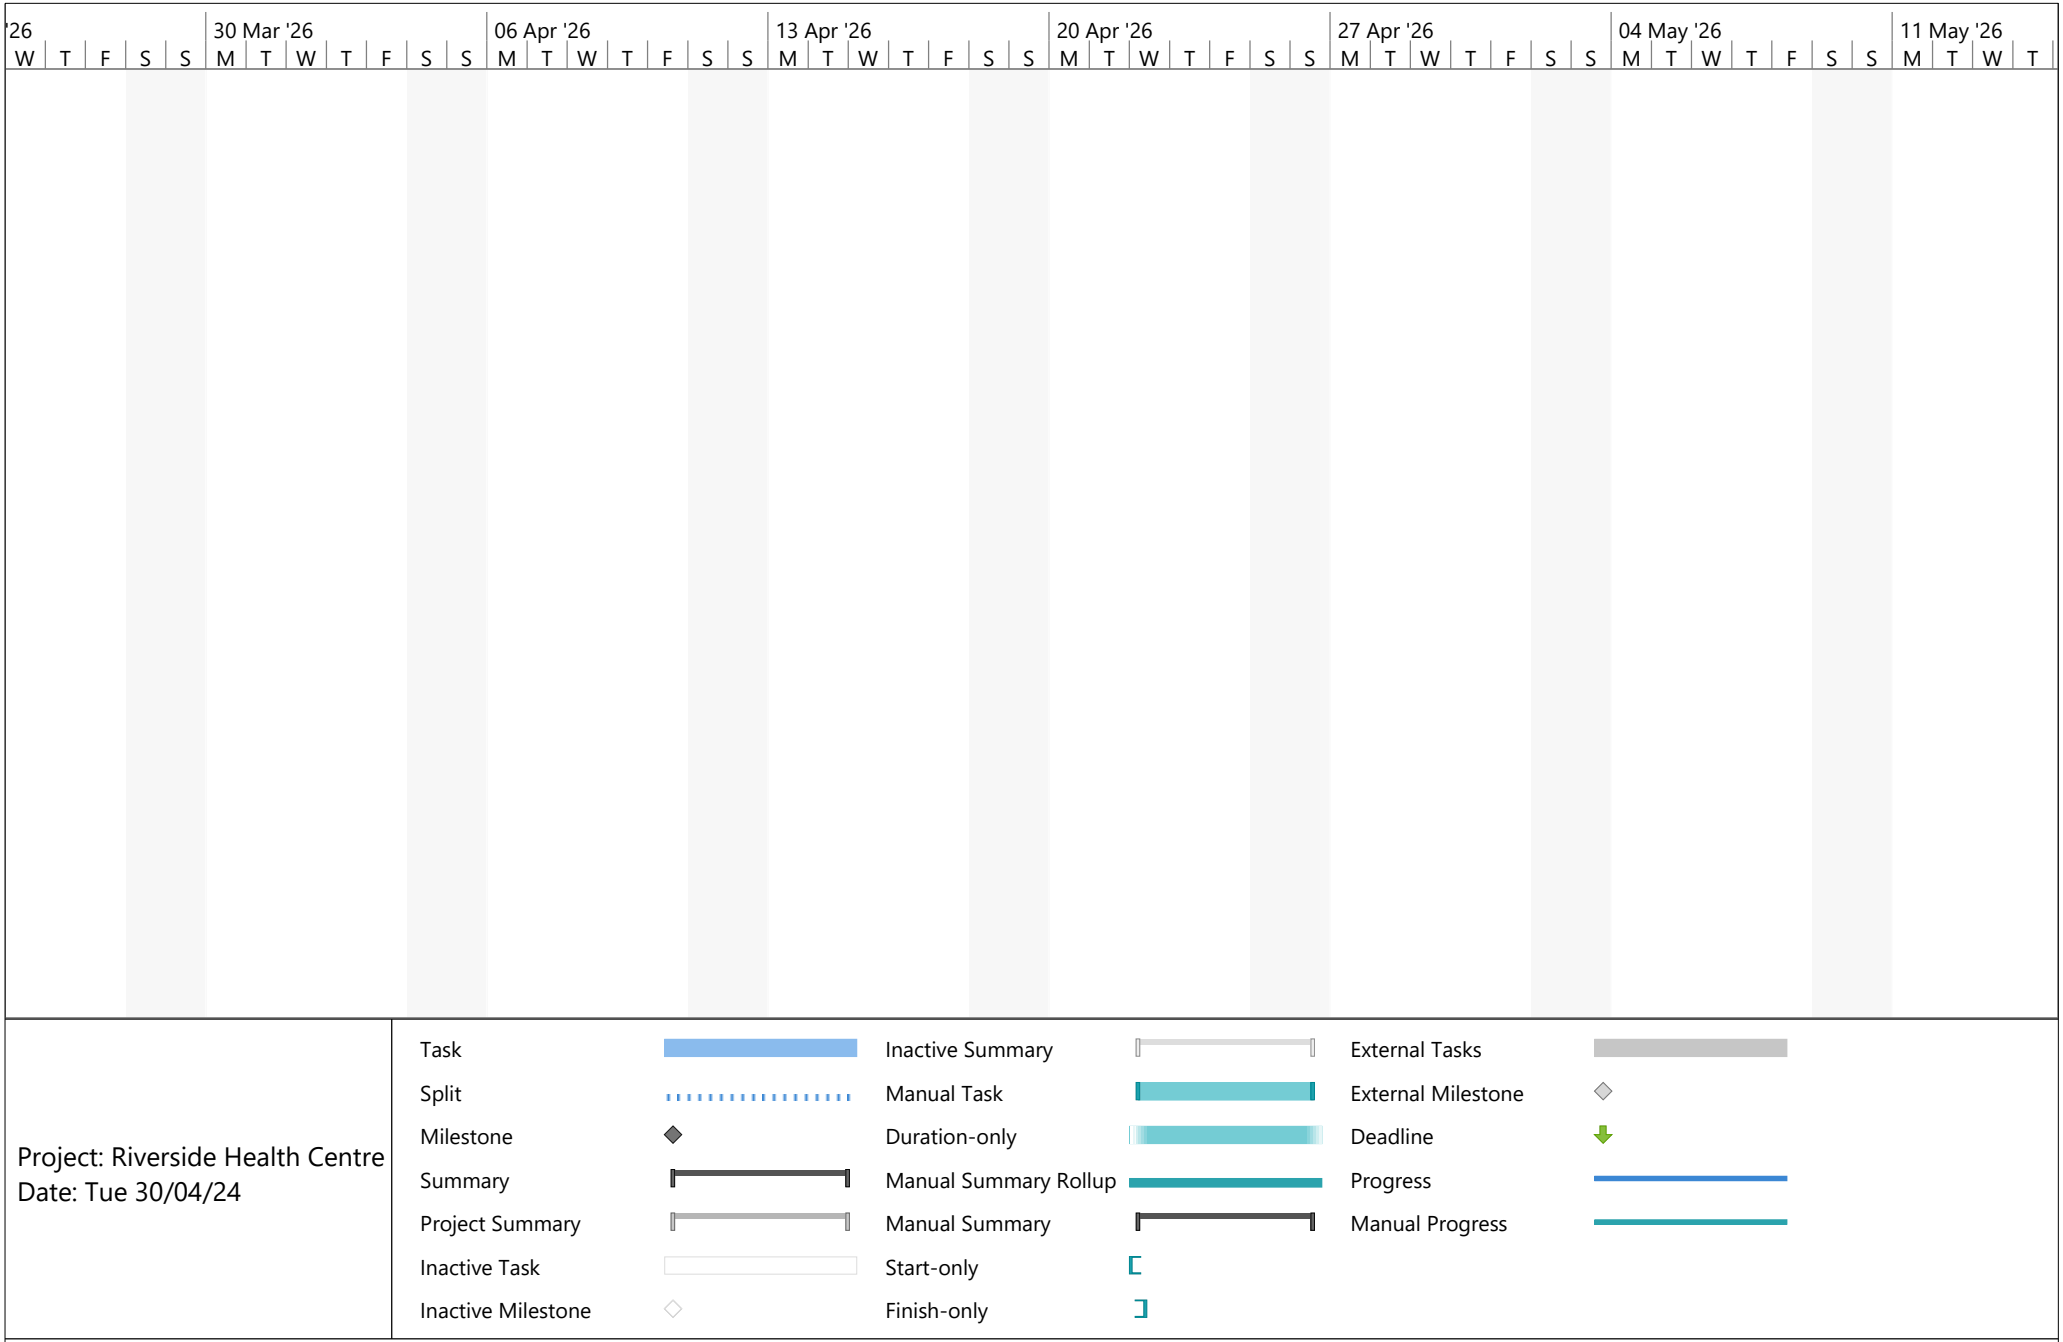


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

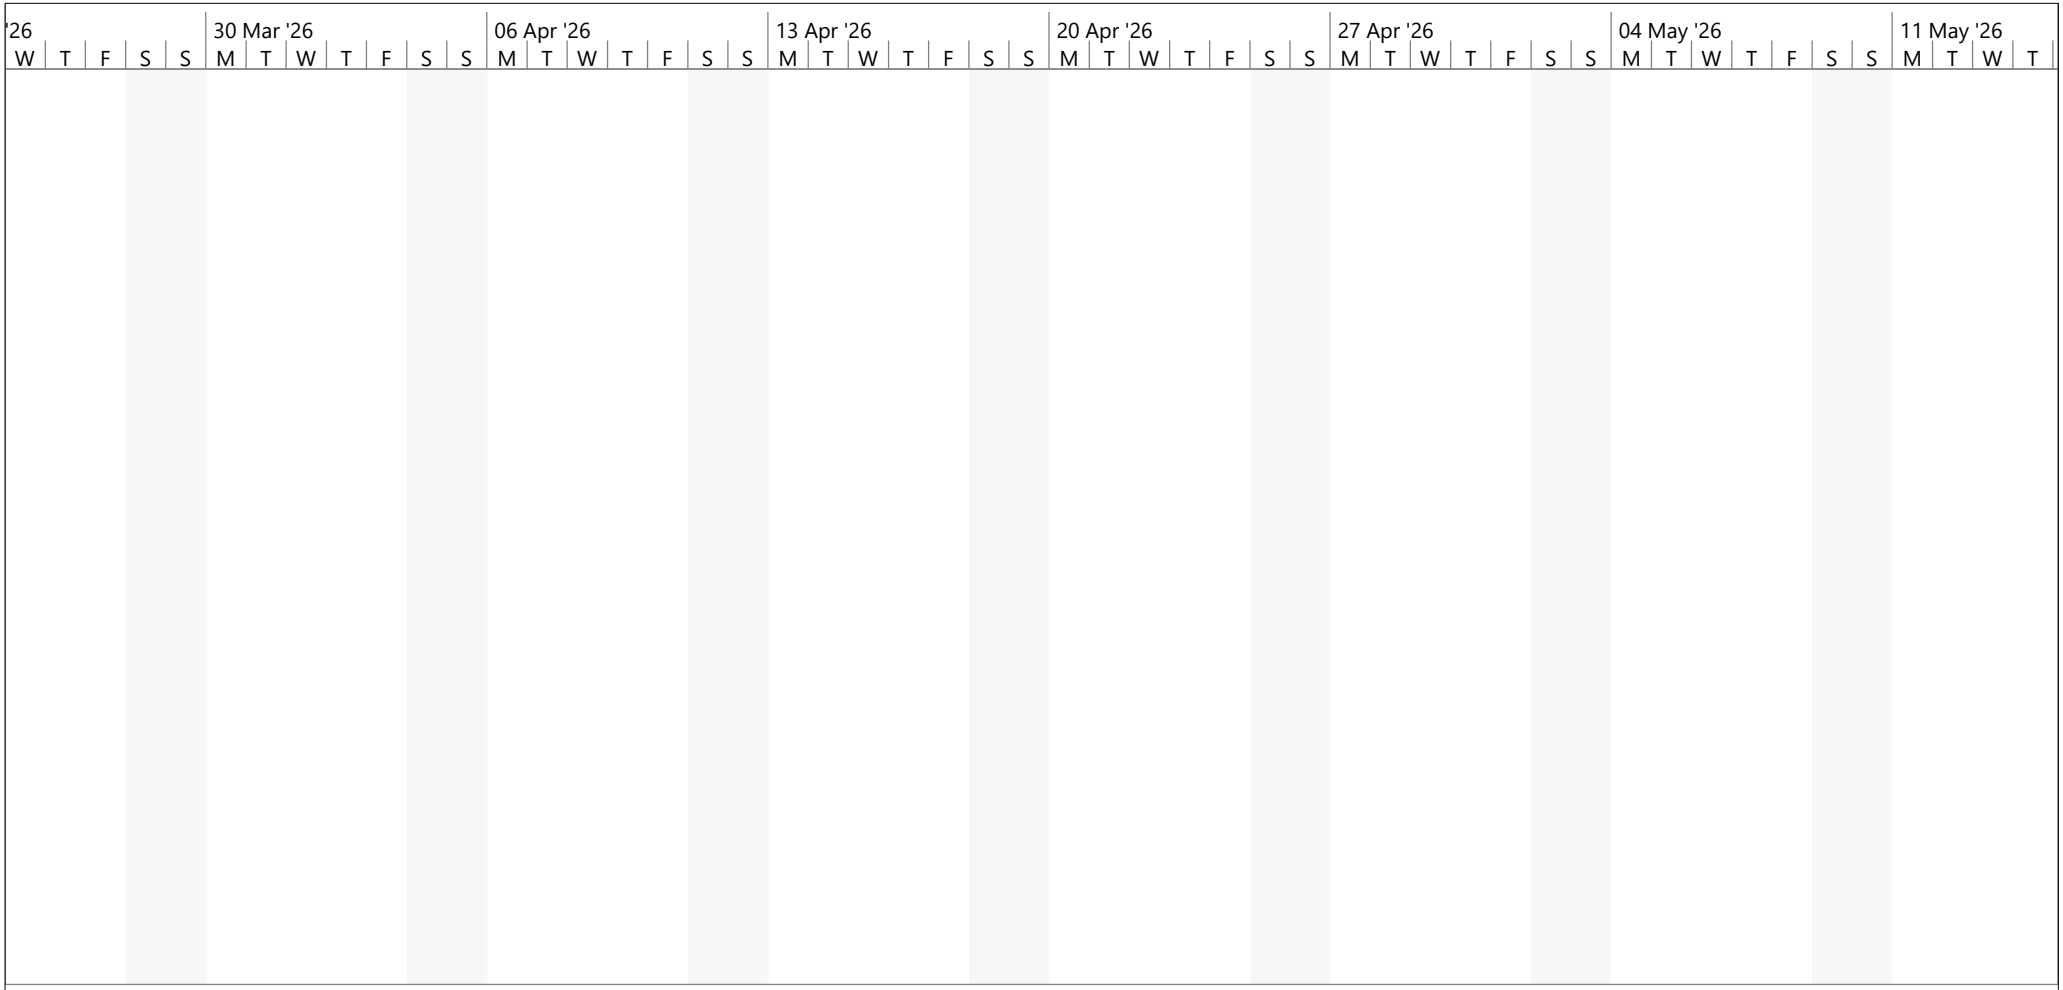


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

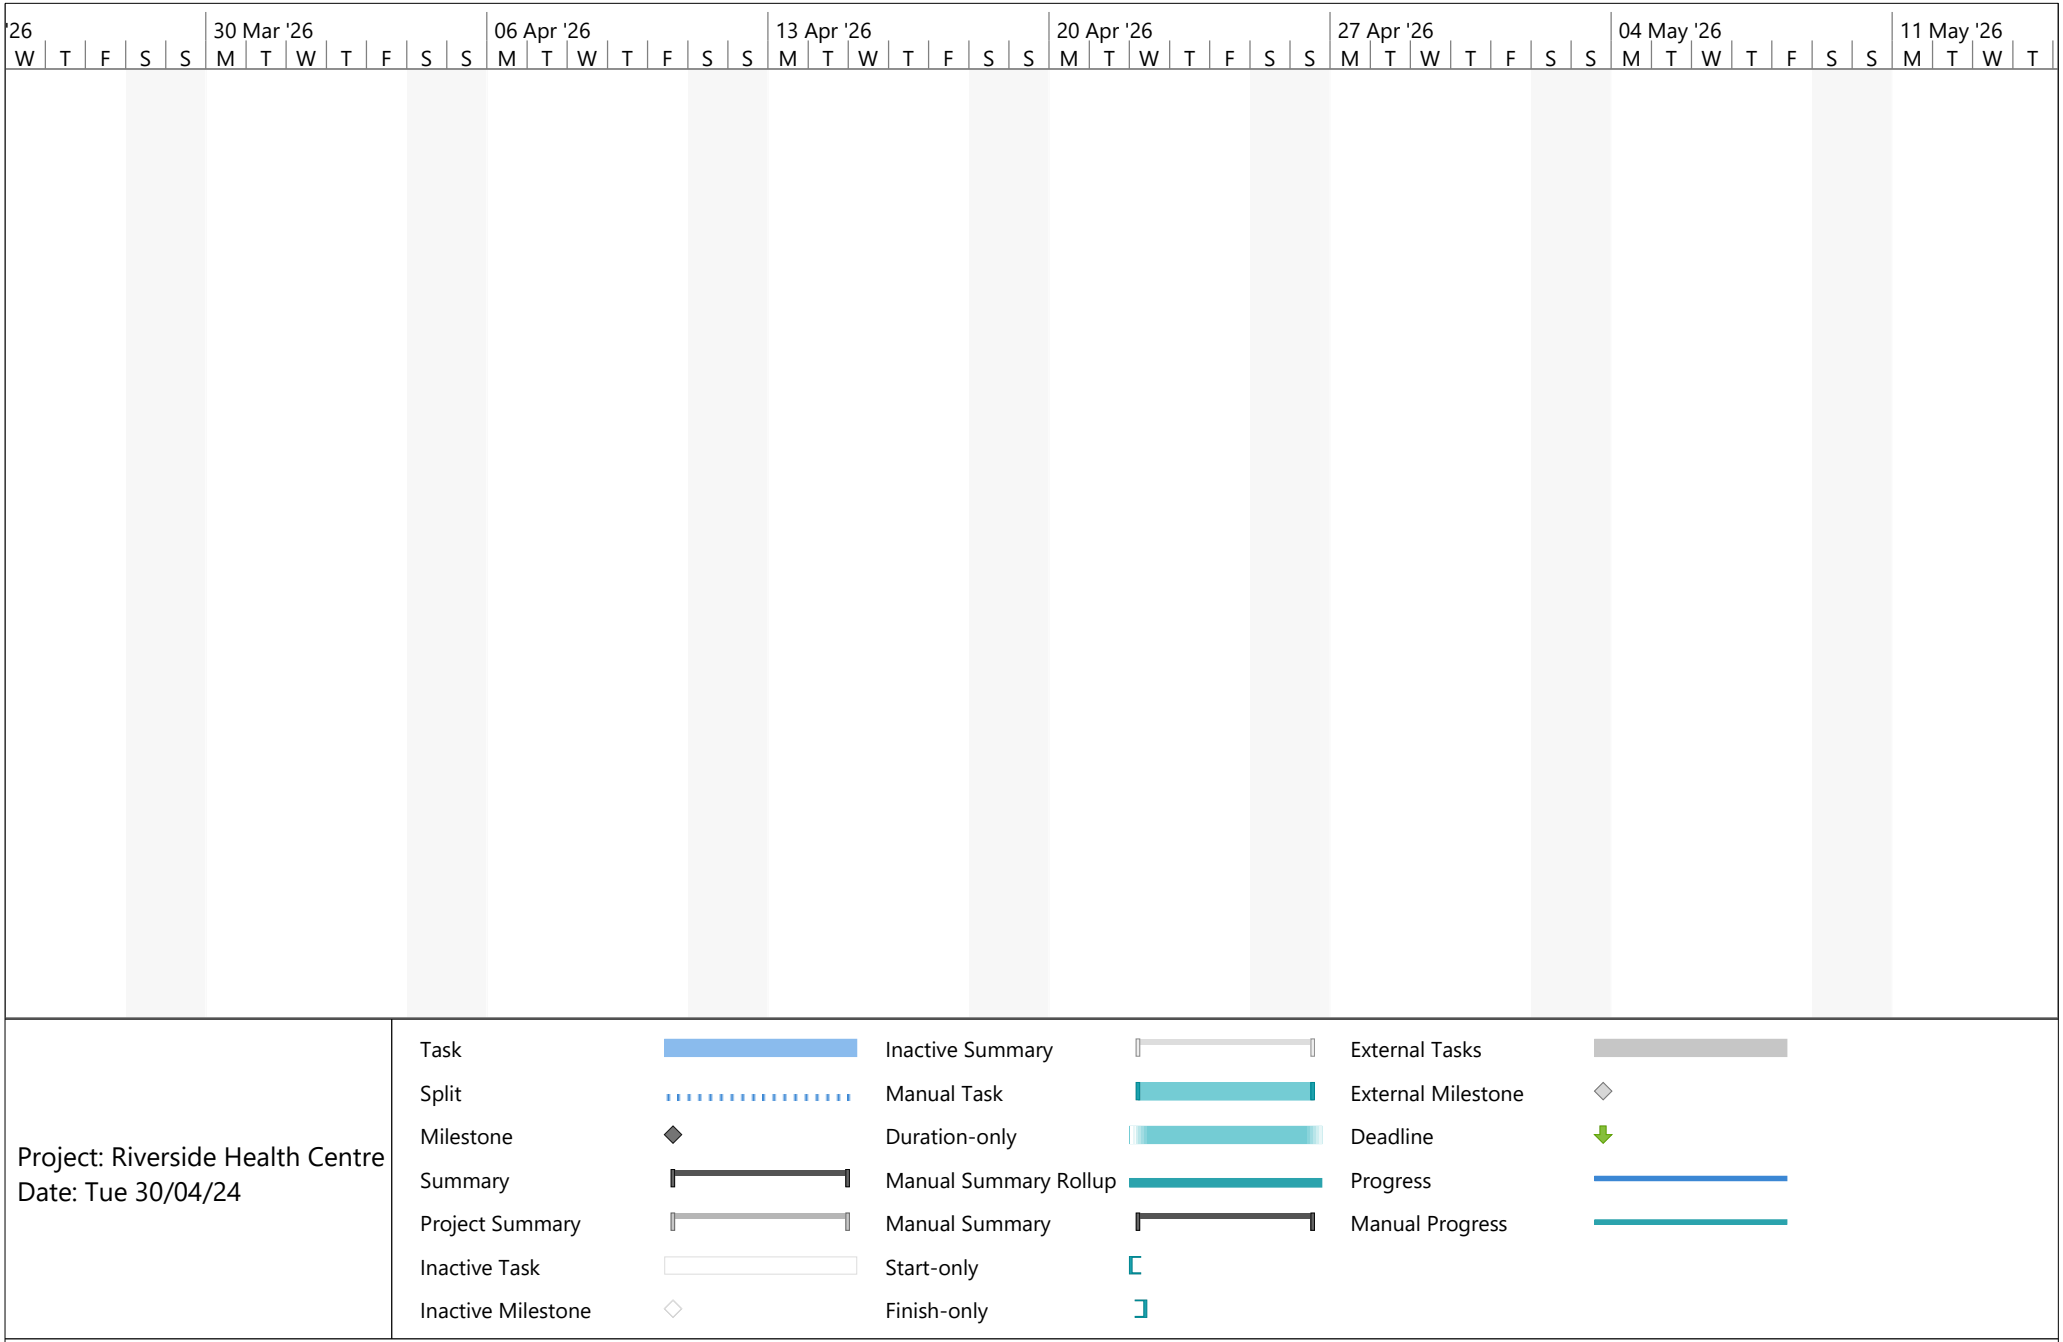


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

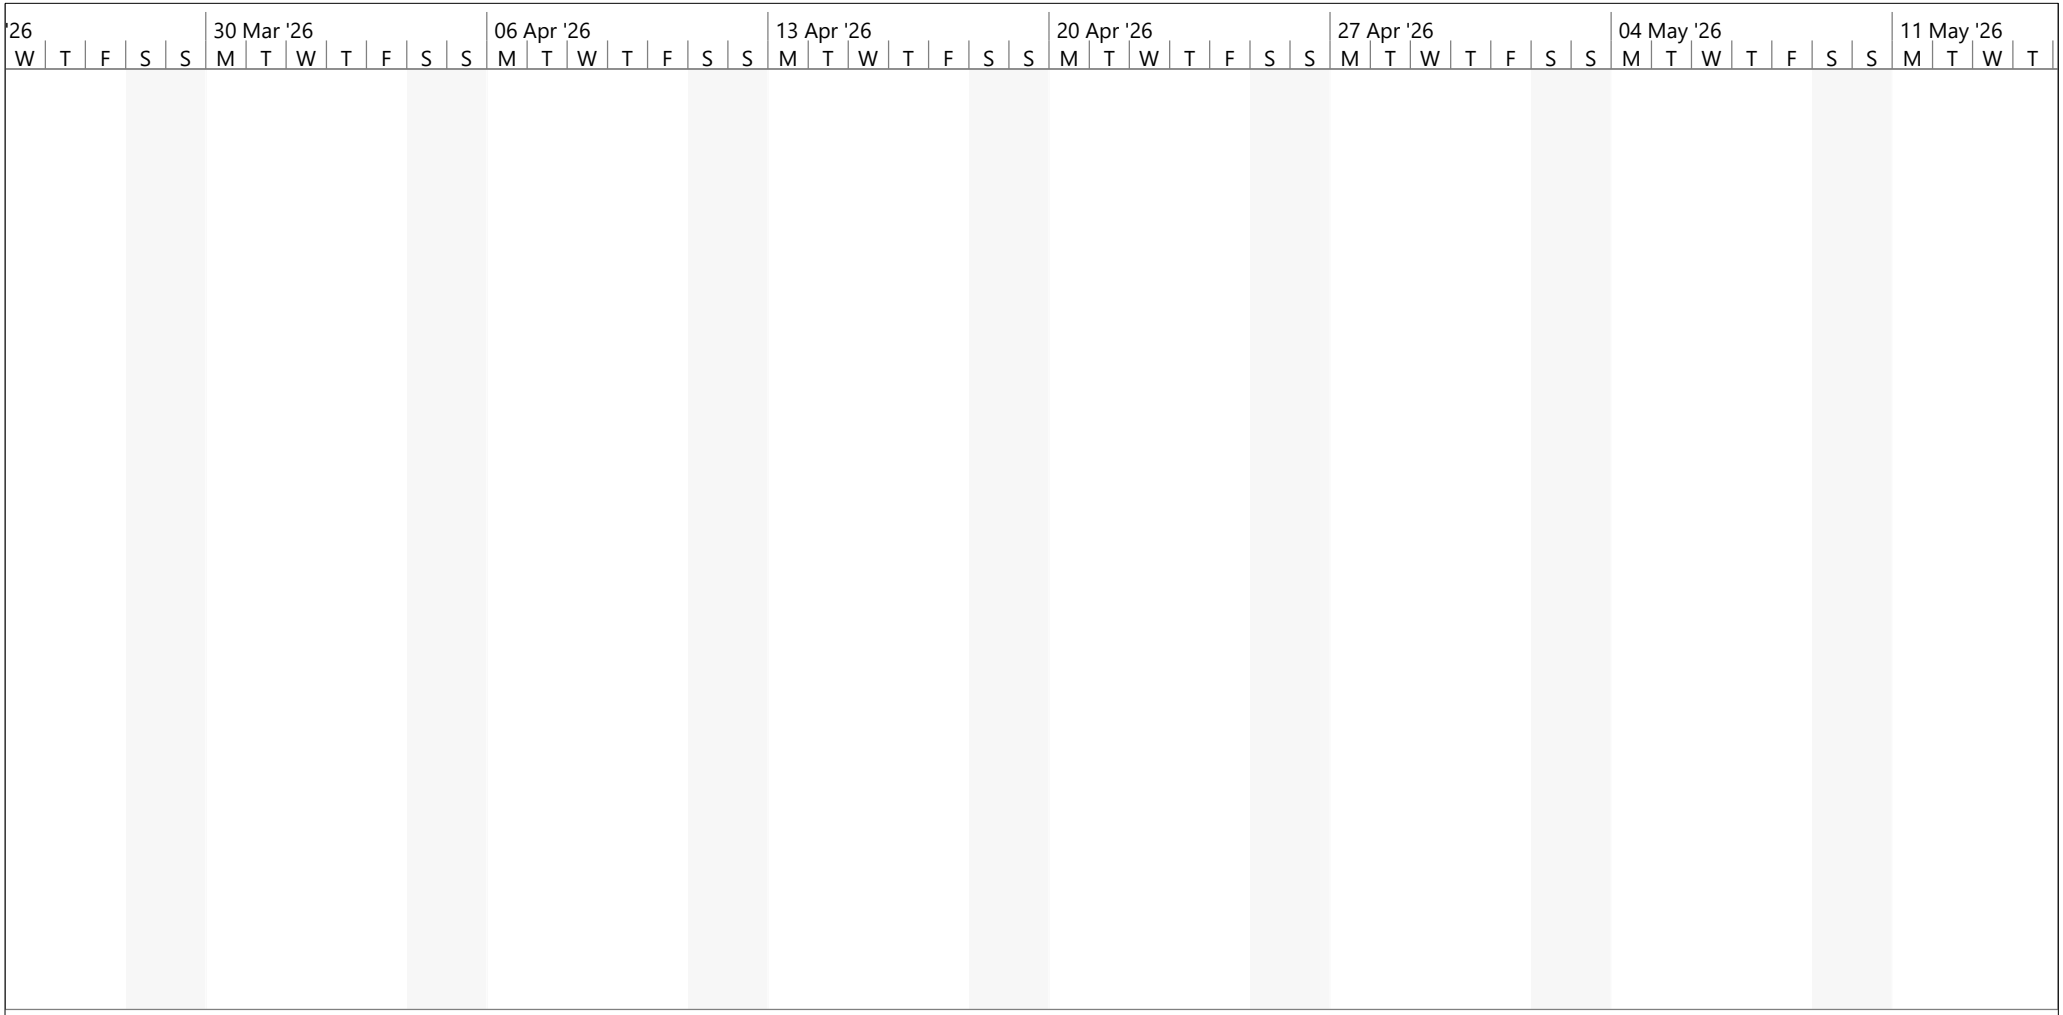


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

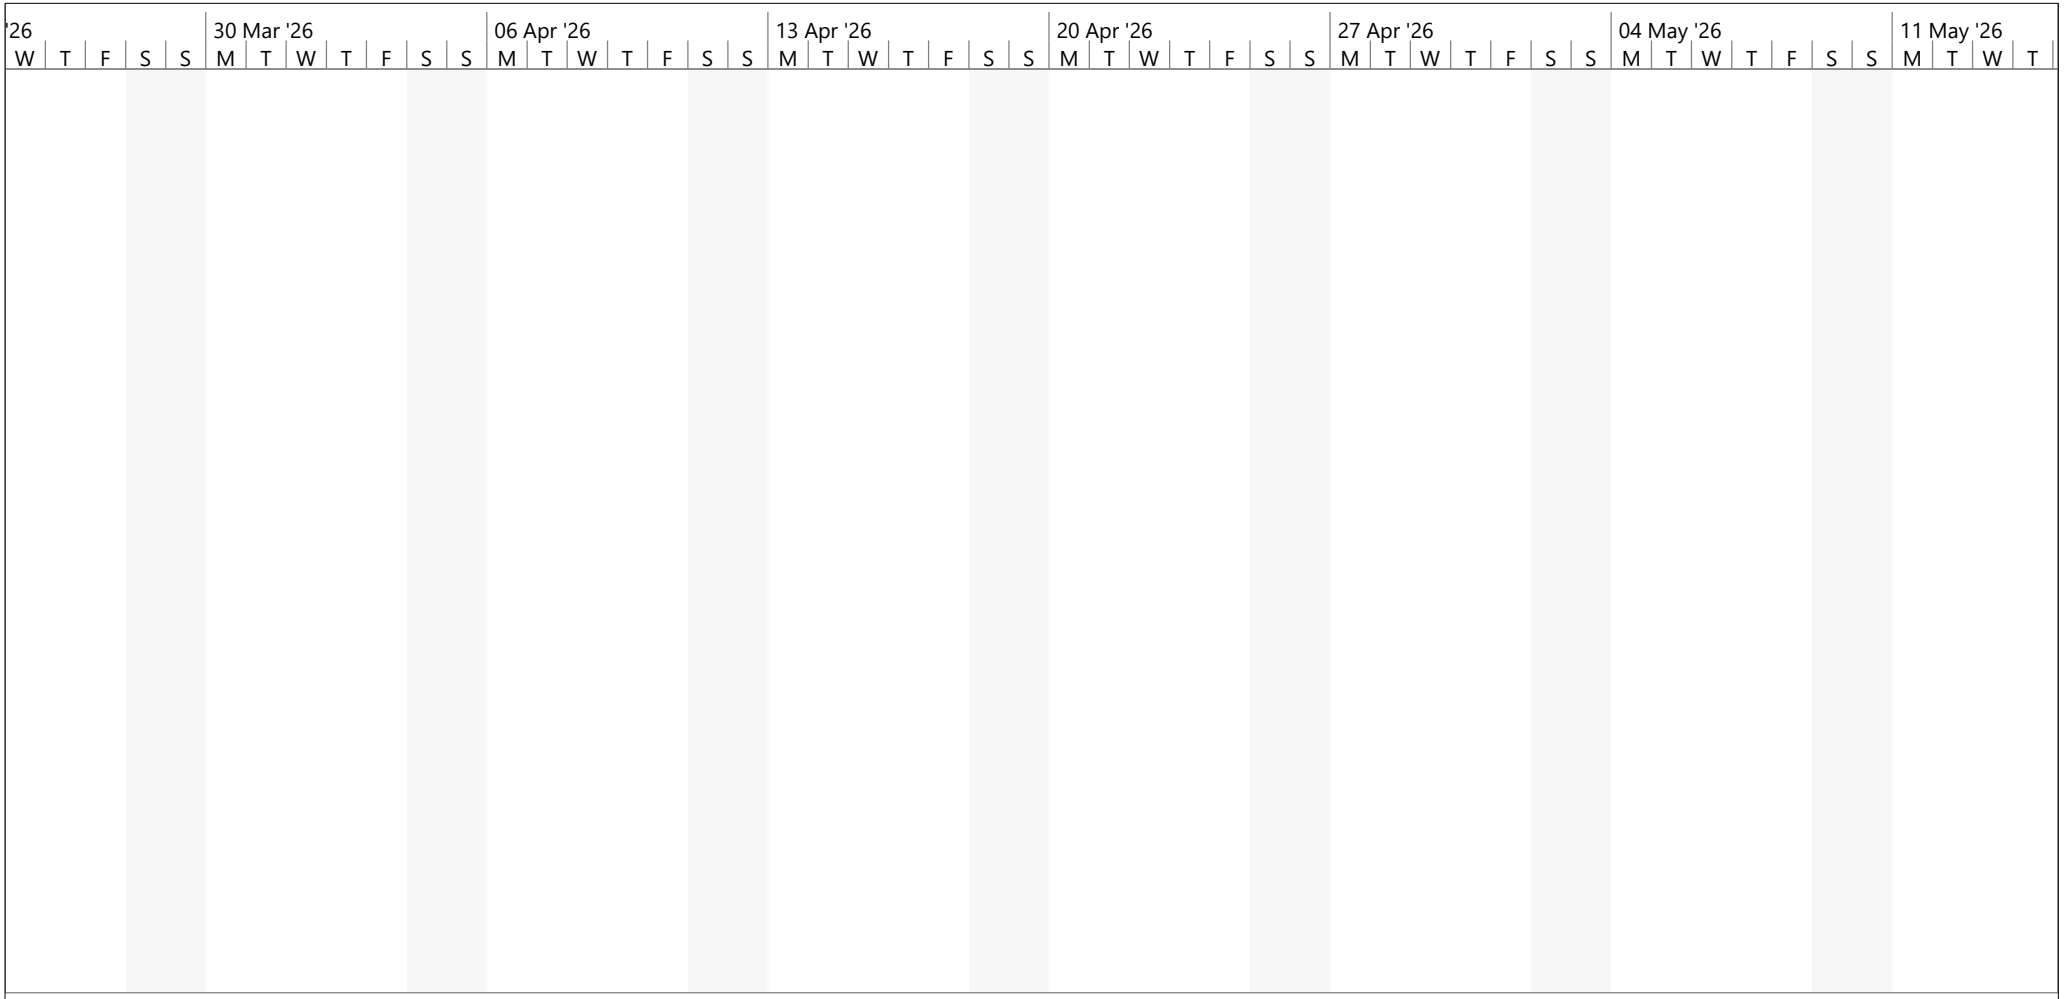


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

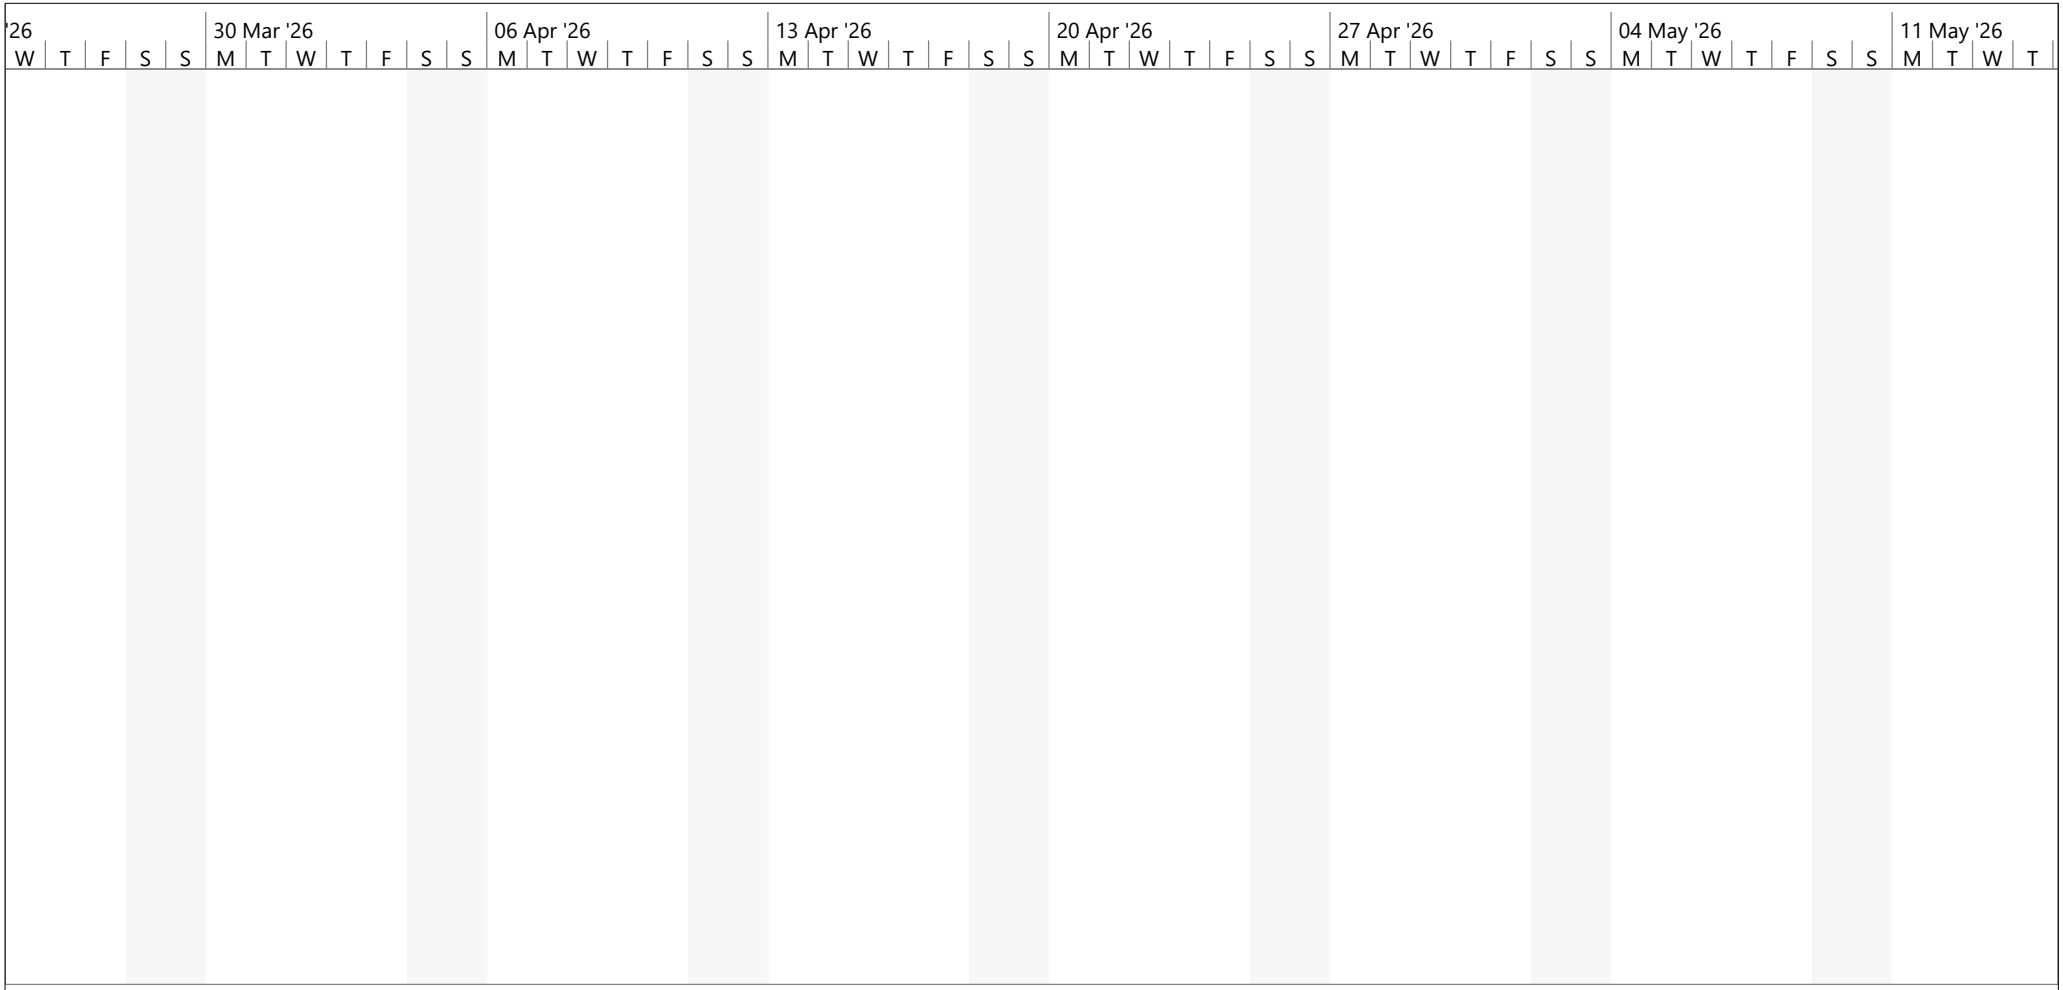

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

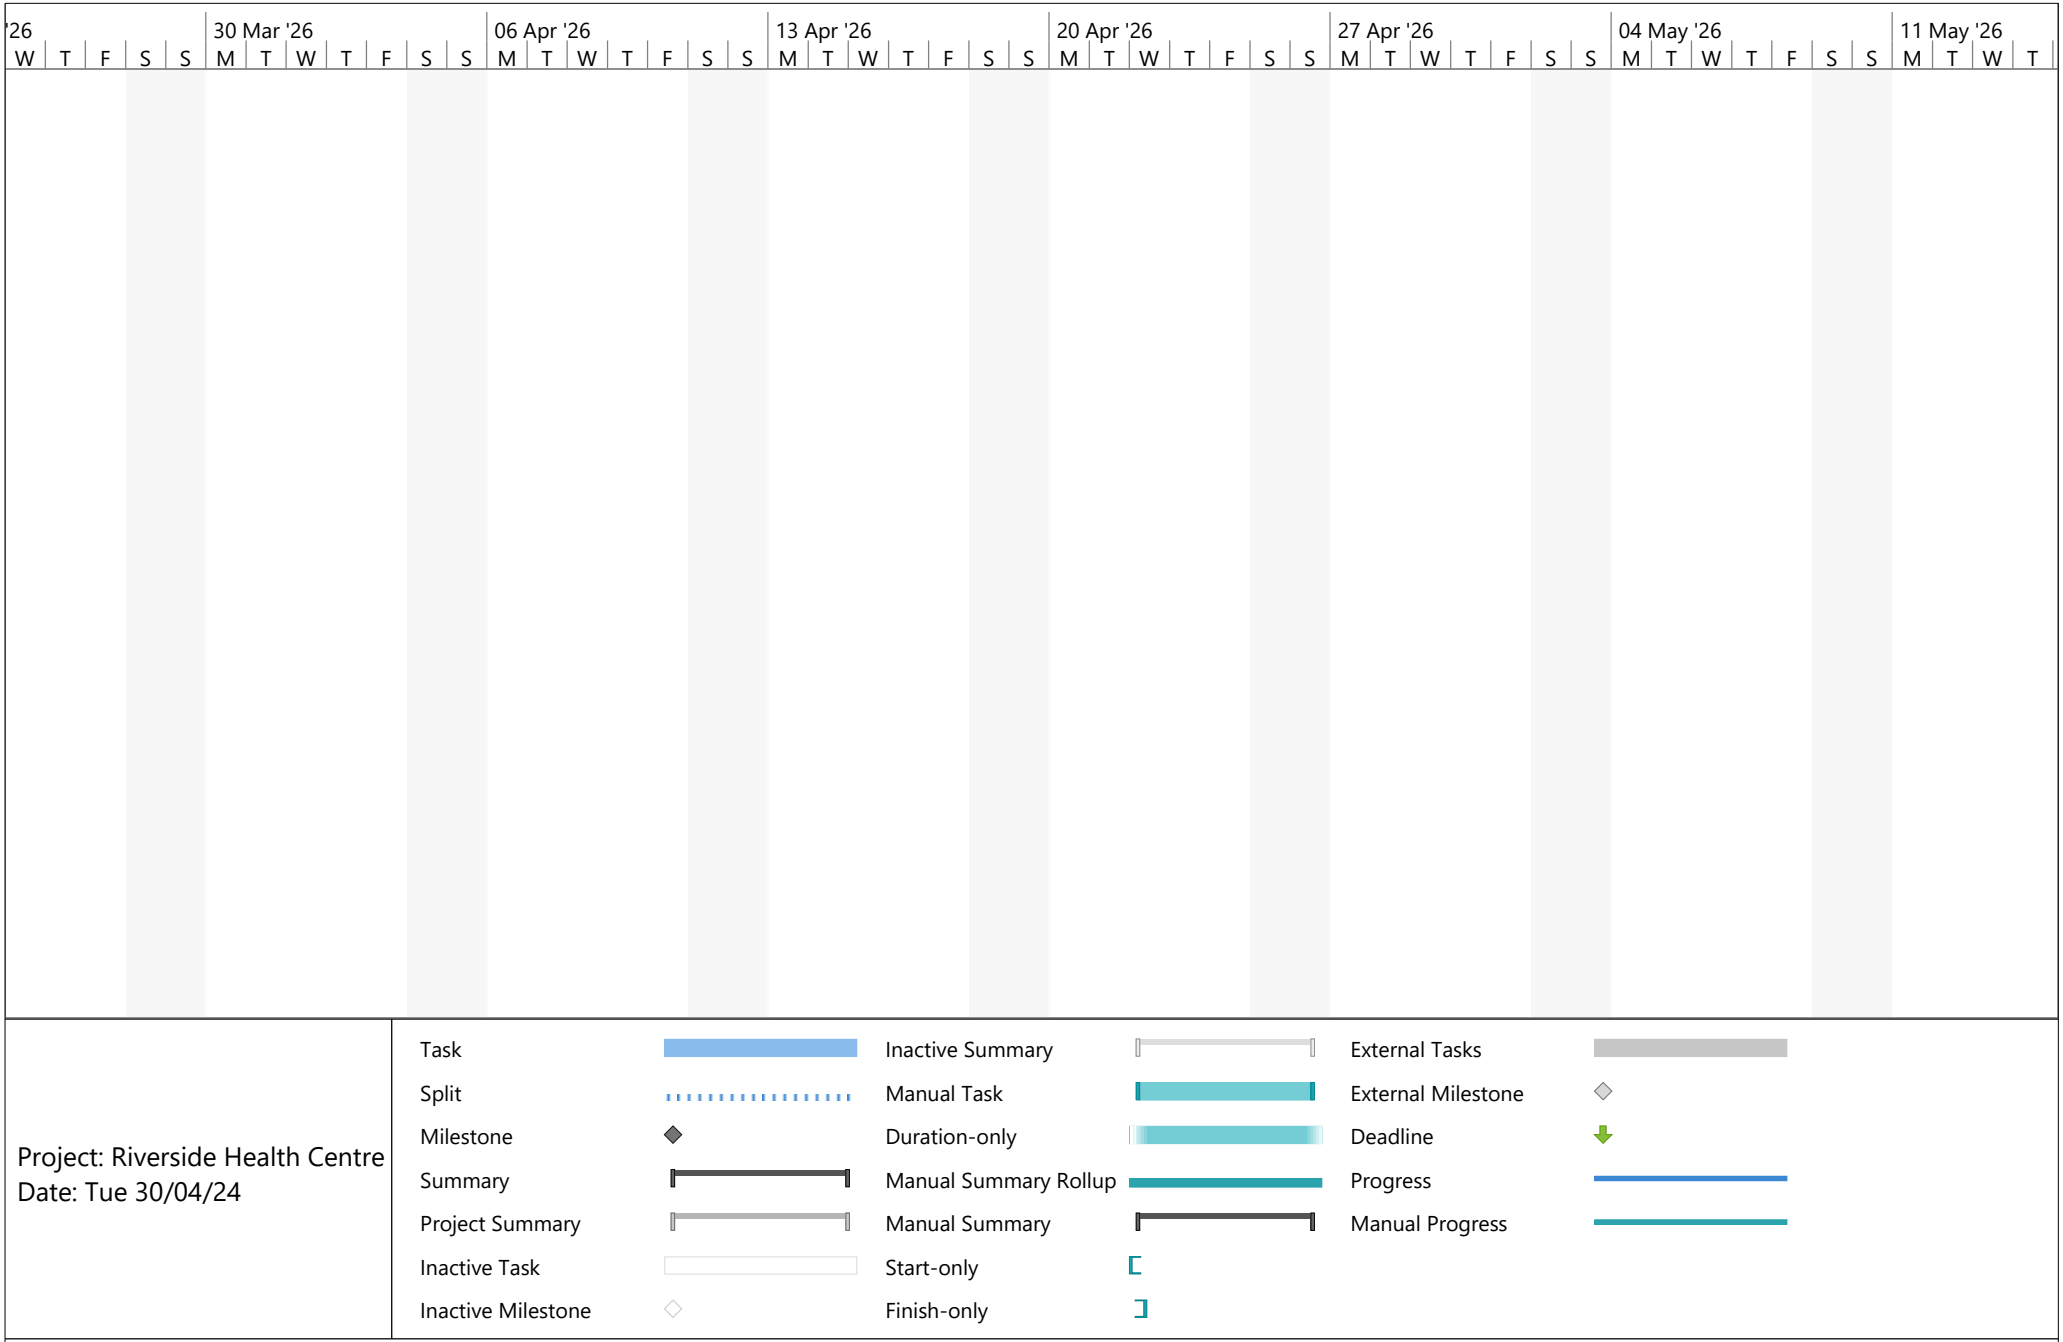
'26
W T F S S
30 Mar '26
M T W T F S S
06 Apr '26
M T W T F S S
13 Apr '26
M T W T F S S
20 Apr '26
M T W T F S S
27 Apr '26
M T W T F S S
04 May '26
M T W T F S S
11 May '26
M T W T
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

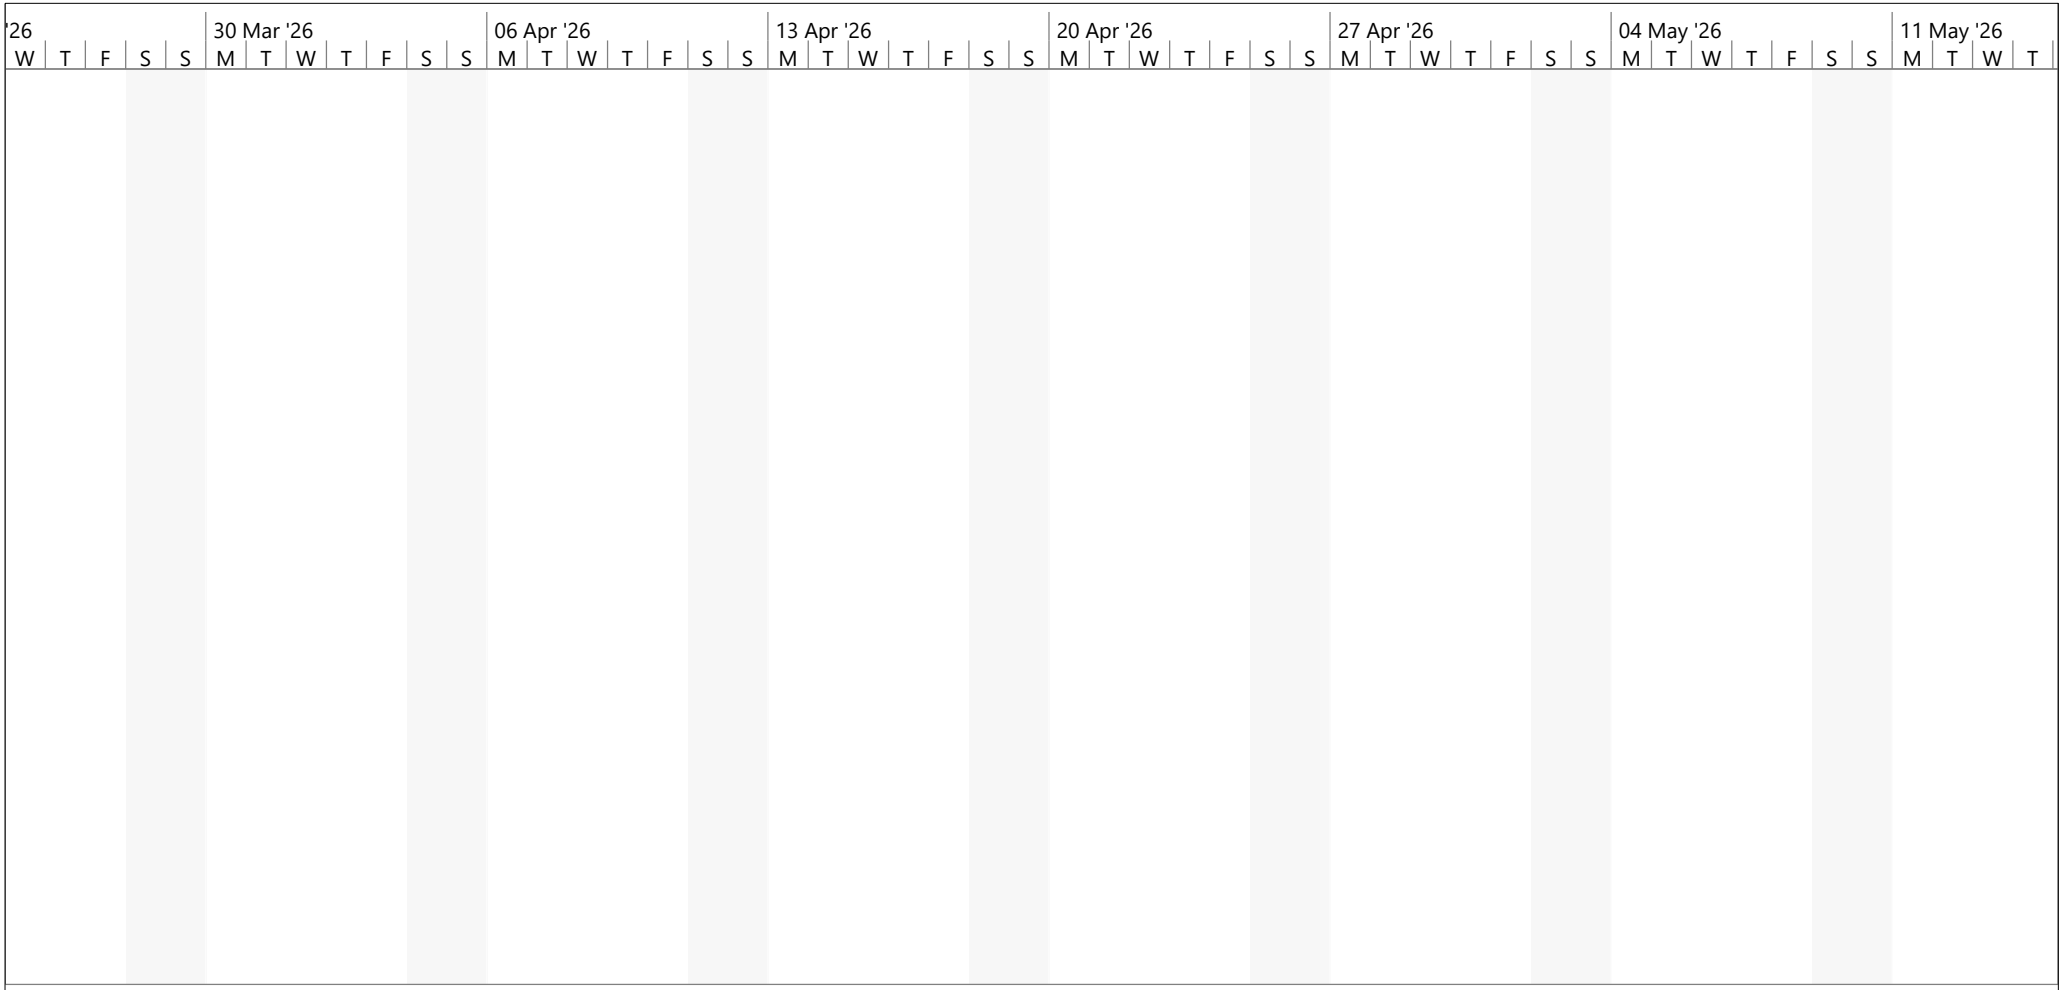


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

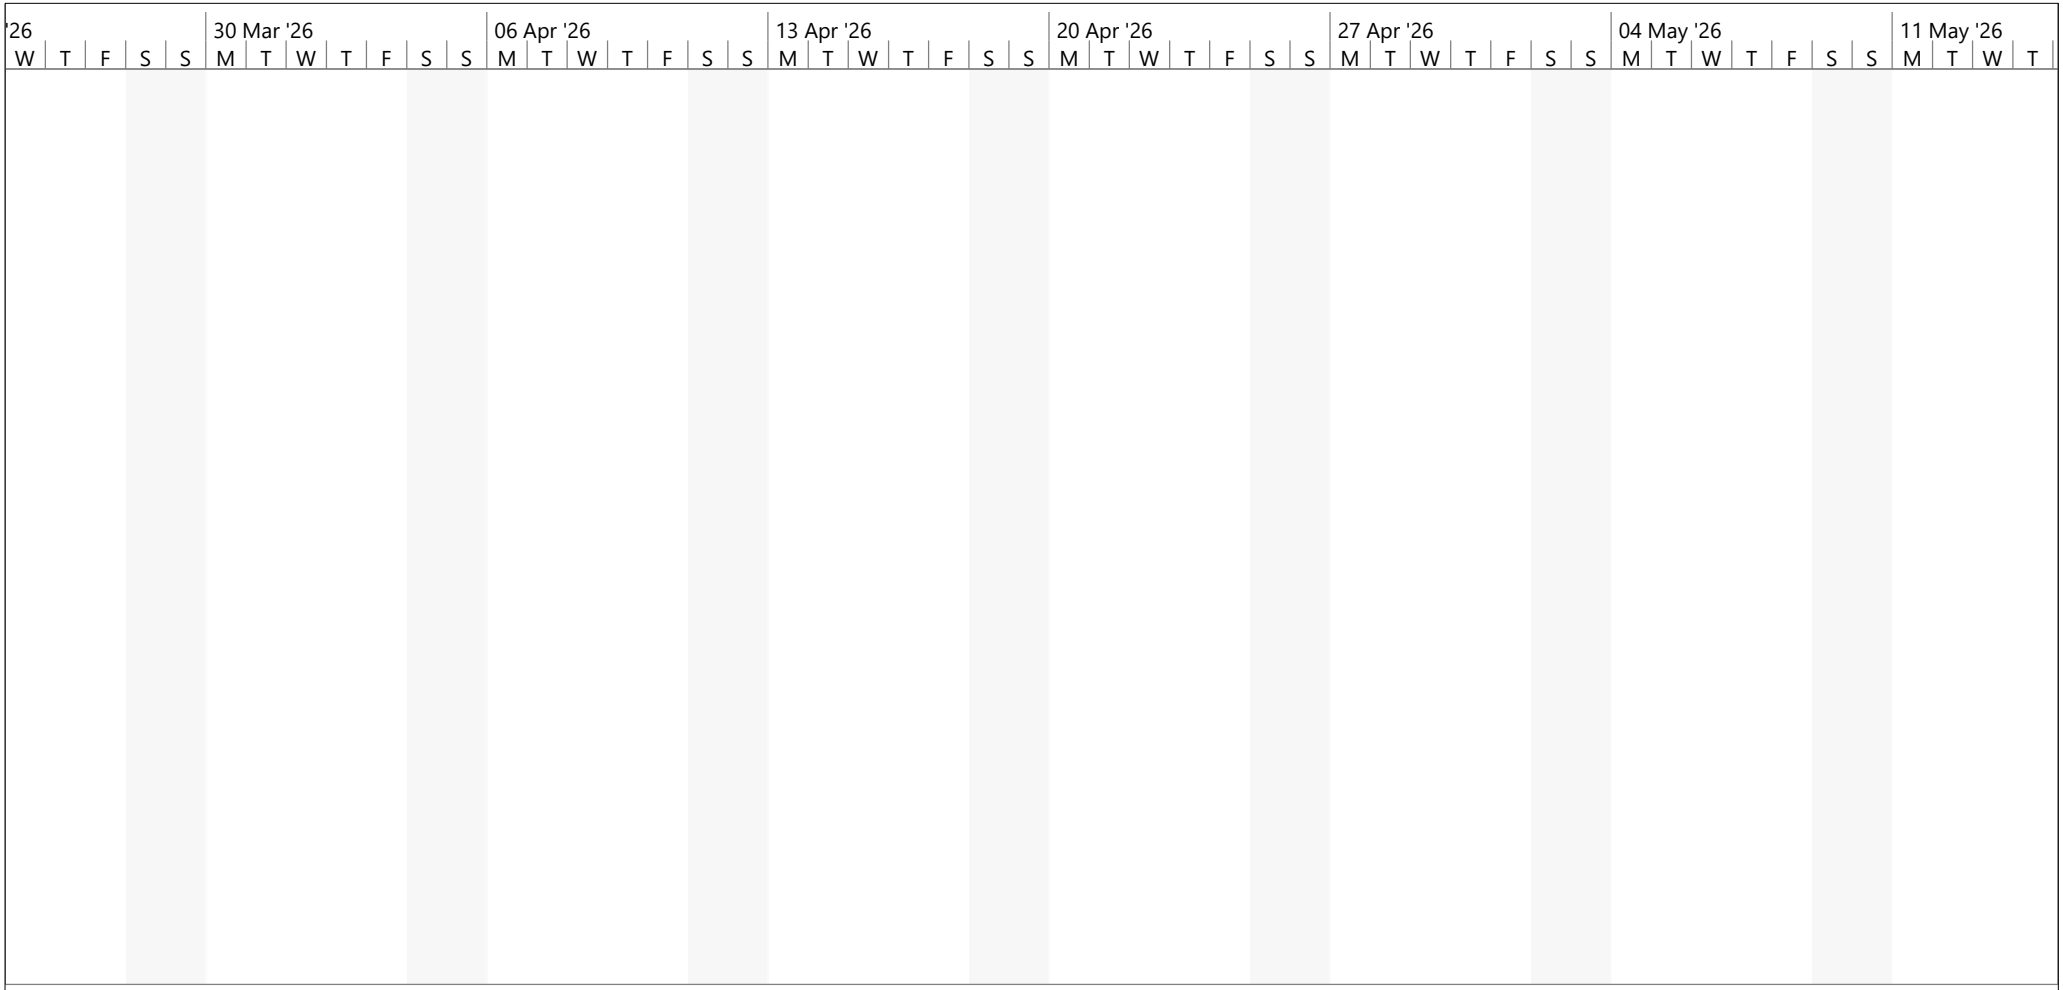


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

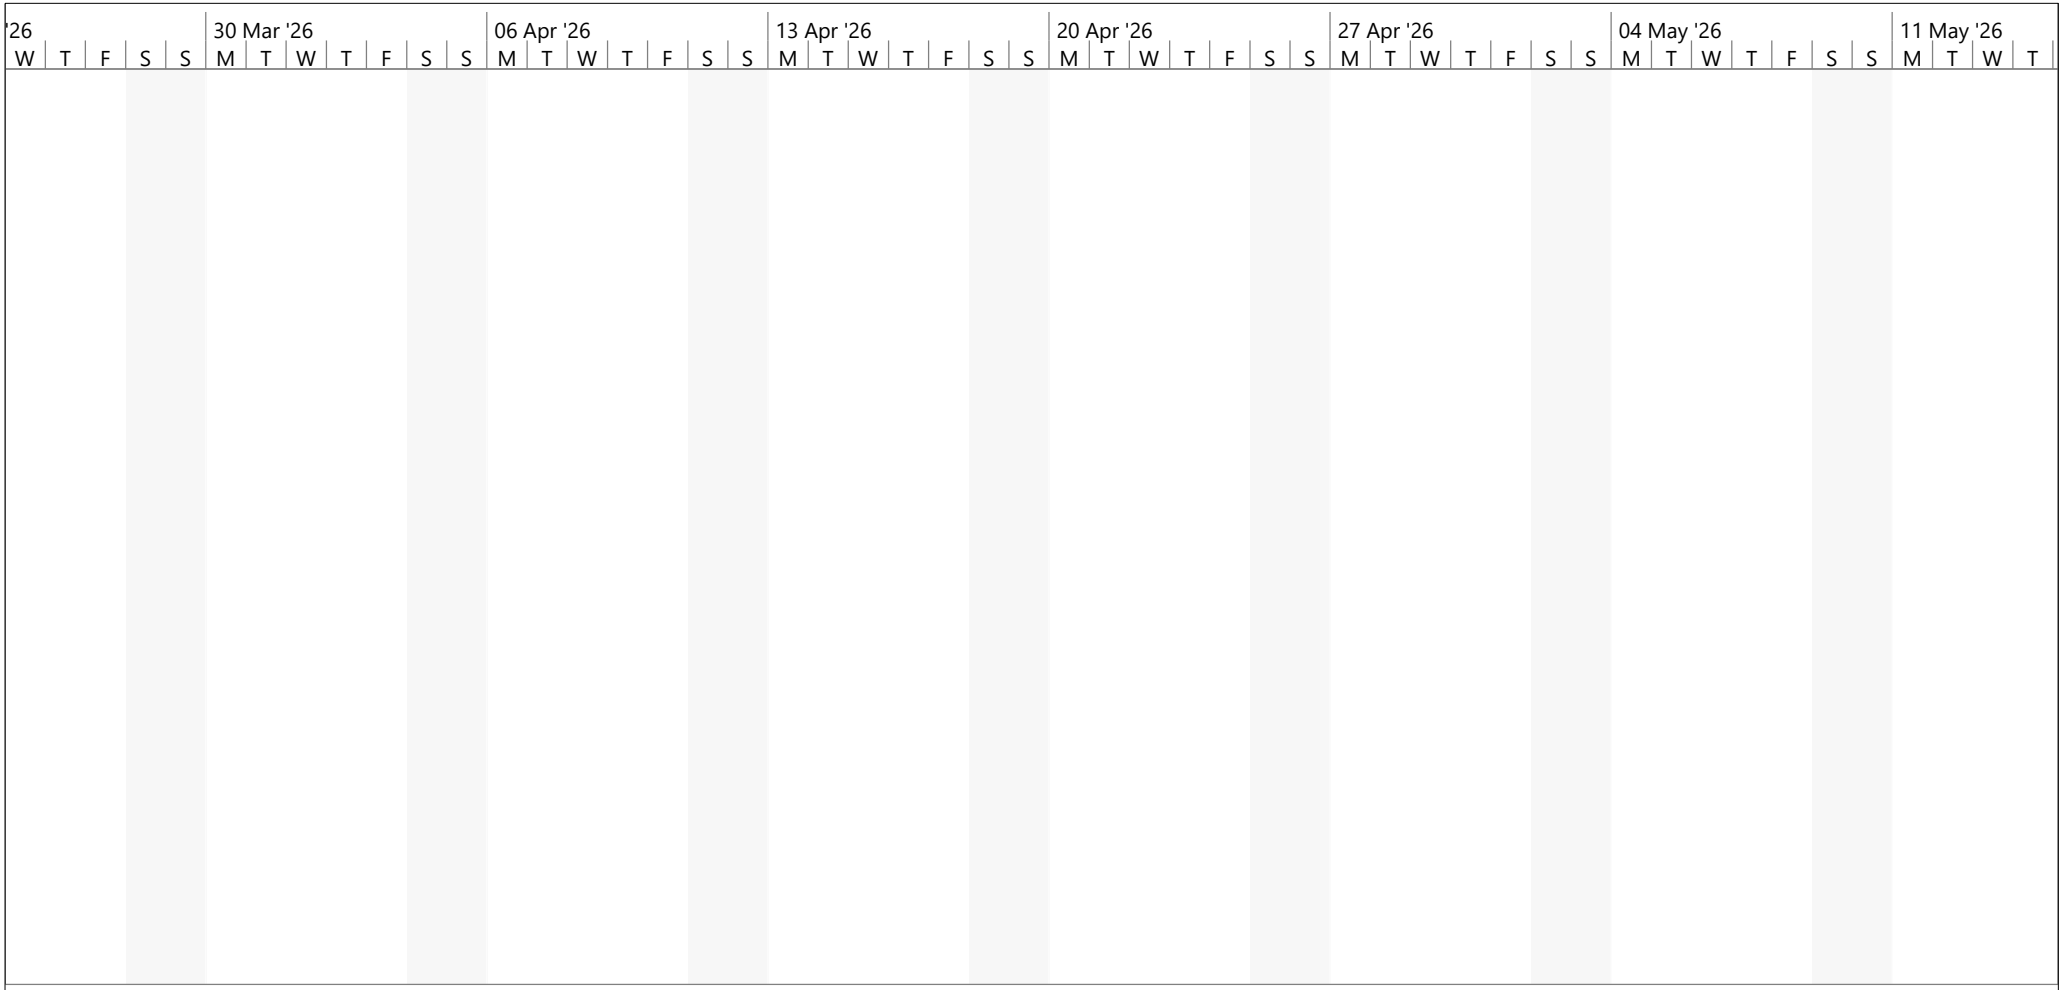


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

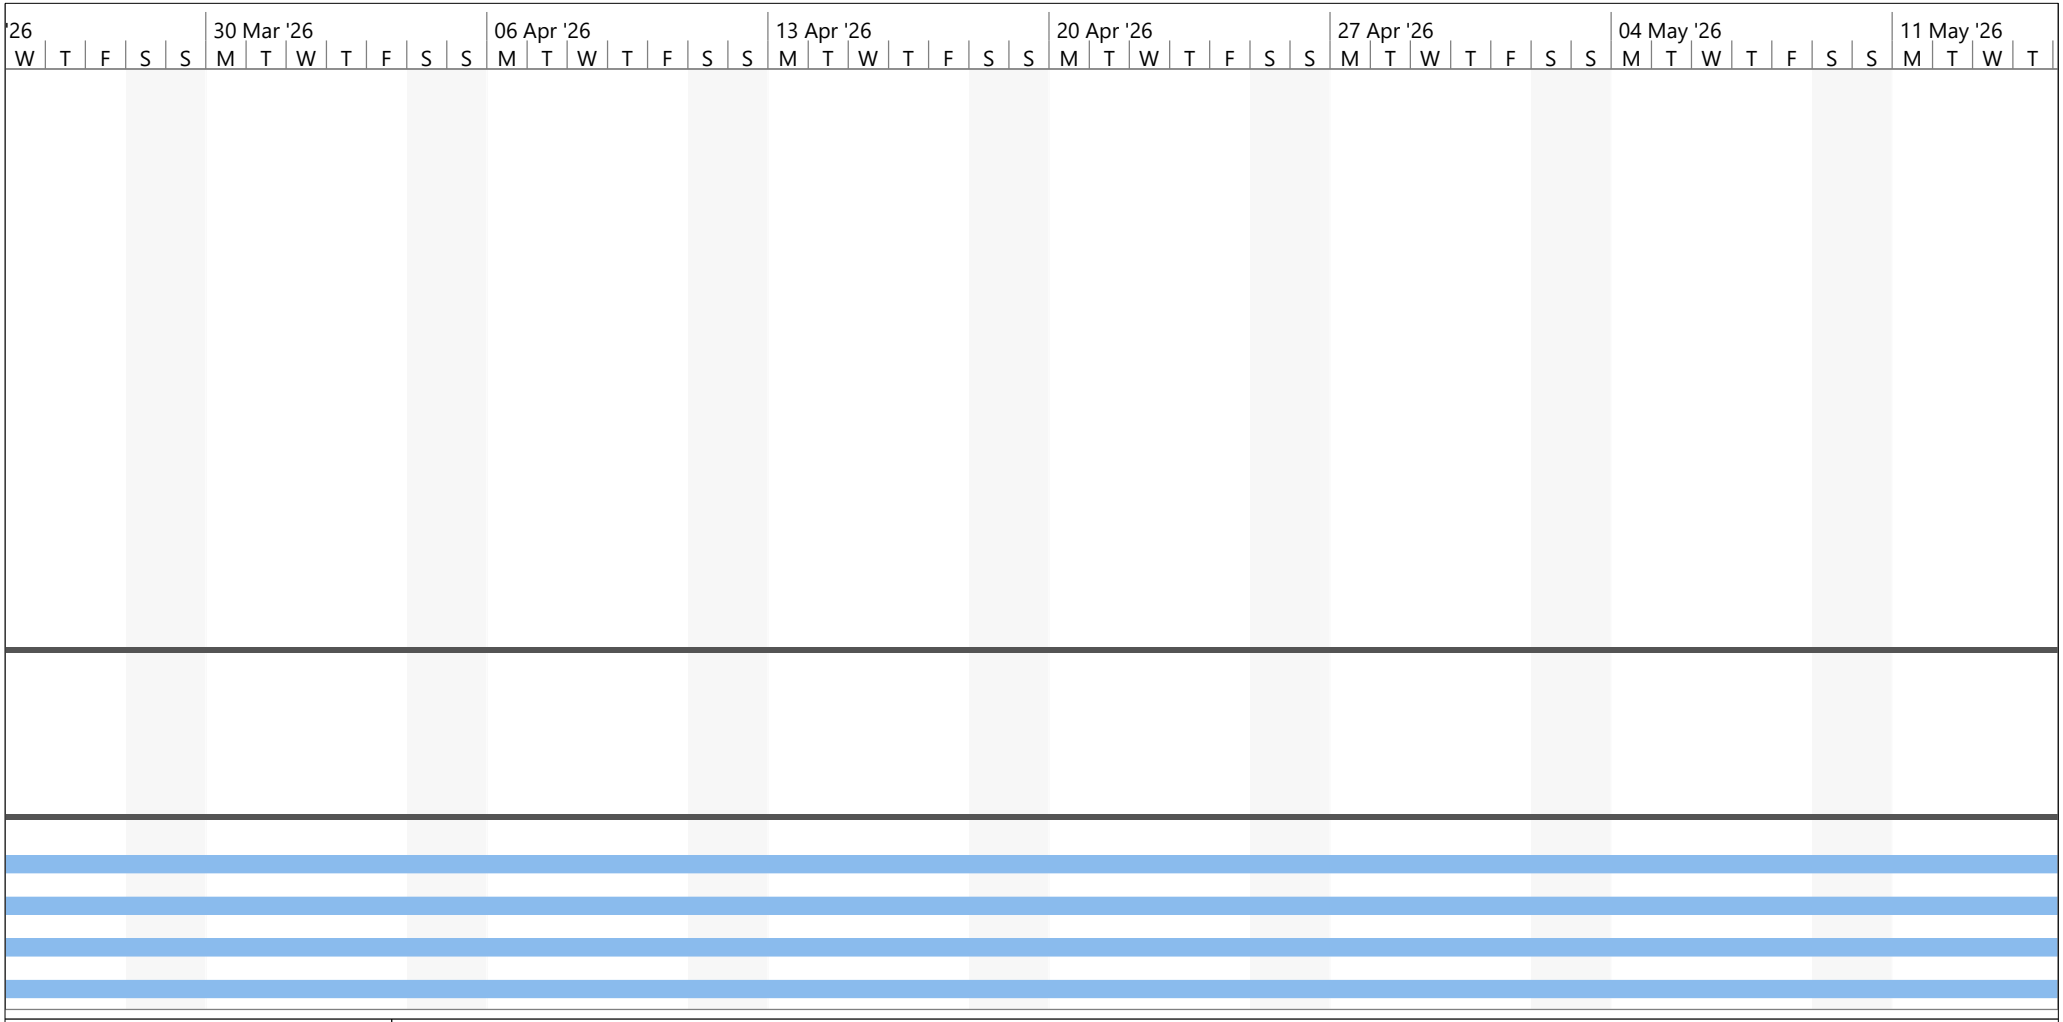


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

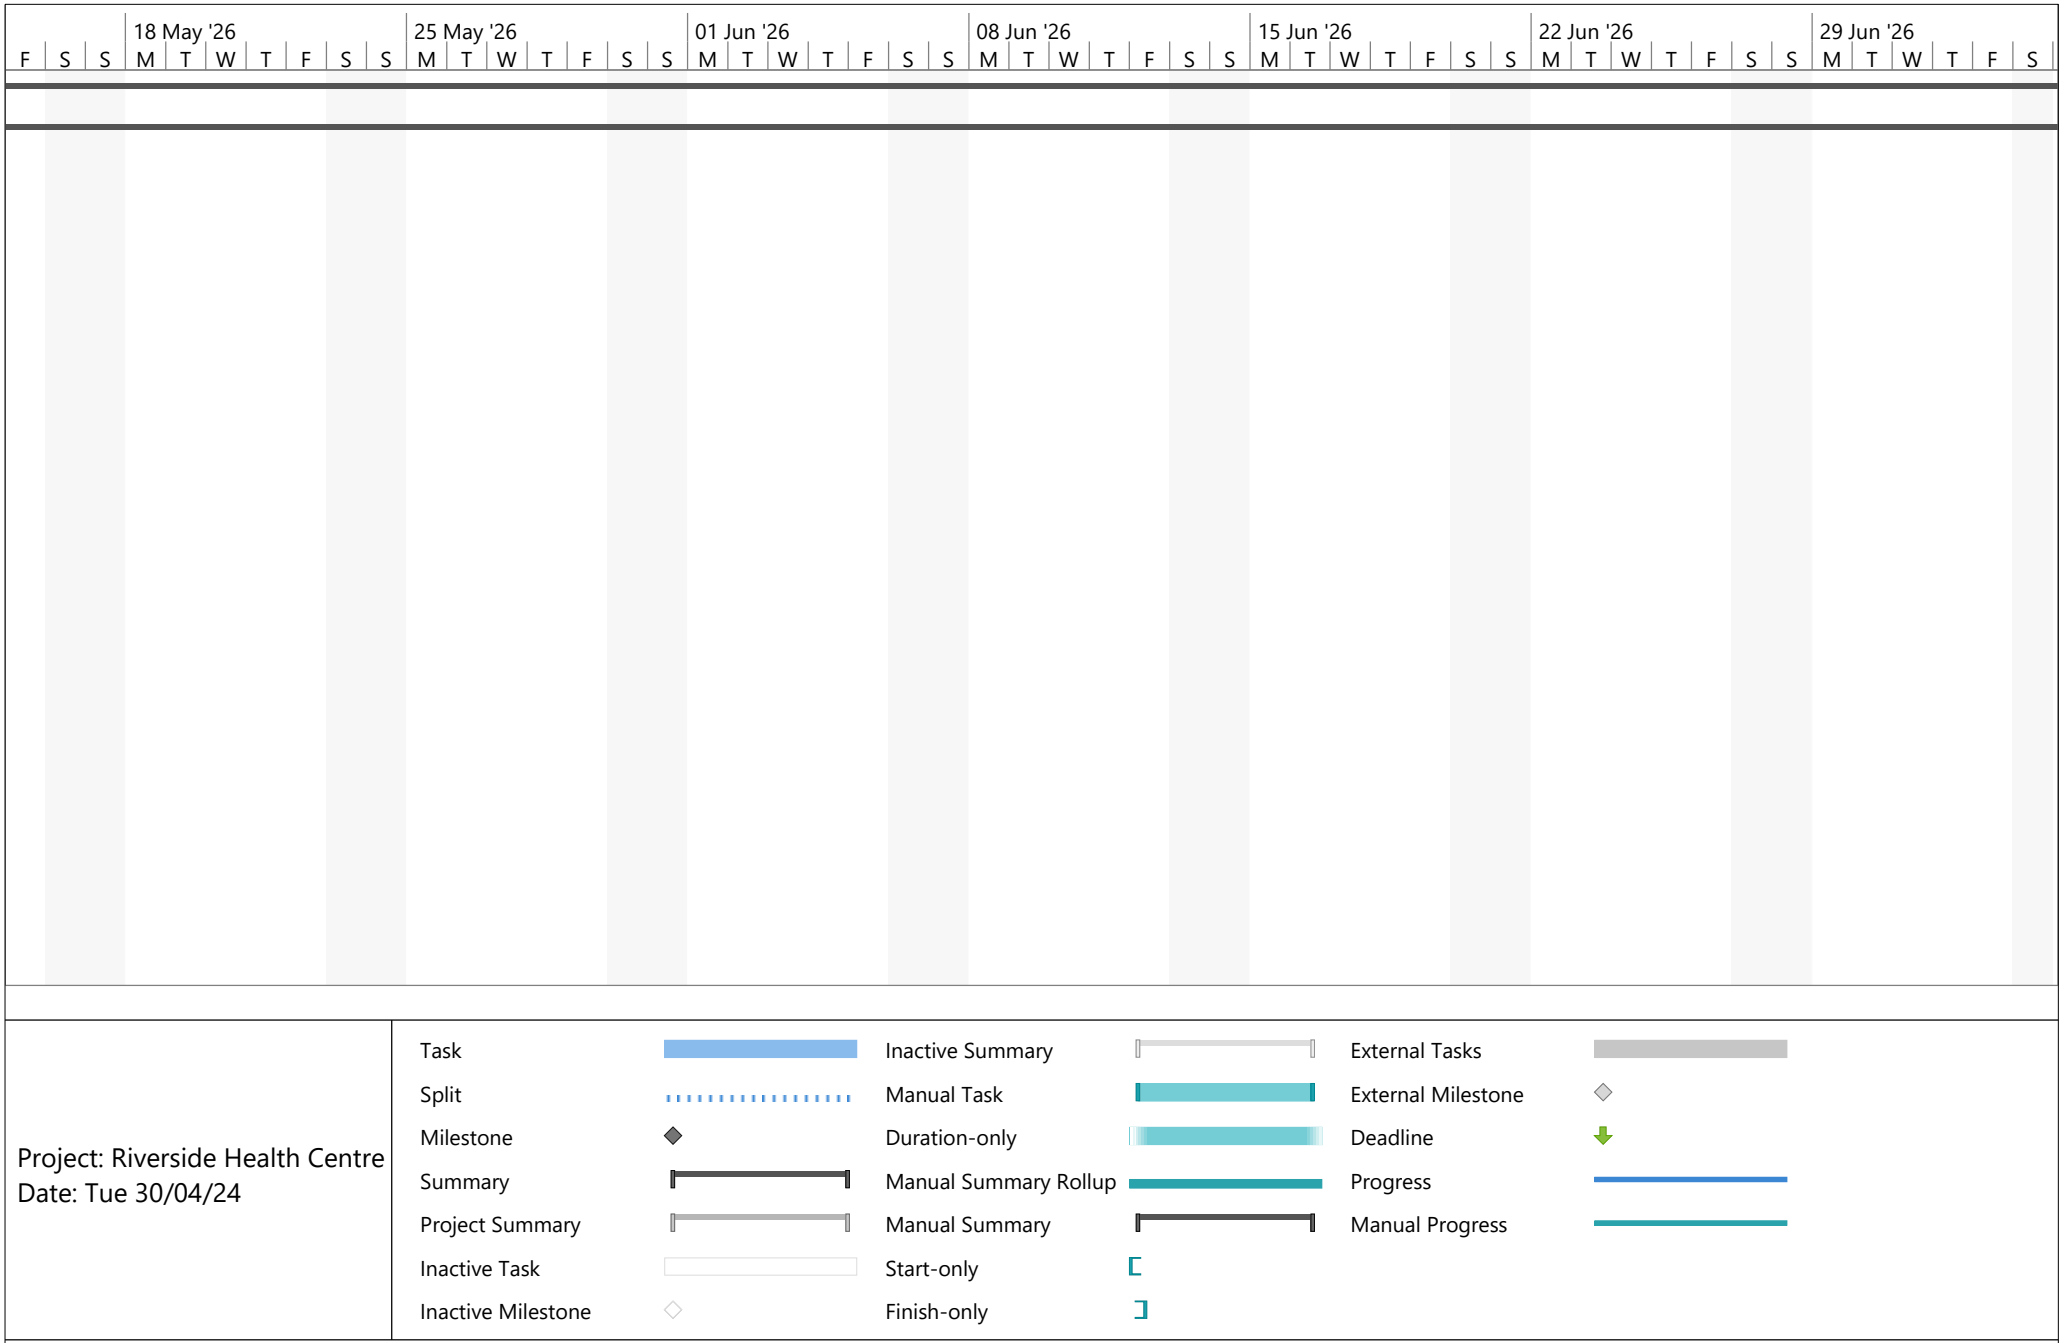


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

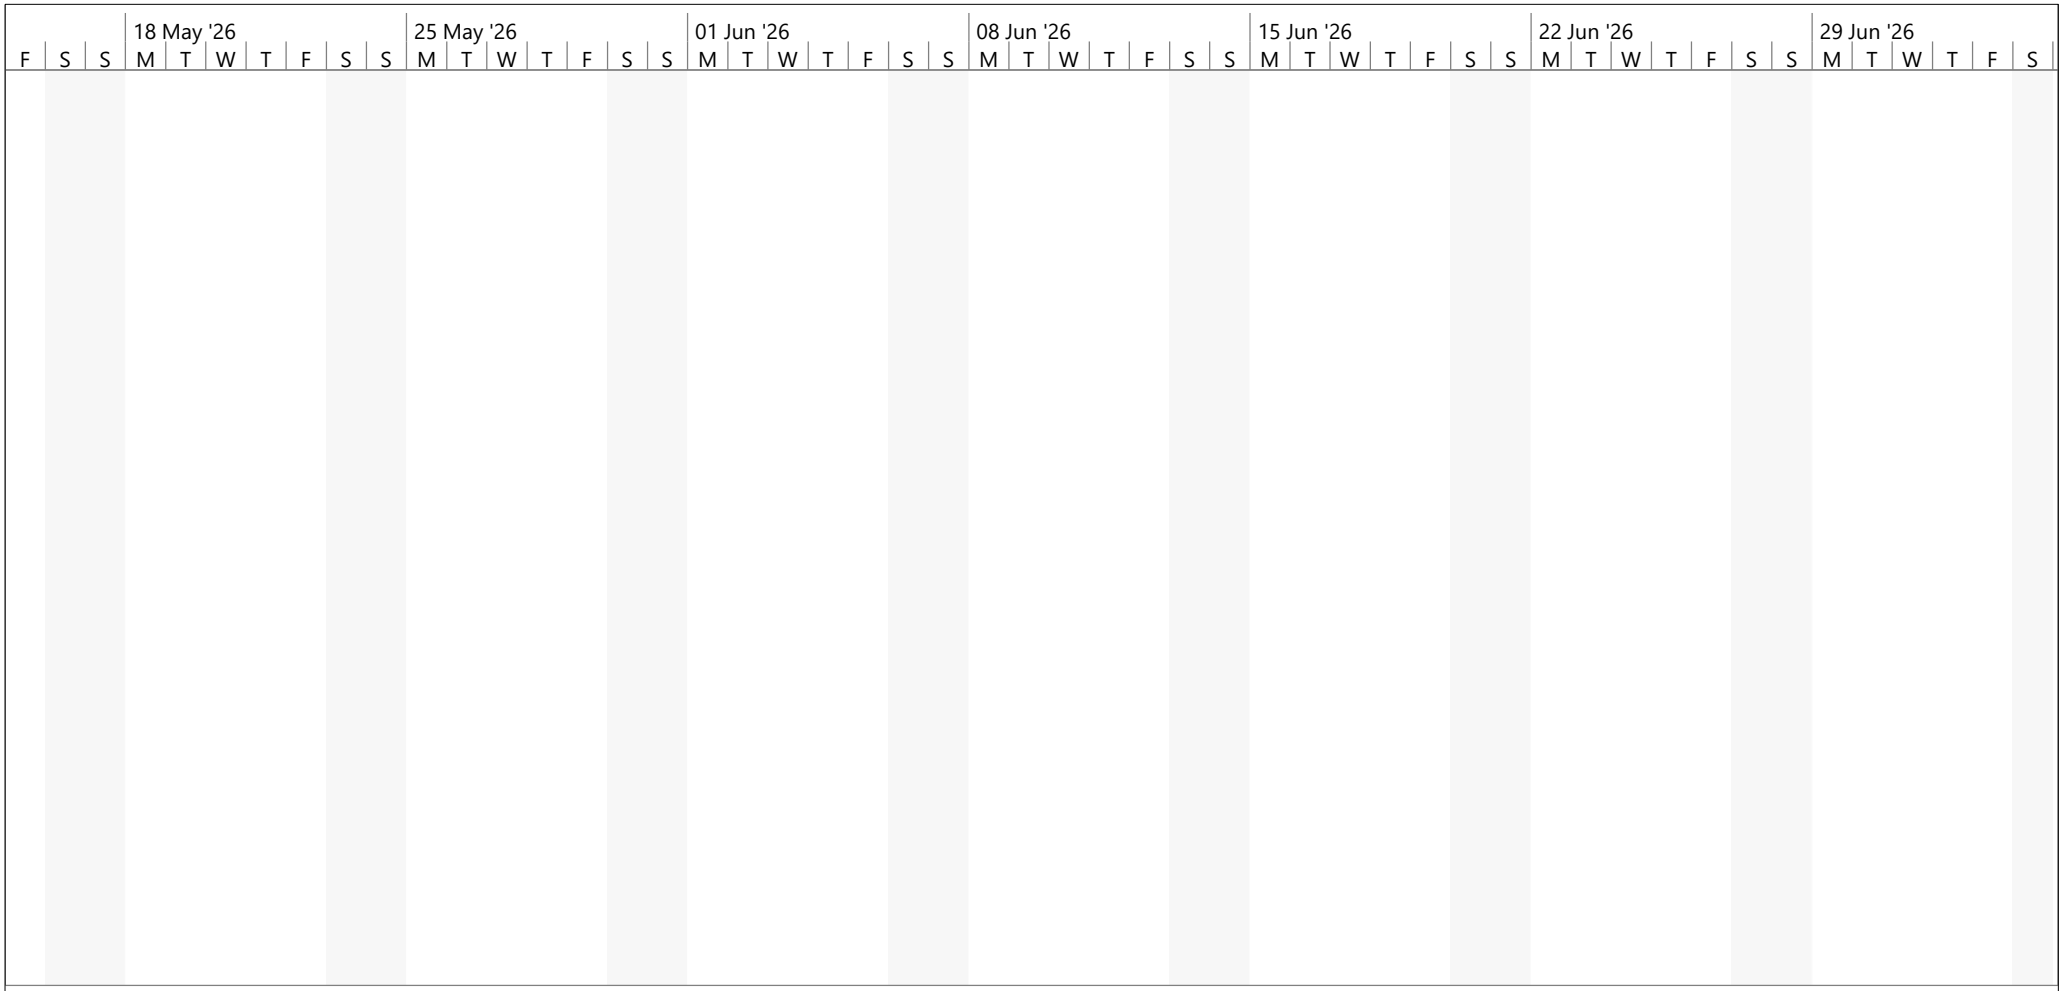


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

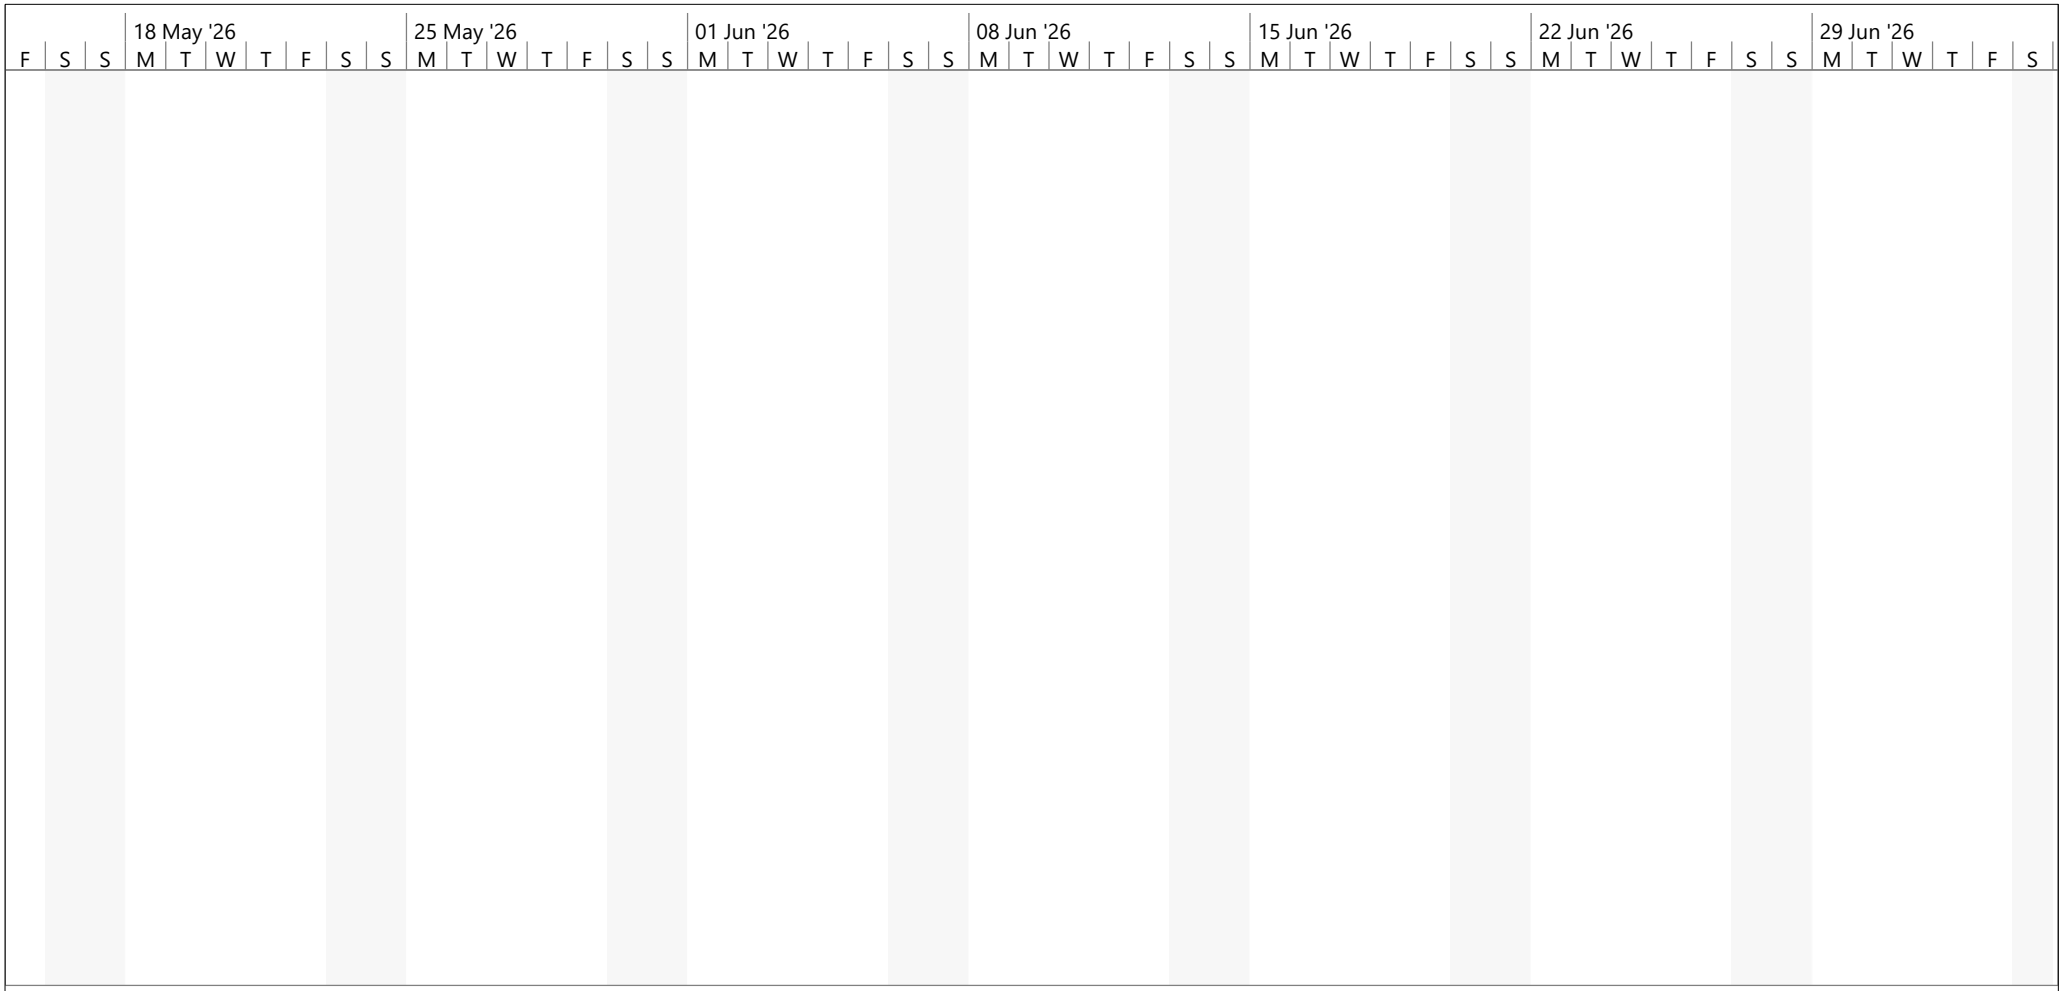


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

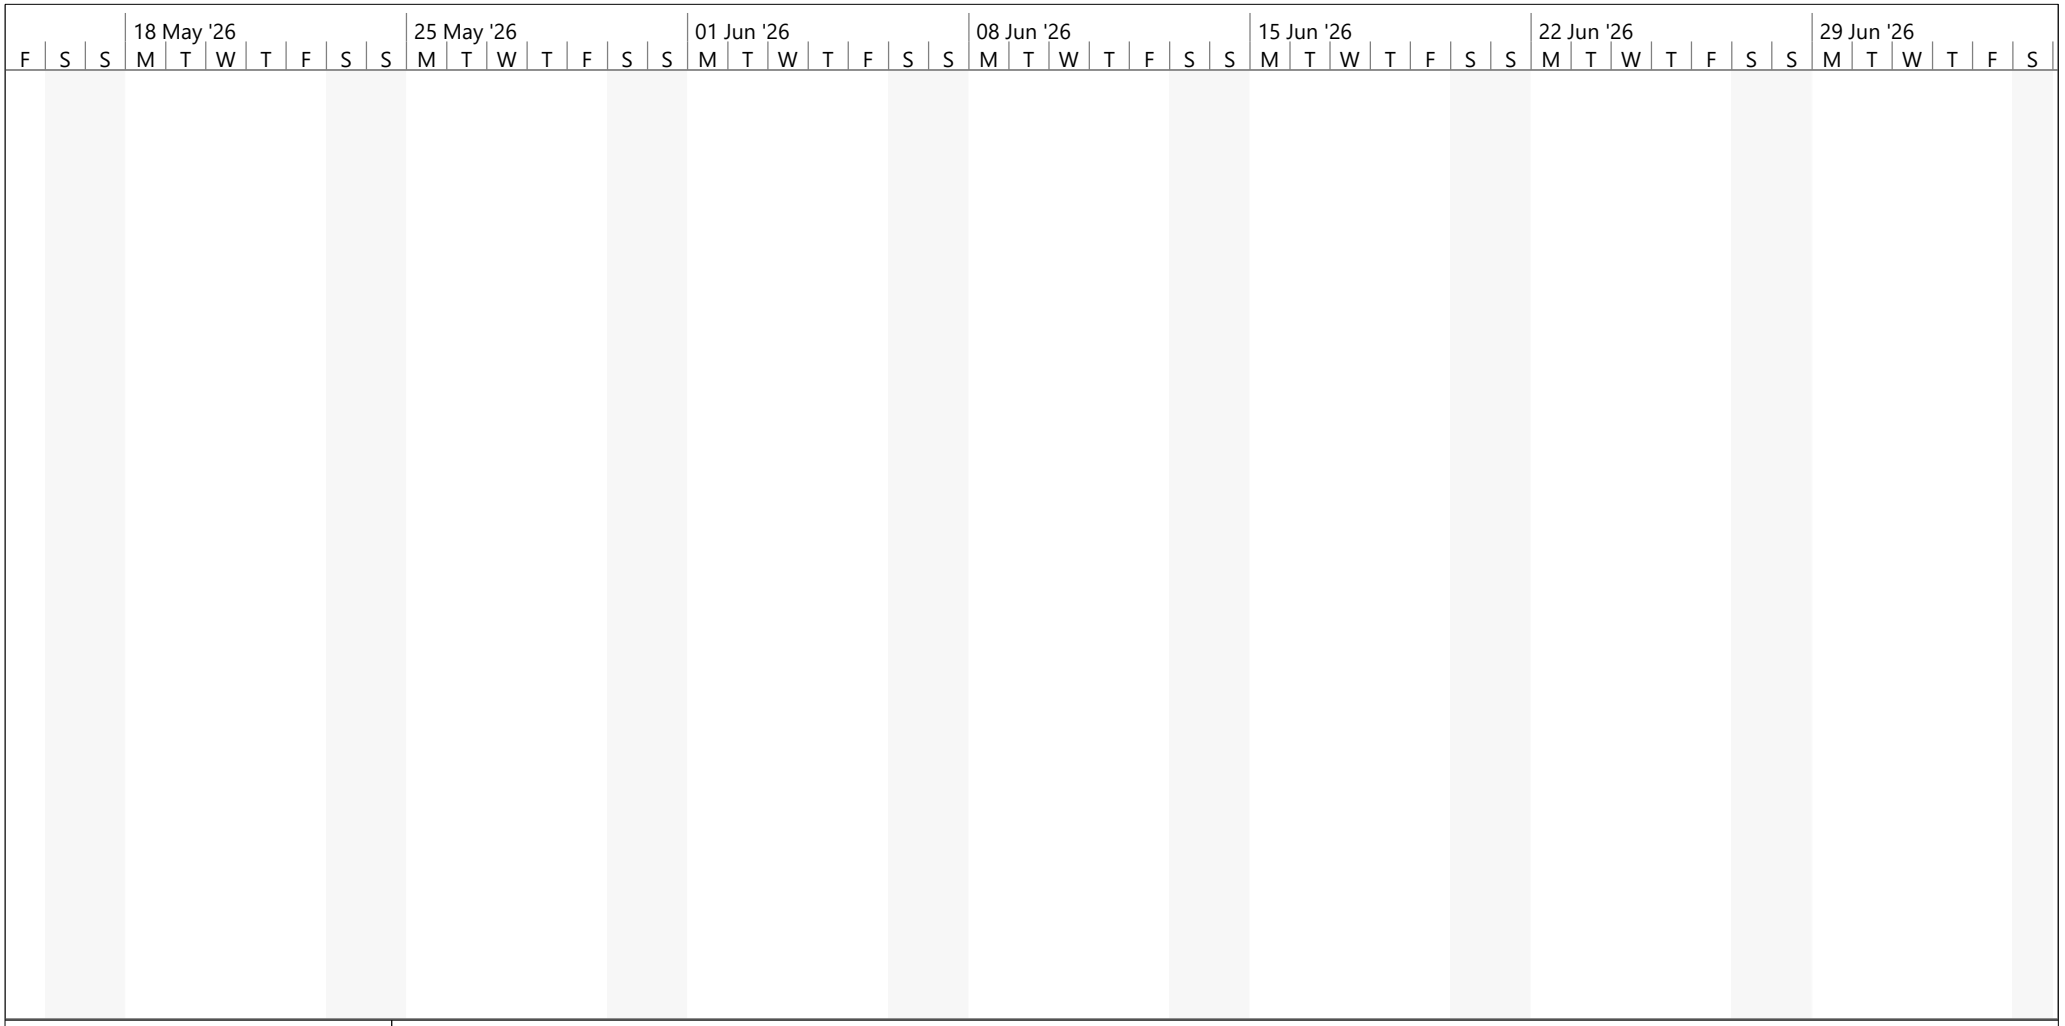


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

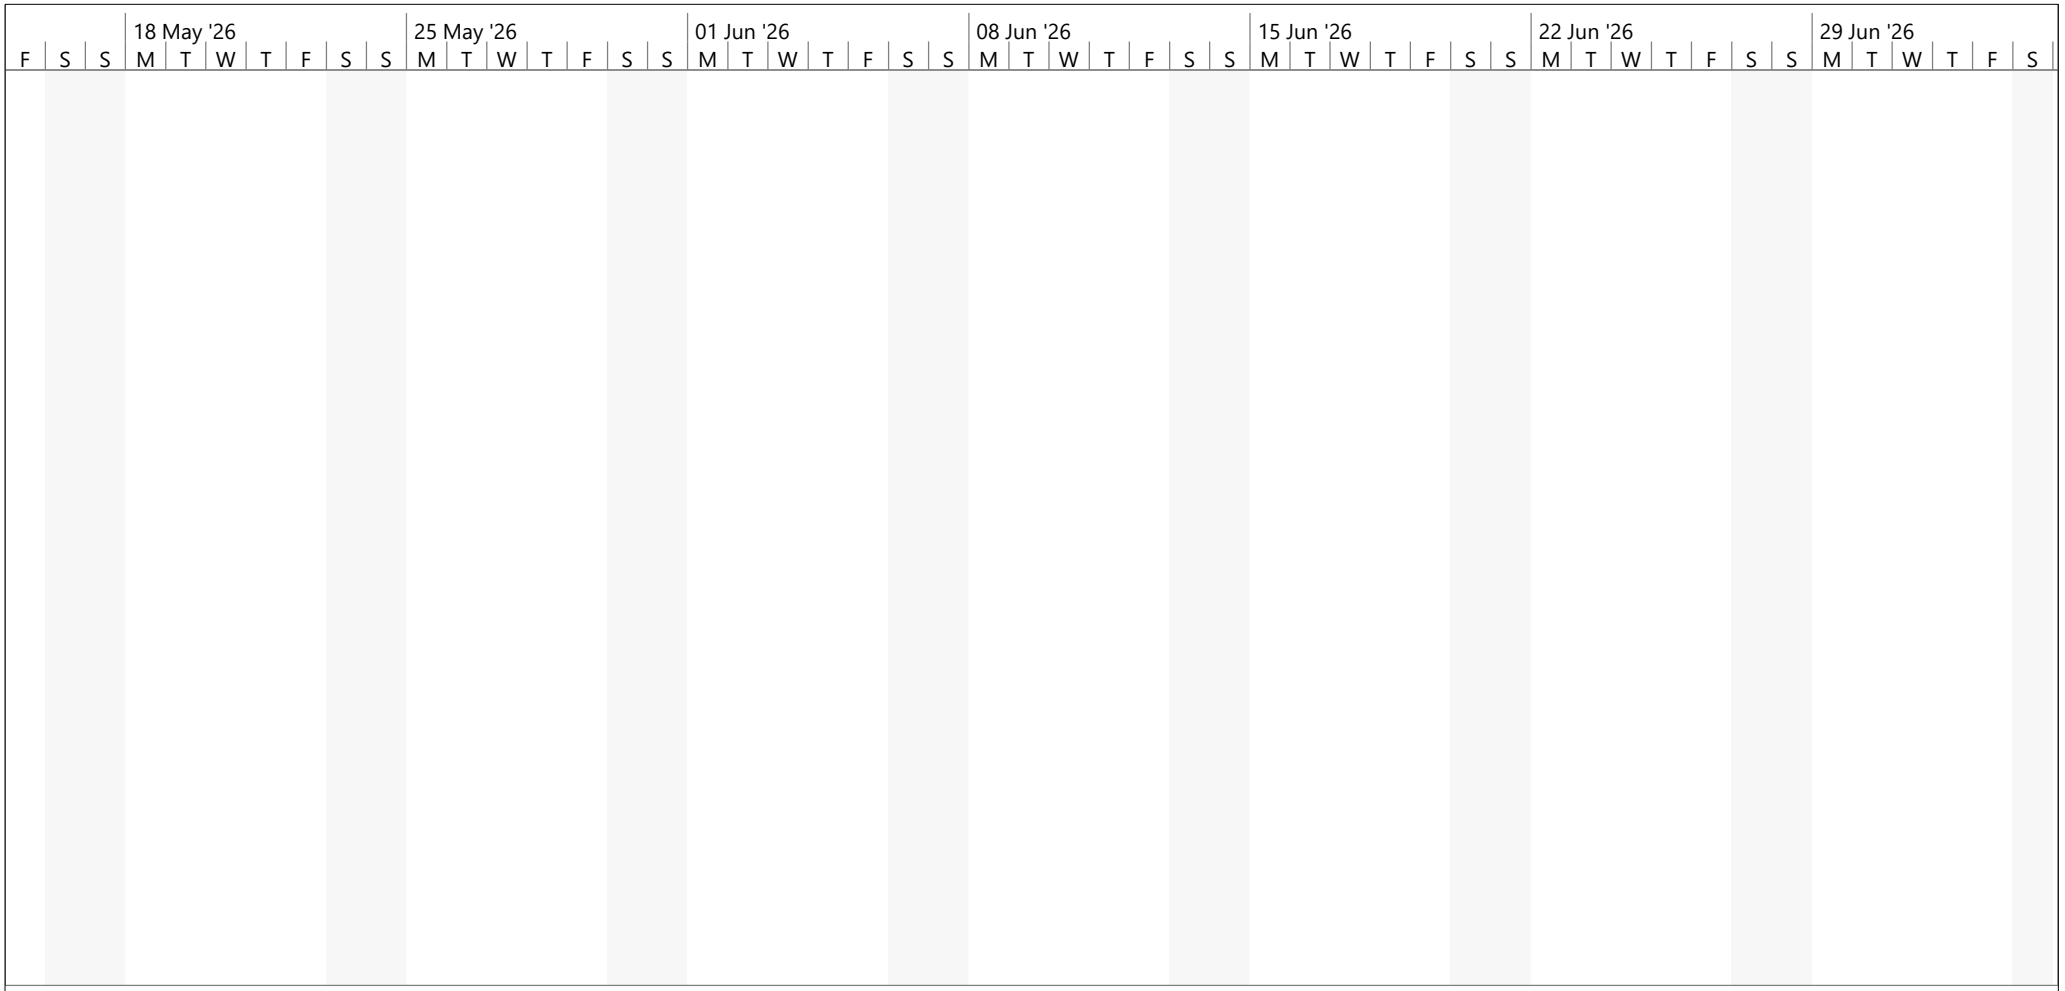


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

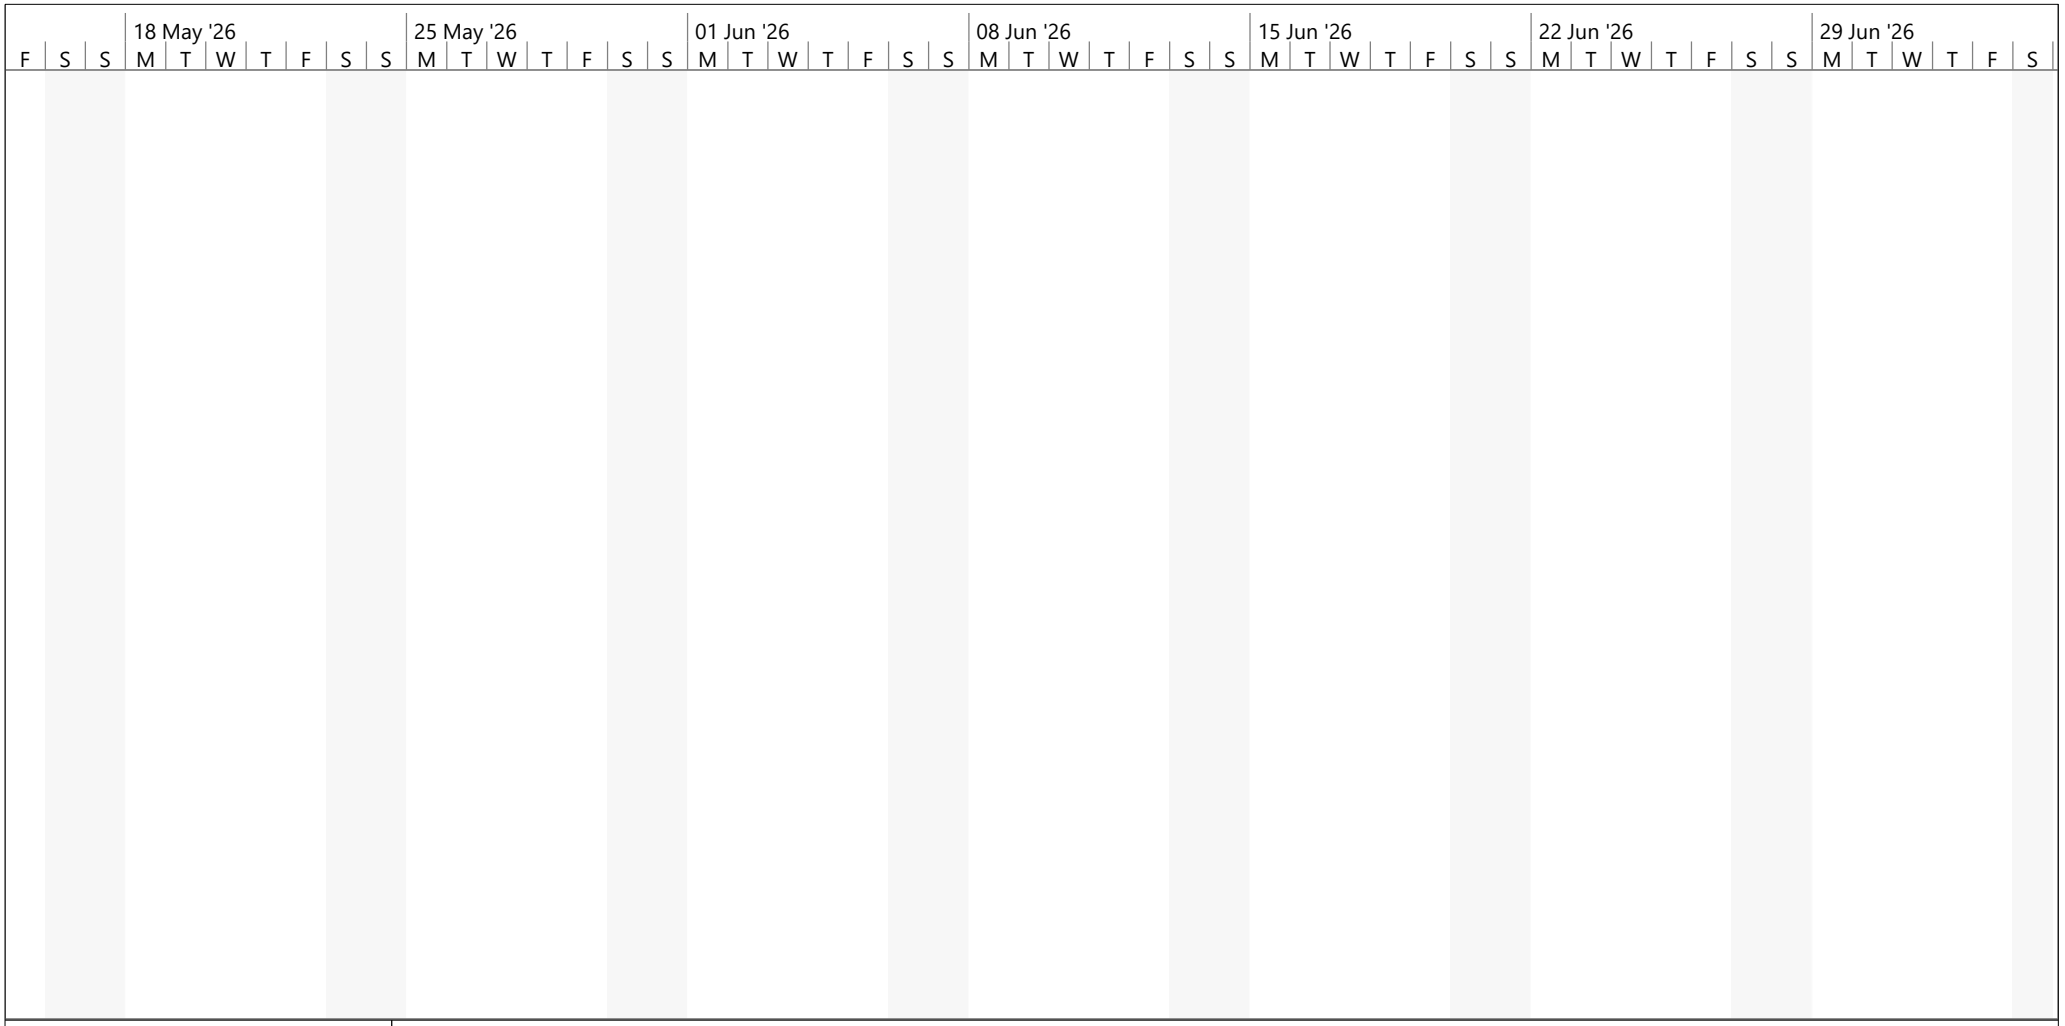


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

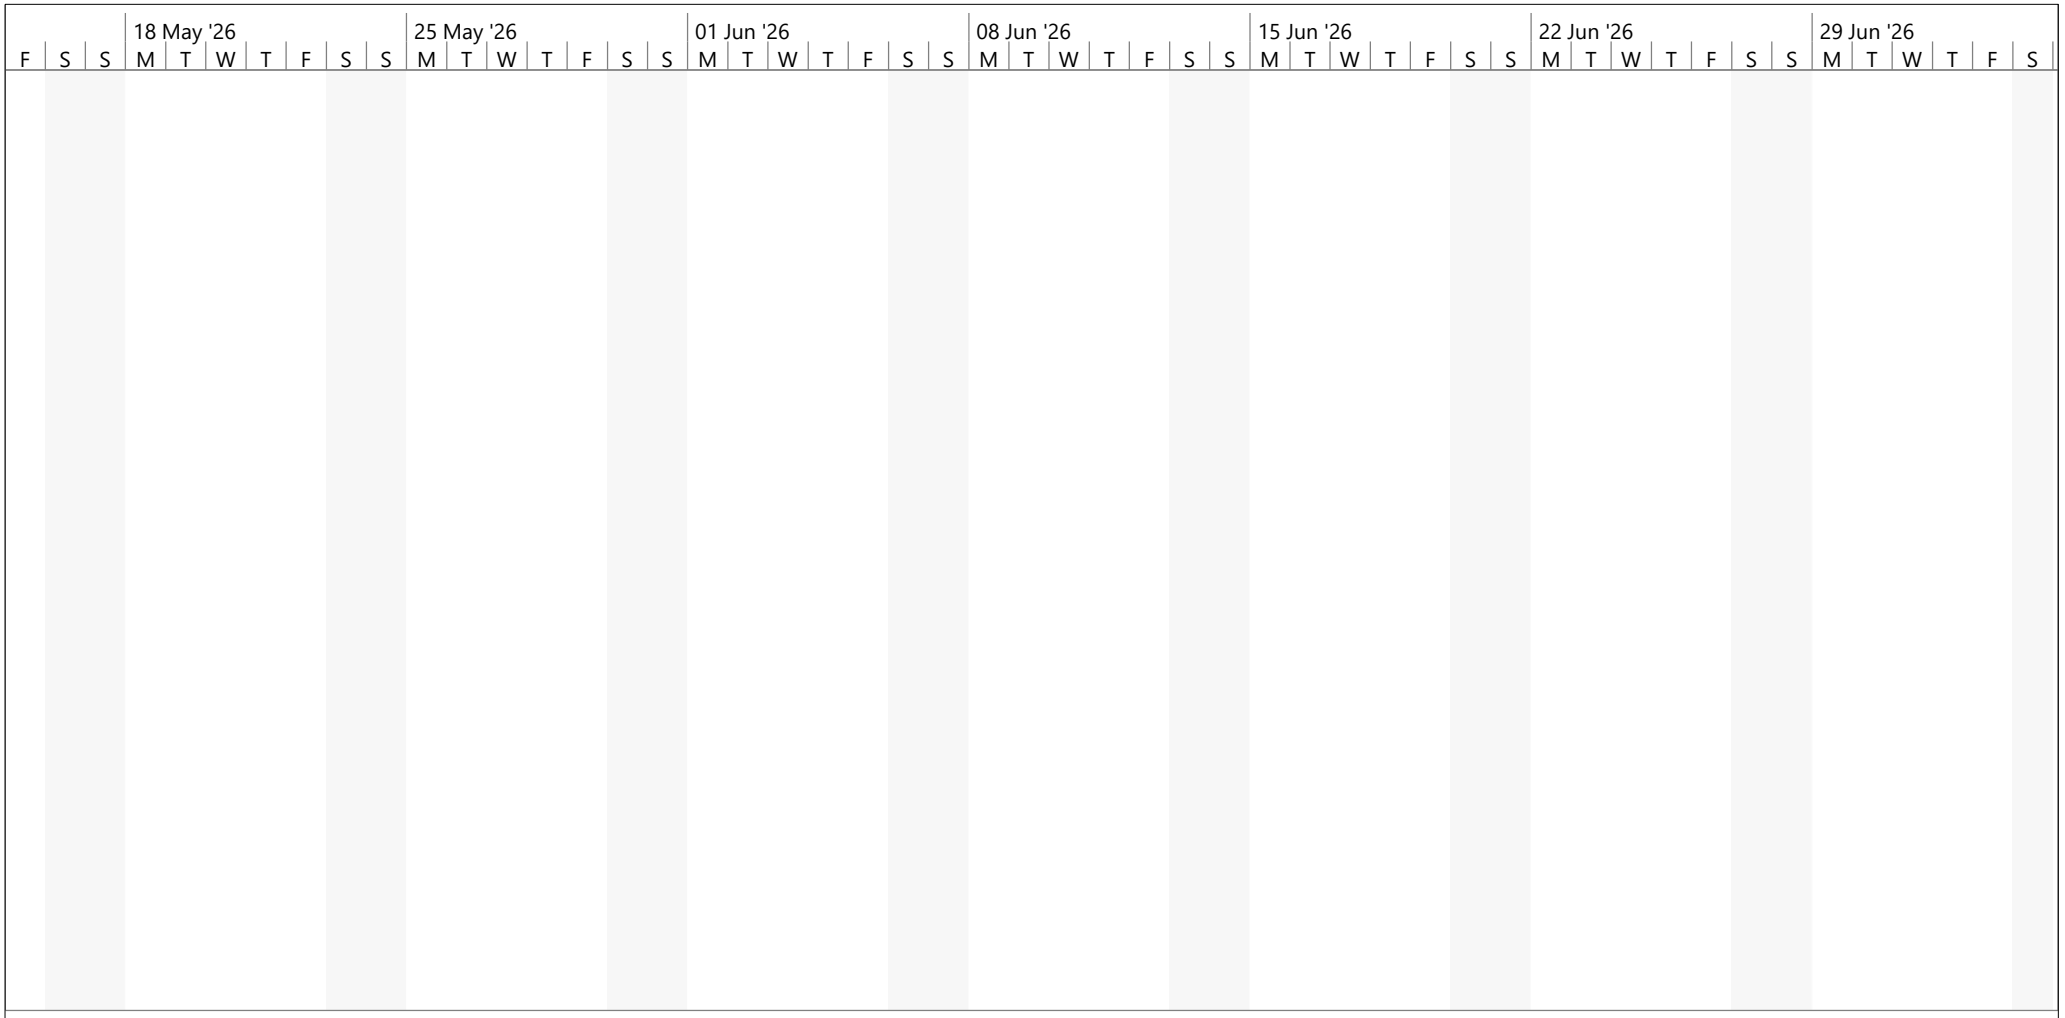


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

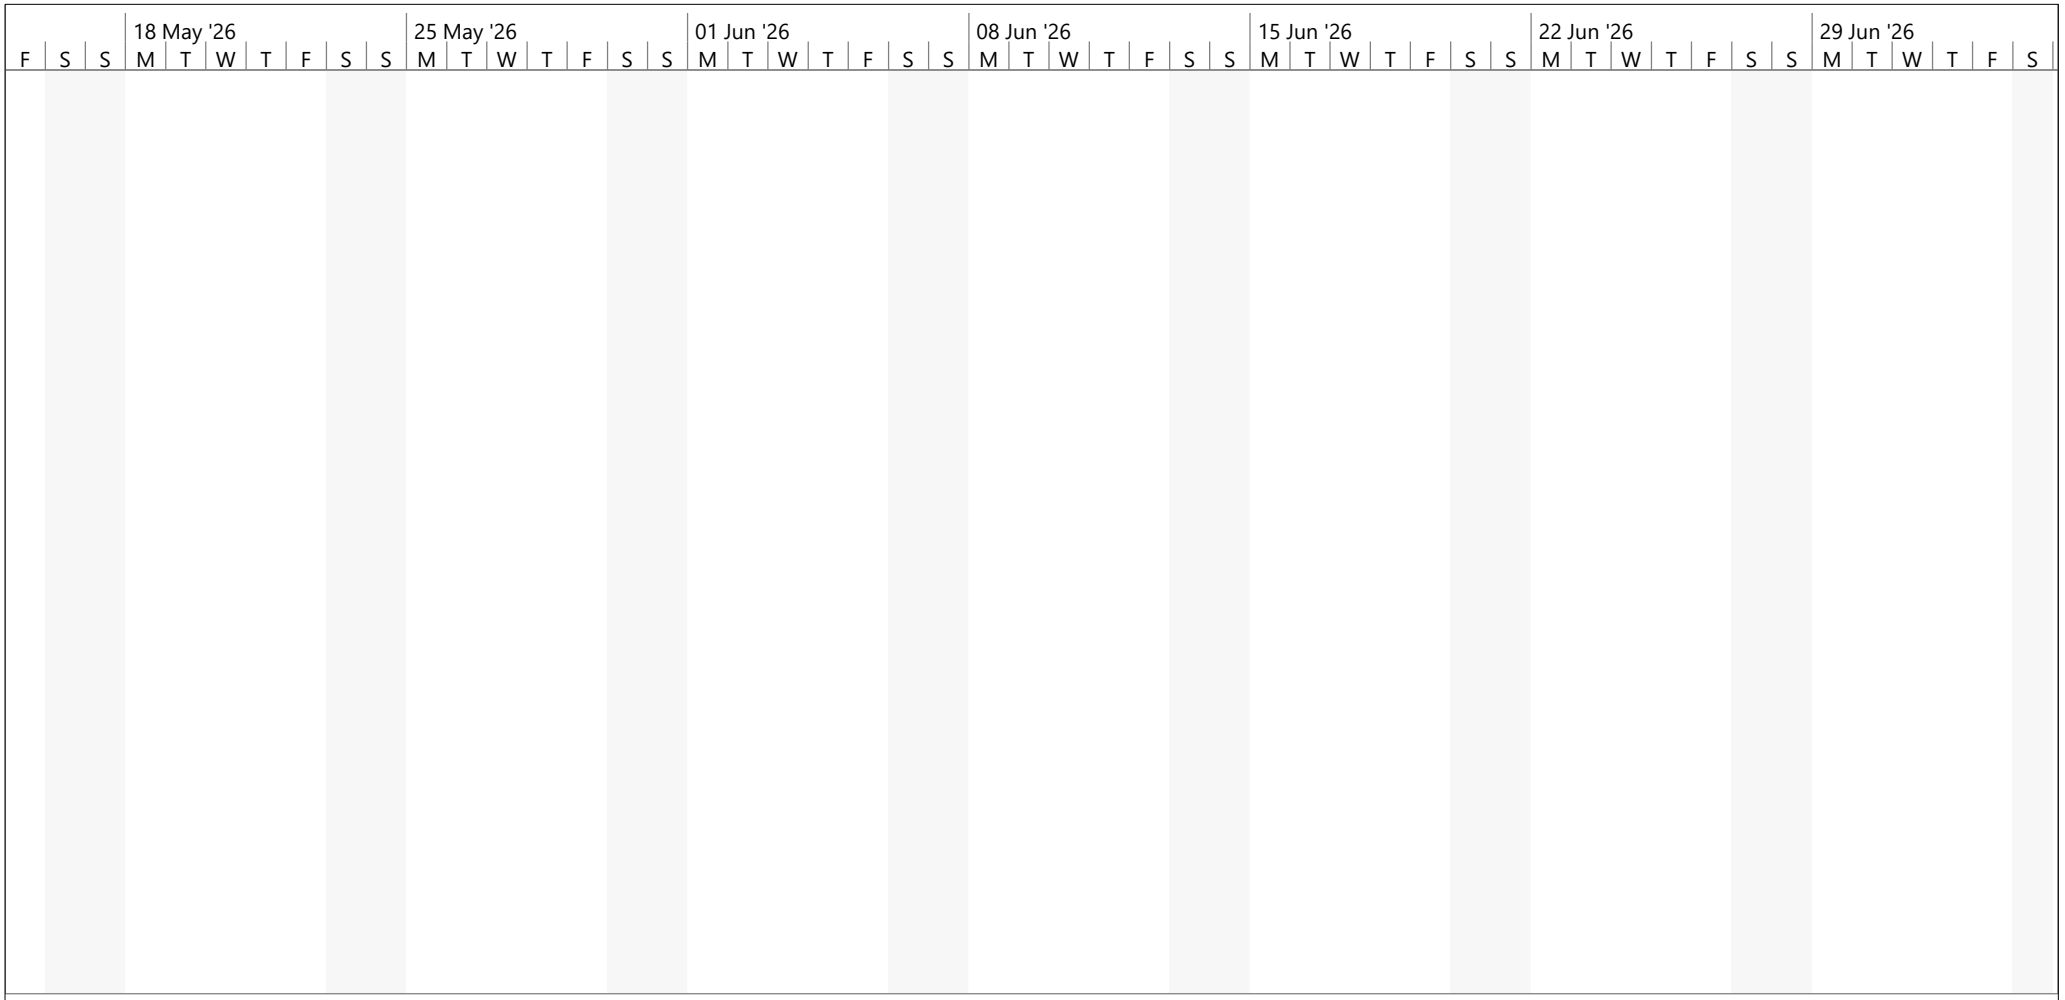


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

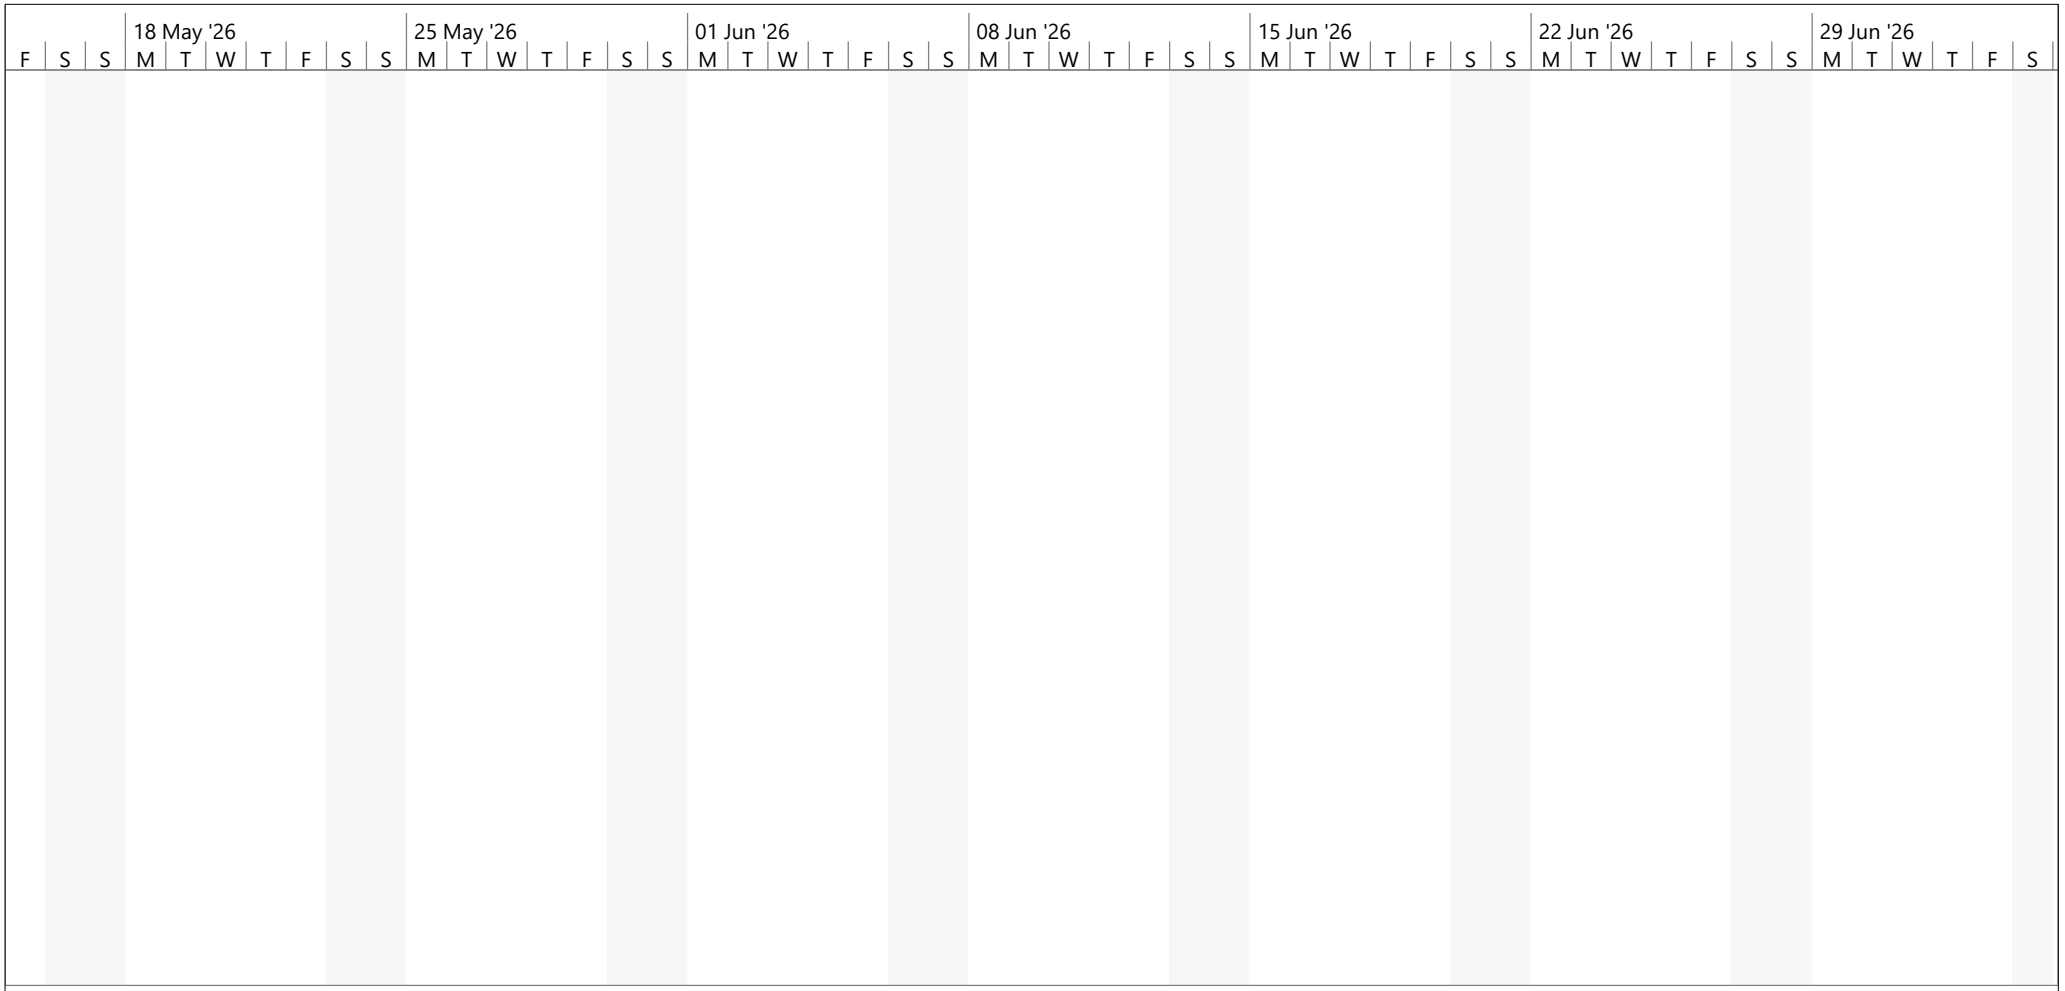


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

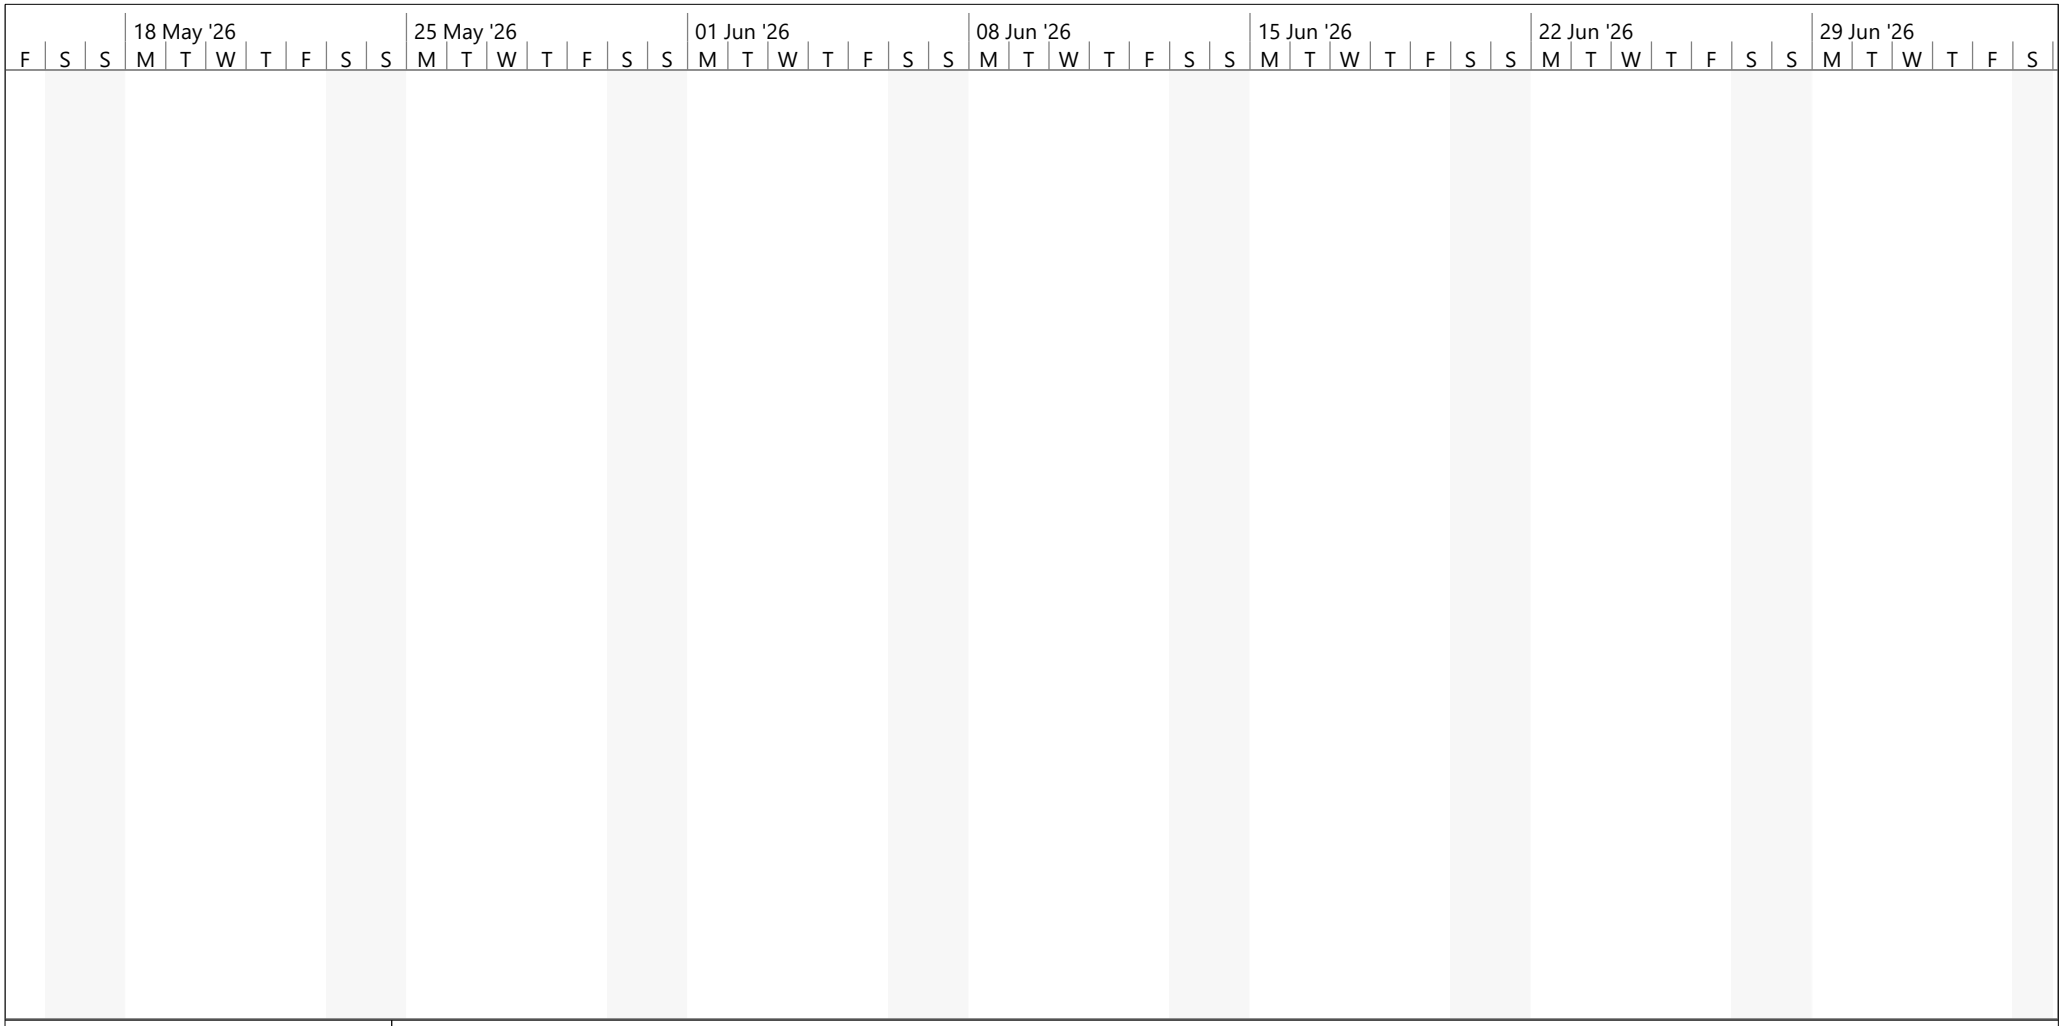


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

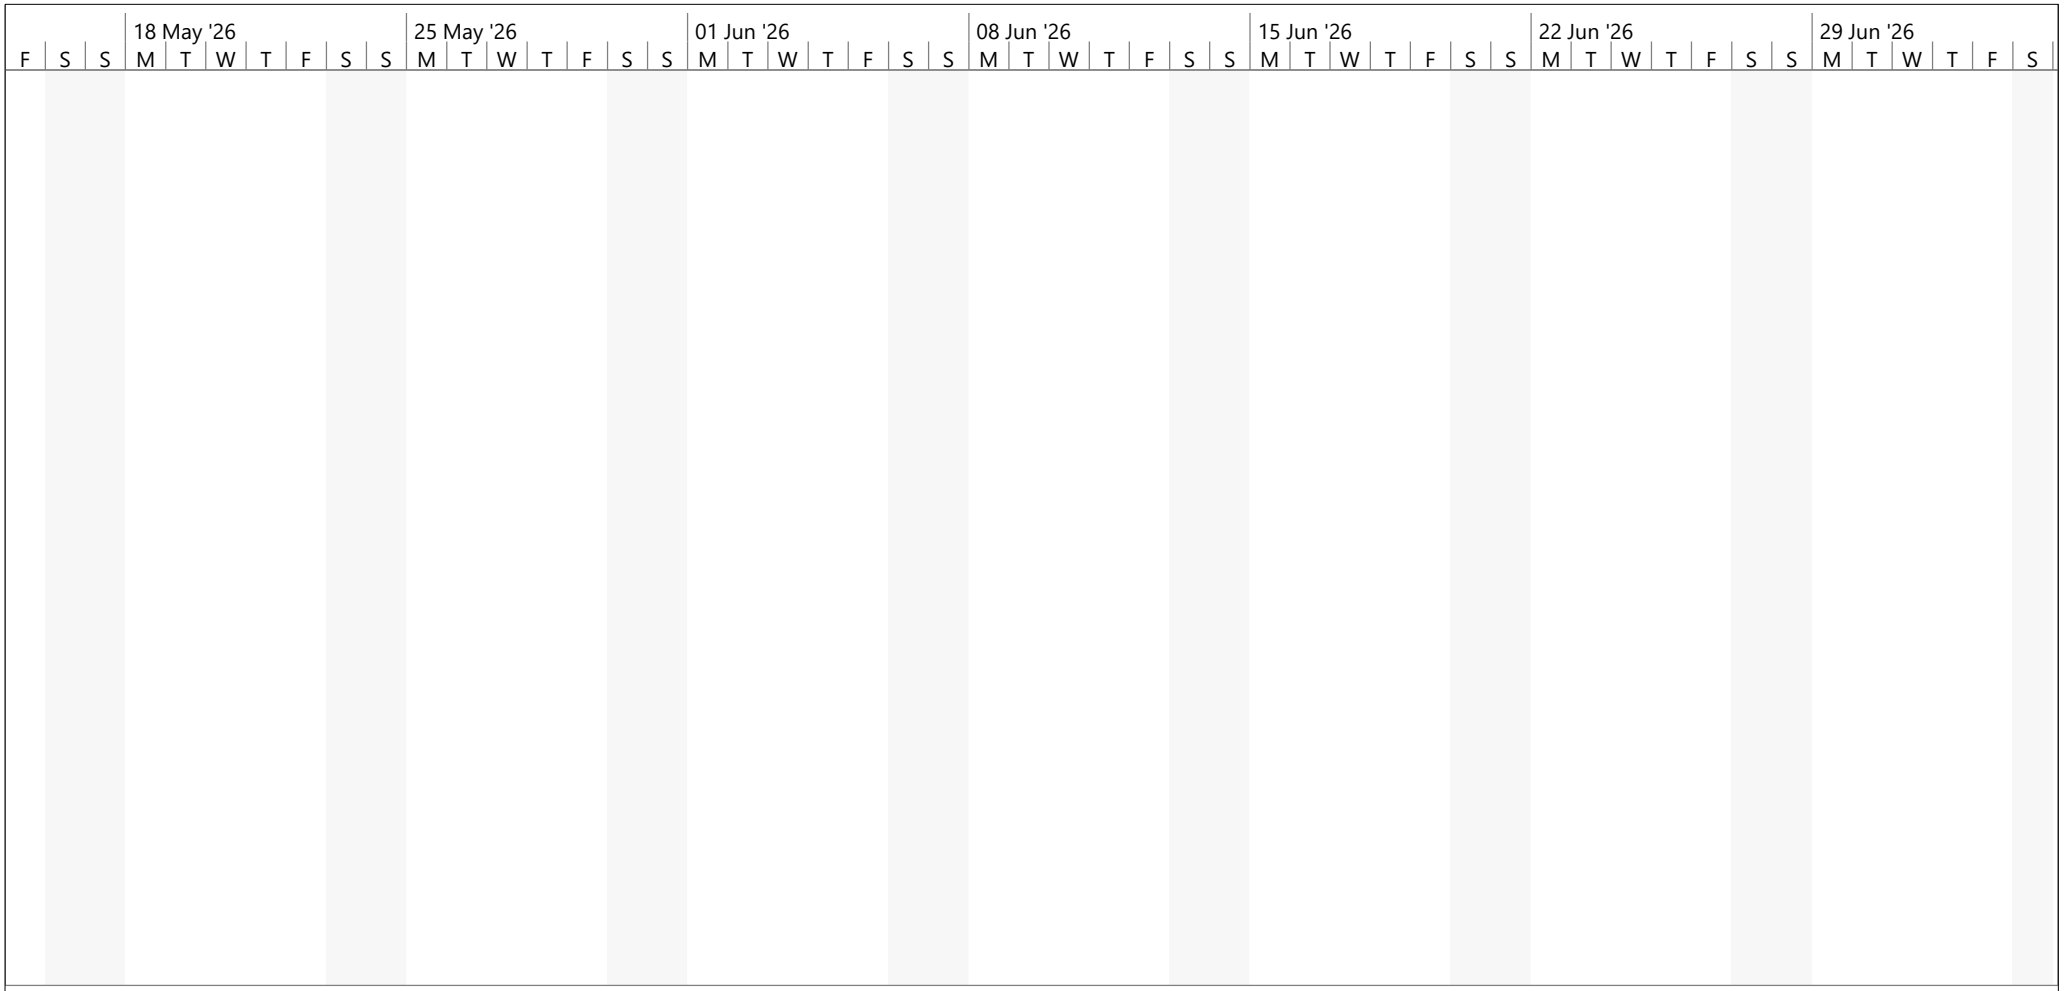


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

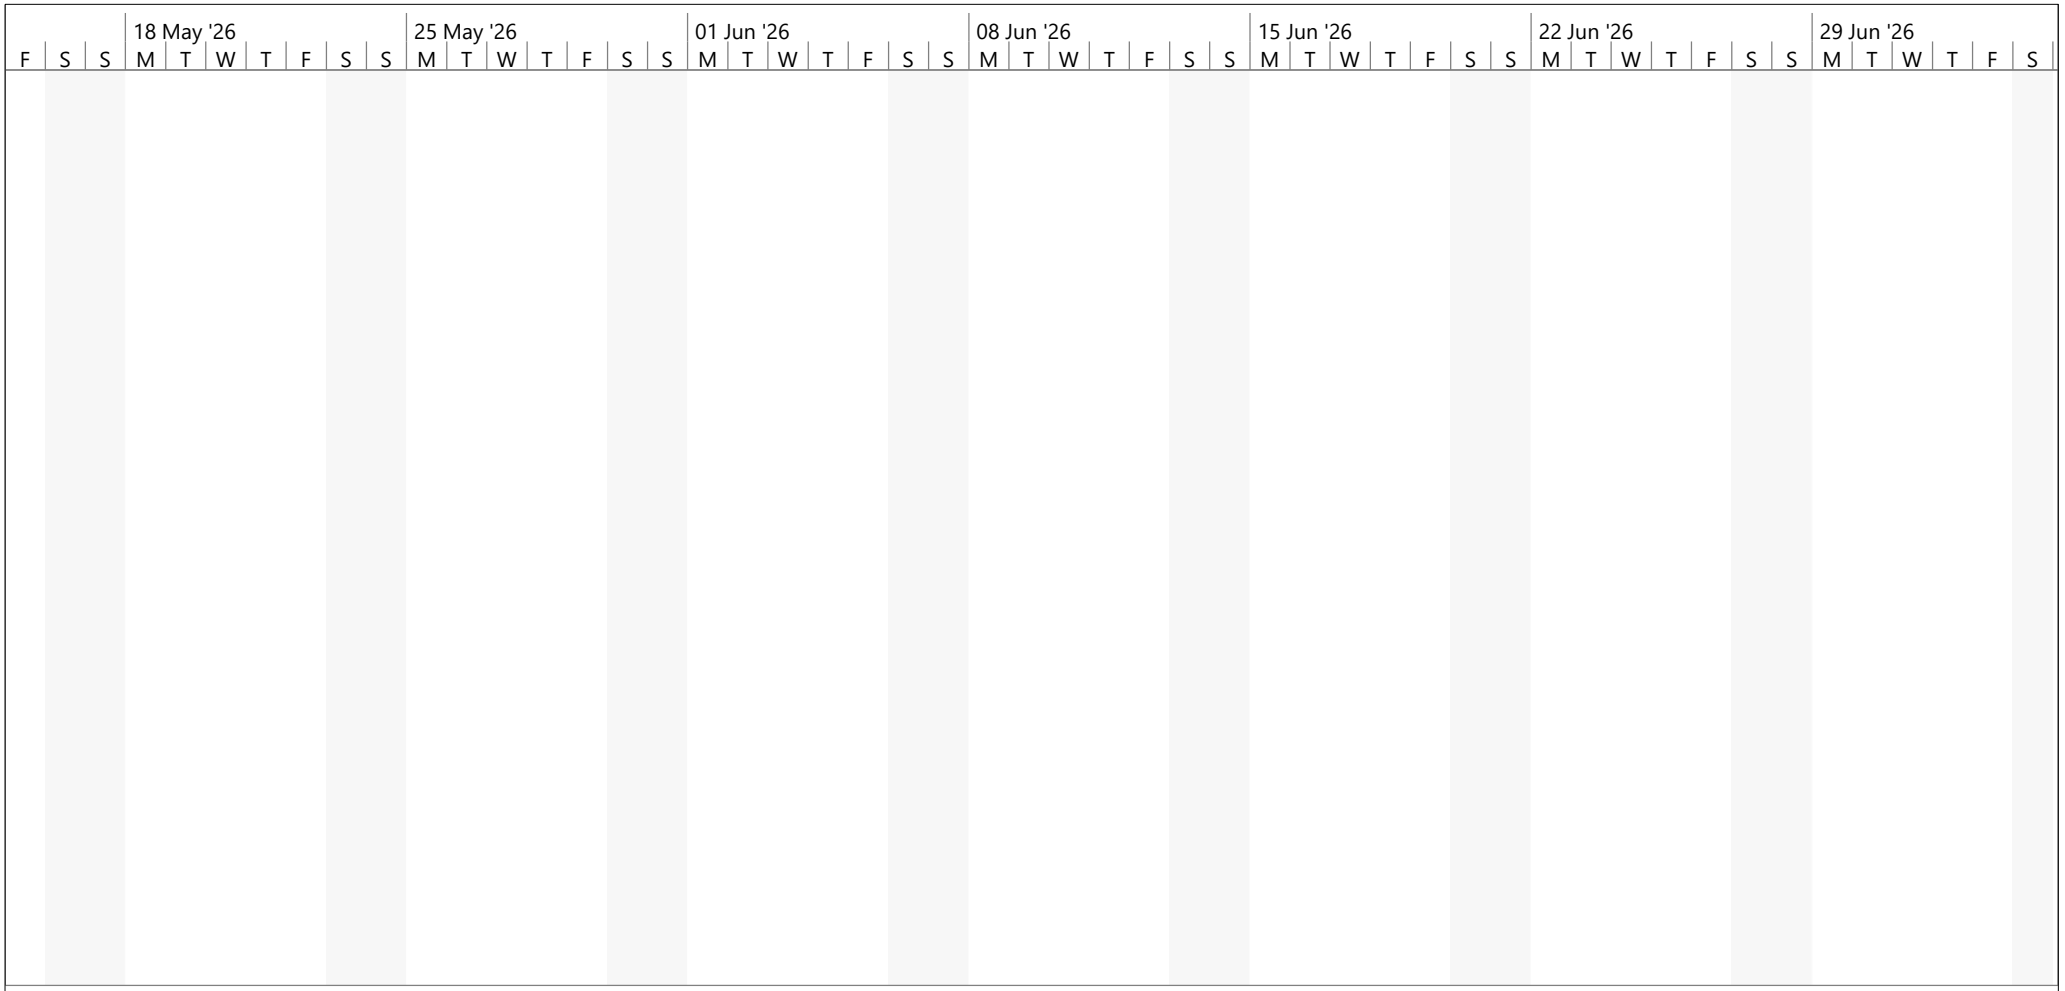


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

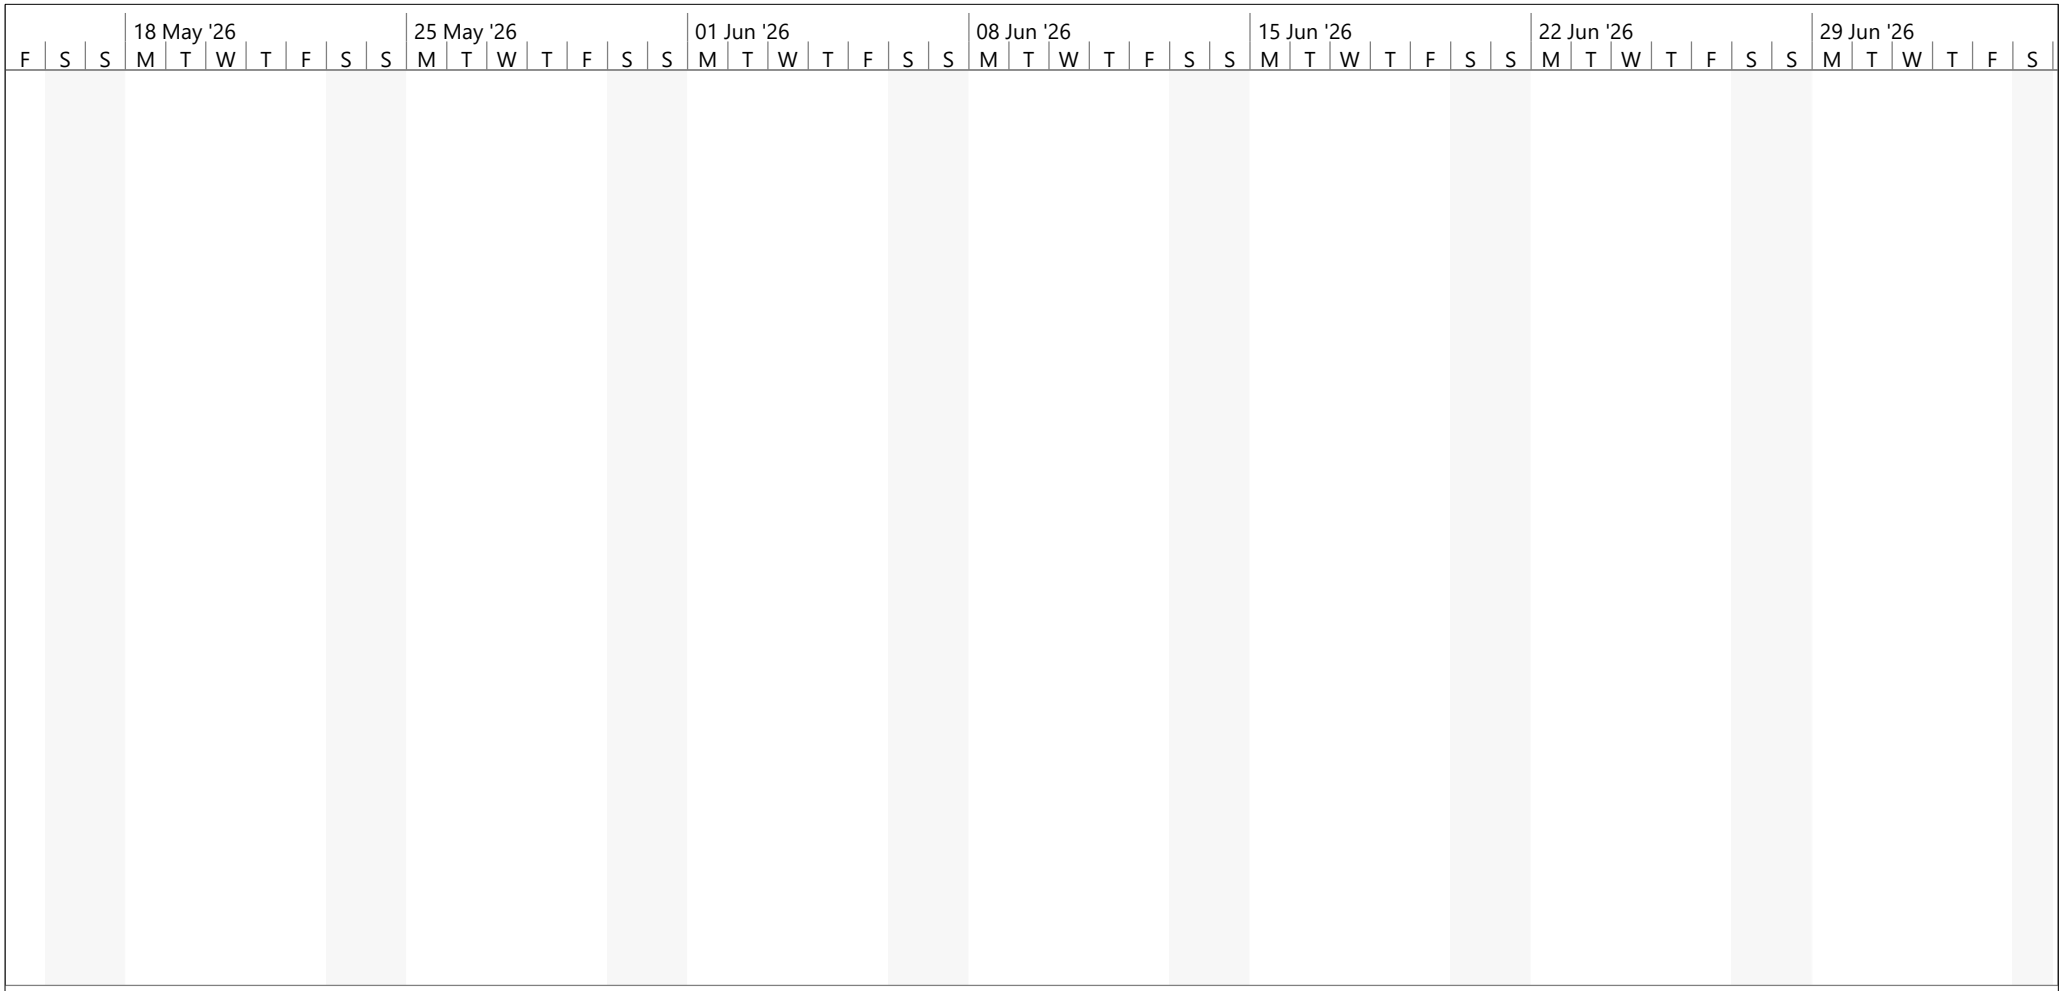


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

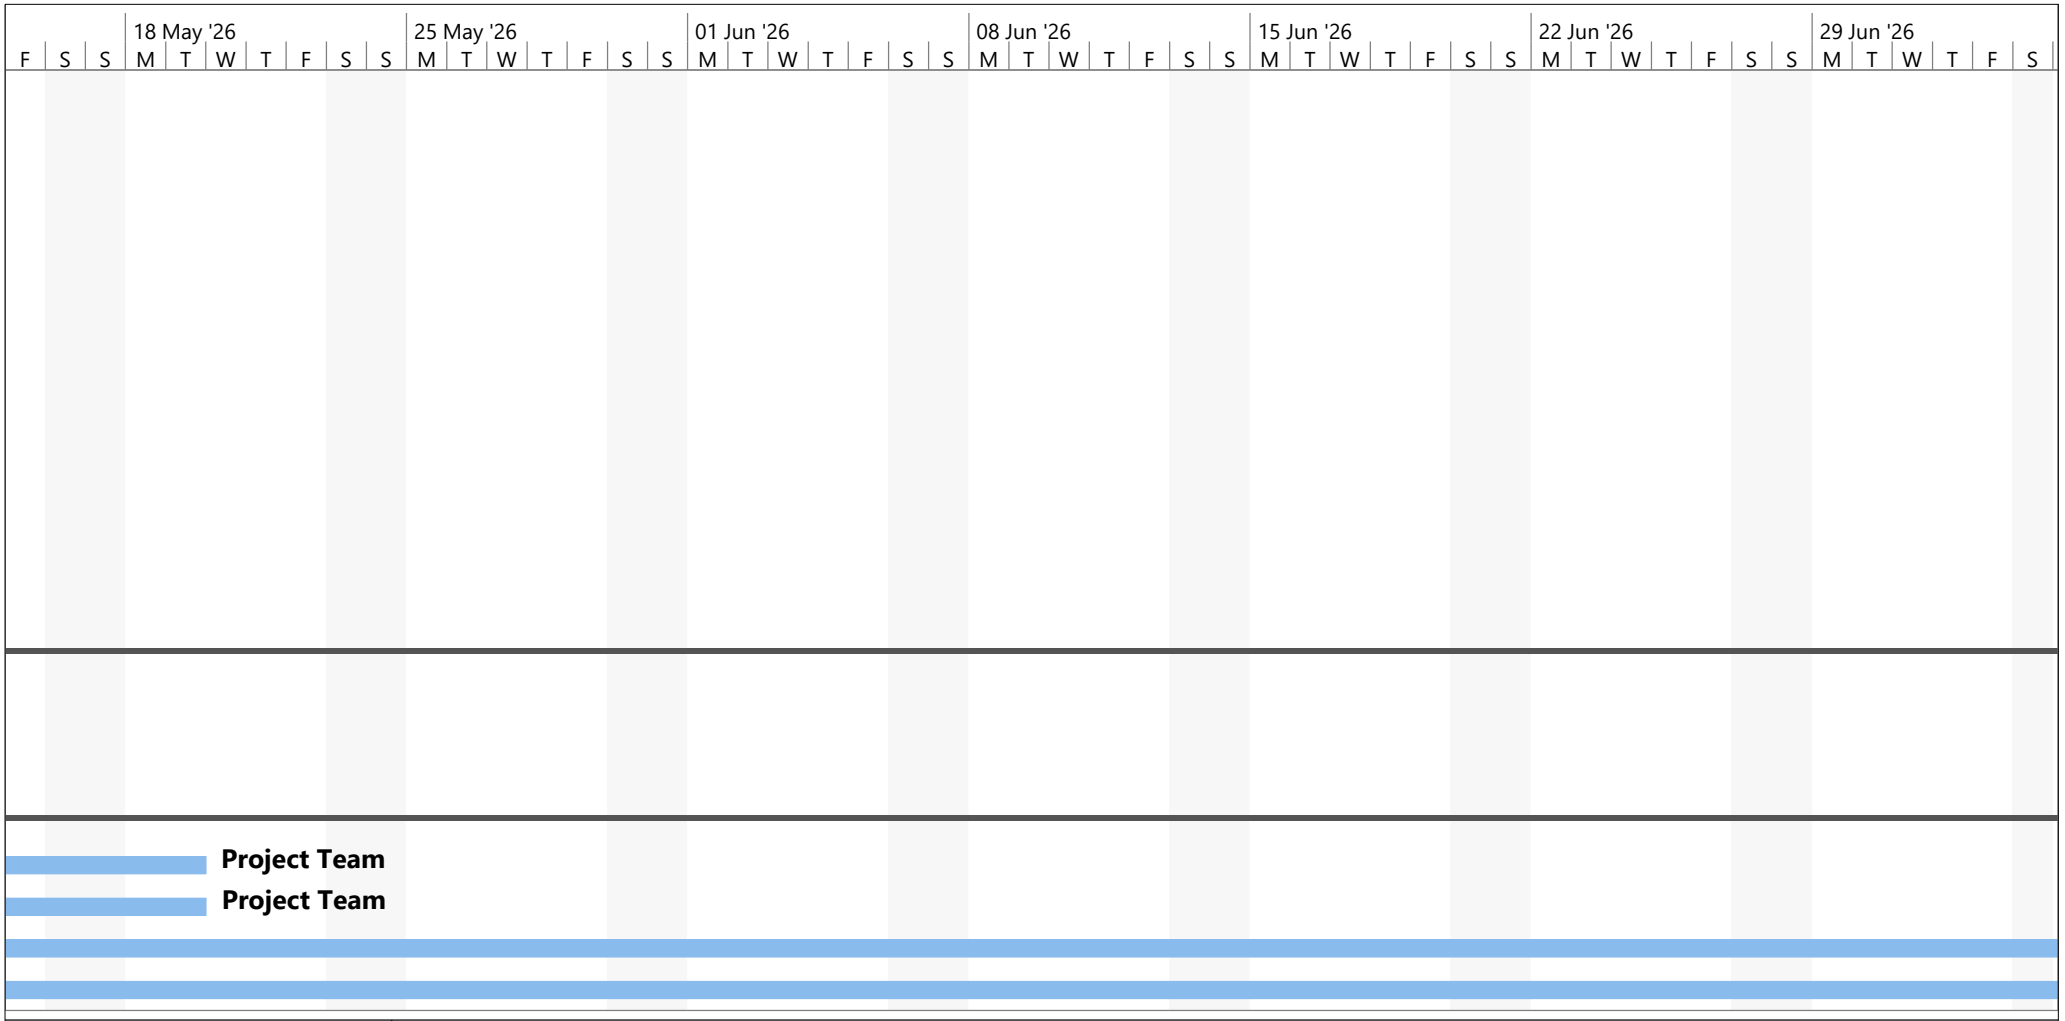


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

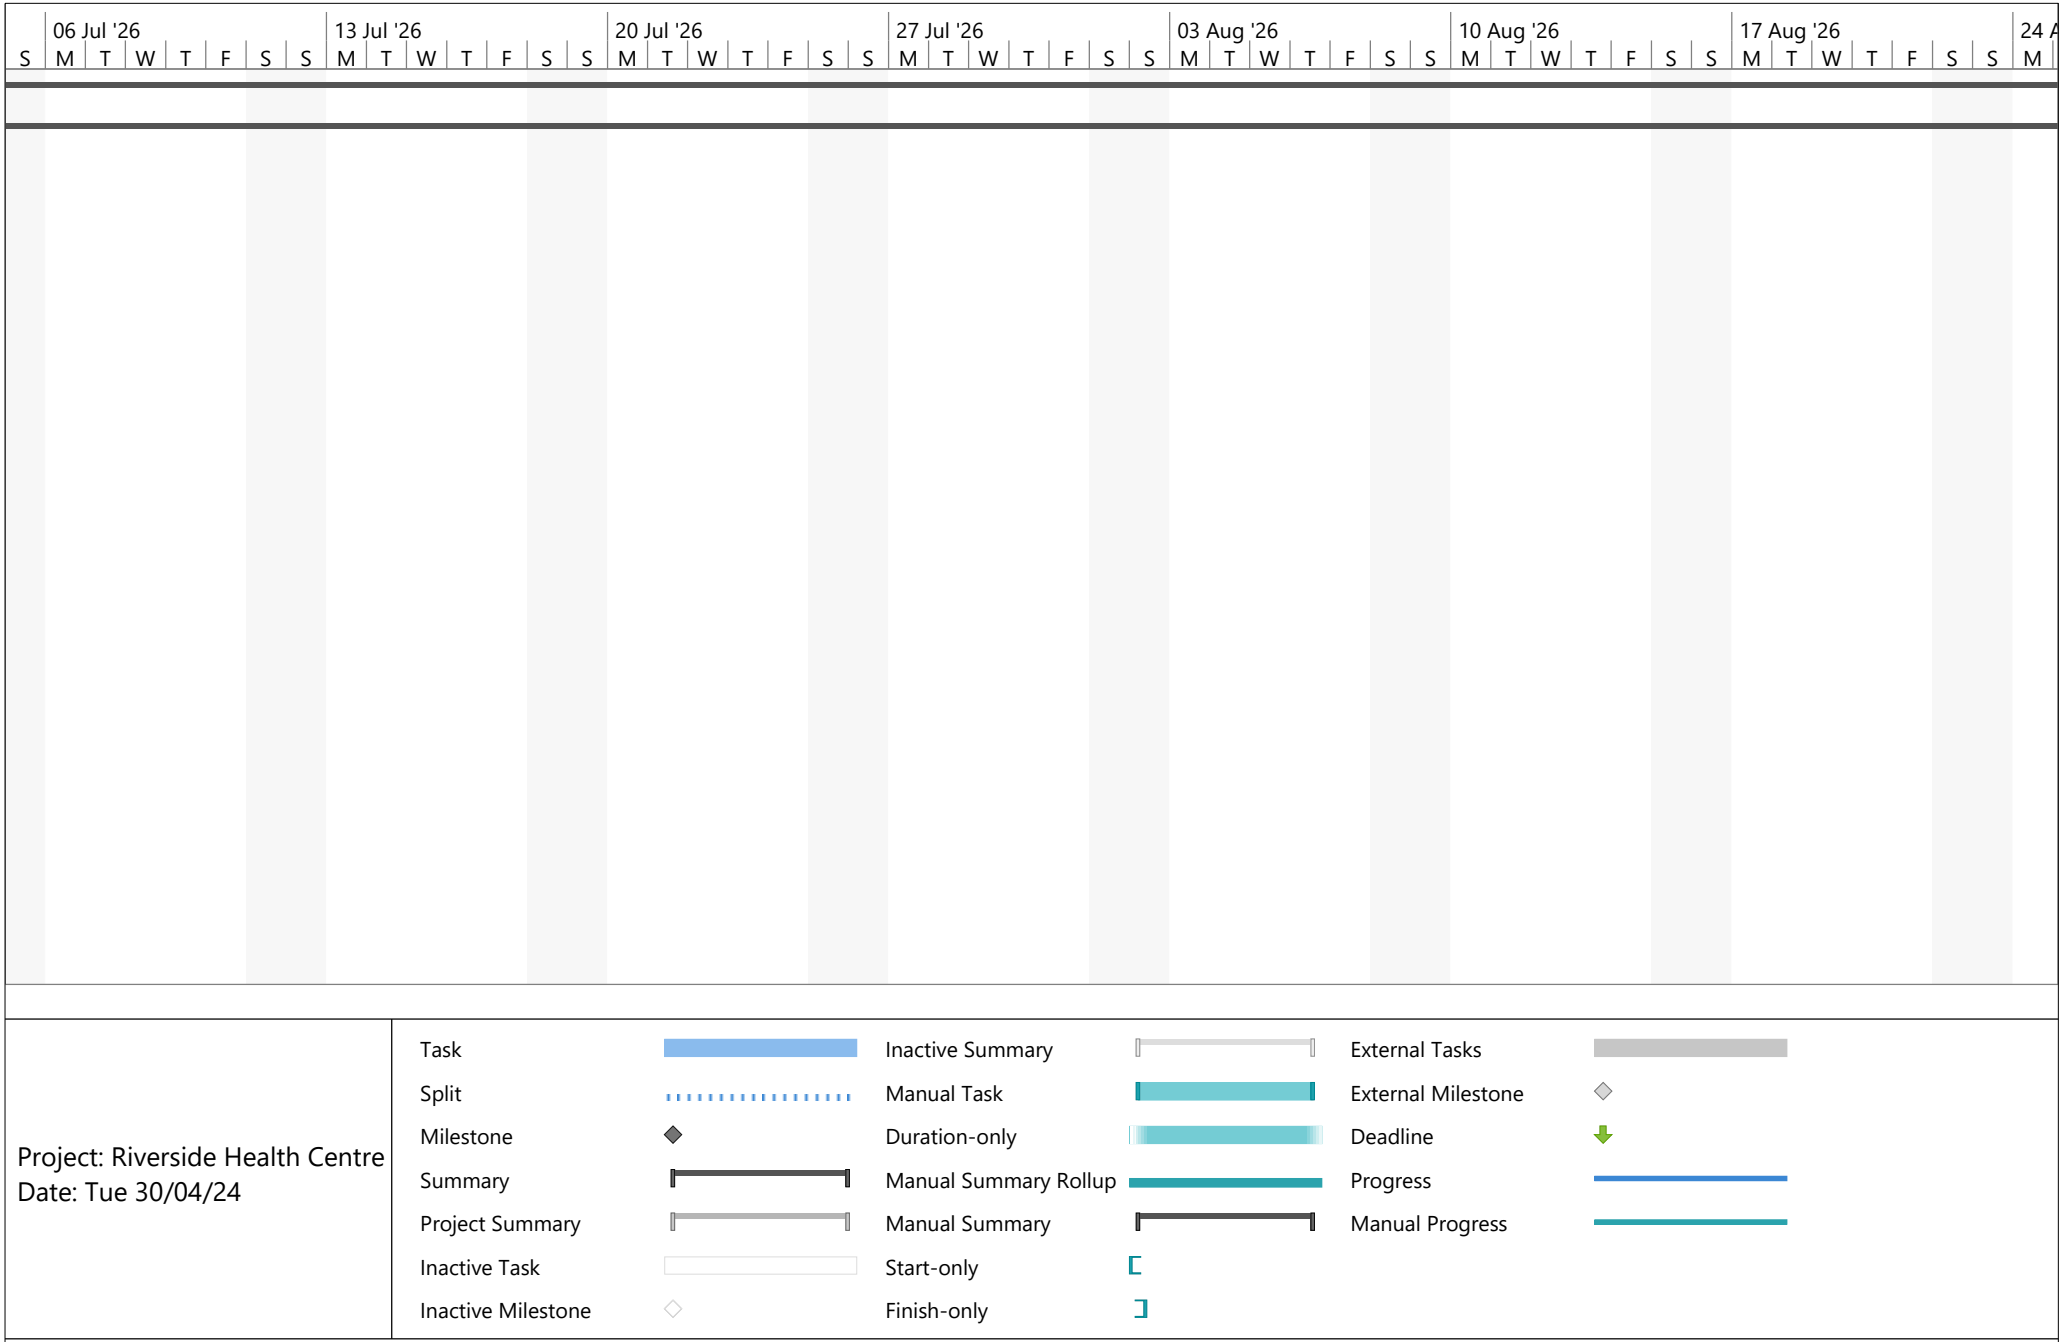


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

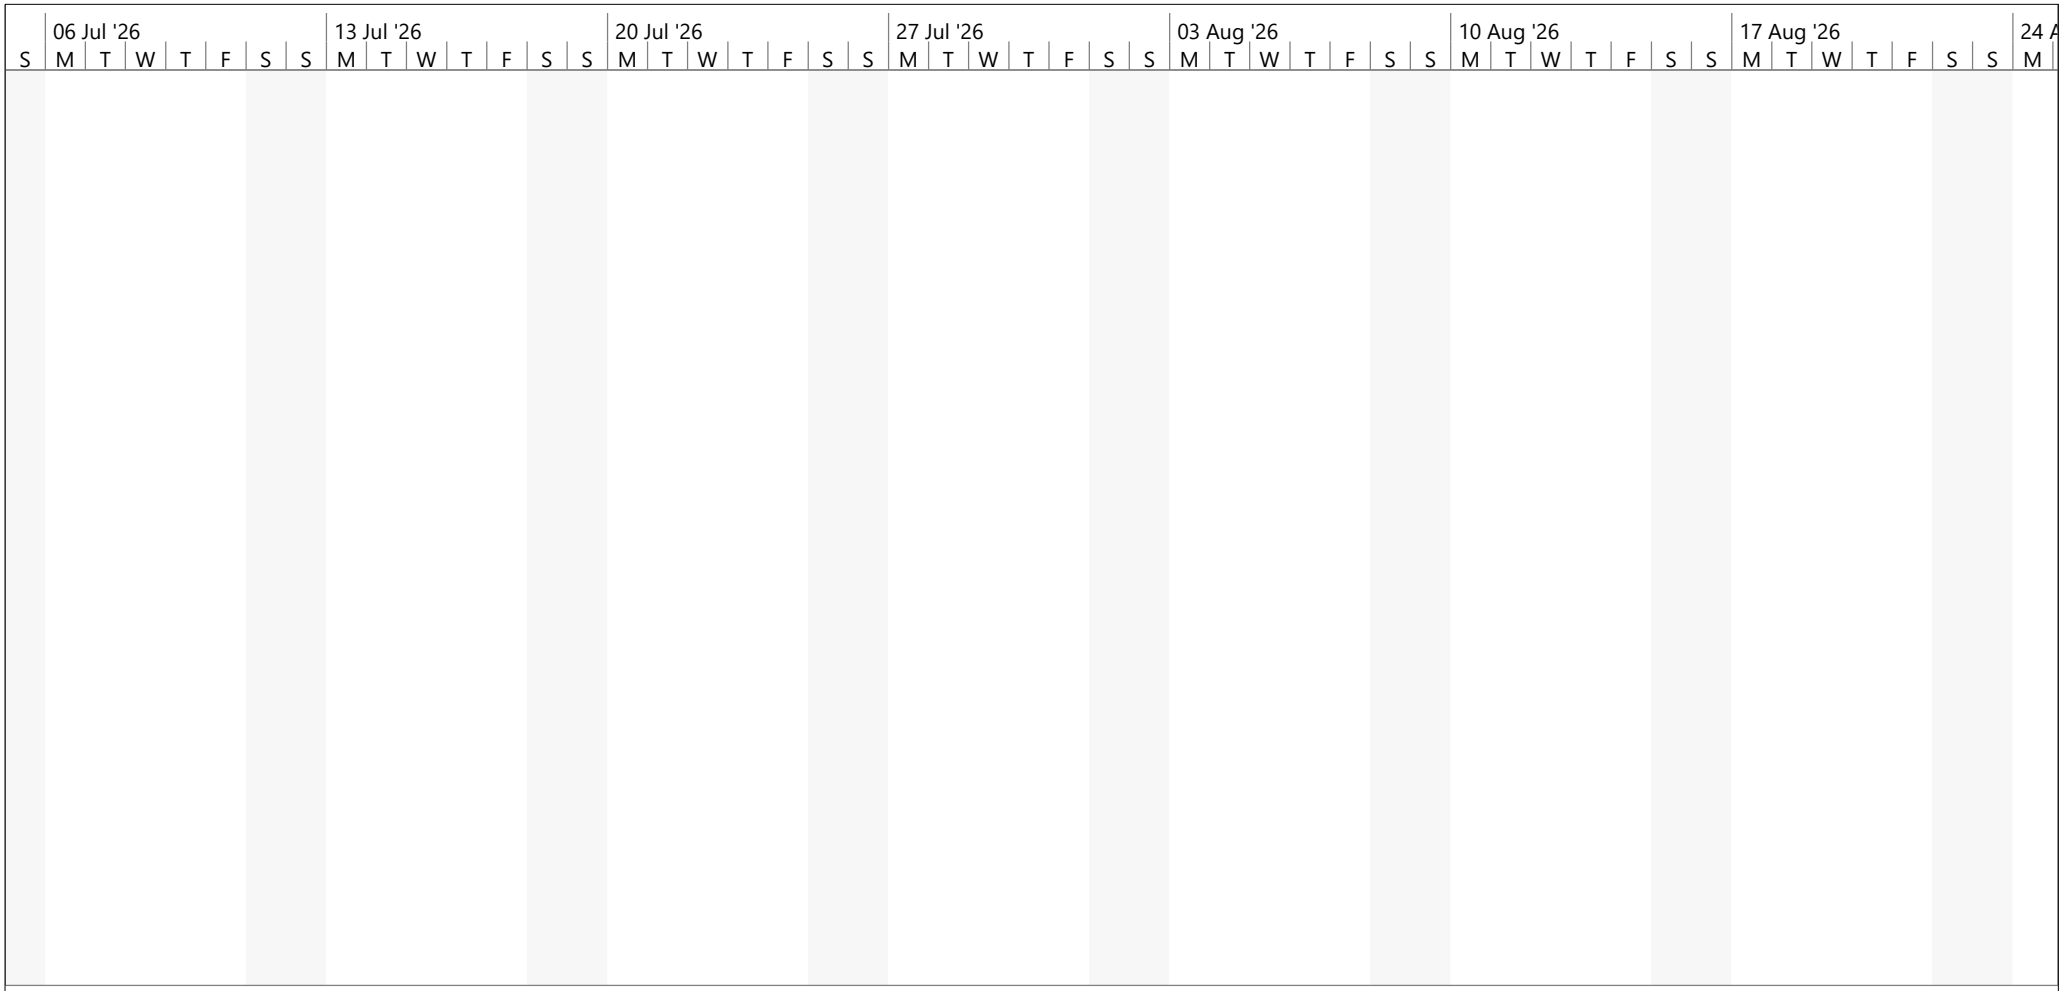


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

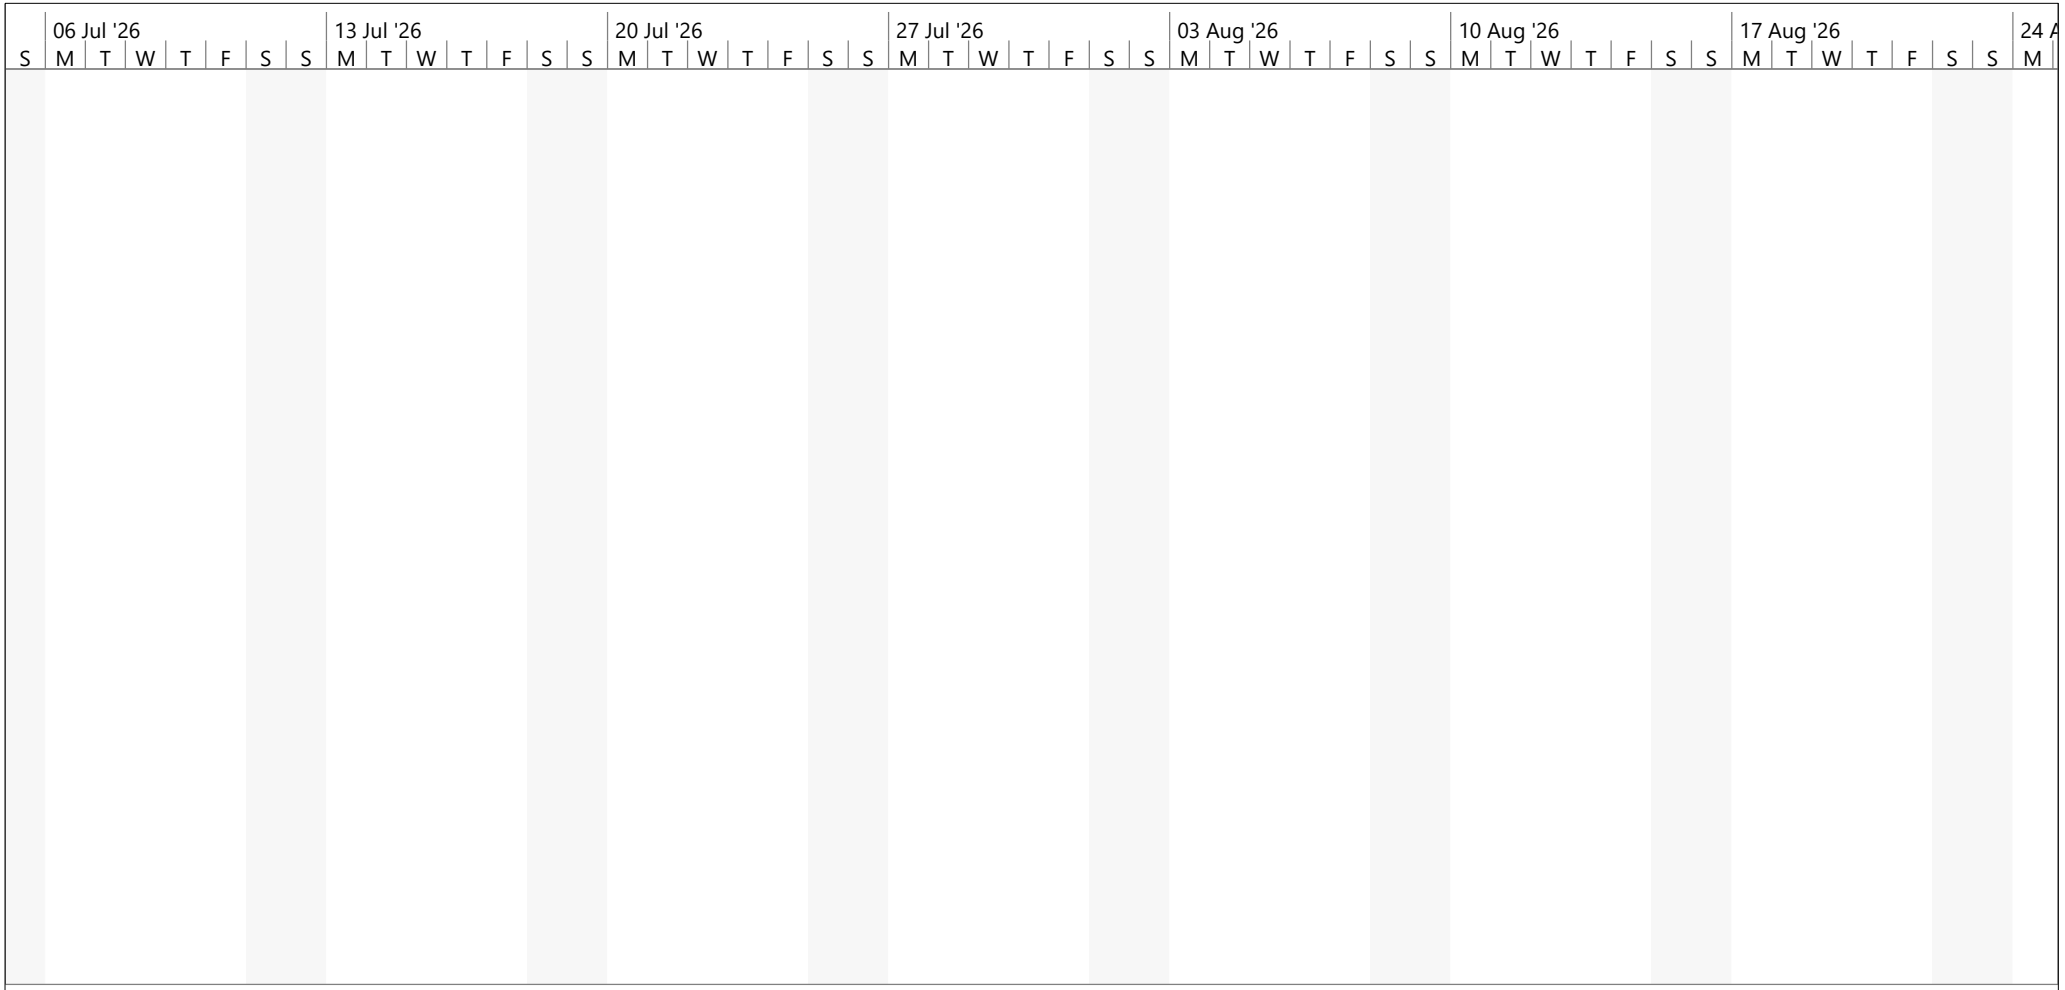


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

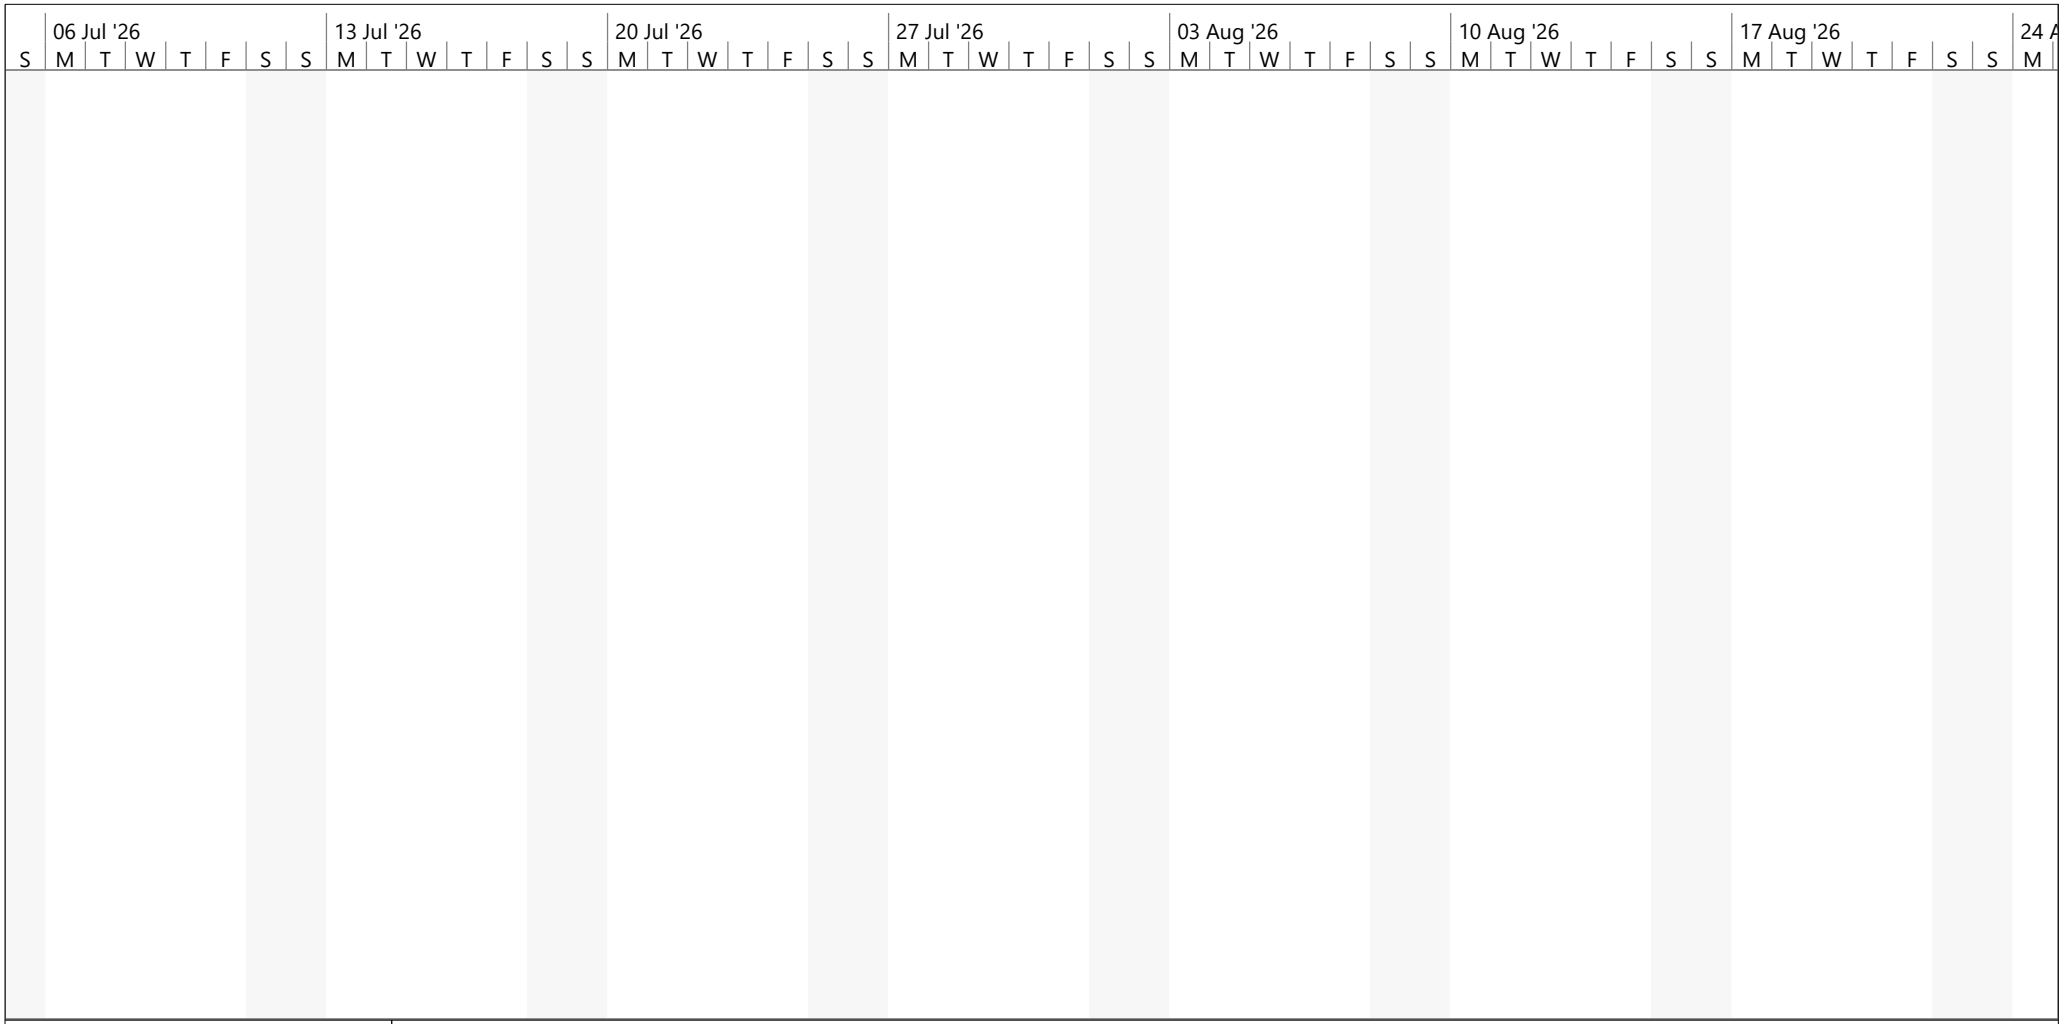


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

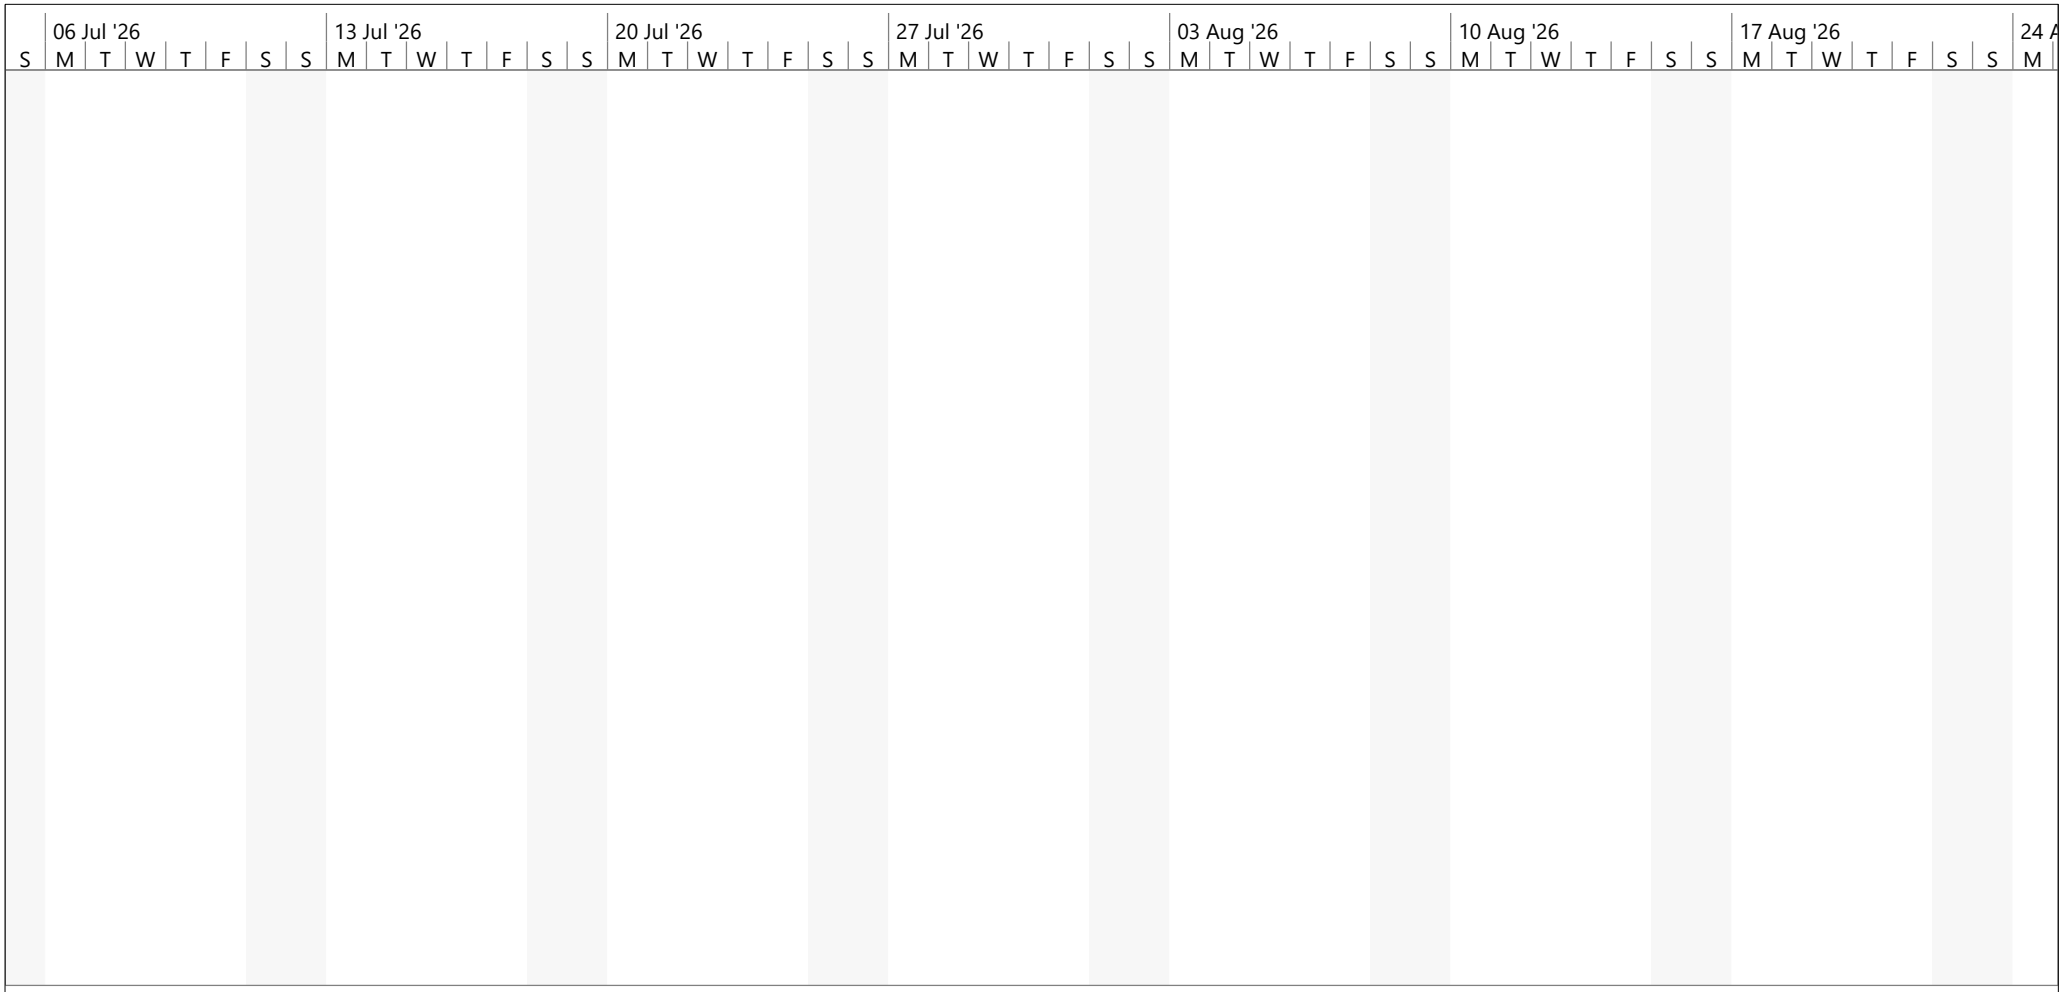


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

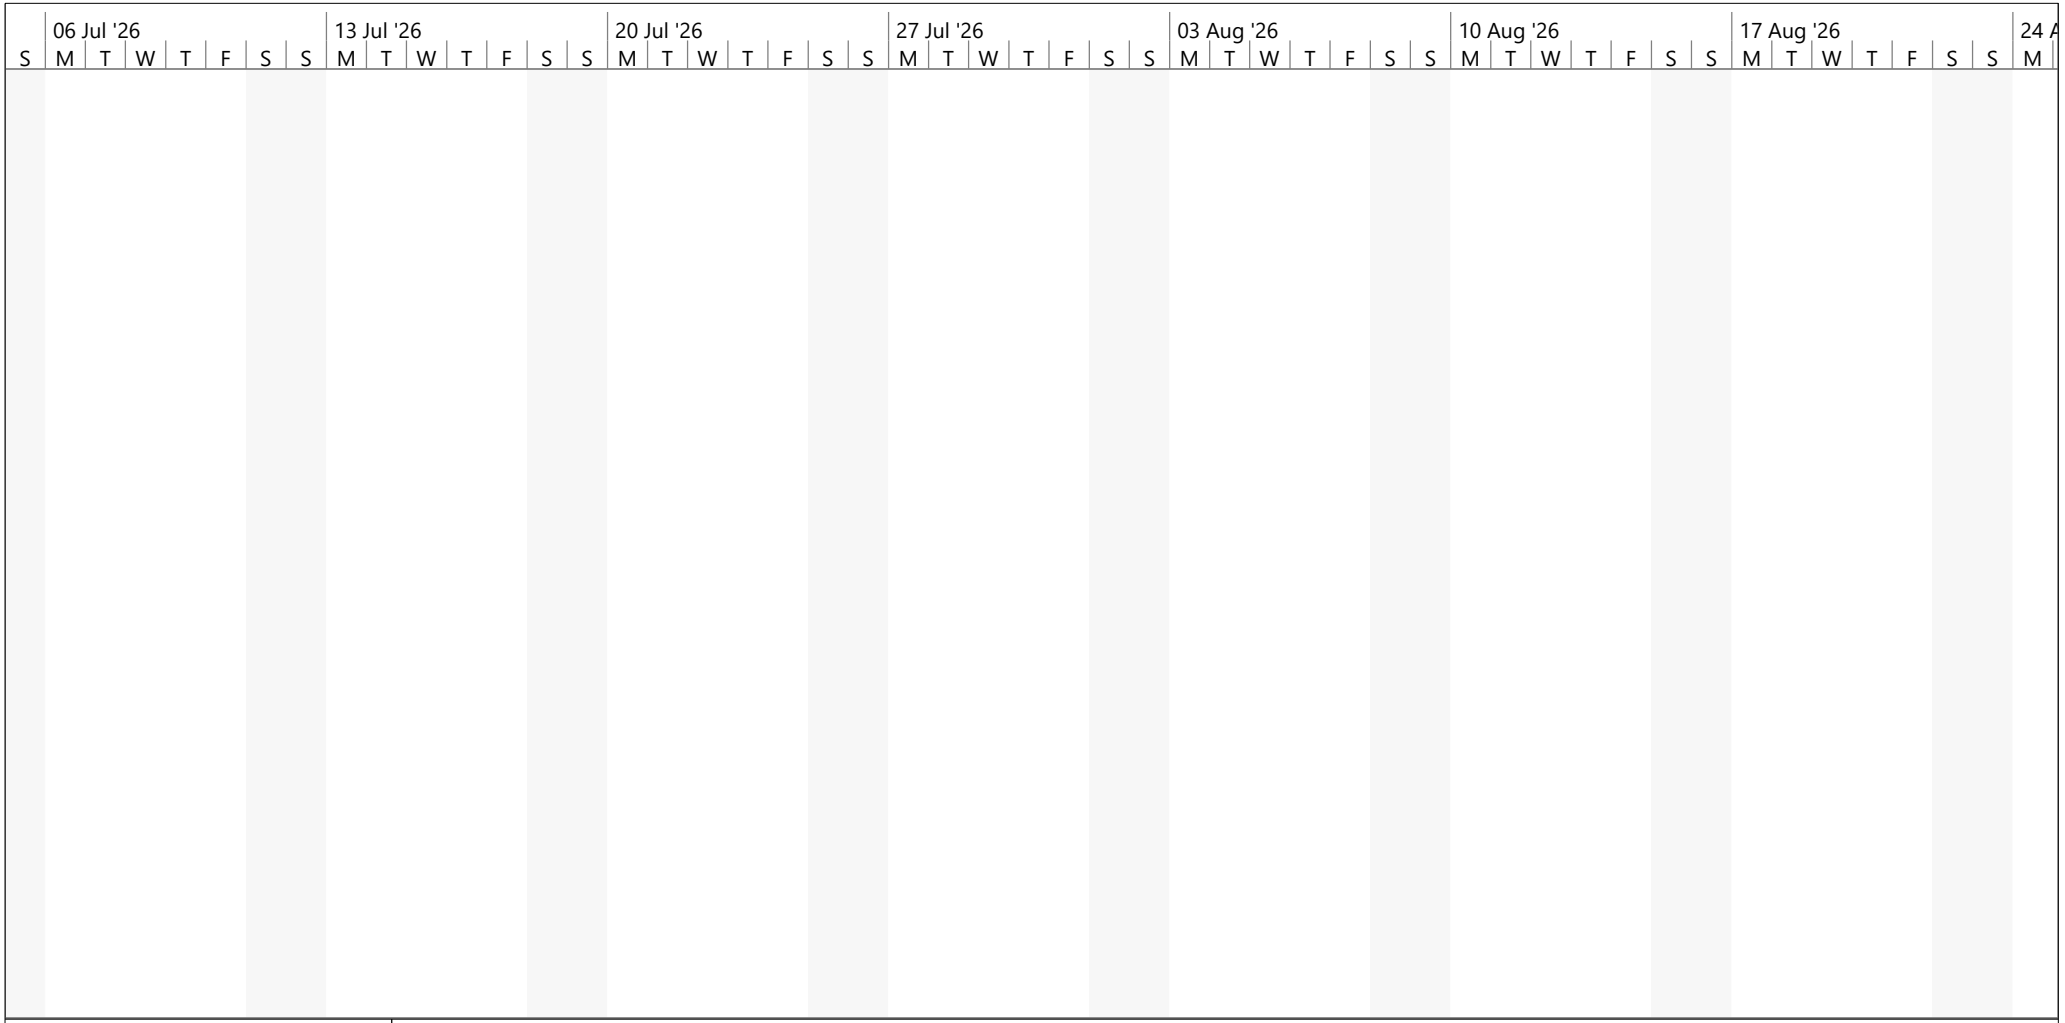


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

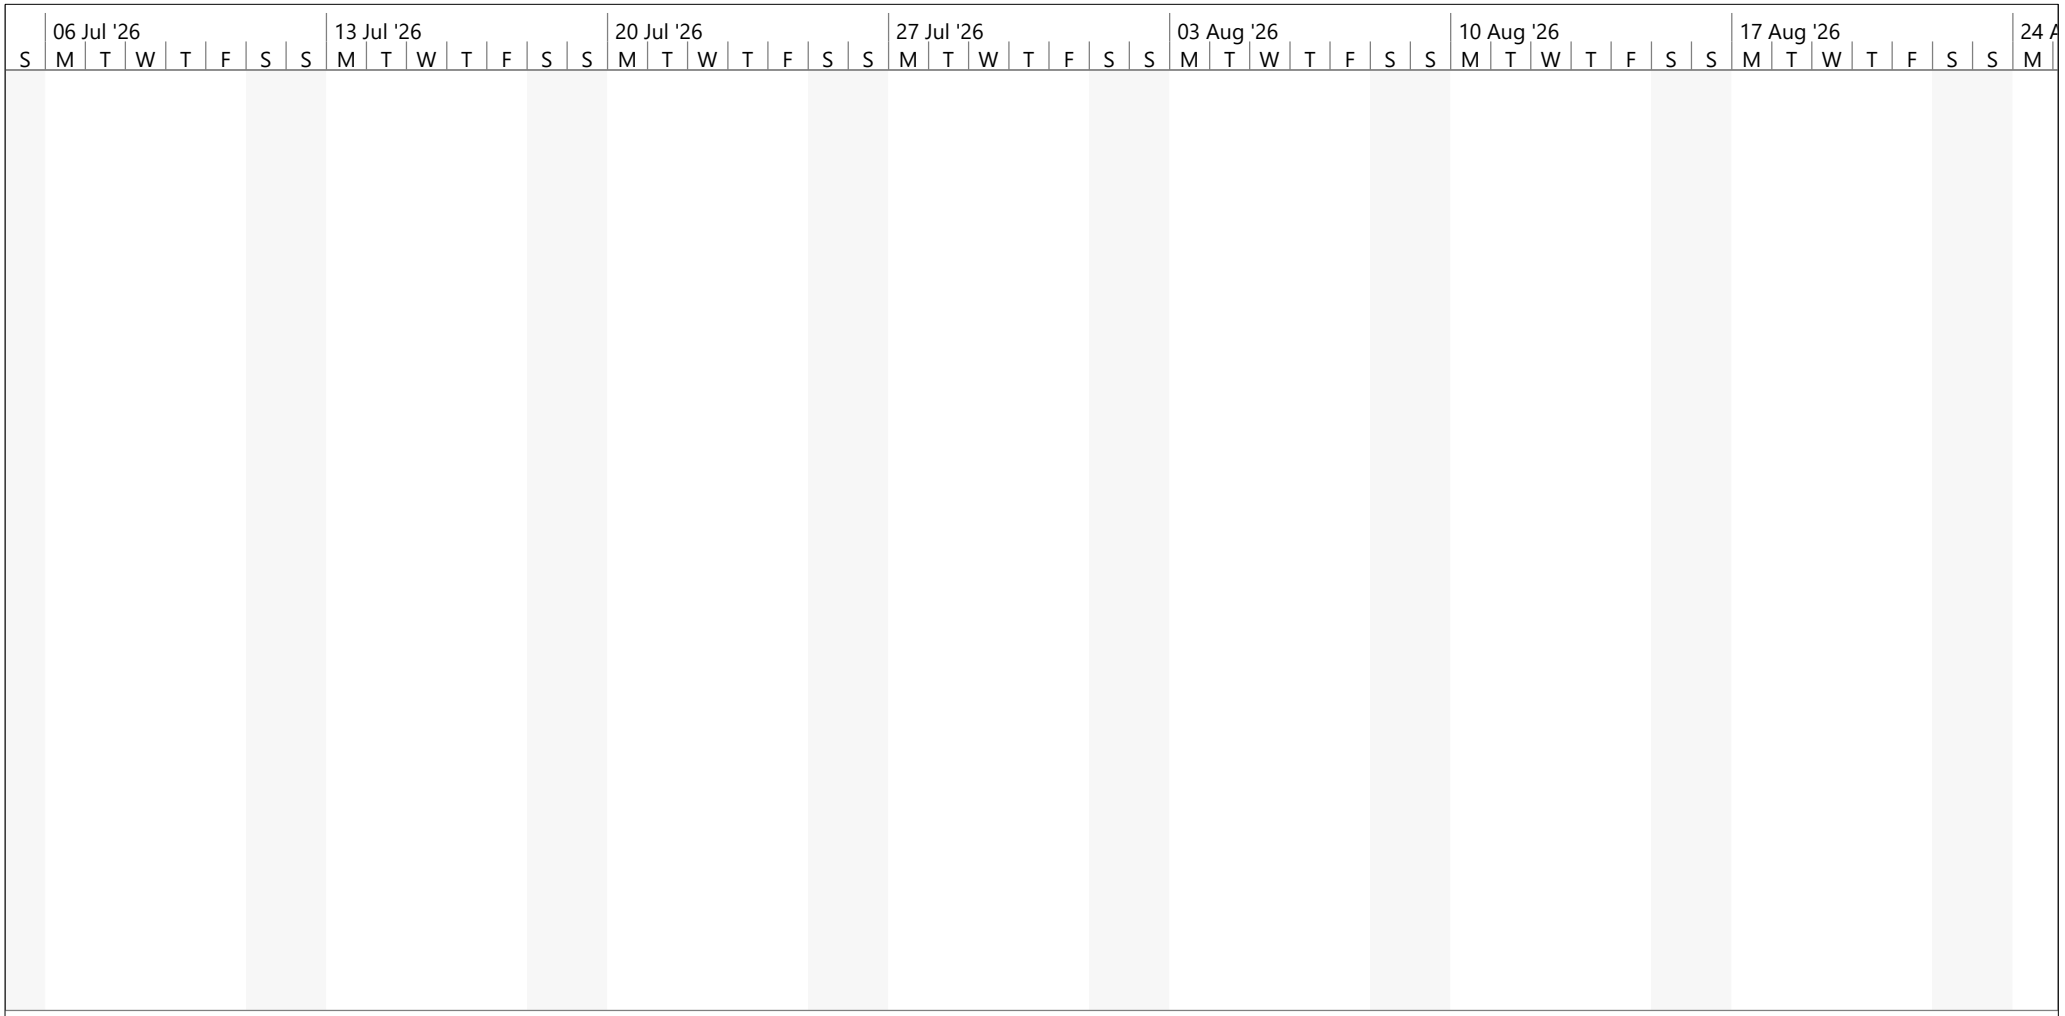


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

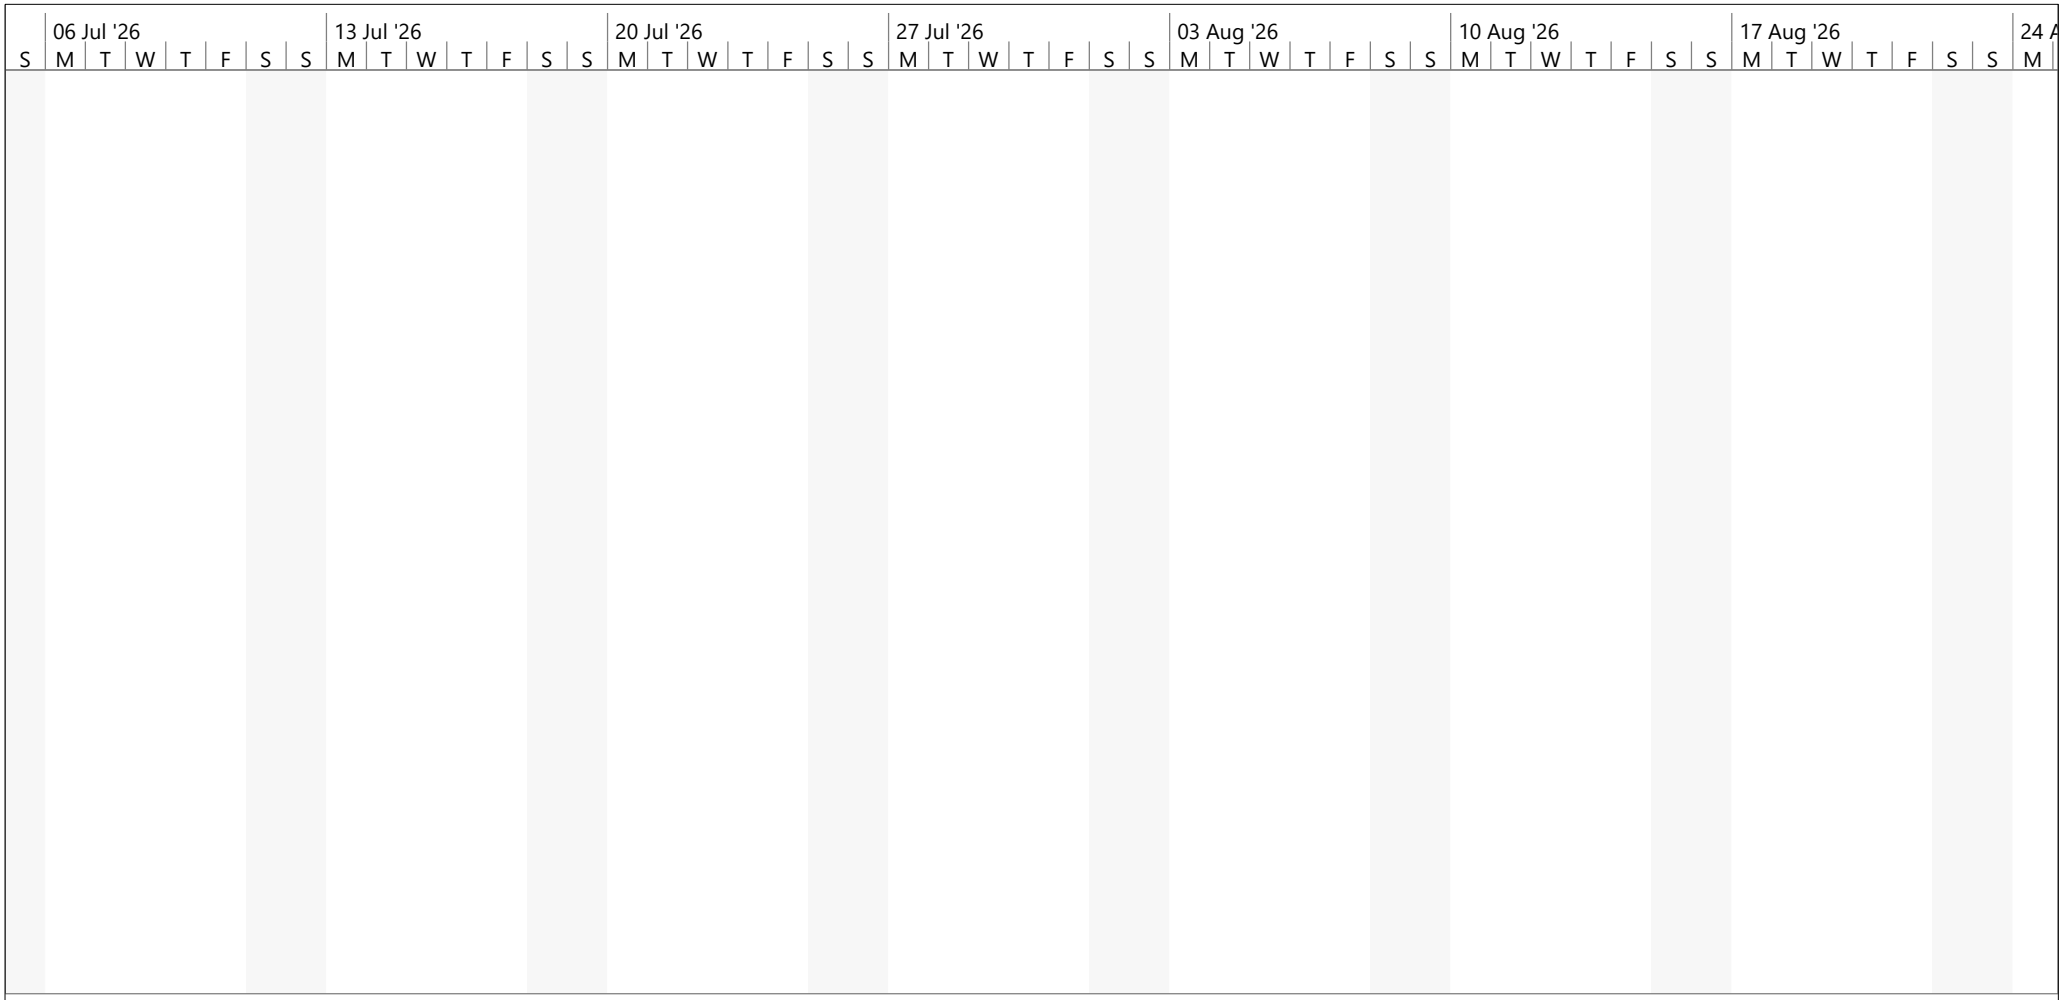


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

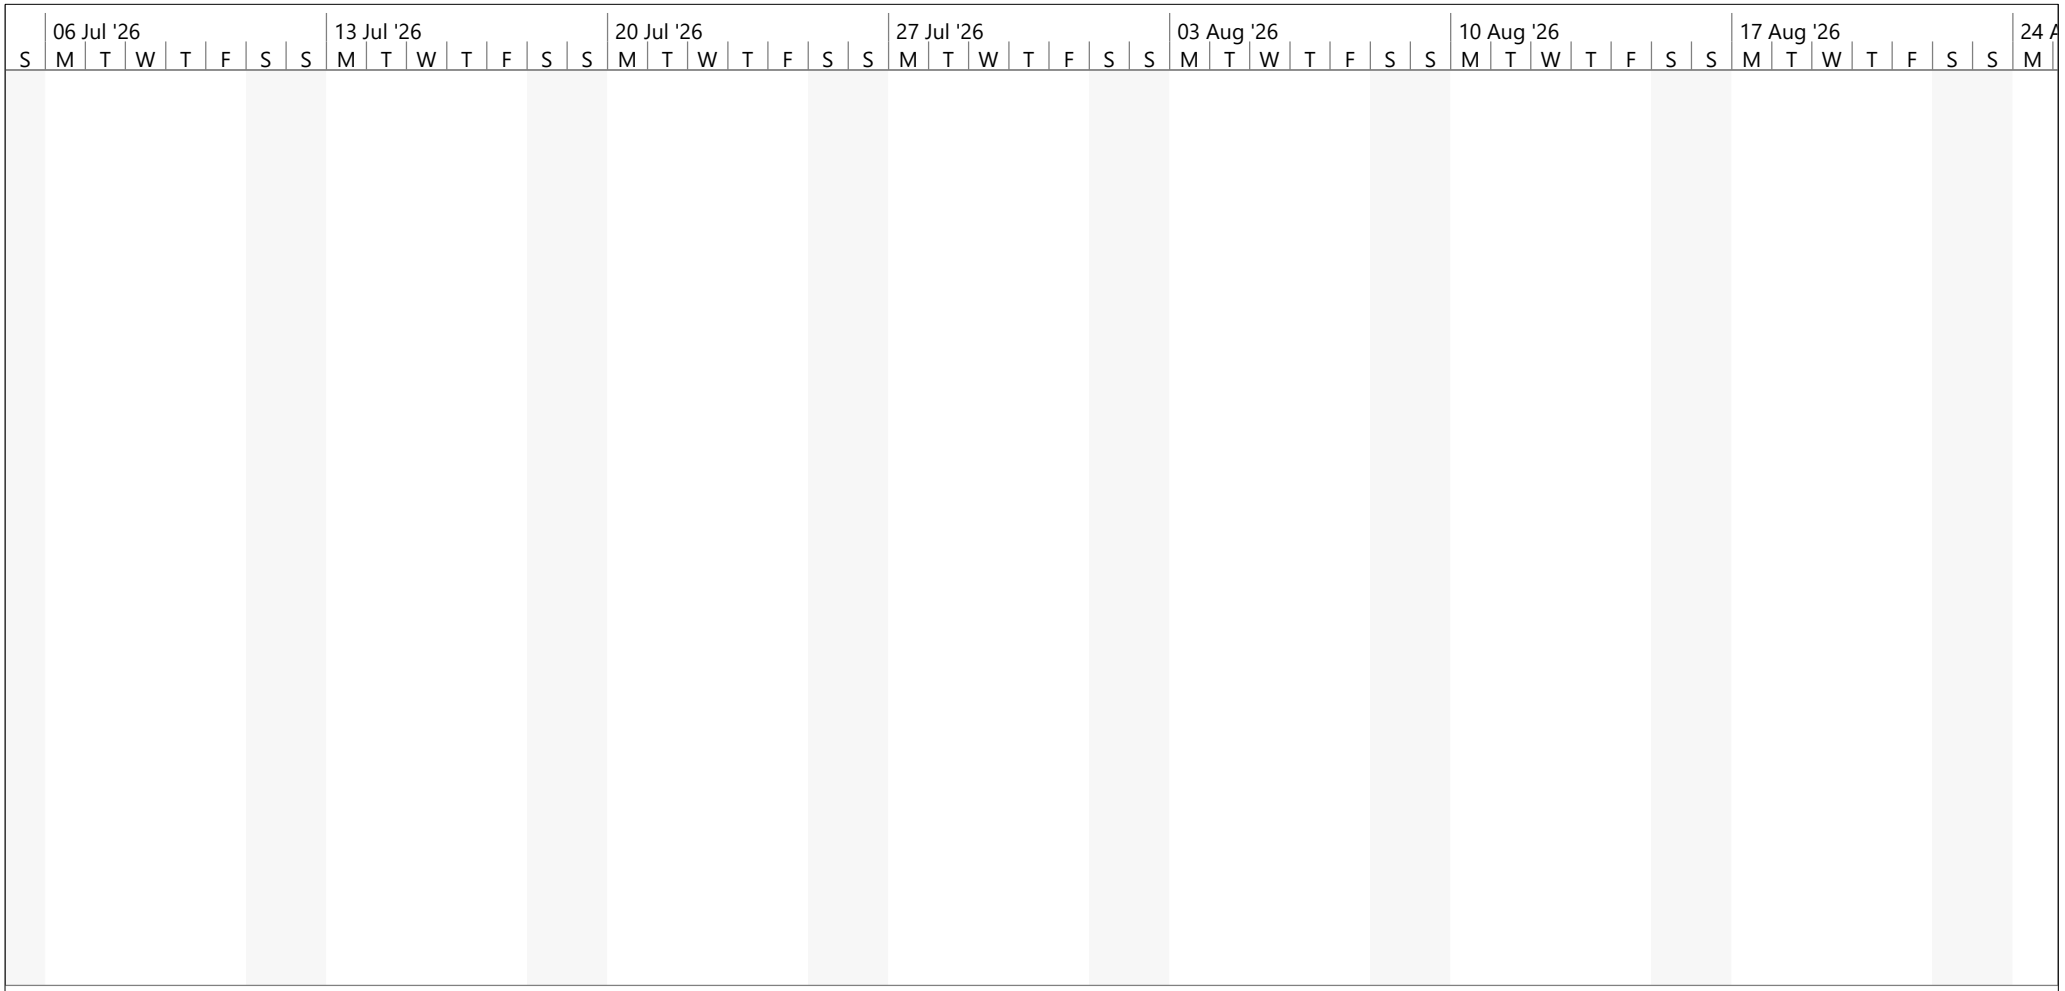


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

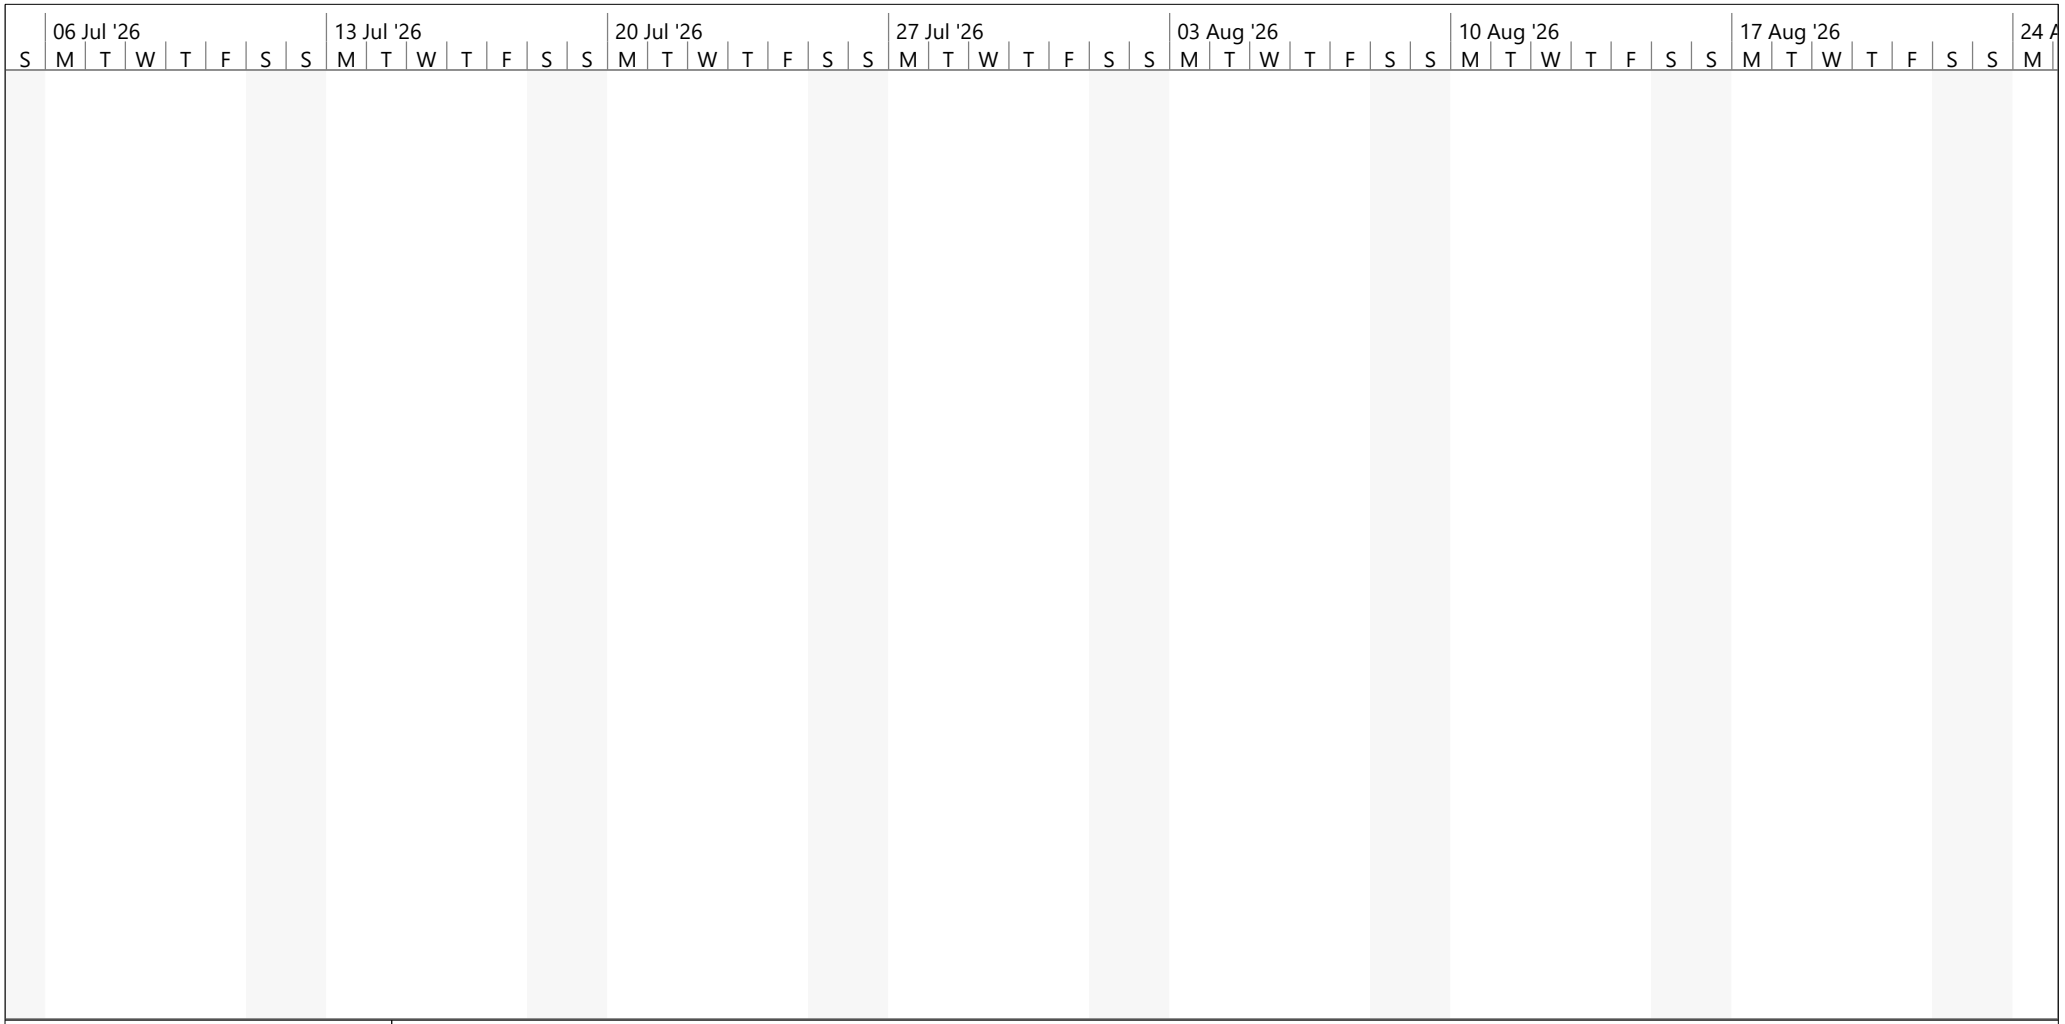


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

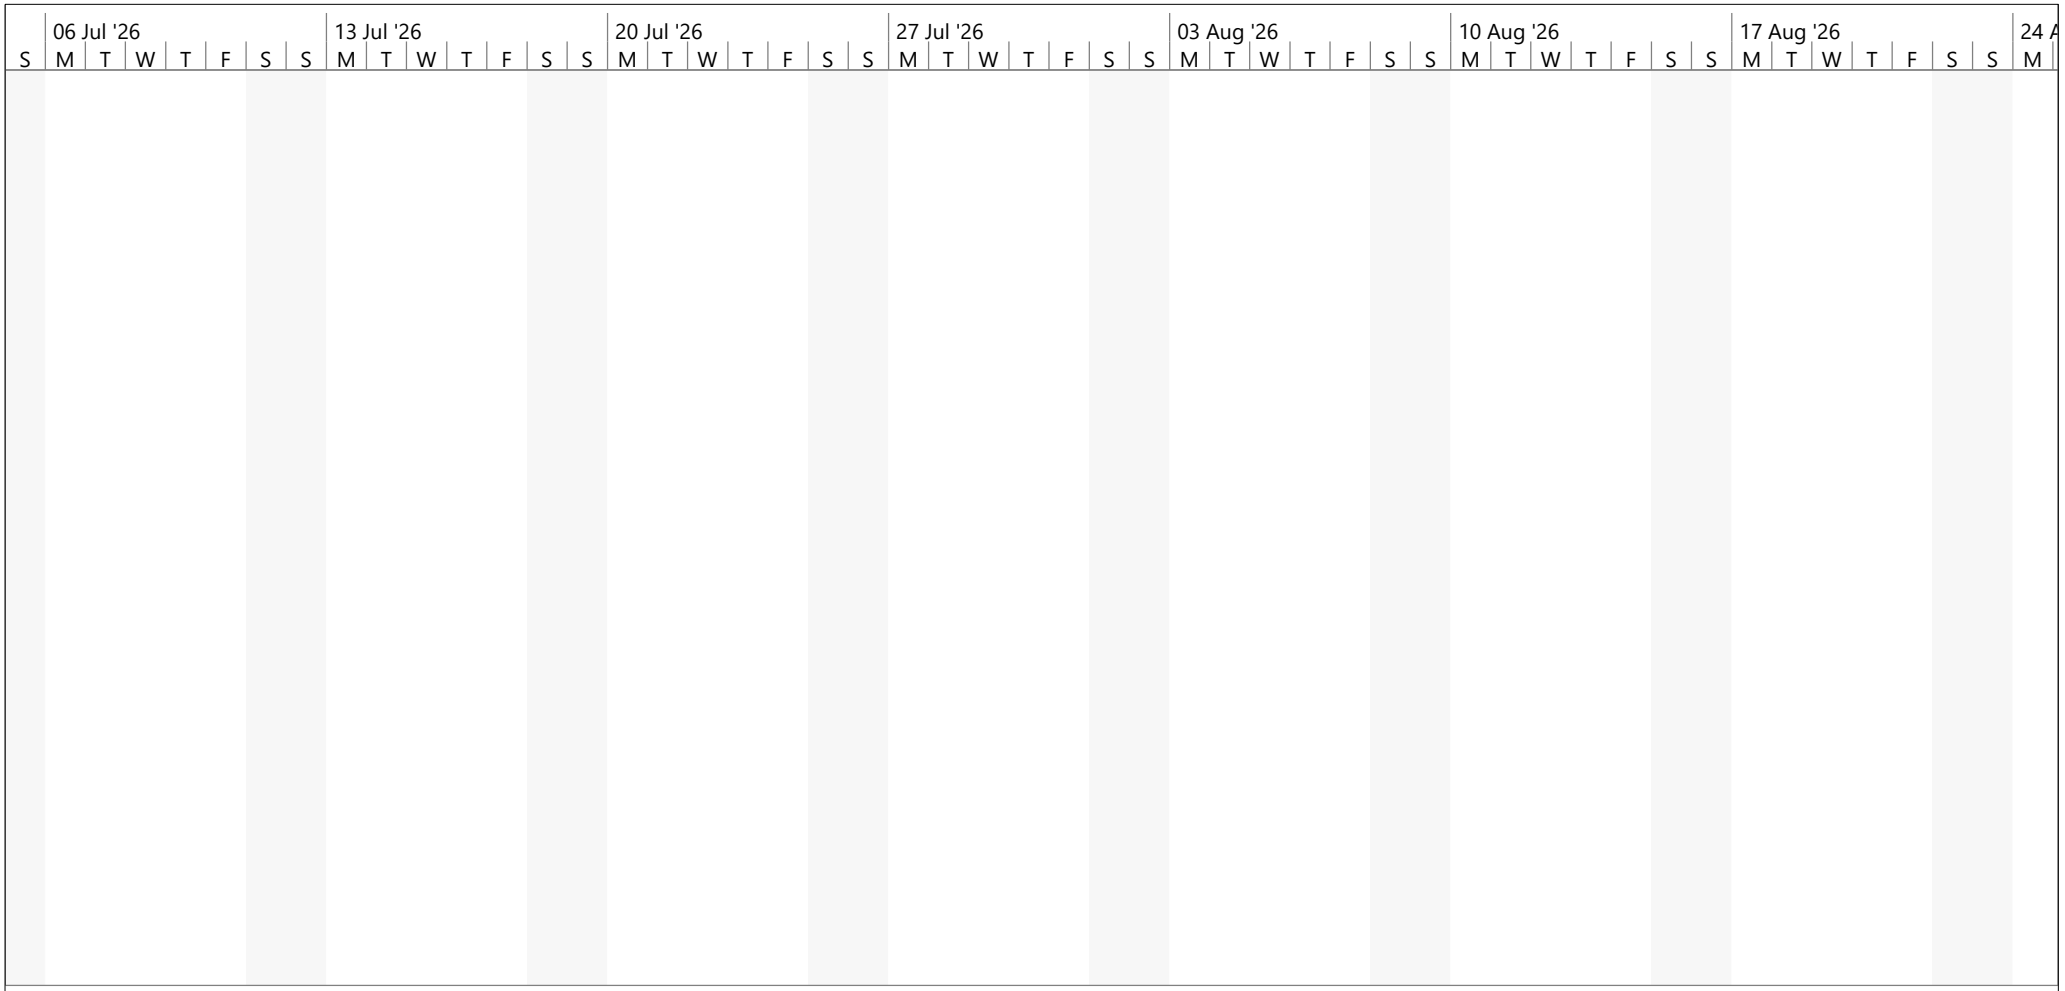


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

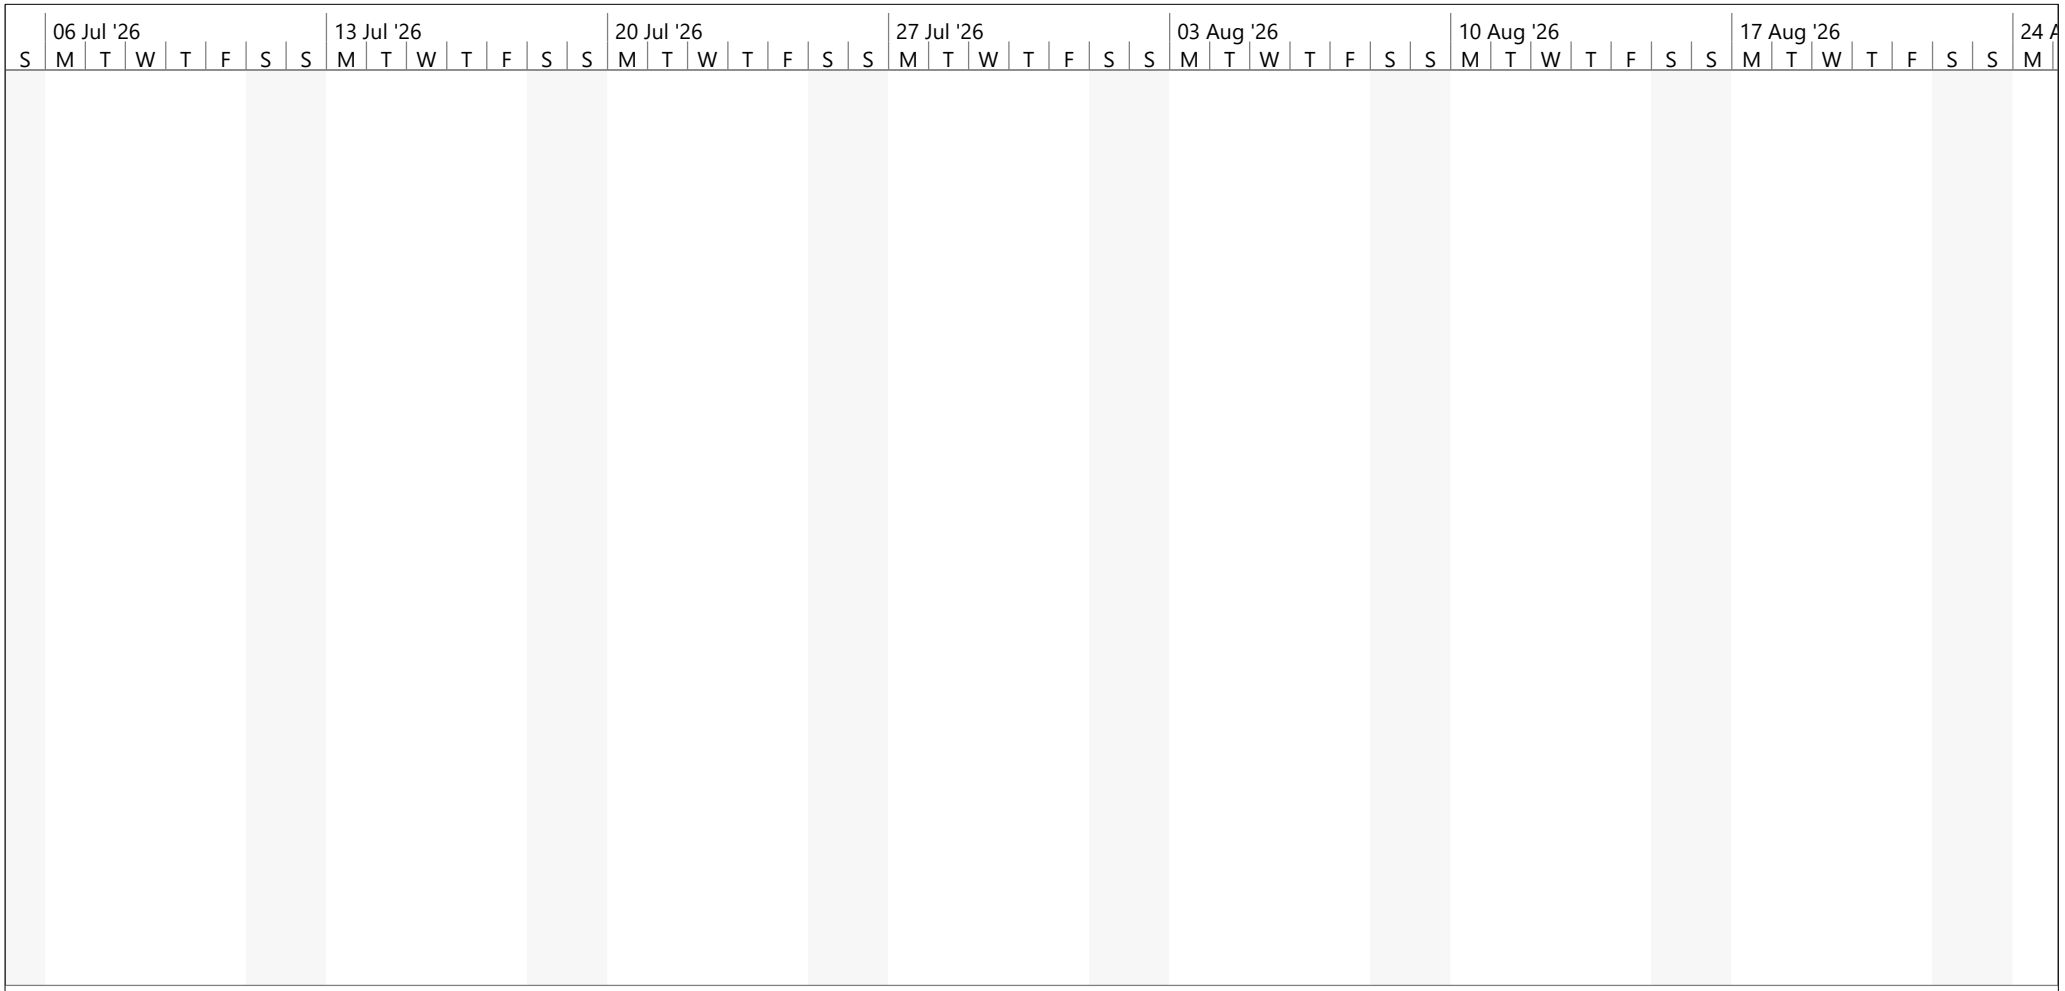


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

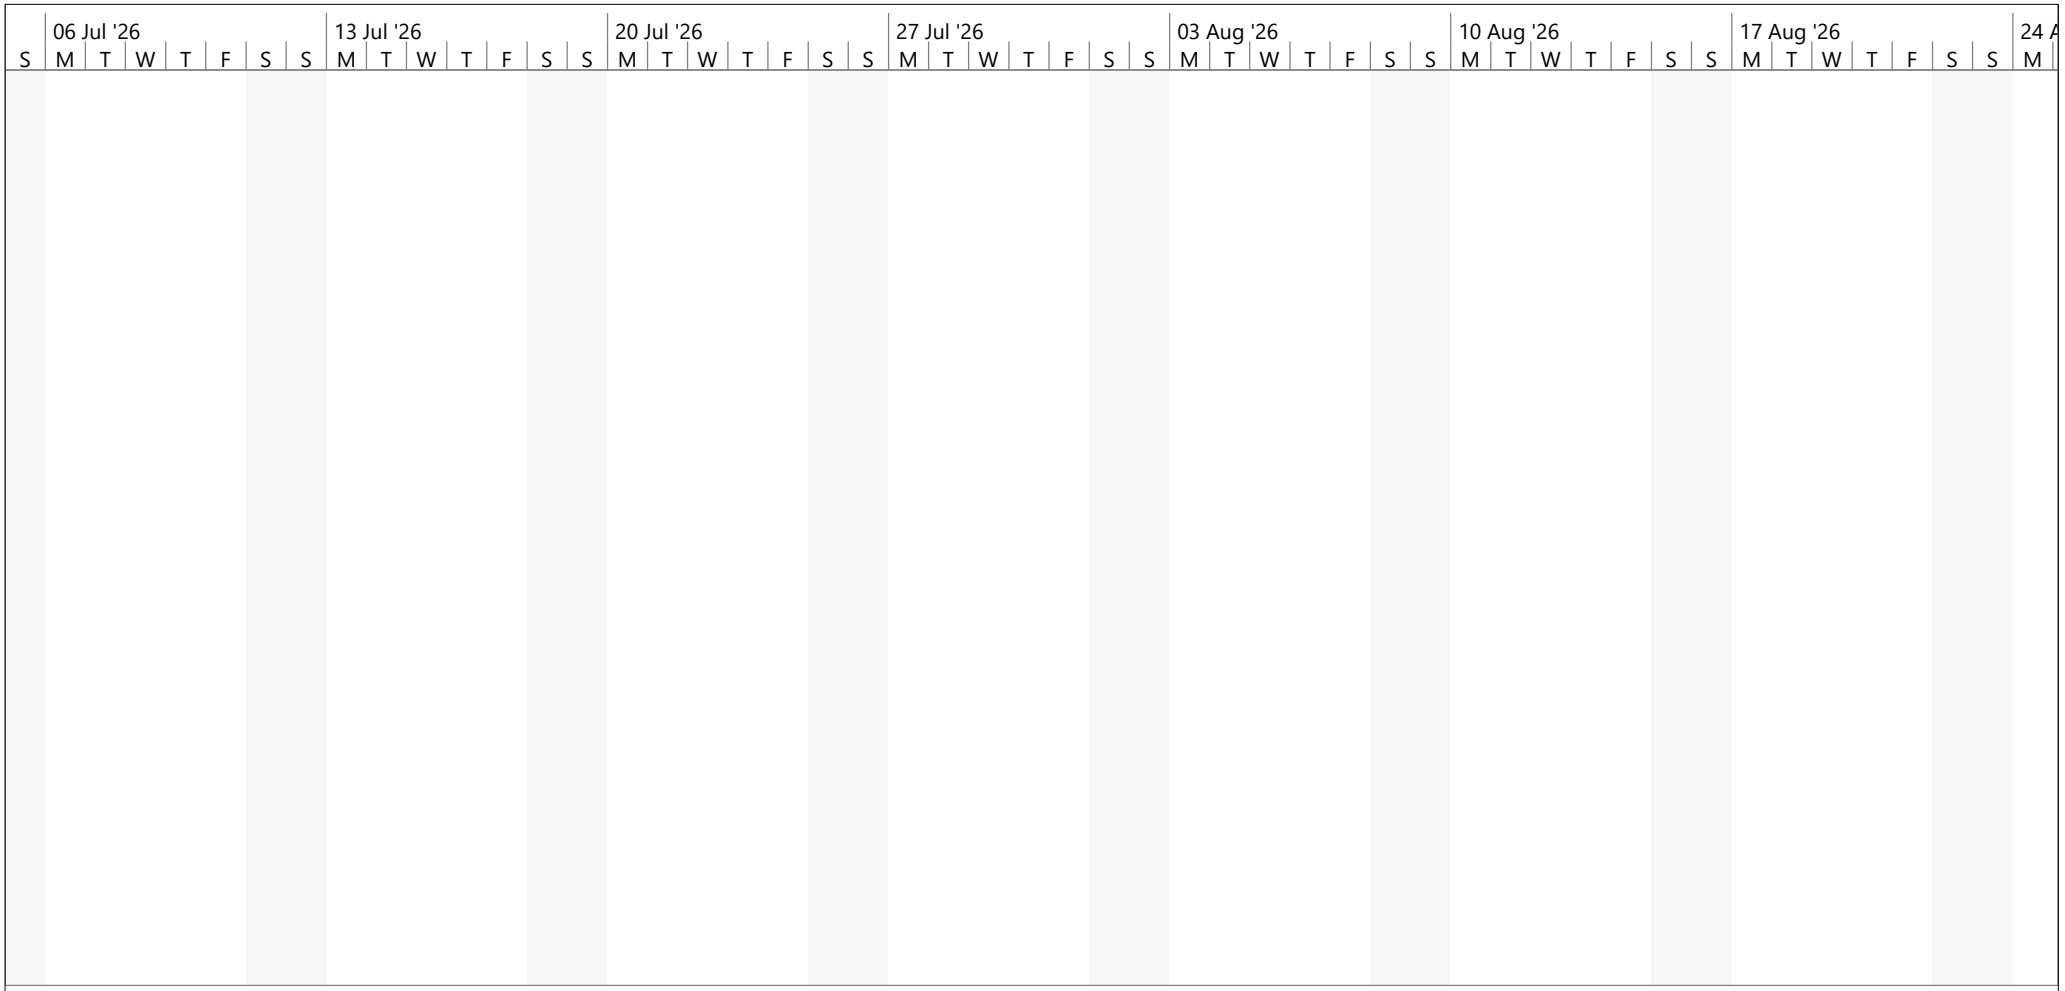


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

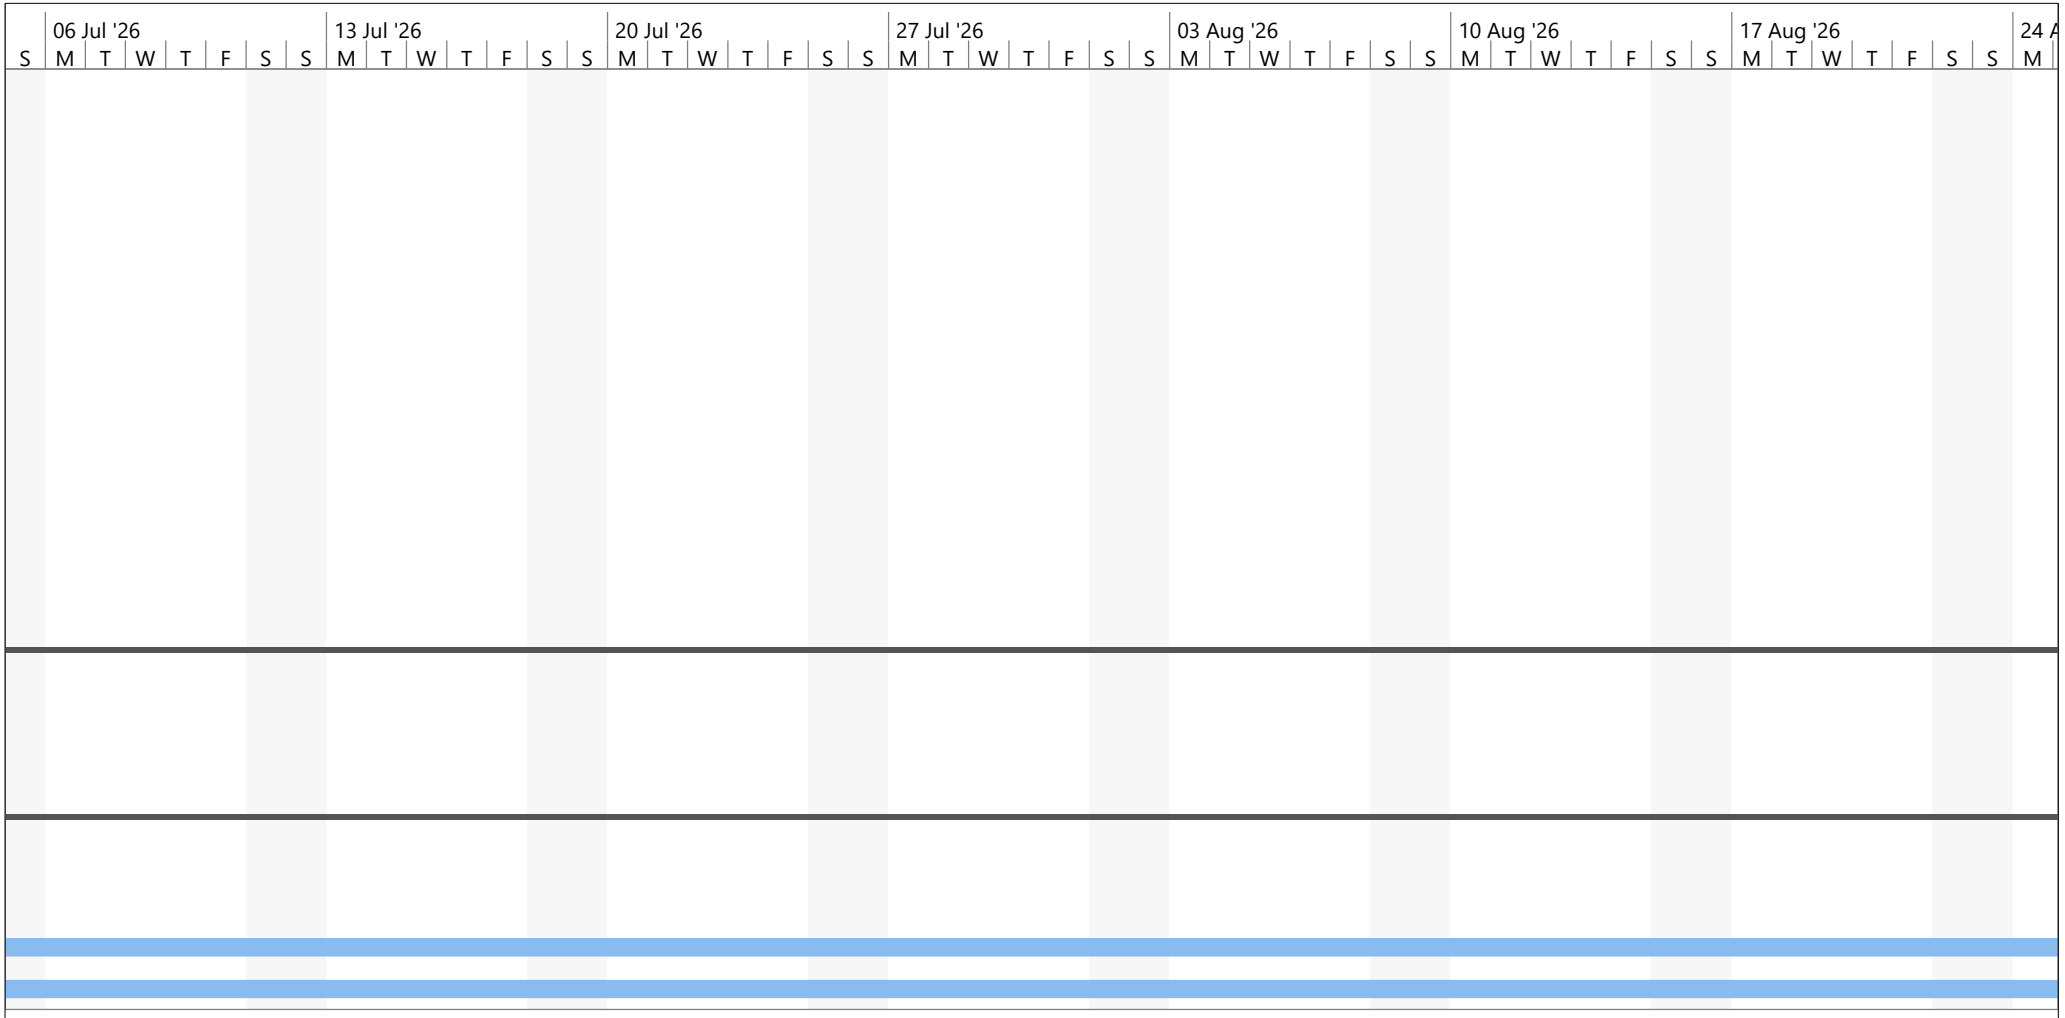


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

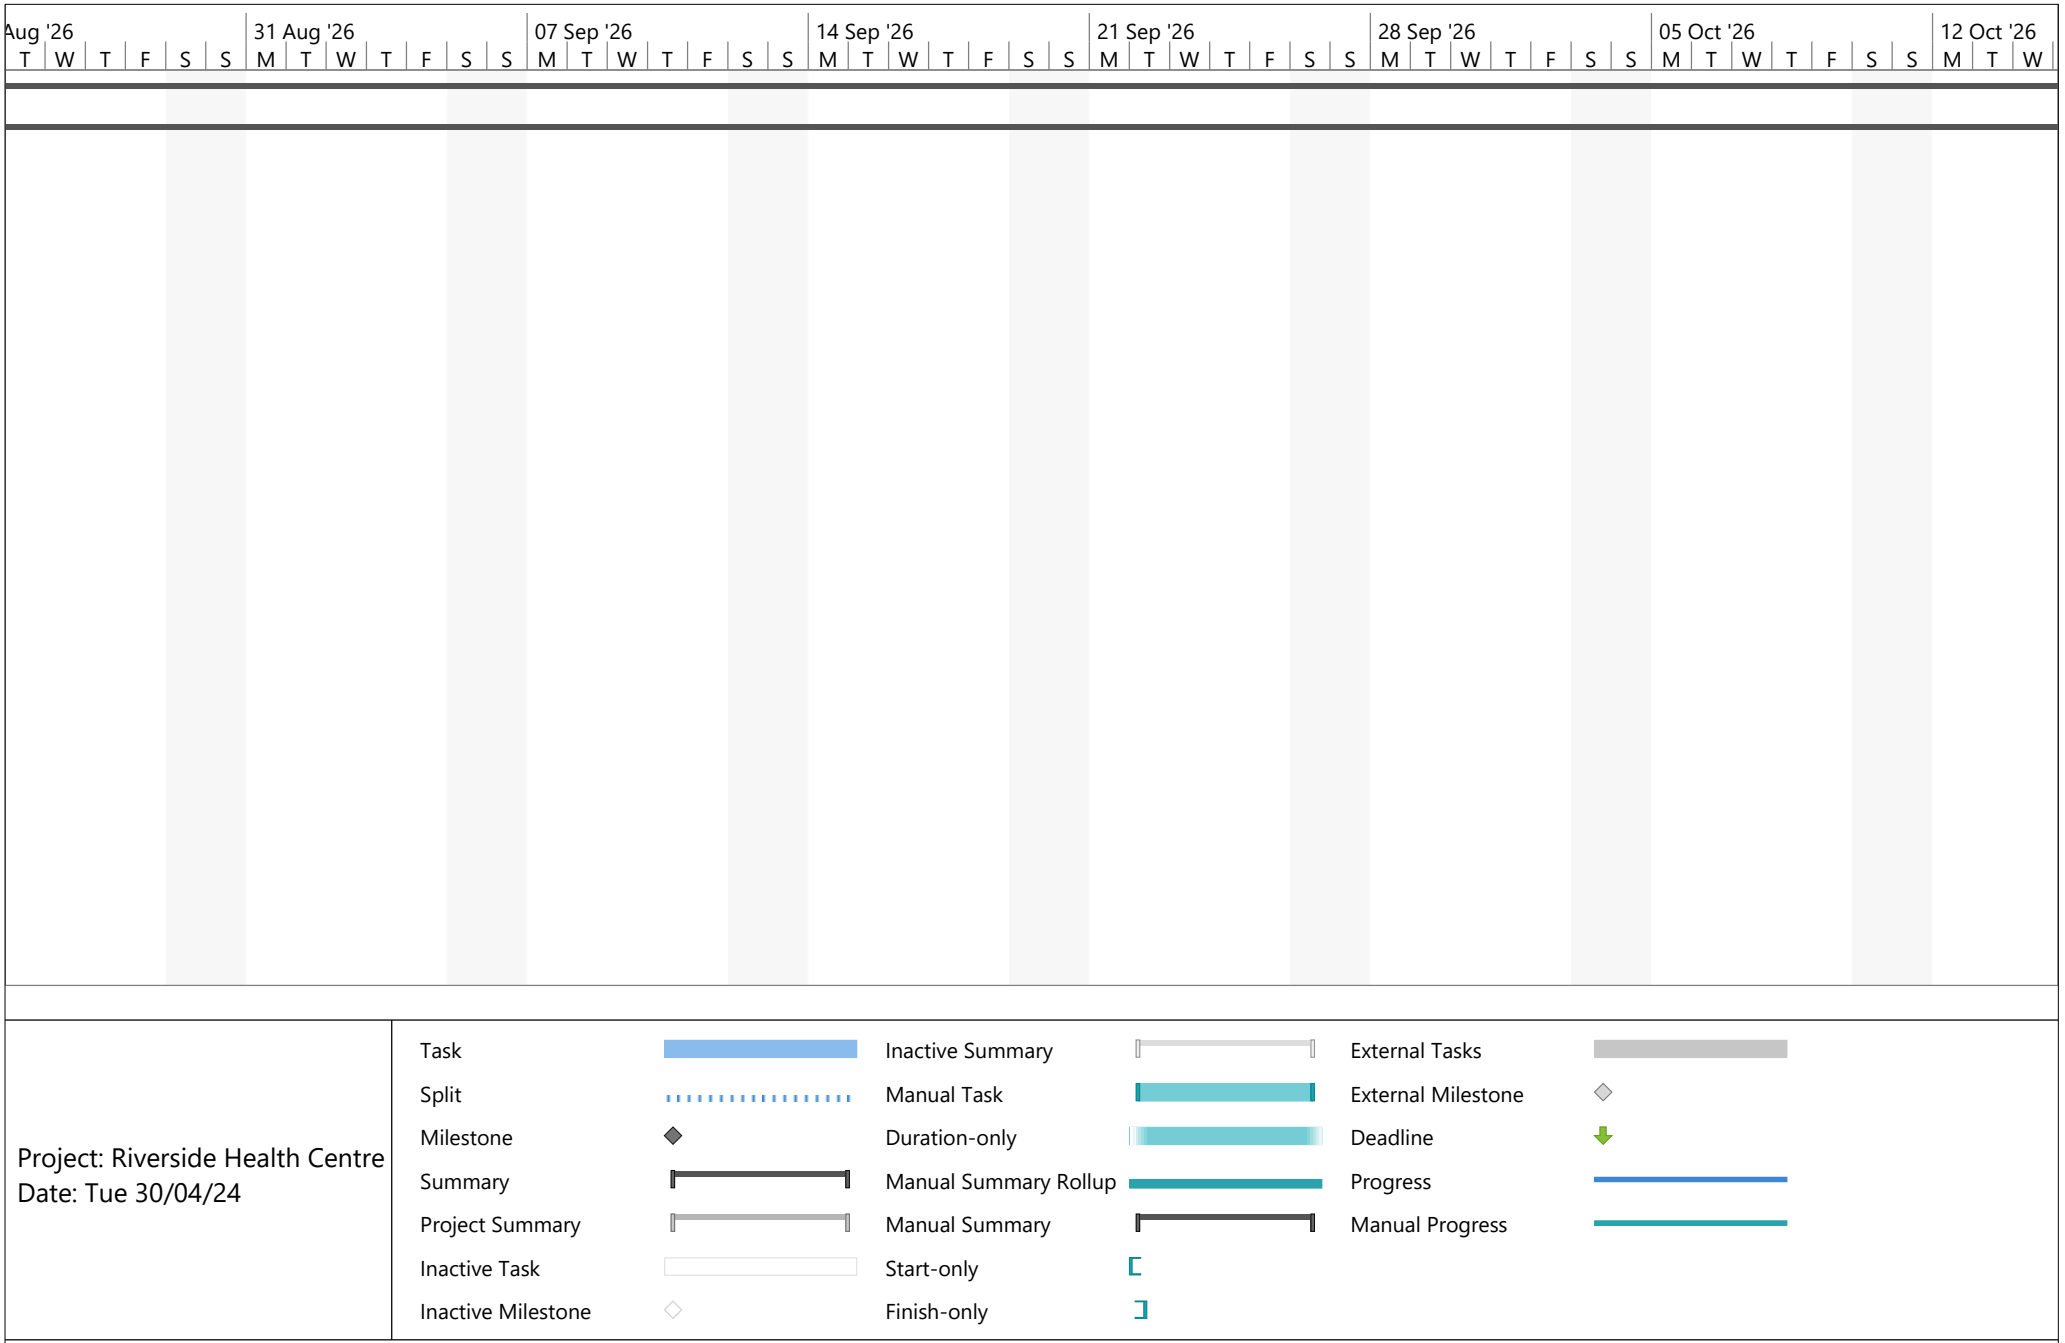


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

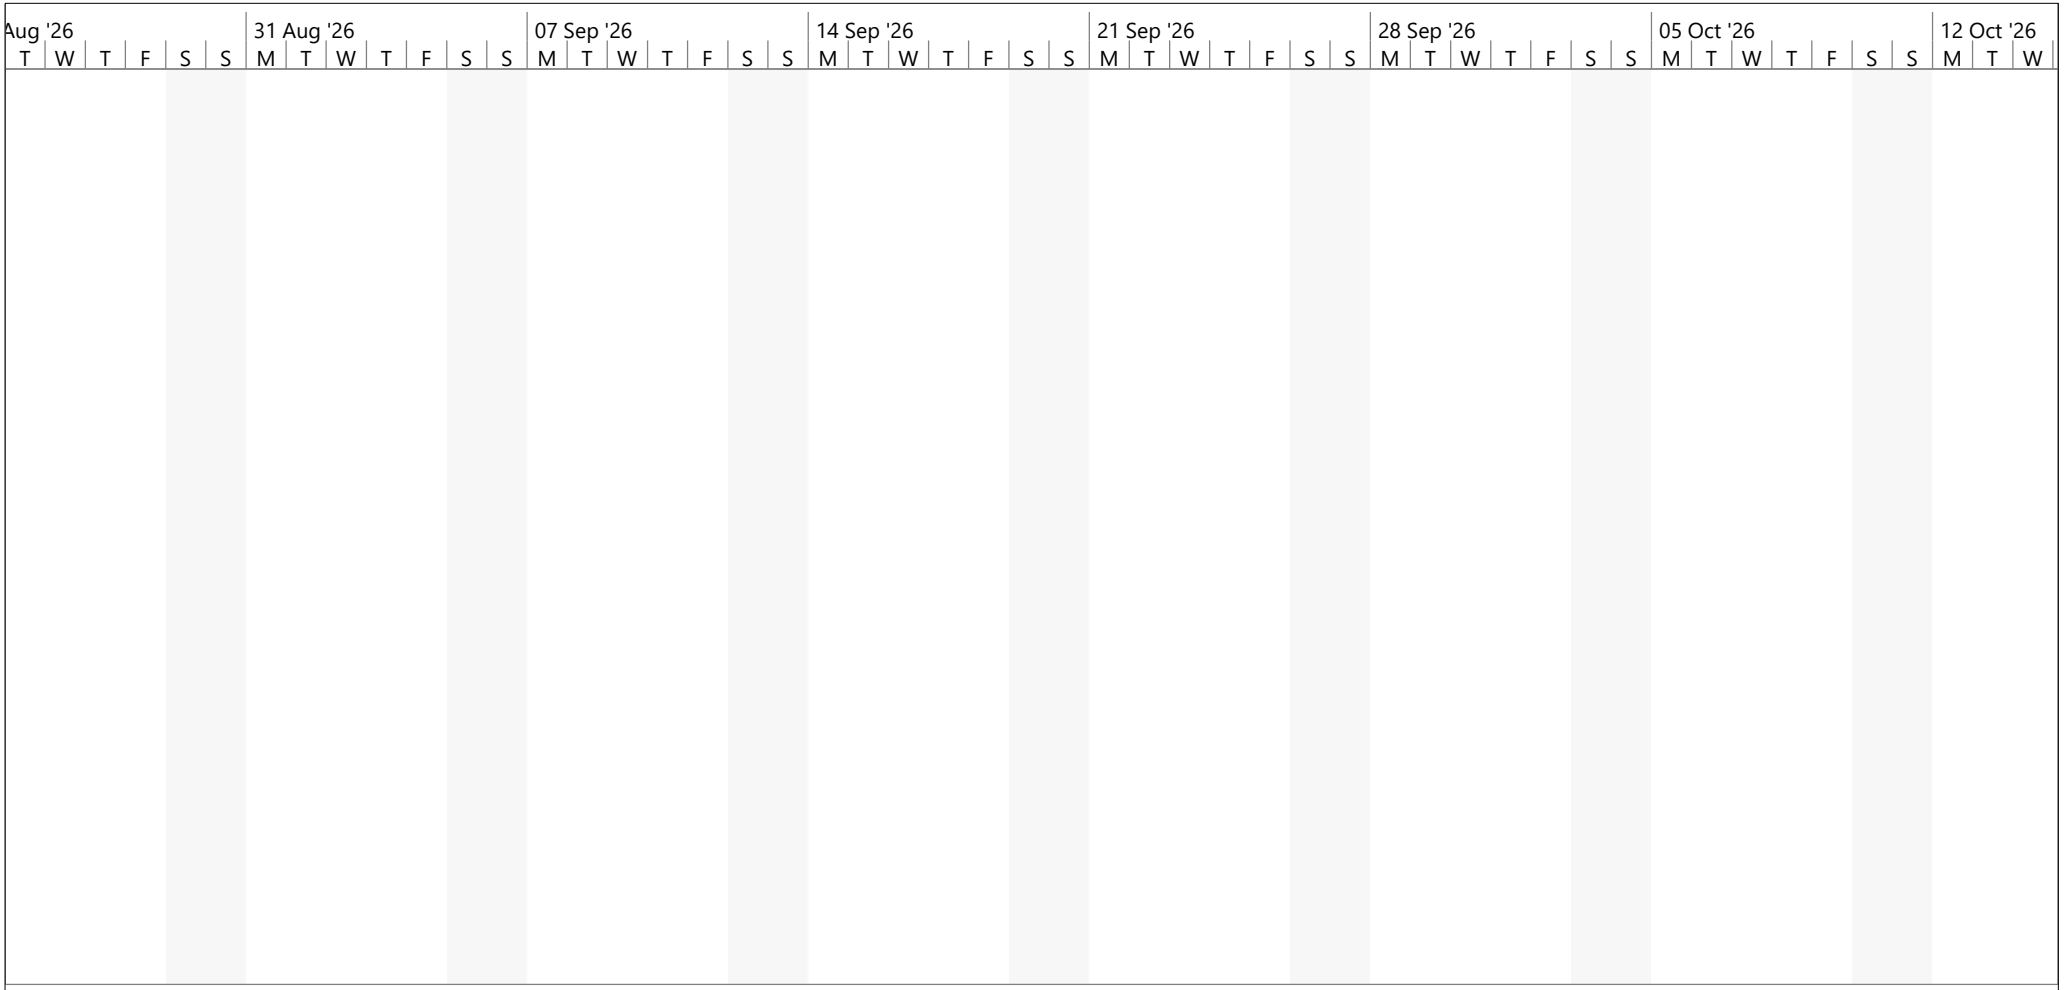


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

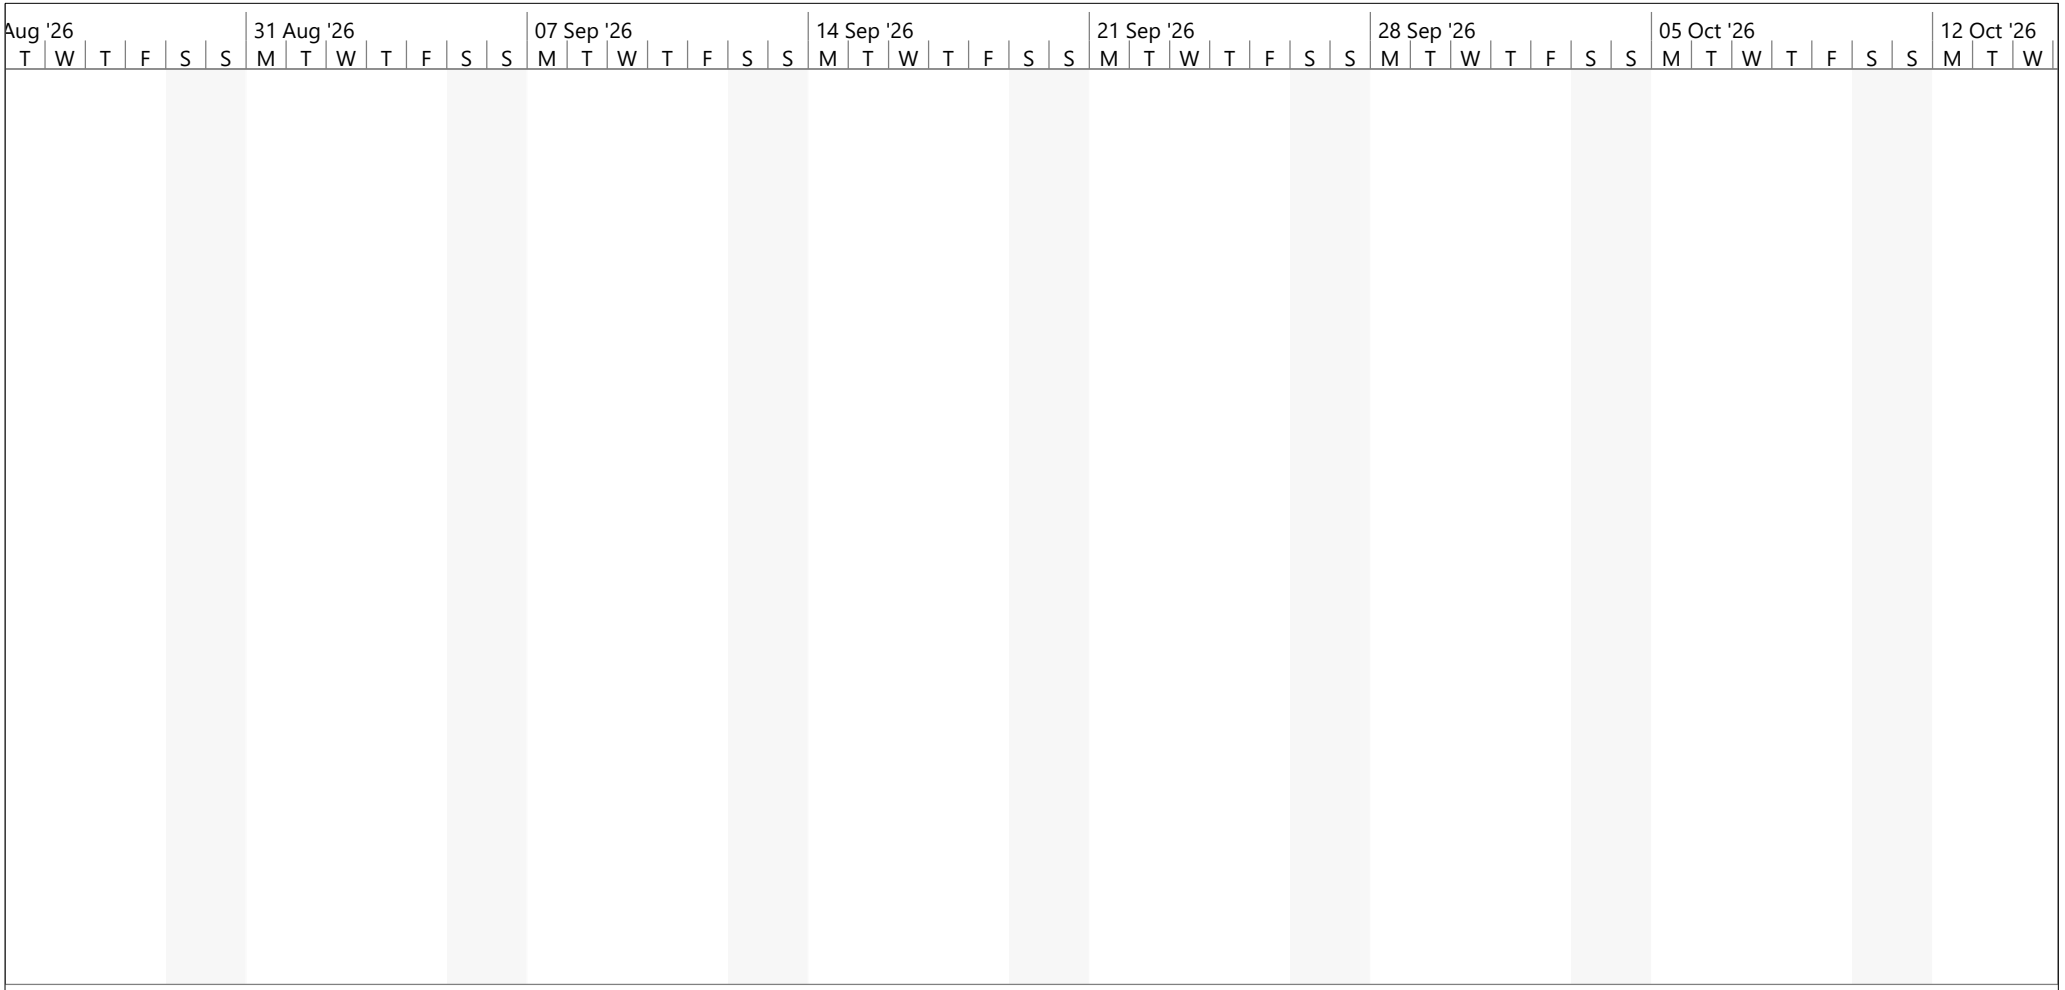


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

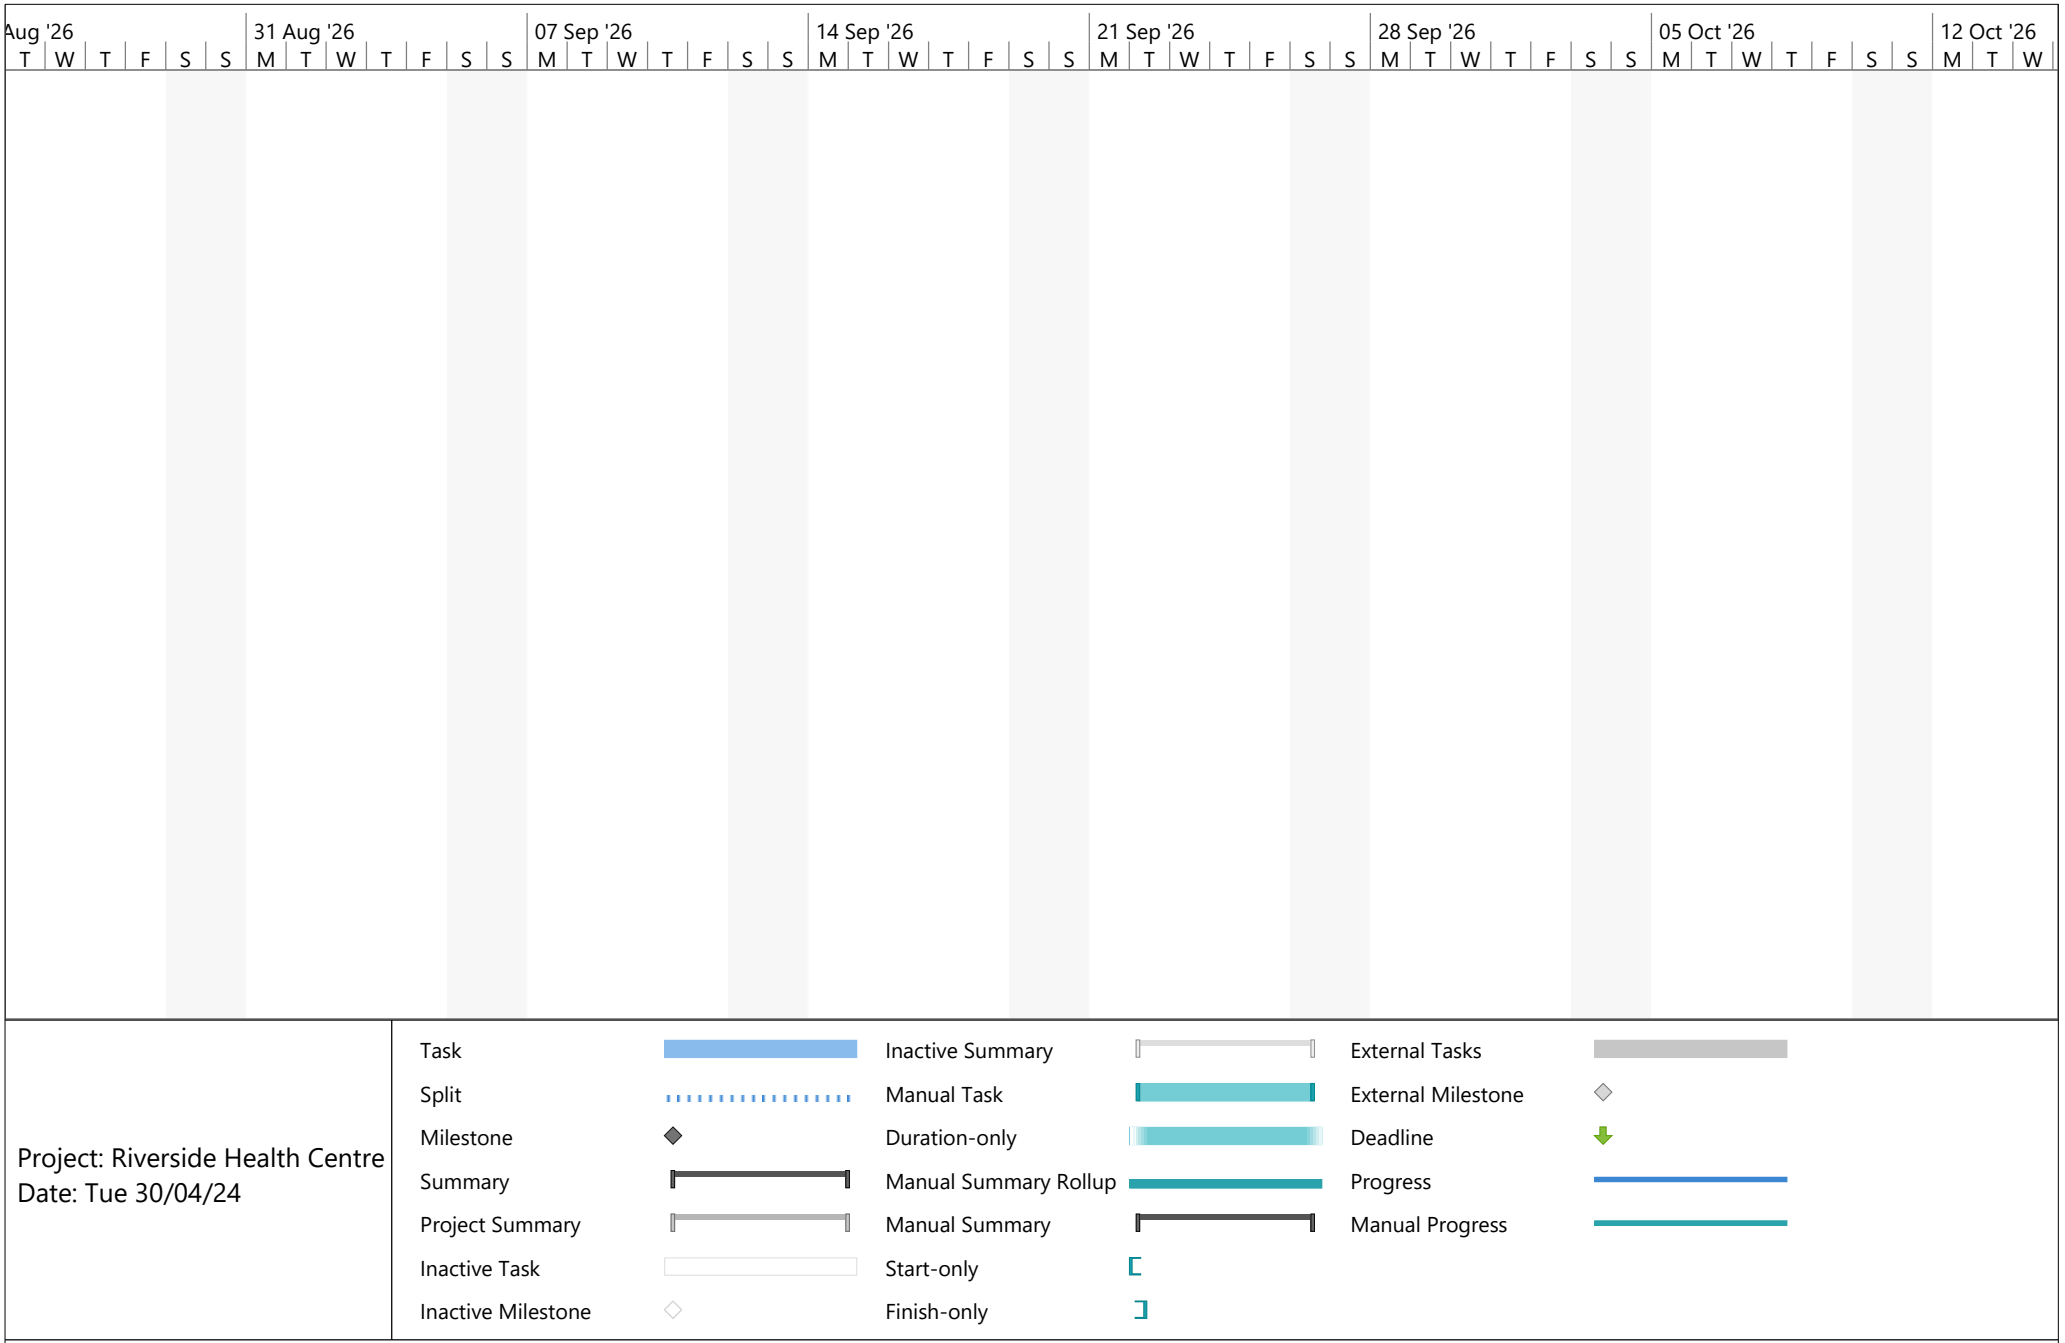


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

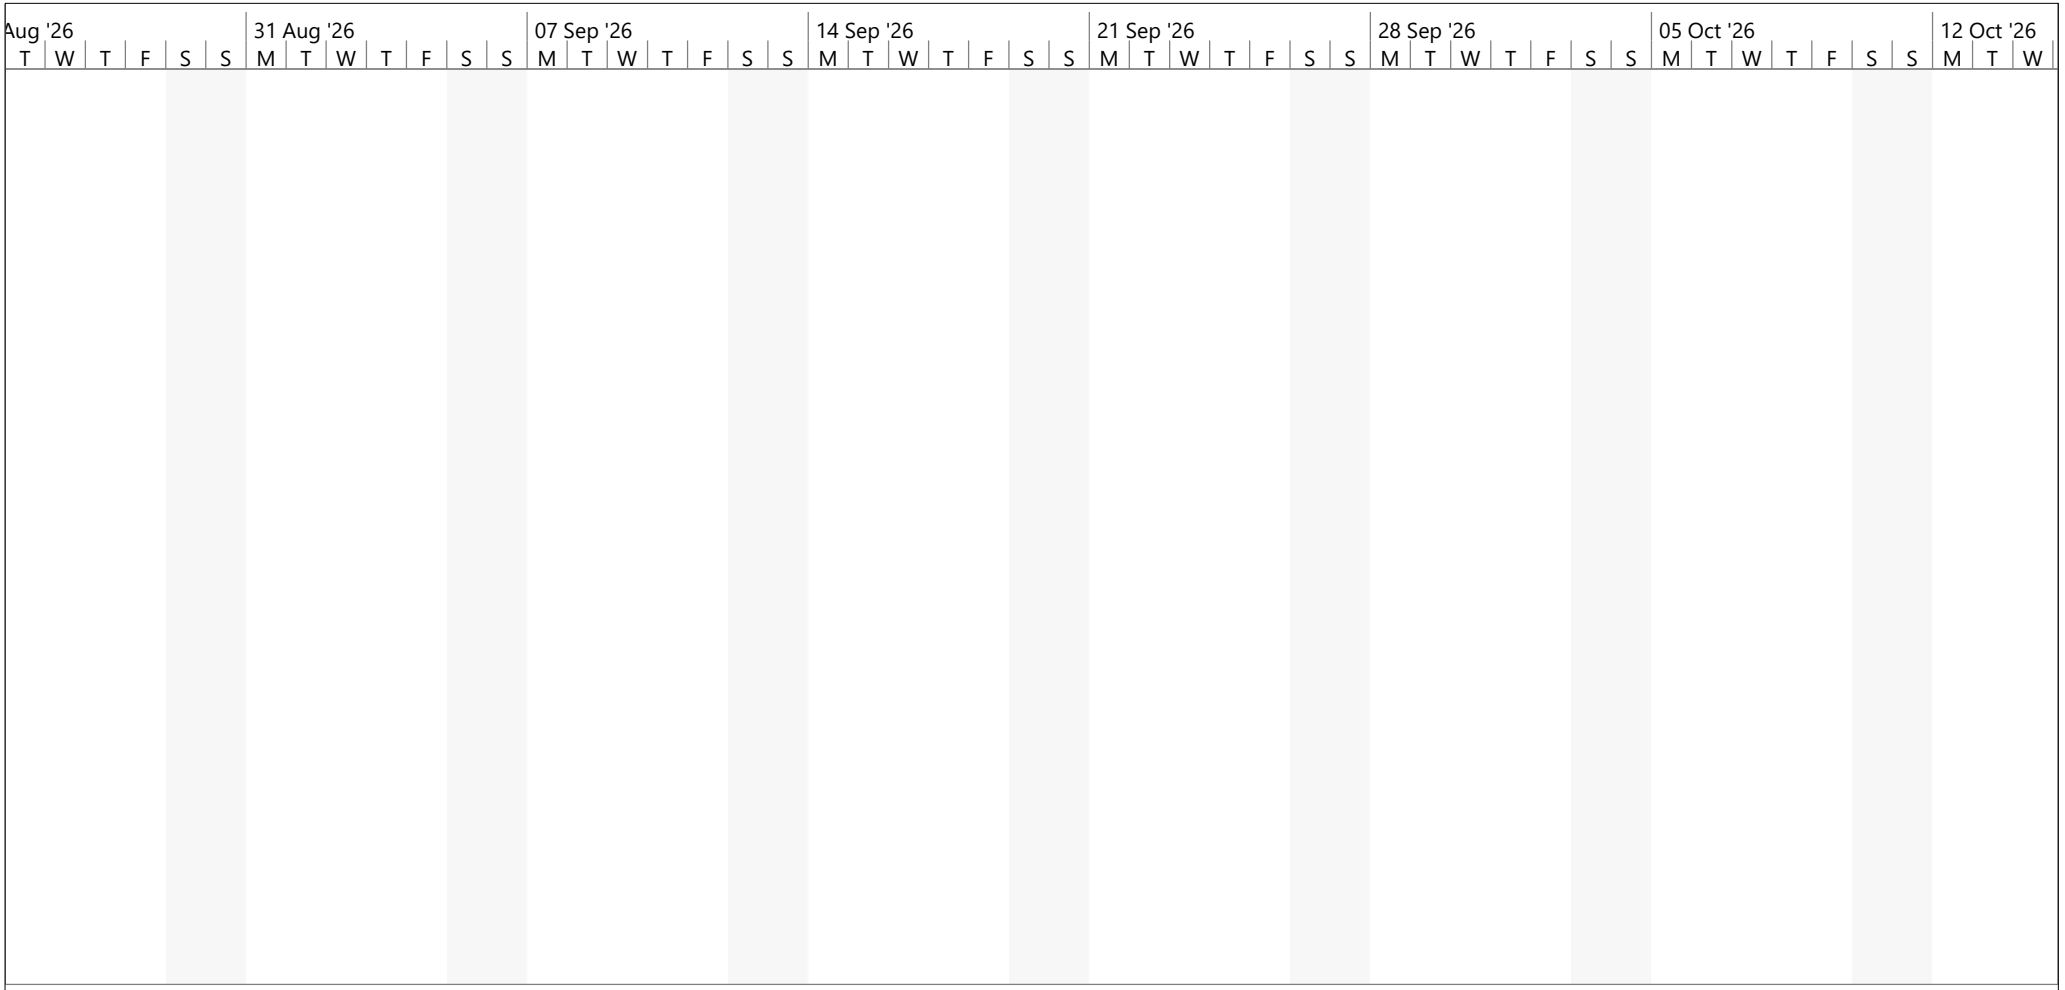


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

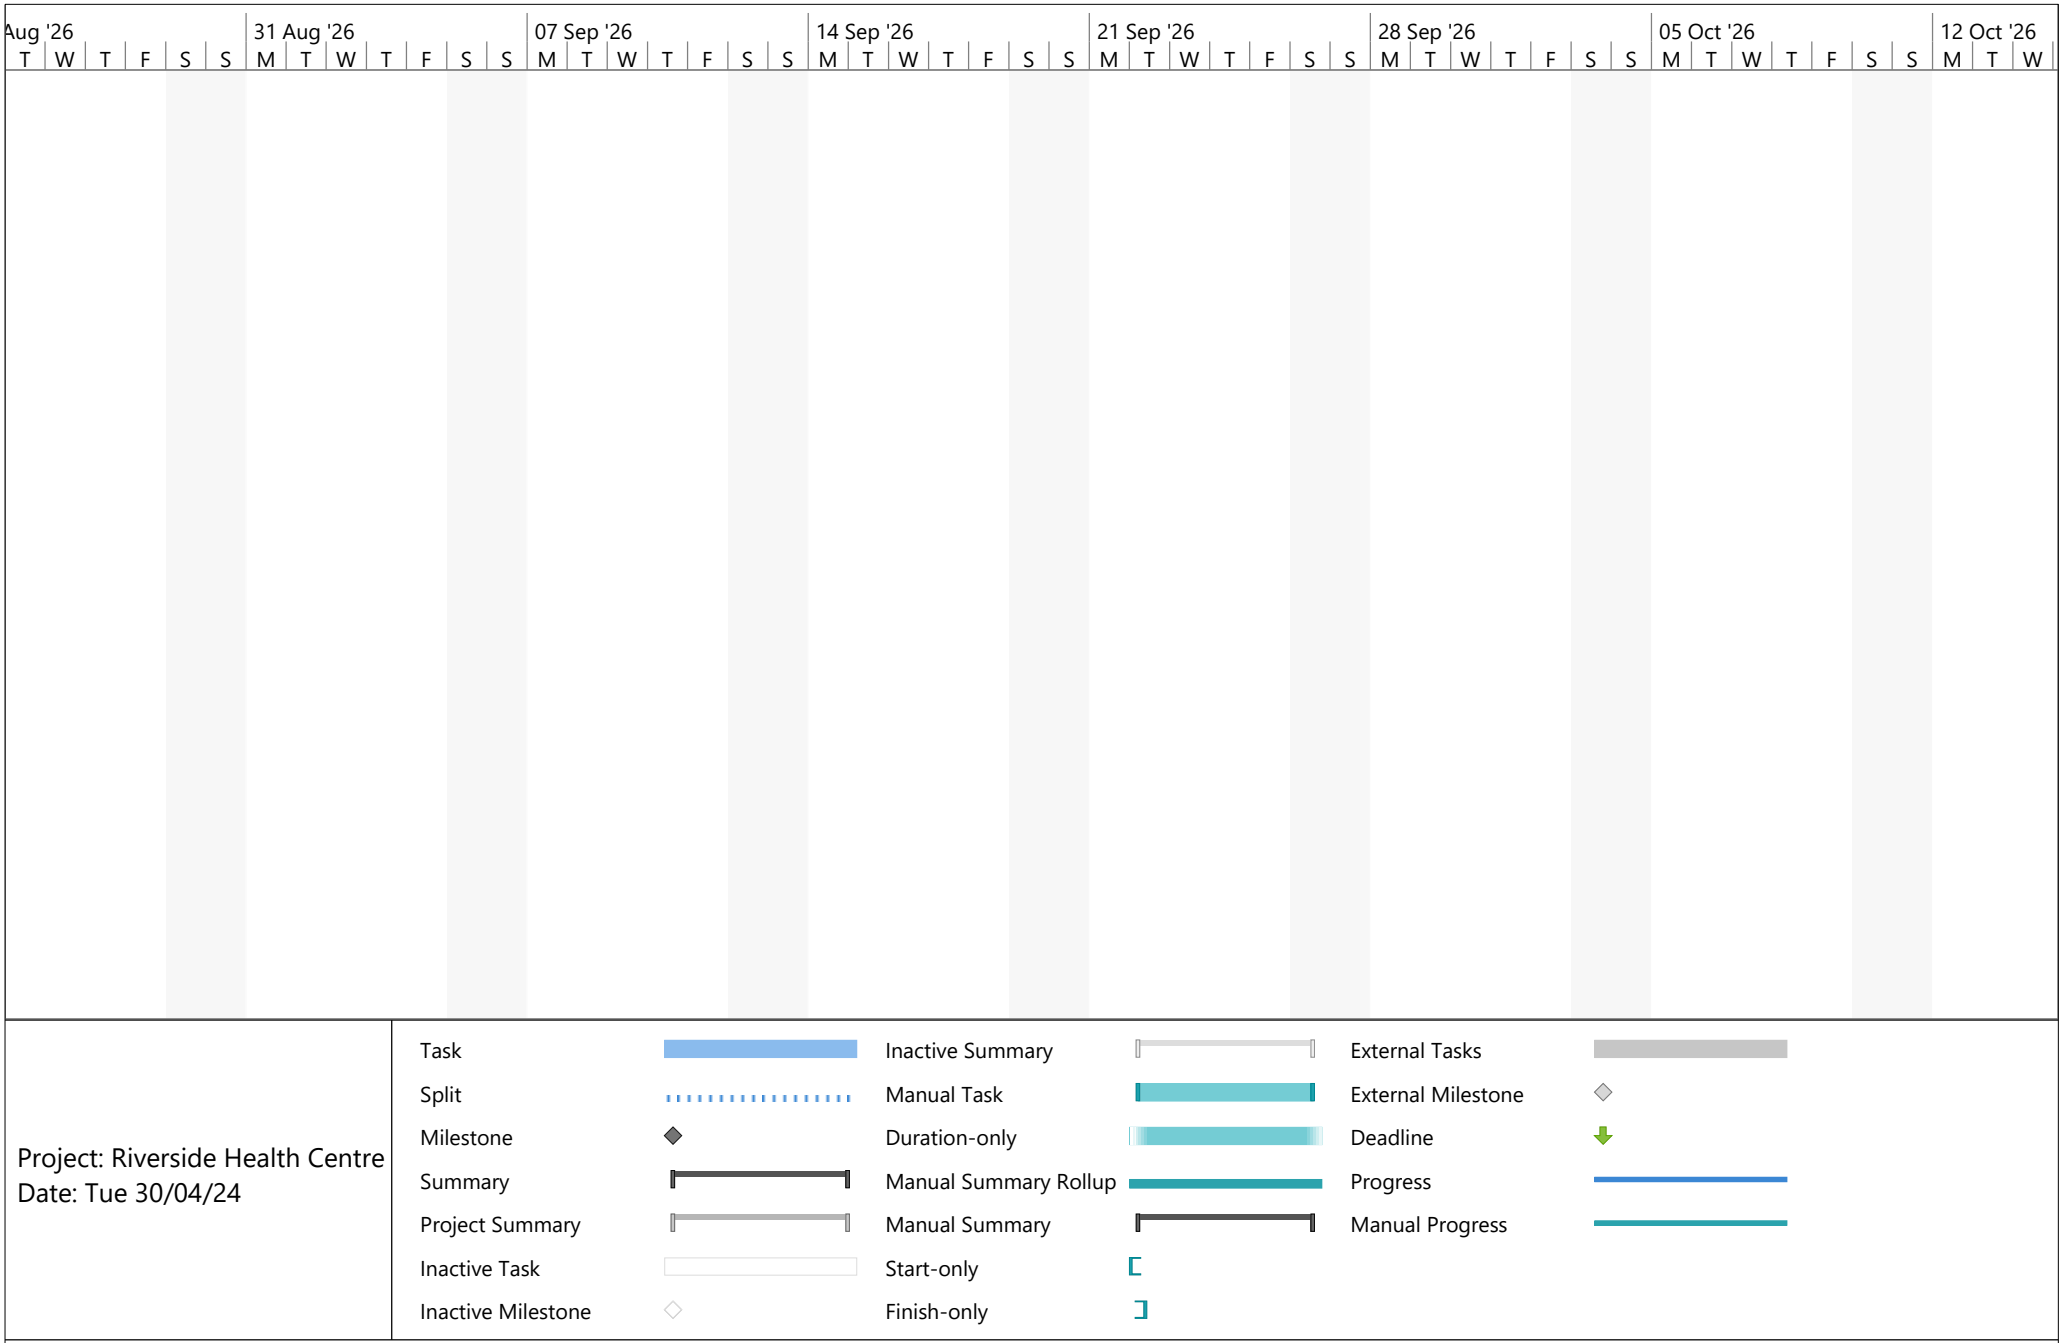


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

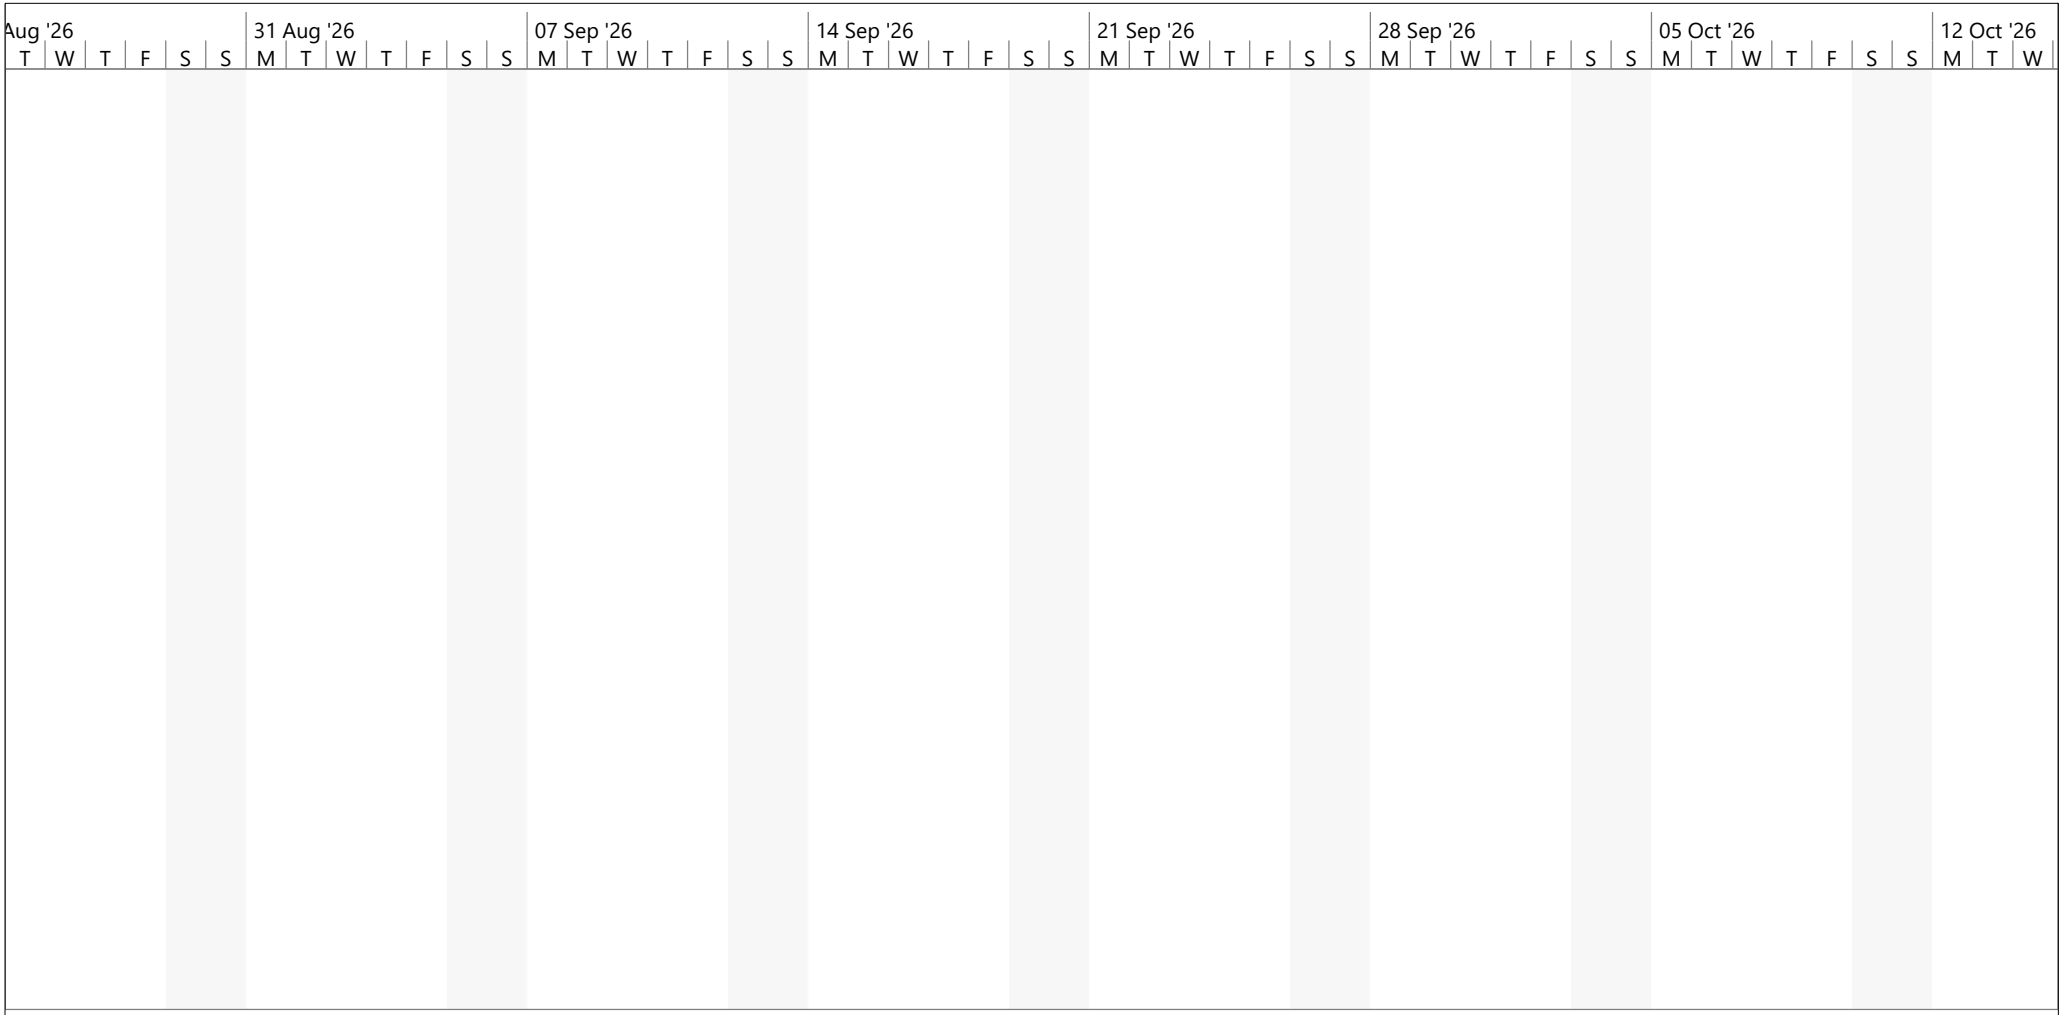


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

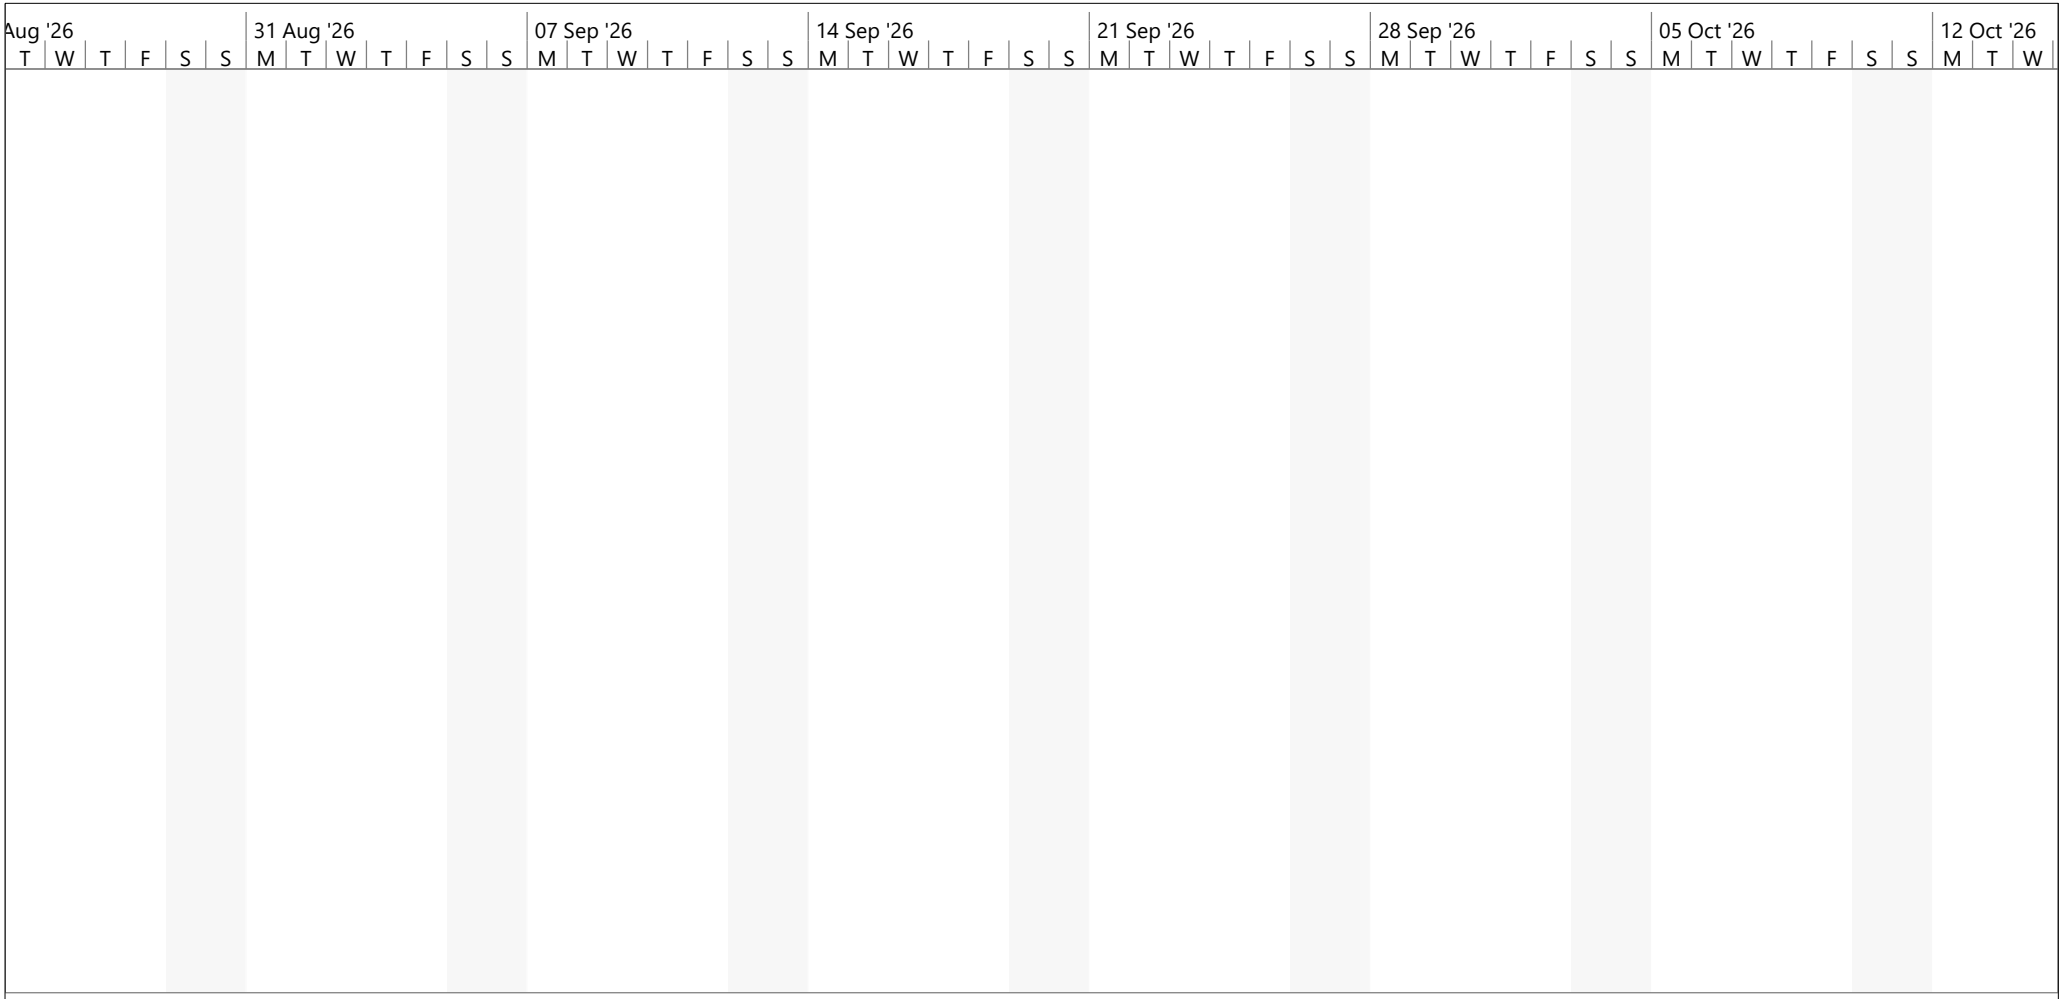


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

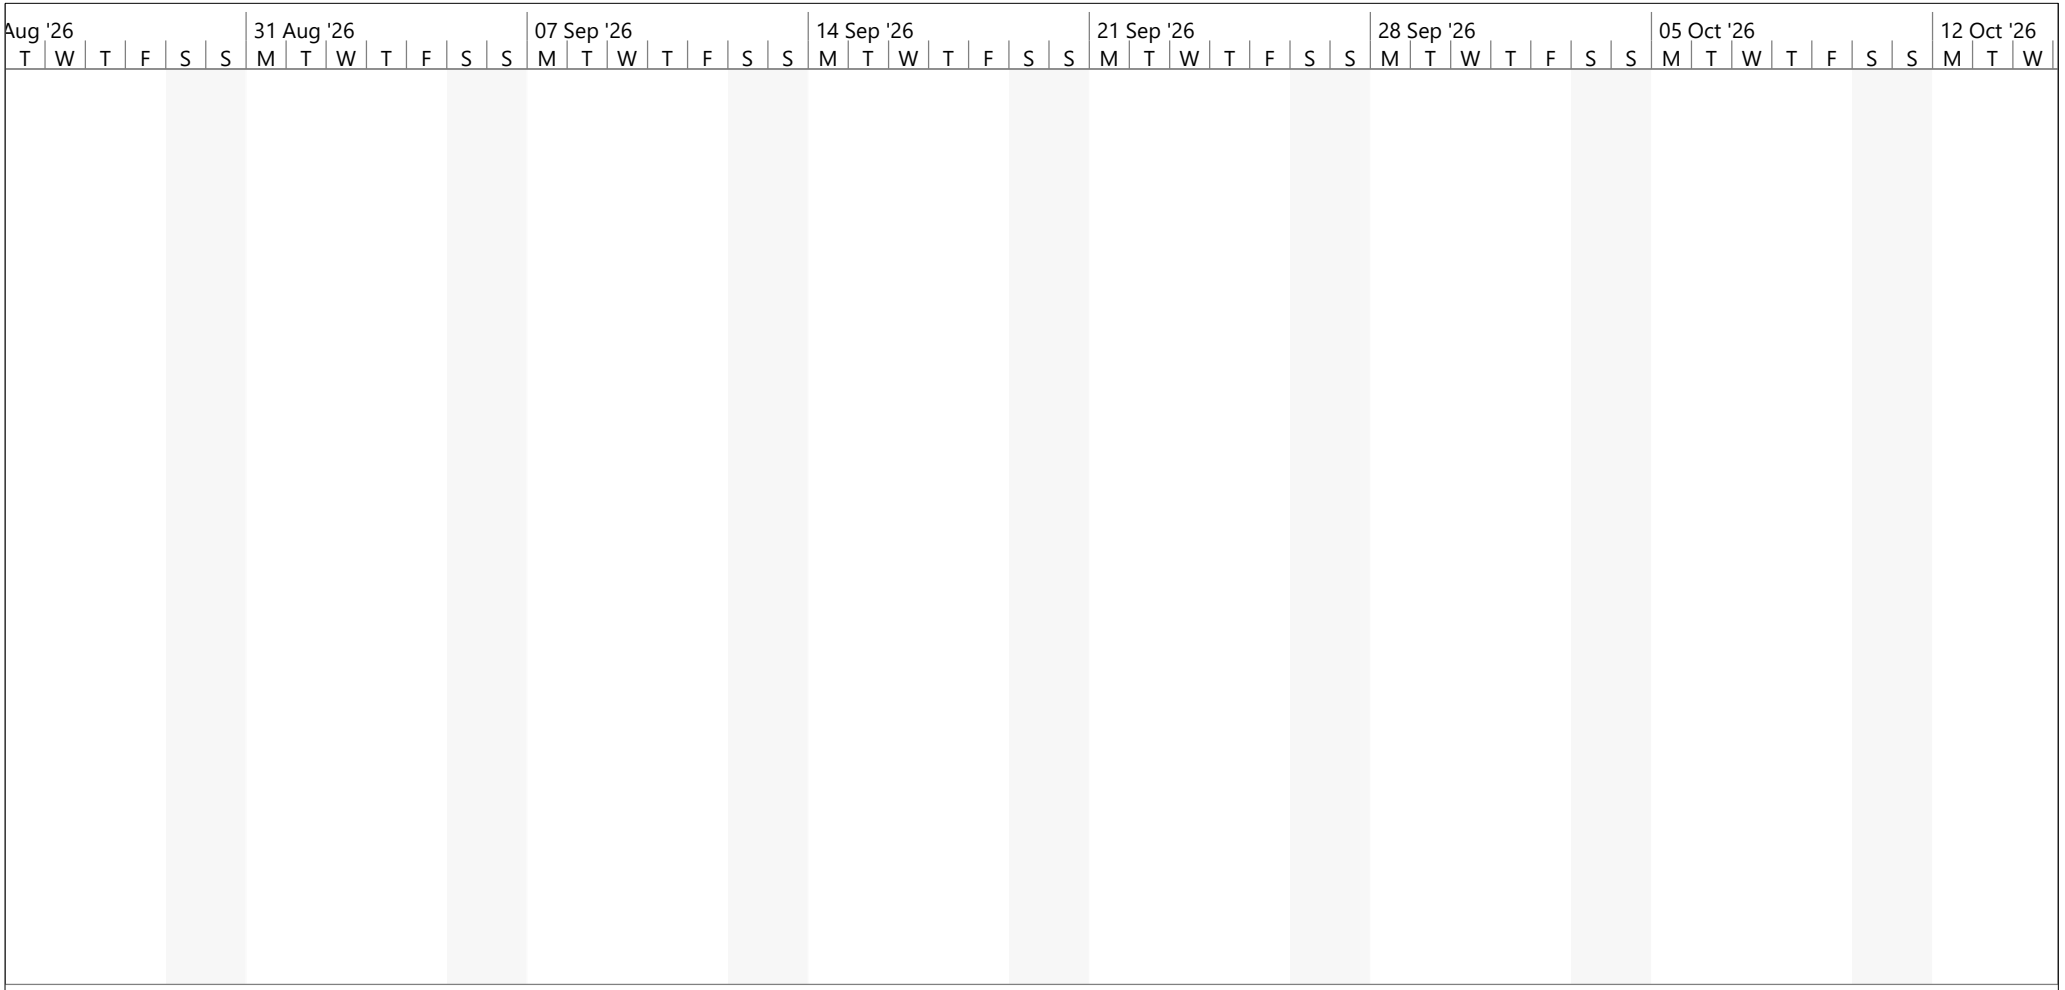


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

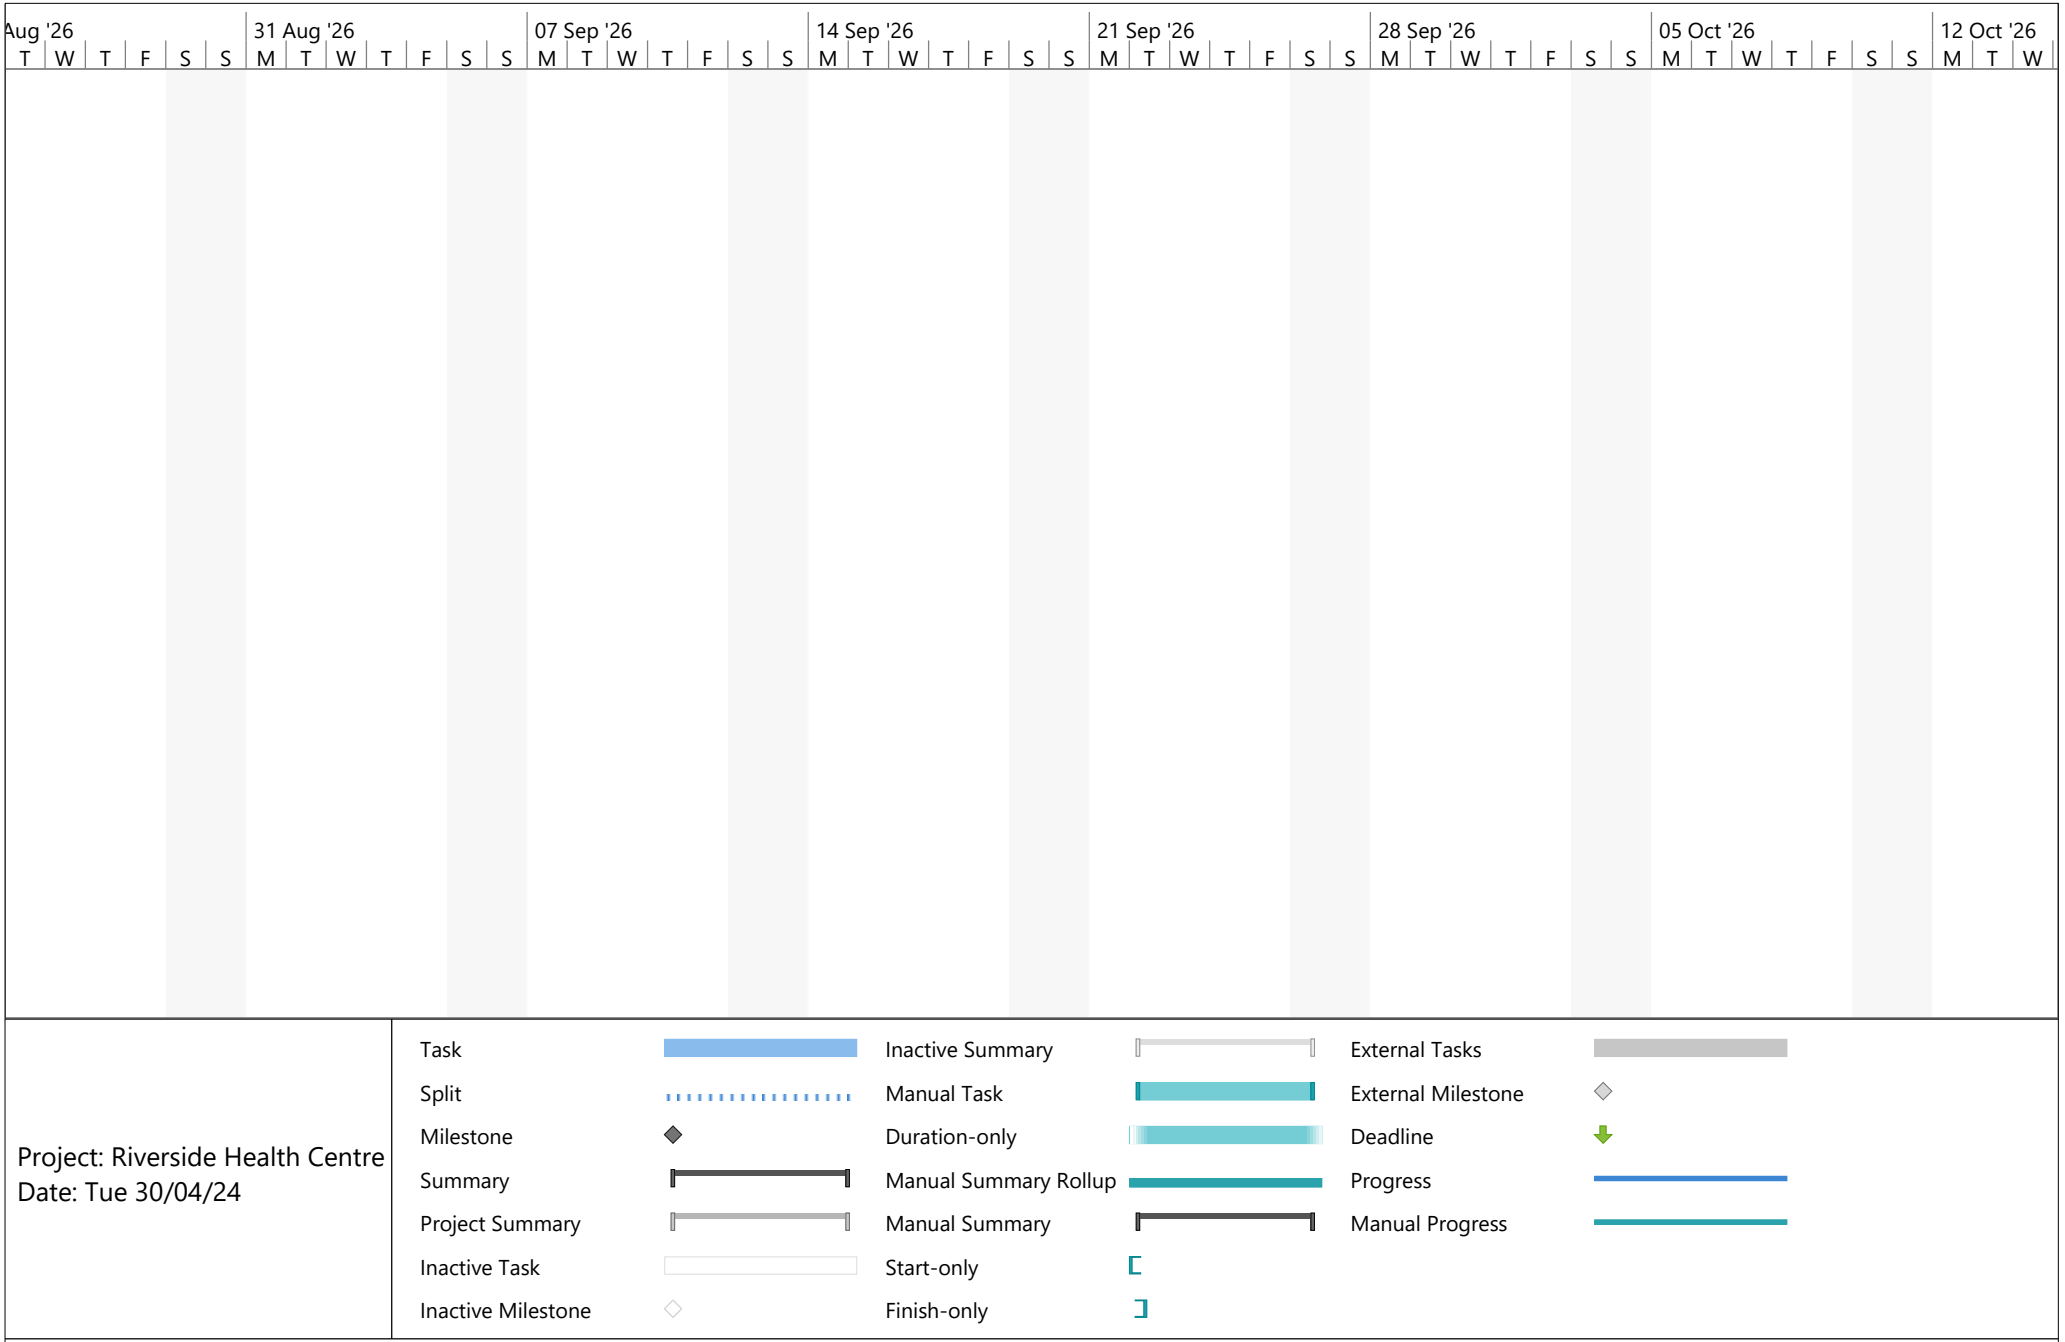


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

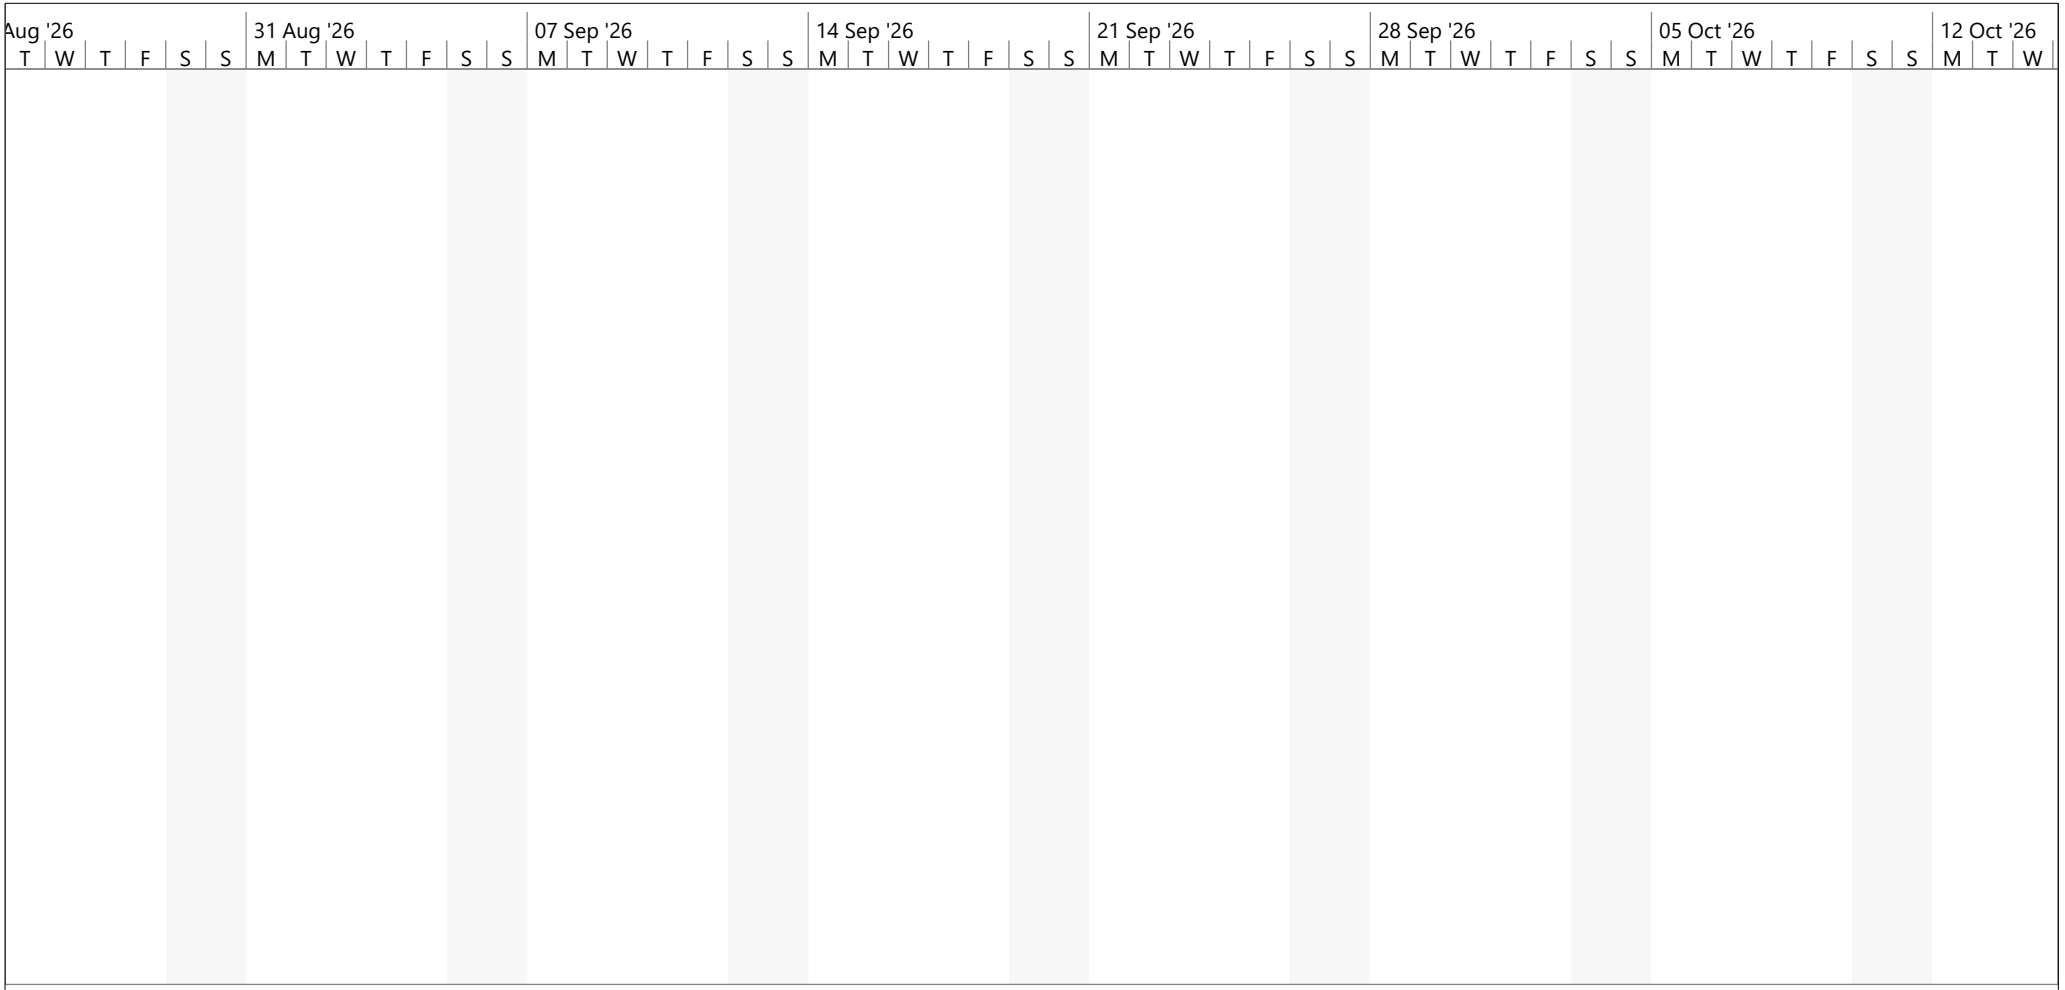


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

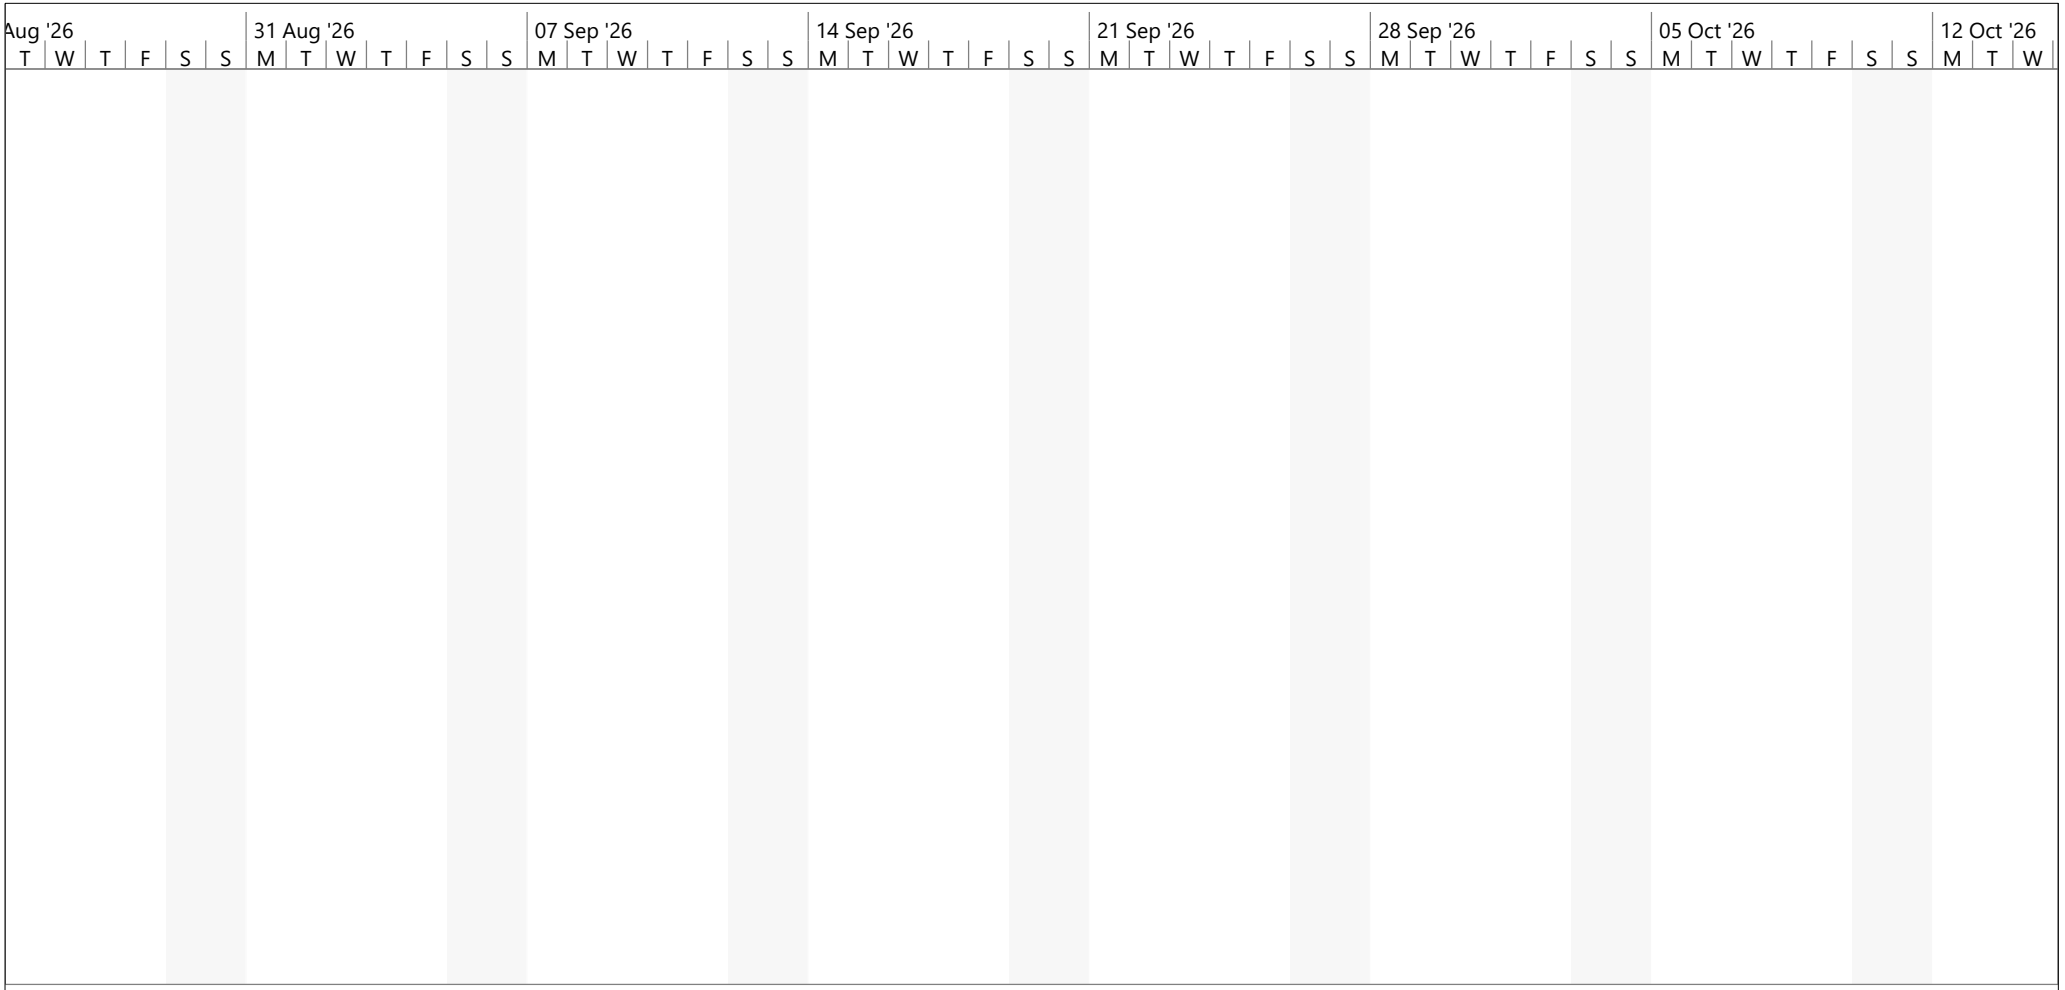


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

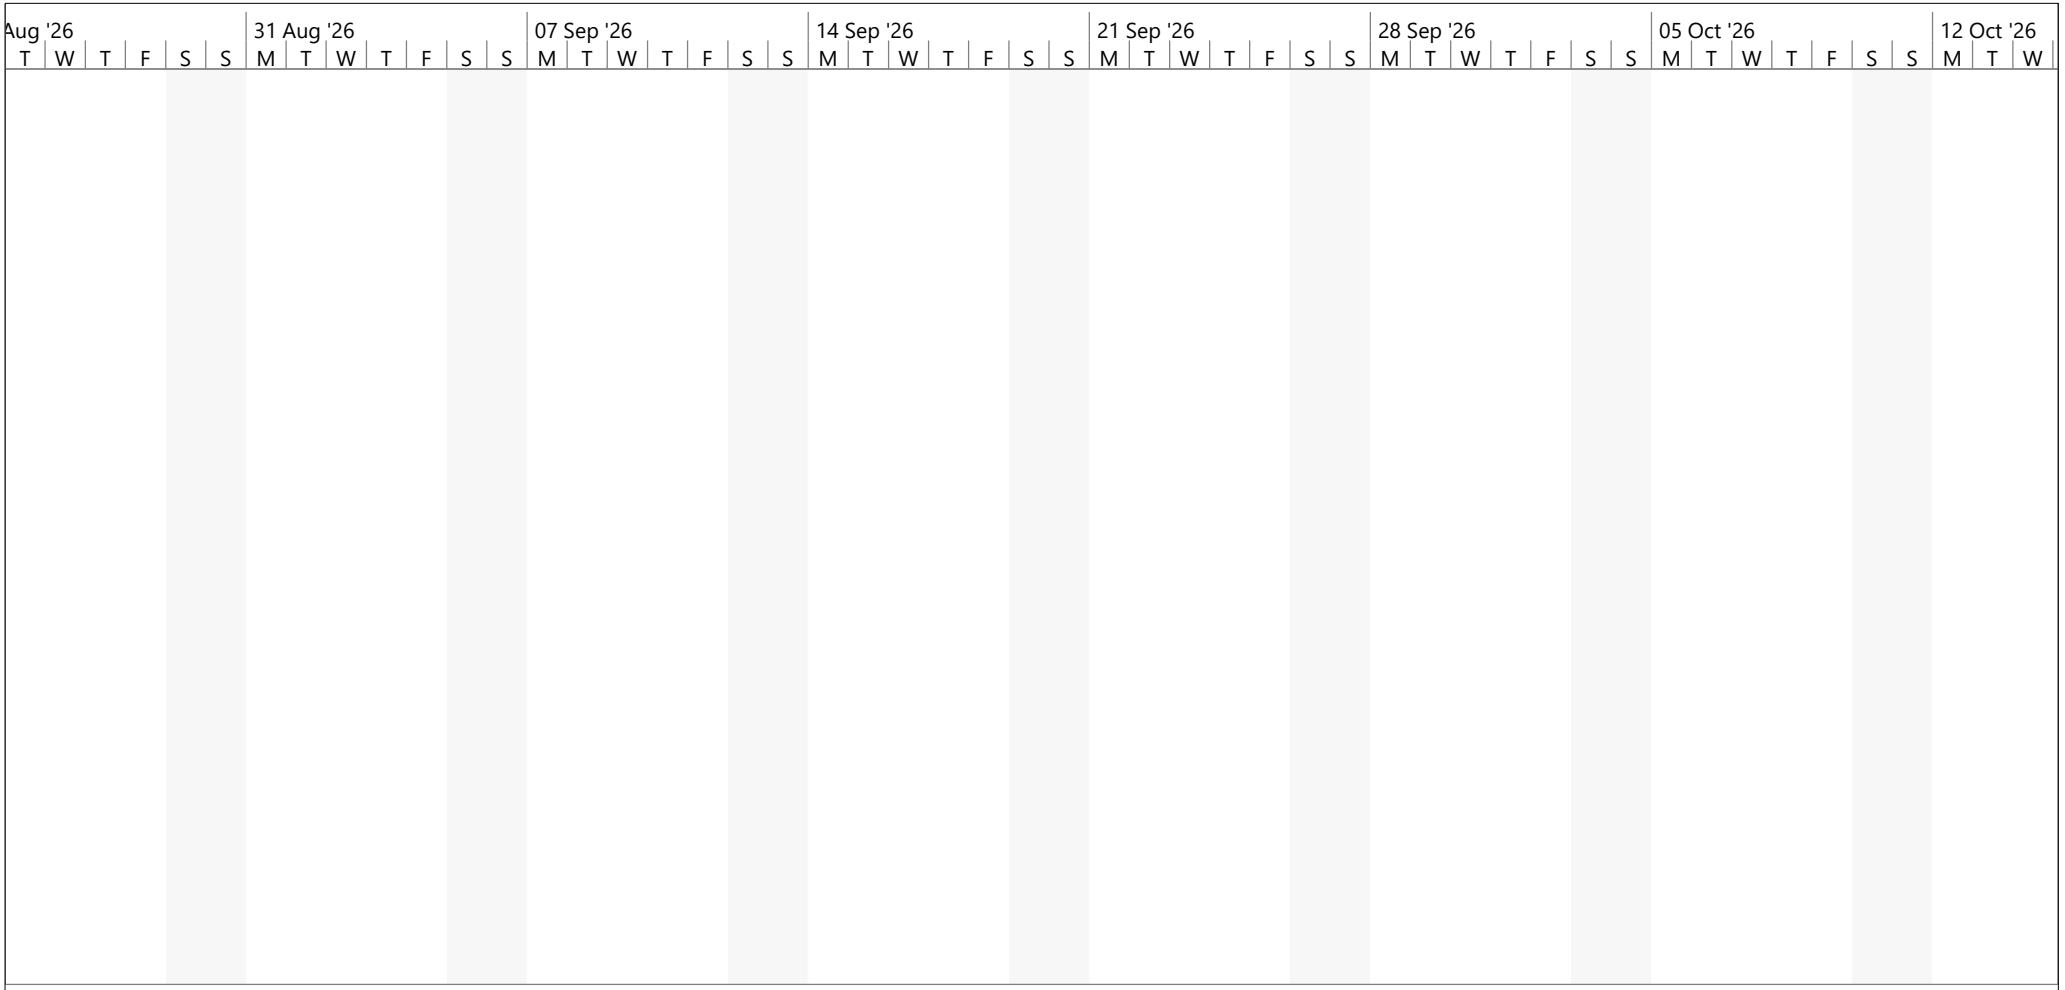


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

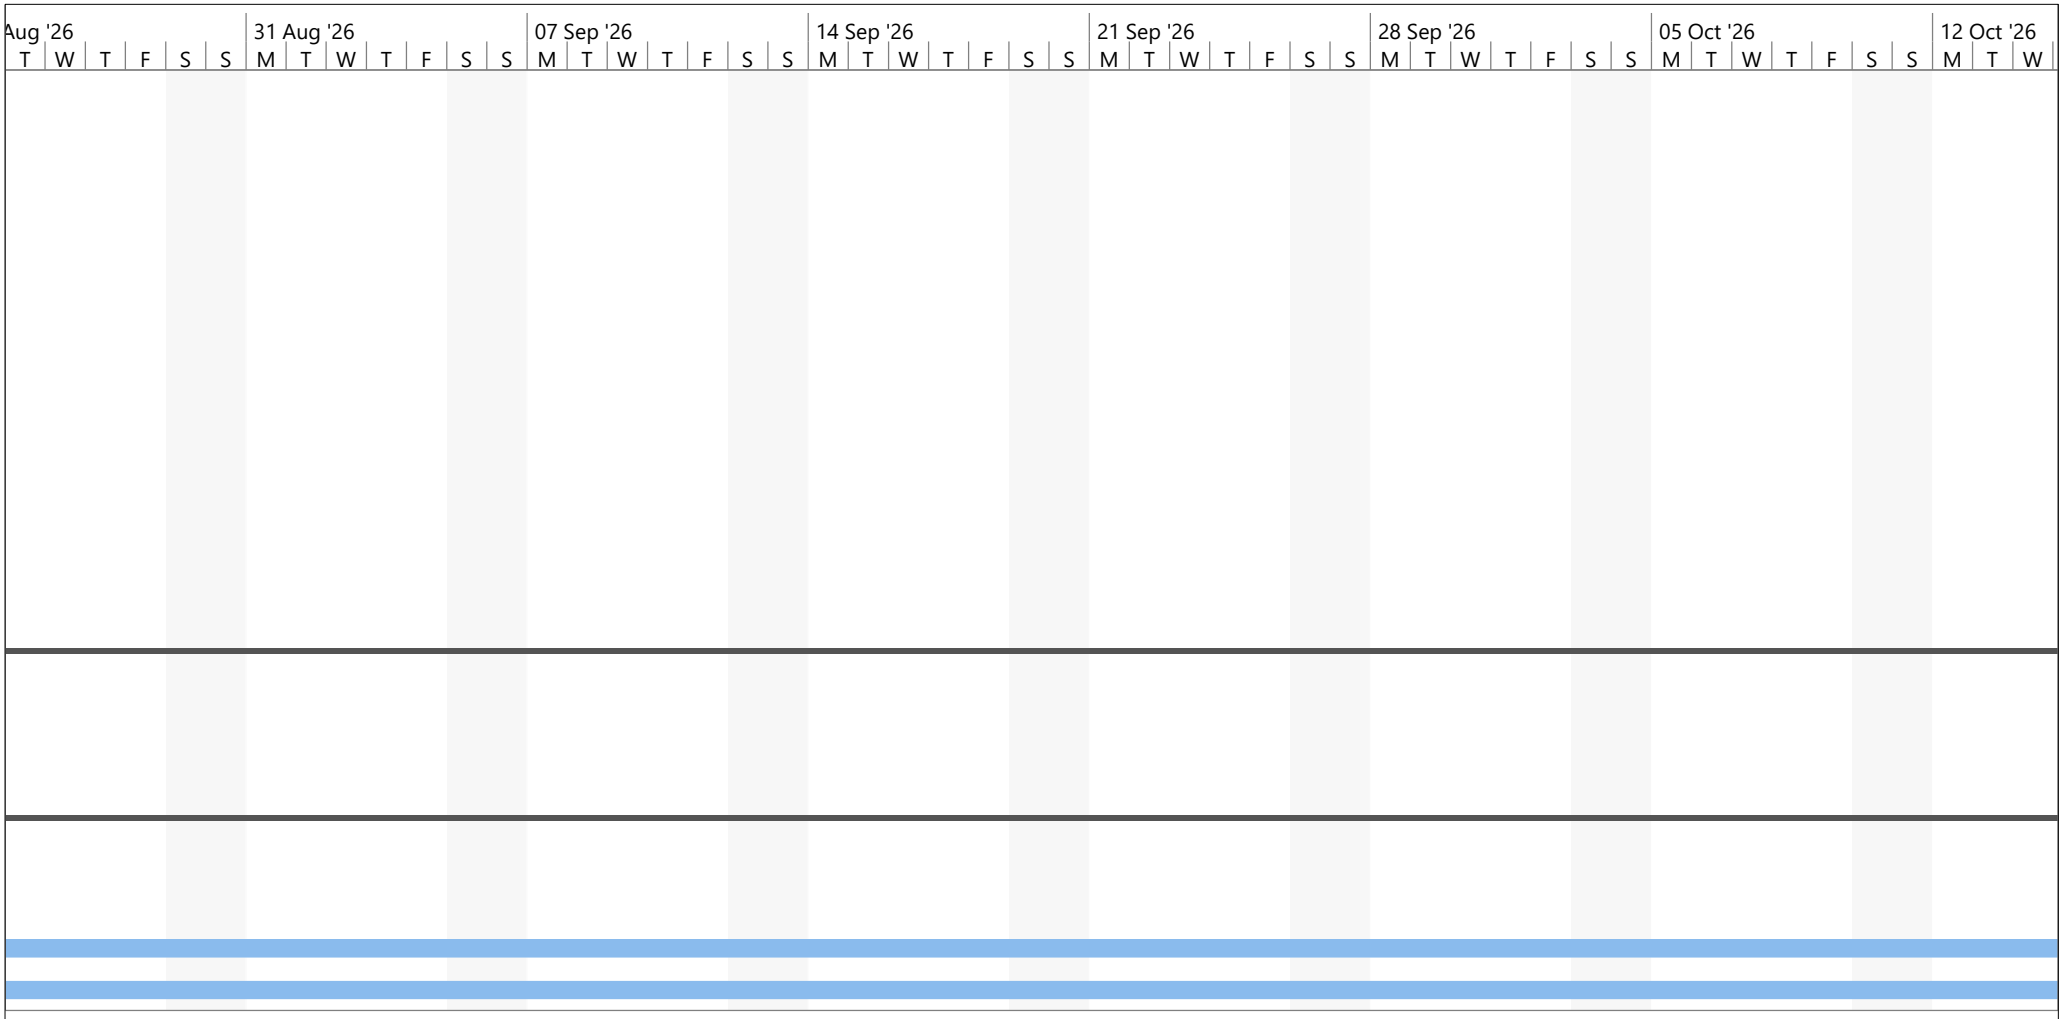


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

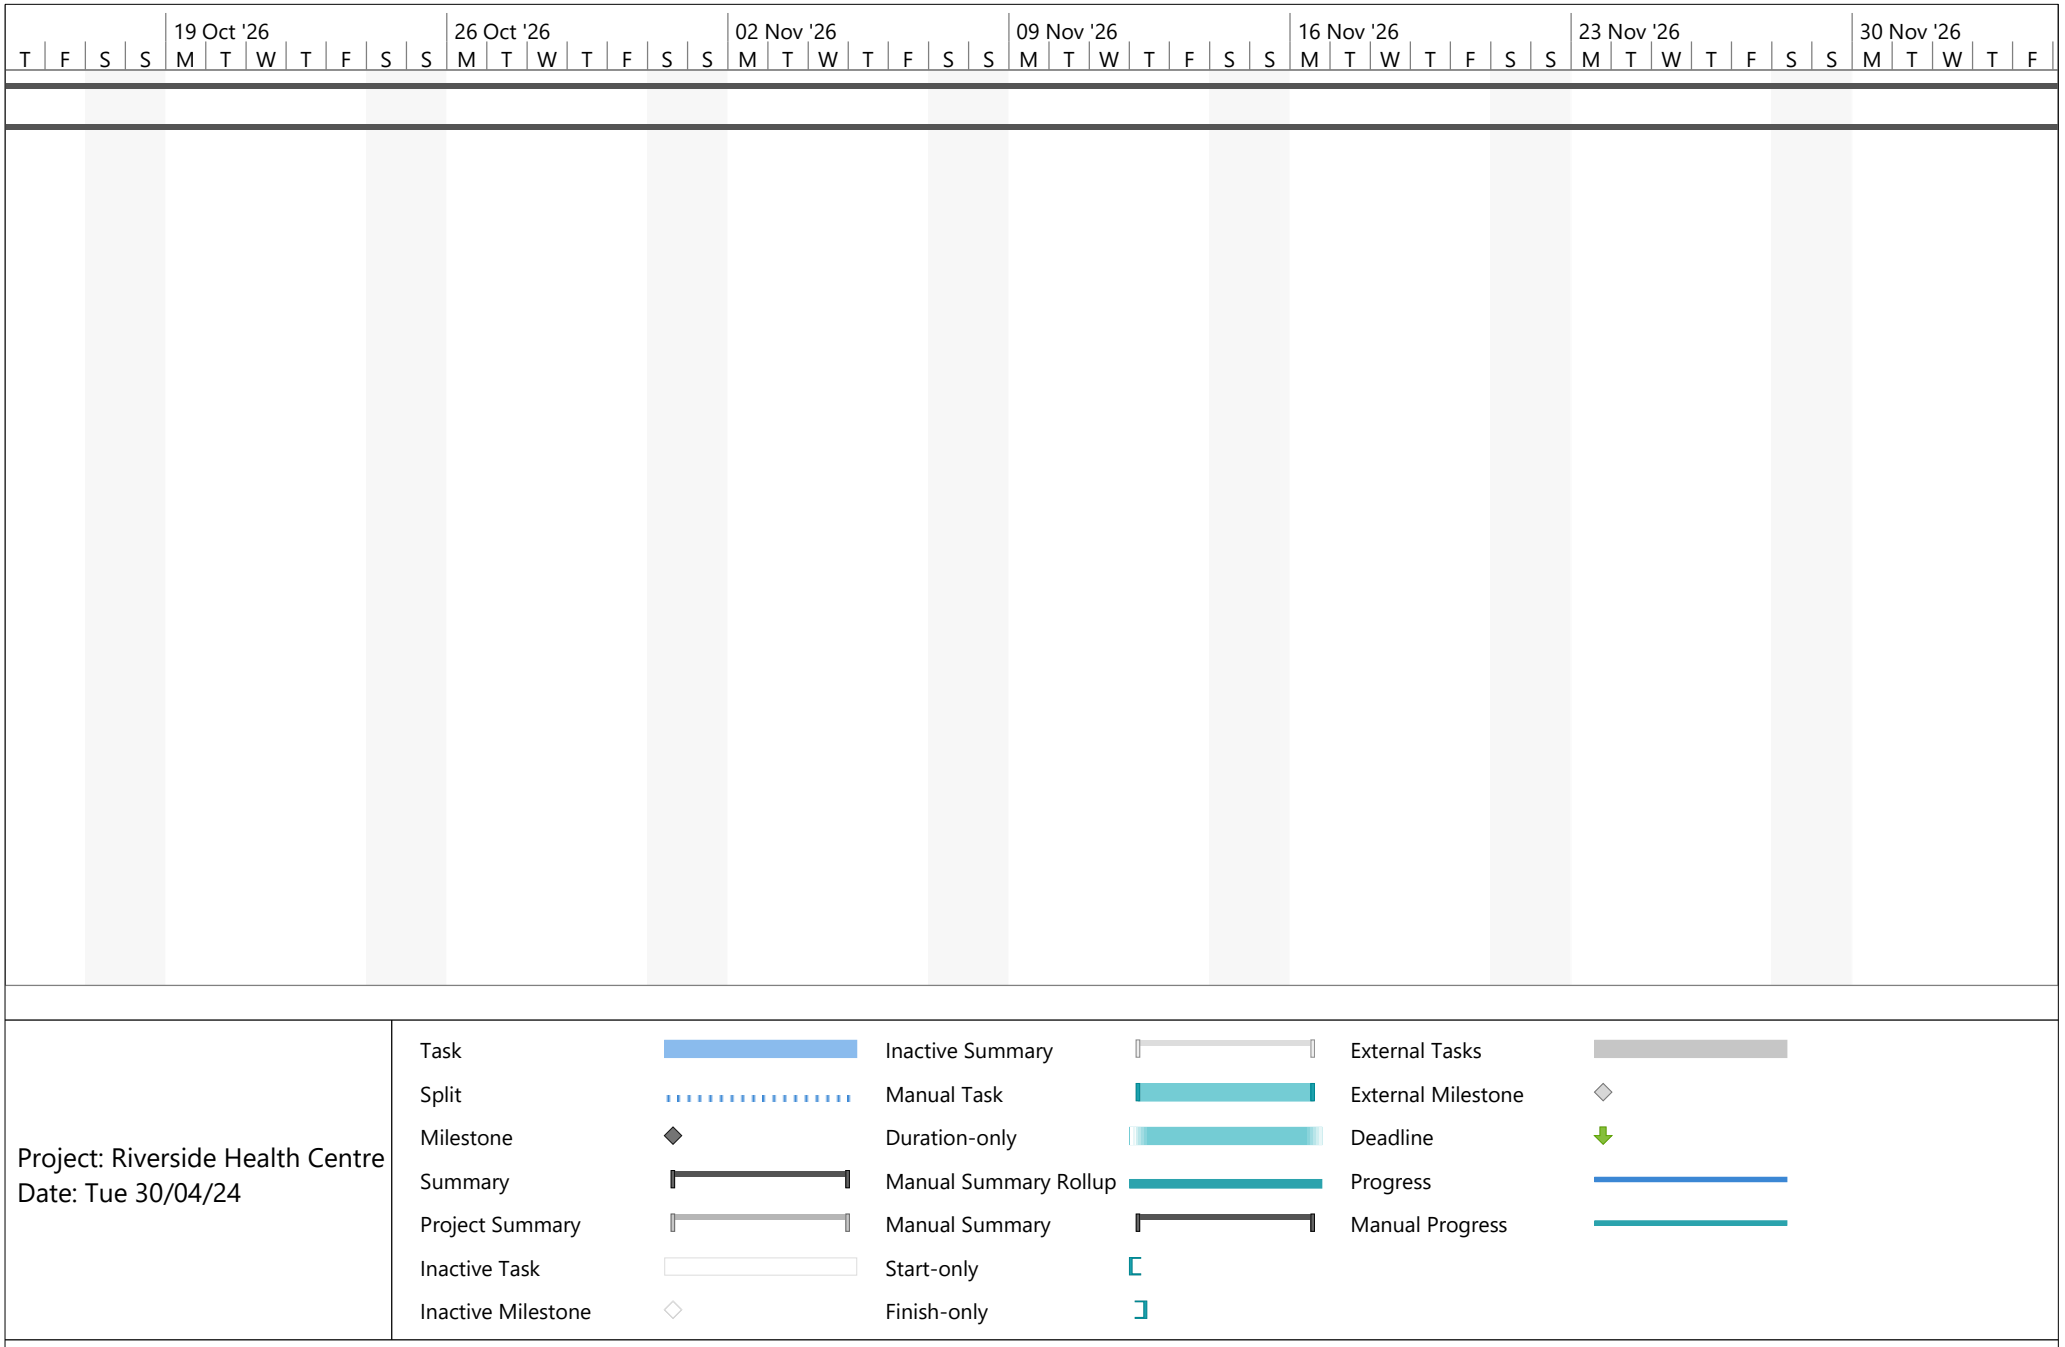

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

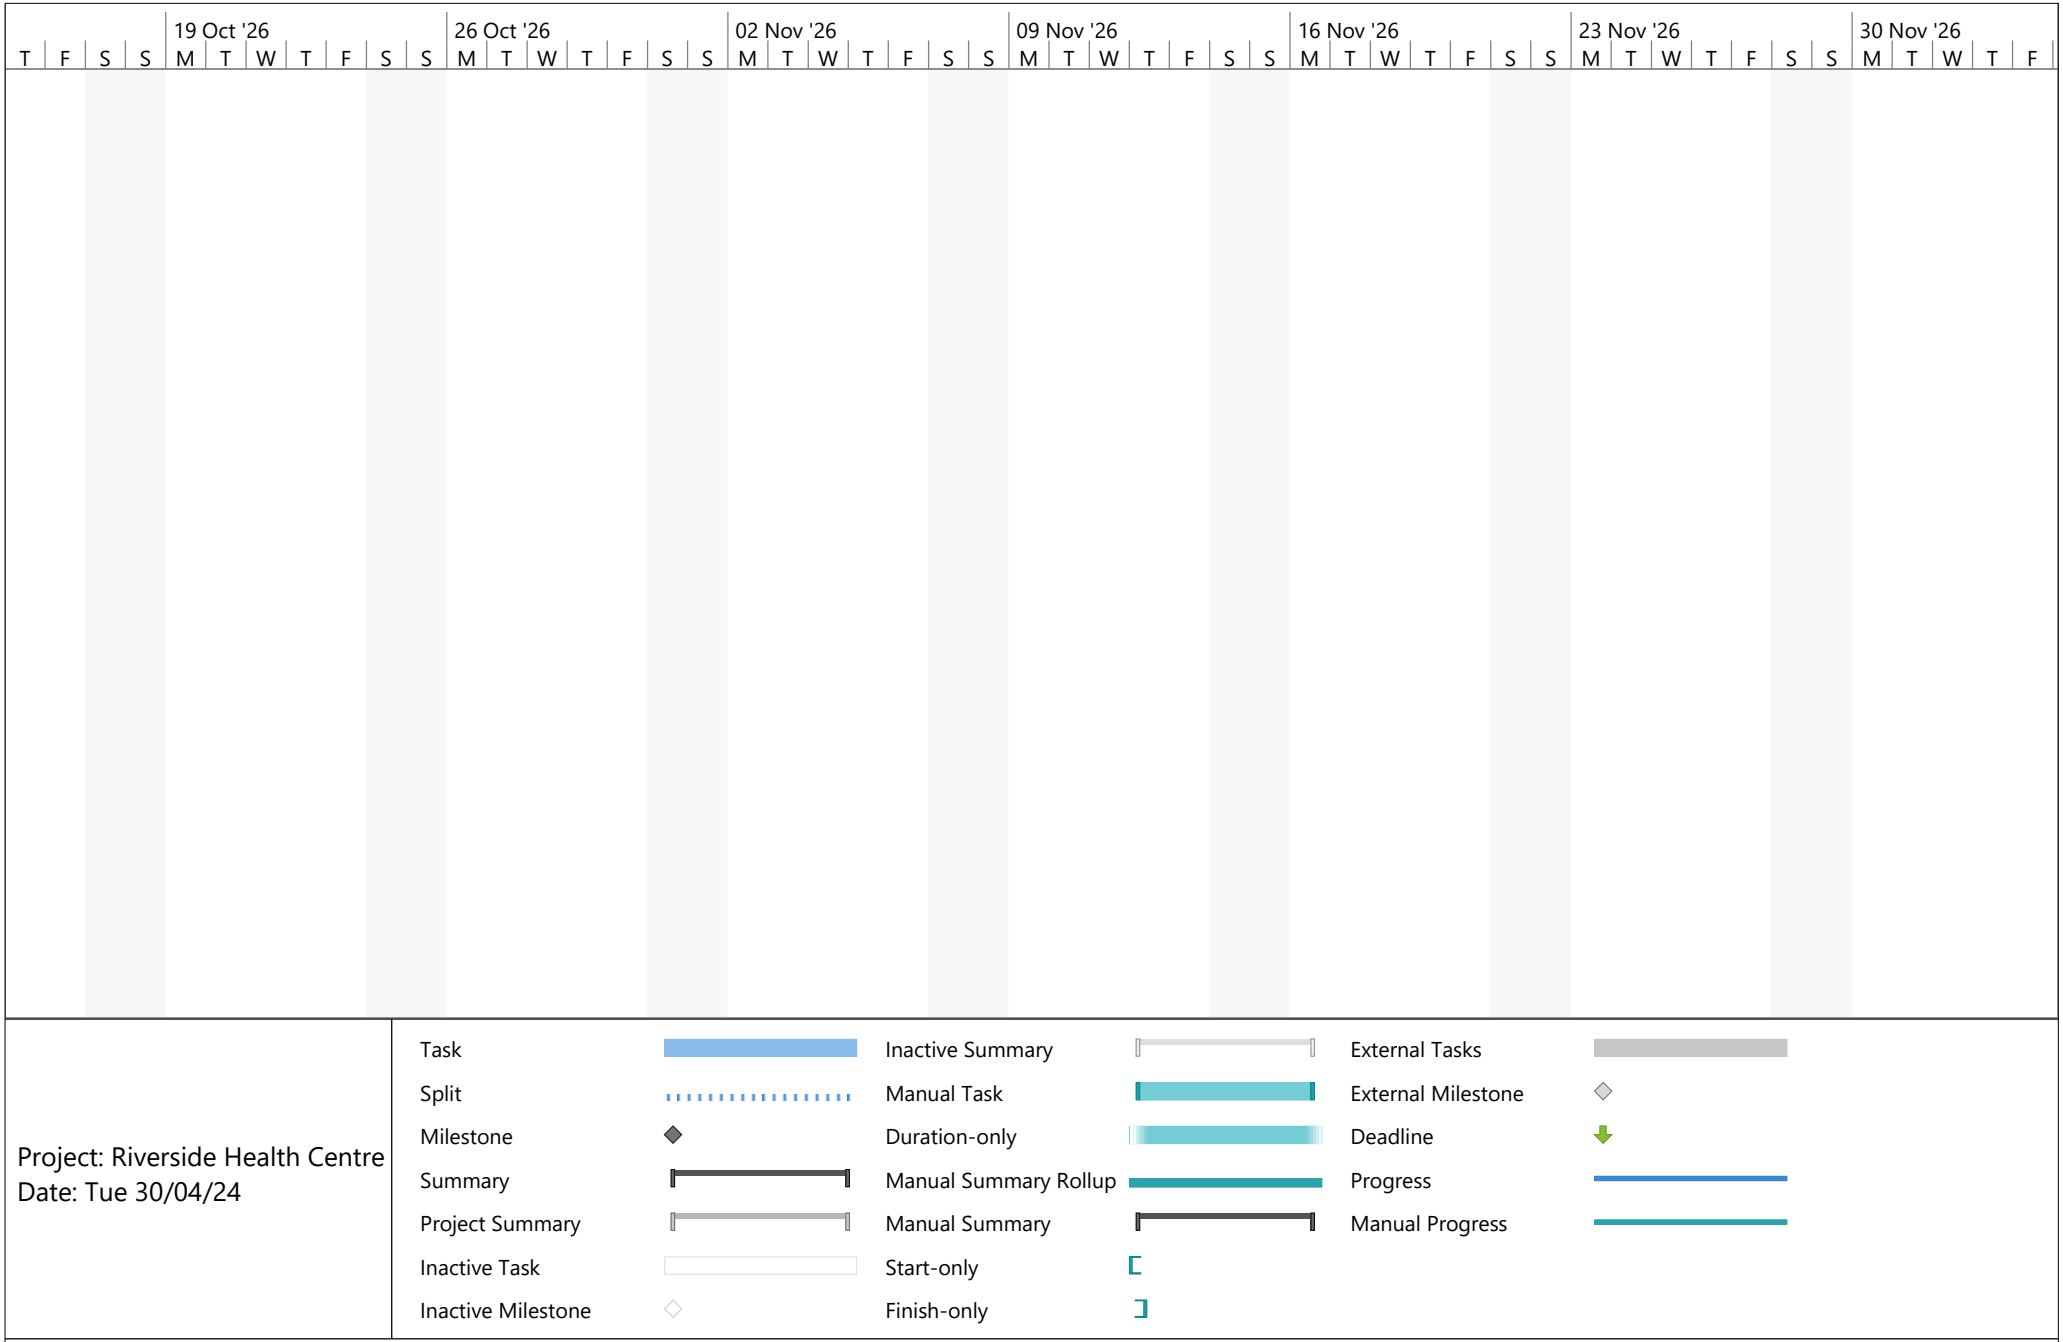


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

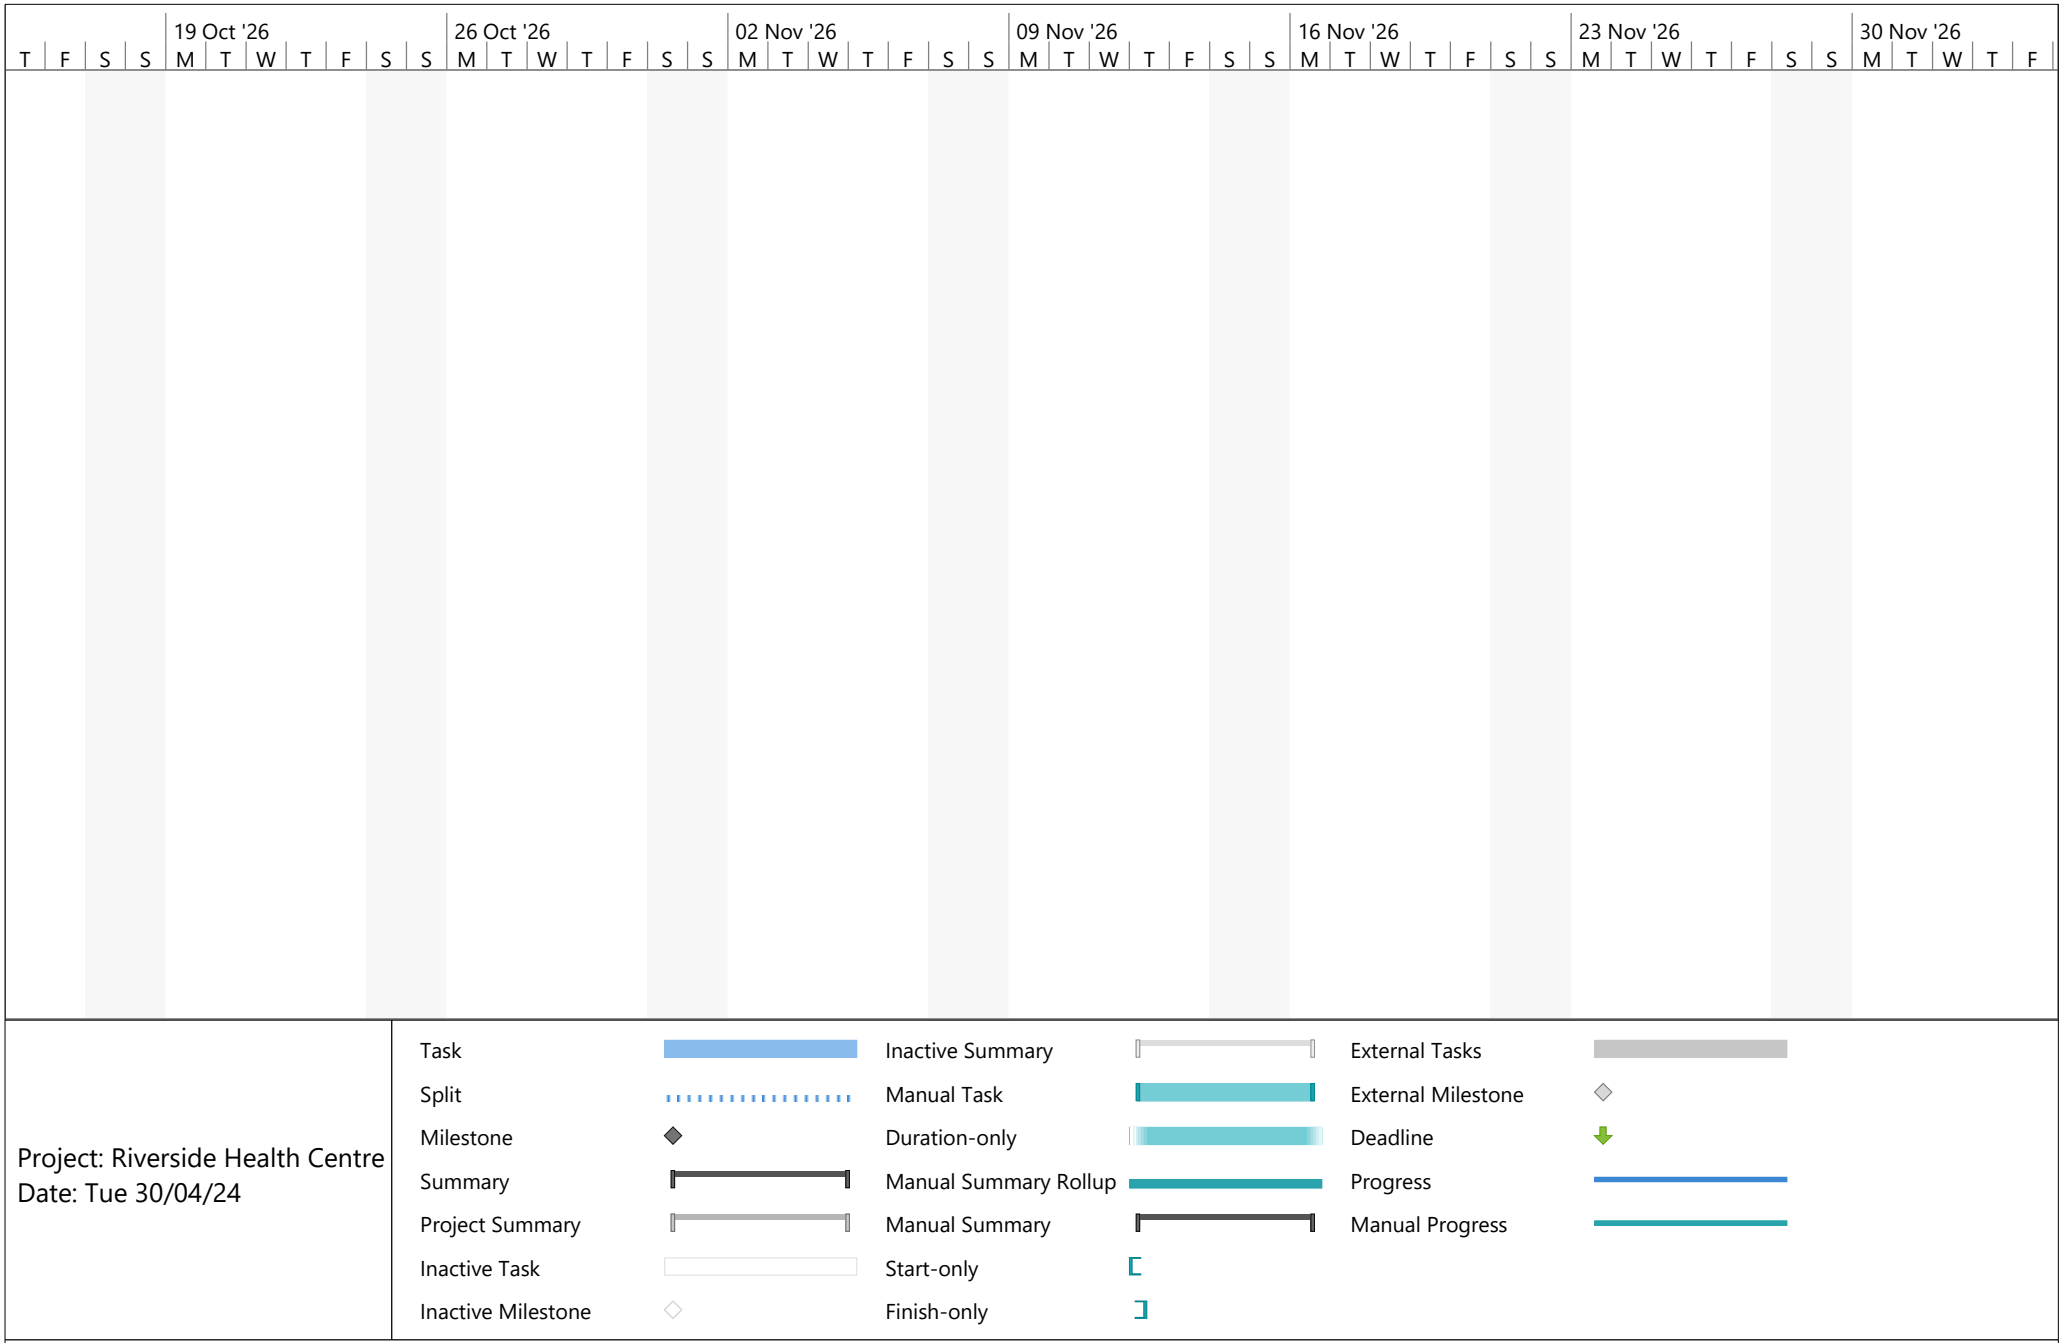


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

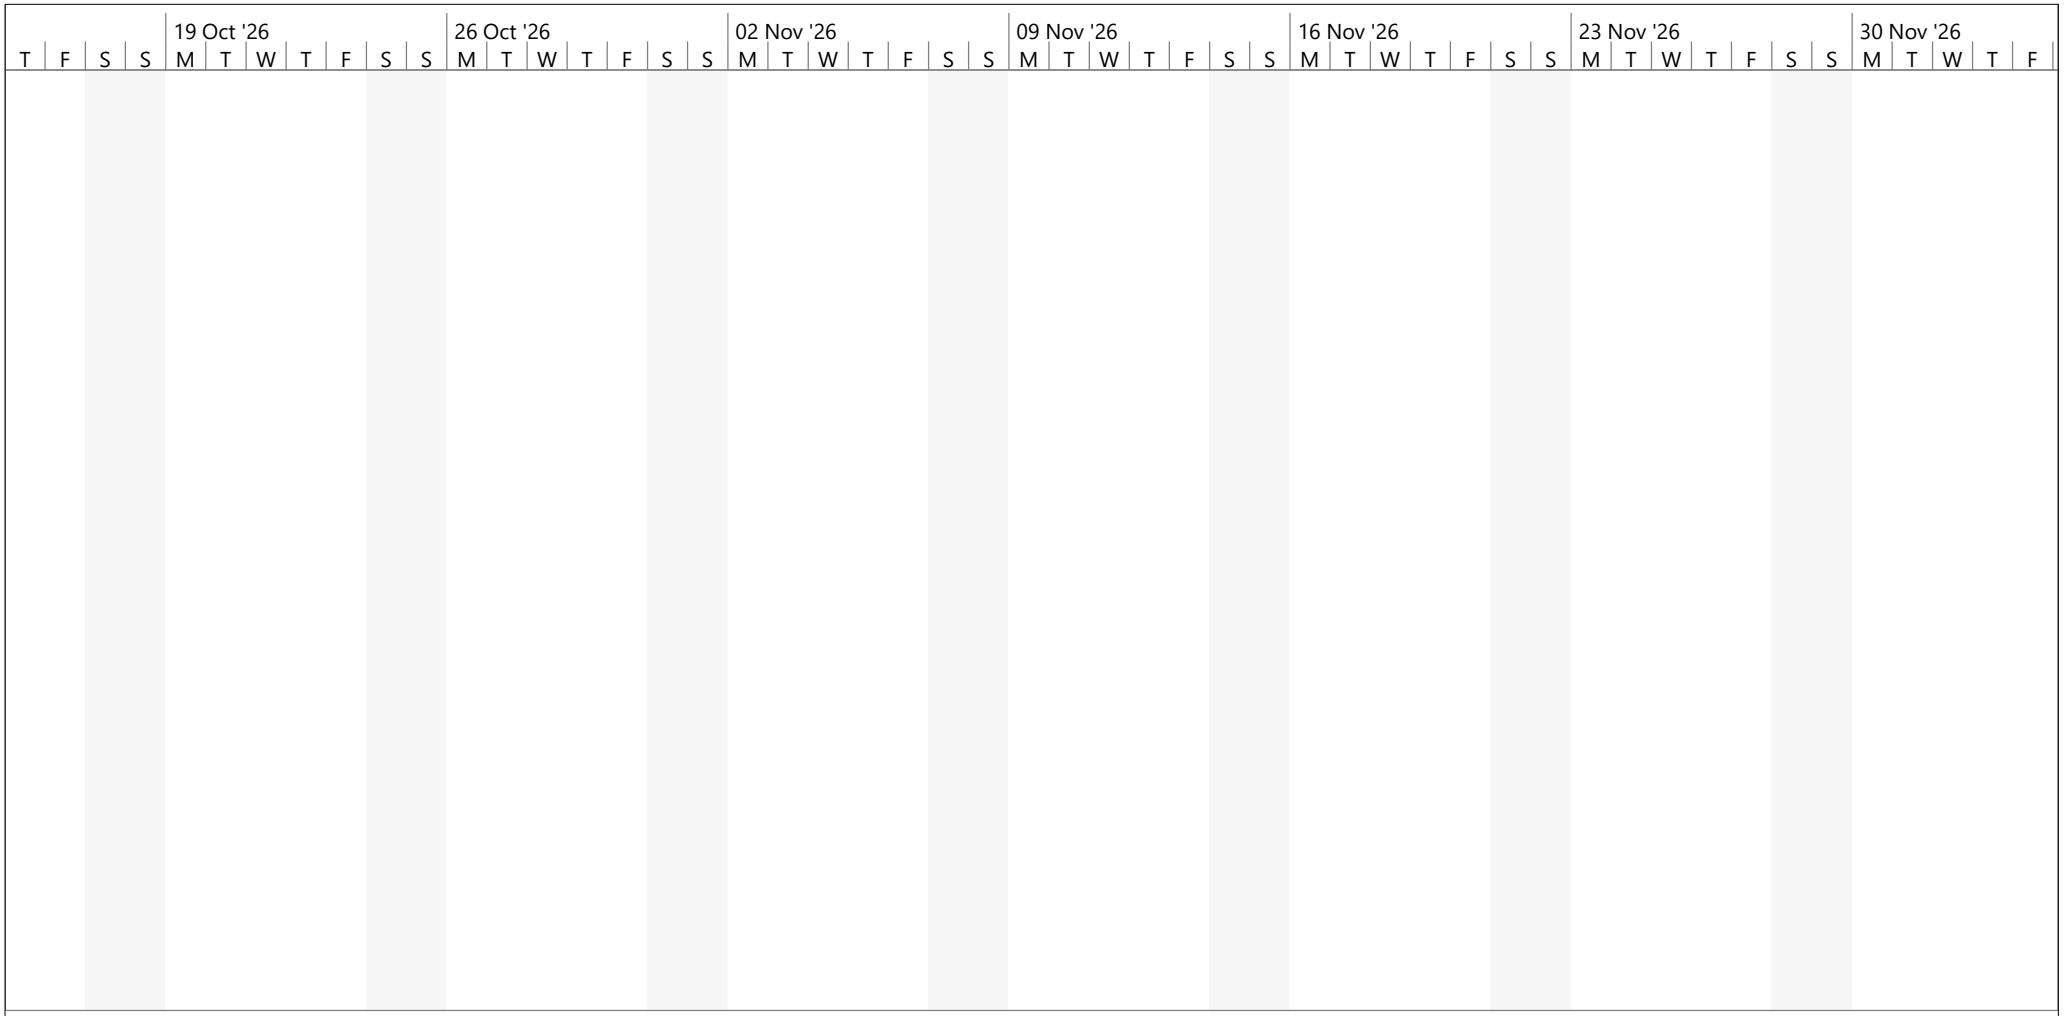


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

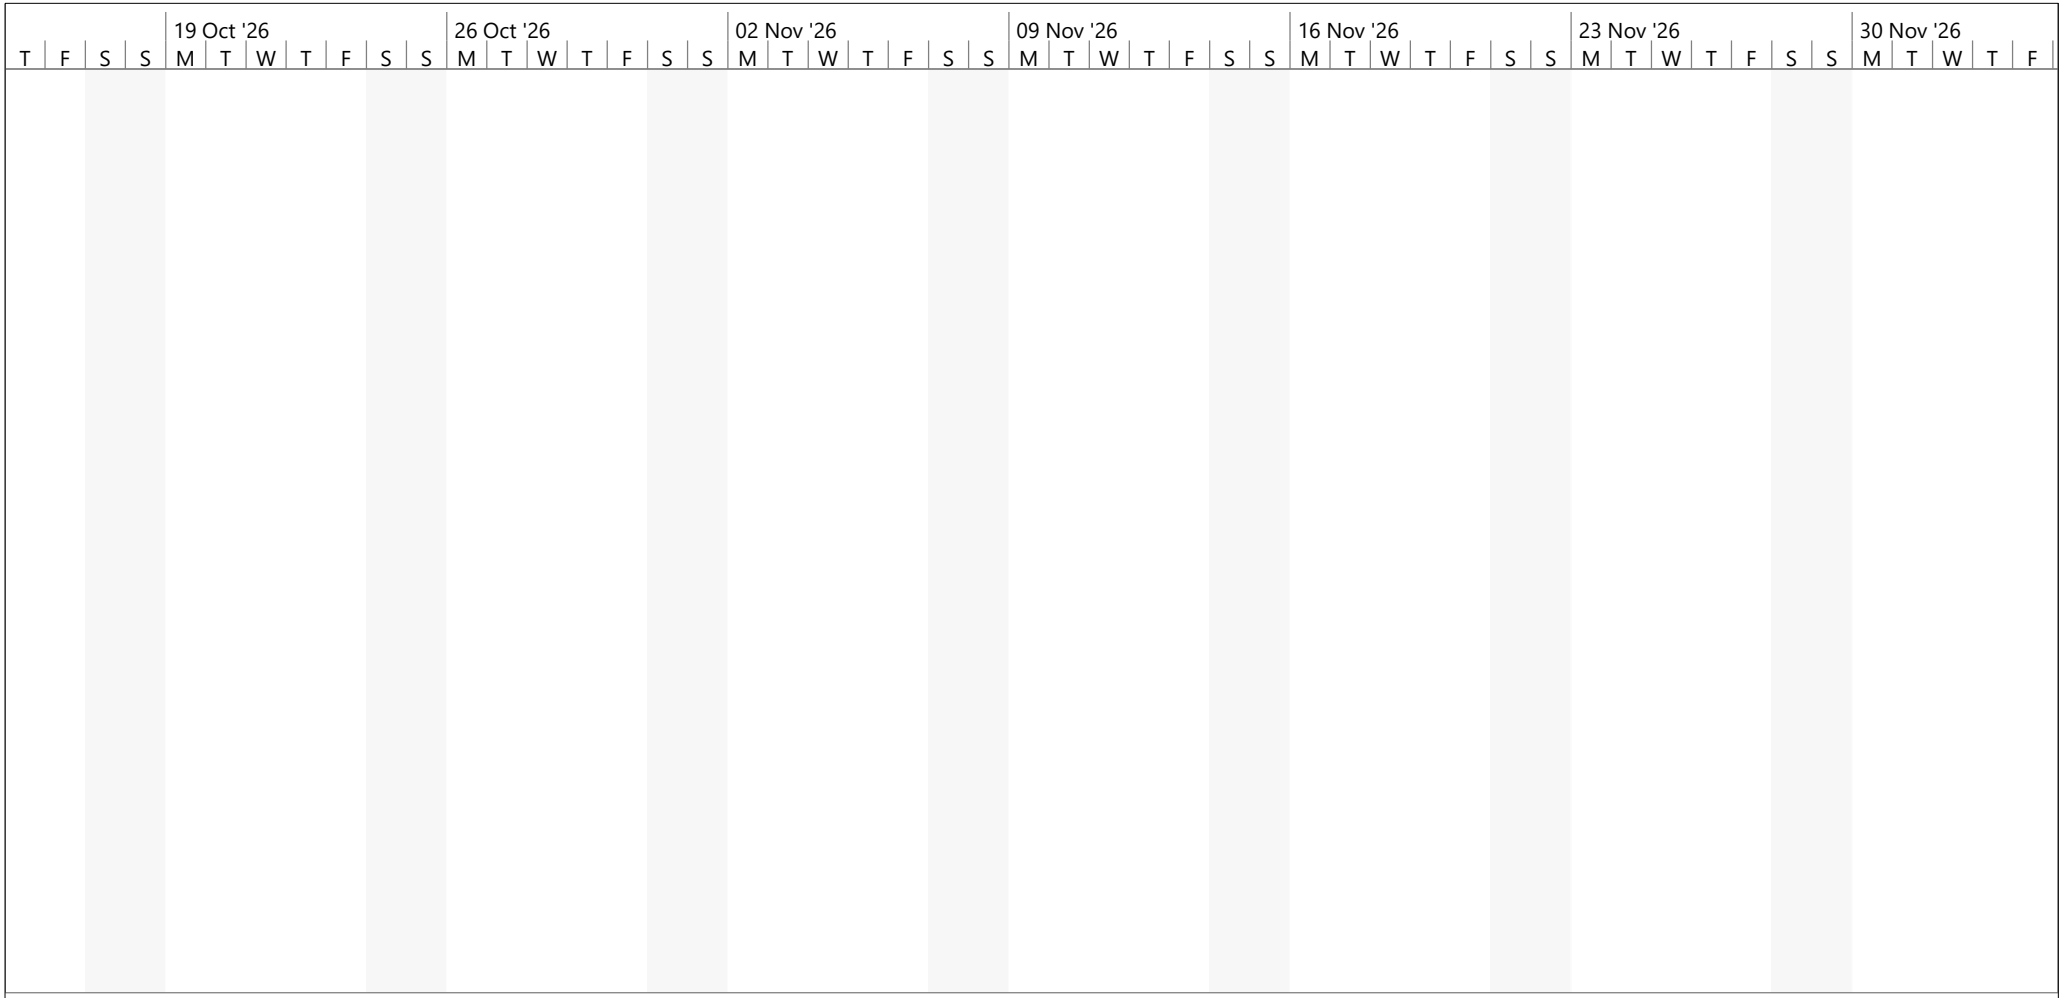


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

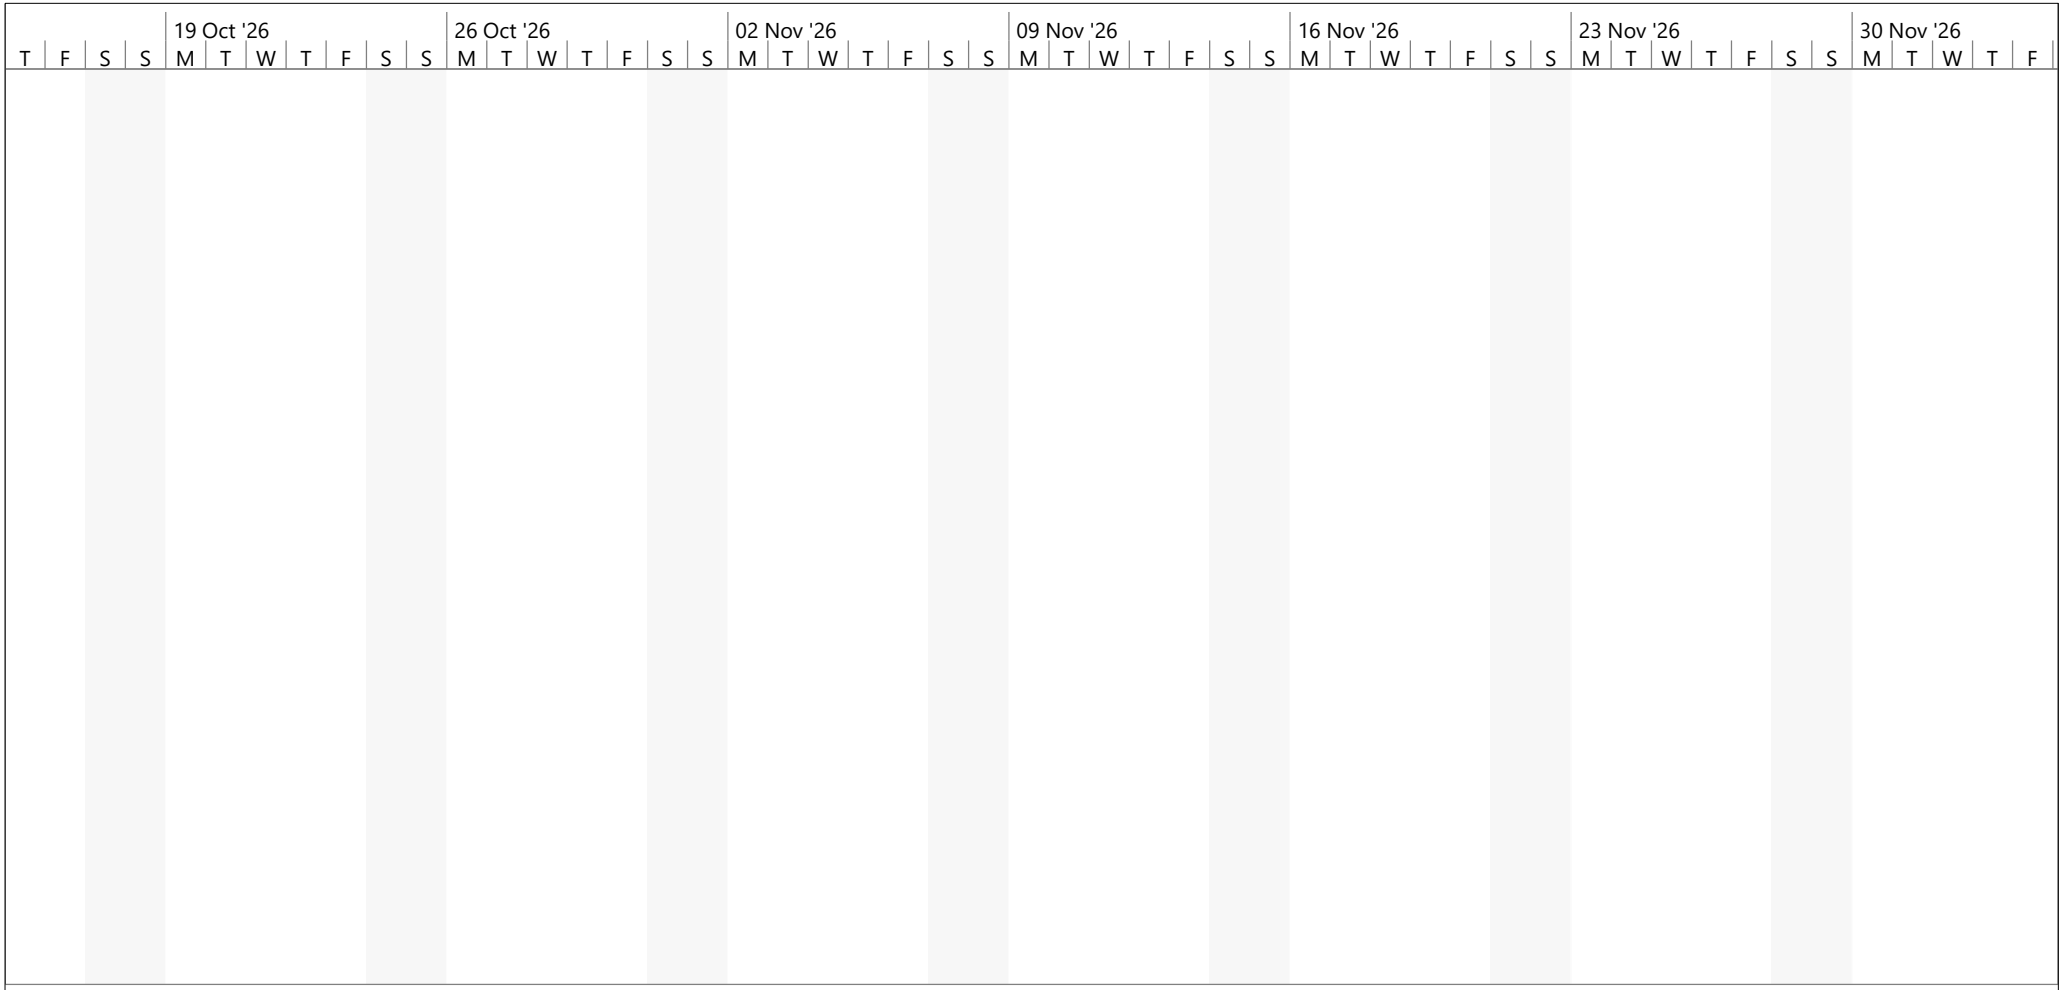

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

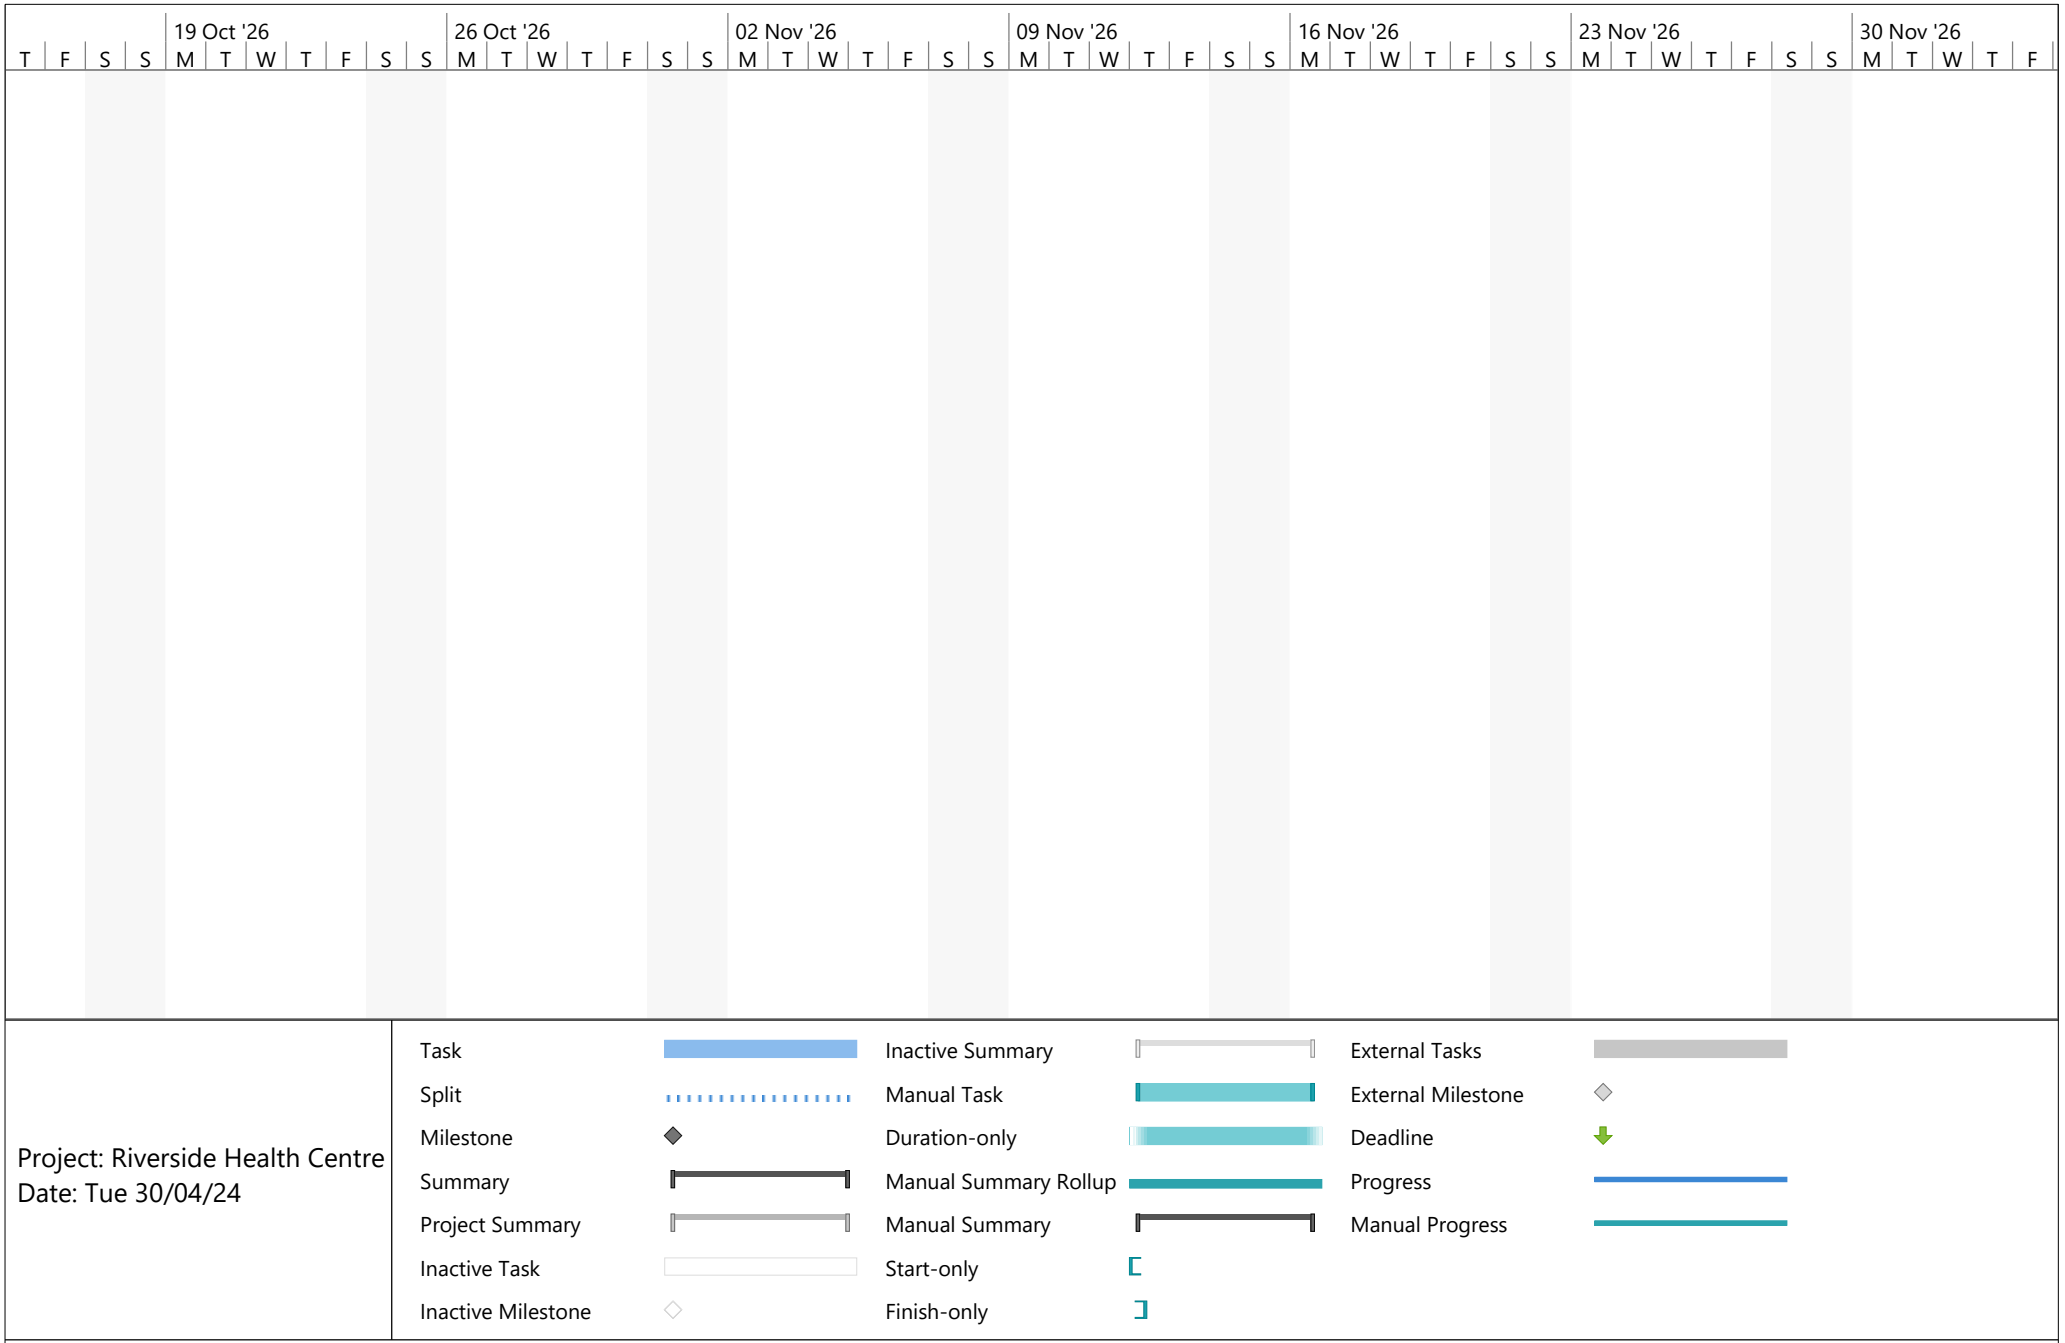

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

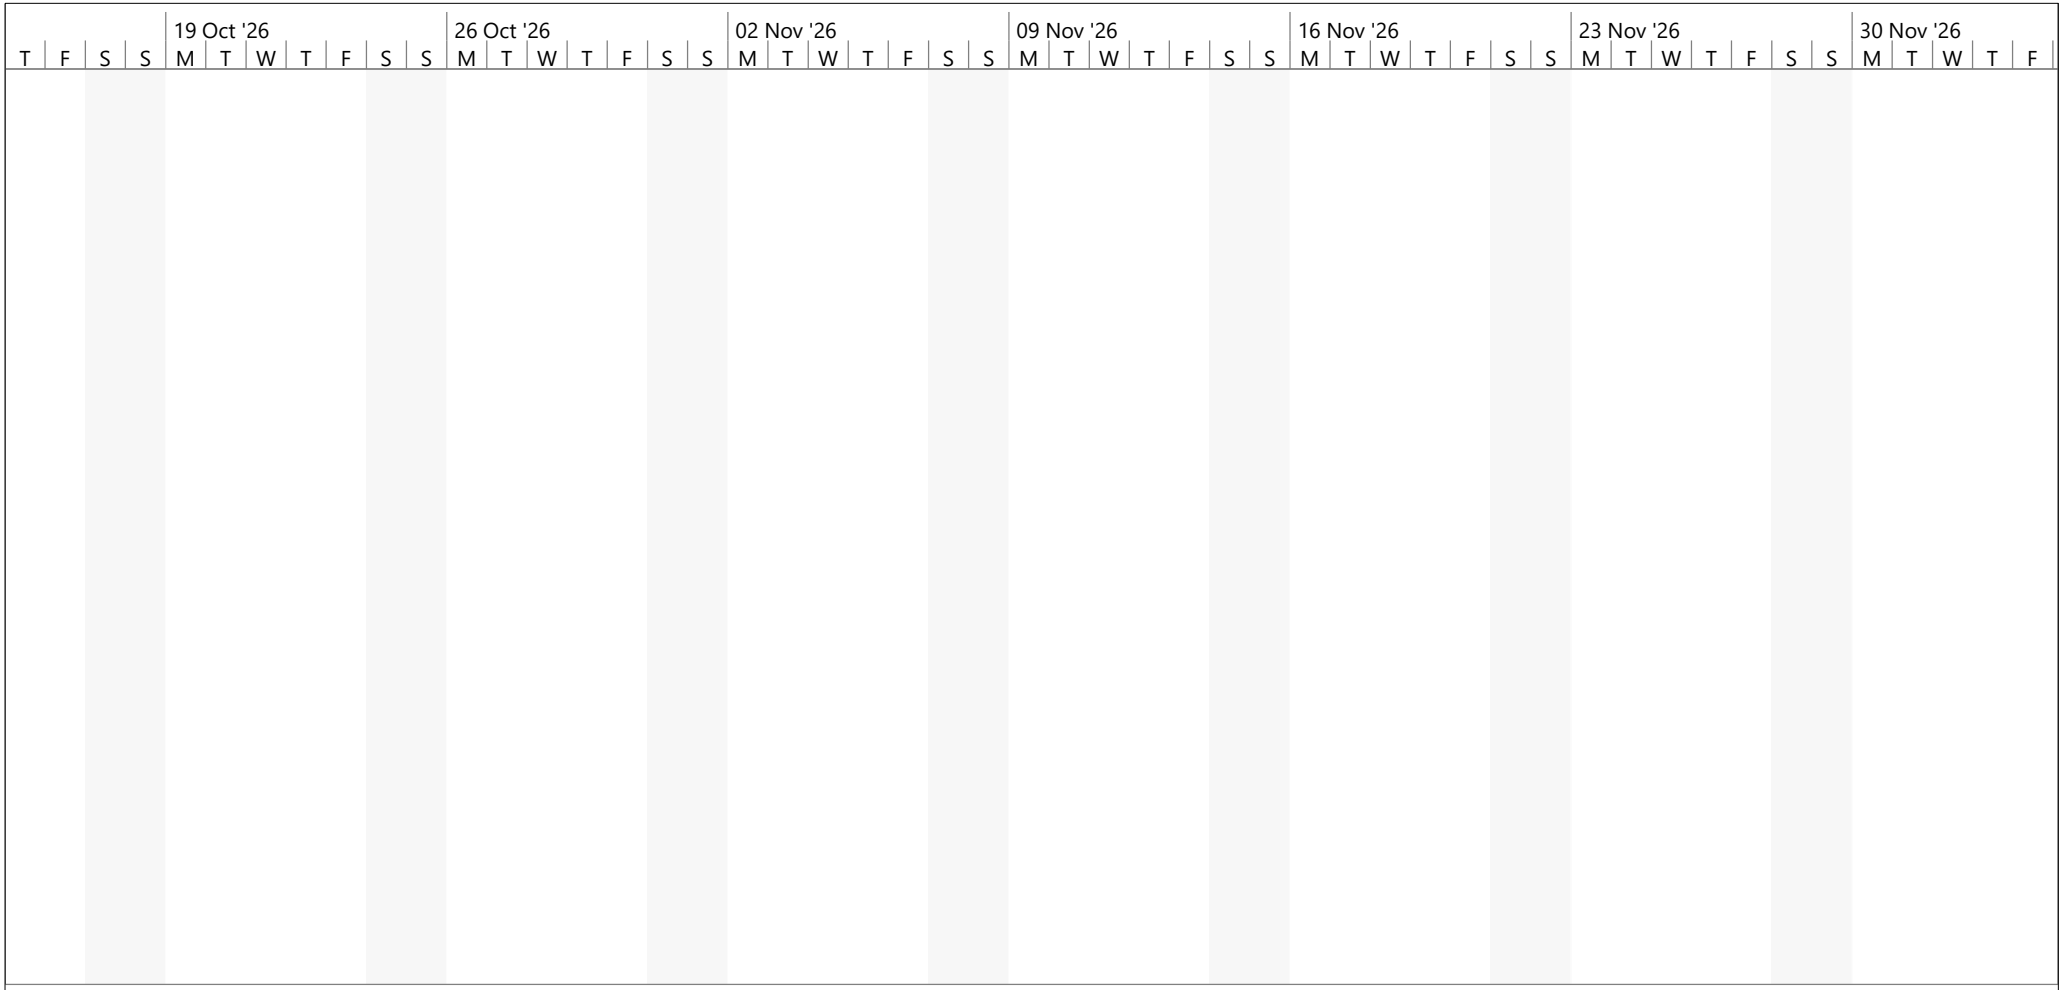


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

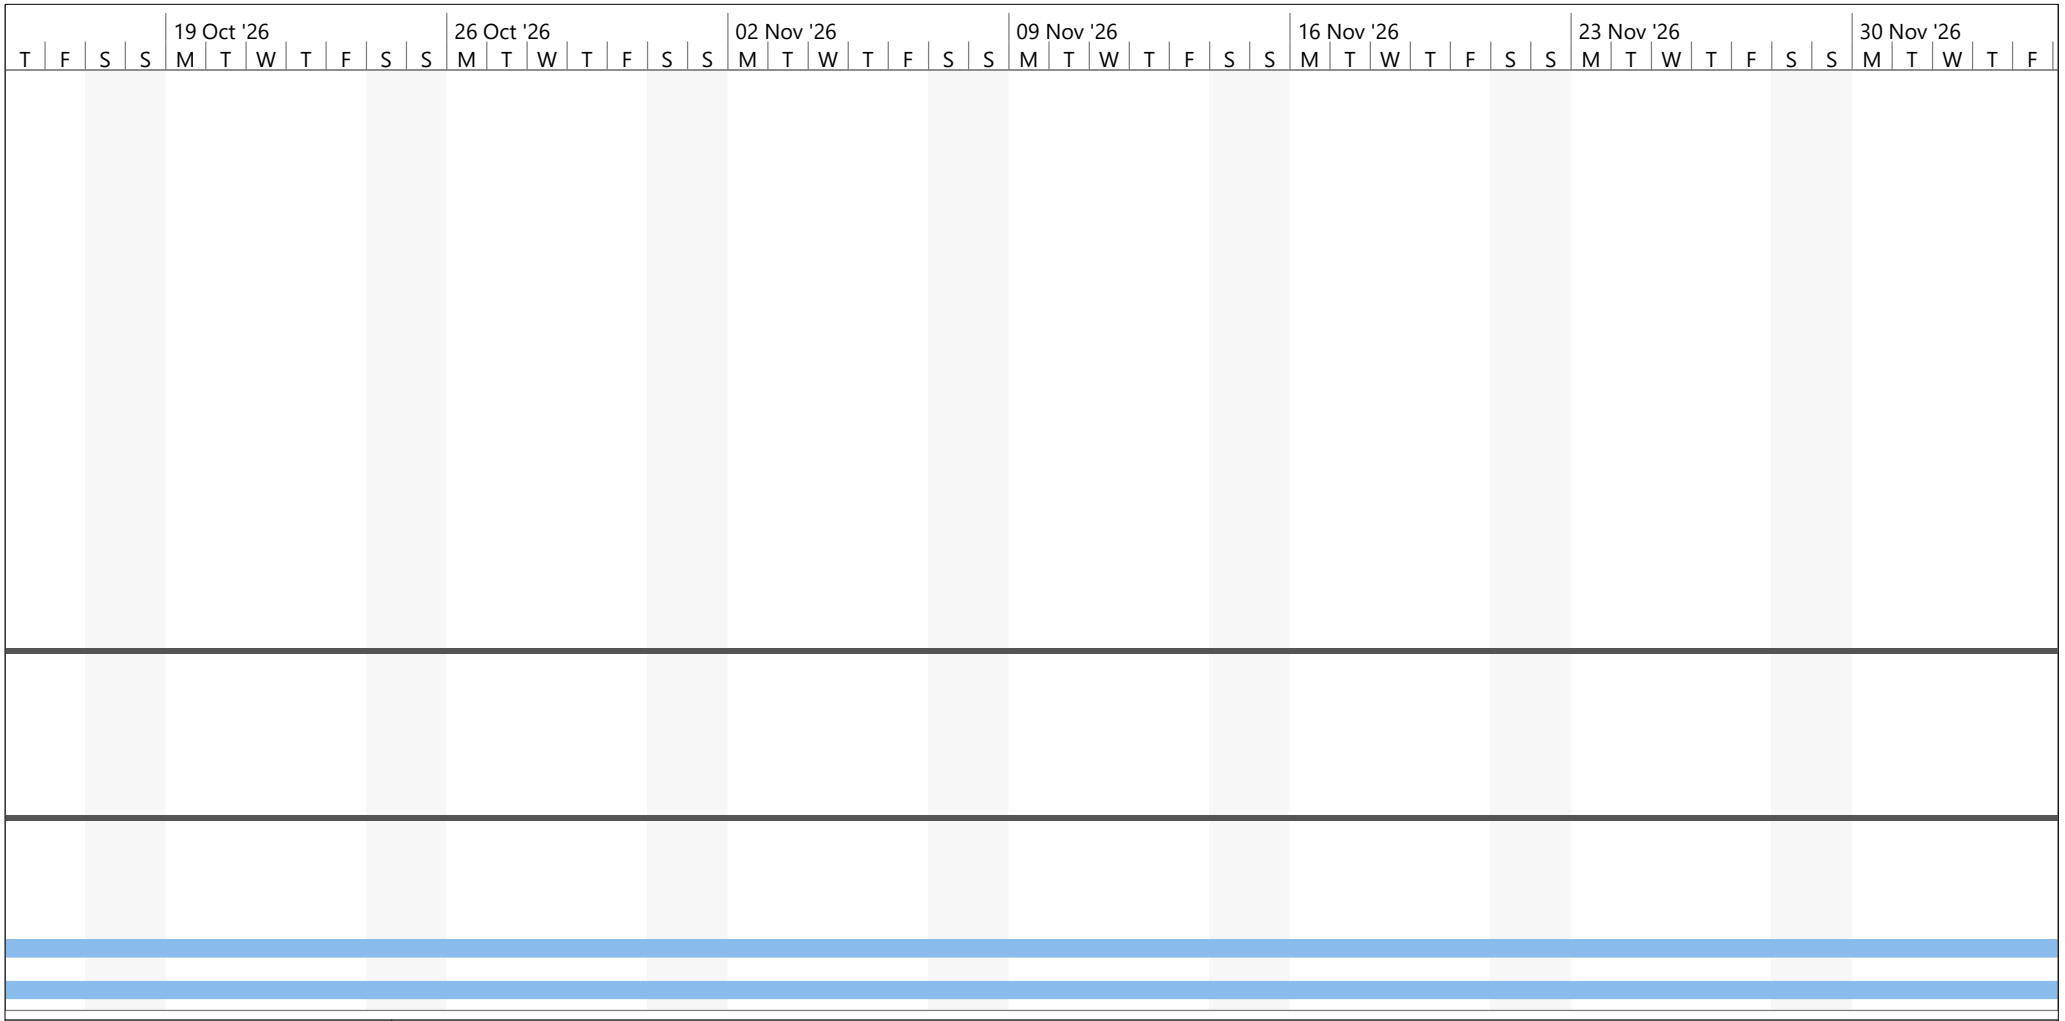


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

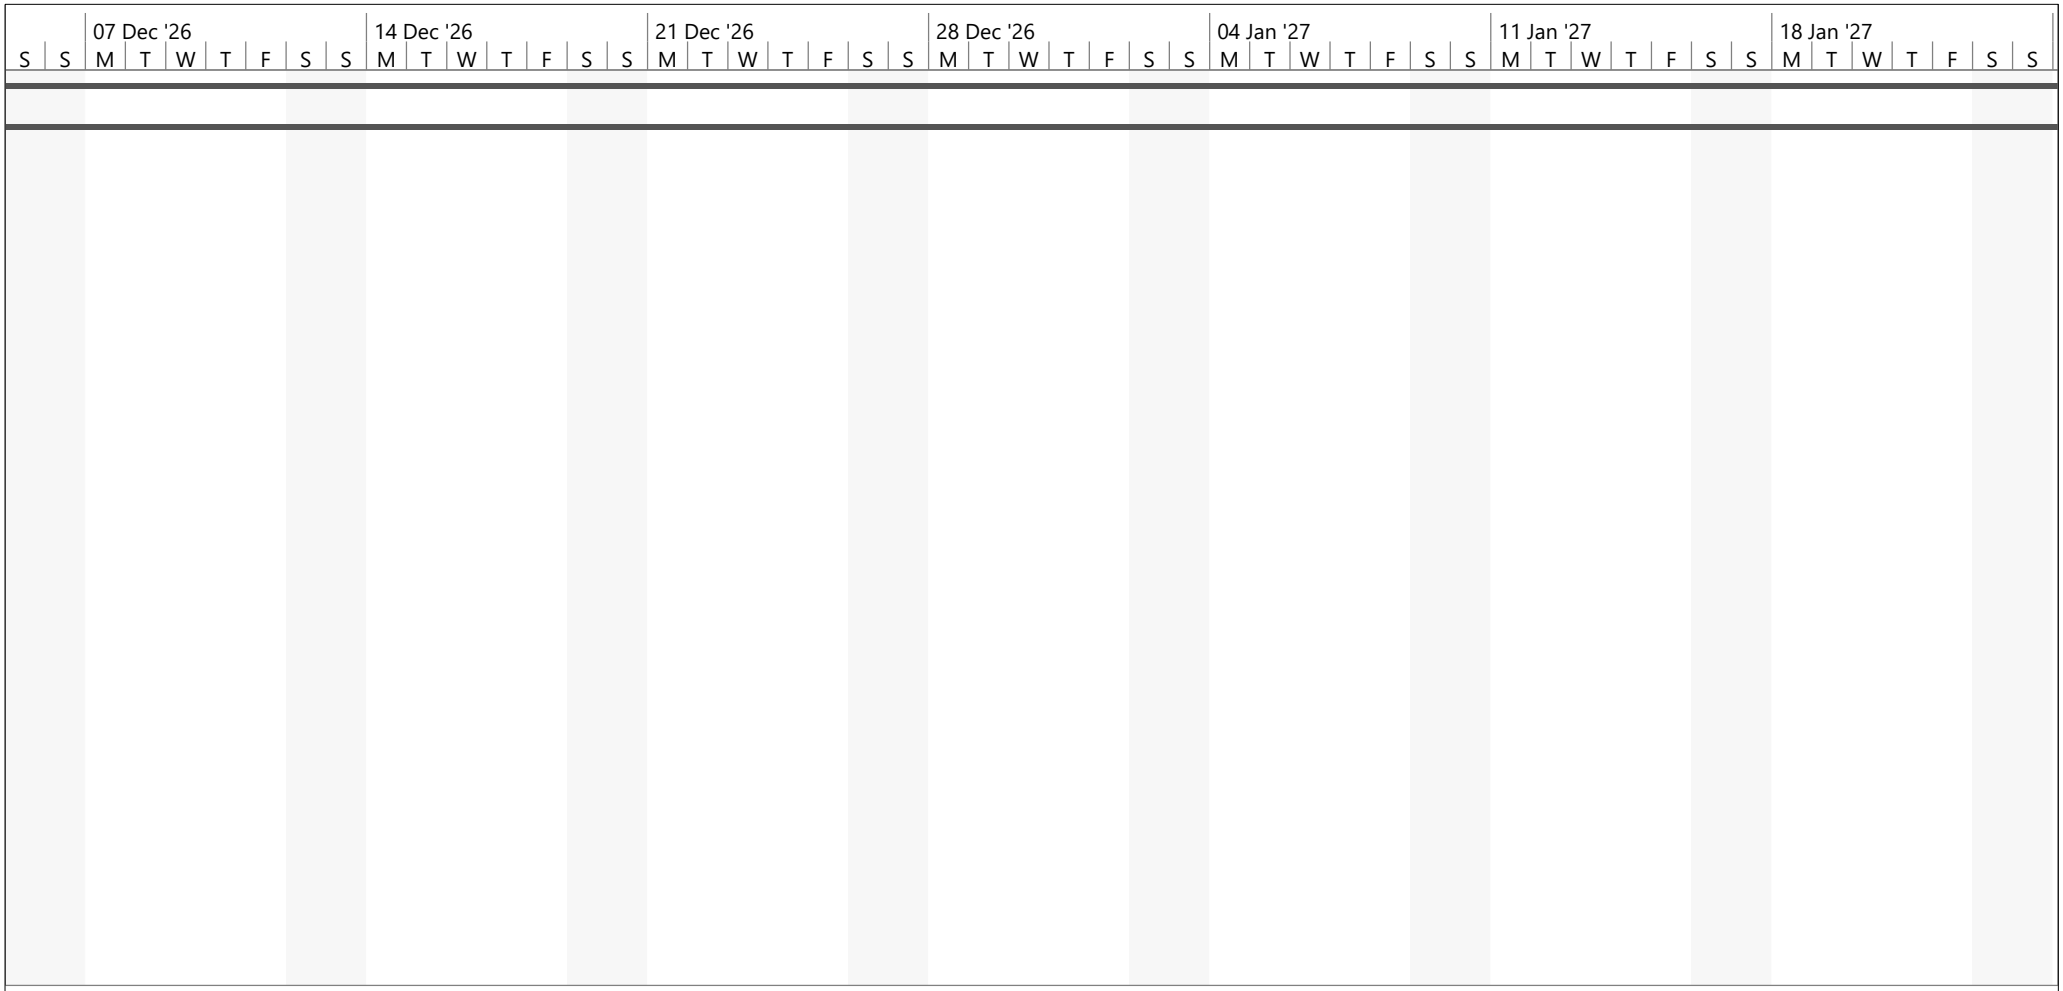


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

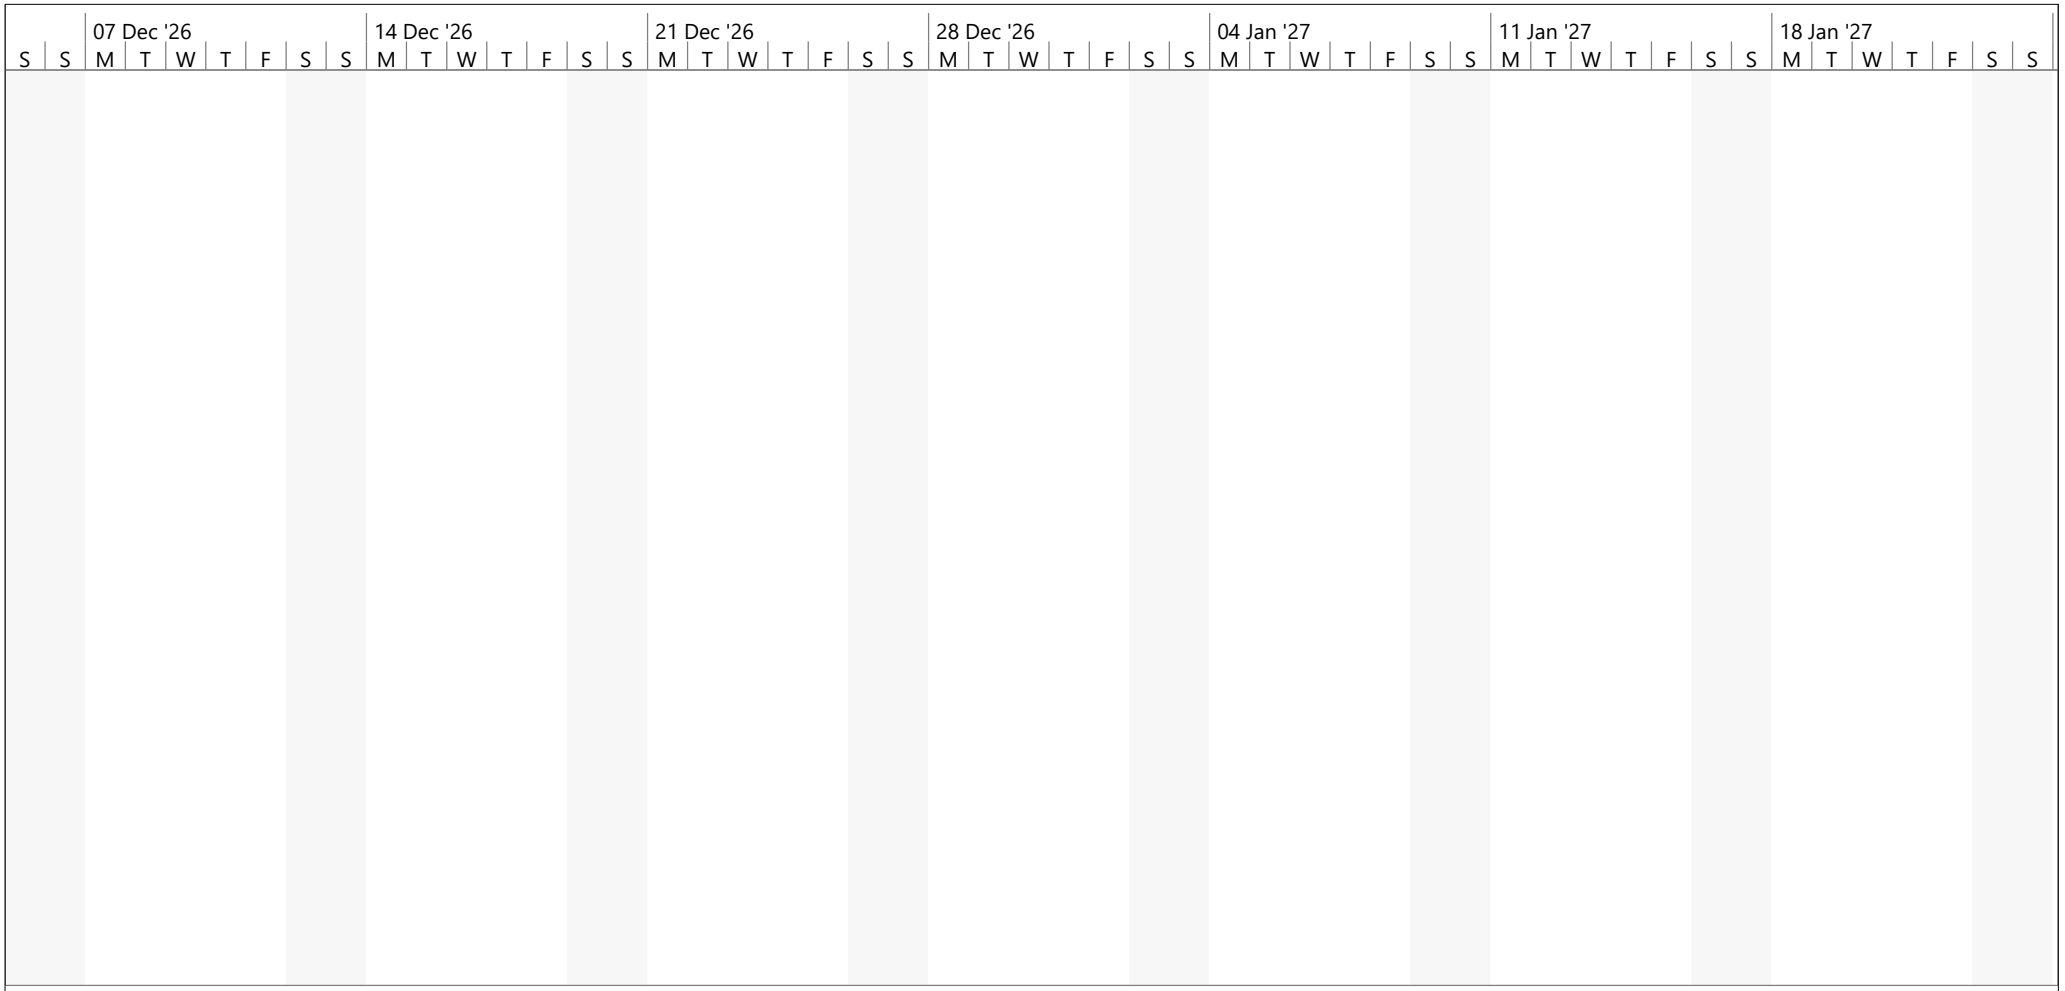


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

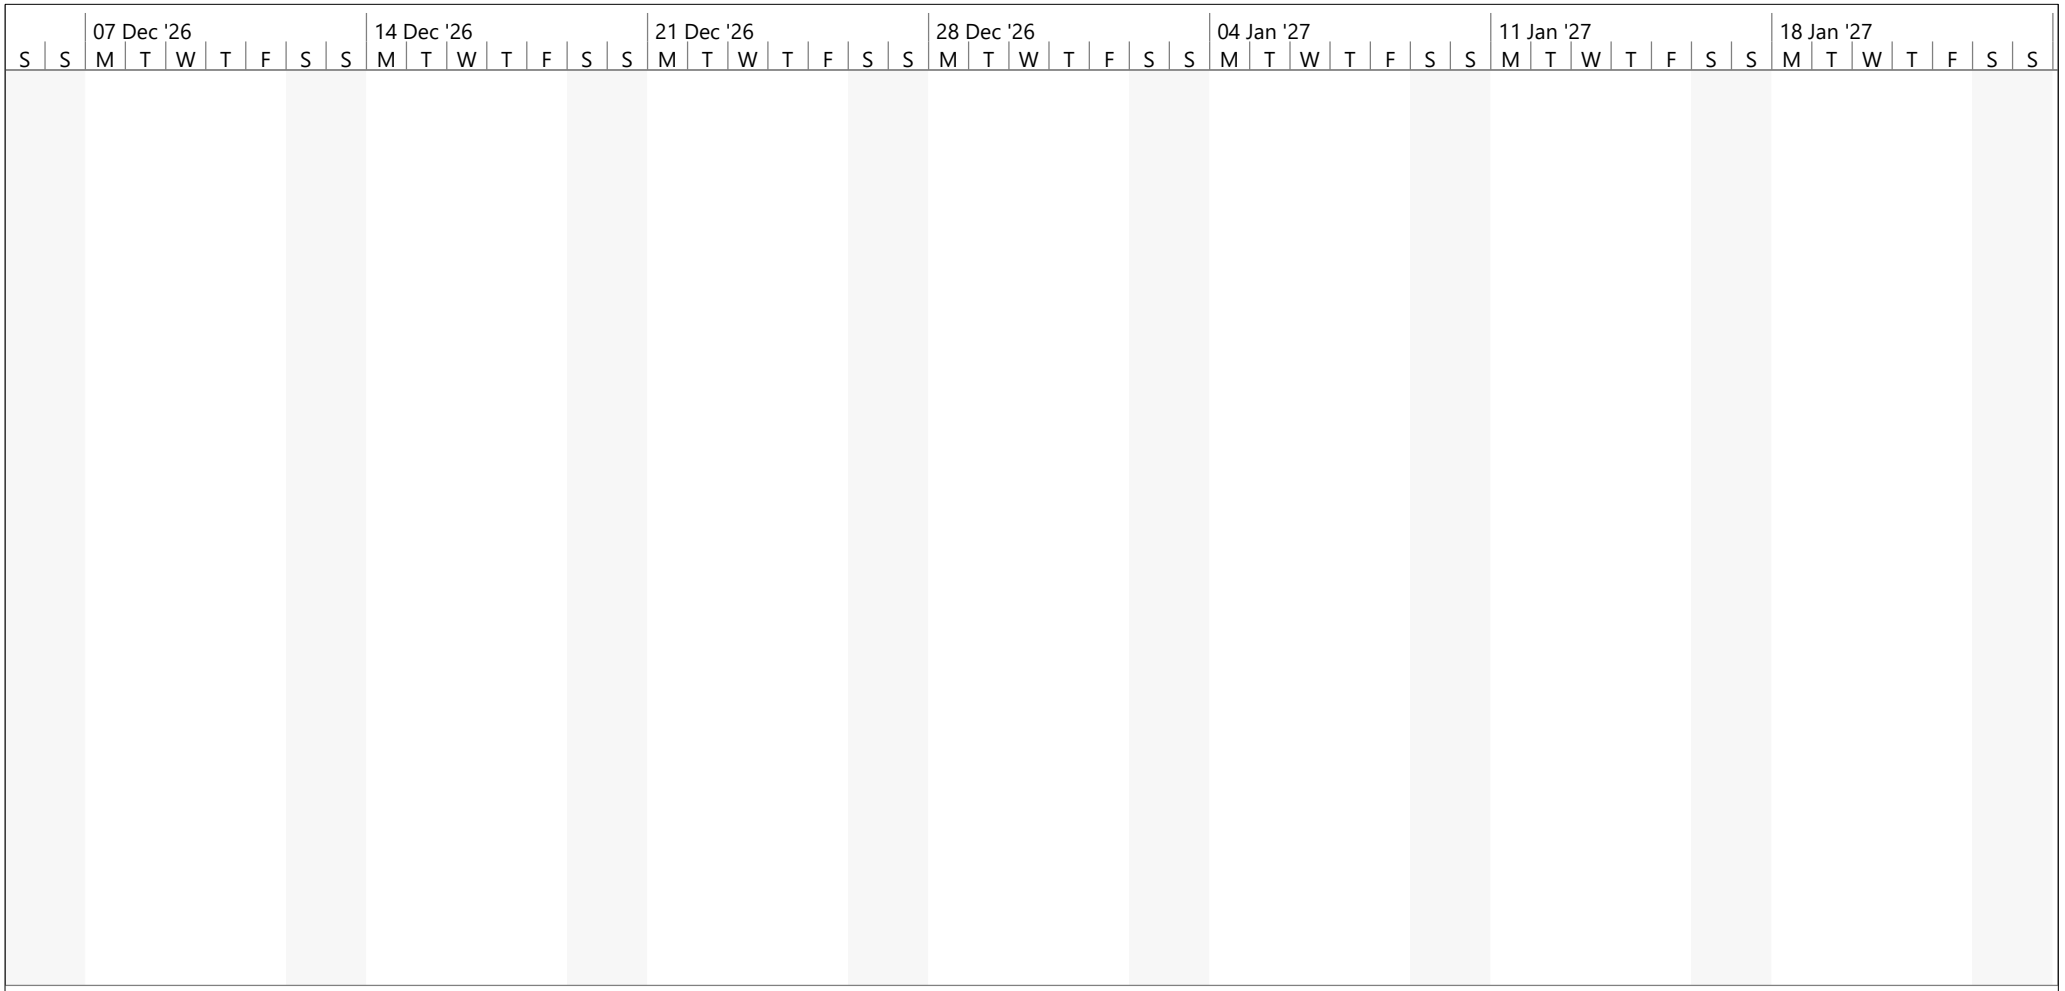

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

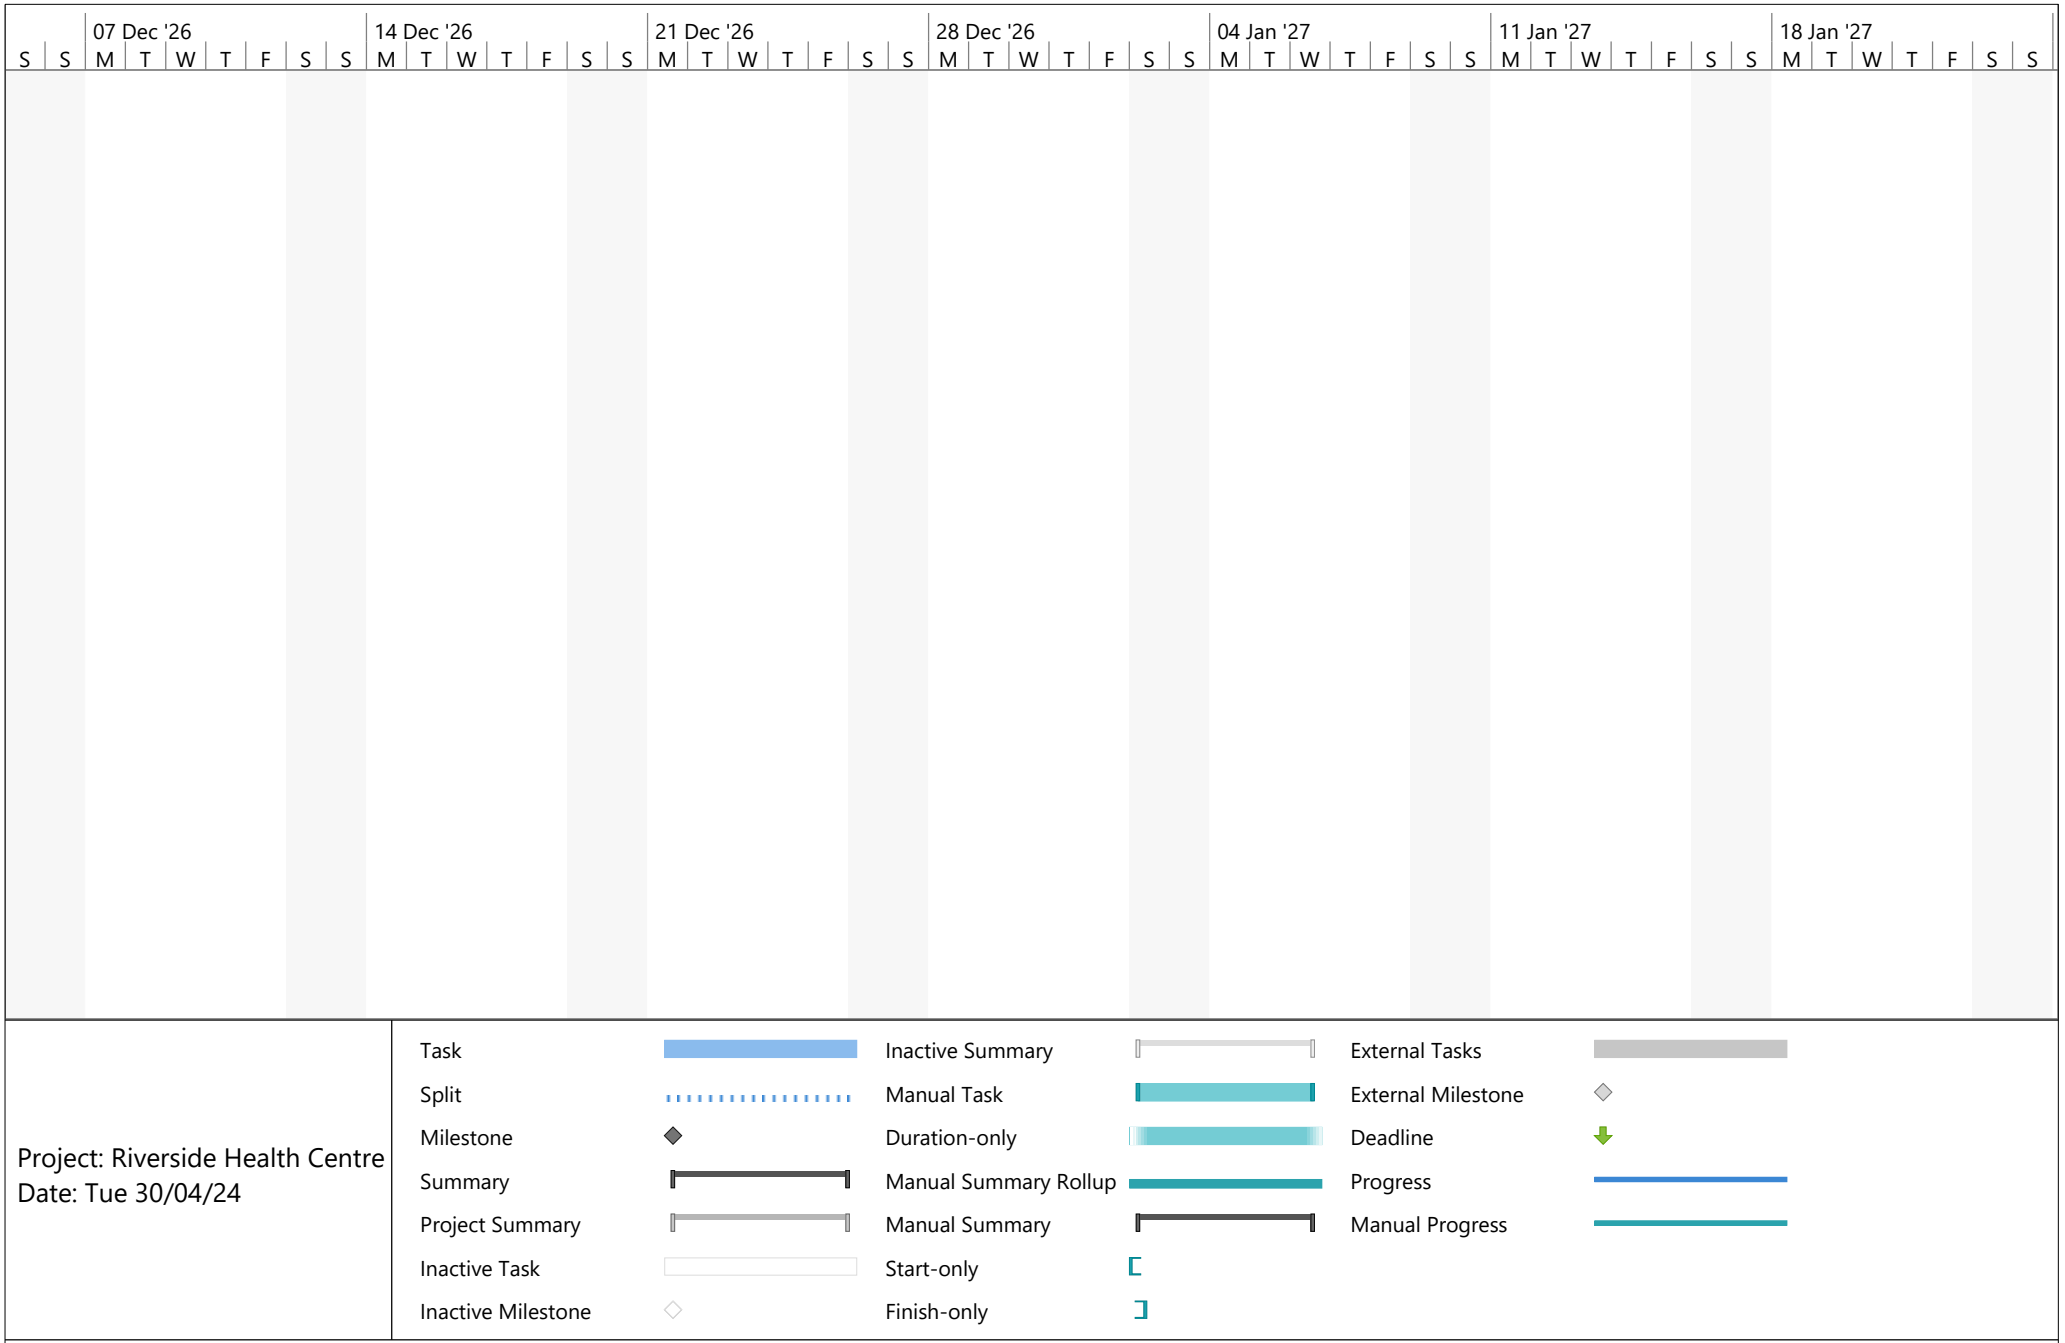

07 Dec '26
14 Dec '26
21 Dec '26
28 Dec '26
04 Jan '27
11 Jan '27
18 Jan '27
S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

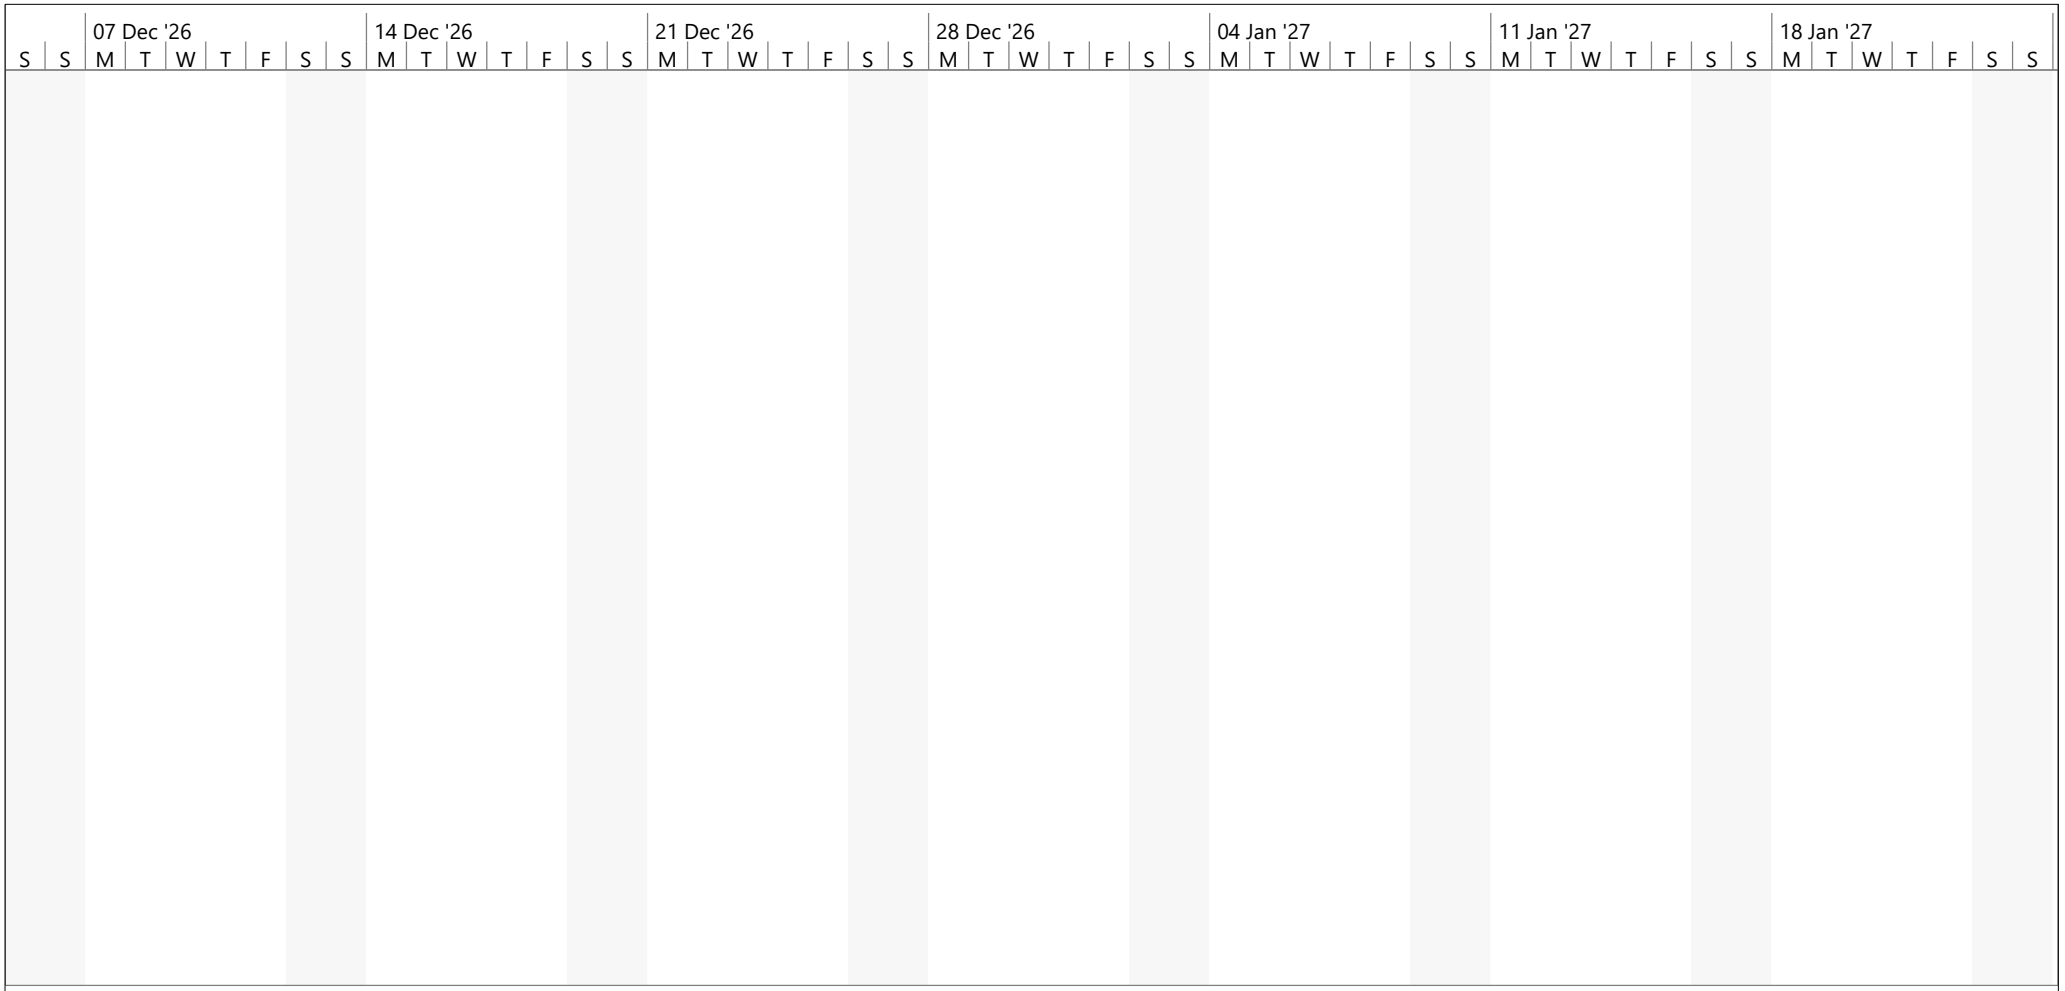

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

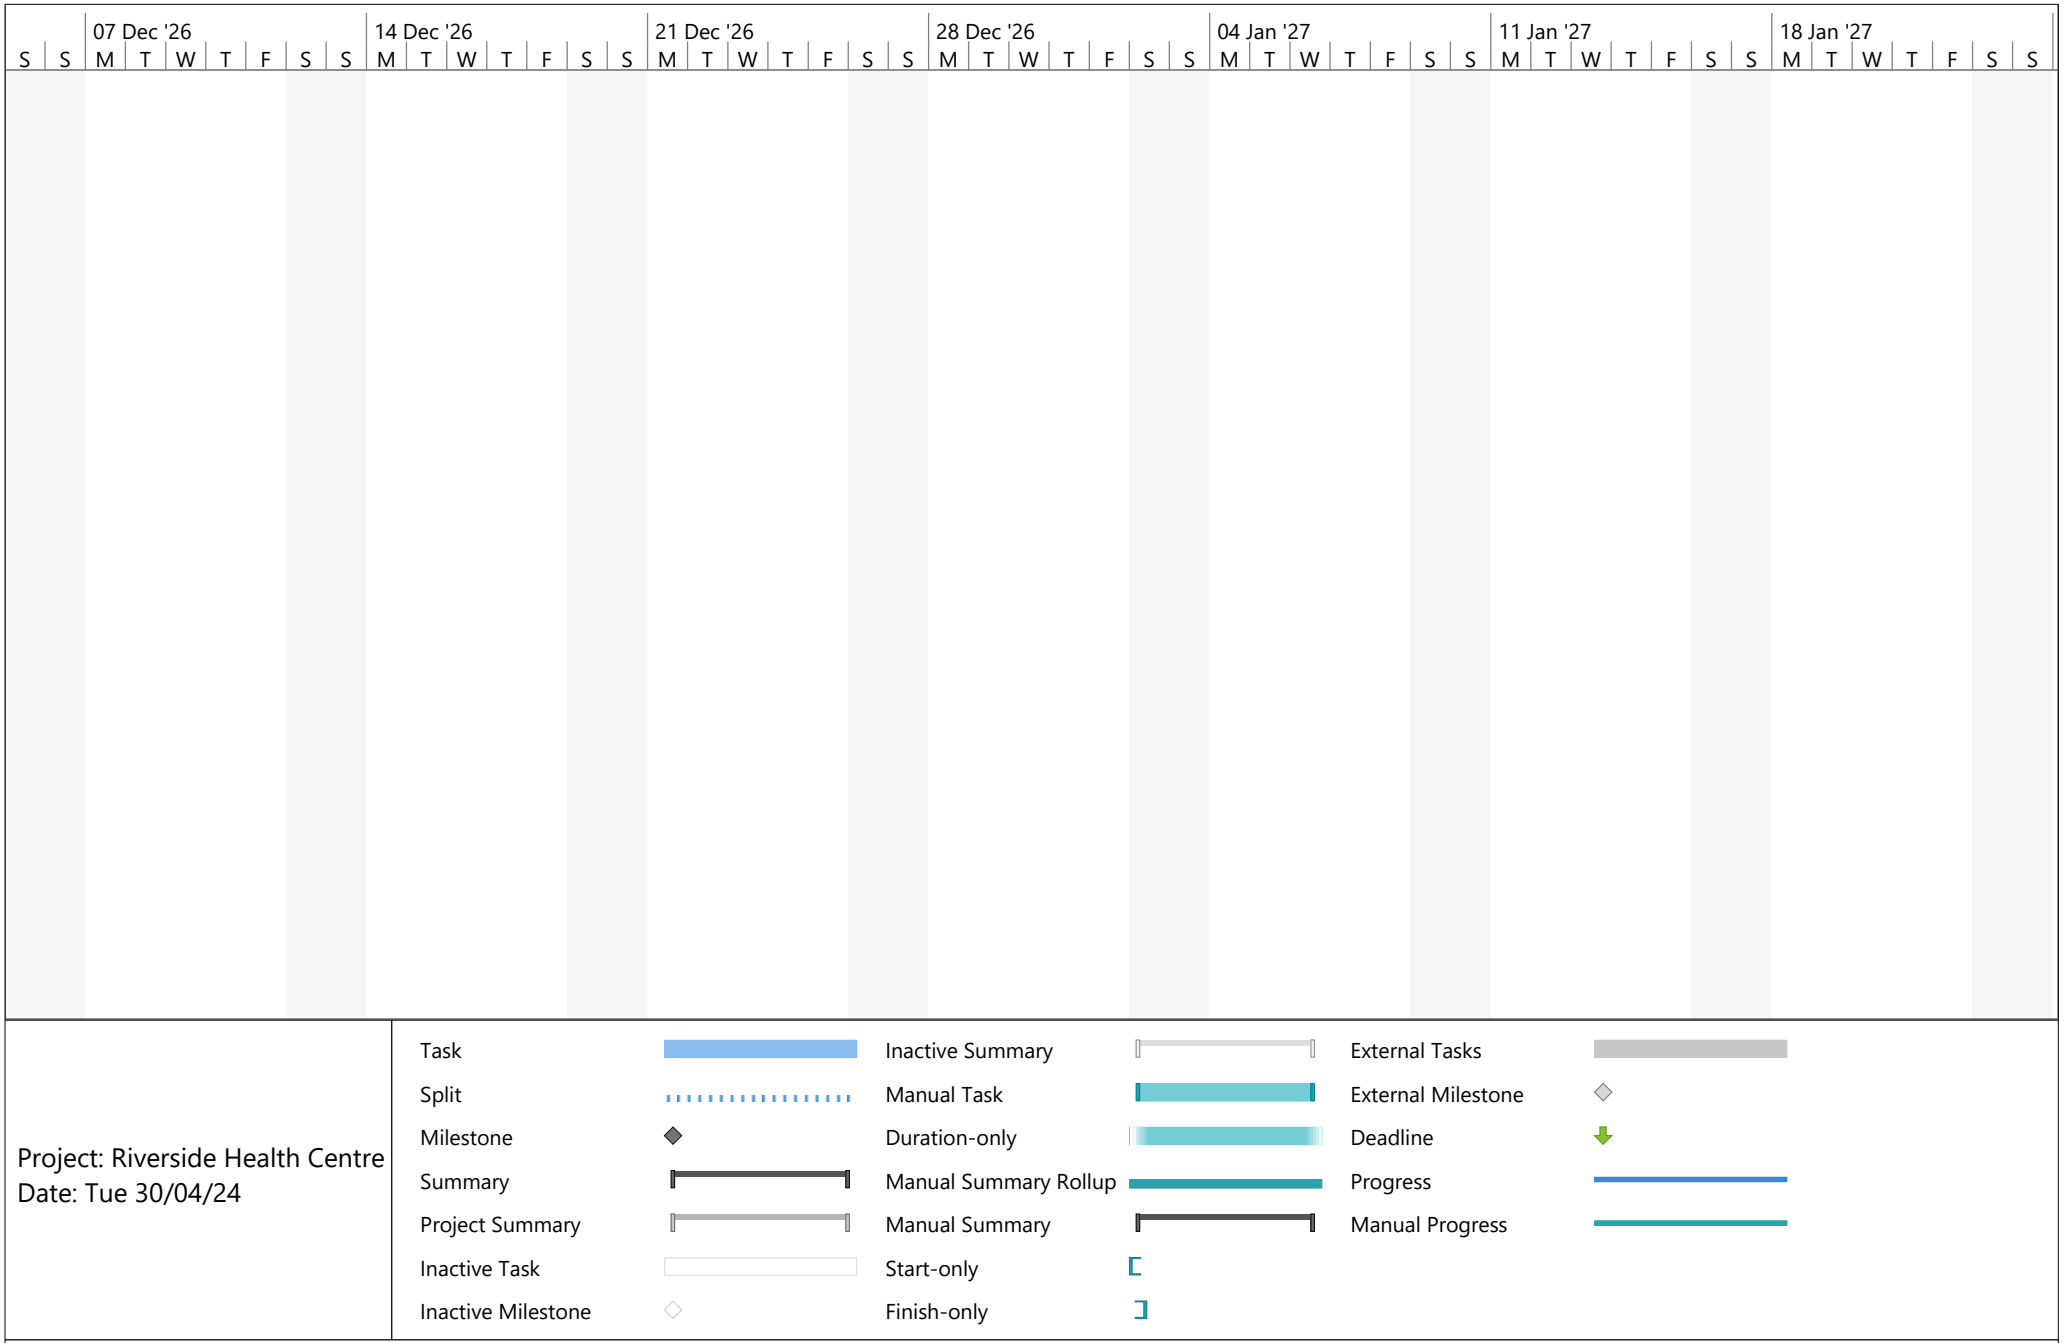
07 Dec '26
14 Dec '26
21 Dec '26
28 Dec '26
04 Jan '27
11 Jan '27
18 Jan '27
S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

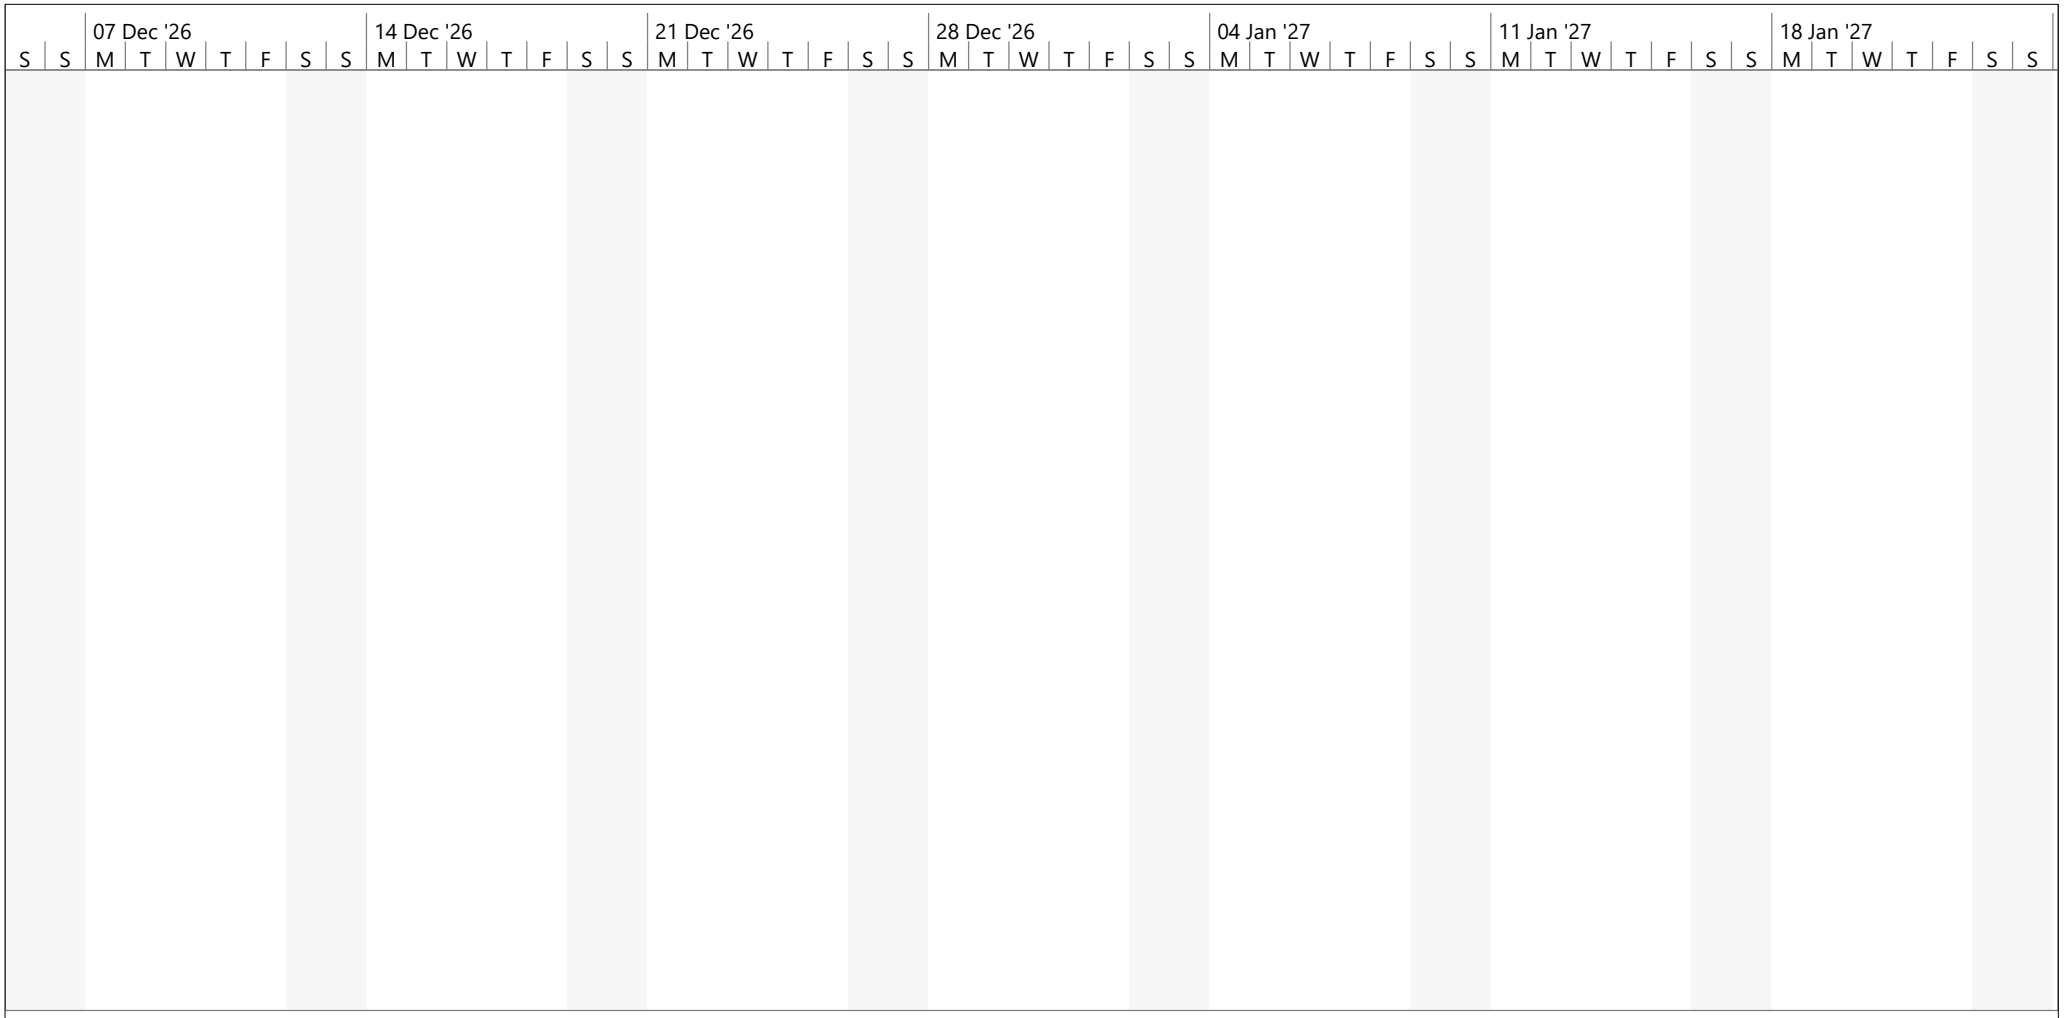


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

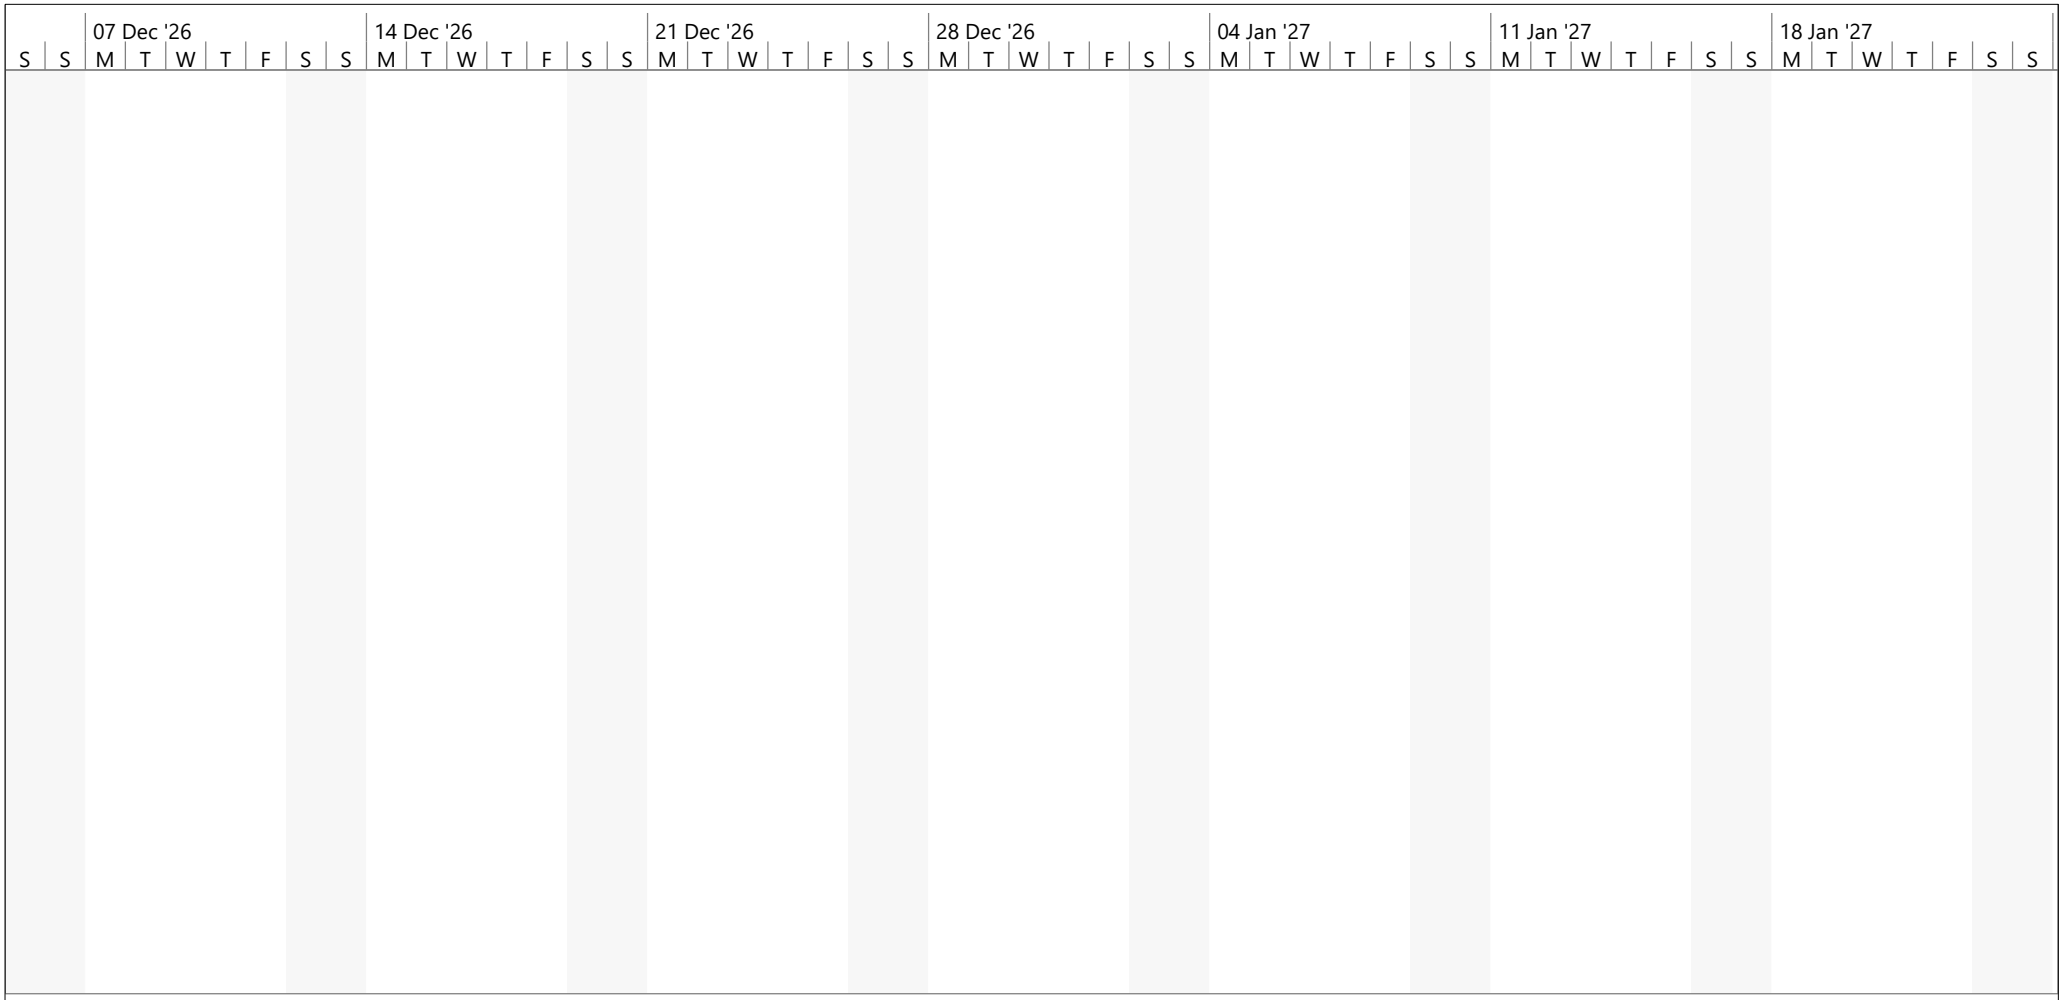


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

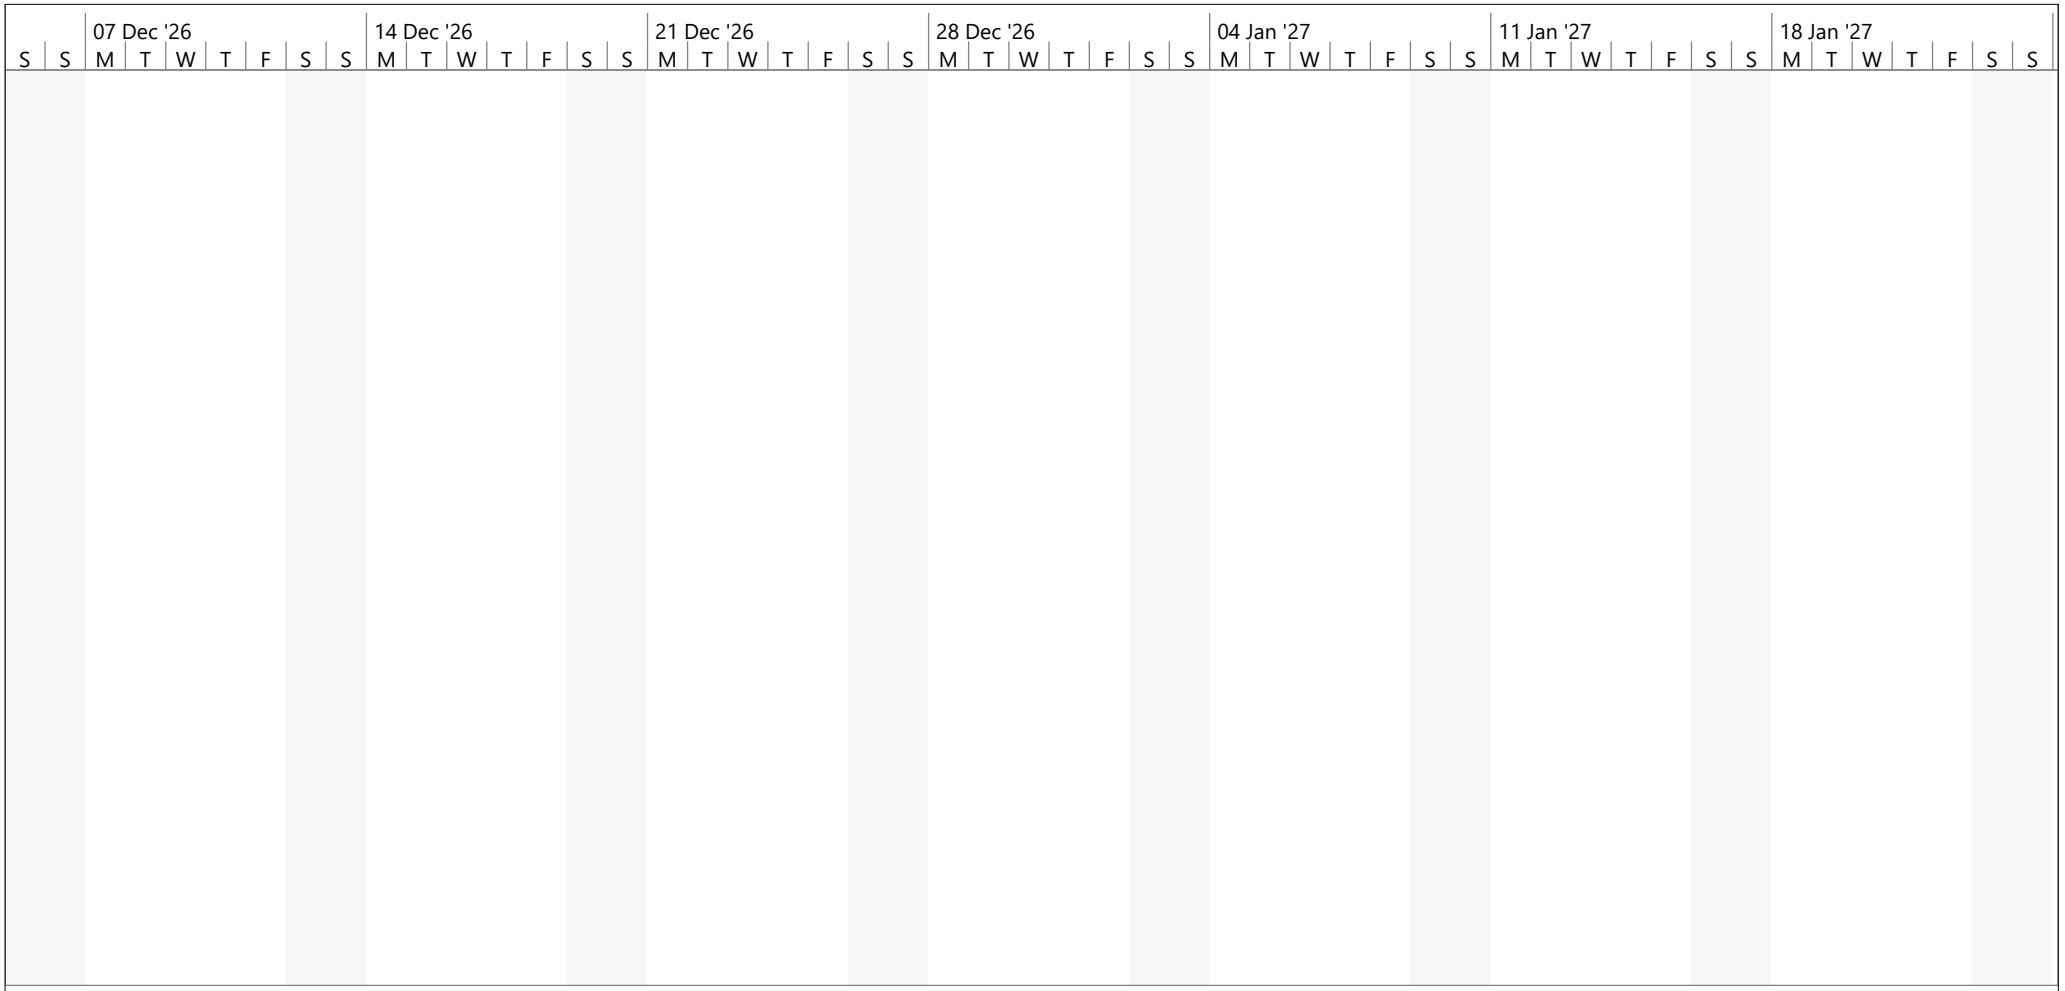

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

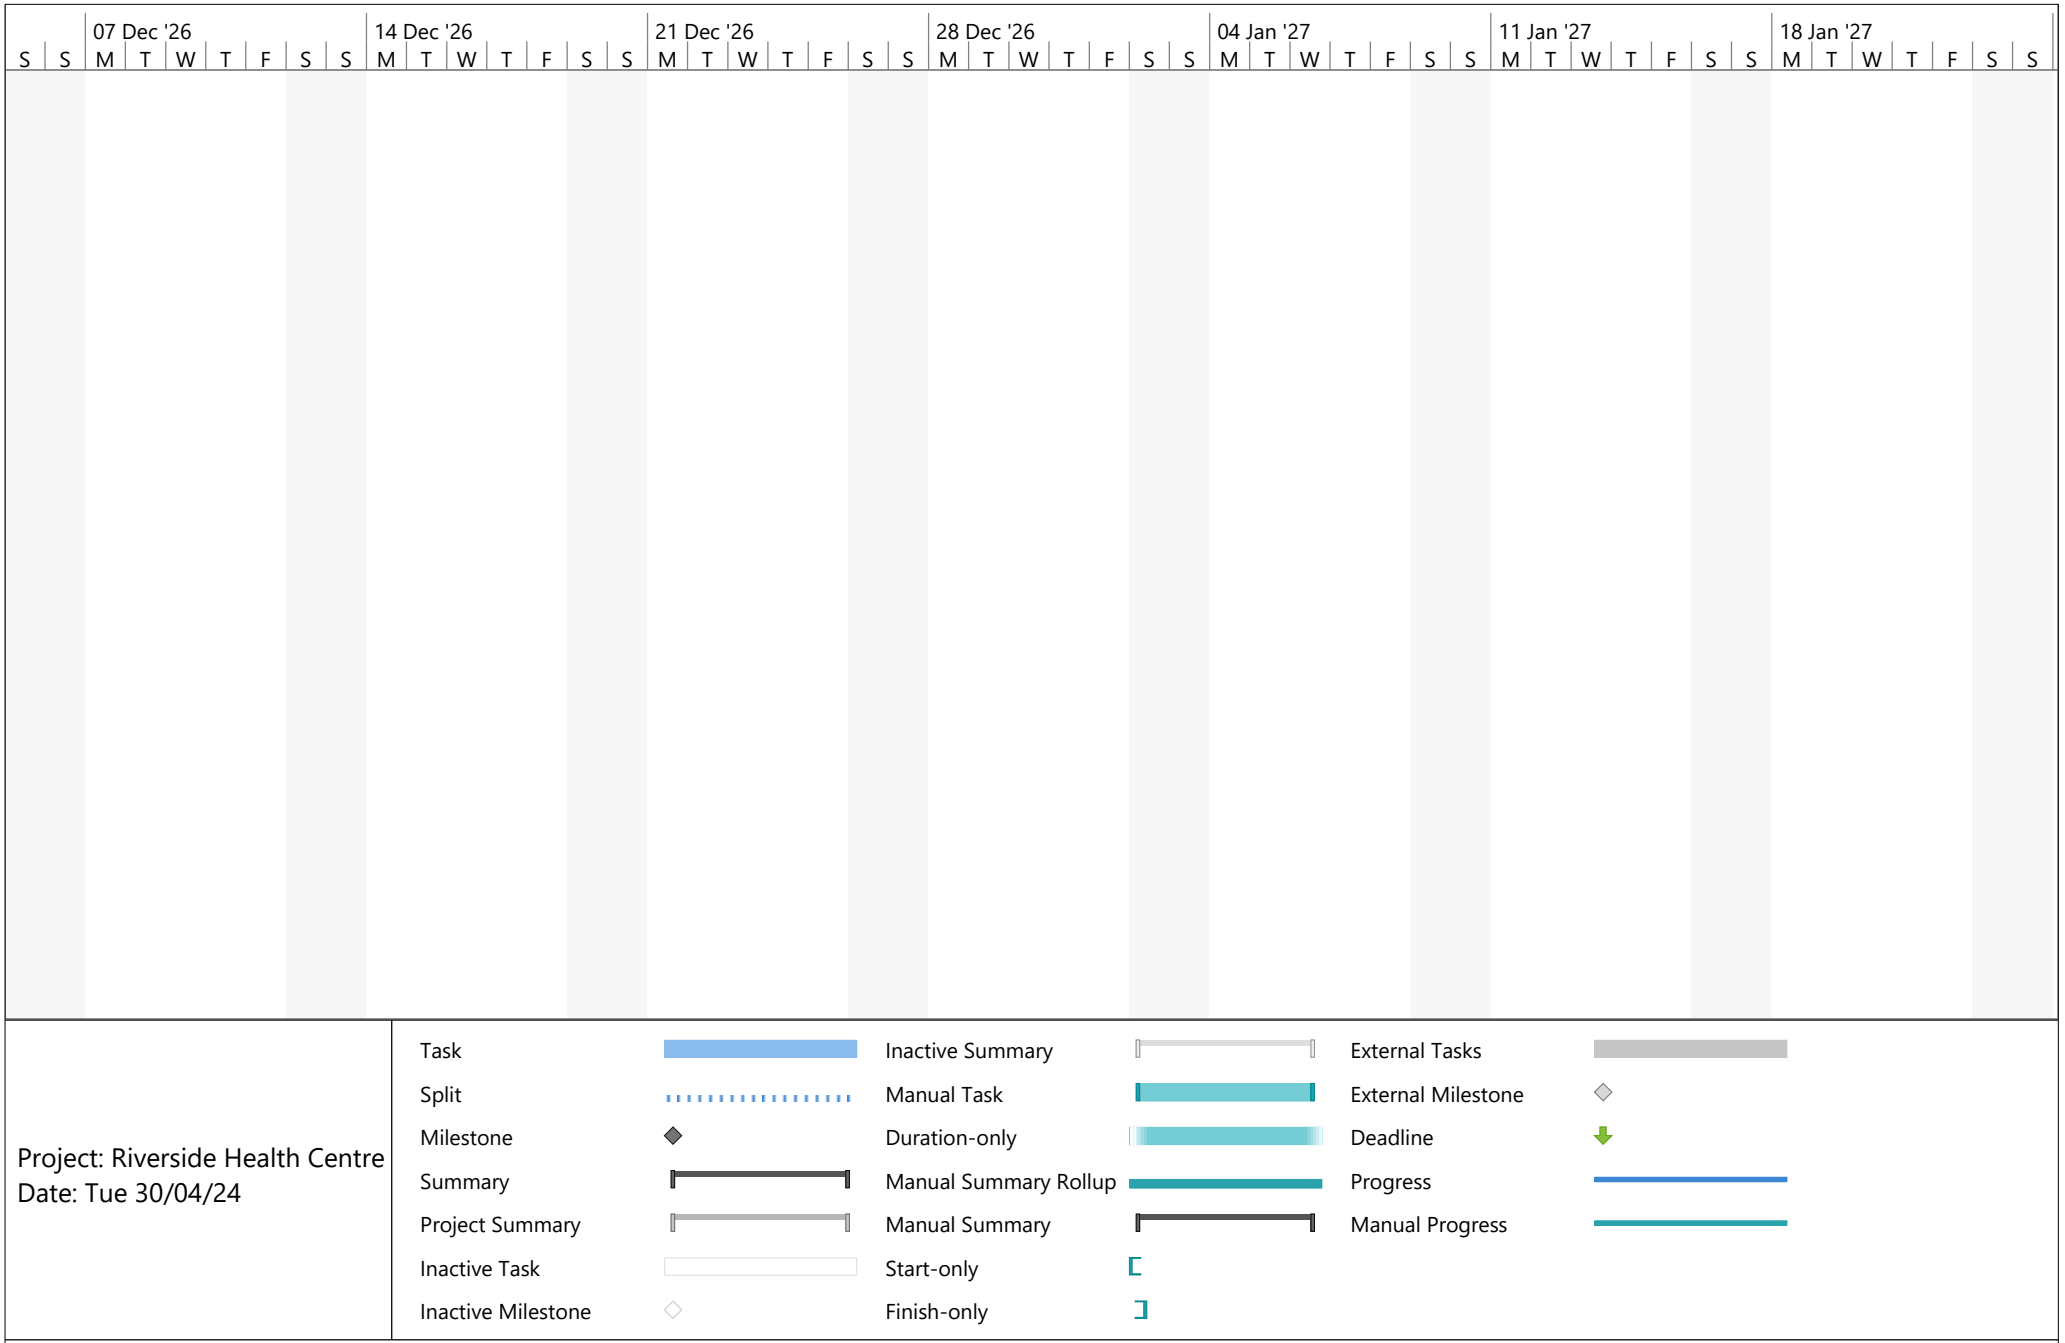
07 Dec '26
14 Dec '26
21 Dec '26
28 Dec '26
04 Jan '27
11 Jan '27
18 Jan '27
S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

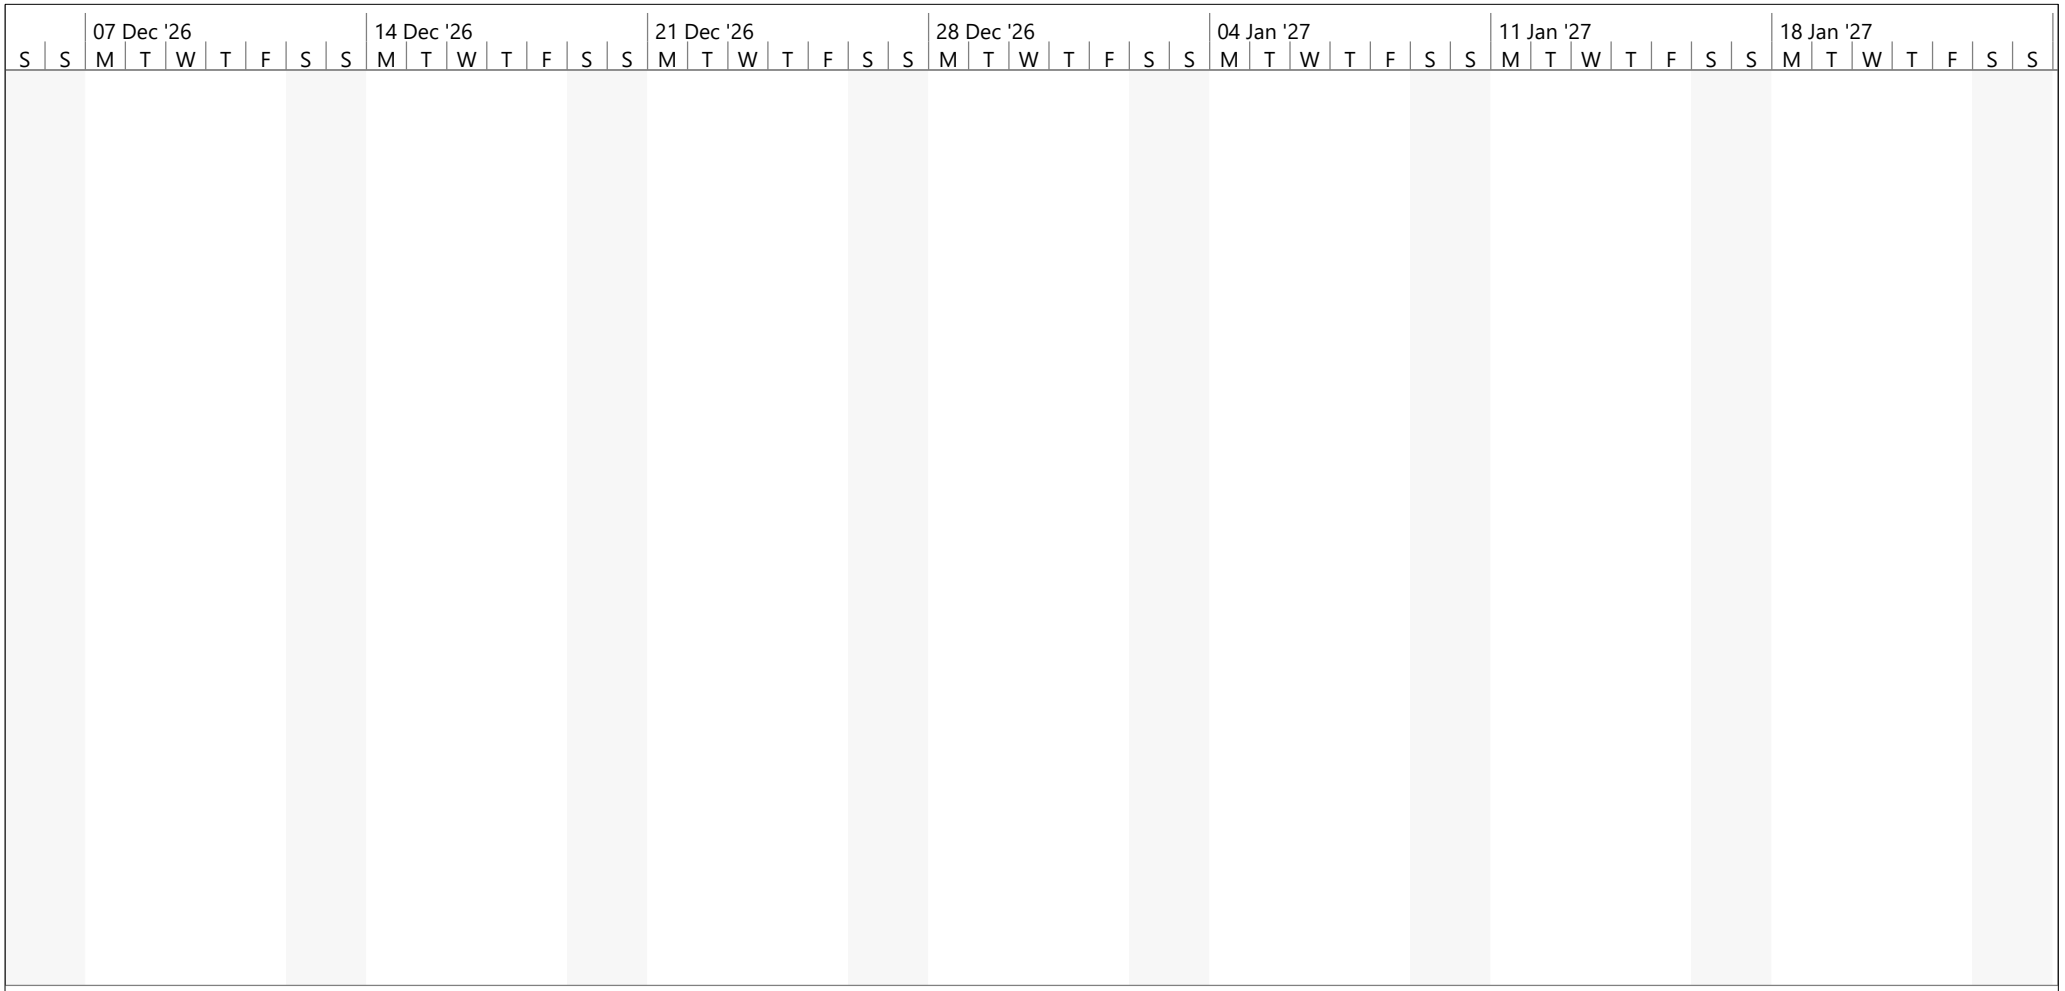


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

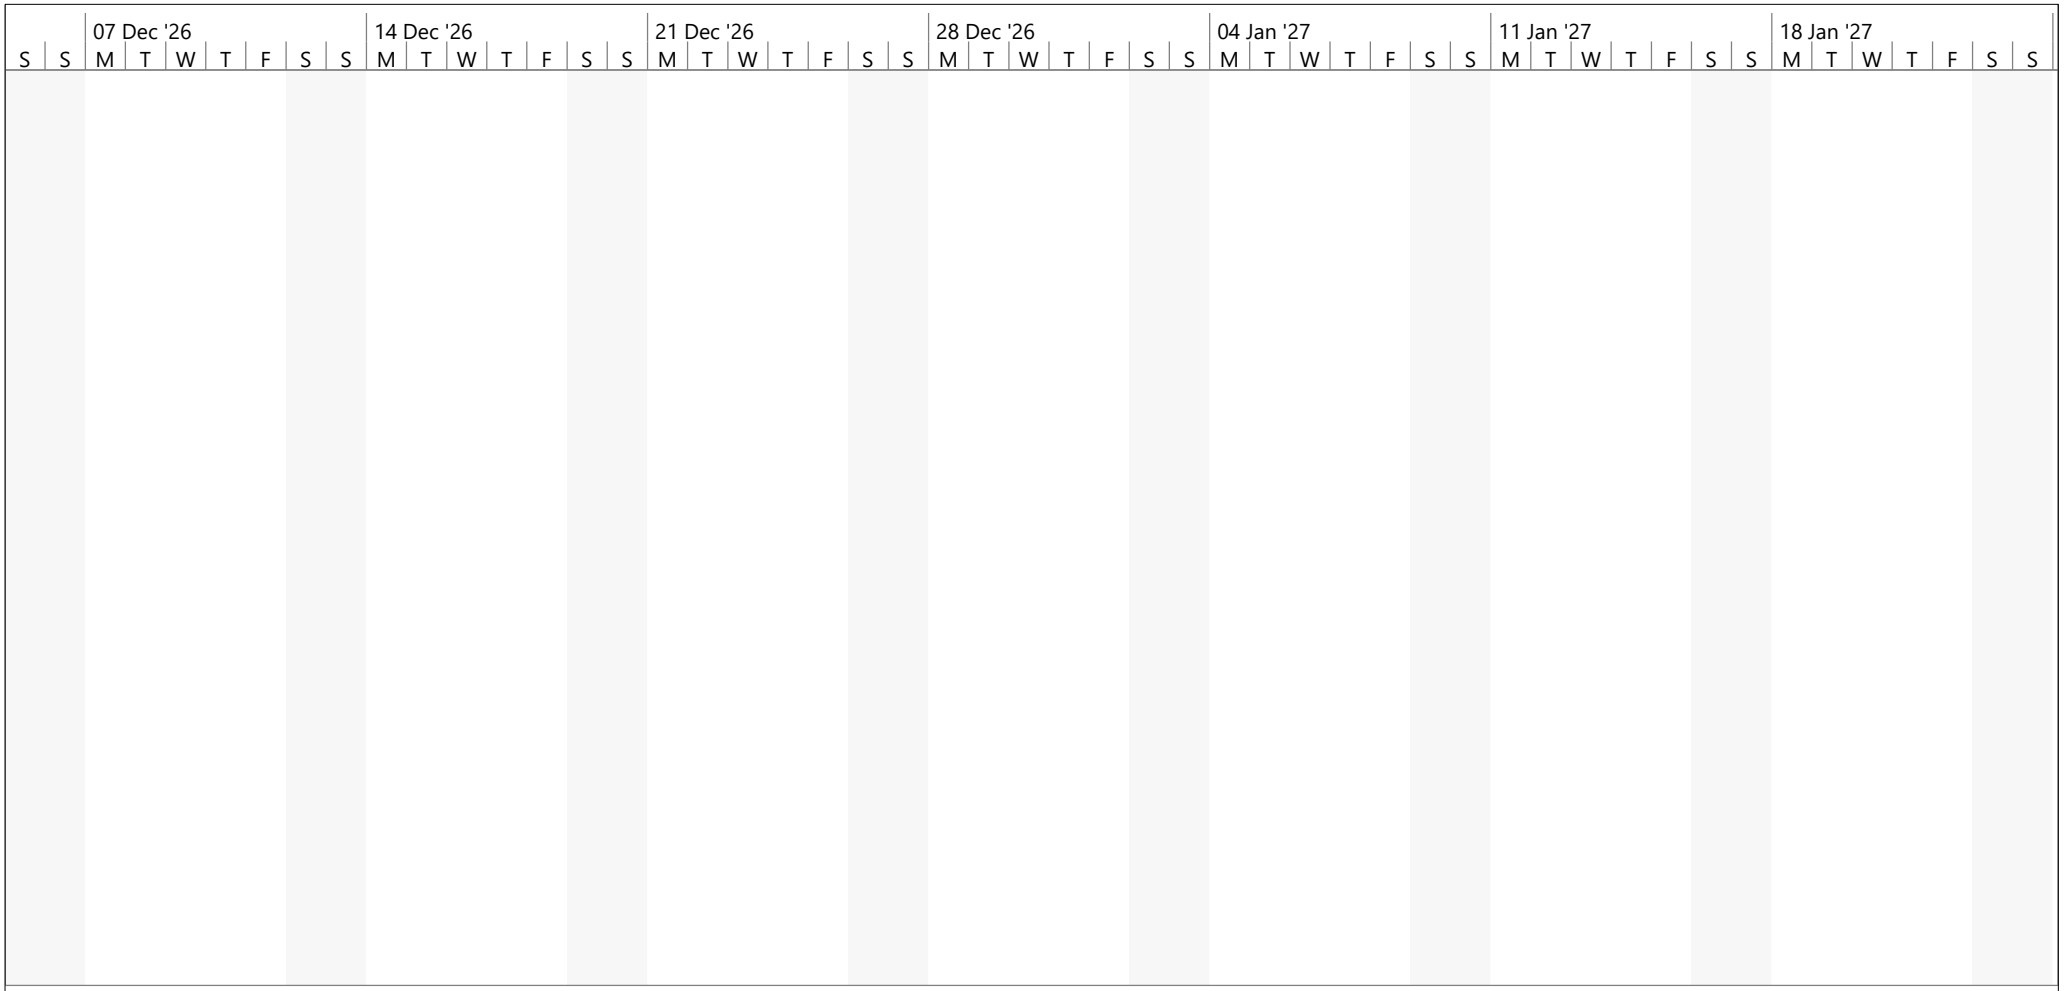


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

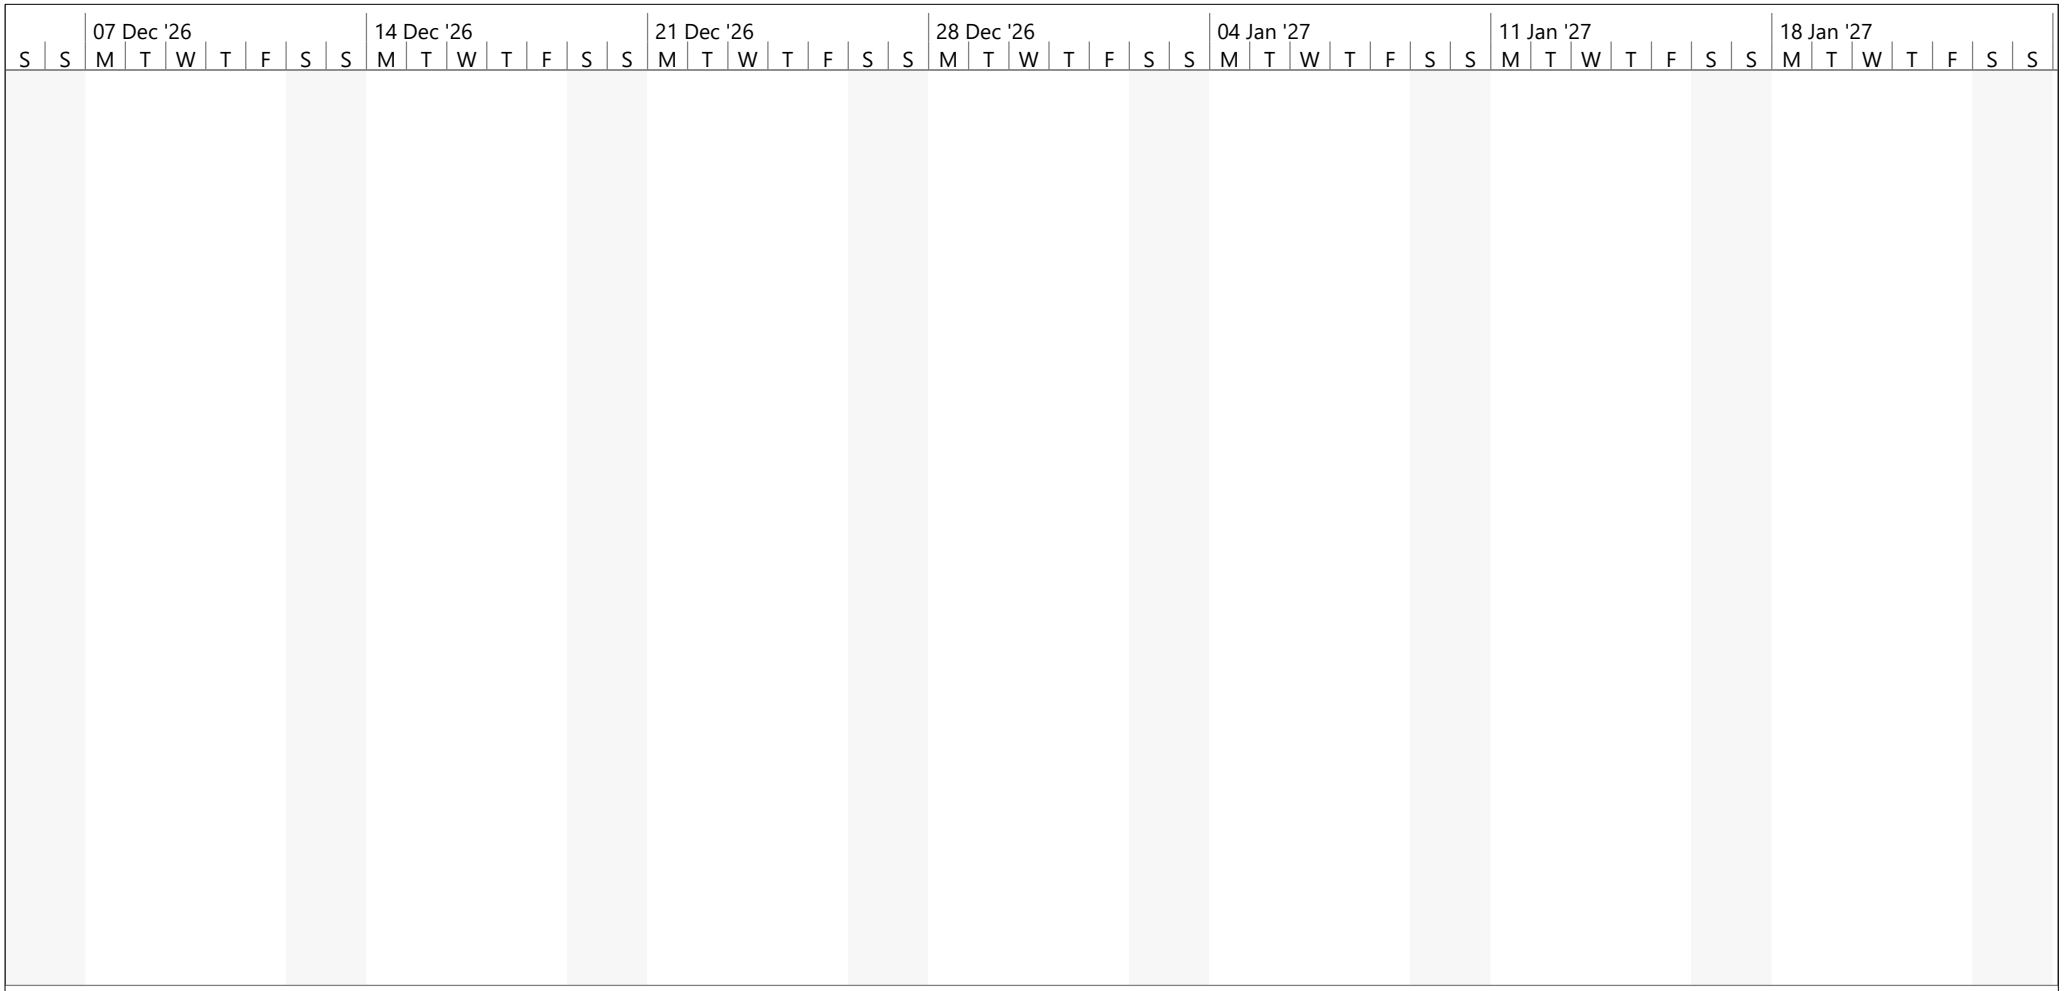


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

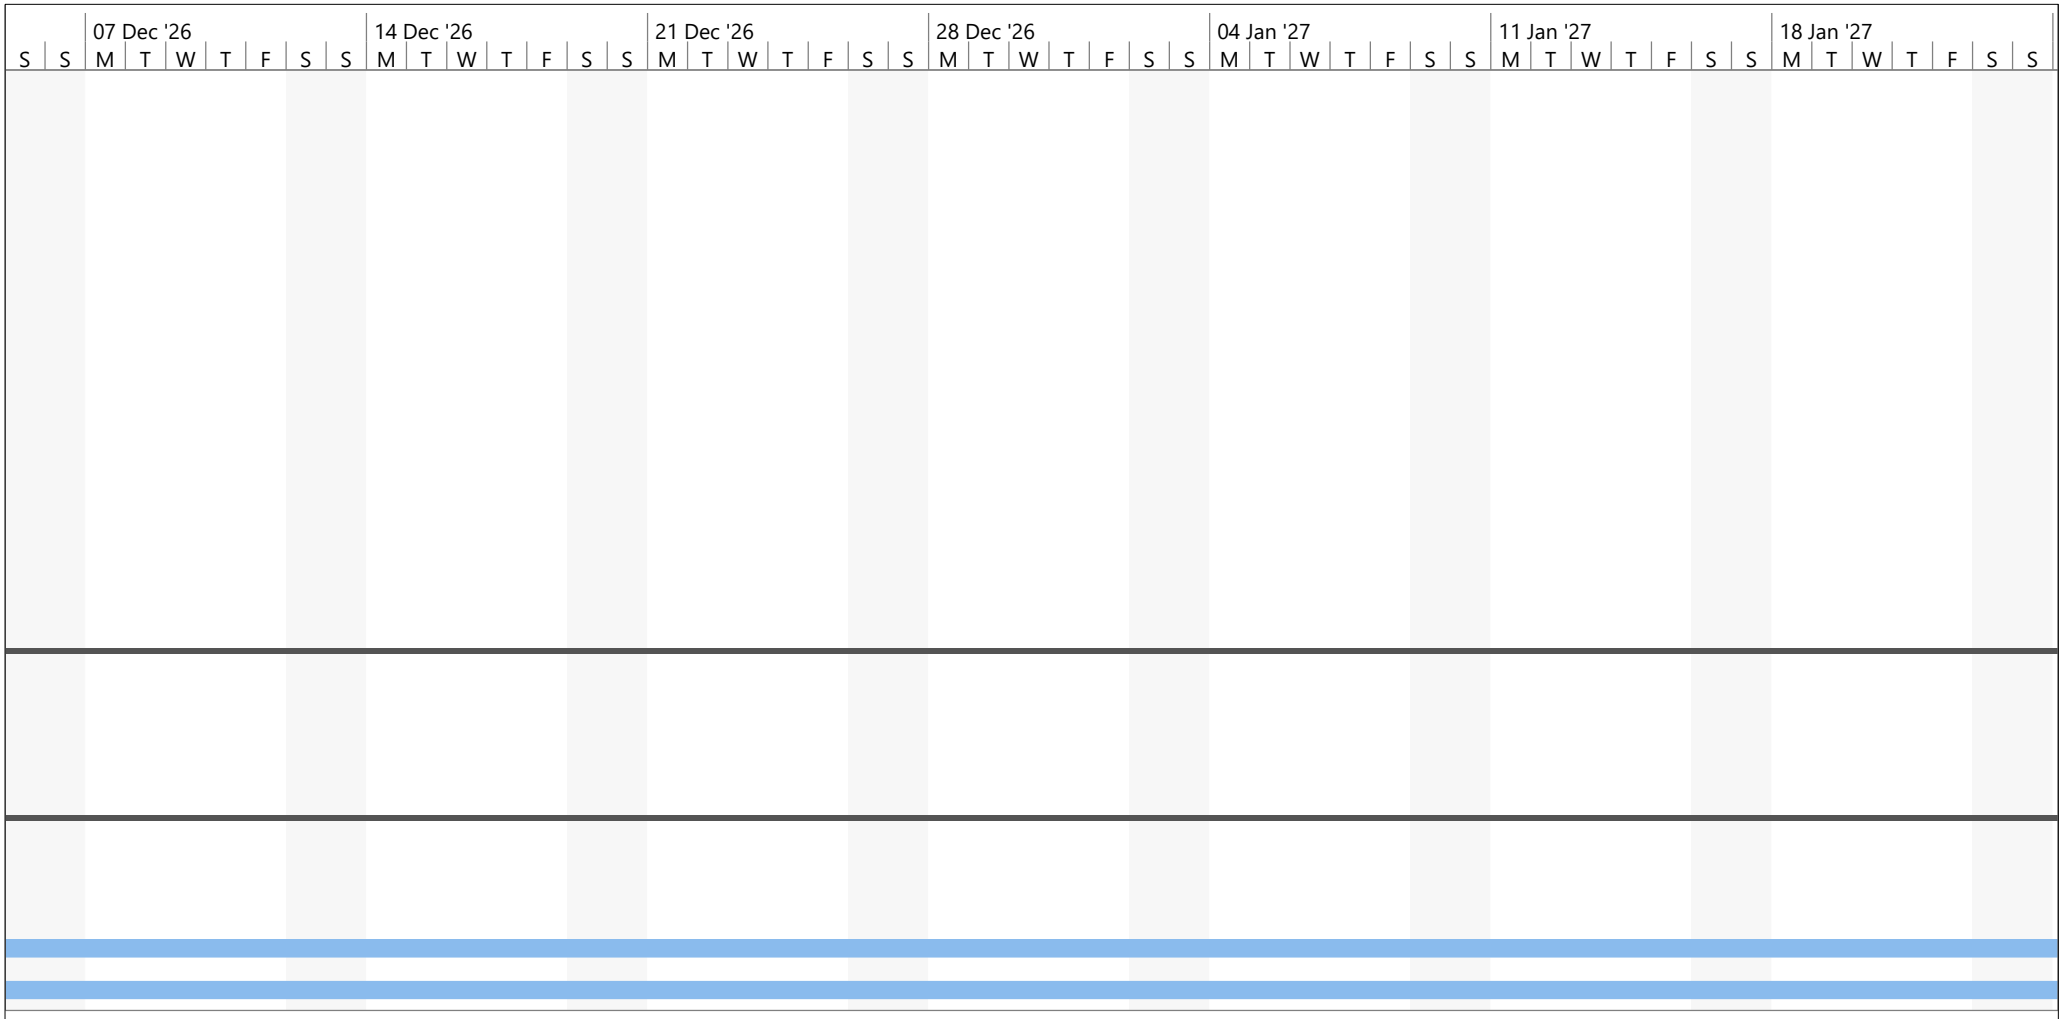


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

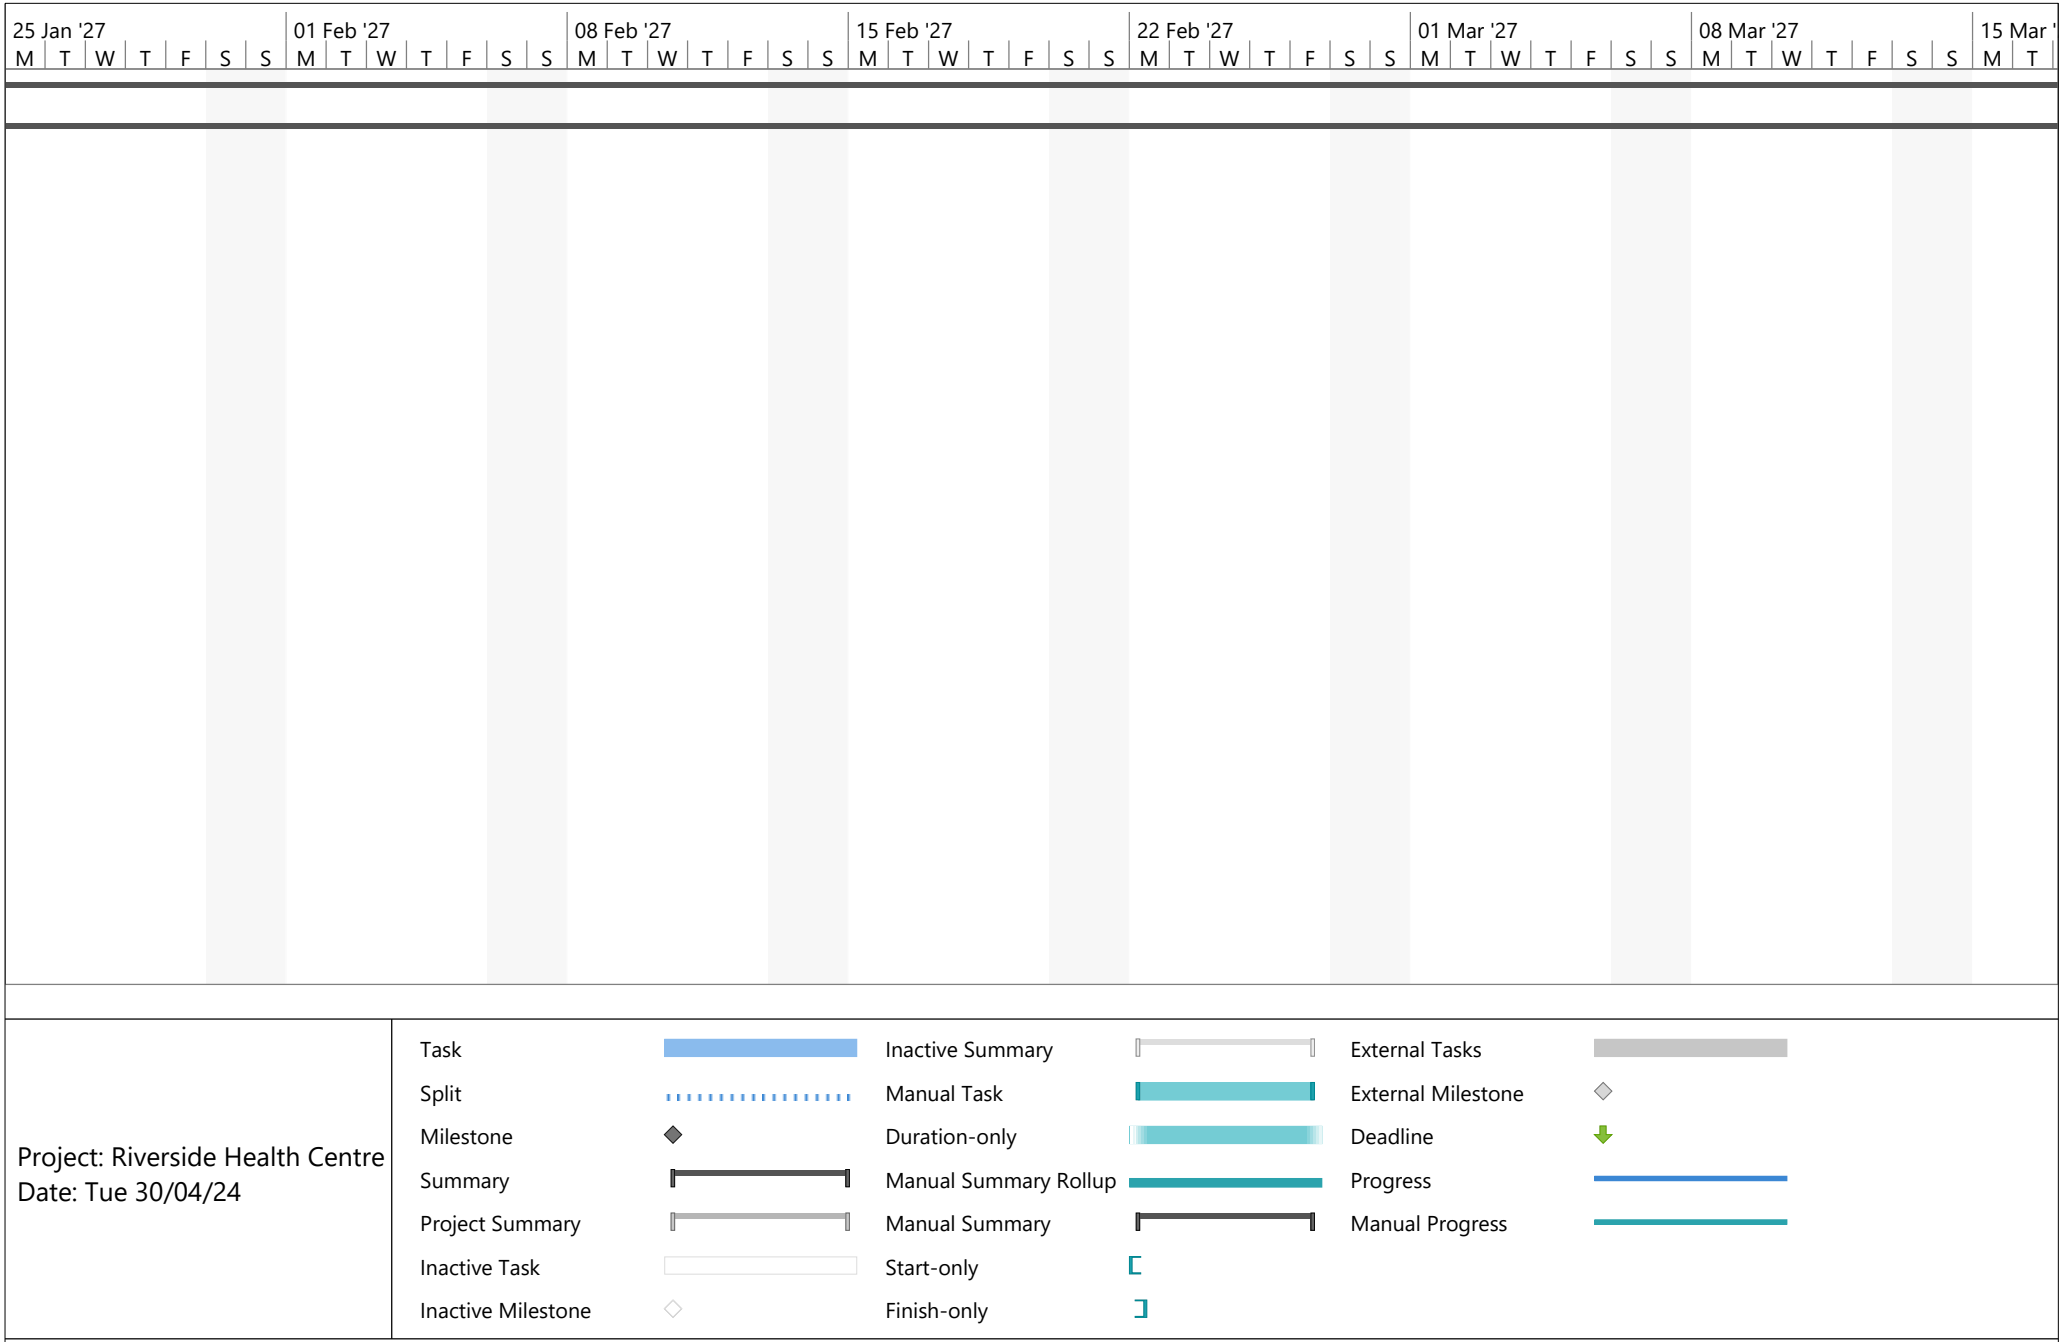


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

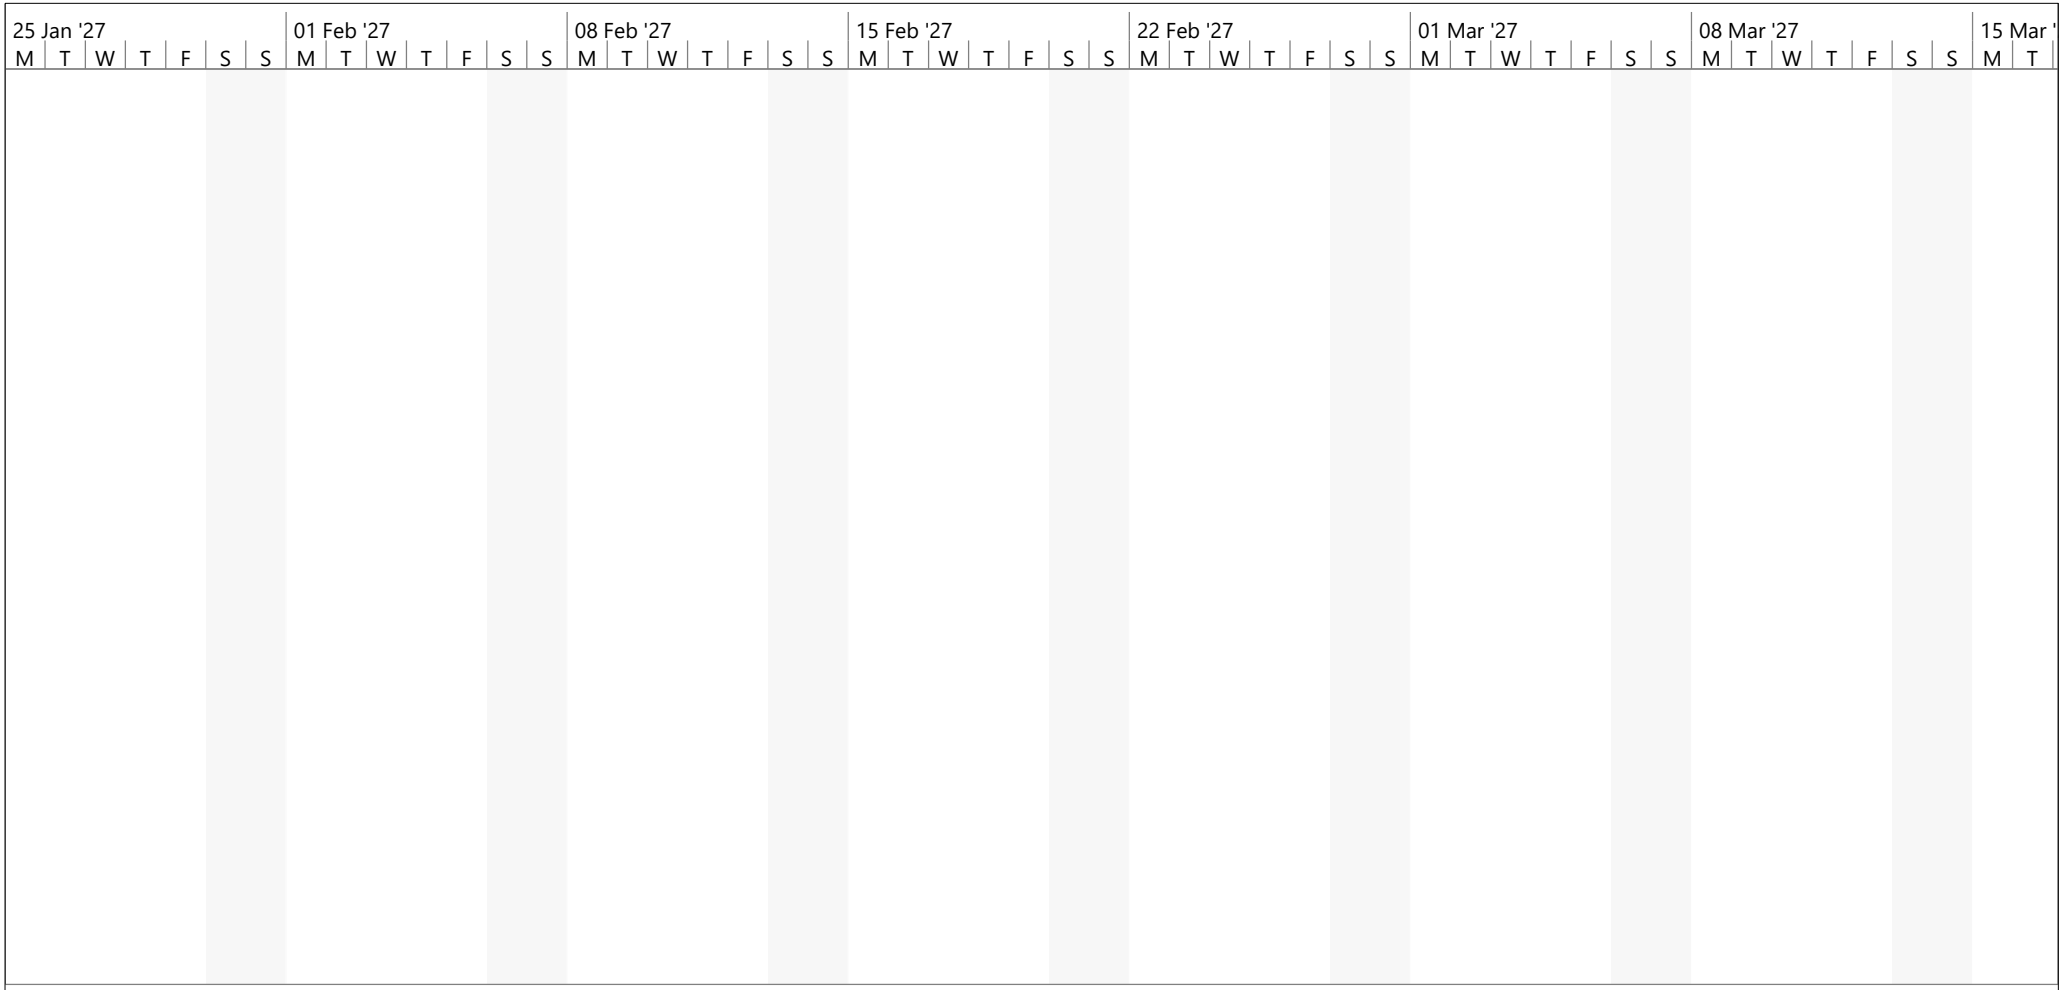


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

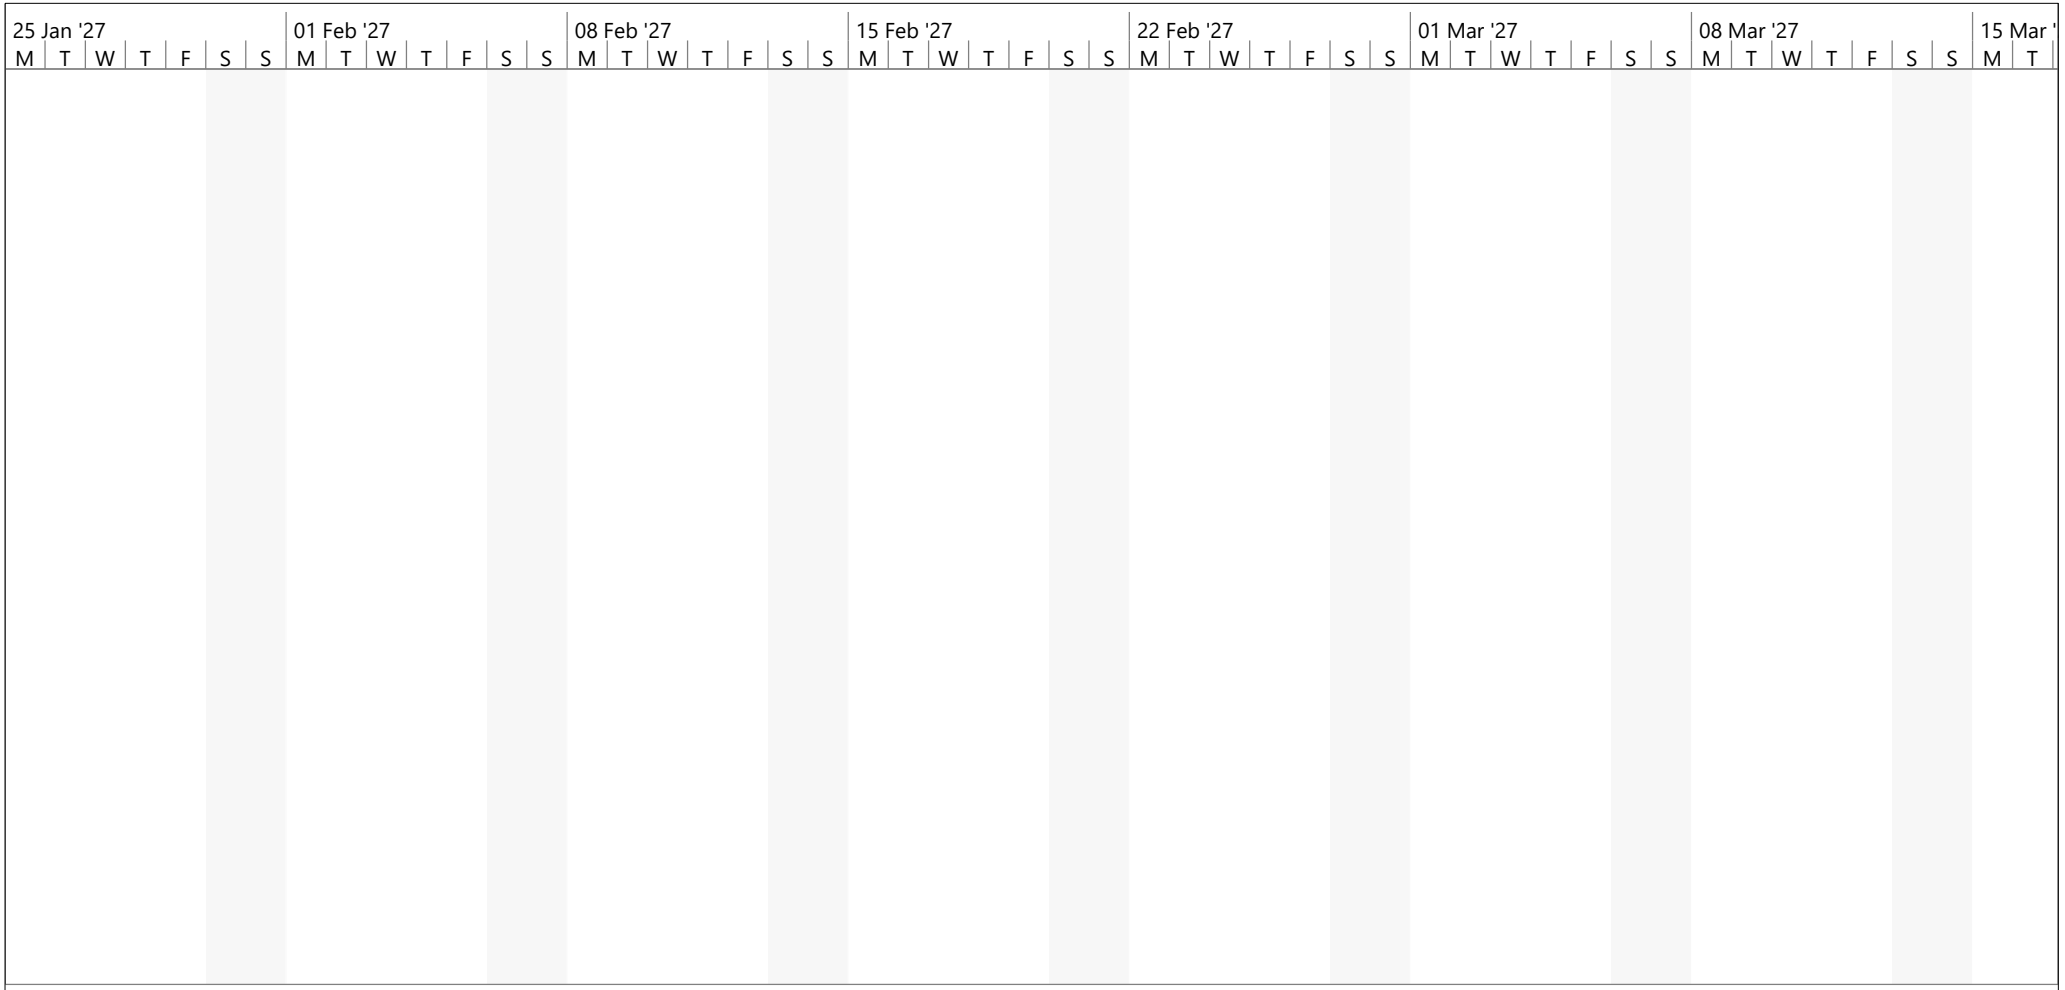


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

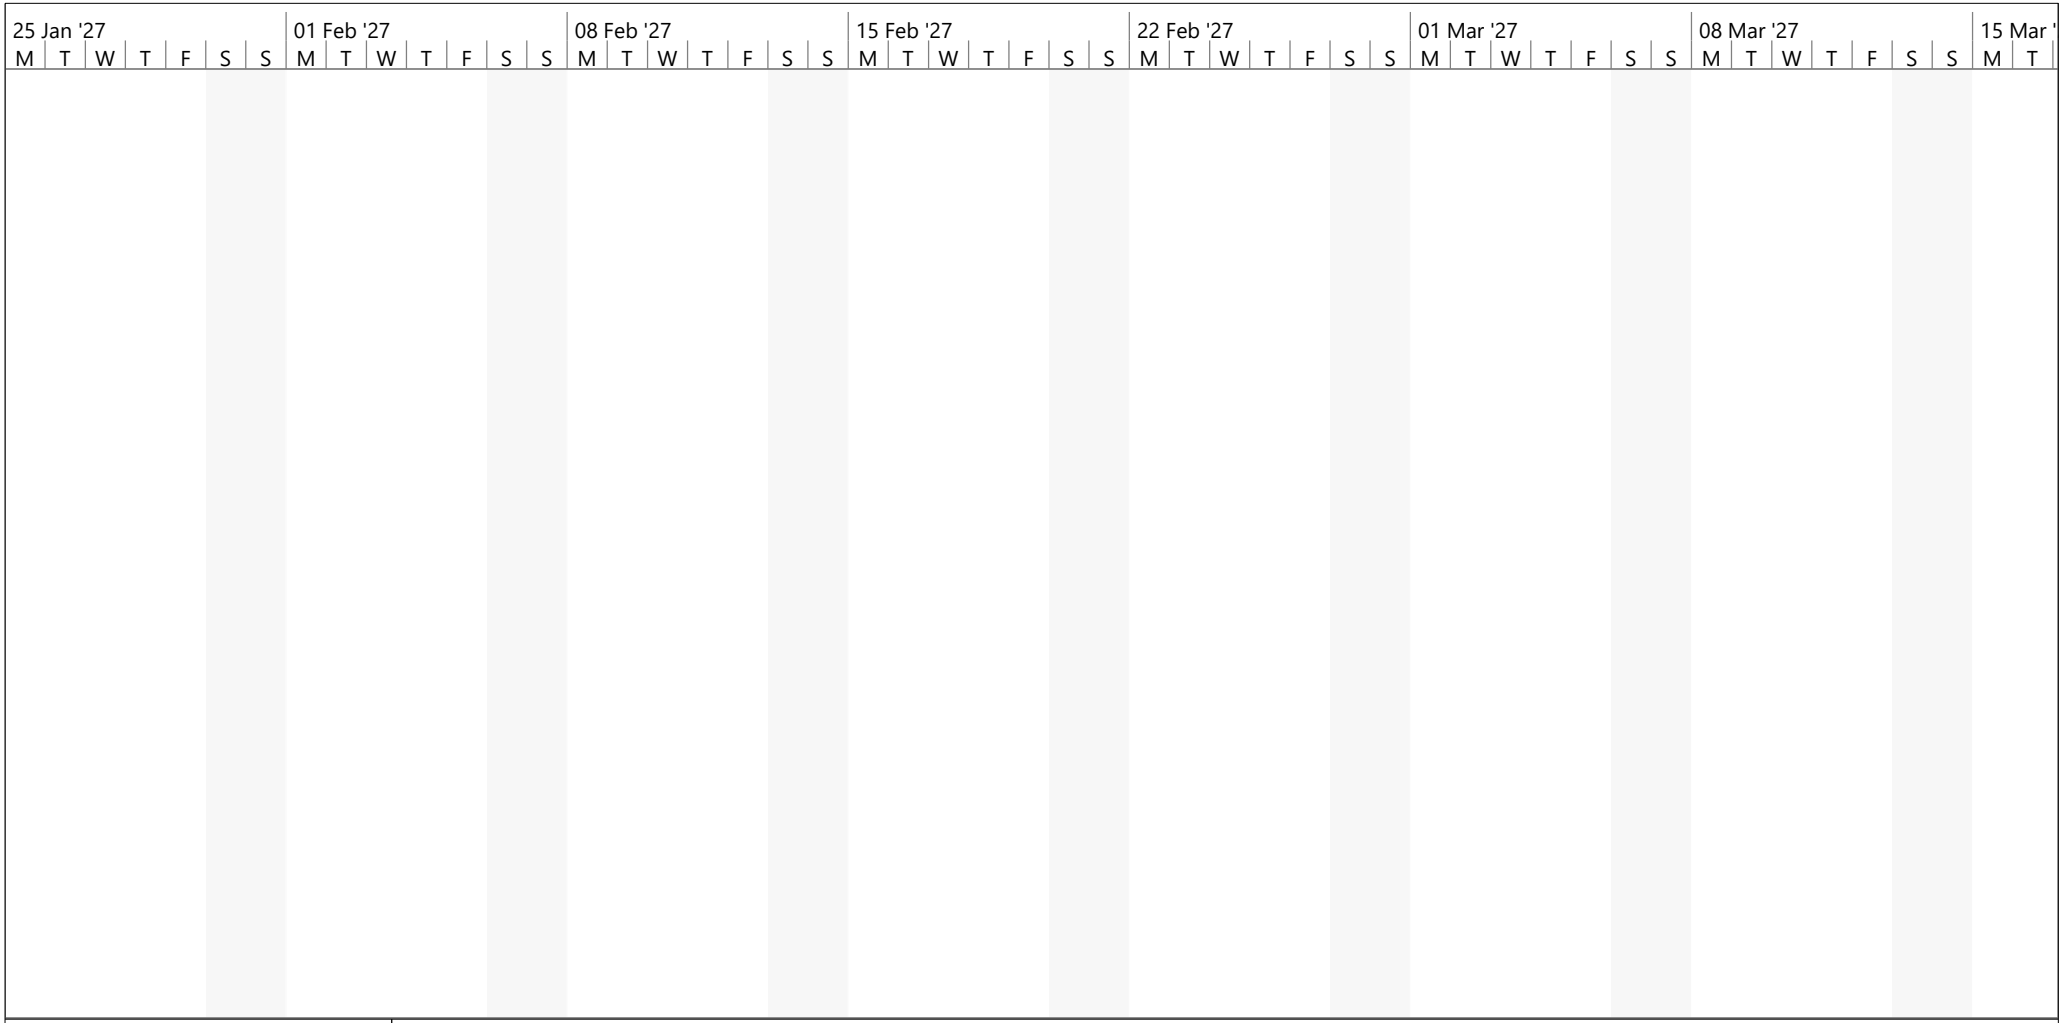


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

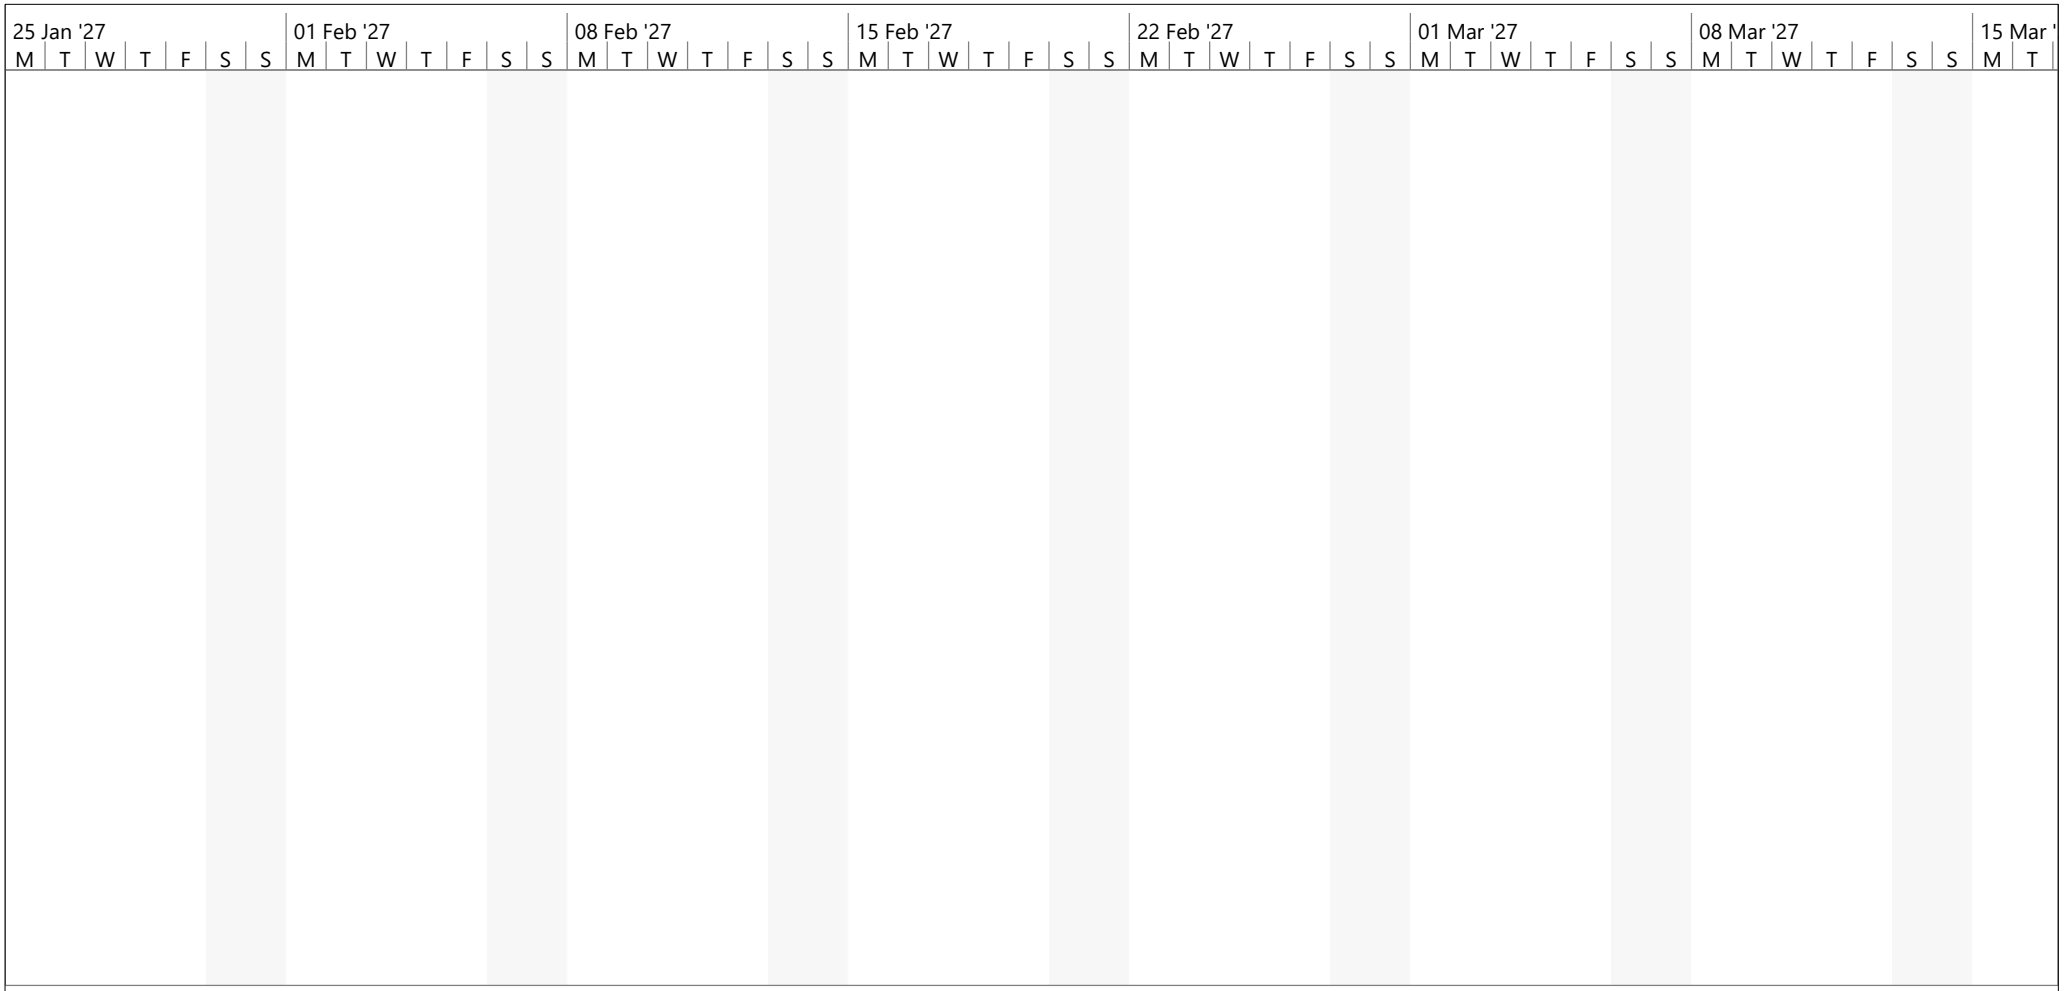


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

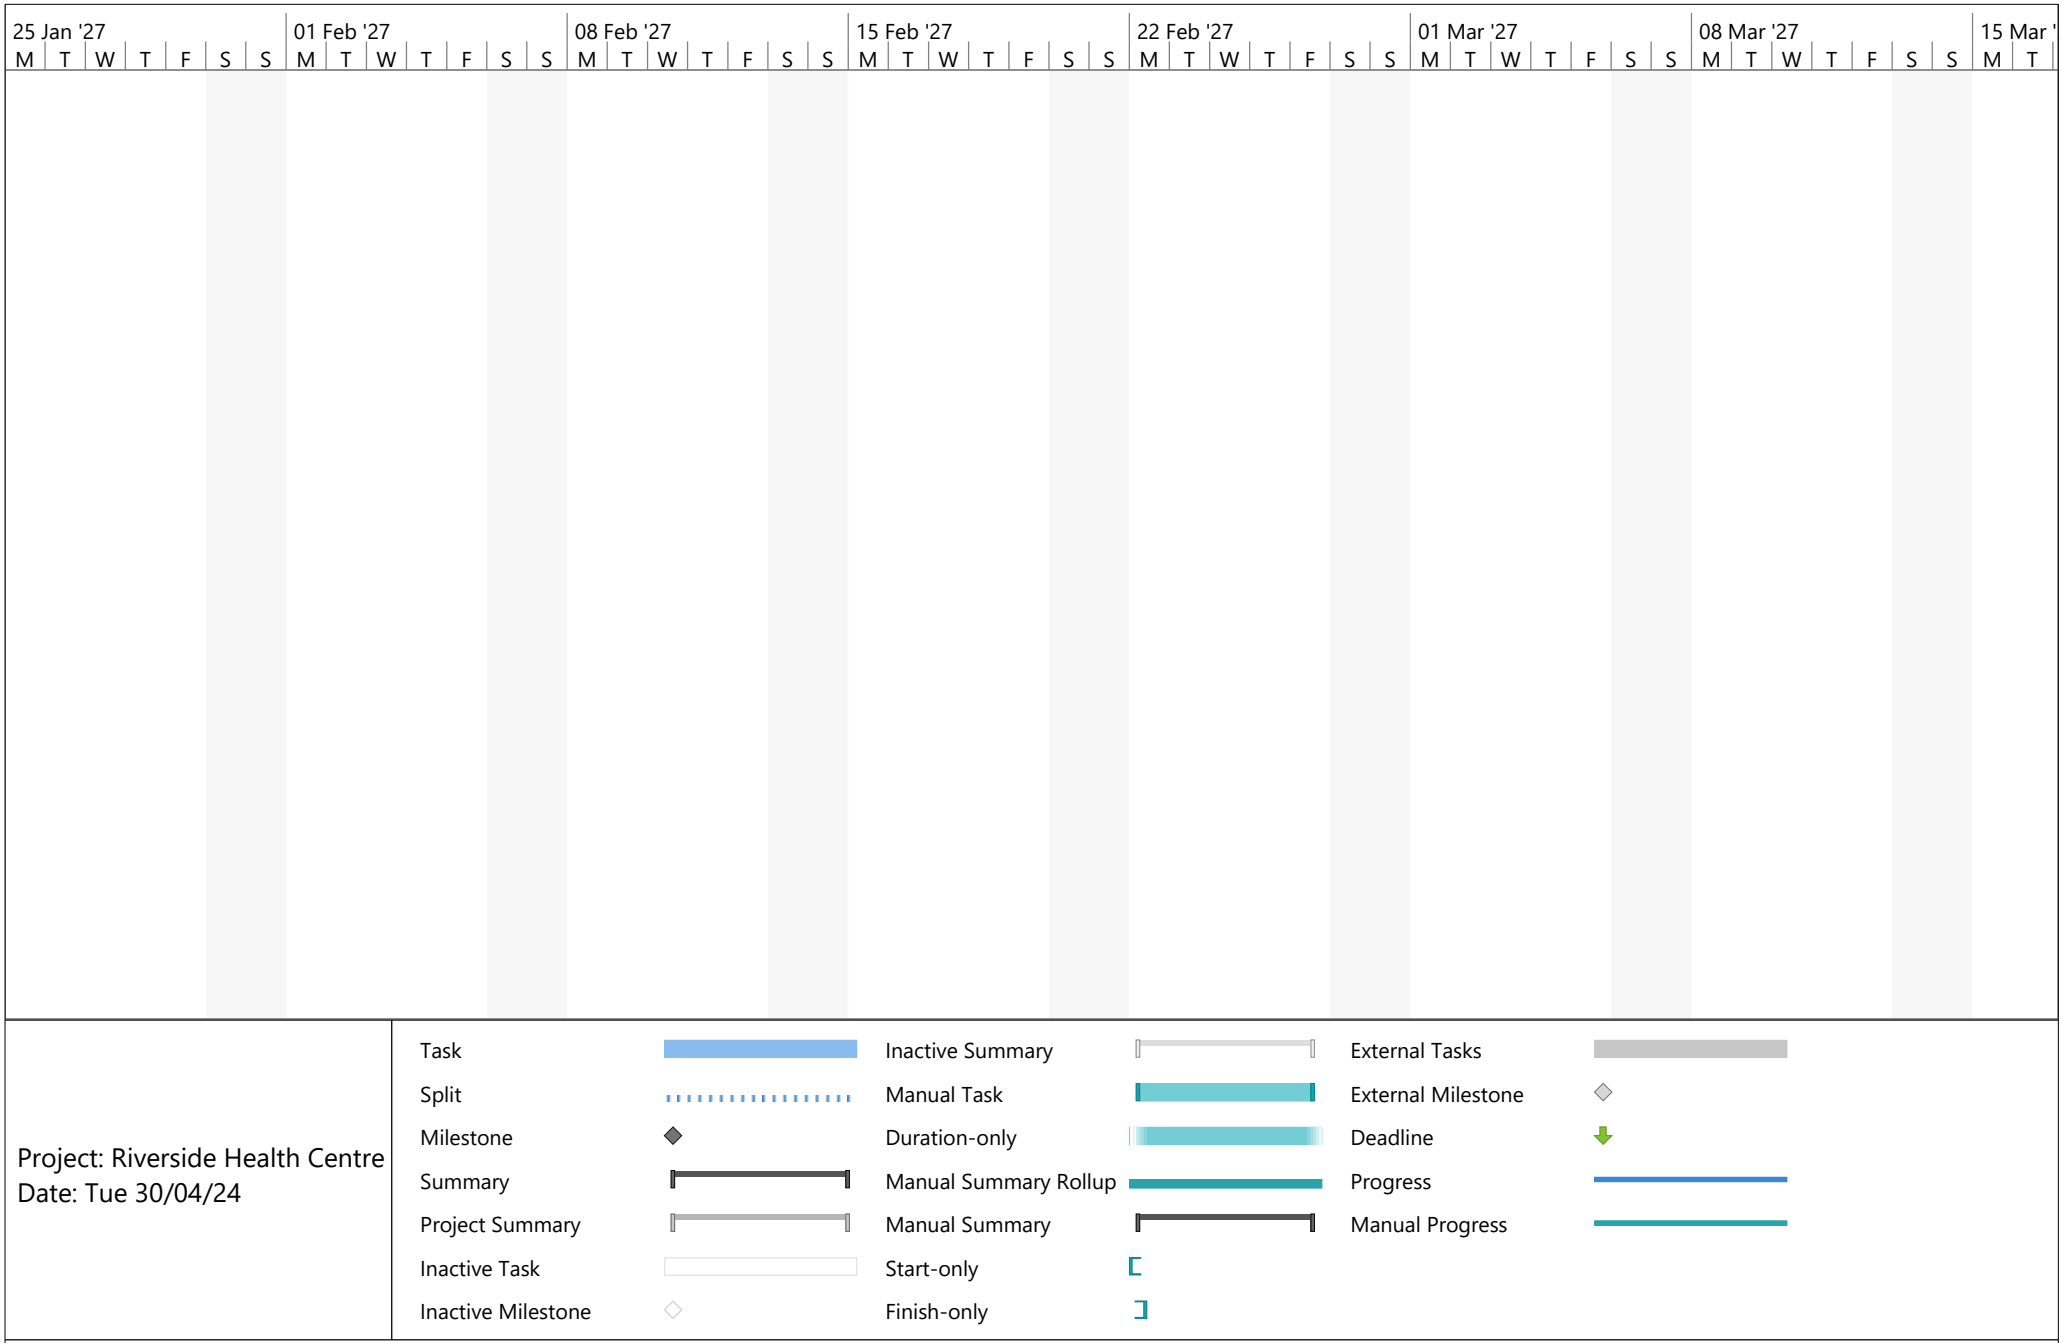


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

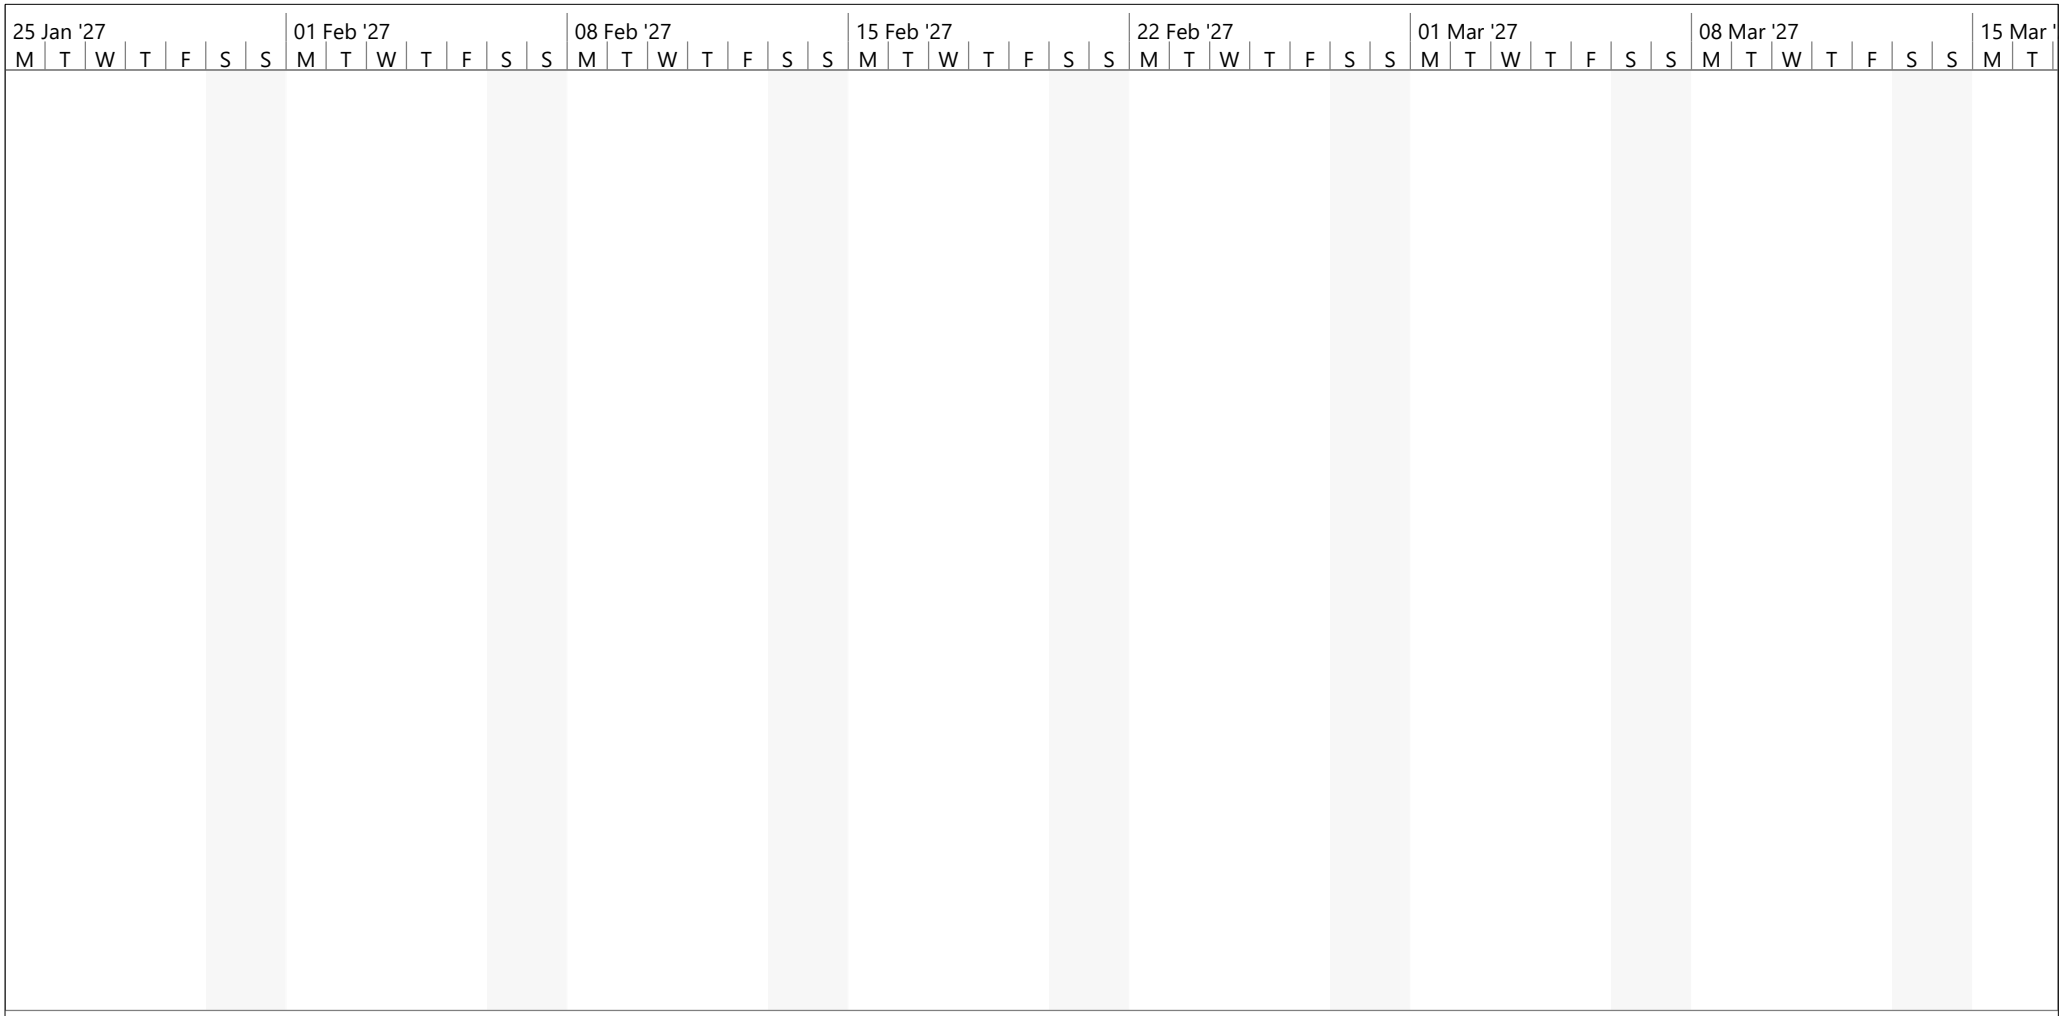


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

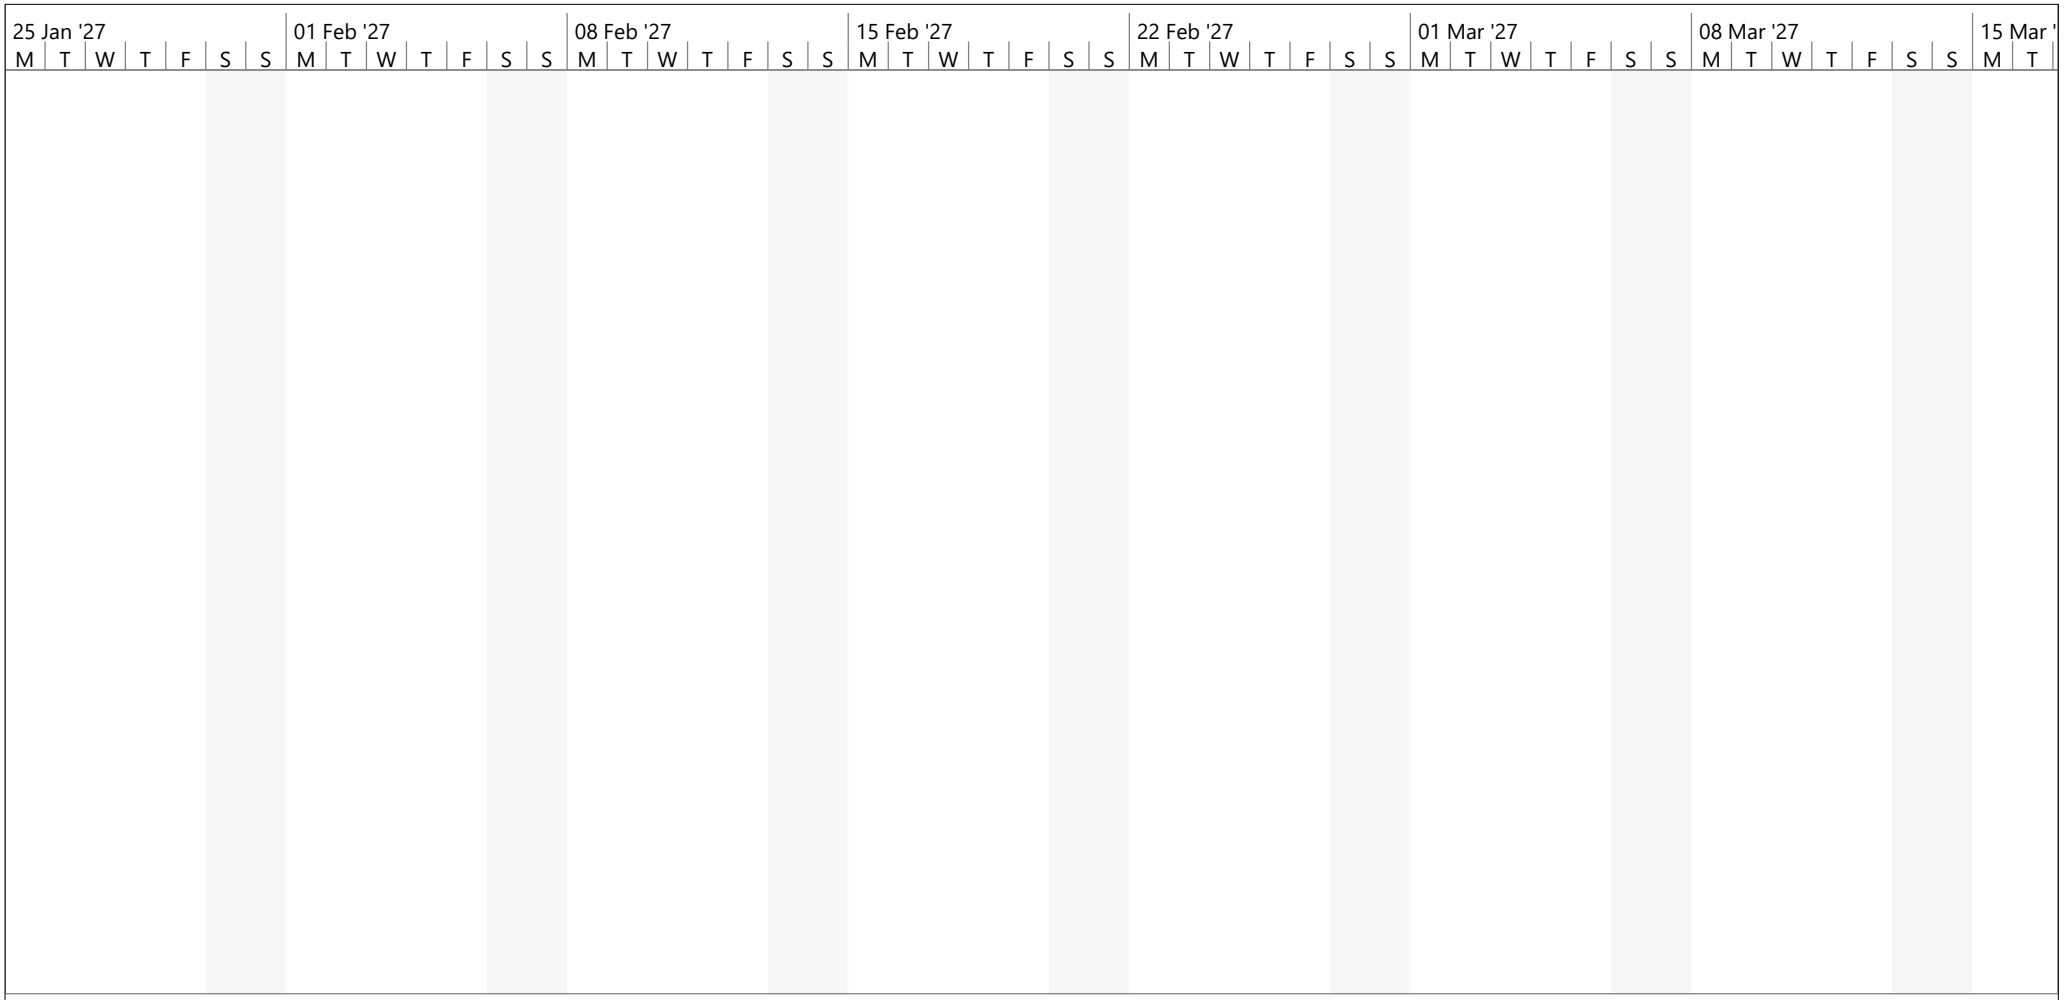


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

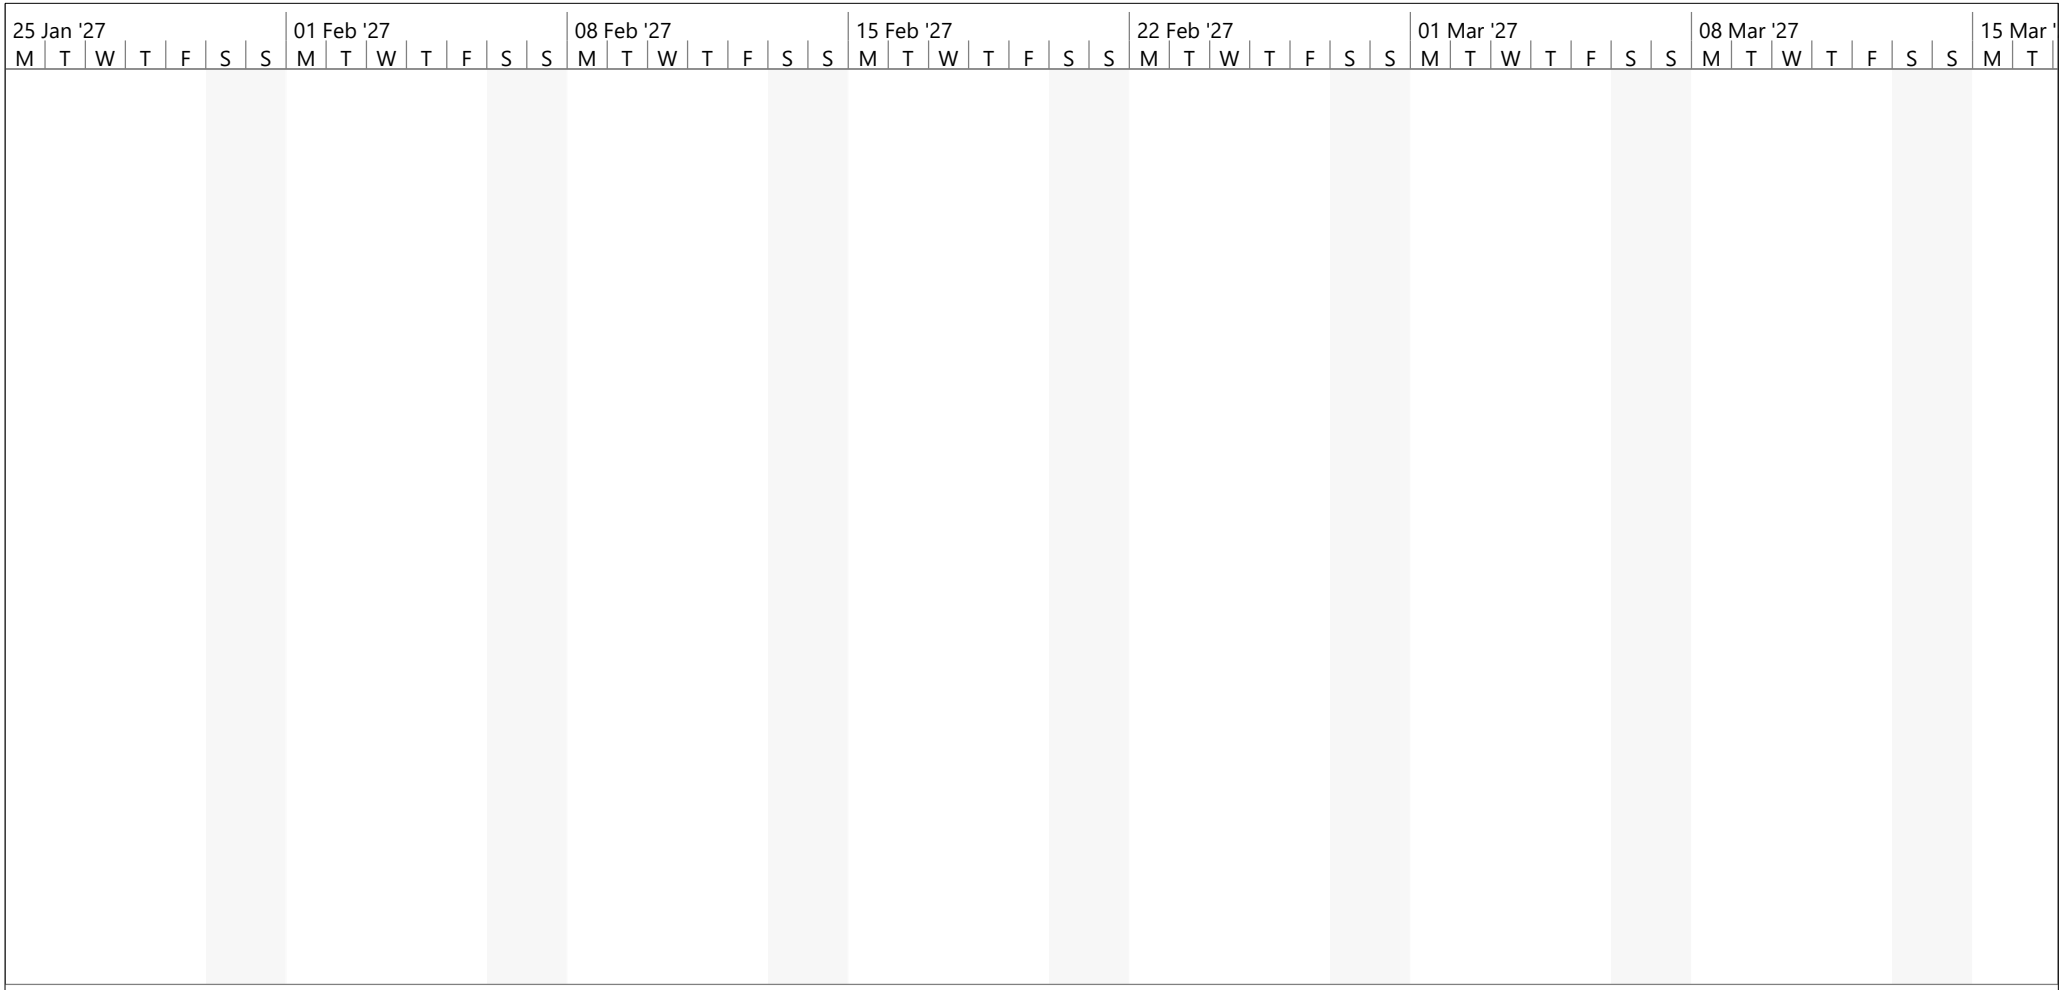


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

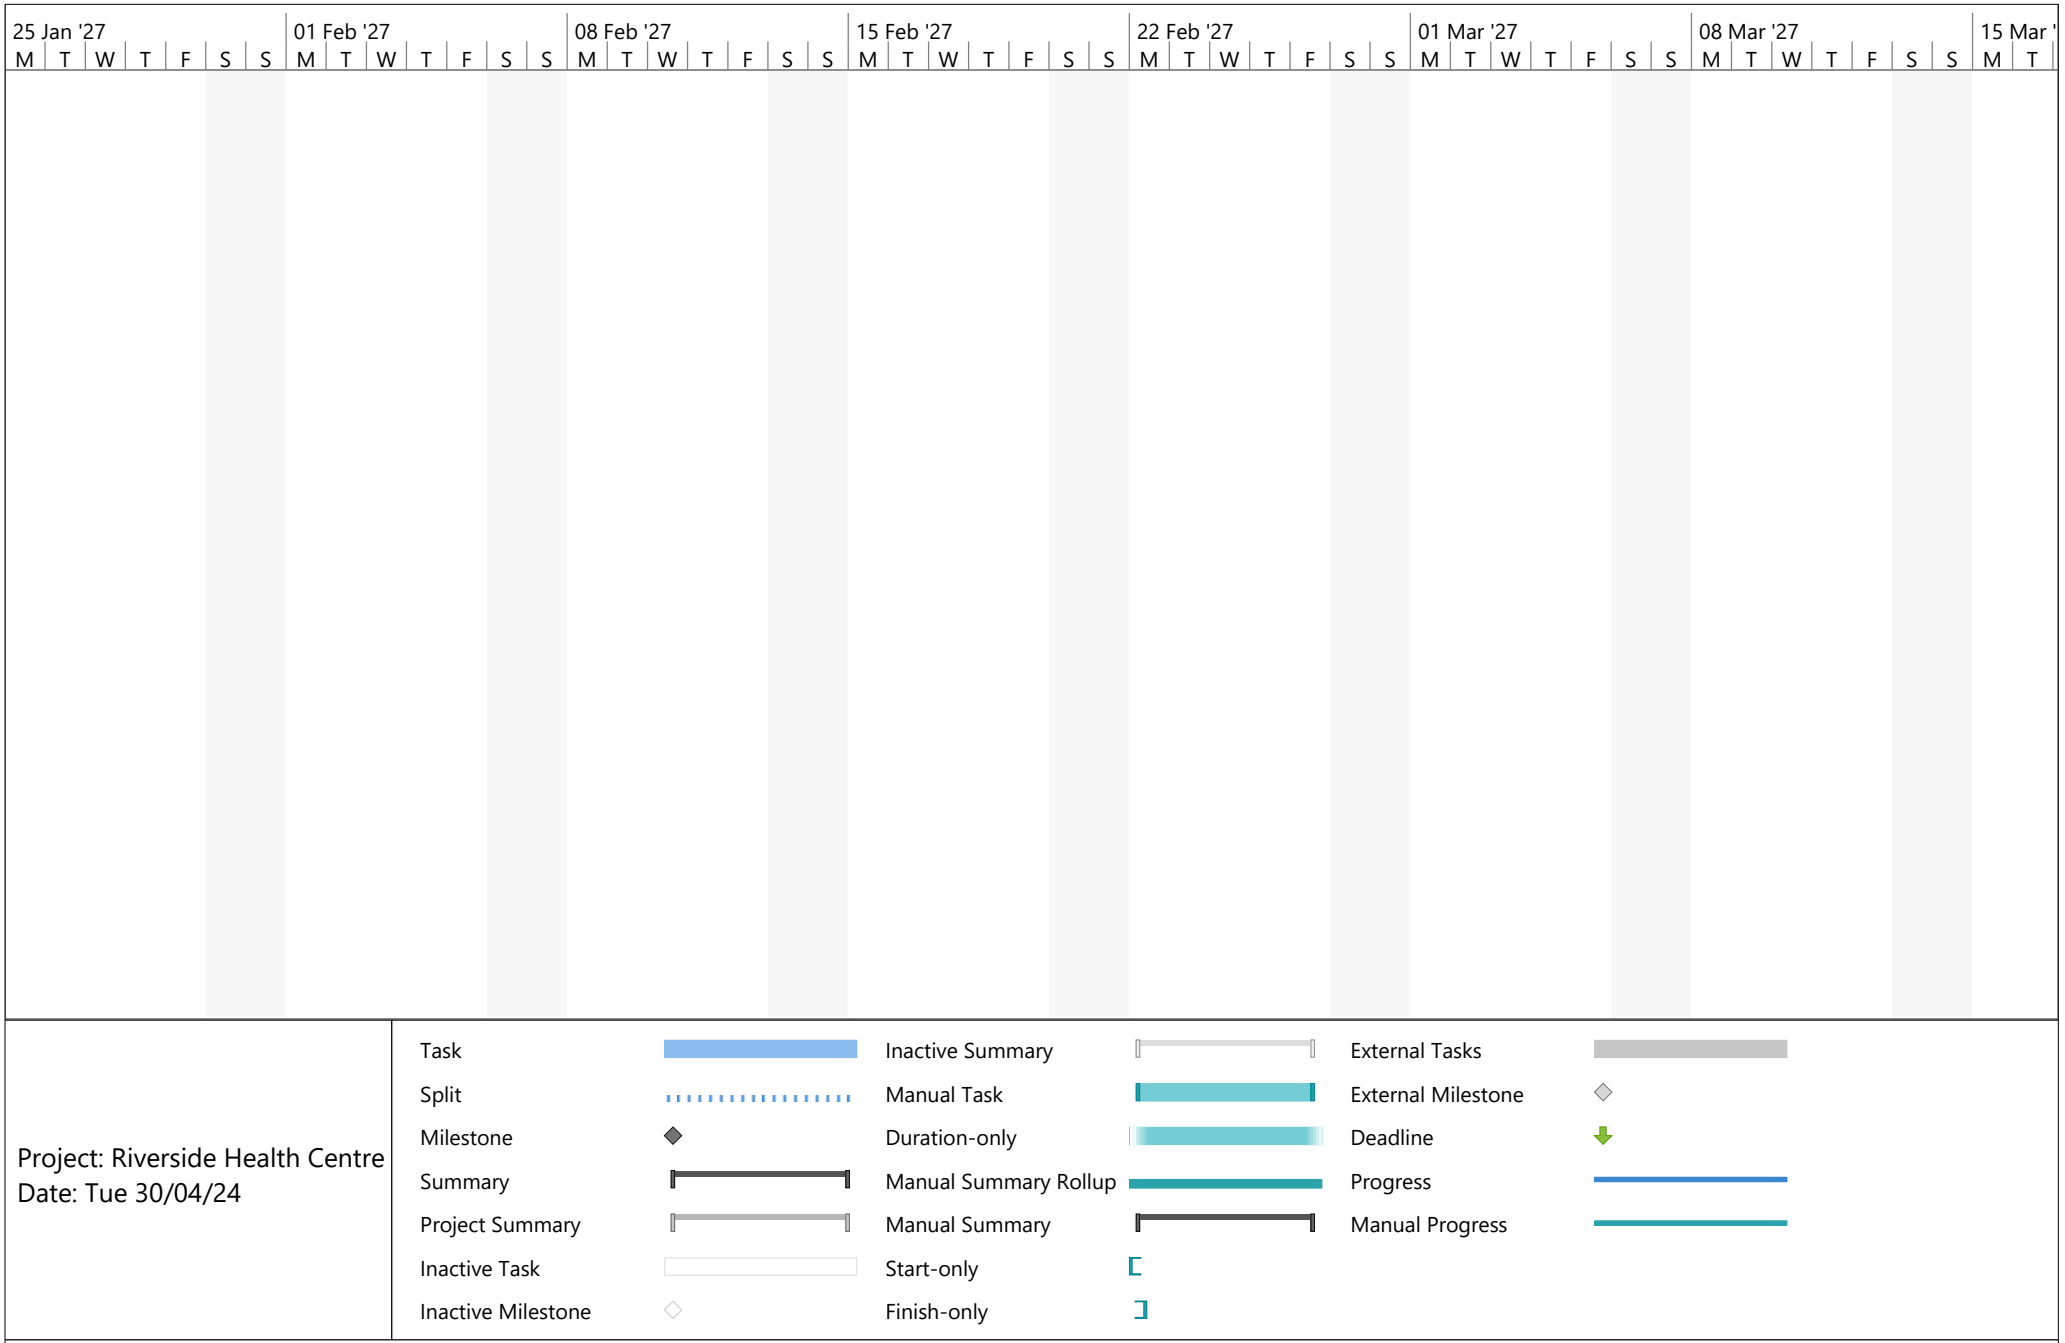


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

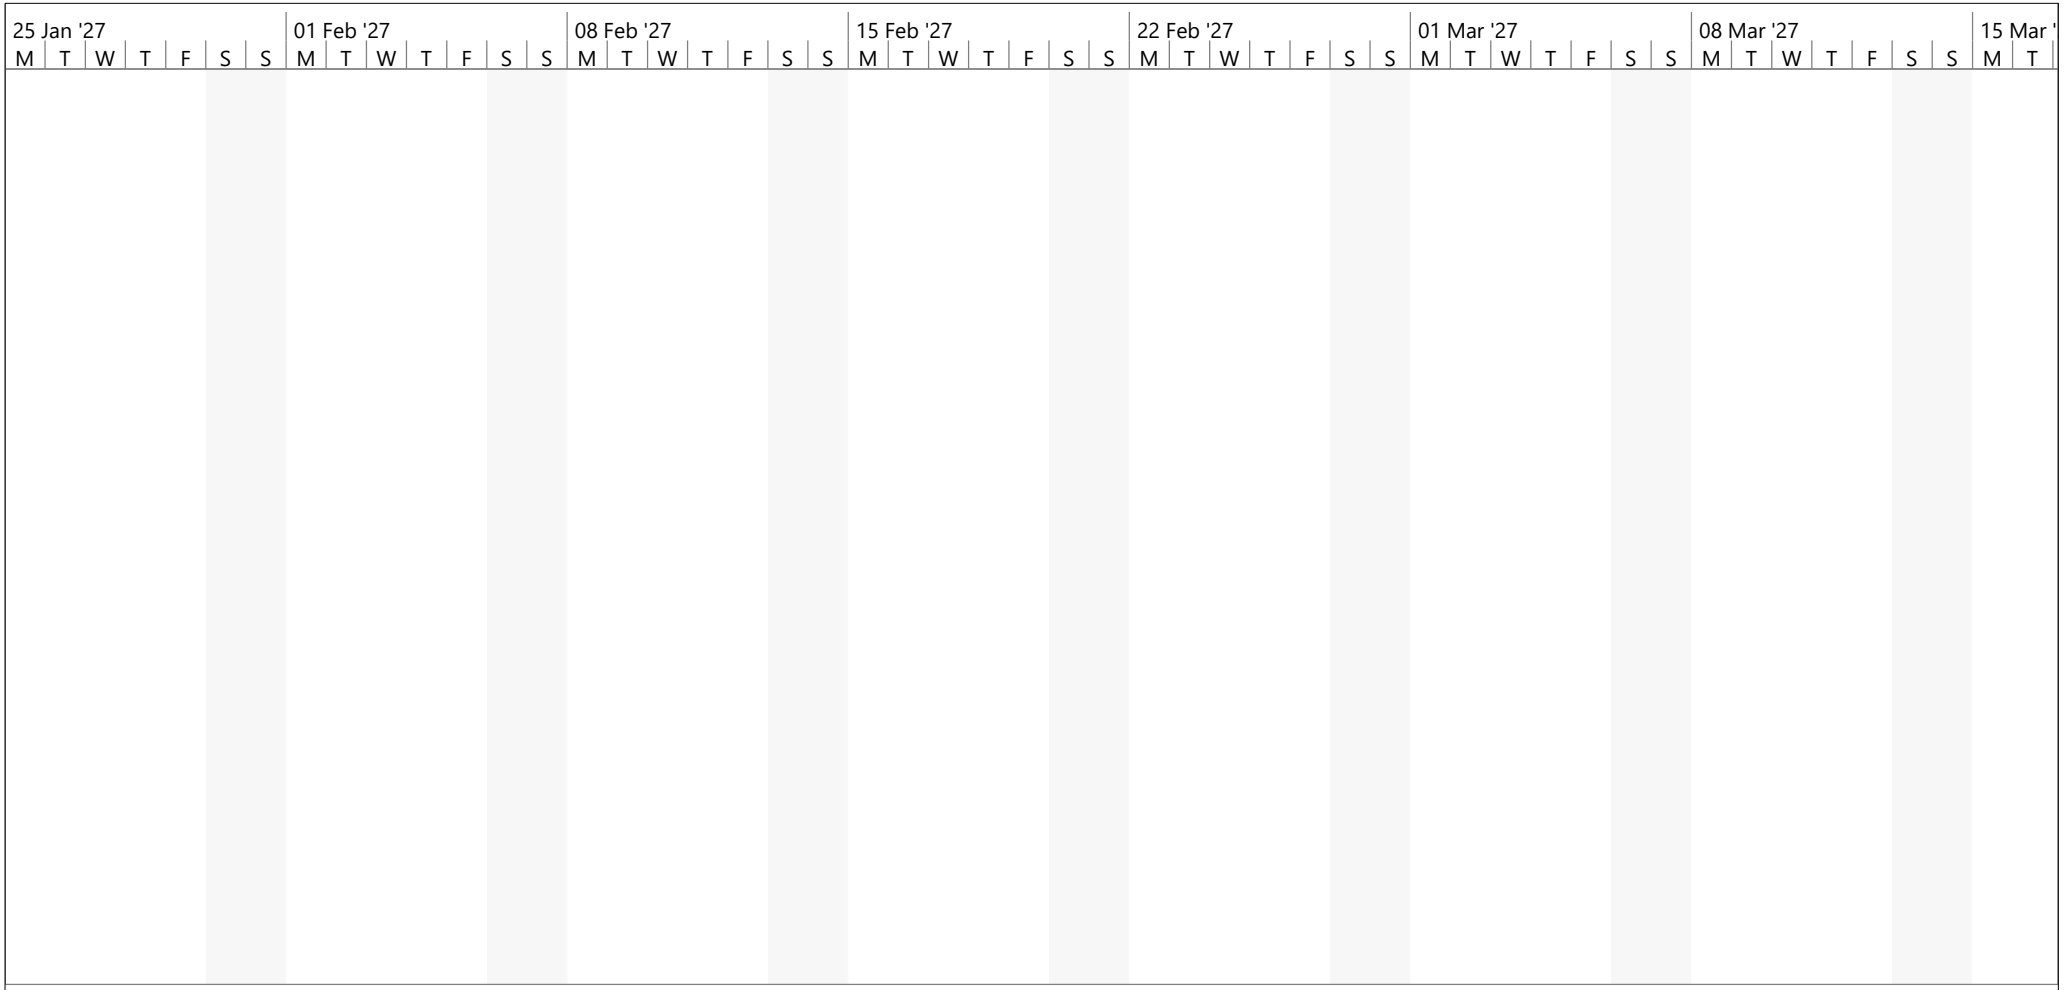


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

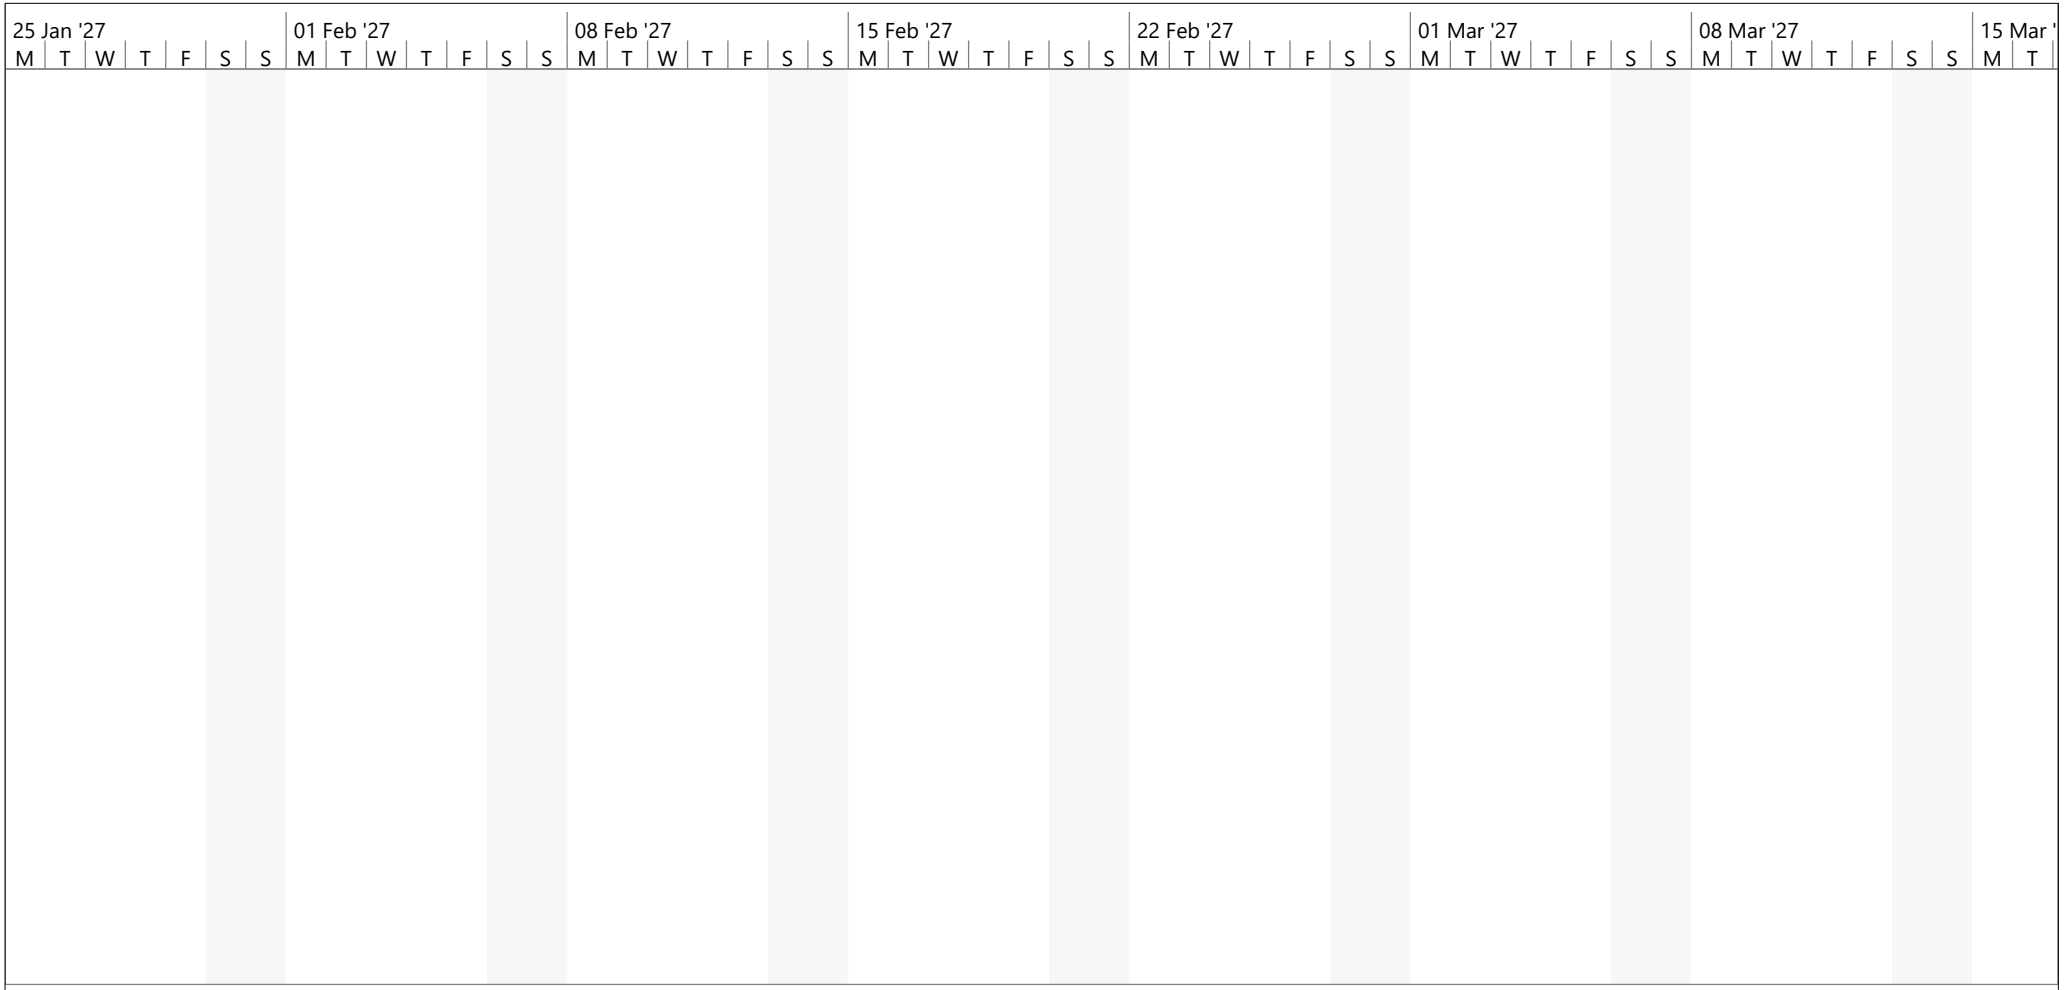


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

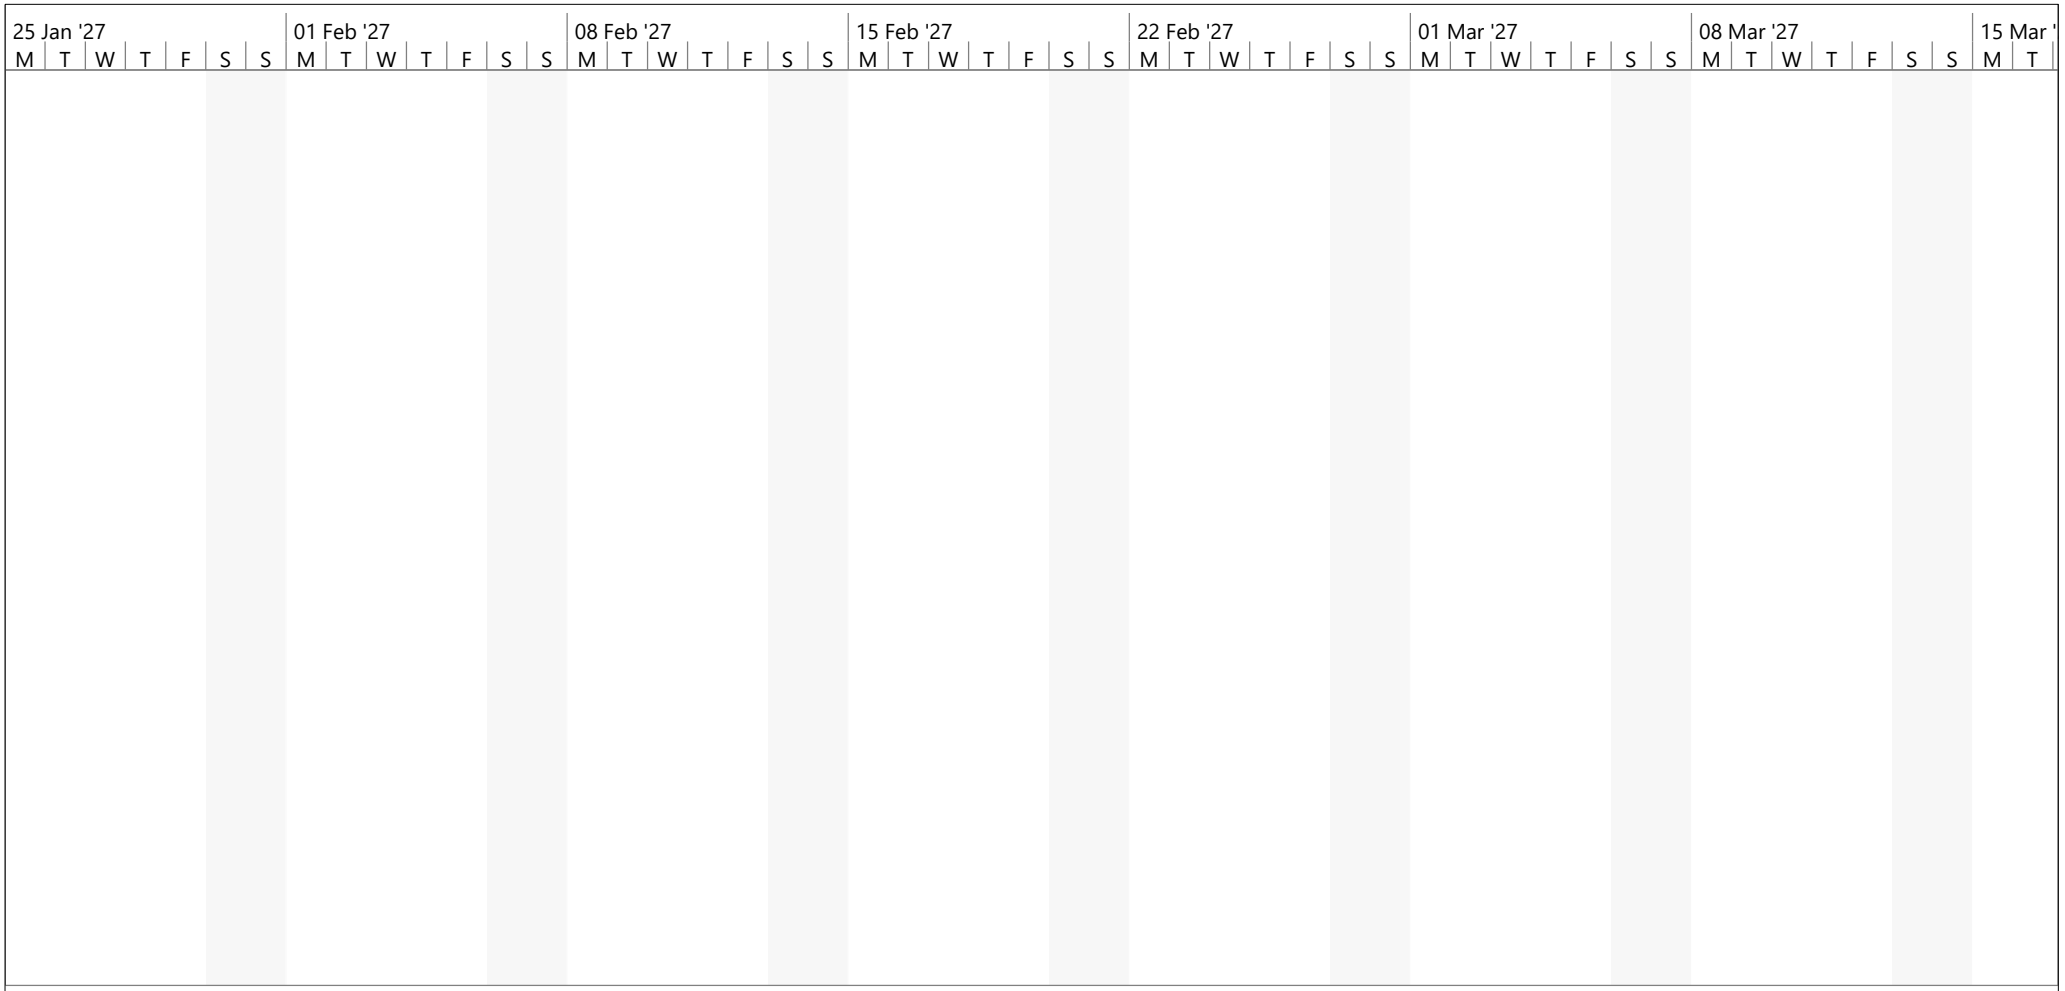

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

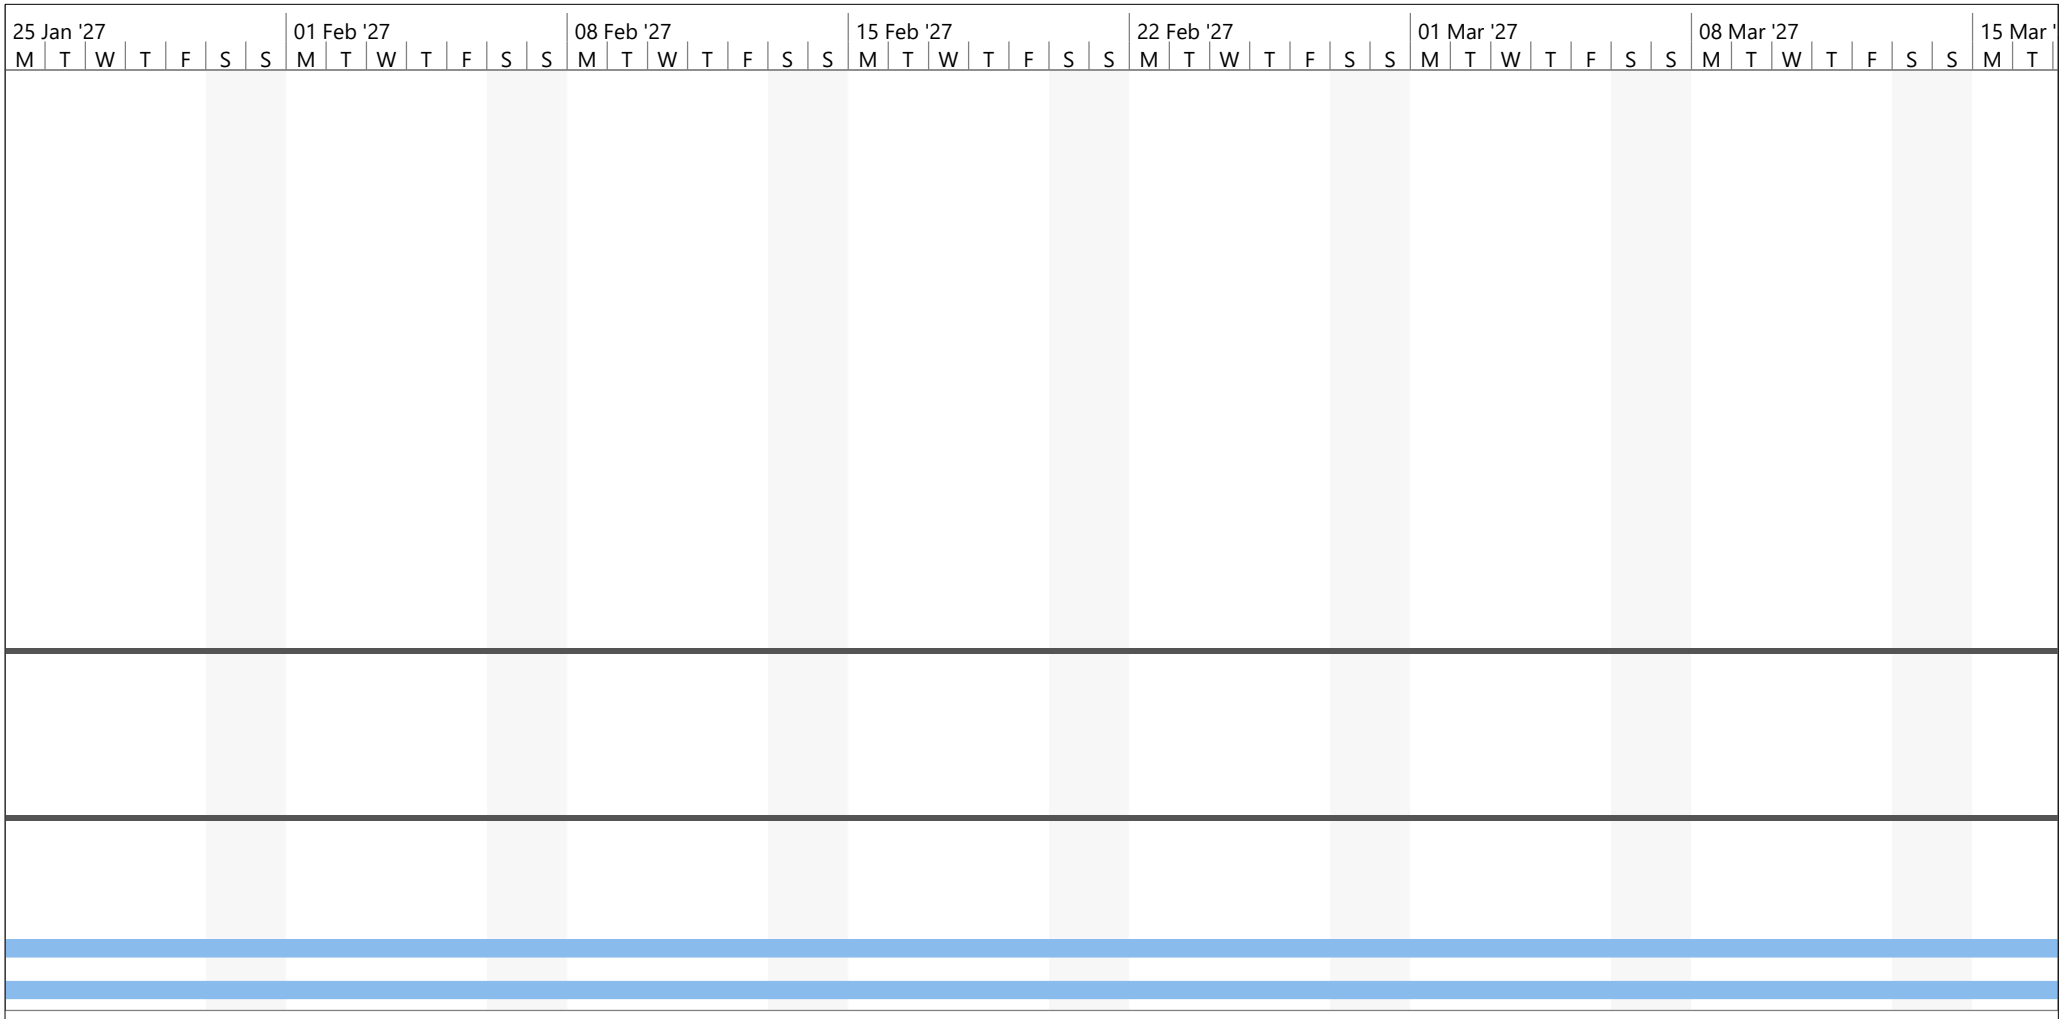


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

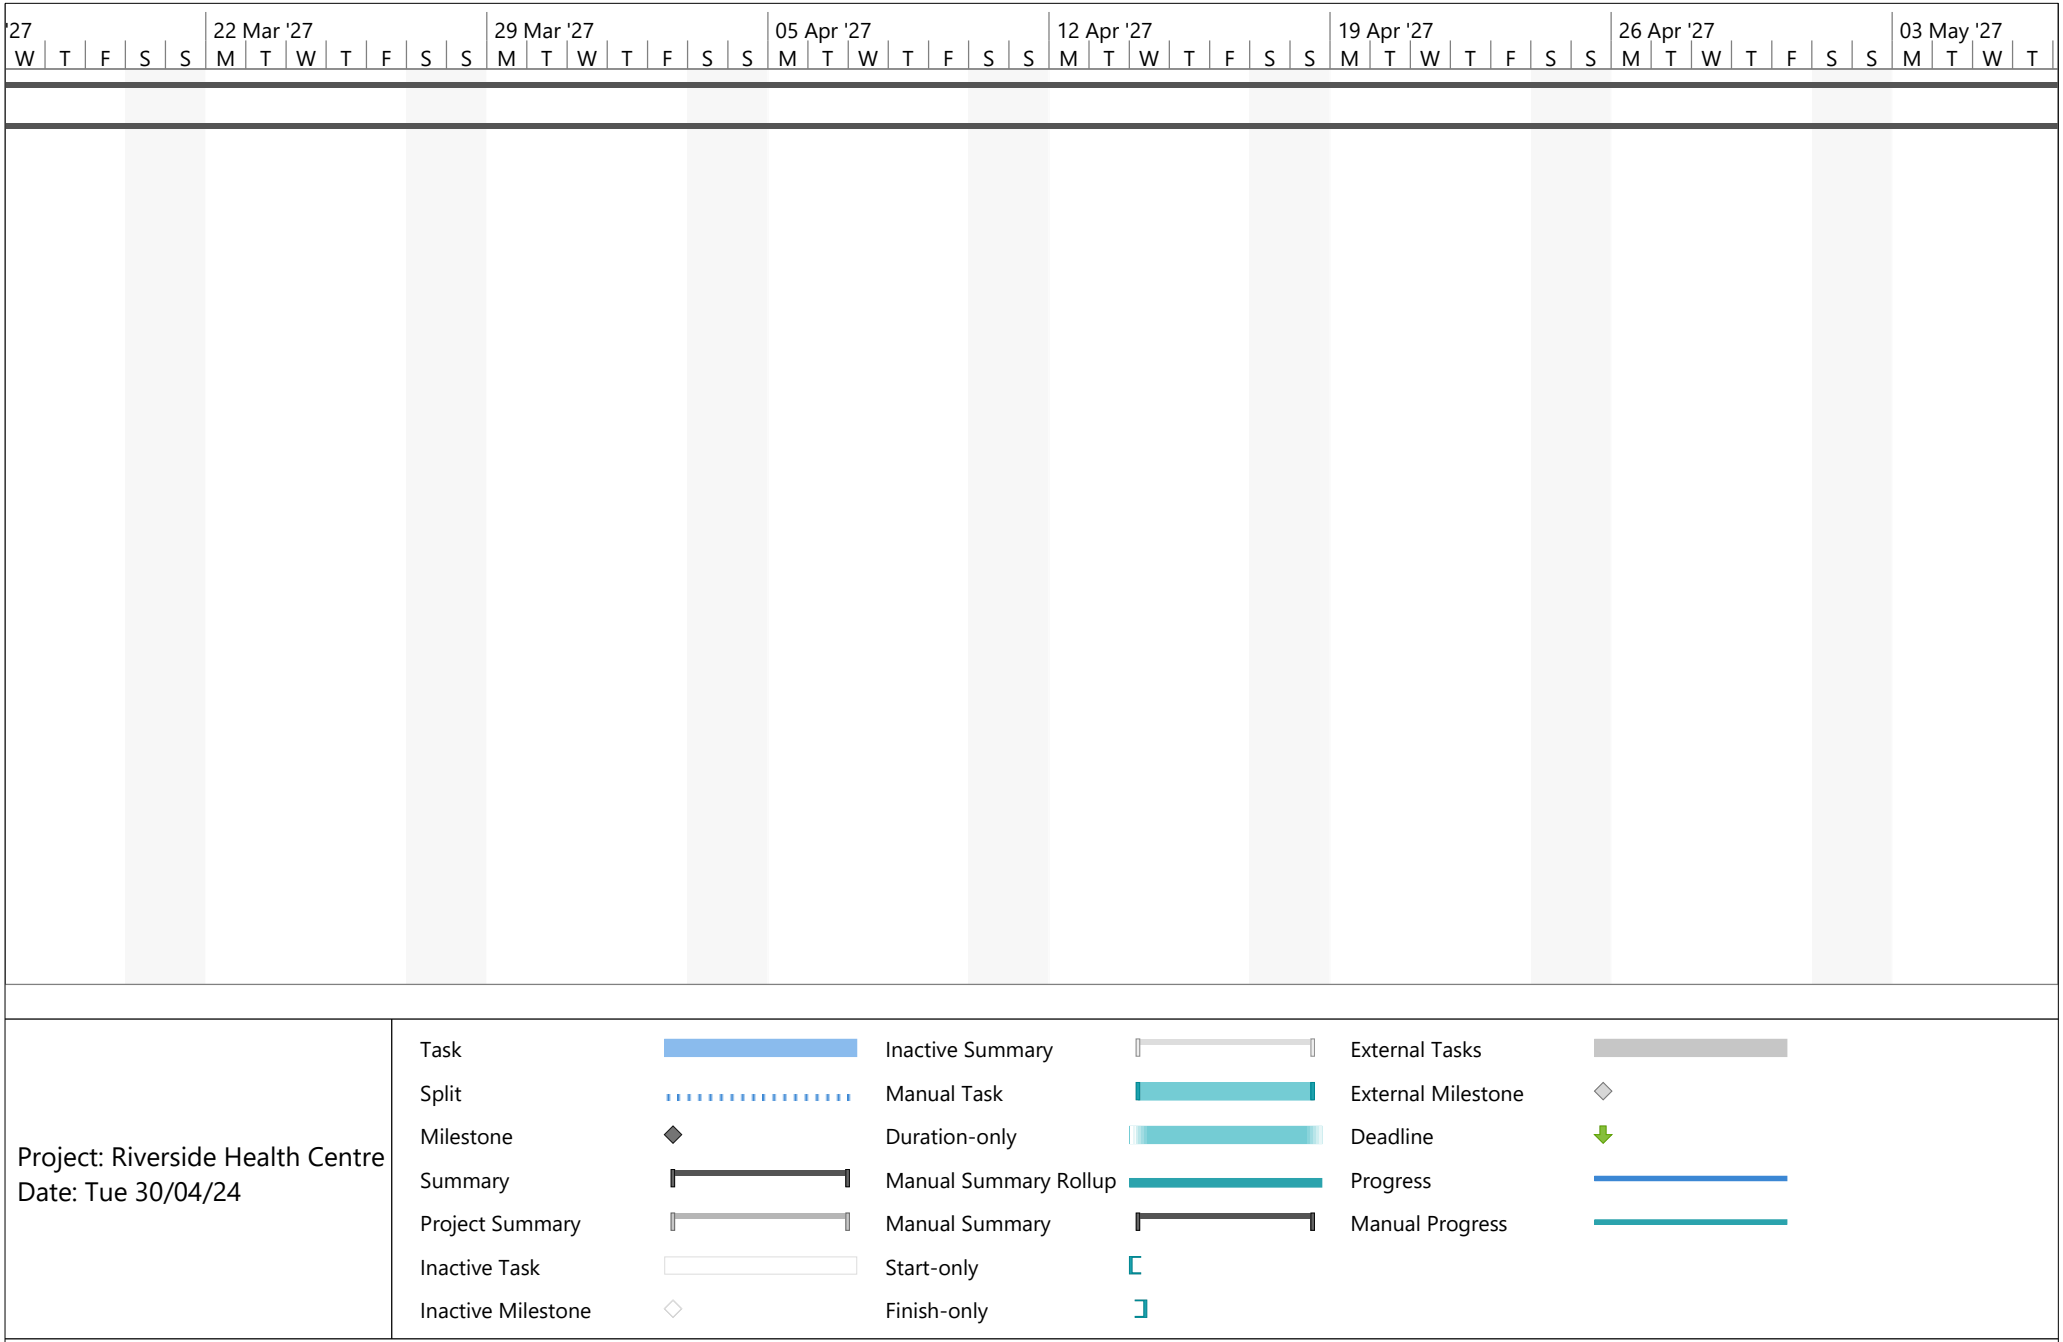


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

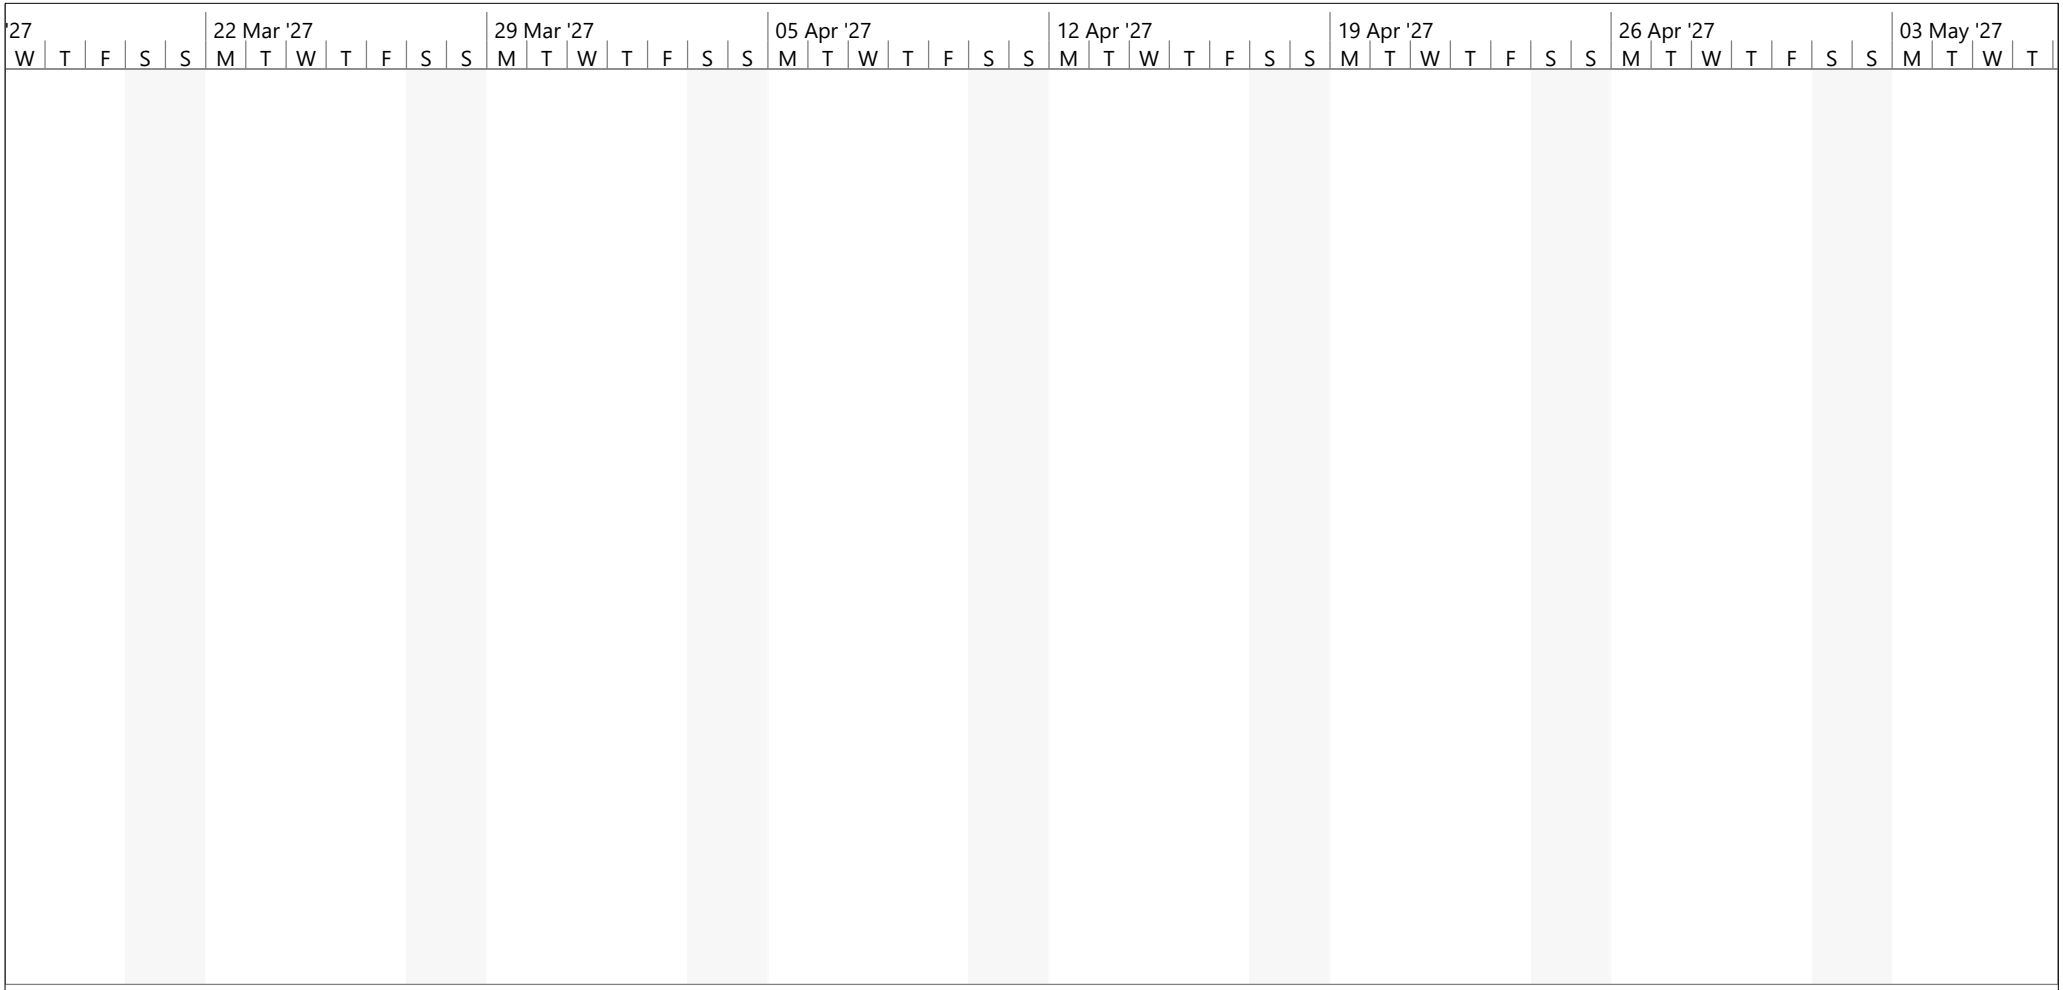


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

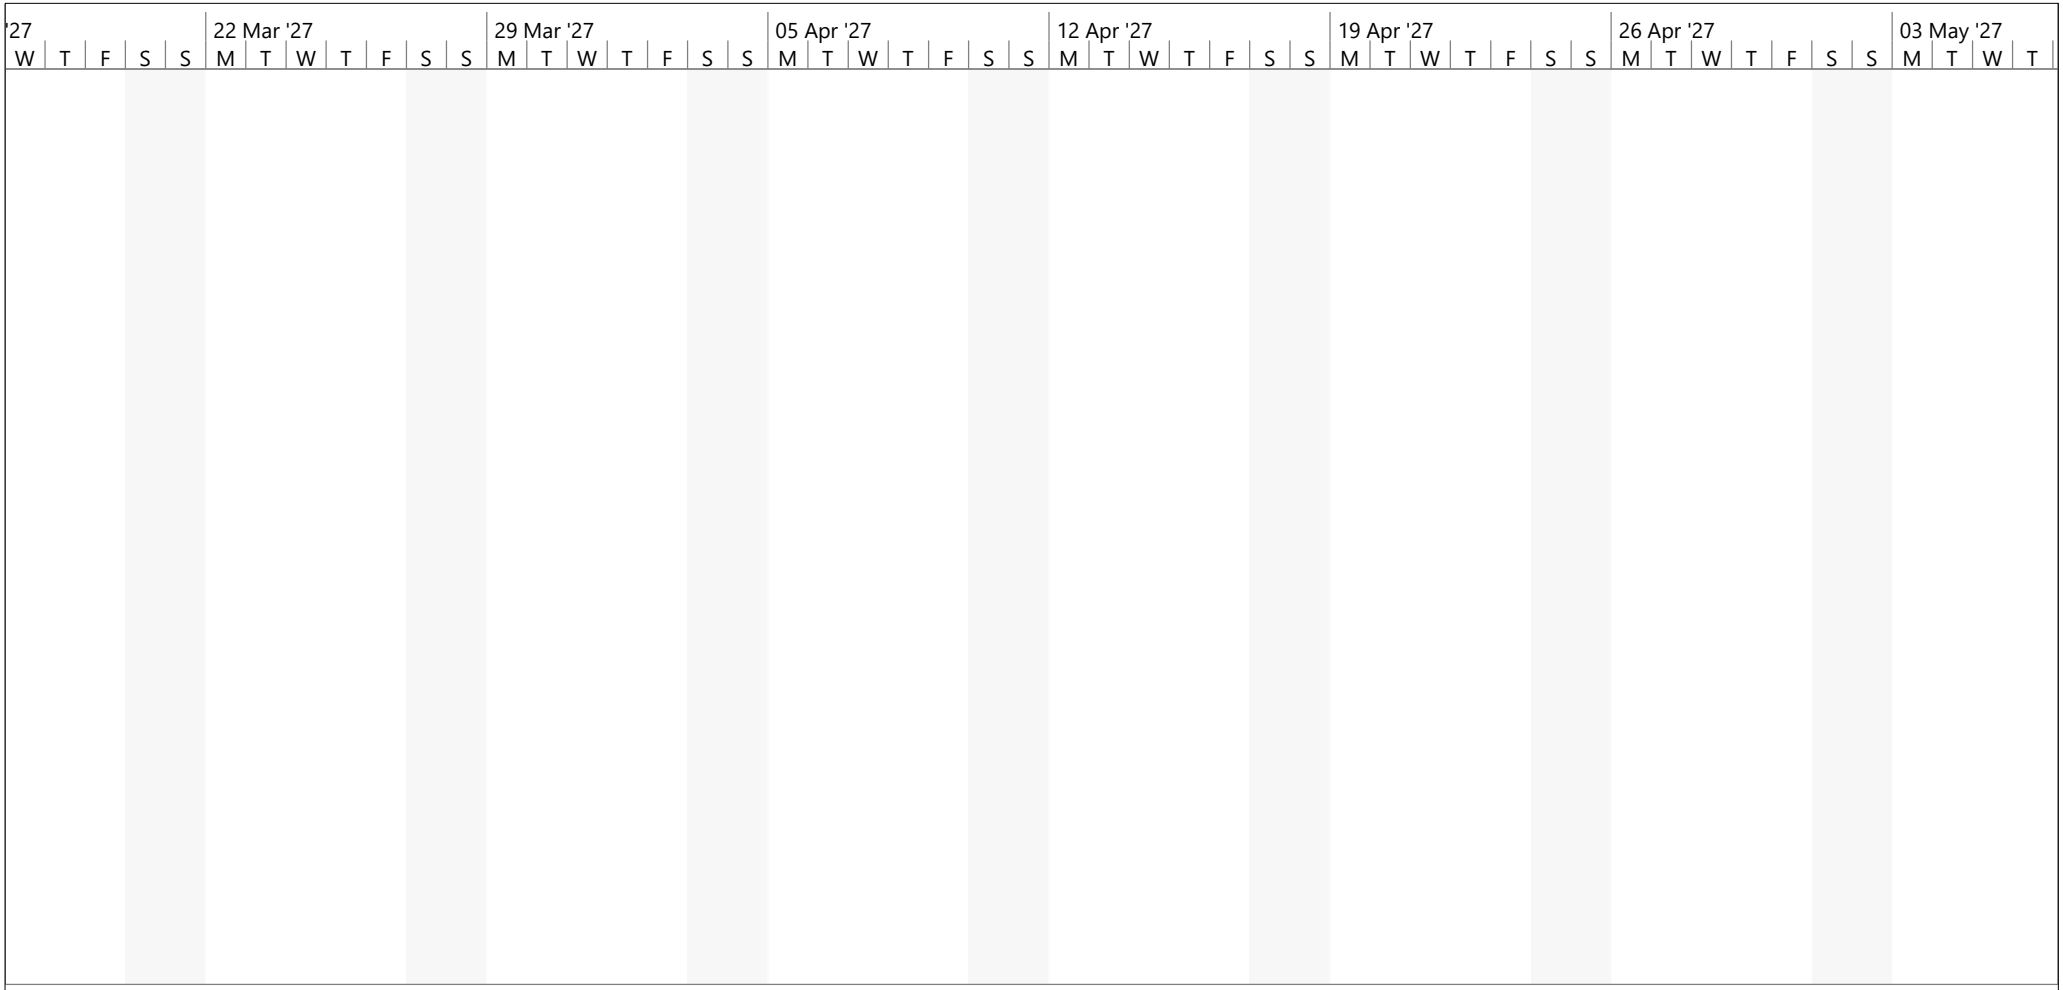

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

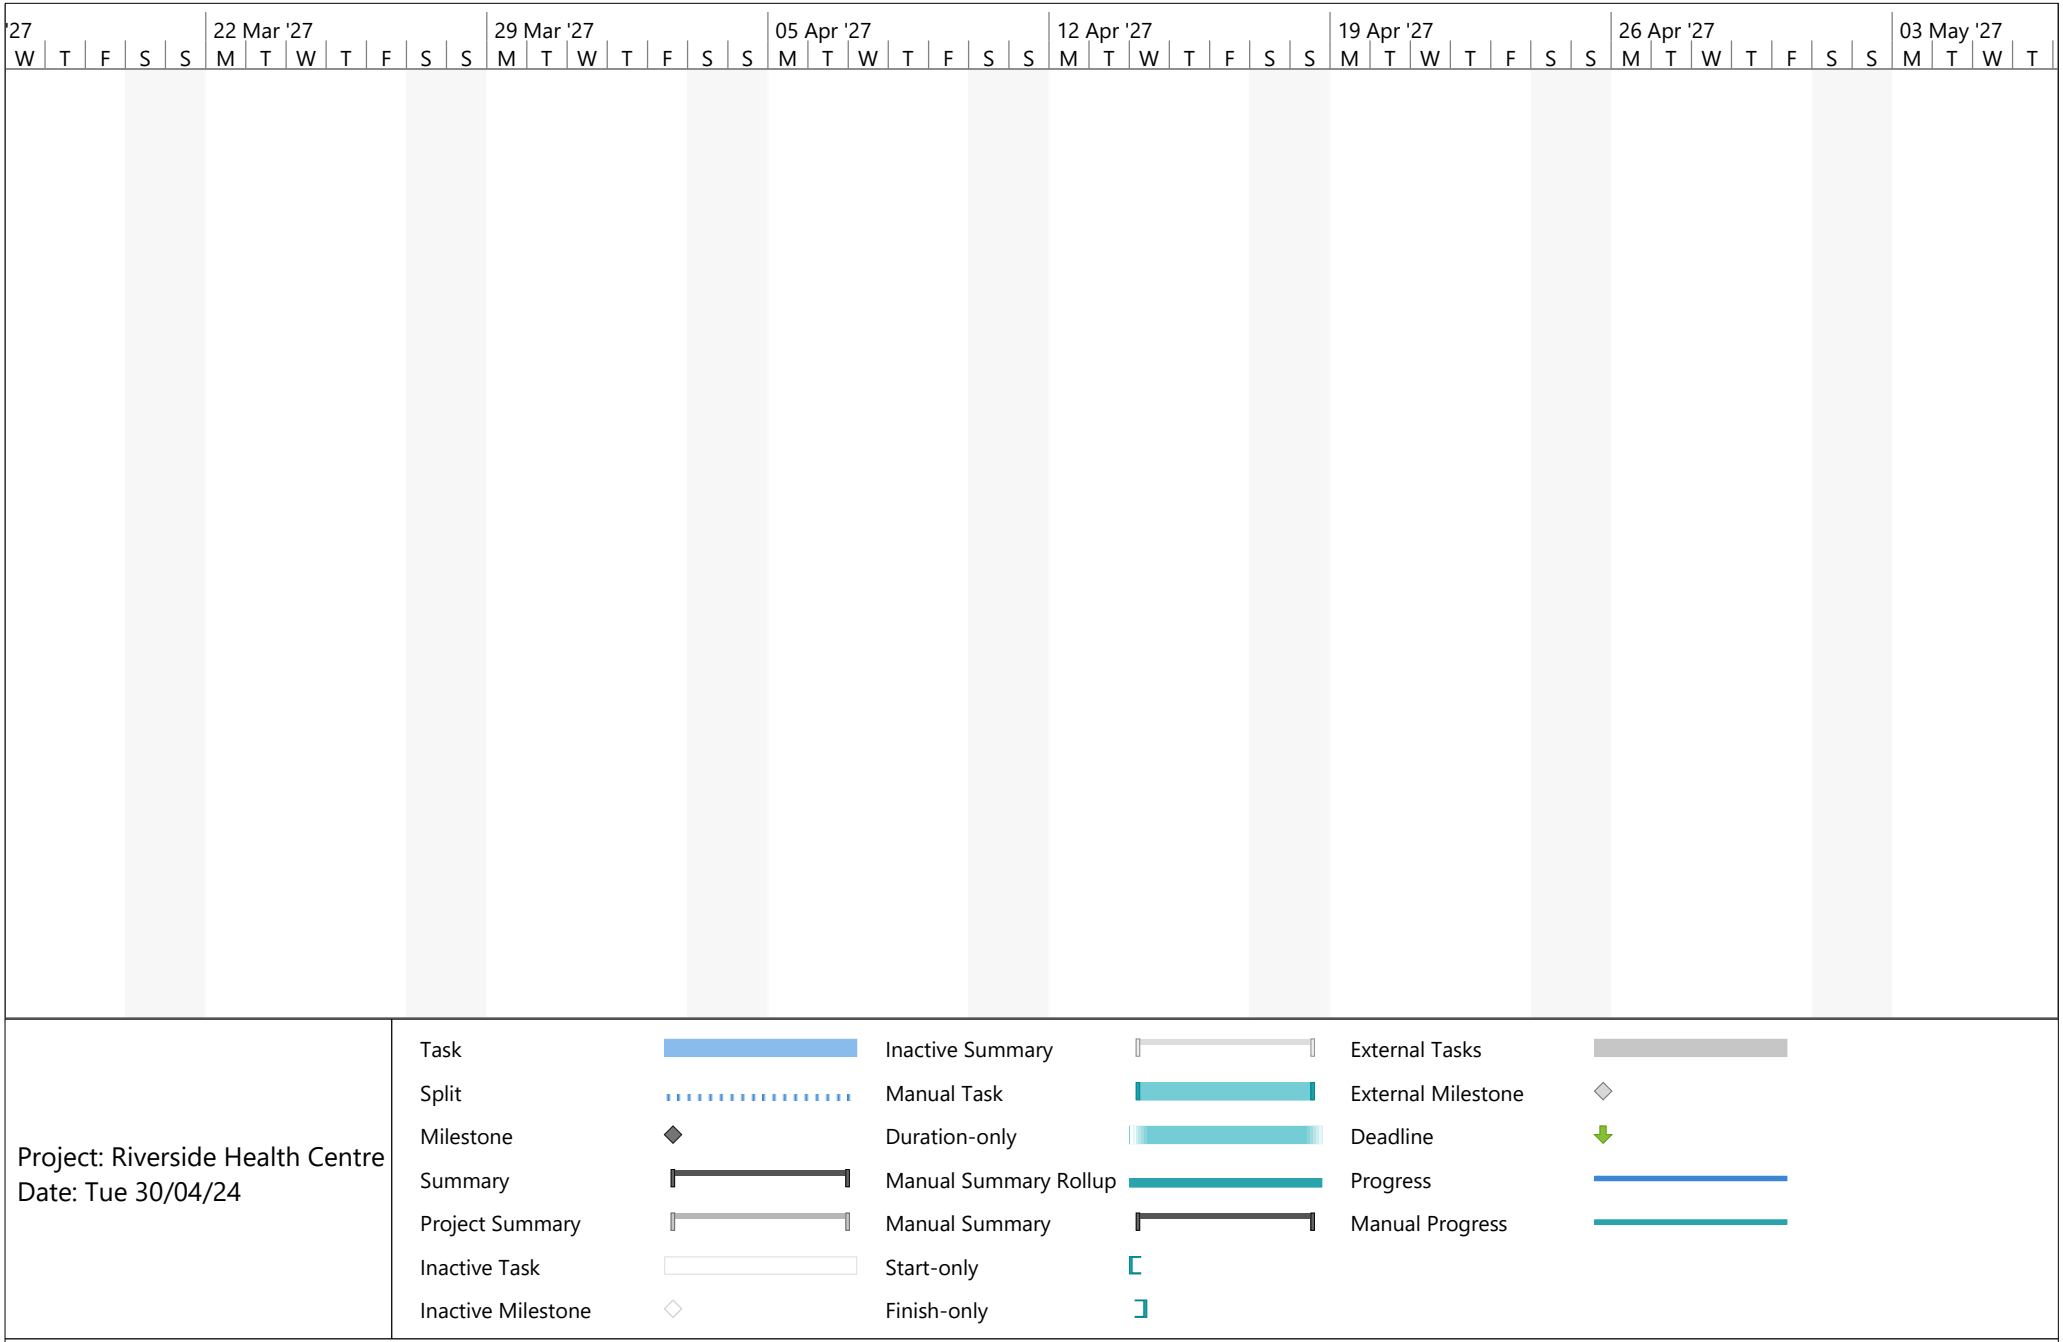
'27
W T F S S
22 Mar '27
M T W T F S S
29 Mar '27
M T W T F S S
05 Apr '27
M T W T F S S
12 Apr '27
M T W T F S S
19 Apr '27
M T W T F S S
26 Apr '27
M T W T F S S
03 May '27
M T W T
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

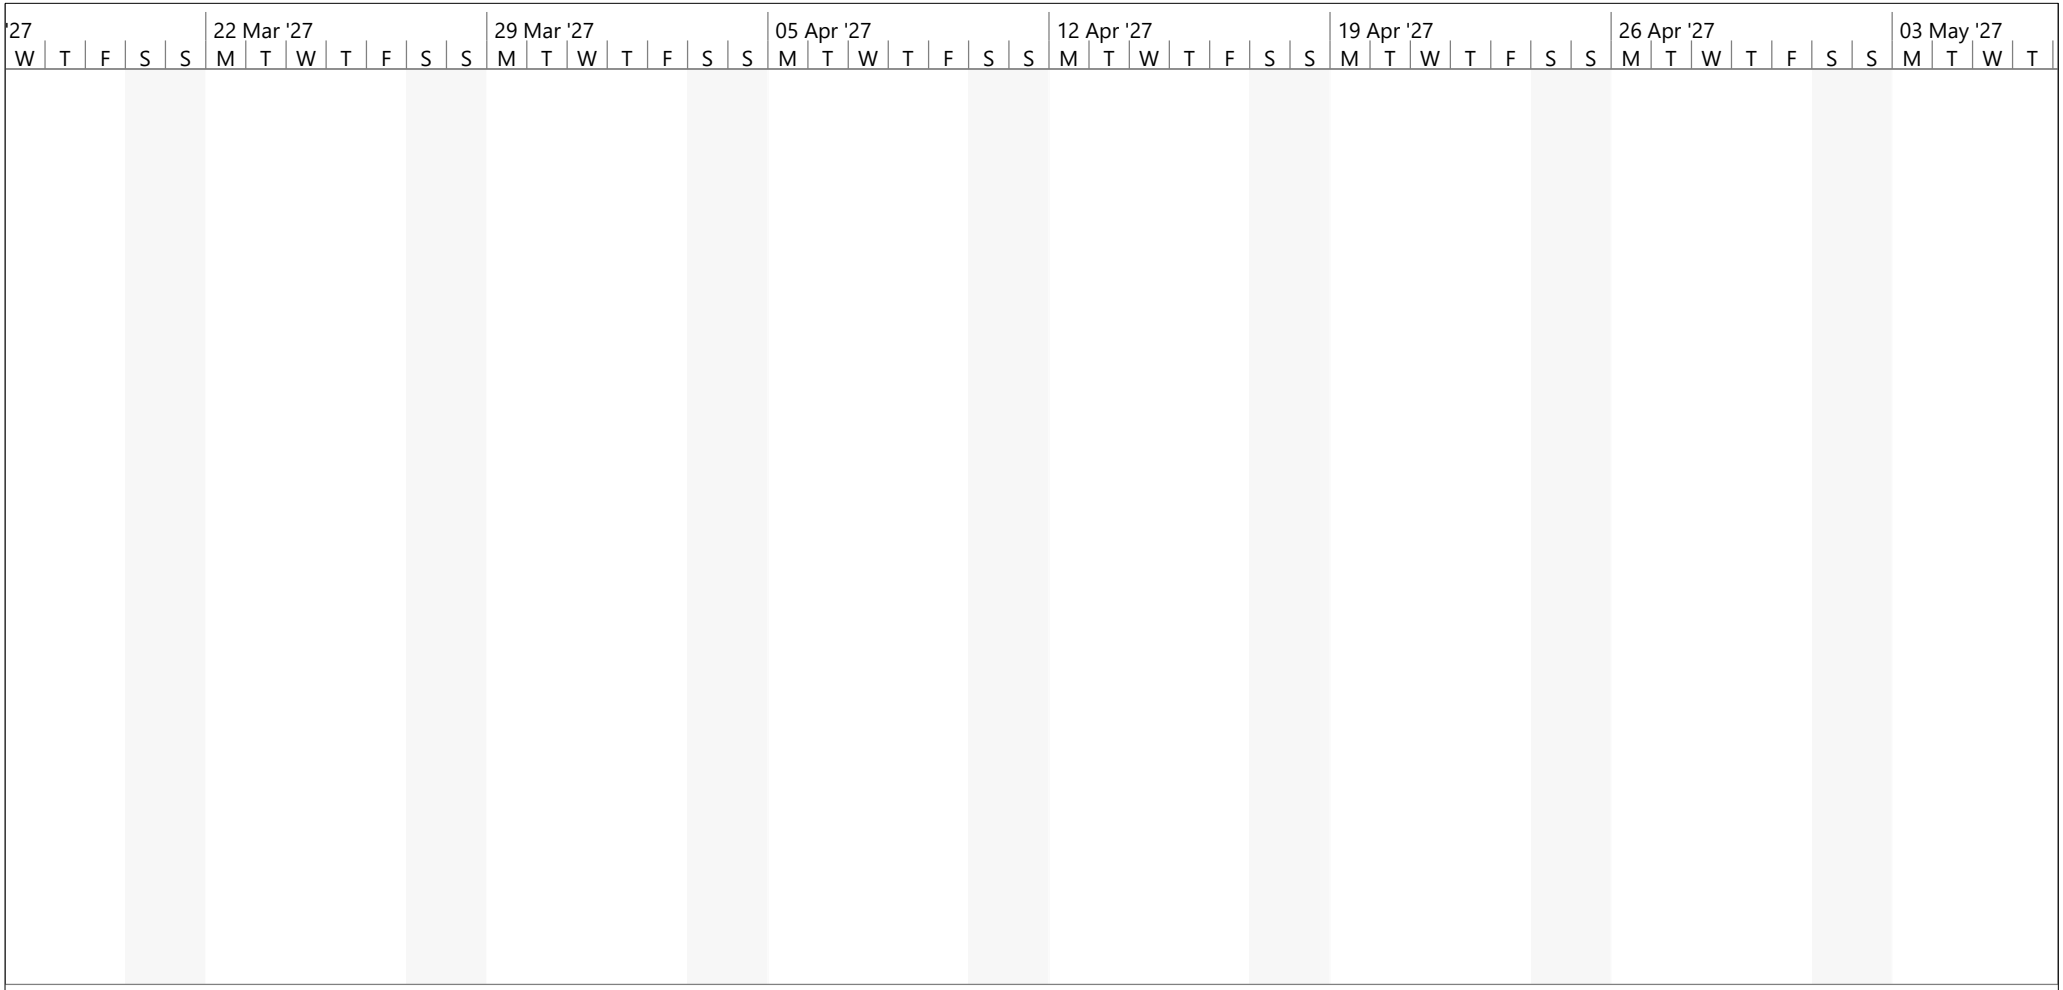


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

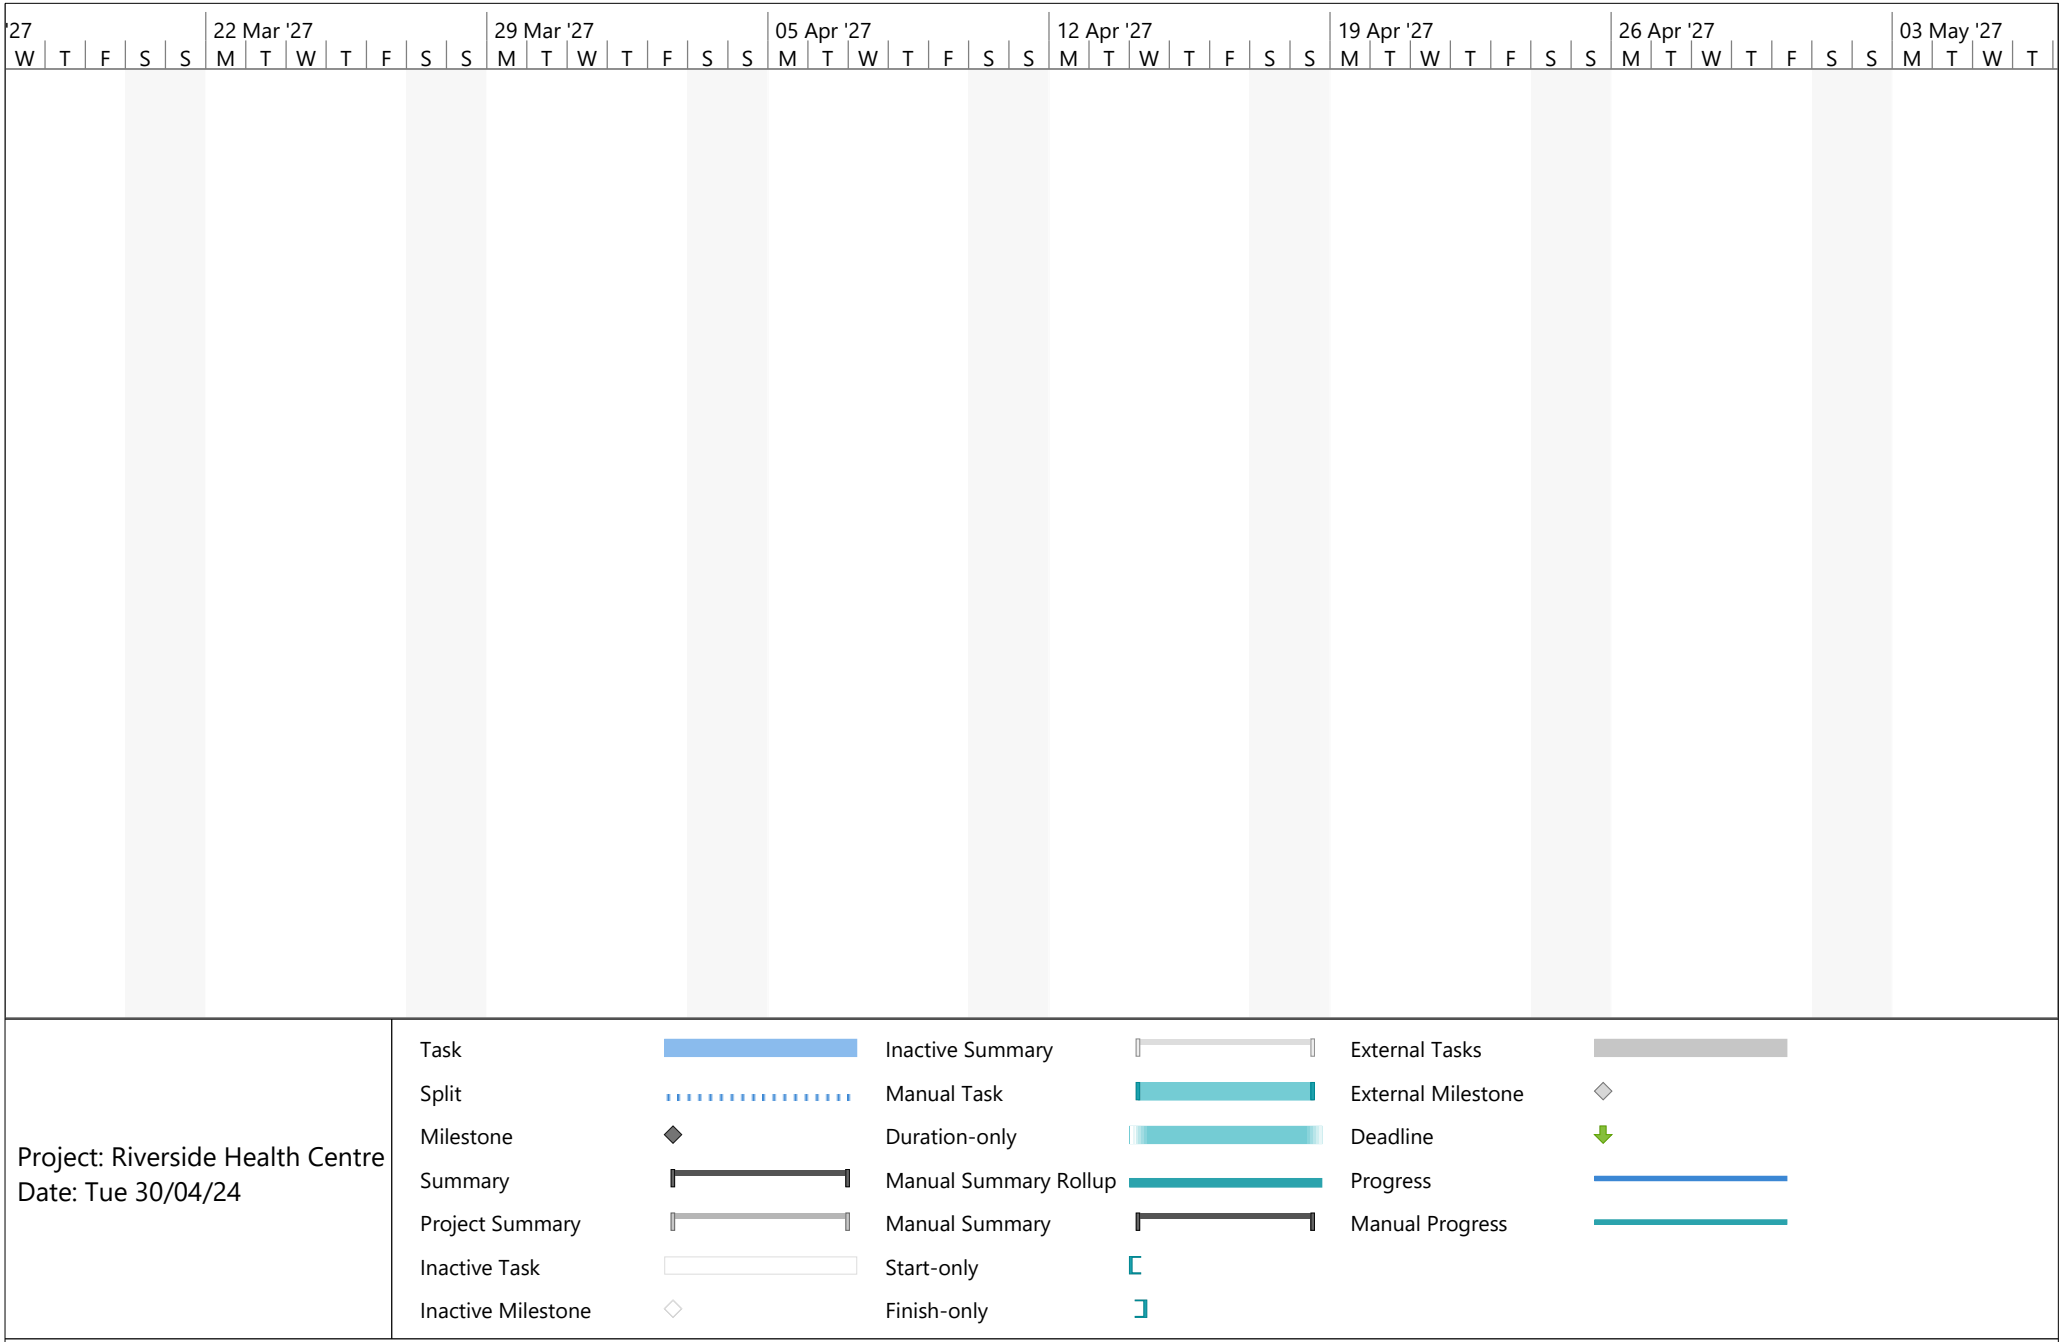


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

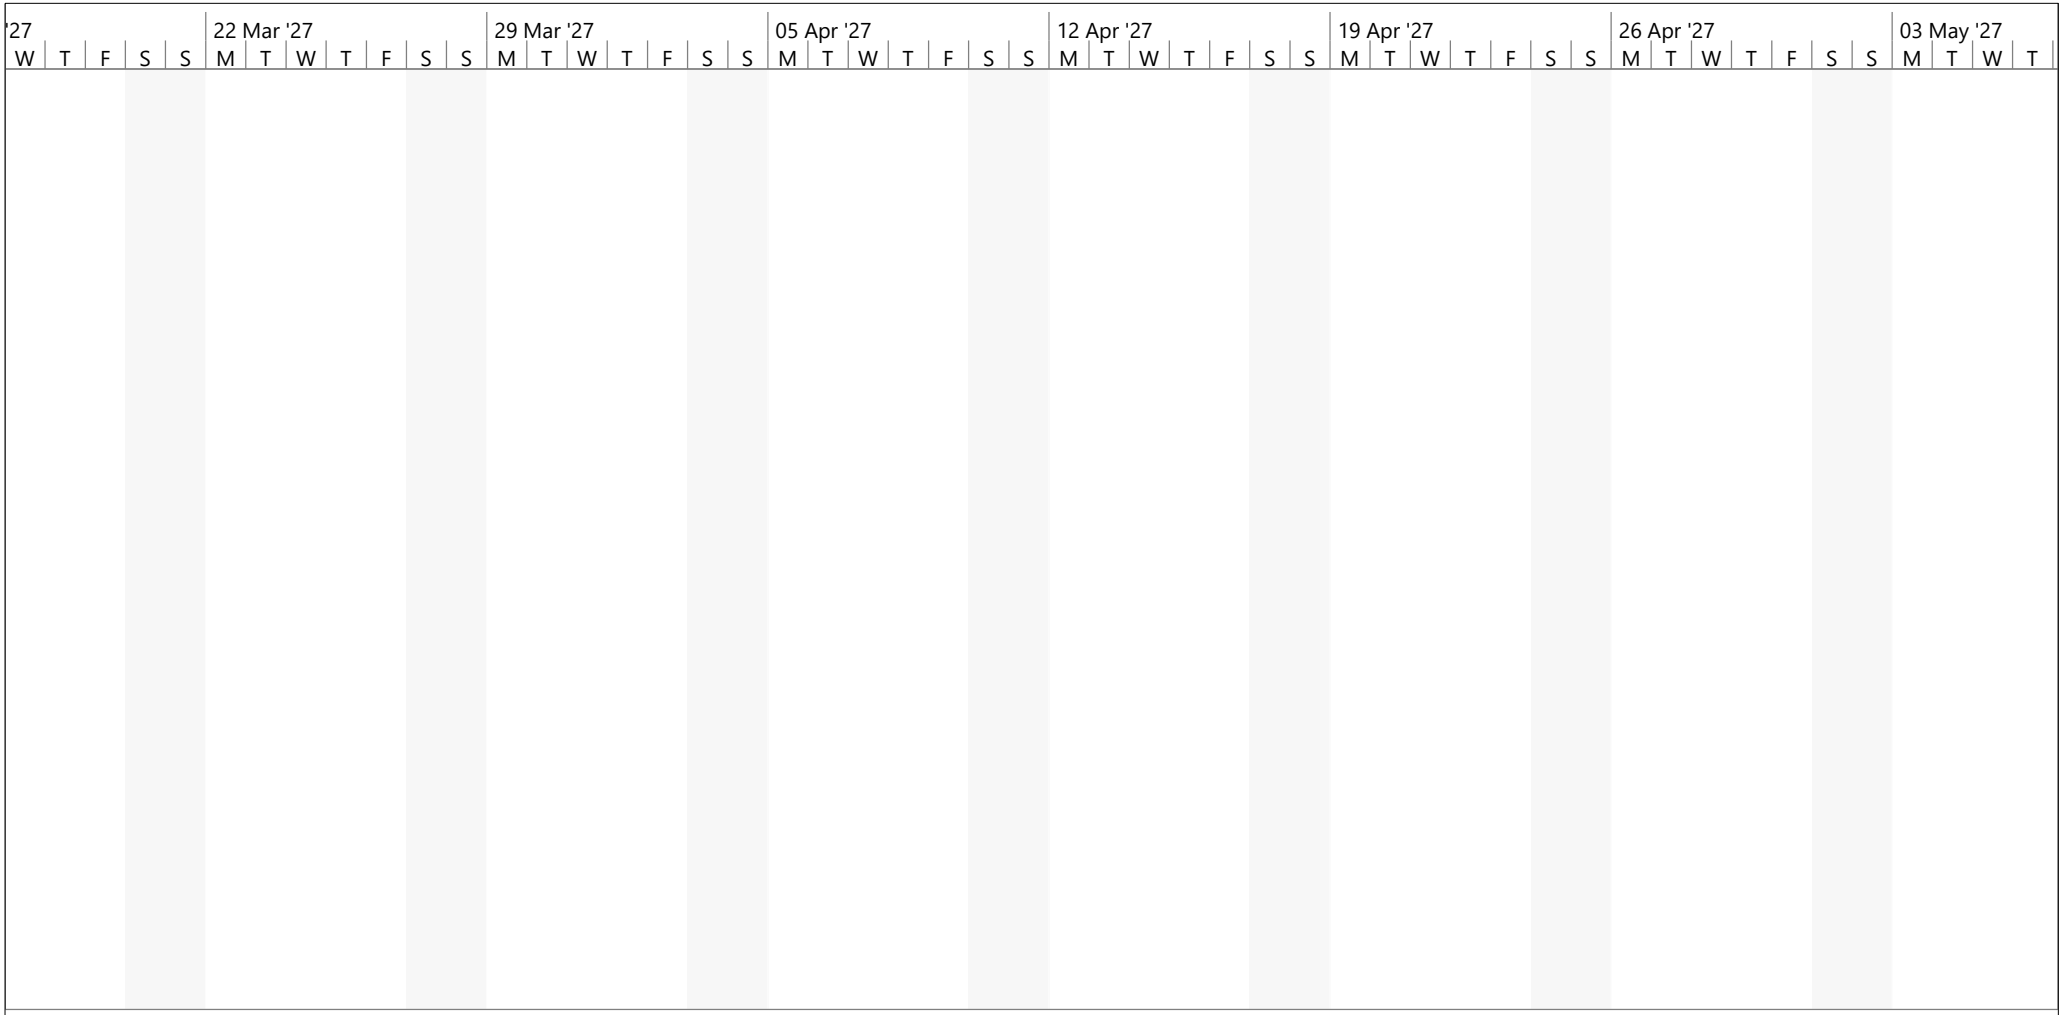


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

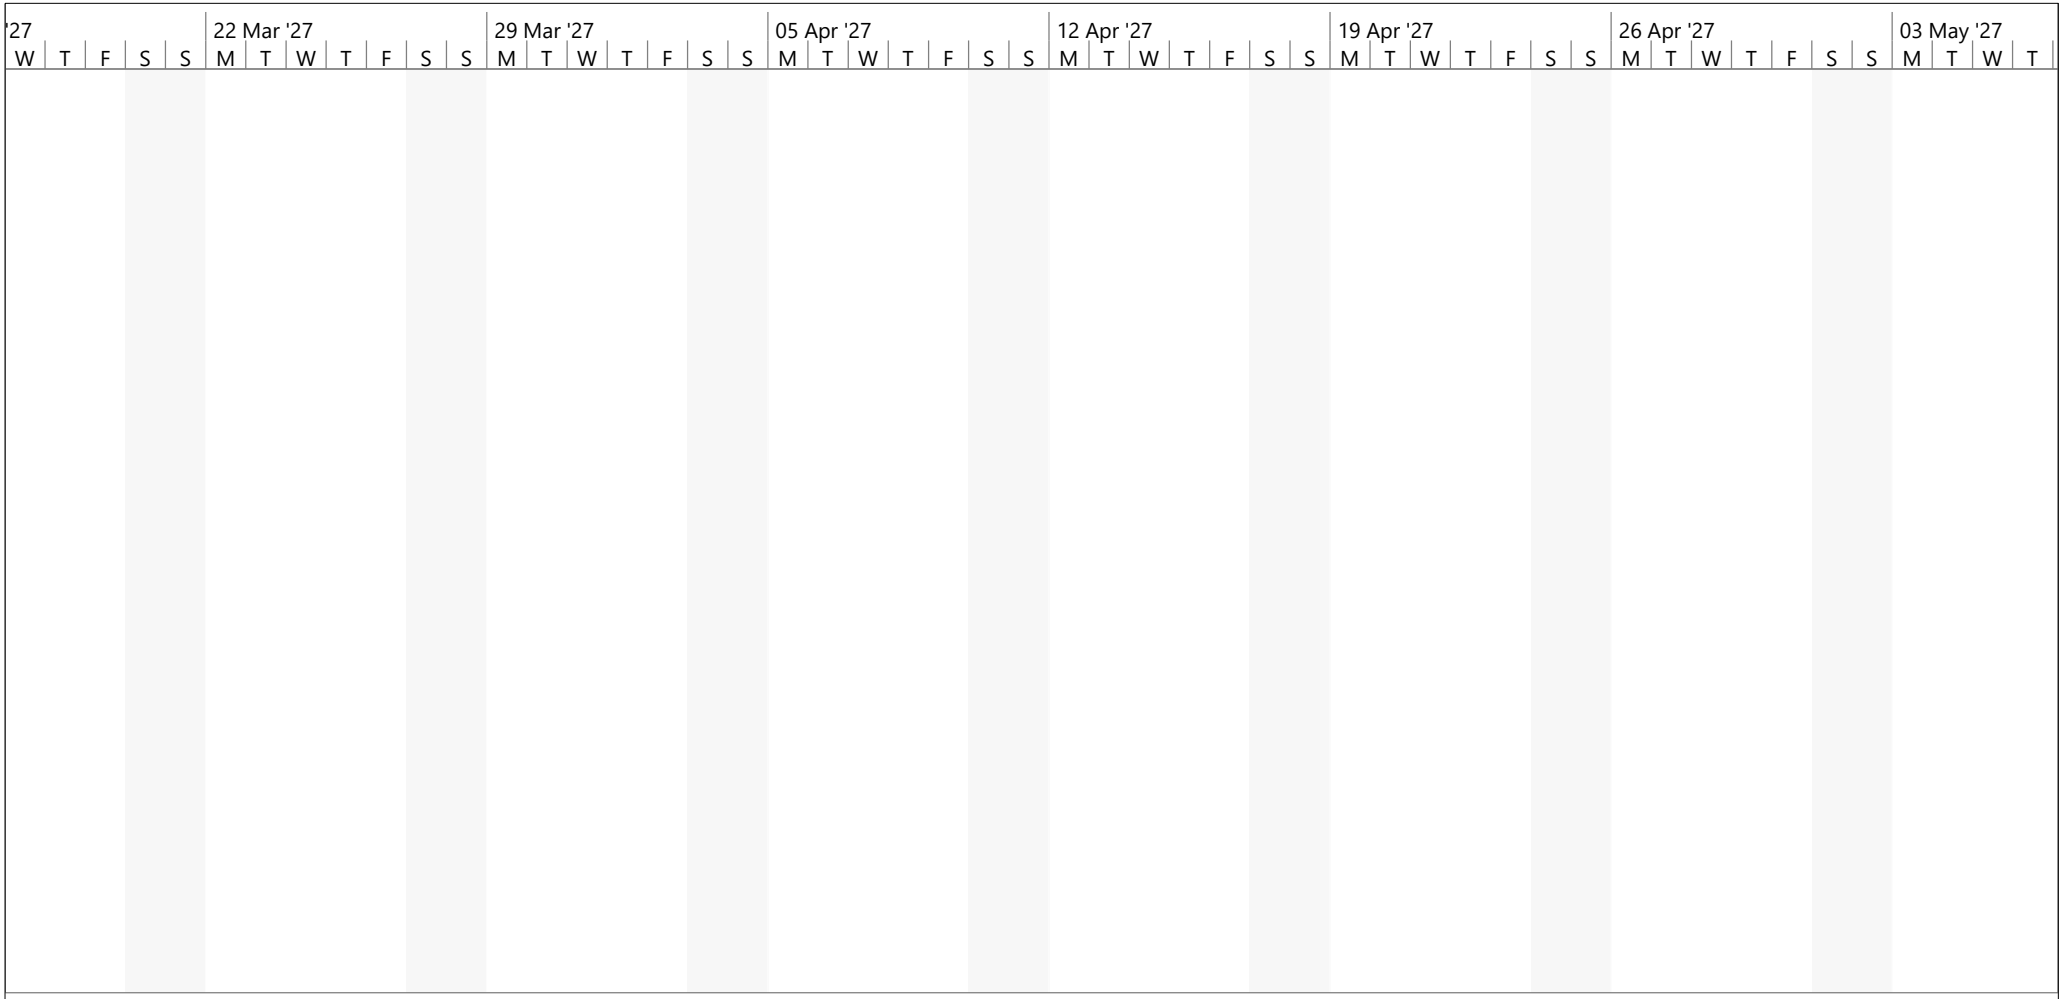


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

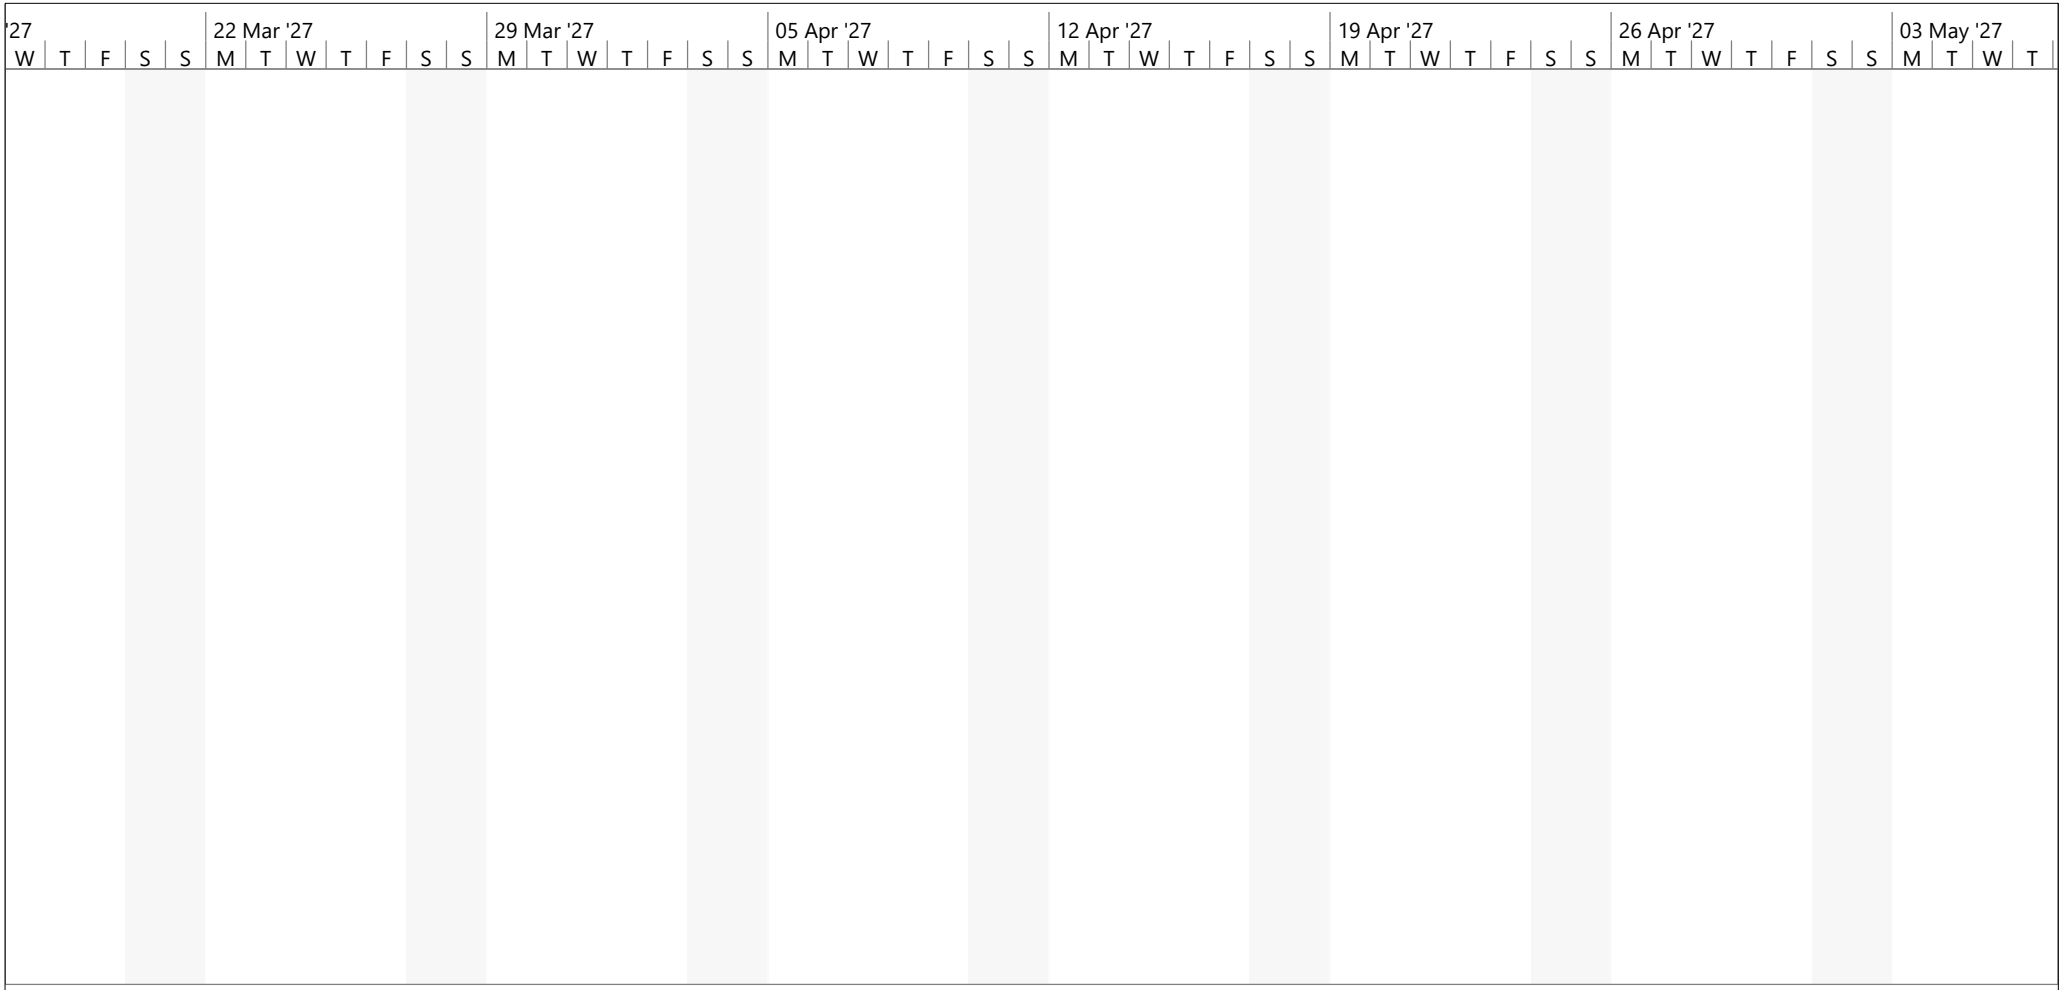

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

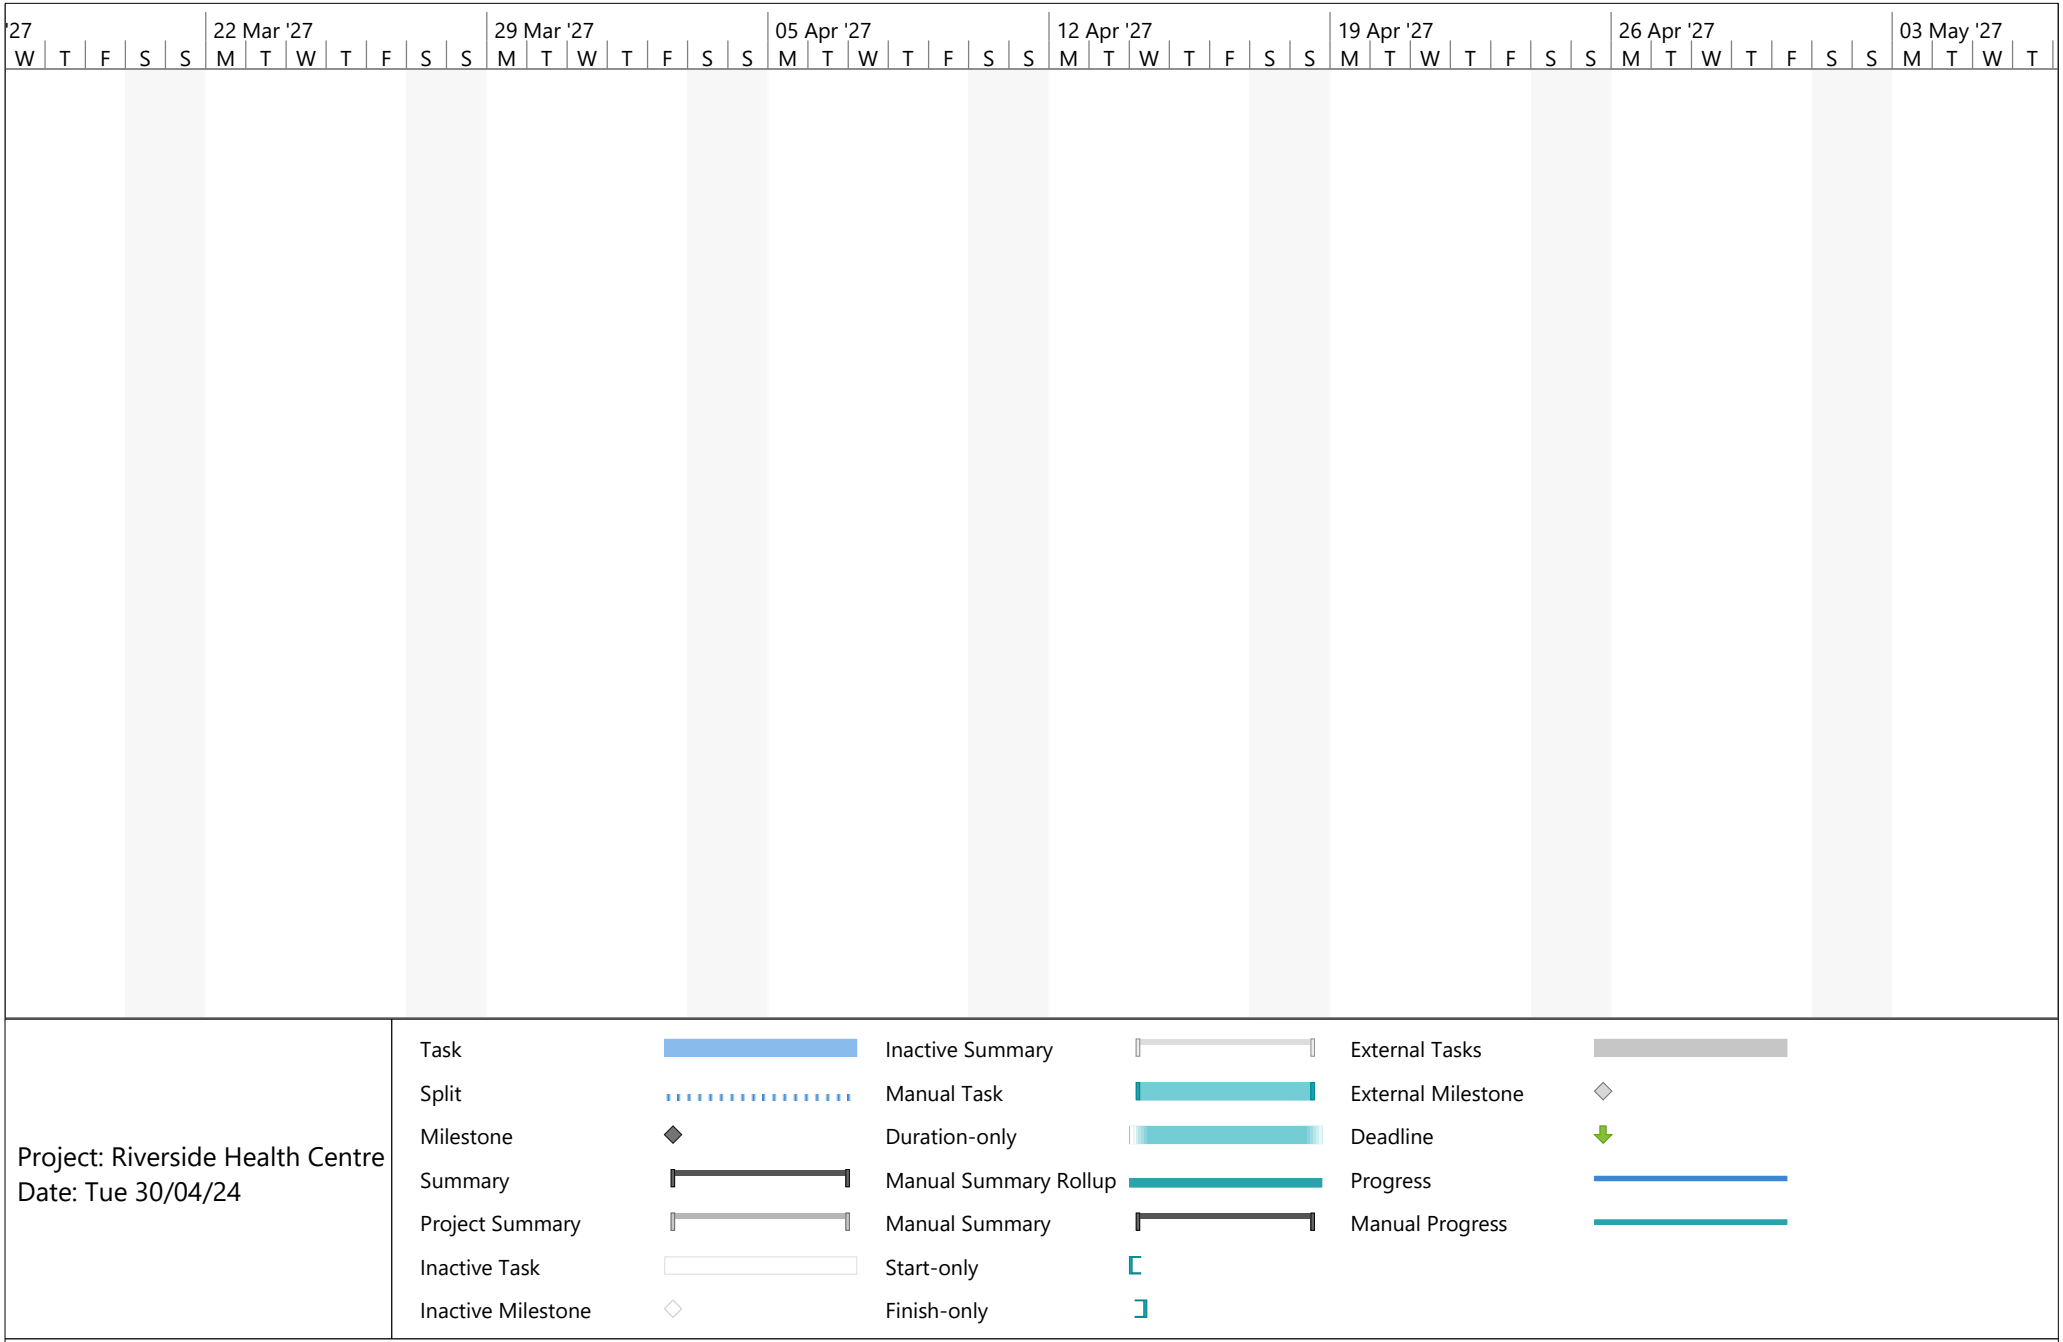
'27
W T F S S
22 Mar '27
M T W T F S S
29 Mar '27
M T W T F S S
05 Apr '27
M T W T F S S
12 Apr '27
M T W T F S S
19 Apr '27
M T W T F S S
26 Apr '27
M T W T F S S
03 May '27
M T W T
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

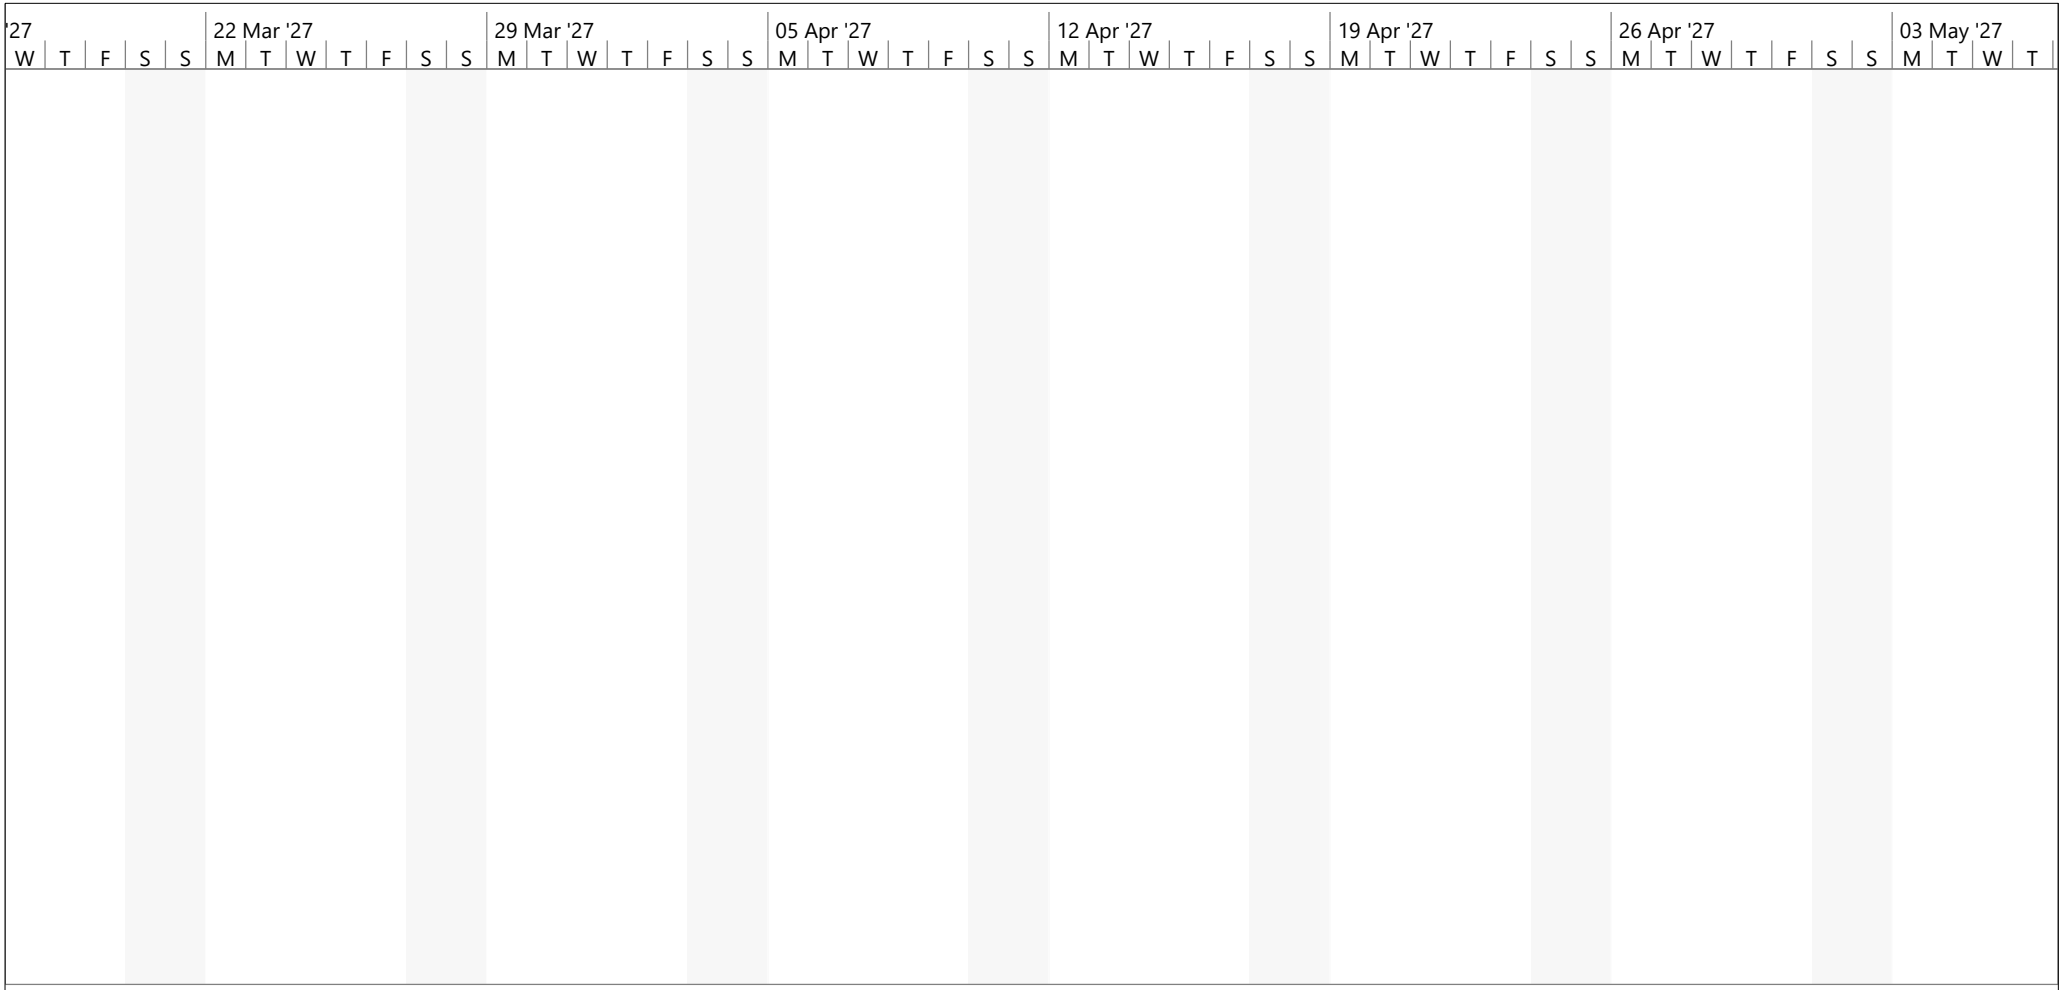


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

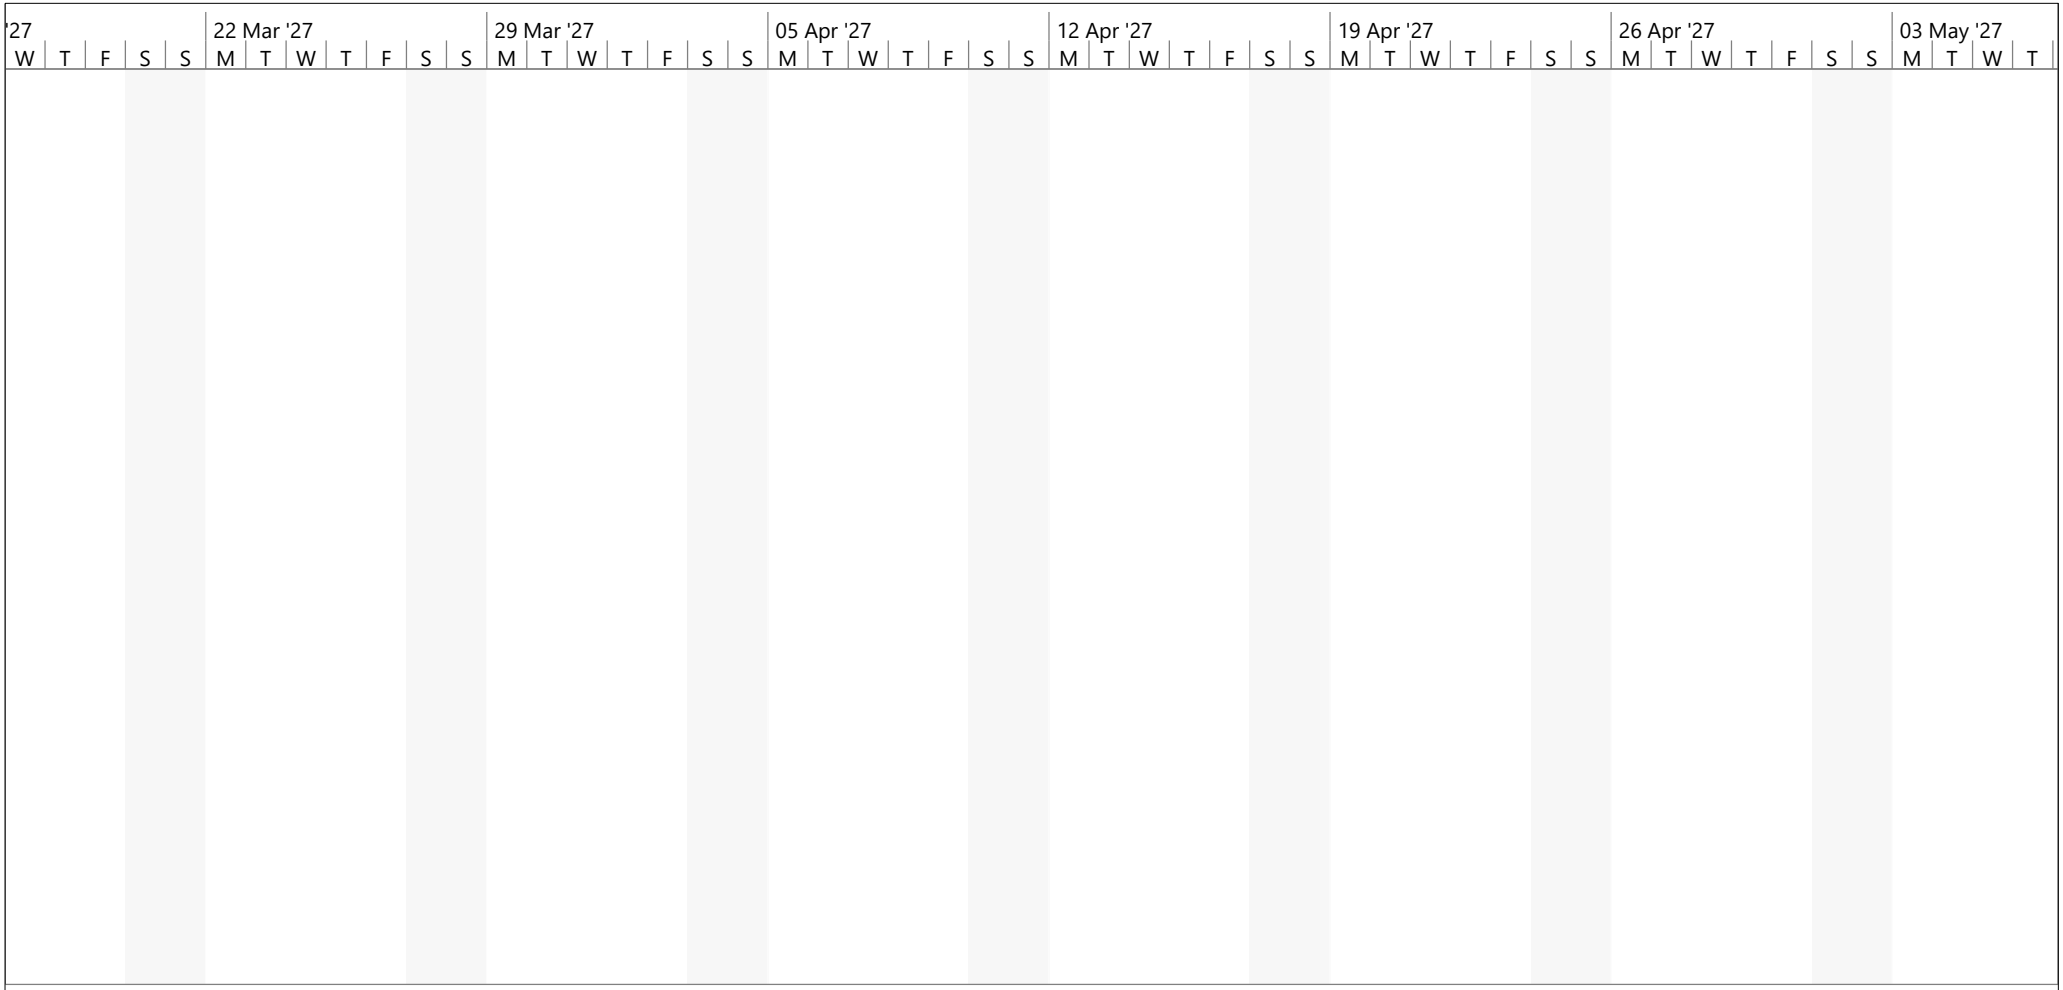


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

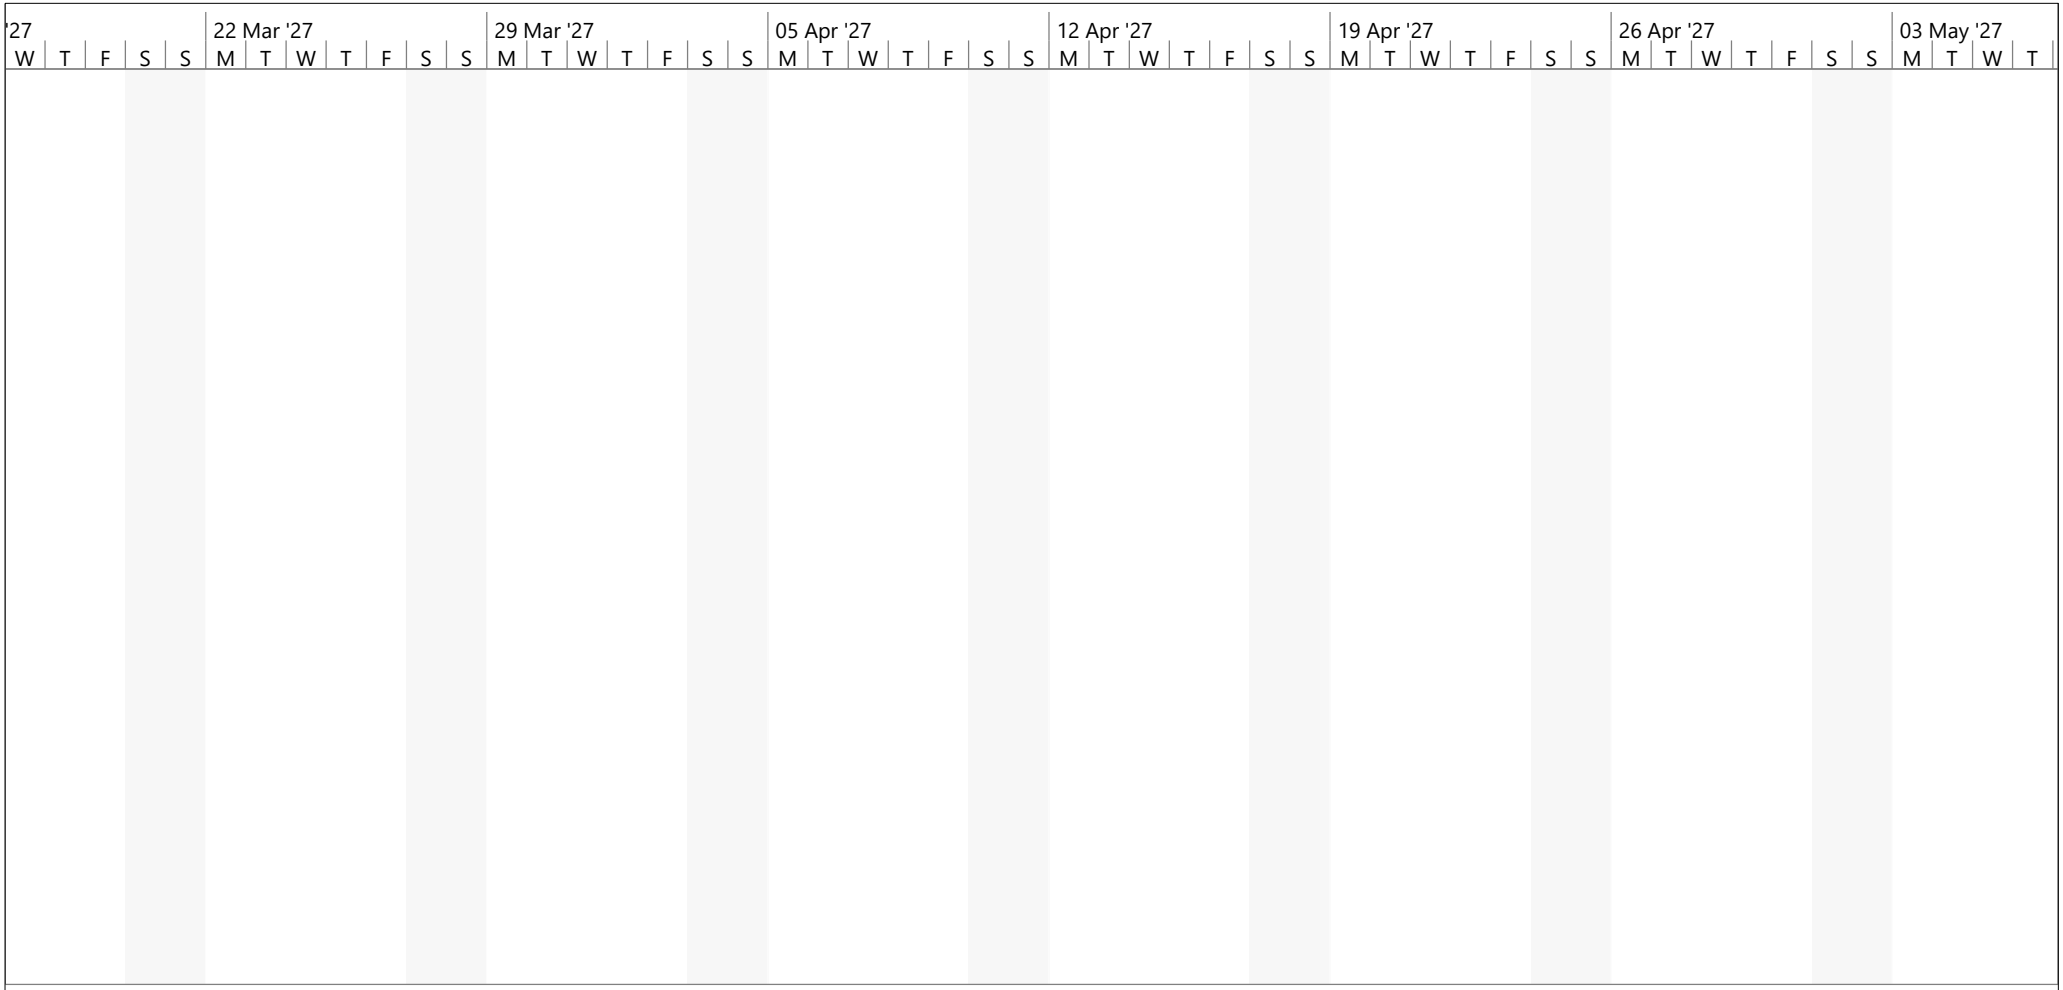


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

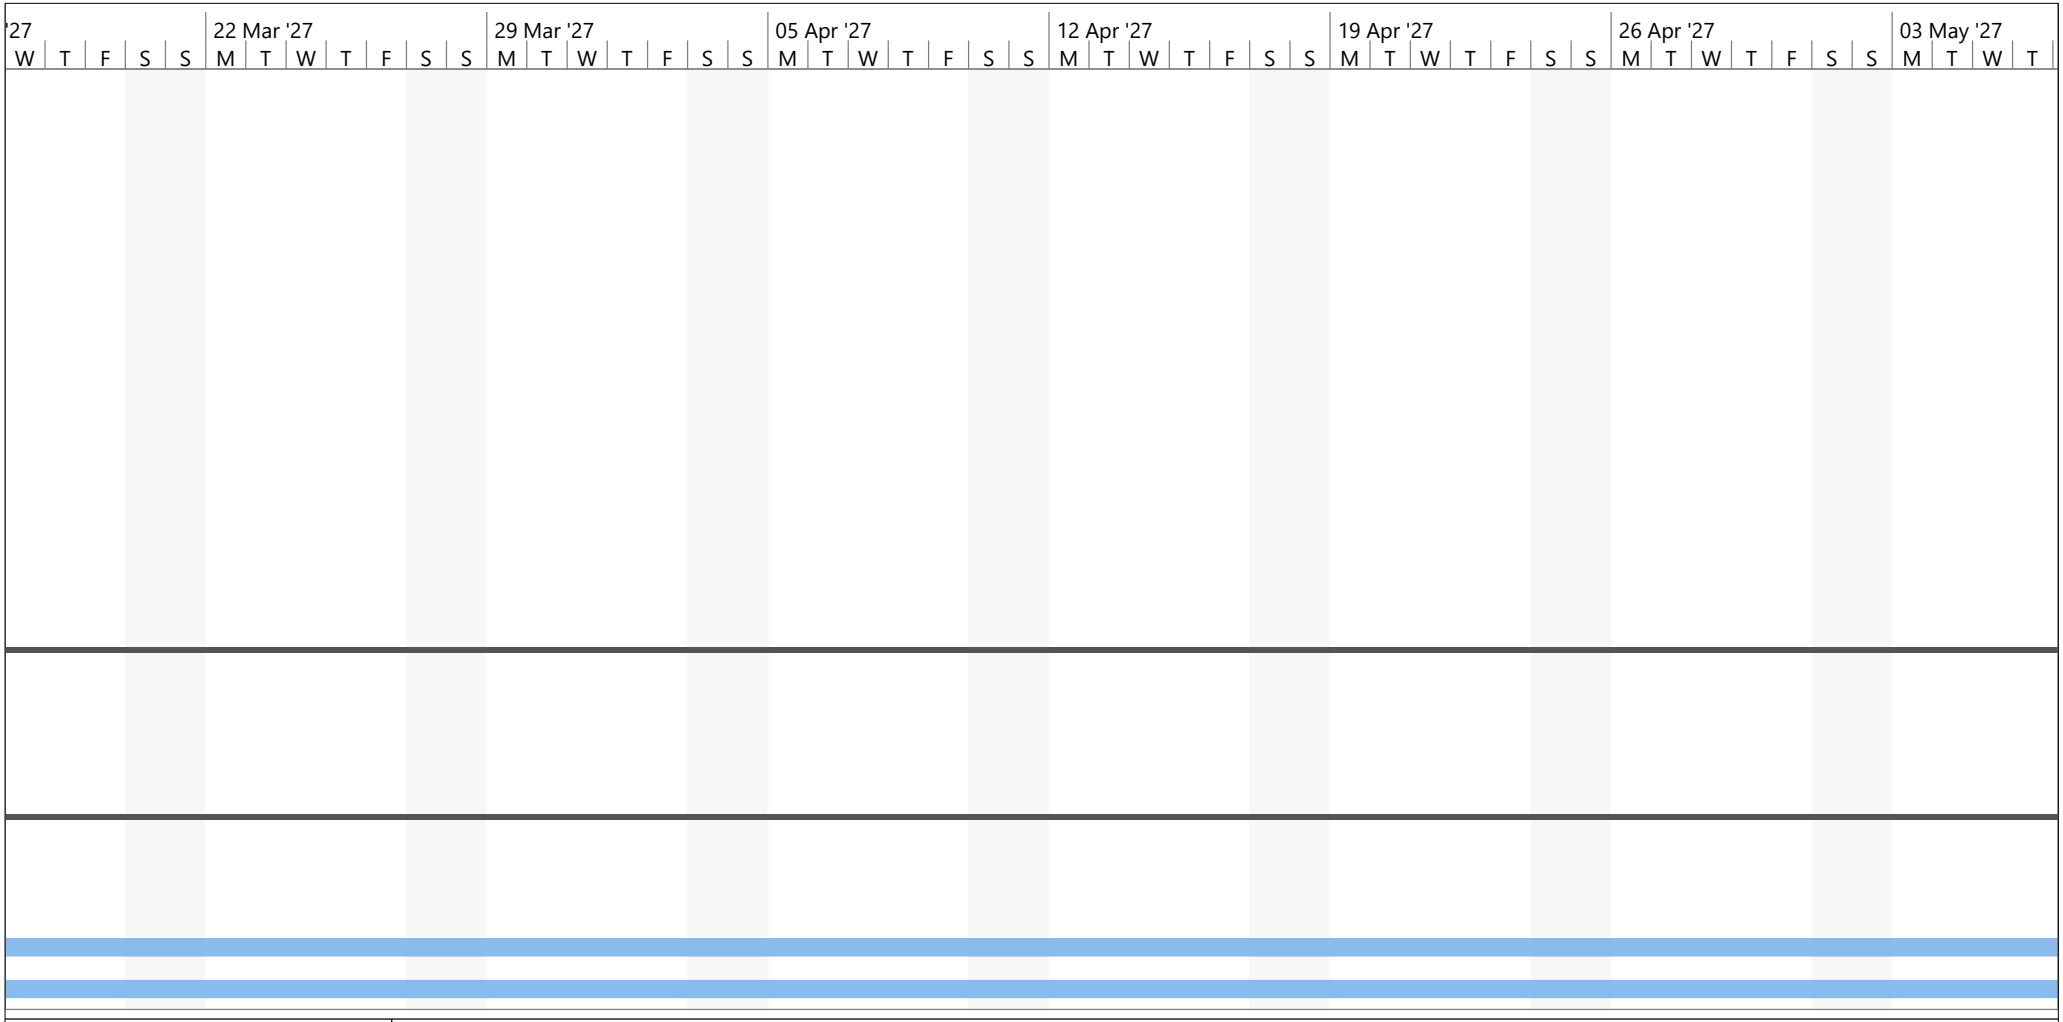


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	




Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

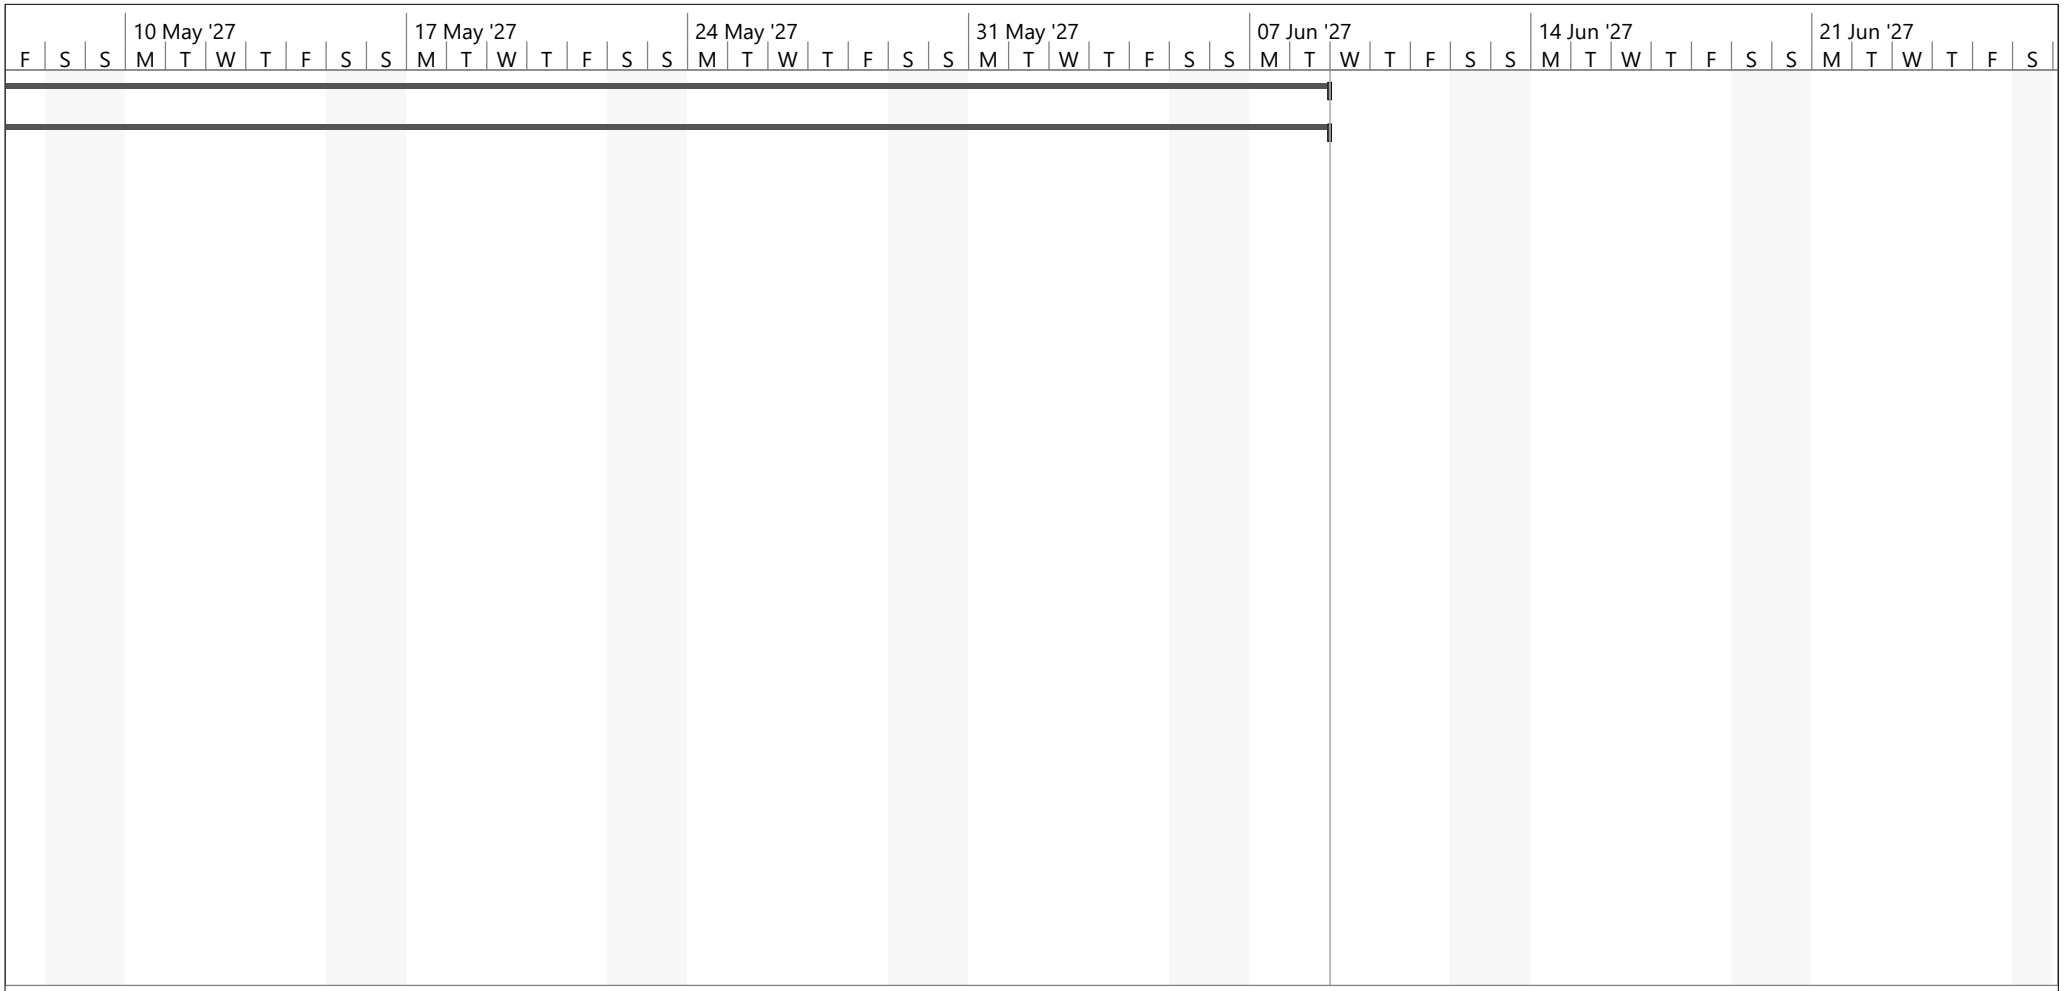


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

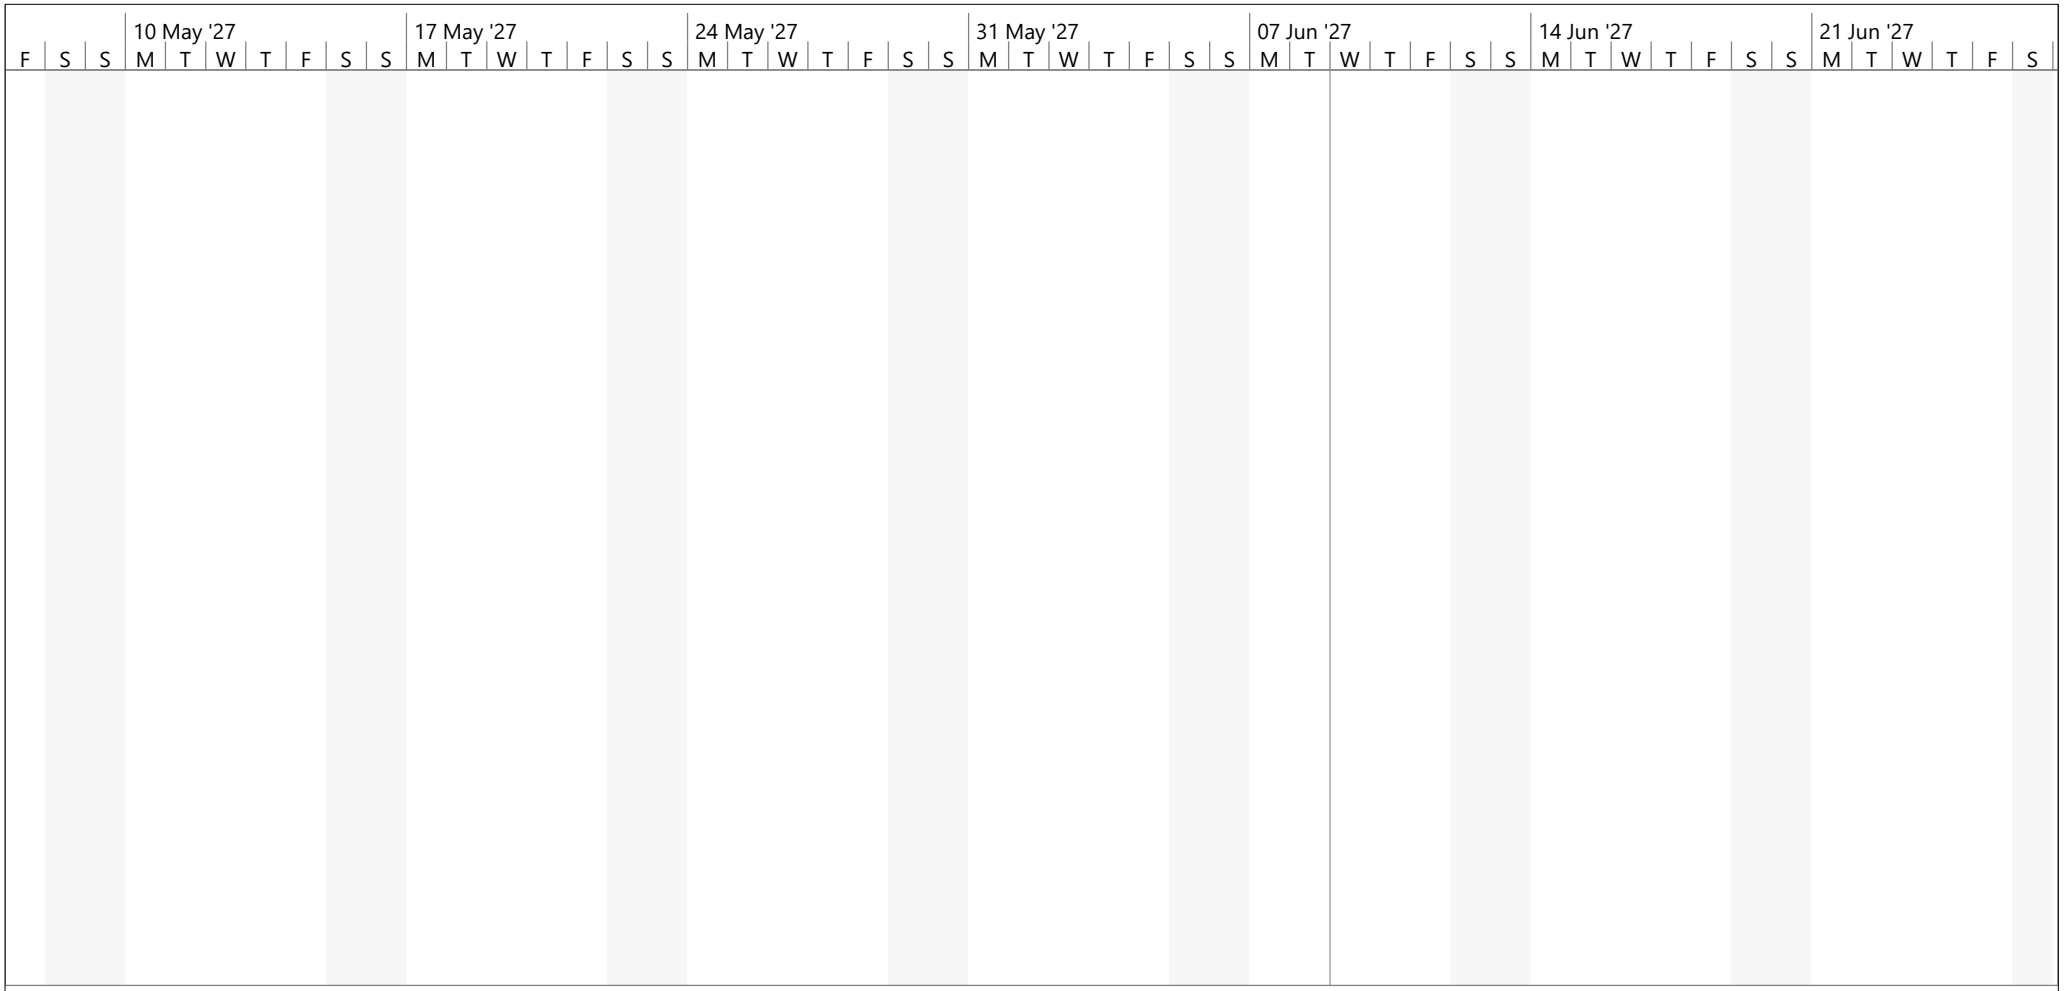


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

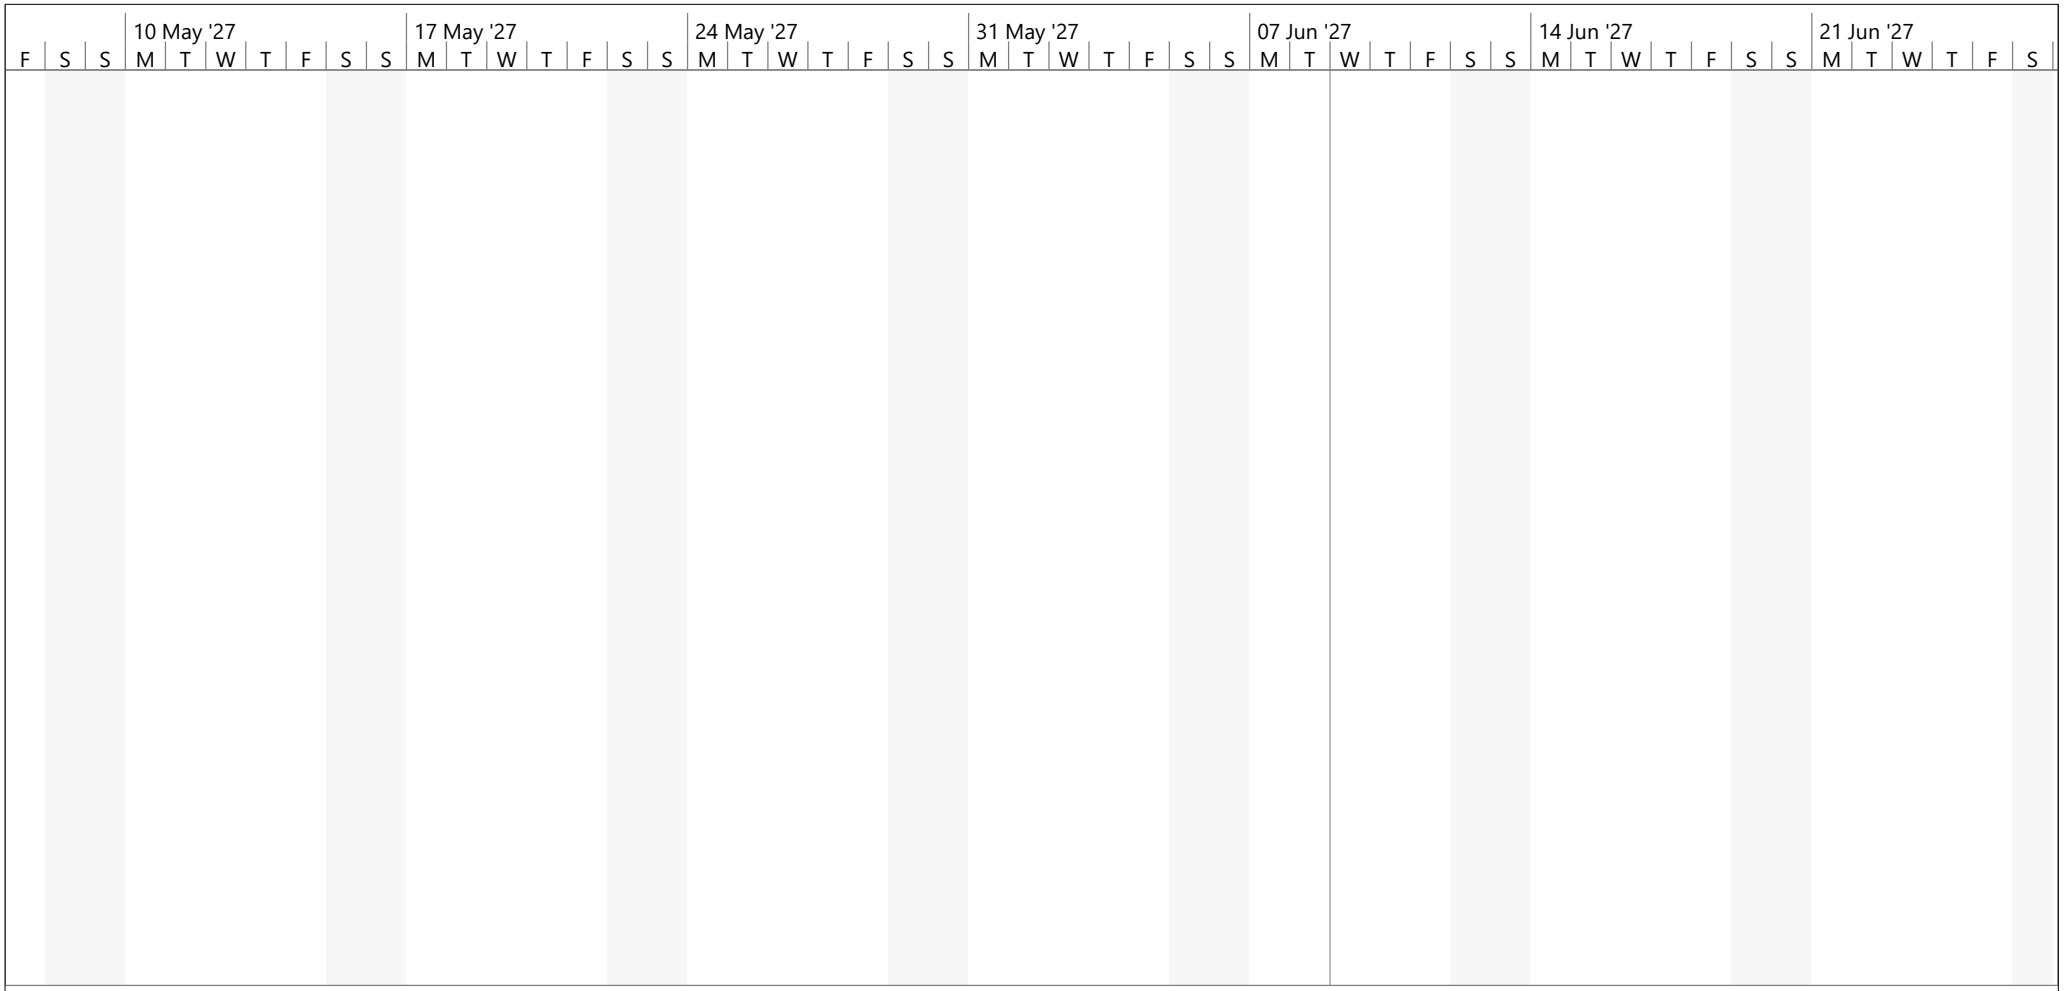


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

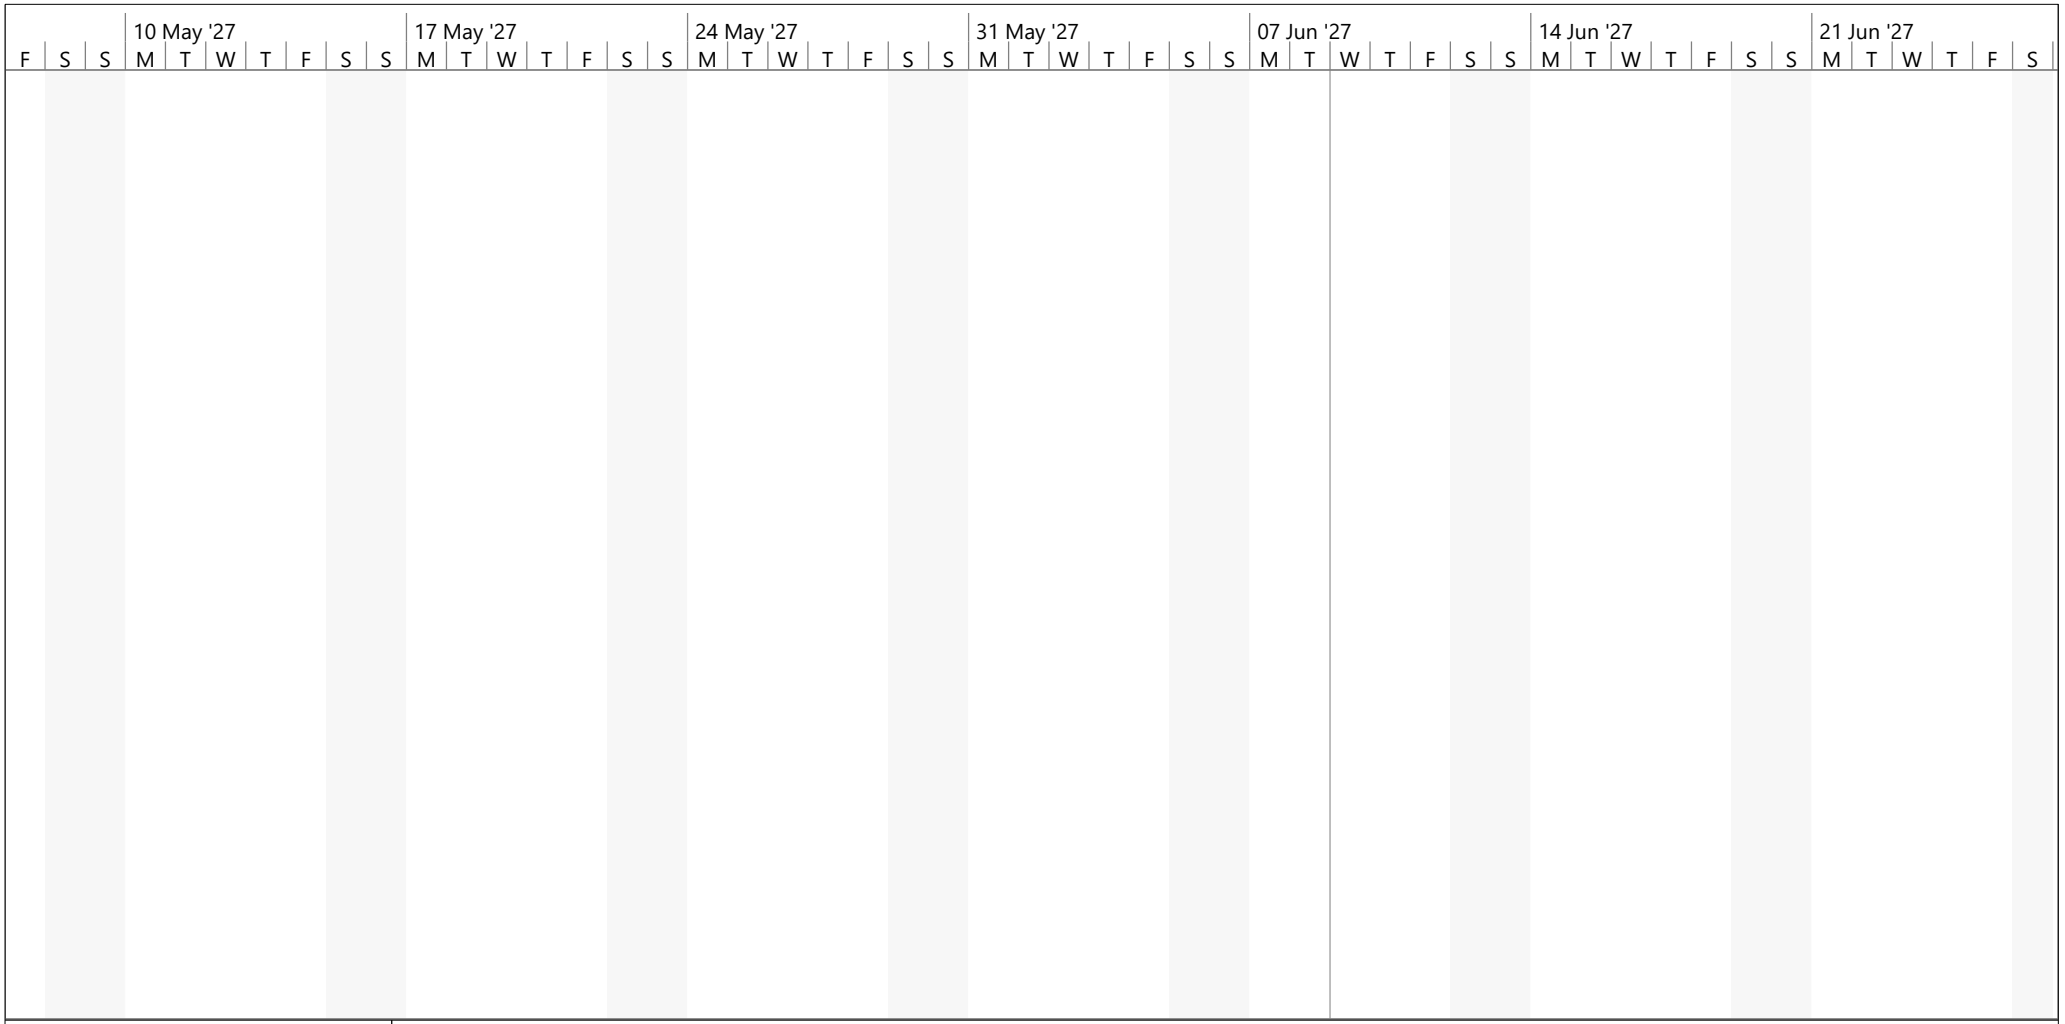


Project: Riverside Health Centre
Date: Tue 30/04/24


Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

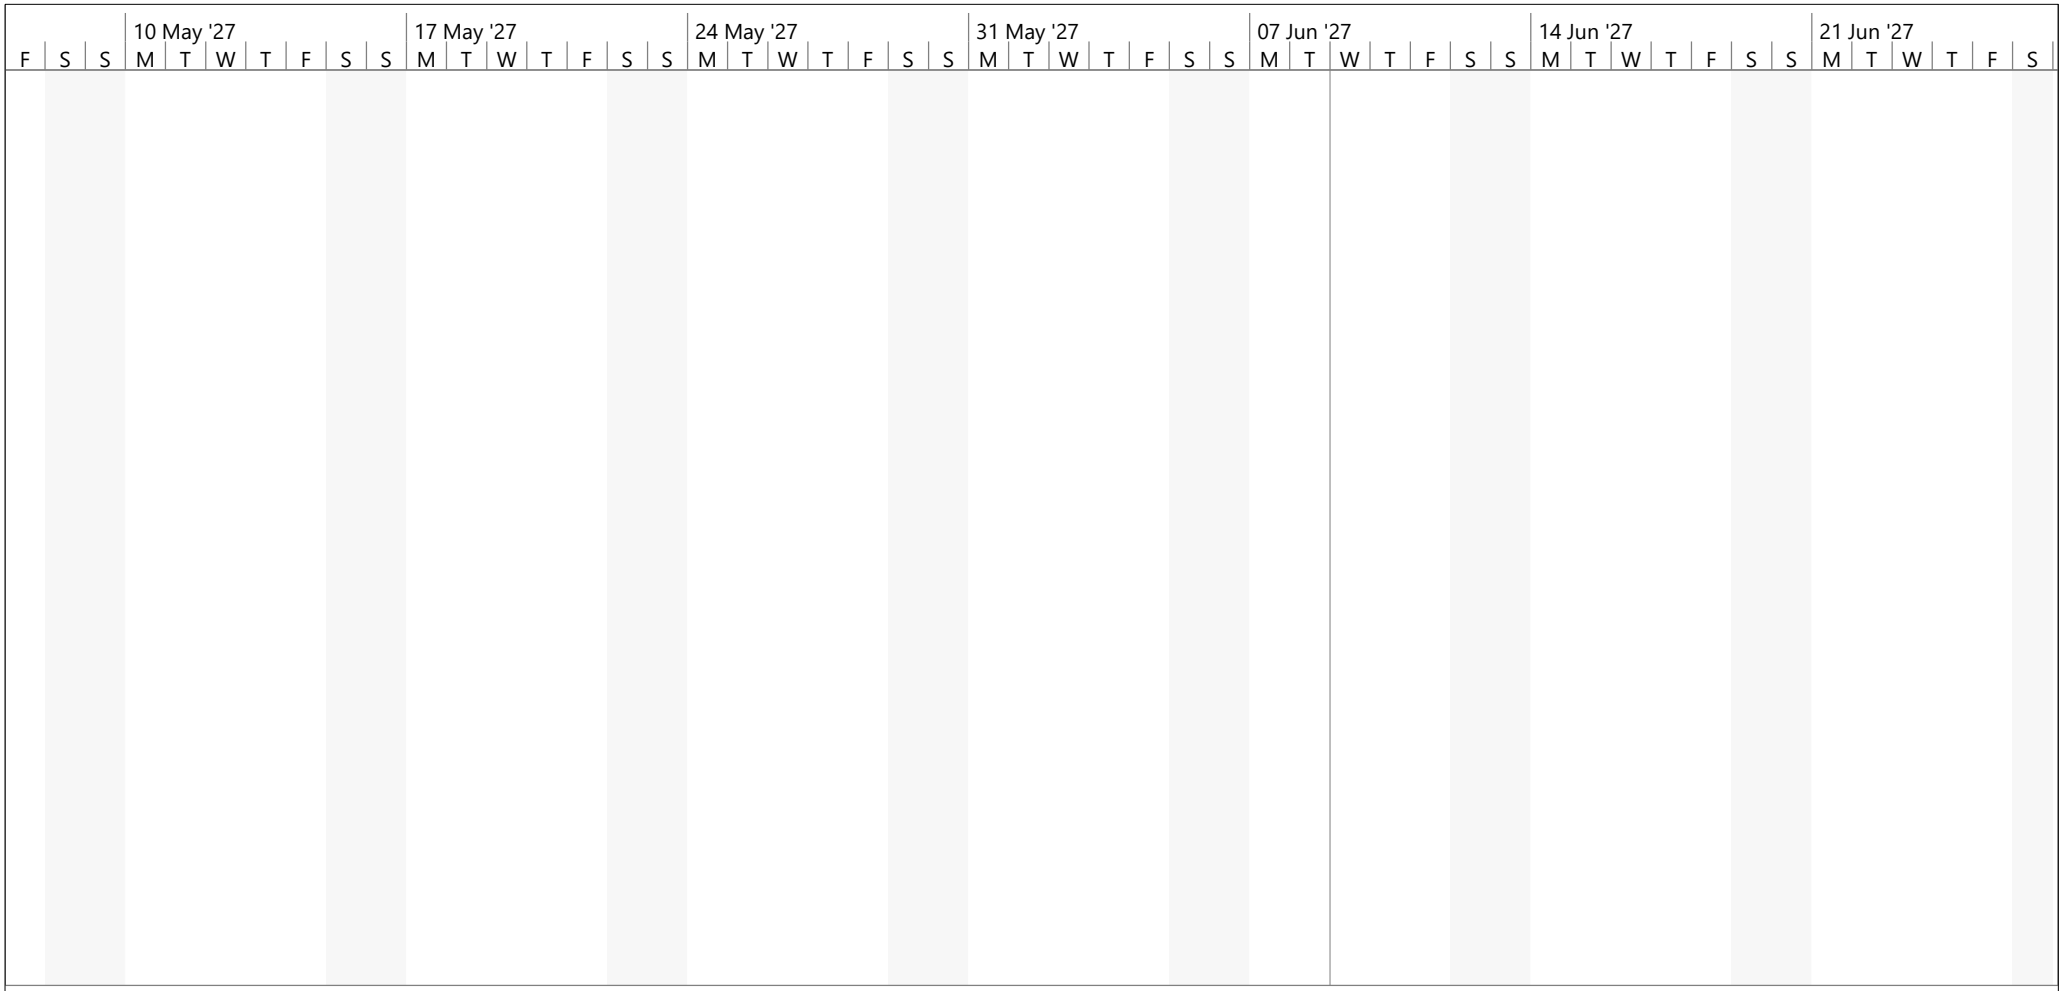

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

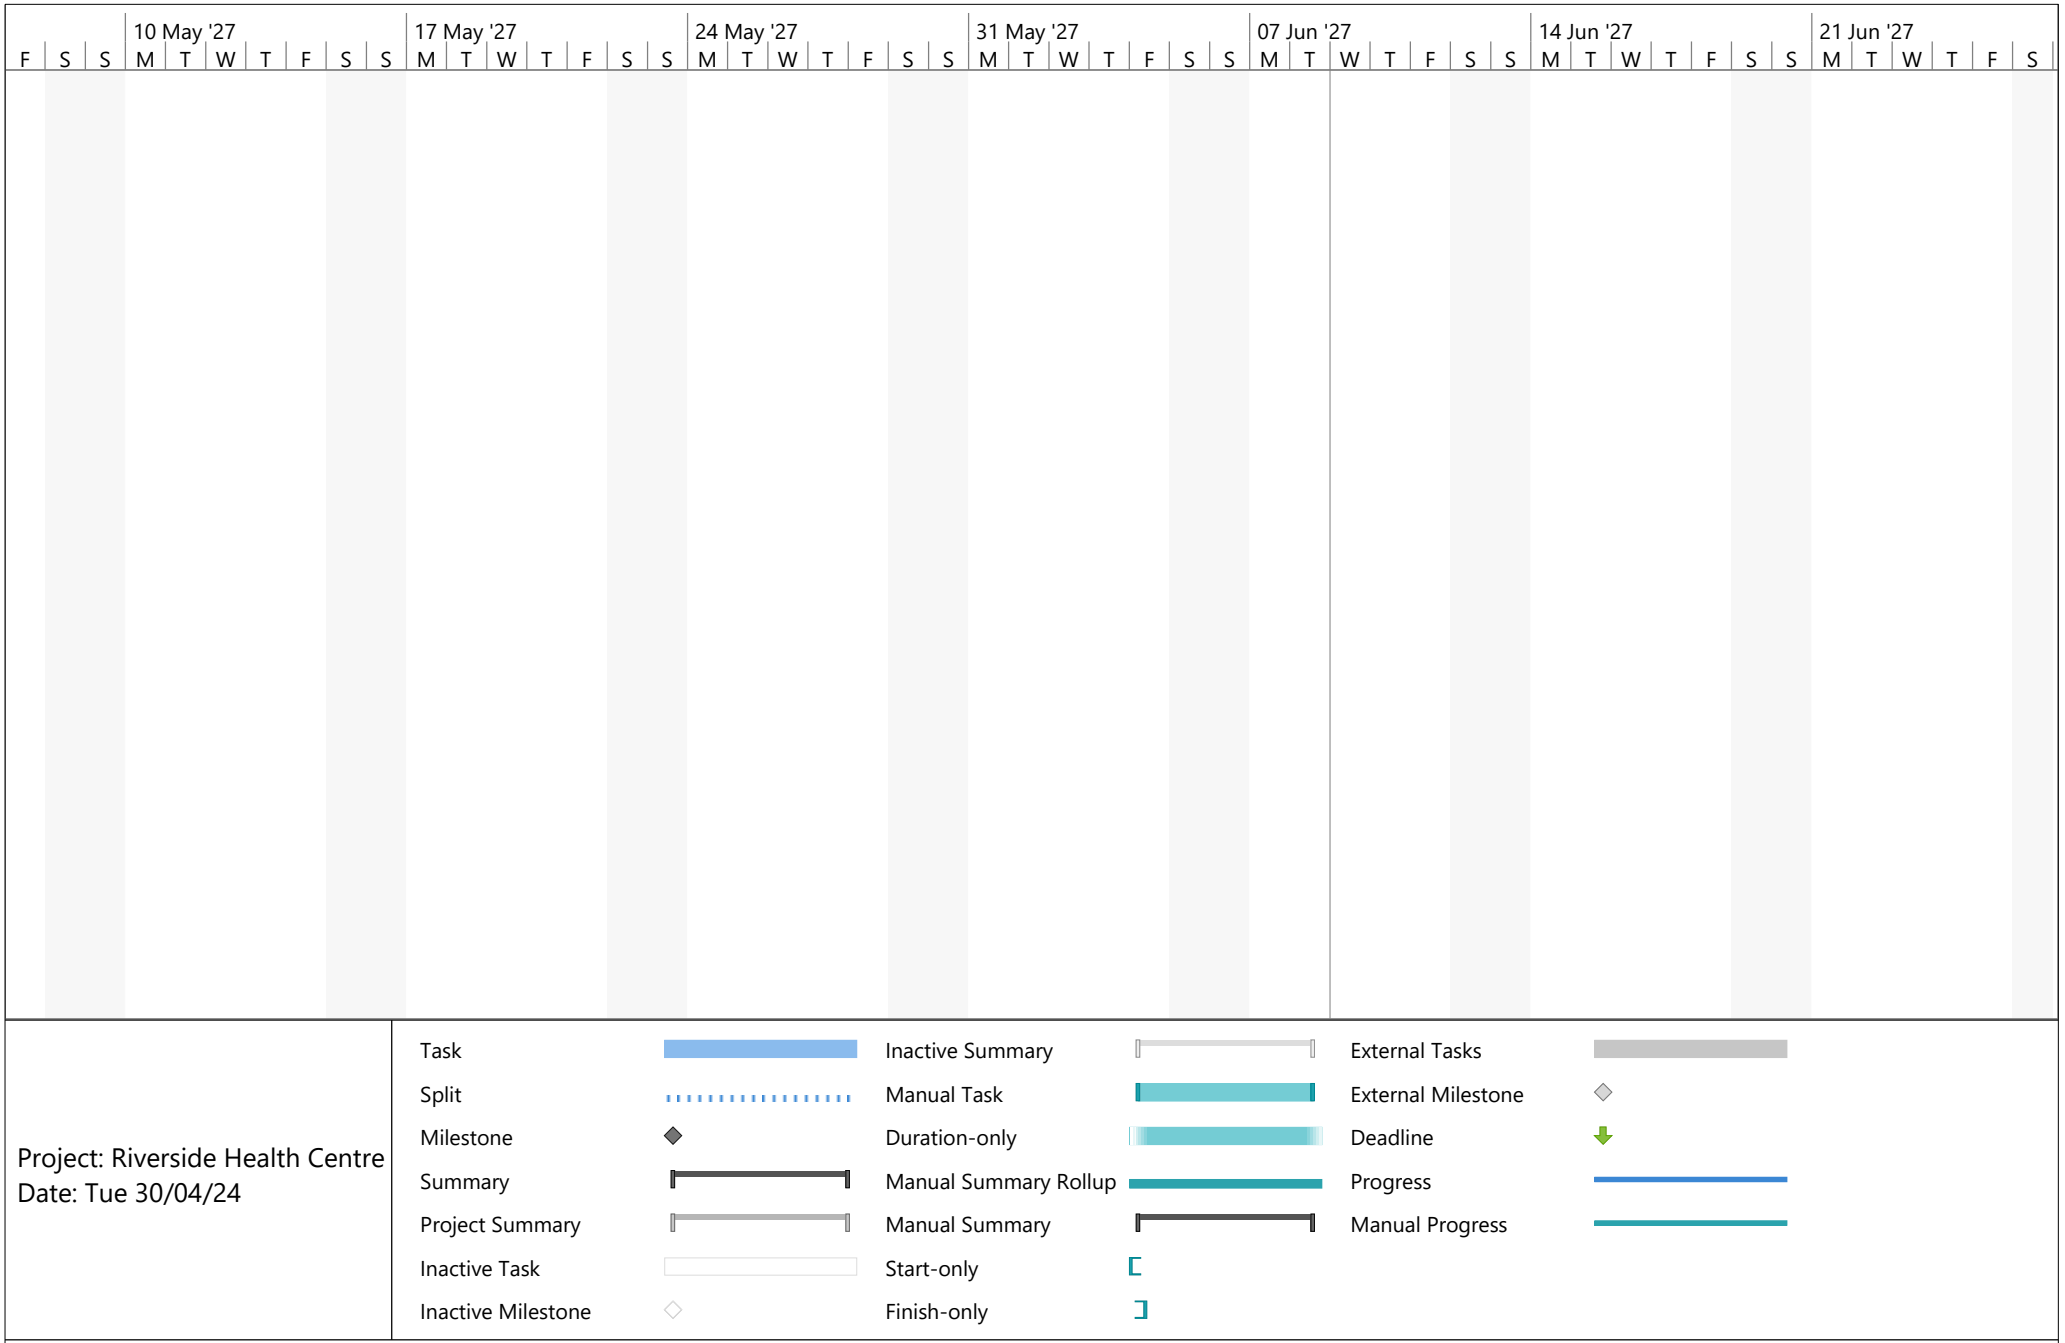
10 May '27
17 May '27
24 May '27
31 May '27
07 Jun '27
14 Jun '27
21 Jun '27
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

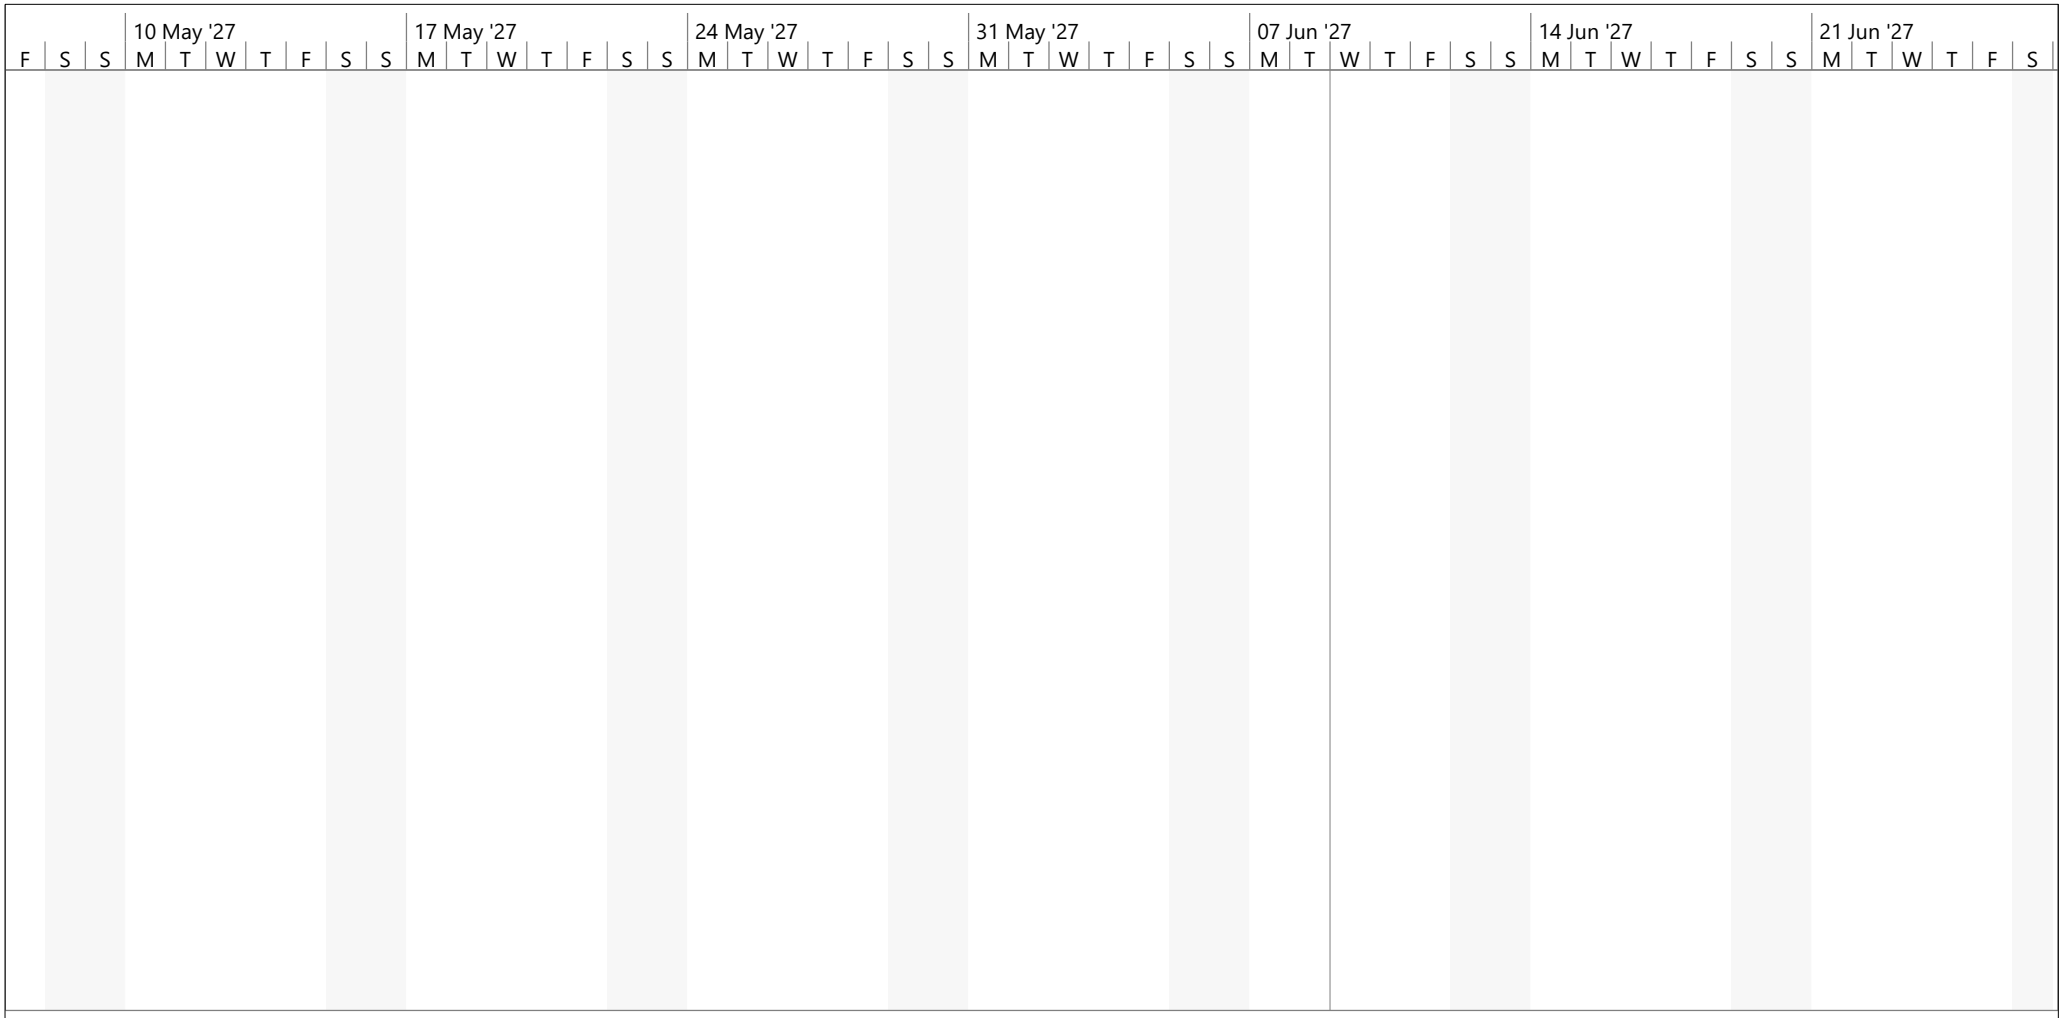


Project: Riverside Health Centre
Date: Tue 30/04/24

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

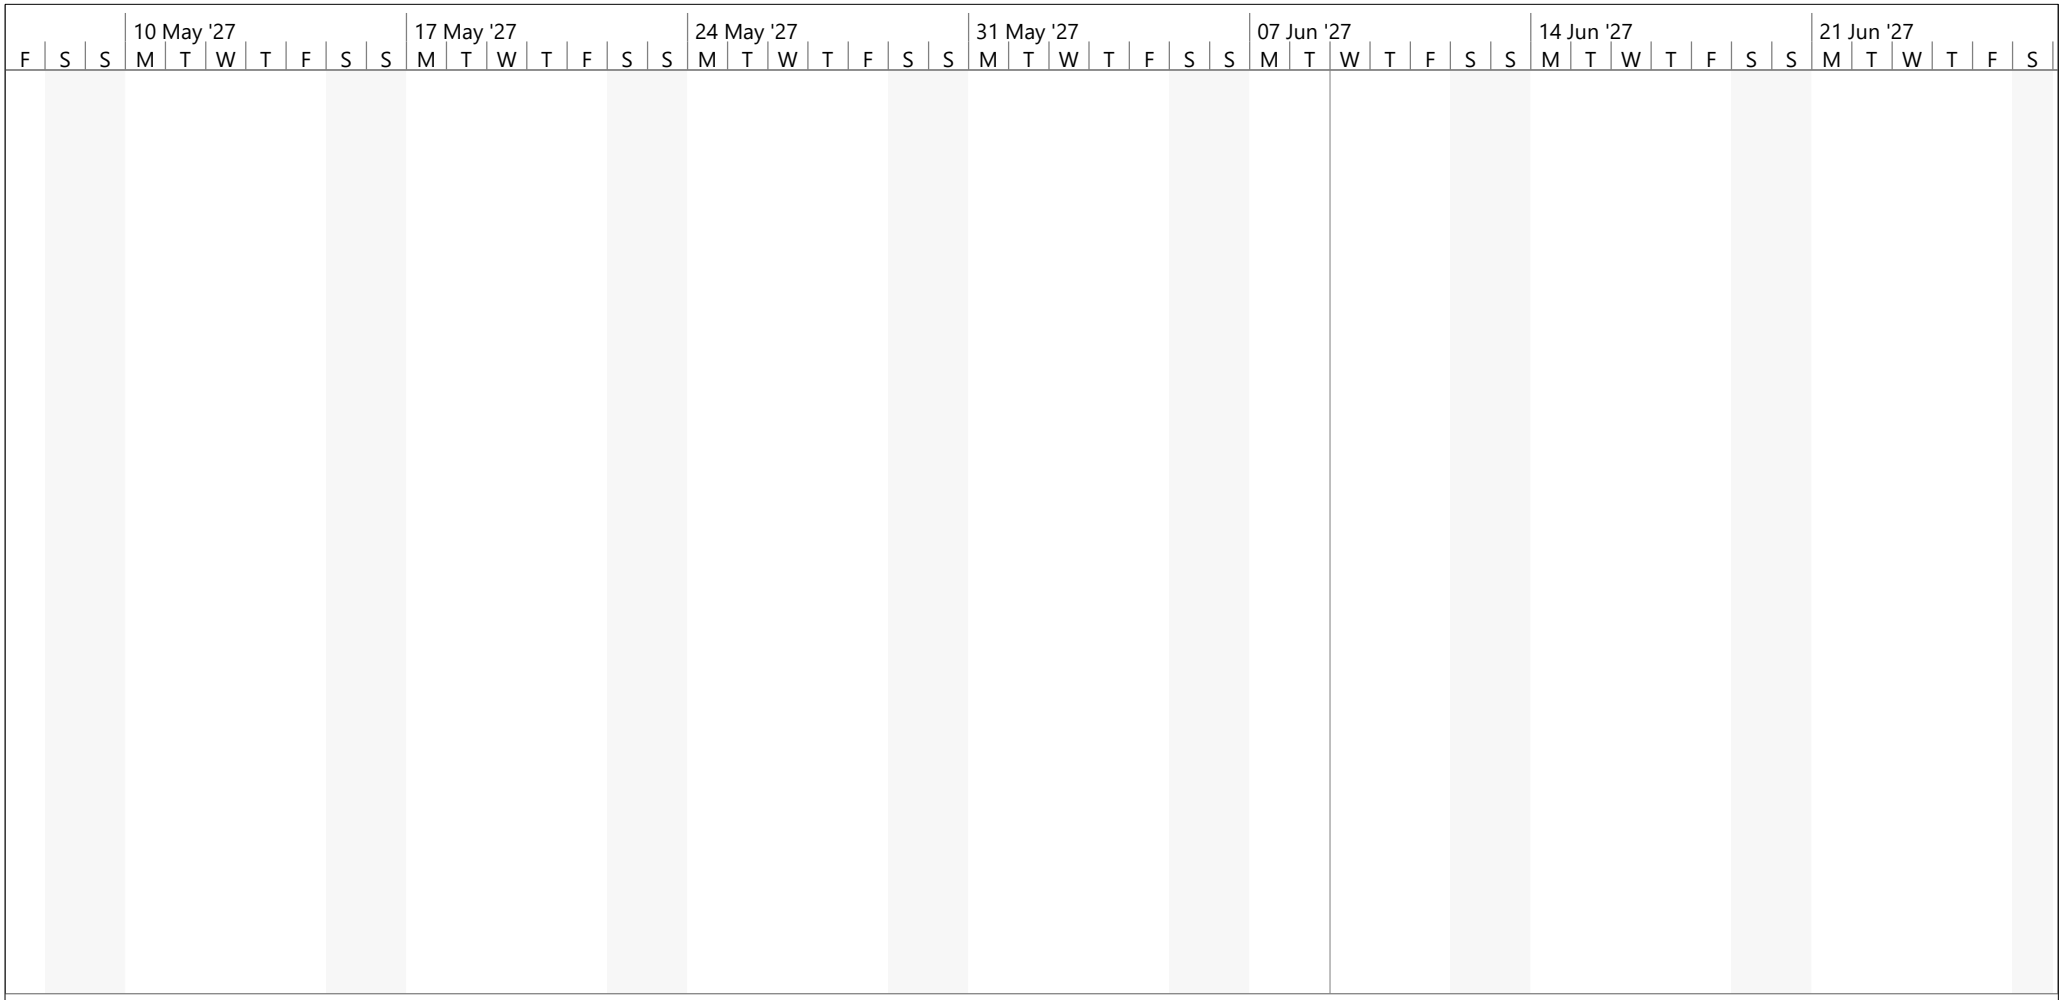


Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

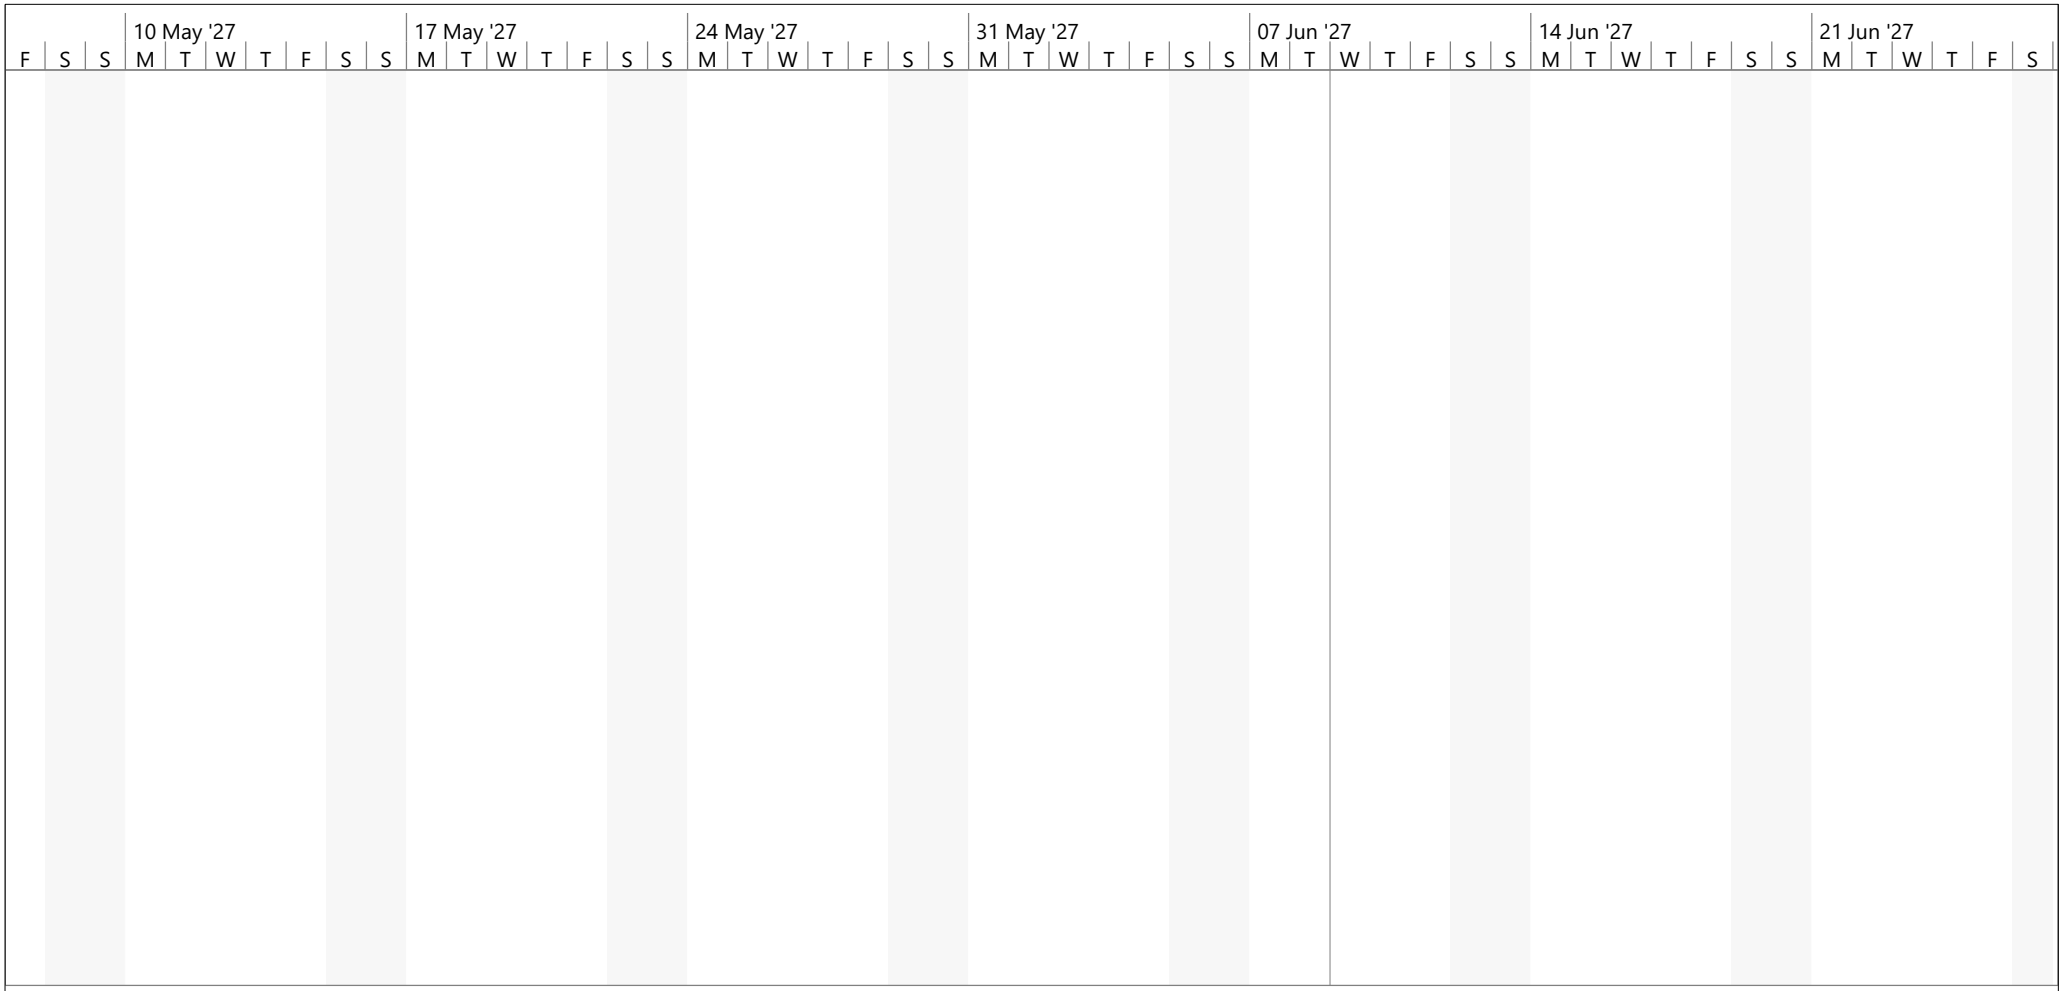

Project: Riverside Health Centre
Date: Tue 30/04/24


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

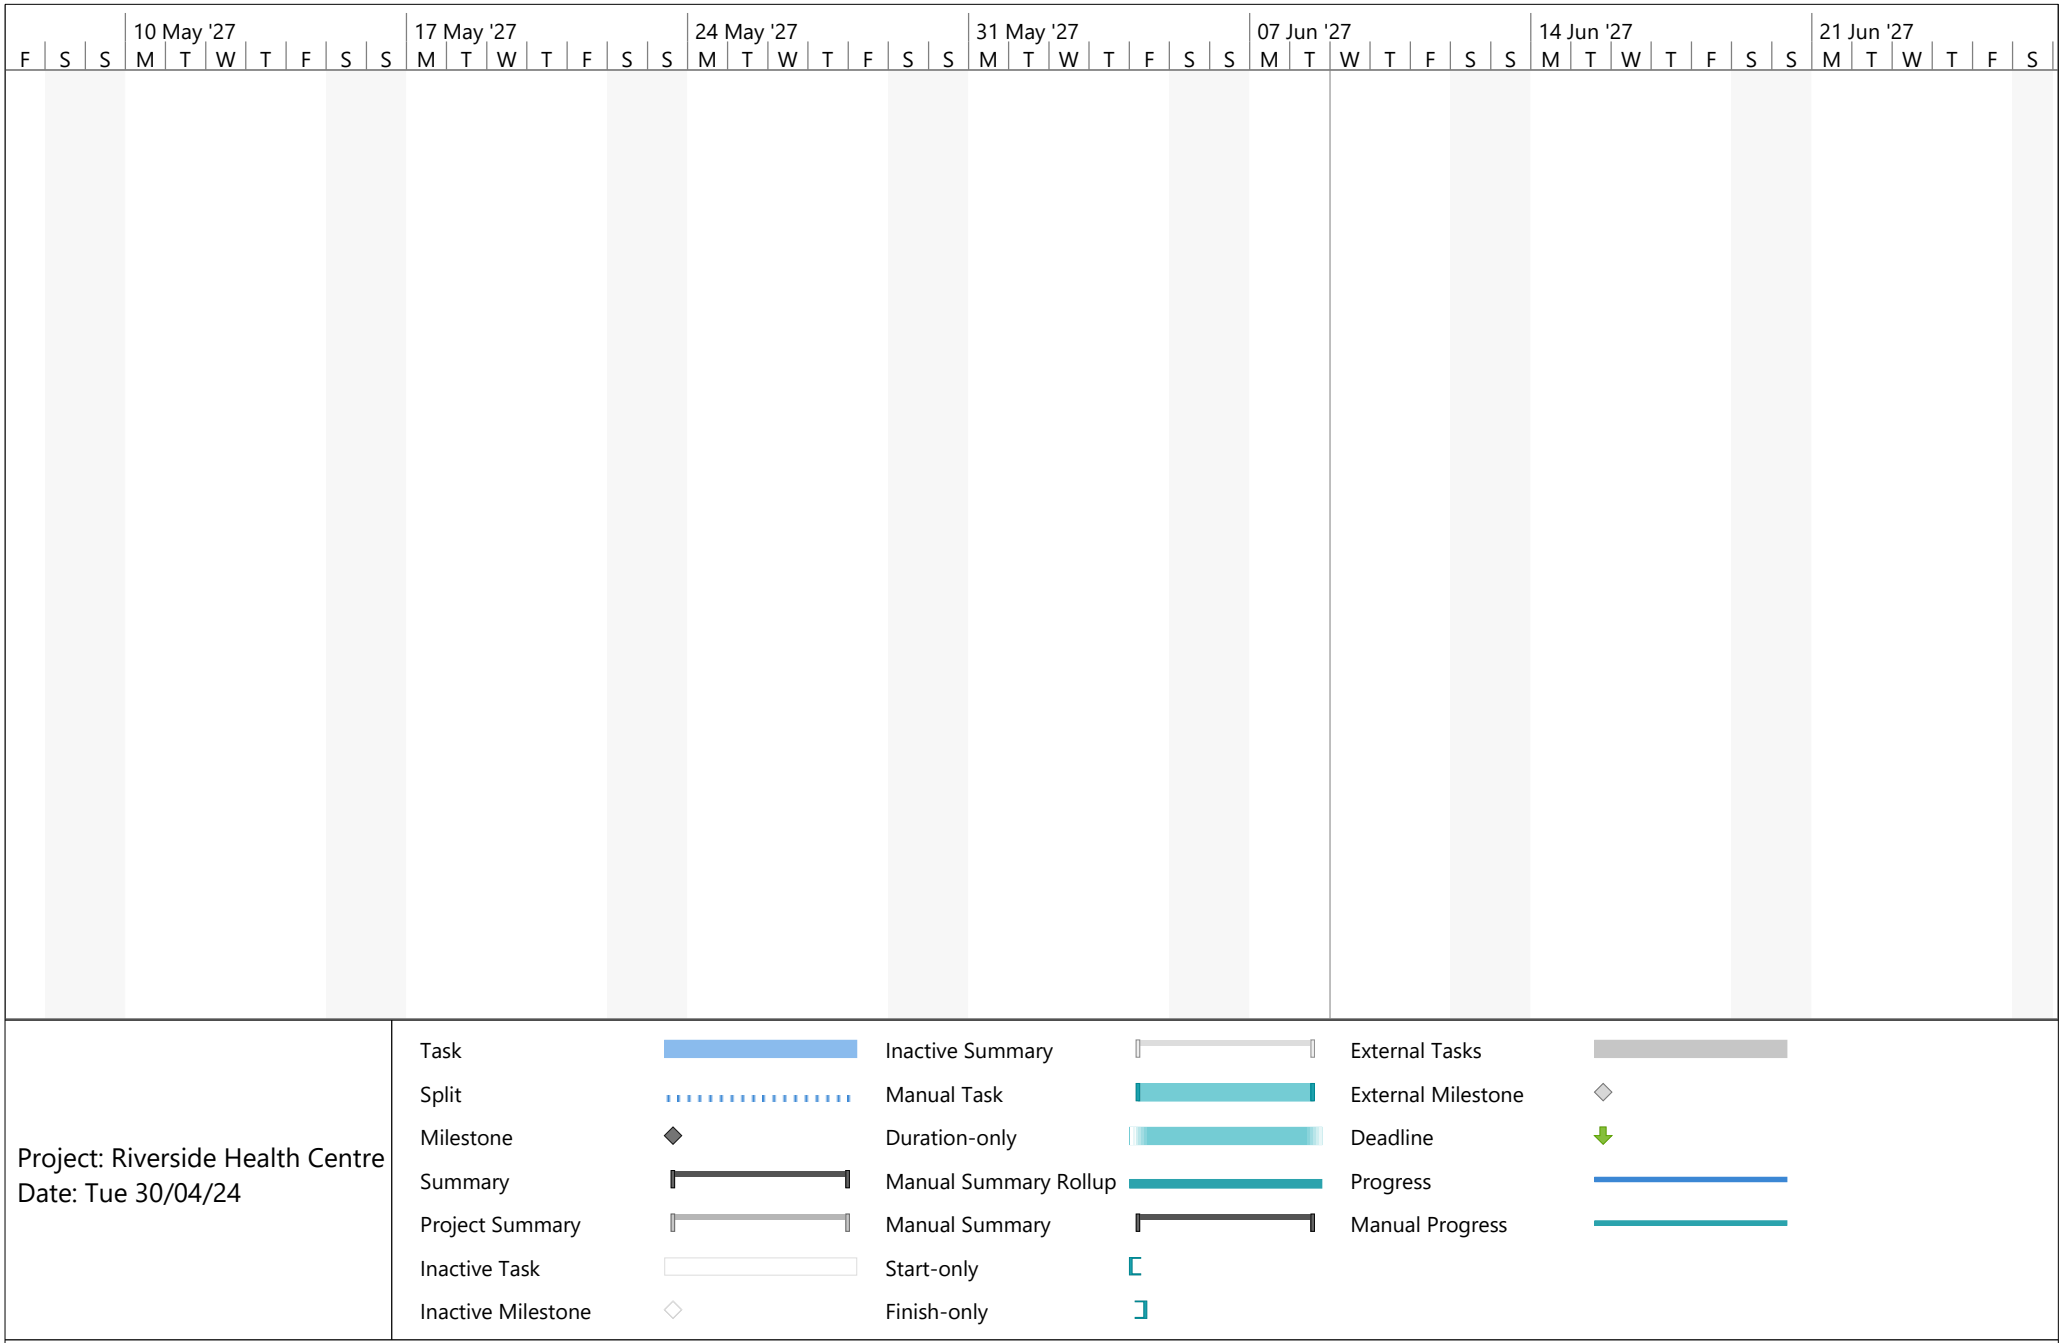
10 May '27
17 May '27
24 May '27
31 May '27
07 Jun '27
14 Jun '27
21 Jun '27
F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S
Project: Riverside Health Centre
Date: Tue 30/04/24
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

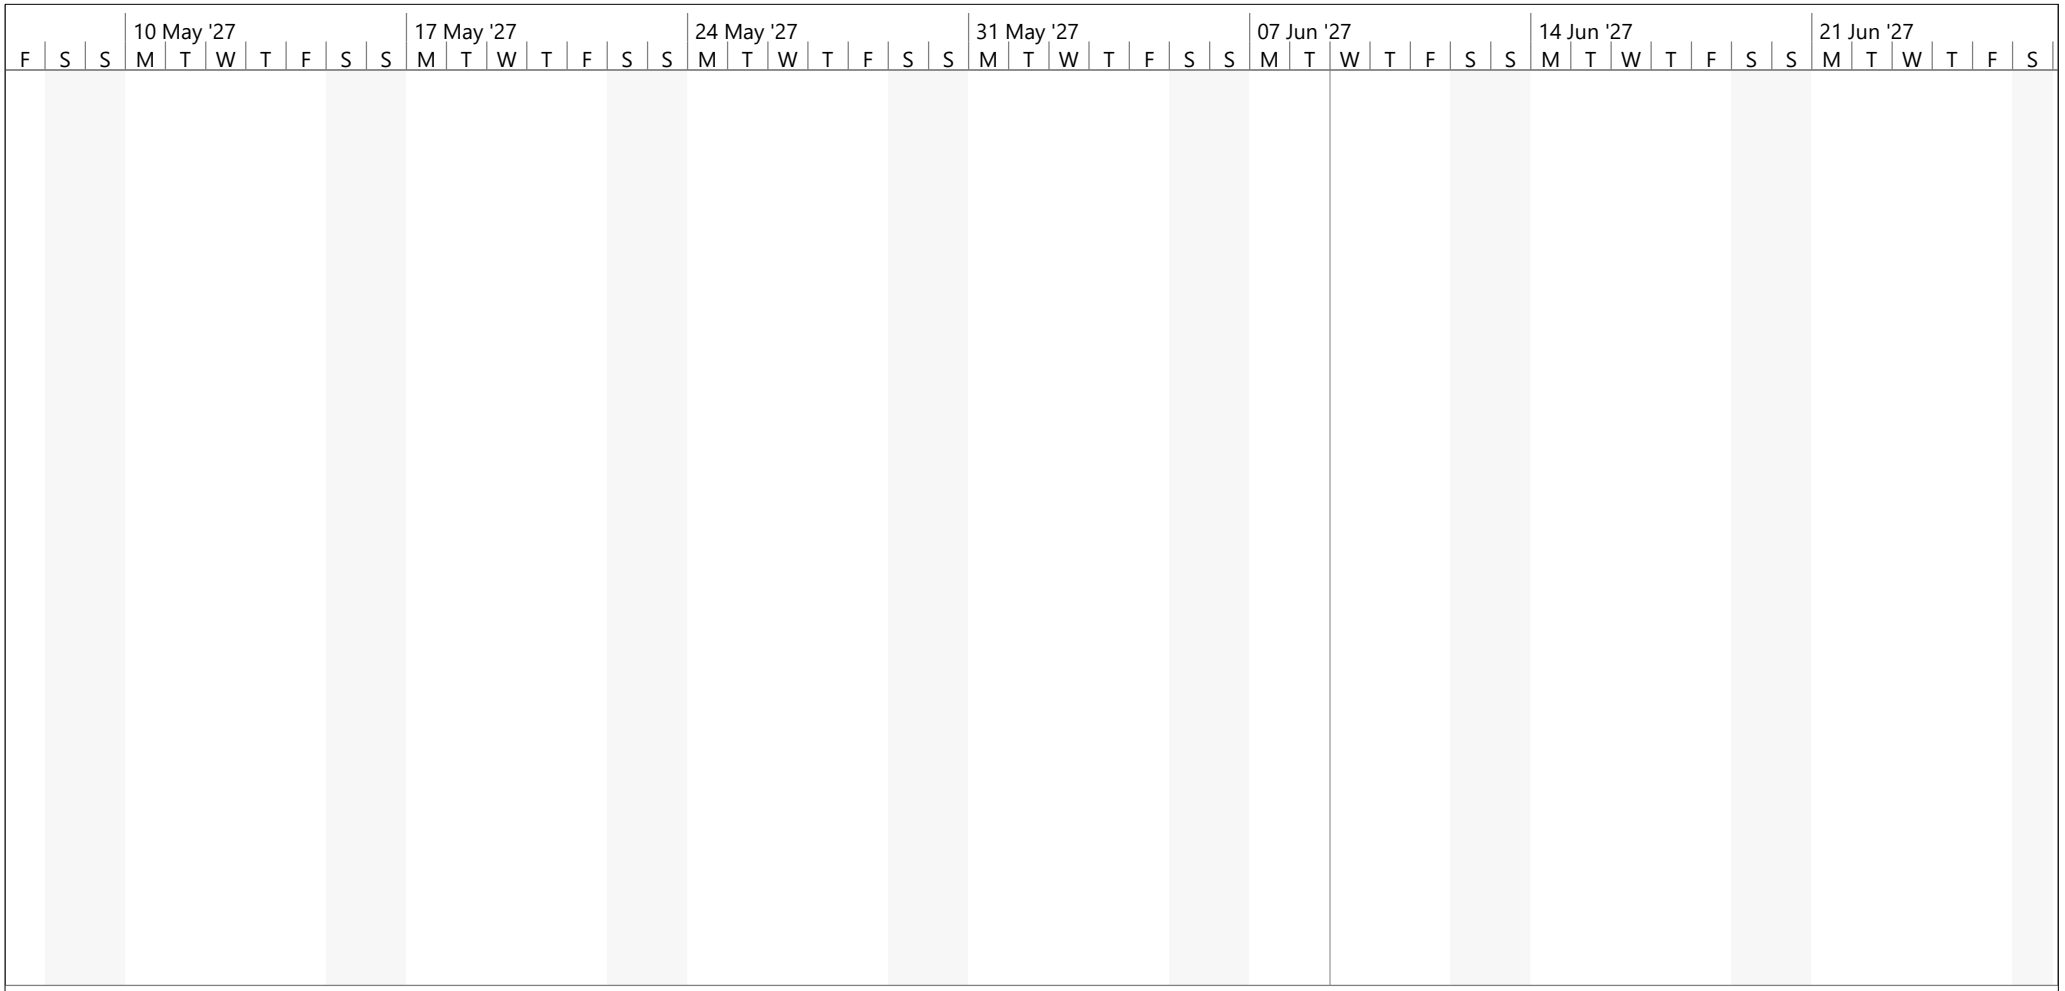


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

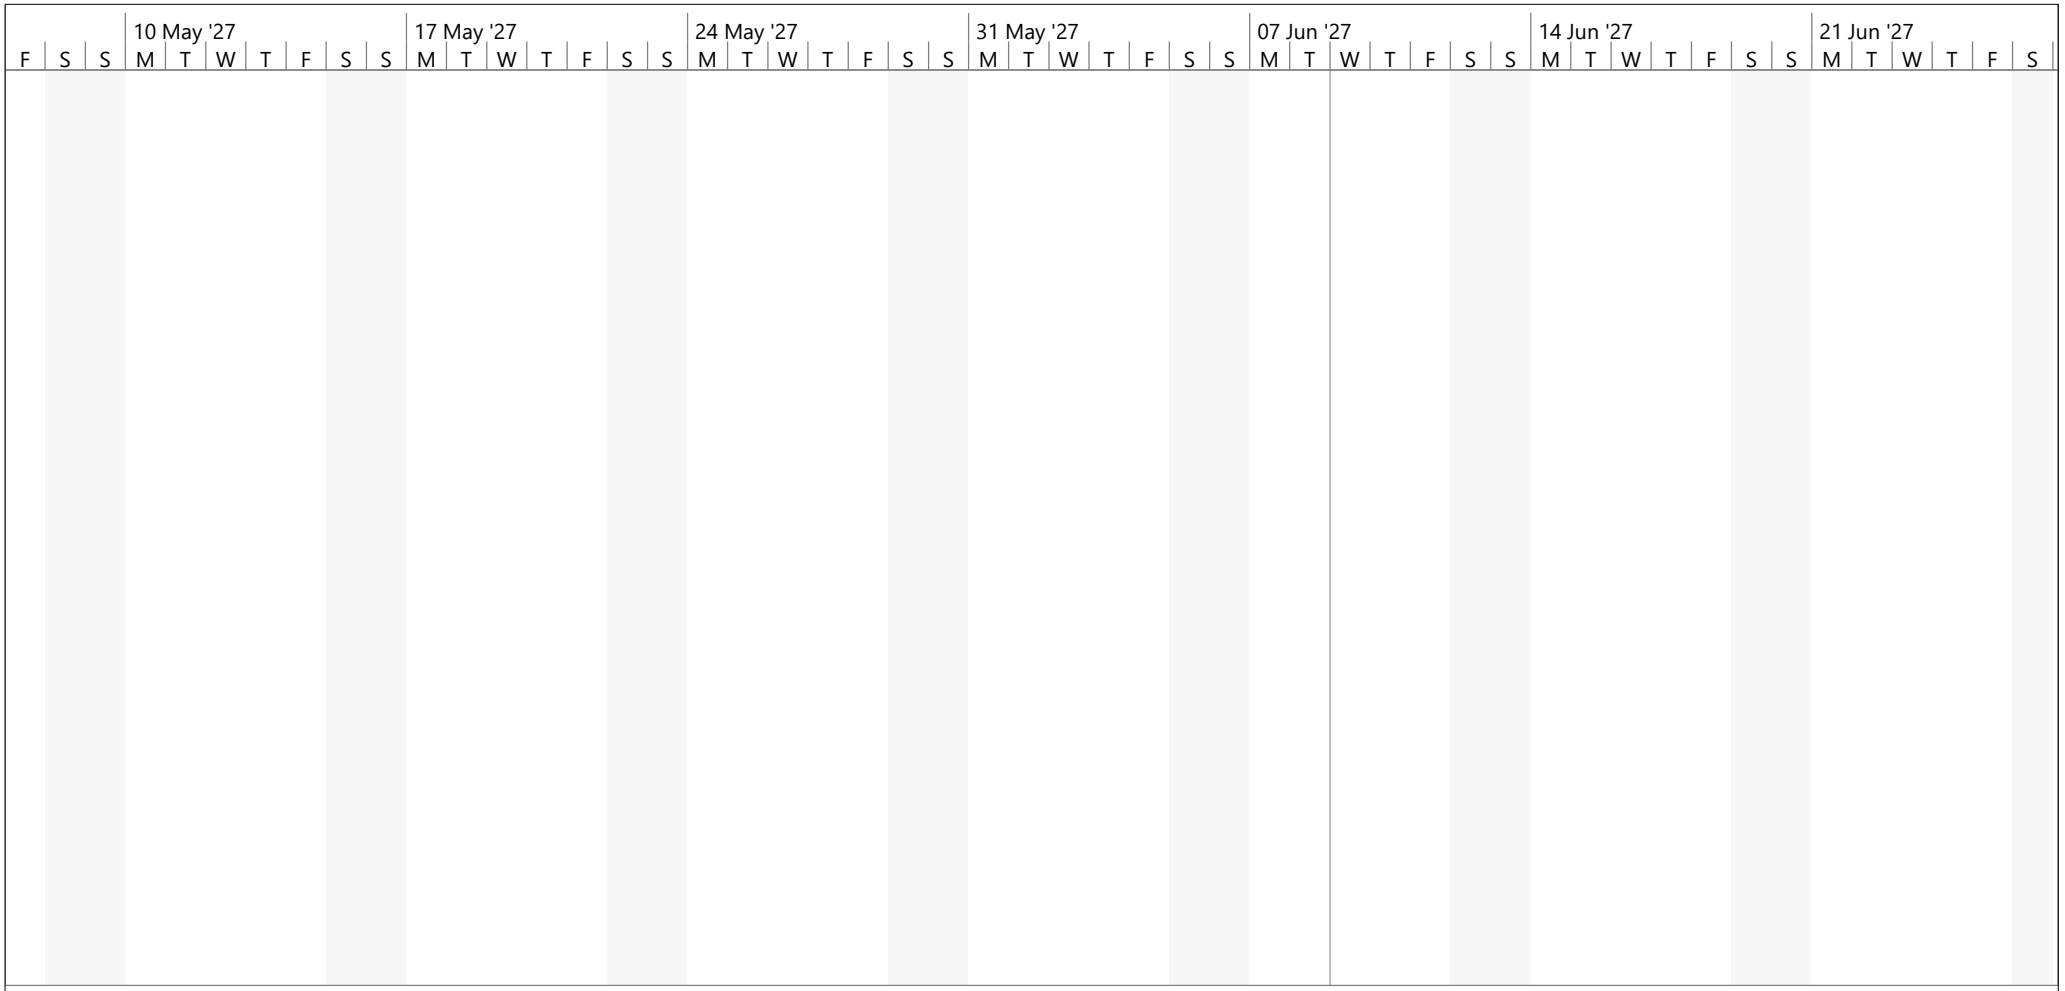


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

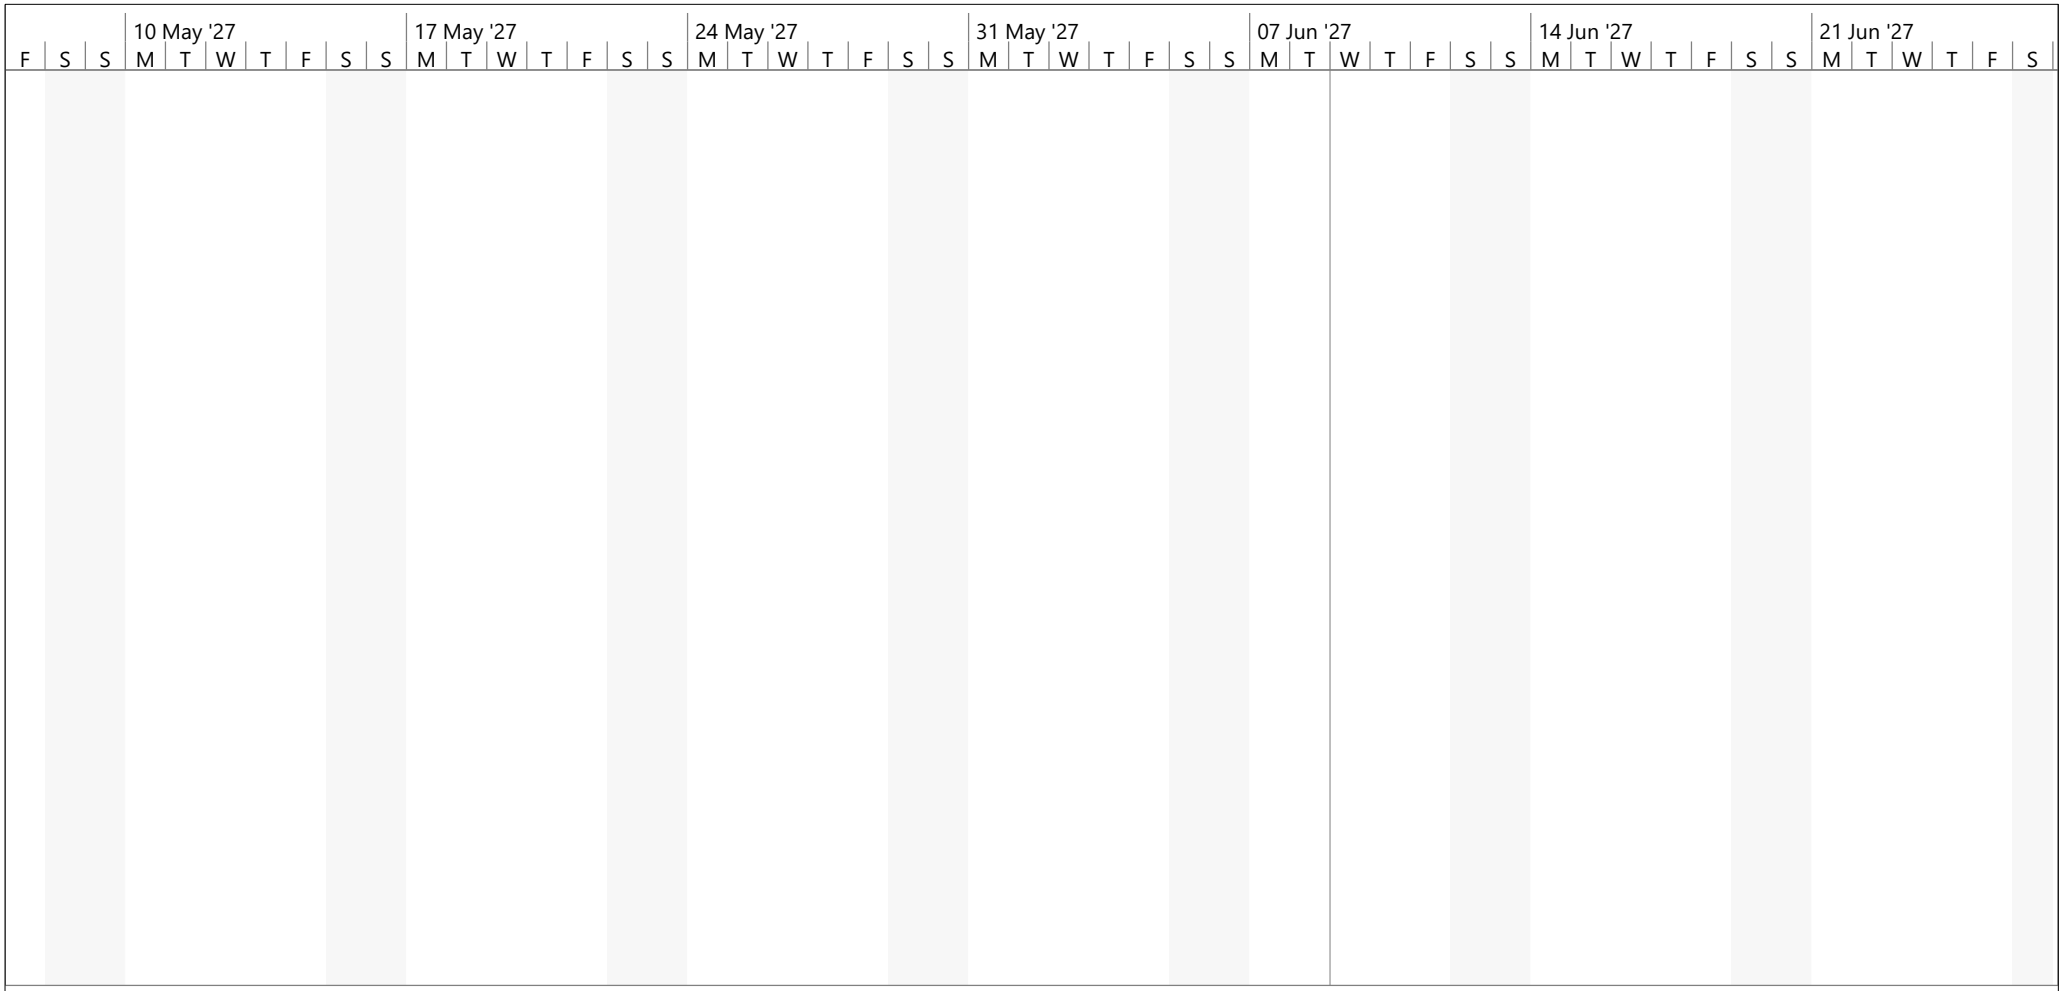


Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

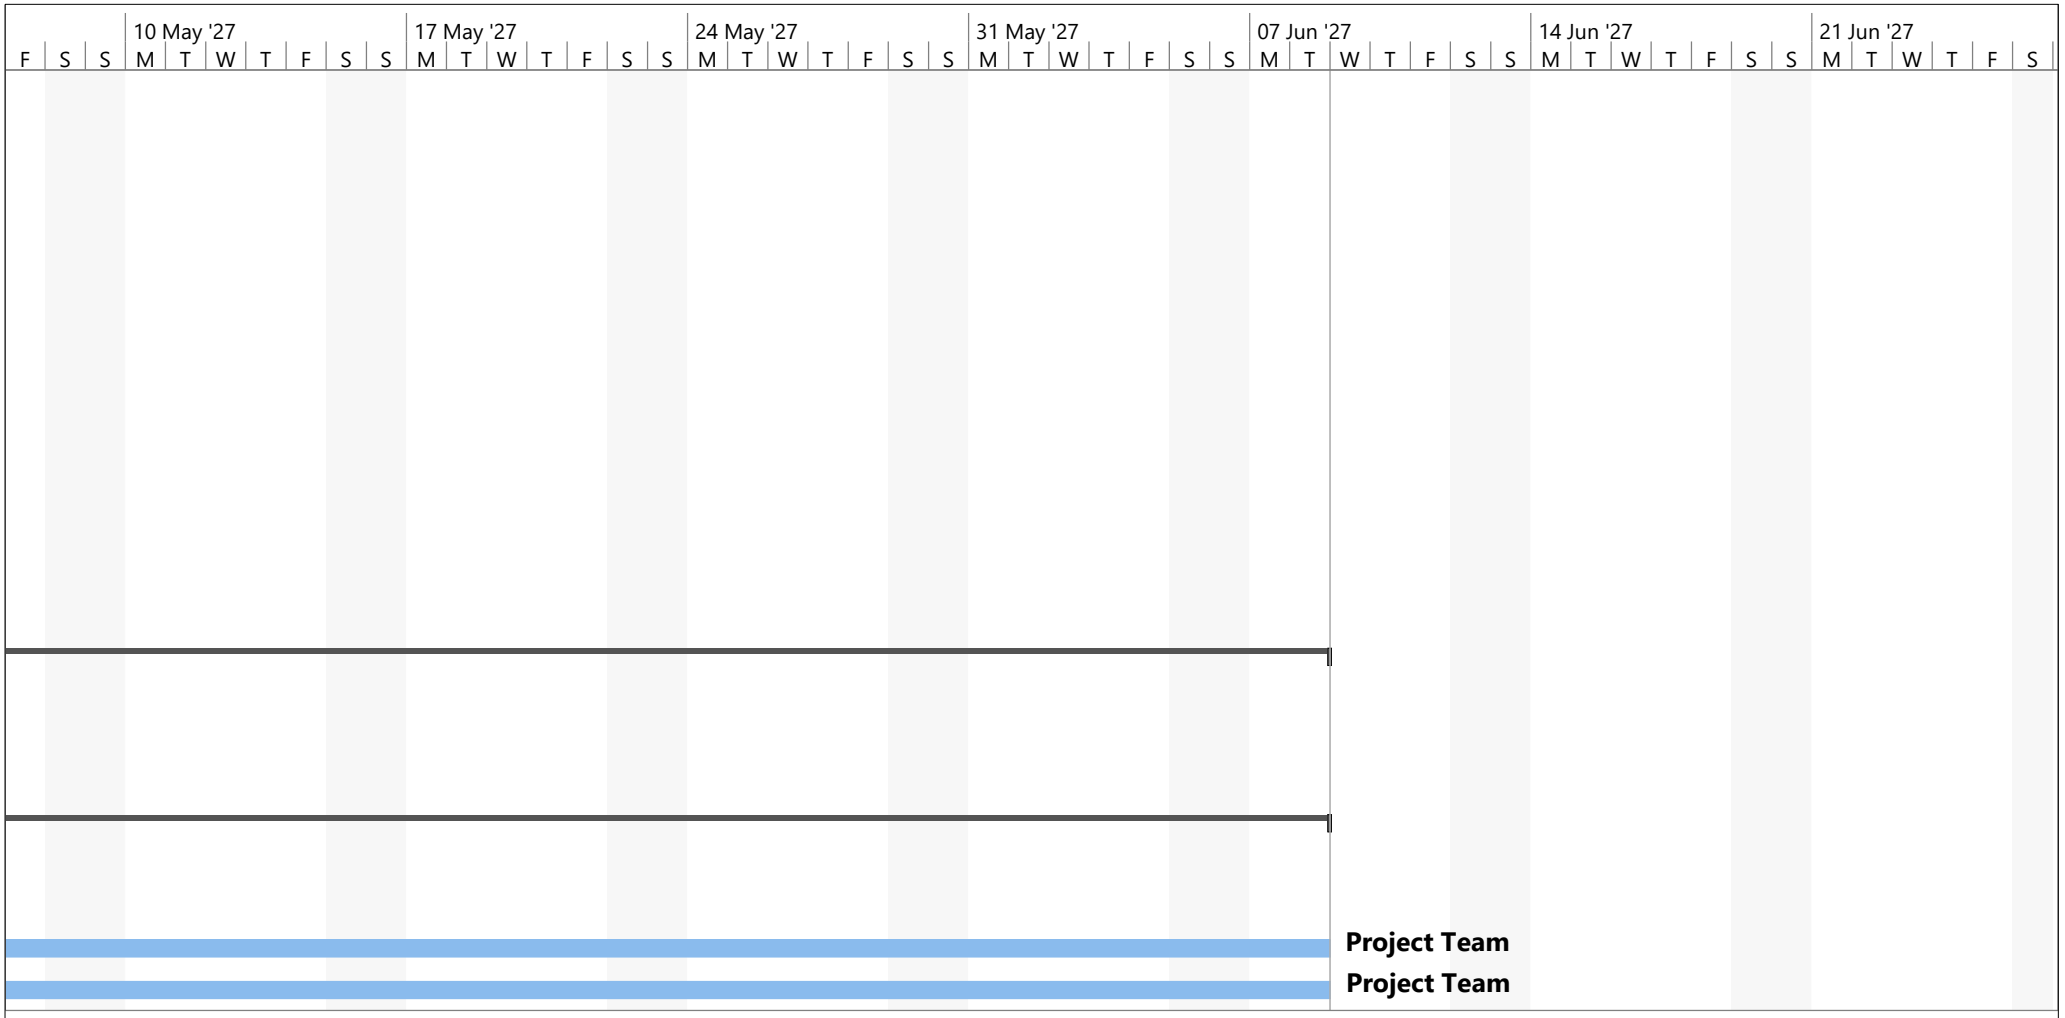

Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: Riverside Health Centre
Date: Tue 30/04/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
